

**405th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
July, 2019**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for July 2019 contains information on the status of the 1623 Central Sector Infrastructure Projects costing ₹150 crore and above. During July 2019, 9 projects have reported completion.
2. During the reference month, out of 1623 projects, 552 projects are delayed with respect to their original schedules and 73 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 73 projects, 34 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	839	219	17	2
2	RAILWAYS	315	141	30	22
3	PETROLEUM	151	47	9	5
4	COAL	105	34	2	0
5	POWER	74	50	4	1
6	URBAN DEVELOPMENT	63	27	6	1
7	HEALTH AND FAMILY WELFARE	20	11	0	0
8	CIVIL AVIATION	13	5	0	0
9	STEEL	9	8	4	3
10	SHIPPING AND PORTS	8	1	0	0
11	FERTILISERS	5	1	1	0
12	MINES	5	0	0	0
13	ATOMIC ENERGY	4	4	0	0
14	TELECOMMUNICATIONS	4	2	0	0
15	INFORMATION AND BROADCASTING	3	1	0	0
16	WATER RESOURCES	2	1	0	0
17	DEFENCE PRODUCTION	2	0	0	0
18	HEAVY INDUSTRY	1	0	0	0
Total		1623	552	73	34

3. Total original cost of implementation of the 1623 projects was ₹19,33,390.22 crore and their anticipated completion cost is likely to be ₹23,21,502.84 crore, which reflects overall cost overruns of ₹3,88,112.62 crore (20.07% of original cost). The expenditure incurred on these projects till July 2019 is ₹9,47,571.45 crore, which is 40.82% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost
Overruns (as on 01-08-2019)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.02
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.02
	COAL				
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEAGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	19.86
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	24.10
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.06
	PETROLEUM				
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	95.30
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	345.92	70.45
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
2	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	5024.35	203.22
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7419.34	197.14
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	155.05
5	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
	RAILWAYS				
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
2	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	04/2011	120.70	1800.00	1391.30
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
4	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15

5	ATTIPPATTU PUTTUR	04/2008	151.84	1105.00	627.74
ROAD TRANSPORT AND HIGHWAYS					
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	880.06
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
3	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	195.04	377.99	93.80
4	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
5	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	03/2012	207.03	389.45	88.11
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	12.88
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	49.05
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	3.58
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58
4	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	488.28	25.85
WATER RESOURCES					
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-08-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00

3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.14
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.07
	COAL				
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	1173.30
2	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
3	BHANEAGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	99.78
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.09
	PETROLEUM				
1	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
2	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
3	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
4	MUMBAI REFINERY EXPANSION PROJECT	09/2015	4199.00	5060.00	861.00
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	821.27
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	6077.52
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7419.34	4922.44
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	9996.59	4643.59
	RAILWAYS				
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12524.00	8069.83
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
	ROAD TRANSPORT AND HIGHWAYS				
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	6786.82
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
3	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2525.80	1137.46
4	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
5	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
	SHIPPING AND PORTS				

1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	31.48
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	7615.00
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	8.30
	URBAN DEVELOPMENT				
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5687.79	506.00
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
4	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1623 projects, 378 are on schedule, 552 are delayed, 355 projects reported cost overrun and 178 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 451 if delay is calculated on the basis of latest schedule of completion. Further, for 670 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 552 delayed projects, 187 (33.87%) projects have overall delay in the range of 1 to 12 months, 121 (21.92%) projects have delay in the range of 13 to 24 months, 132 (23.91%) projects have delay in the range of 25 to 60 months and 112 (20.28%) projects have delay of 61 months and above. **The average time overrun in these 552 delayed projects is 29.07 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-08-2019)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36

	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
2	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	12/2020	9
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	12/2020	8
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	12/2019	6
5	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	08/2022	6
	COAL				
1	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2022	144
2	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
4	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2020	120
5	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2021	120
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	09/2019	34
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	10/2020	83
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	09/2019	28
3	AIIMS - OPD(NEW)	08/2014	05/2017	08/2019	27
4	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	09/2019	19
5	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	09/2019	16
	INFORMATION AND BROADCASTING				
1	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	02/2019	11/2019	9
	PETROLEUM				
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
2	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	12/2019	81
3	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2019	79
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
5	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014	08/2019	58
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	08/2019	129
3	BARH STPP(3X660MW) NTPC	02/2005	10/2011	08/2021	118
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	08/2019	116
5	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2022	114
	RAILWAYS				
1	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
2	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2021	252
3	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	06/2022	235
5	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	03/2006	03/2025	228
	ROAD TRANSPORT AND HIGHWAYS				
1	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2019	140

1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	213.50	06/2019	12/2019
3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	219.91	219.91	65.45	03/2020	12/2020
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	233.38	233.38	84.73	04/2020	12/2020
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	232.44	03/2021	03/2021
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	09/2019
3	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	18.45	03/2022	03/2022
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	6860.71	11/2021	11/2021
5	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	319.81	03/2020	03/2020
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	147.00	11/2013	10/2020
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	184.93	06/2020	08/2020
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	244.66	04/2020	06/2020
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	241.39	09/2018	N.A.
HEAVY INDUSTRY							
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	335.03	09/2019	09/2019
INFORMATION AND BROADCASTING							
1	NATIONAL FILM HERITAGE MISSION	11/2014	597.41	597.41	29.80	N.A.	N.A.
2	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	204.32	204.32	0.00	02/2019	11/2019

3	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	167.70	167.70	0.00	03/2020	03/2020
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.57	02/2017	10/2021
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
5	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	07/2014	247.00	247.00	0.00	03/2021	03/2021
POWER							
1	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10927.32	09/2010	N.A.
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3268.00	10/2017	N.A.
4	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	210.72	04/2016	12/2019
5	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1152.85	04/2020	12/2023
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2010.00	654.07	07/2012	03/2024
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	274.97	03/2019	03/2020
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	148.43	03/2006	03/2025
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	559.91	541.07	07/2014	N.A.
ROAD TRANSPORT AND HIGHWAYS							
1	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	131.71	N.A.	10/2020
2	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED	01/1991	319.68	369.77	113.67	N.A.	N.A.

	SHOULDERS (KM 40 TO KM 219.945) OF NH-104						
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	278.45	08/2016	N.A.
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	411.12	12/2010	N.A.
4	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	600.00	257.90	1.45	12/2017	05/2020
5	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	05/2016	970.00	970.00	109.97	05/2020	05/2020
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.03	06/2017	N.A.
3	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	117.63	10/2018	09/2019
URBAN DEVELOPMENT							
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.

WATER RESOURCES							
1	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	233.57	233.57	32.20	12/2019	12/2019

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-08-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5784.74
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	0.00	296.92
2	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.10	0.00	493.85
3	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	347.15
4	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	539.59
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	228.90
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	508.29
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	0.00	1285.65
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7522.82
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10927.32
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7419.34	7494.35
4	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	2187.32	2237.45
5	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	0.00	2969.55

	RAILWAYS				
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	654.07
2	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	541.07
3	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	815.41
4	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	669.21
5	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	927.86
	ROAD TRANSPORT AND HIGHWAYS				
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	472.00
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	319.96
3	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	0.00	451.15
4	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	326.35
5	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	337.08
	SHIPPING AND PORTS				
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	411.12
2	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.00	275.58
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	0.00	15811.82
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.77
4	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	5188.00
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	0.00	422.79
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	0.00	16417.99

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-08-2019)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	03/2016	N.A.	N.A.
3	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
4	MURAIIDH UG TURN-KEY PROJECT	02/2011	04/2014	N.A.	N.A.
5	MOONIDH XV SEAM UG	08/2011	04/2015	N.A.	N.A.
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 4	12/2016	05/2018	03/2019	N.A.
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
3	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	N.A.
INFORMATION AND BROADCASTING					
1	NATIONAL FILM HERITAGE MISSION	11/2014	N.A.	N.A.	N.A.
MINES					
1	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
3	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	03/2015	N.A.	N.A.
4	RESID UPGRADATION PROJECT	03/2013	11/2015	N.A.	N.A.
5	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	05/2015	04/2019	06/2019	10/2018
POWER					
1	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
4	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
5	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
3	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	N.A.
4	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	02/2009	N.A.	N.A.
5	ETAWAH-MAINPURI (NL),NCR	04/1997	12/2008	03/2015	03/2015
ROAD TRANSPORT AND HIGHWAYS					

1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	N.A.	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	N.A.	N.A.
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	12/2017	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
4	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 31.07.2019 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	839	17
2	RAILWAYS	315	30
3	PETROLEUM	151	9
4	COAL	105	2
5	POWER	74	4
6	URBAN DEVELOPMENT	63	6
7	HEALTH AND FAMILY WELFARE	20	0
8	CIVIL AVIATION	13	0
9	STEEL	9	4
10	SHIPPING AND PORTS	8	0
11	FERTILISERS	5	1
12	MINES	5	0
13	ATOMIC ENERGY	4	0
14	TELECOMMUNICATIONS	4	0
15	INFORMATION AND BROADCASTING	3	0
16	WATER RESOURCES	2	0
17	DEFENCE PRODUCTION	2	0
18	HEAVY INDUSTRY	1	0
	Total	1623	73

TABLE-2

Month wise List of Completed Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2019			
	<u>COAL</u>			
1	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI (NORTHERN COAL FIELDS LIMITED) - [N06000033]	259.40	03/2012	266.38
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) (NORTHERN COAL FIELDS LIMITED) - [N06000091]	1,131.28	03/2018	796.85
	<u>PETROLEUM</u>			
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000175]	3,076.00	09/2017	3,450.30
	<u>POWER</u>			
4	BONGAIGAON THERMAL POWER PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000041]	4,375.35	10/2011	7,000.00
5	TRIPURA GAS BASED POWER PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000071]	421.01	07/2013	963.23
	<u>RAILWAYS</u>			
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) RAILWAY) - [N22000113]	653.19	03/2014	862.17
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000357]	567.51	03/2018	421.60
	May,2019			
	<u>COAL</u>			
8	MAKARDHOKRA I OC (WESTERN COAL FIELDS LIMITED) - [N06000119]	266.23	03/2021	144.38
	<u>PETROLEUM</u>			
9	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000084]	736.65	09/2011	331.47
10	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000290]	474.15	05/2019	348.64
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	WESTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000035]	477.69	09/2010	691.96
12	KUDGI STPP STAGE 1 (NATIONAL THERMAL POWER CORPORATION) - [N18000131]	15,166.19	01/2017	15,364.00
13	SOLAPUR STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000133]	9,395.18	01/2017	8,617.00
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000158]	539.82	06/2016	434.33
15	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000174]	3,363.12	12/2016	2,244.00
16	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000222]	790.13	06/2019	575.24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000145]	1,585.00	05/2013	2,023.33
18	JORBAT - BARAPANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000180]	536.00	01/2014	845.41
19	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S EPC(PUBLIC WORKS DEPT OF STATE) - [N24000241]	177.18	03/2016	40.51
20	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000242]	158.65	03/2016	103.50
21	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW EPC(PUBLIC WORKS DEPT OF STATE) - [N24000243]	244.08	03/2016	38.32
22	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000244]	340.00	03/2016	2.00
23	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000246]	244.30	12/2016	2.00
24	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S (PUBLIC WORKS DEPT OF STATE) - [N24000249]	218.31	12/2015	208.28
25	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000250]	260.39	11/2016	188.00
26	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000255]	220.72	11/2016	155.30
27	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000261]	267.16	11/2017	308.33
28	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A EPC(DEPT OF ROAD TRANSPORT & HIGHWAYS) - [N24000262]	201.12	02/2015	150.19
29	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) (PUBLIC WORKS DEPT OF STATE) - [N24000263]	241.61	02/2017	178.94

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
30	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN EPC(PUBLIC WORKS DEPT OF STATE) - [N24000265]	297.78	02/2017	284.89
31	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC (PUBLIC WORKS DEPT OF STATE) - [N24000266]	361.30	07/2014	203.29
32	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) EPC(PUBLIC WORKS DEPT OF STATE) - [N24000267]	258.99	07/2014	200.44
33	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC EPC(PUBLIC WORKS DEPT OF STATE) - [N24000268]	251.55	02/2015	172.65
34	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000269]	175.03	-	152.53
35	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP EPC(PUBLIC WORKS DEPT OF STATE) - [N24000272]	266.00	-	182.13
36	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000273]	314.43	-	216.96
37	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000277]	185.82	-	142.23
38	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500- KM 130.00 DHAMTARI- KANKER SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000278]	213.47	03/2015	182.91
39	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV EPC(PUBLIC WORKS DEPT OF STATE) - [N24000279]	298.34	03/2015	269.93
40	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I EPC(PUBLIC WORKS DEPT OF STATE) - [N24000280]	262.54	03/2015	215.11
41	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00- 342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000283]	169.26	12/2012	280.72
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000284]	170.21	11/2014	140.09
43	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849- KM 317.406 KAWARDHA- SIMGA SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000286]	394.20	-	332.62
44	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000288]	422.34	-	406.40
45	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE EPC(PUBLIC WORKS DEPT OF STATE) - [N24000289]	435.90	-	380.41
46	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000290]	279.68	-	286.96
47	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000291]	463.65	-	536.84

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
48	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000292]	573.96	-	557.08
49	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000293]	480.21	-	372.37
50	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000299]	224.83	05/2015	189.85
51	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU EPC(PUBLIC WORKS DEPT OF STATE) - [N24000300]	309.01	09/2015	391.89
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION EPC(PUBLIC WORKS DEPT OF STATE) - [N24000303]	417.61	06/2014	261.29
53	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000310]	377.83	07/2017	318.66
54	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000329]	497.89	04/2017	735.92
55	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000330]	629.74	-	721.04
56	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000336]	227.74	10/2016	187.85
57	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000369]	269.26	10/2016	212.72
58	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI EPC(PUBLIC WORKS DEPT OF STATE) - [N24000370]	483.38	-	470.16
59	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000372]	616.36	-	554.68
60	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000374]	486.74	-	415.58
61	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000377]	397.04	10/2016	368.49
62	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000381]	257.80	02/2016	59.30
63	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000383]	312.79	-	258.86
64	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K EPC(PUBLIC WORKS DEPT OF STATE) - [N24000384]	319.80	-	289.40
65	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000387]	264.16	-	533.18

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
66	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000390]	1,494.48	02/2011	2,158.50
67	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000393]	774.57	03/2018	613.58
68	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000394]	532.49	05/2017	386.02
69	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000399]	317.76	03/2017	344.30
70	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000403]	283.45	10/2016	285.18
71	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000404]	578.38	-	481.30
72	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA EPC(PUBLIC WORKS DEPT OF STATE) - [N24000405]	789.83	-	608.55
73	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000406]	208.87	05/2016	206.78
74	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000409]	176.22	02/2018	0.10
75	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000410]	641.02	12/2017	449.66
76	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000416]	224.83	04/2015	189.85
77	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000418]	493.94	03/2017	503.25
78	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000419]	165.00	09/2010	174.57
79	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000420]	104.00	09/2010	218.29
80	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000421]	235.08	05/2018	235.08
81	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000447]	670.82	02/2015	590.00
82	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000474]	327.32	05/2017	301.41
83	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000476]	273.06	-	199.72

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
84	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000512]	207.88	-	179.58
85	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000526]	899.21	-	748.74
86	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000529]	207.88	-	179.58
87	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000536]	377.64	03/2014	755.28
88	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO (PUBLIC WORKS DEPT OF STATE) - [N24000538]	292.98	11/2014	160.96
89	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000561]	244.00	07/2018	231.90
90	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000573]	322.01	08/2014	267.00
91	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY - KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000615]	334.22	06/2016	334.22
92	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000647]	162.51	05/2016	136.31
93	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 (PUBLIC WORKS DEPT OF STATE) - [N24000856]	170.00	02/2015	115.57
94	REHABILITATION AND UPGRADATION OF PURANPUR - KHUTAR SECTION FROM KM 38.00 TO KM 82.00 OF NH-730 TO 2 (PUBLIC WORKS DEPT OF STATE) - [N24001142]	225.96	06/2018	174.63
	June,2019			
	<u>RAILWAYS</u>			
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) (NORTH CENTRAL RAILWAY) - [220100007]	158.77	03/1994	682.34
96	AMRAVATI-NARKHER NL(CR) (CENTRAL RAILWAYS) - [220100118]	663.01	06/1999	726.33
97	CALICUT-MANGALORE (DL) (SR) (SOUTHERN RAILWAY) - [220100151]	240.00	-	0.01
98	MANDARHILL-DUMKA-RAMPURHAT (NL),ER (EASTERN RAILWAYS) - [220100168]	1,125.89	03/2016	1,180.08
99	KARUR-SALEM(NL),SR (SOUTHERN RAILWAY) - [220100191]	155.55	-	863.54
100	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR (NORTH CENTRAL RAILWAY) - [220100243]	108.00	12/2009	455.39
101	KATIHAR - JOGBANI (GC)(NEFR) (NORTH EAST FRONTIER RAILWAY) - [220100247]	792.46	12/2010	944.80

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
102	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) (NORTH EASTERN RAILWAY) - [220100256]	744.71	-	917.49
103	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) (SOUTHERN RAILWAY) - [220100263]	280.00	-	942.28
104	JIND-SONEPAT (NL),NR (NORTHERN RAILWAY) - [220100280]	238.56	03/2012	785.75
105	KODERMA GIRIDH (NL), ECR (EAST CENTRAL RAILWAYS) - [220100306]	768.87	-	988.38
106	MAHARAJGANJ-MASRAKH (NL) - NER (NORTH EASTERN RAILWAY) - [220100316]	218.19	06/2018	380.50
107	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000049]	732.81	03/2008	2,191.46
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE (SOUTHERN RAILWAY) - [N22000080]	343.17	-	1,110.44
109	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) (NORTHERN RAILWAY) - [N22000088]	369.90	03/2010	891.24
110	AGARTALA SABROOM, NL, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000099]	1,142.00	03/2014	3,354.18
111	DAKSHIN-BARASAL-LAKSHMIKANTAPUR (EASTERN RAILWAYS) - [N22000116]	259.51	02/2012	148.37
112	GHUTIASHARIF-CANNING (ER) (EASTERN RAILWAYS) - [N22000117]	193.08	12/2011	154.30
113	PANDABESWAR-CHINPAI DOUBLING (ER) (EASTERN RAILWAYS) - [N22000118]	293.74	12/2010	128.78
114	BHOJIPUR TANAKPUR VIA PILIBHIT (NORTH EASTERN RAILWAY) - [N22000132]	195.64	-	450.62
115	AUNRIHAR MANDUADIH (NORTH EASTERN RAILWAY) - [N22000133]	199.75	08/2018	287.33
116	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000164]	309.44	12/2015	529.27
117	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC (SOUTHERN RAILWAY) - [N22000188]	271.24	-	468.58
118	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA (NORTH EAST FRONTIER RAILWAY) - [N22000194]	895.00	03/2007	1,566.57
119	CHENGANNUR-CHINGAVANAM (SOUTHERN RAILWAY) - [N22000203]	191.72	-	447.03
120	LUMDING-HOJAI PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000211]	246.07	03/2019	490.29
121	MEERUT-MUZAFARNAGAR PATCH DL (NORTHERN RAILWAY) - [N22000267]	377.44	-	430.12
122	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER- CHANDIGARH (NORTHERN RAILWAY) - [N22000290]	338.54	-	384.61
123	JAKHAL-MANSA DOUBLING ON SPR SECTION (NORTHERN RAILWAY) - [N22000291]	162.96	-	160.25
124	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI (SOUTHERN RAILWAY) - [N22000303]	460.94	01/1999	0.01
125	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000439]	458.63	03/2015	367.71
126	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000440]	200.84	03/2014	394.51
127	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000446]	600.00	03/2010	673.80

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
128	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000450]	199.55	03/2009	238.61
129	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. (SOUTHERN RAILWAY) - [N22000453]	208.00	03/2012	206.20
130	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. (SOUTHERN RAILWAY) - [N22000454]	241.00	03/2014	293.37
131	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR- LUCKNOW (NORTH EASTERN RAILWAY) - [N22000455]	233.00	04/1999	349.37
132	MANDHANA - BRAHMAWART NEW LINE PROJECT. (NORTH EASTERN RAILWAY) - [N22000458]	609.04	04/1999	1,806.84
133	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM (EAST CENTRAL RAILWAYS) - [N22000474]	624.47	02/2016	3,376.08
	July,2019			
	<u>COAL</u>			
134	NORTH URIMARI OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000084]	179.87	03/2012	163.23
	<u>STEEL</u>			
135	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) (RASTRIYA ISPAT NIGAM LIMITED) - [N12000120]	465.85	07/2018	390.25
	<u>PETROLEUM</u>			
136	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000072]	3,957.00	12/2018	2,707.26
137	PARADIP-RAIPUR- RANCHI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000088]	1,793.00	12/2016	1,788.86
138	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) (INDIAN OIL CORPORATION LIMITED) - [N16000187]	191.96	05/2015	76.28
139	REPLACEMENT OF KV SECTION OF KSPL Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000287]	279.00	08/2018	200.05
	<u>POWER</u>			
140	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) (SATLUJ JAL VIDYUT NIGAM LIMITED) - [N18000235]	330.00	11/2017	331.46
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
141	BHOPAL-BIORA (4L) OF NH-12 IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000380]	704.26	05/2015	5.21
	<u>TELECOMMUNICATIONS</u>			

Month wise List of Completed Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
142	MADHYA PRADESH ACCESS (LOT1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000110]	215.30	05/2018	33.46

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2019			
	<u>RAILWAYS</u>			
1	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL (RAIL VIKAS NIGAM LTD.) - [220100149]	631.78	12/2012	762.72
2	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR (NORTHERN RAILWAY) - [220100258]	625.30	06/2007	848.84
3	TAMLUK DIGHA,LINE DOUBLING (SER) (SOUTH EASTERN RAILWAY) - [N22000097]	293.97	06/2005	0.00
4	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) (NORTH WESTERN RAILWAY) - [N22000112]	829.74	03/2015	823.85
5	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE (EASTERN RAILWAYS) - [N22000248]	268.52	-	0.00
6	MUNIRABAD (GINGERA) -RAICHUR NL (SOUTH WESTERN RAILWAY) - [N22000257]	179.65	-	940.47
7	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL (NORTHERN RAILWAY) - [N22000268]	396.04	-	225.18
8	CHANDIGARH-BADDI NL (NORTHERN RAILWAY) - [N22000296]	328.14	-	233.84
9	MM FROM BURAMARA-CHAKULIA (SOUTH EASTERN RAILWAY) - [N22000305]	466.48	-	0.83
10	MIRAJ-LONDA (SOUTH WESTERN RAILWAY) - [N22000327]	1,830.00	-	254.57
11	CHHINDWARA-MANDLA FORT GC (SOUTH EAST CENTRAL RAILWAY) - [N22000481]	556.54	03/2012	0.00
12	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM (SOUTH EAST CENTRAL RAILWAY) - [N22000482]	1,471.93	03/2022	0.00
	<u>WATER RESOURCES</u>			
13	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [300100001]	542.90	12/2007	0.00
	July,2019			
	<u>STEEL</u>			
14	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000085]	188.93	04/2015	138.83
15	REVAMPING OF SINTER MACHINES - 1 AND 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000091]	343.00	10/2016	254.65
16	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000097]	4,749.00	09/2017	110.95

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
17	2 MTPA PELLET PLANT AT NAGARNAR (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000115]	818.00	06/2020	31.60
	<u>RAILWAYS</u>			
18	BHADUTOLA-JHARGRAM VIA LALGARH (NL) (SOUTH EASTERN RAILWAY) - [N22000161]	289.64	-	0.13
19	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI (NORTHERN RAILWAY) - [N22000270]	654.00	-	0.00
20	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR (NORTHERN RAILWAY) - [N22000271]	1,239.00	-	0.00
21	HISSAR-SIRSA VIA AGROHA AND FATEHABAD (NORTHERN RAILWAY) - [N22000292]	400.00	-	0.00
22	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH (NORTHERN RAILWAY) - [N22000293]	876.00	-	0.00
23	MM FROM PANSKURA-GHATAL NL (SOUTH EASTERN RAILWAY) - [N22000309]	276.69	-	0.00
24	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI(SOUTH EASTERN RAILWAY) - [N22000397]	1,013.45	12/2021	0.01
25	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO(SOUTH EASTERN RAILWAY) - [N22000398]	524.43	12/2021	184.33

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1608
No of Projects Completed/Dropped/Frozen in Current Month	21
No of Projects added in Current Month	36
No of Projects in Current Month	1623

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	552 (34.01%)	23 (1.42%)	378(23.29%)	162 (9.98%)	508(31.30%)	1623
Latest Approved (Date)	451 (27.79%)	29 (1.79%)	484(29.82%)	146 (9.00%)	513(1.61%)	1623

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1347	16,33,642.55	18,69,484.47	7,22,669.43	38.70	2,35,841.92	14.40
Project with Revision in Cost	276	4,47,897.68	4,52,018.37	2,24,902.02	49.80	4,120.69	.90
Total	1,623	20,81,540.23	23,21,502.84	9,47,571.45	40.82	2,39,962.61	11.53
Original Cost of All Projects							
Original Cost	1,623	19,33,390.22	23,21,502.84	9,47,571.45	40.82	3,88,112.62	20.07

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	552	8,32,528.77	10,61,373.16	5,34,920.69	50.40	2,28,844.39	27.49
Latest Approved (RCE)	451	6,40,983.26	7,57,878.90	3,32,872.84	43.90	1,16,895.64	18.24

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	73	1,15,583.01	1,49,251.31	66,999.64	44.90	33,668.30	29.10
Total	73	1,15,583.01	1,49,251.31	66,999.64	44.89	33,668.30	29.13


Summary of projects in the Flash Report for the month of July, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1608
Number of Projects completed/dropped/frozen in Current Month	21
	0
Number of Projects Added in Current Month	36
Number of Projects in Current Month	1623

Brief Analysis

Project Status with respect to Original Schedule: Out of 1623 projects, 23 projects are ahead of schedule, 378 projects are on schedule 552 projects are delayed. 508 projects do not have fixed dates of commissioning. 162 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

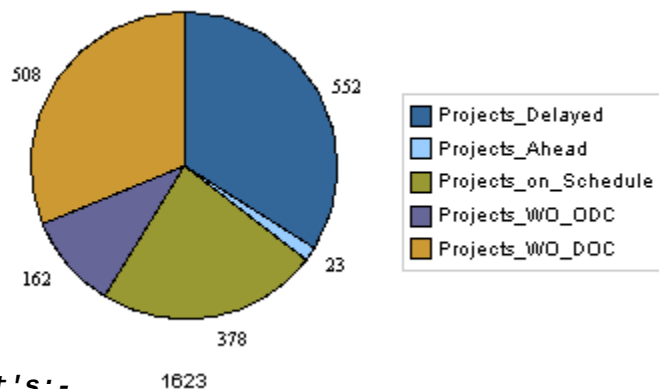

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1623 projects when sanctioned, was of the order of Rs. 1933390.22 crore but this was subsequently revised to Rs. 2321502.84 crore implying a cost overrun of 20.1%. The expenditure incurred on these projects till July, 2019 is Rs. 947571.45 crore, which is 40.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

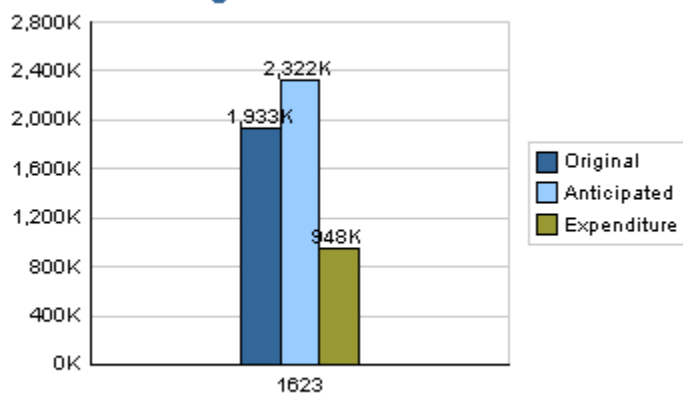


TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) RS. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	105	99,835.93	1,00,289.27	0.45	11	25,725.94	28,037.55	8.99
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
8	PETROLEUM	151	2,46,407.34	2,53,901.92	3.04	27	42,112.82	52,074.16	23.65
9	POWER	74	2,87,196.40	3,60,575.39	25.55	30	1,54,828.95	2,28,724.99	47.73
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
12	RAILWAYS	315	4,61,117.38	6,67,113.52	44.67	189	1,78,097.92	3,95,346.58	121.98
13	ROAD TRANSPORT AND HIGHWAYS	839	4,93,493.25	5,10,239.55	3.39	67	37,589.35	55,162.90	46.75
14	SHIPPING AND PORTS	8	10,757.29	11,199.74	4.11	3	760.89	1,545.44	103.11
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	83.58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,92,886.88	3.33	14	29,058.09	35,281.91	21.42
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
18	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0.00
Total		1623	19,33,390.22	23,21,502.84	20.07	355	5,37,474.24	9,43,308.81	75.51

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	76	1,20,064.65	1,69,040.57	40.79	10	19,702.74	69,195.19	251.20
2	ARUNACHAL PRADESH	38	19,572.19	38,023.50	94.27	5	9,284.82	27,736.13	198.73
3	ASSAM	47	25,166.52	29,070.62	15.51	15	5,905.43	10,082.62	70.73
4	BIHAR	93	87,682.20	1,32,726.30	51.37	34	40,725.01	85,844.74	110.79
5	GOA	12	5,779.51	5,789.94	0.18	1	280.16	290.59	3.72
6	GUJARAT	55	64,314.47	70,750.56	10.01	7	14,572.13	21,164.55	45.24
7	HARYANA	32	22,390.13	23,907.66	6.78	3	1,900.58	3,505.00	84.42
8	HIMACHAL PRADESH	12	16,702.17	26,812.70	60.53	2	6,886.58	16,997.11	146.82
9	JAMMU AND KASHMIR	13	24,646.76	50,095.76	103.26	1	2,500.00	27,949.00	1017.96
10	KARNATAKA	65	74,513.97	77,491.82	4.00	12	8,855.40	12,068.26	36.28
11	KERALA	22	39,078.60	41,891.46	7.20	6	13,310.89	16,319.29	22.60
12	MADHYA PRADESH	74	84,134.46	91,226.06	8.43	9	28,541.25	37,229.83	30.44
13	MAHARASHTRA	261	2,37,745.85	2,46,454.54	3.66	29	37,209.80	51,204.06	37.61
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	181.17
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	1	906.46	6,000.00	561.92
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	95.51
17	NAGALAND	26	14,842.43	15,515.91	4.54	1	2,326.52	3,000.00	28.95
18	ODISHA	97	1,06,511.40	1,08,955.39	2.29	18	27,663.32	33,686.84	21.77
19	PUNJAB	27	13,539.35	15,093.54	11.48	5	3,867.41	5,421.60	40.19
20	RAJASTHAN	62	47,167.18	54,596.11	15.75	13	17,425.66	24,854.59	42.63
21	SIKKIM	9	3,476.73	6,308.80	81.46	2	1,521.76	4,353.83	186.10
22	TAMIL NADU	69	1,19,531.37	1,37,822.56	15.30	23	37,211.30	57,551.00	54.66
23	TRIPURA	7	1,977.29	2,139.55	8.21	5	1,436.39	1,598.65	11.30
24	UTTAR PRADESH	107	1,39,916.34	1,44,181.28	3.05	18	37,732.02	43,157.71	14.38
25	WEST BENGAL	62	55,912.54	67,624.82	20.95	21	21,256.89	33,305.47	56.68
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	2	552.41	679.33	22.98
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	24	55,715.65	63,190.88	13.42	6	6,981.71	14,456.94	107.07
29	CHHATISGARH	35	73,823.69	85,478.21	15.79	8	34,846.39	46,931.47	34.68
30	JHARKHAND	45	60,234.46	64,107.45	6.43	7	21,033.35	24,910.12	18.43
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	9	10,197.17	19,115.09	87.45
32	TELANGANA	57	40,255.16	43,275.56	7.50	12	6,282.64	9,429.38	50.09
33	MULTI STATE	131	3,17,640.98	4,23,586.25	33.35	64	1,08,510.31	2,15,720.78	98.80
Total		1623	19,33,390.22	23,21,502.84	20.07	355	5,37,474.24	9,43,308.81	75.51

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	105	99,835.93	1,00,289.27	0.45	34	18,387.03	19,603.41	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34 - 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
7	STEEL	9	26,228.23	33,485.23	27.67	8	25,964.87	33,221.87	12 - 62
8	PETROLEUM	151	2,46,407.34	2,53,901.92	3.04	47	1,08,790.72	1,12,546.03	1 - 110
9	POWER	74	2,87,196.40	3,60,575.39	25.55	50	1,82,985.40	2,41,775.27	1 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	11	4,693.67	4,793.45	2 - 83
12	RAILWAYS	315	4,61,117.38	6,67,113.52	44.67	141	1,75,159.00	2,56,812.50	1 - 264
13	ROAD TRANSPORT AND HIGHWAYS	839	4,93,493.25	5,10,239.55	3.39	219	1,27,865.13	1,33,024.22	1 - 140
14	SHIPPING AND PORTS	8	10,757.29	11,199.74	4.11	1	600.00	257.90	29 - 29
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	11 - 58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,92,886.88	3.33	27	93,270.17	94,423.16	2 - 89
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
18	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	-
Total		1623	19,33,390.22	23,21,502.84	20.07	552	8,32,528.77	10,61,373.16	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	76	1,20,064.65	1,69,040.57	40.79	41	71,419.90	1,17,667.36	1 - 168
2	ARUNACHAL PRADESH	38	19,572.19	38,023.50	94.27	11	5,692.01	10,630.52	15 - 116
3	ASSAM	47	25,166.52	29,070.62	15.51	13	6,308.08	8,062.23	1 - 140
4	BIHAR	93	87,682.20	1,32,726.30	51.37	19	37,443.97	62,919.59	6 - 118
5	GOA	12	5,779.51	5,789.94	0.18	0	0.00	0.00	-
6	GUJARAT	55	64,314.47	70,750.56	10.01	15	30,118.07	36,362.47	2 - 120
7	HARYANA	32	22,390.13	23,907.66	6.78	11	7,992.20	9,579.20	1 - 118
8	HIMACHAL PRADESH	12	16,702.17	26,812.70	60.53	3	6,676.35	12,753.87	15 - 147
9	JAMMU AND KASHMIR	13	24,646.76	50,095.76	103.26	4	14,917.75	40,366.75	10 - 235
10	KARNATAKA	65	74,513.97	77,491.82	4.00	26	48,580.66	49,671.35	3 - 264
11	KERALA	22	39,078.60	41,891.46	7.20	9	17,162.14	18,789.69	8 - 89
12	MADHYA PRADESH	74	84,134.46	91,226.06	8.43	33	30,591.32	36,328.50	2 - 54
13	MAHARASHTRA	261	2,37,745.85	2,46,454.54	3.66	80	1,15,625.77	1,16,859.98	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	3	5,188.43	13,198.46	36 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	3	1,149.47	1,149.47	2 - 16
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	15,515.91	4.54	4	3,525.63	4,199.11	36 - 79
18	ODISHA	97	1,06,511.40	1,08,955.39	2.29	36	48,623.45	50,984.87	3 - 177
19	PUNJAB	27	13,539.35	15,093.54	11.48	7	3,169.78	3,570.93	1 - 28
20	RAJASTHAN	62	47,167.18	54,596.11	15.75	17	21,515.47	27,119.94	1 - 70
21	SIKKIM	9	3,476.73	6,308.80	81.46	3	1,673.35	4,505.42	51 - 82
22	TAMIL NADU	69	1,19,531.37	1,37,822.56	15.30	26	72,372.62	79,968.99	2 - 133
23	TRIPURA	7	1,977.29	2,139.55	8.21	2	908.56	989.00	6 - 21
24	UTTAR PRADESH	107	1,39,916.34	1,44,181.28	3.05	26	40,107.65	42,907.55	2 - 68
25	WEST BENGAL	62	55,912.54	67,624.82	20.95	27	28,477.16	34,485.77	9 - 171
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	24	55,715.65	63,190.88	13.42	7	3,956.64	4,429.21	8 - 83
29	CHHATISGARH	35	73,823.69	85,478.21	15.79	14	39,819.26	50,888.18	3 - 84
30	JHARKHAND	45	60,234.46	64,107.45	6.43	17	22,808.71	23,934.89	4 - 120
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	10	25,218.73	33,623.06	6 - 114
32	TELANGANA	57	40,255.16	43,275.56	7.50	19	19,314.02	20,180.20	2 - 156
33	MULTI STATE	131	3,17,640.98	4,23,586.25	33.35	59	92,177.36	1,31,937.32	1 - 252
Total		1623	19,33,390.22	23,21,502.84	20.07	552	8,32,528.77	10,61,373.16	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	4	77,000.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	105	1,01,009.23	1,00,289.27	-0.71	34	19,560.33	19,603.41	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34 - 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
7	STEEL	9	26,228.23	33,485.23	27.67	0	0.00	0.00	-
8	PETROLEUM	151	2,52,983.09	2,53,901.92	0.36	29	71,250.20	71,383.17	1 - 110
9	POWER	74	3,12,374.35	3,60,575.39	15.43	30	64,455.28	87,586.48	1 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	11	4,693.67	4,793.45	2 - 83
12	RAILWAYS	315	5,63,450.06	6,67,113.52	18.40	116	1,77,953.45	2,06,192.16	1 - 264
13	ROAD TRANSPORT AND HIGHWAYS	839	4,96,280.73	5,10,239.55	2.81	192	1,16,730.30	1,20,774.76	0 - 140
14	SHIPPING AND PORTS	8	10,428.79	11,199.74	7.39	1	258.00	257.90	29 - 29
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58 - 58
16	URBAN DEVELOPMENT	63	1,87,205.75	1,92,886.88	3.03	25	81,621.05	82,612.32	0 - 89
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
18	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	-
Total		1623	20,81,540.23	23,21,502.84	11.53	451	6,40,983.26	7,57,878.90	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns[^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	105	1,01,009.23	1,00,289.27	-0.71	10	19,818.83	20,957.14	5.74
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
8	PETROLEUM	151	2,52,983.09	2,53,901.92	0.36	13	16,950.80	20,051.58	18.29
9	POWER	74	3,12,374.35	3,60,575.39	15.43	25	1,25,916.75	1,74,634.84	38.69
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
12	RAILWAYS	315	5,63,450.06	6,67,113.52	18.40	162	1,37,113.85	2,47,117.96	80.23
13	ROAD TRANSPORT AND HIGHWAYS	839	4,96,280.73	5,10,239.55	2.81	84	42,936.89	58,003.76	35.09
14	SHIPPING AND PORTS	8	10,428.79	11,199.74	7.39	3	774.39	1,545.44	99.57
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	63	1,87,205.75	1,92,886.88	3.03	10	28,341.60	34,022.73	20.05
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
18	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0.00
Total		1623	20,81,540.23	23,21,502.84	11.53	318	4,17,142.59	6,69,569.63	60.51

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	133- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	105	1,01,009.23	1,00,289.27	-0.71	7	1,996.80	2,867.24	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34- 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
7	STEEL	9	26,228.23	33,485.23	27.67	0	0.00	0.00	0- 0
8	PETROLEUM	151	2,52,983.09	2,53,901.92	0.36	3	3,848.56	4,109.31	6- 110
9	POWER	74	3,12,374.35	3,60,575.39	15.43	11	38,843.29	61,974.49	12- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	1	414.11	513.89	83- 83
12	RAILWAYS	315	5,63,450.06	6,67,113.52	18.40	57	54,015.96	84,294.75	6- 252
13	ROAD TRANSPORT AND HIGHWAYS	839	4,96,280.73	5,10,239.55	2.81	30	18,920.54	23,453.55	1- 140
14	SHIPPING AND PORTS	8	10,428.79	11,199.74	7.39	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58- 58
16	URBAN DEVELOPMENT	63	1,87,205.75	1,92,886.88	3.03	5	8,075.79	9,067.06	9- 40
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
18	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0- 0
Total		1623	20,81,540.23	23,21,502.84	11.53	120	1,53,943.42	2,74,322.93	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	105	99,835.93	1,00,289.27	0.45	8	7,903.91	9,947.65	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34- 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	62- 62
8	PETROLEUM	151	2,46,407.34	2,53,901.92	3.04	15	27,653.77	32,936.44	1- 110
9	POWER	74	2,87,196.40	3,60,575.39	25.55	25	1,32,711.57	1,91,501.44	12- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	1	414.11	513.89	83- 83
12	RAILWAYS	315	4,61,117.38	6,67,113.52	44.67	80	78,571.46	1,69,181.44	3- 240
13	ROAD TRANSPORT AND HIGHWAYS	839	4,93,493.25	5,10,239.55	3.39	32	18,583.06	24,035.87	1- 140
14	SHIPPING AND PORTS	8	10,757.29	11,199.74	4.11	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	11- 58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,92,886.88	3.33	7	8,739.54	9,892.53	5- 70
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
18	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0- 0
Total		1623	19,33,390.22	23,21,502.84	20.07	178	3,41,941.59	5,83,091.00	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	76	1,20,064.65	1,69,040.57	40.79	4	12,472.36	59,091.13	2 - 168
2	ARUNACHAL PRADESH	38	19,572.19	38,023.50	94.27	2	2,635.83	7,574.34	36 - 116
3	ASSAM	47	25,166.52	29,070.62	15.51	5	1,309.95	3,221.05	12 - 140
4	BIHAR	93	87,682.20	1,32,726.30	51.37	10	30,865.91	56,349.24	12 - 118
5	GOA	12	5,779.51	5,789.94	0.18	0	0.00	0.00	-
6	GUJARAT	55	64,314.47	70,750.56	10.01	5	13,479.15	19,879.88	12 - 120
7	HARYANA	32	22,390.13	23,907.66	6.78	2	1,395.00	2,982.00	100 - 111
8	HIMACHAL PRADESH	12	16,702.17	26,812.70	60.53	1	3,919.59	9,997.11	147 - 147
9	JAMMU AND KASHMIR	13	24,646.76	50,095.76	103.26	1	2,500.00	27,949.00	235 - 235
10	KARNATAKA	65	74,513.97	77,491.82	4.00	5	3,185.52	4,292.22	3 - 36
11	KERALA	22	39,078.60	41,891.46	7.20	4	11,137.83	12,789.42	15 - 32
12	MADHYA PRADESH	74	84,134.46	91,226.06	8.43	6	17,231.95	23,065.44	6 - 36
13	MAHARASHTRA	261	2,37,745.85	2,46,454.54	3.66	17	20,618.88	27,006.94	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	108 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	0	0.00	0.00	-
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	15,515.91	4.54	1	2,326.52	3,000.00	79 - 79
18	ODISHA	97	1,06,511.40	1,08,955.39	2.29	14	24,702.14	30,563.13	3 - 177
19	PUNJAB	27	13,539.35	15,093.54	11.48	3	1,589.83	1,990.98	1 - 28
20	RAJASTHAN	62	47,167.18	54,596.11	15.75	7	14,217.88	19,822.35	5 - 48
21	SIKKIM	9	3,476.73	6,308.80	81.46	2	1,521.76	4,353.83	51 - 82
22	TAMIL NADU	69	1,19,531.37	1,37,822.56	15.30	8	17,651.33	26,599.21	12 - 133
23	TRIPURA	7	1,977.29	2,139.55	8.21	2	908.56	989.00	6 - 21
24	UTTAR PRADESH	107	1,39,916.34	1,44,181.28	3.05	7	13,162.81	16,500.52	5 - 68
25	WEST BENGAL	62	55,912.54	67,624.82	20.95	11	15,634.97	21,658.62	12 - 141
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	24	55,715.65	63,190.88	13.42	2	1,633.32	2,105.89	17 - 83
29	CHHATISGARH	35	73,823.69	85,478.21	15.79	6	32,944.43	44,443.91	9 - 62
30	JHARKHAND	45	60,234.46	64,107.45	6.43	3	14,773.55	15,899.73	18 - 35
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	5	7,847.16	16,277.99	19 - 114
32	TELANGANA	57	40,255.16	43,275.56	7.50	6	3,177.10	4,121.53	39 - 144
33	MULTI STATE	131	3,17,640.98	4,23,586.25	33.35	32	60,735.91	1,00,575.57	8 - 240
Total		1623	19,33,390.22	23,21,502.84	20.07	178	3,41,941.59	5,83,091.00	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	157	22
2	ROAD TRANSPORT AND HIGHWAYS	143	2
3	PETROLEUM	56	5
4	POWER	42	2
5	URBAN DEVELOPMENT	16	1
6	COAL	14	0
7	STEEL	6	3
8	ATOMIC ENERGY	4	0
9	SHIPPING AND PORTS	3	0
10	CIVIL AVIATION	2	0
11	TELECOMMUNICATIONS	2	0
12	MINES	1	0
13	HEAVY INDUSTRY	1	0
14	WATER RESOURCES	1	0
	Total	448	35

TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	448
No of Projects Completed/Dropped/Frozen in Current Month	5
No of Projects added in Current Month	4
No of Projects in Current Month	448

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	186 (41.52%)	6 (1.34%)	94 (20.98%)	52 (11.61%)	110(4.55%)	448
Latest Approved (Date)	136 (30.36%)	8 (1.79%)	145(32.37%)	48 (10.71%)	11124.78%)	448

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	377	12,34,454.26	14,55,484.52	5,60,116.86	38.50	2,21,030.26	17.90
Project with Revision in Cost	71	3,69,350.81	3,71,751.31	1,91,084.22	51.40	2,400.50	.60
Total	448	16,03,805.07	18,27,235.83	7,51,201.08	41.11	2,23,430.76	13.93
Original Cost of All Projects							
Original Cost	448	14,56,628.08	18,27,235.83	7,51,201.08	41.11	3,70,607.75	25.44

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	186	6,78,850.87	9,02,306.99	4,54,632.36	50.40	2,23,456.12	32.92
Latest Approved (RCE)	136	5,12,109.54	6,23,087.67	2,65,807.85	42.70	1,10,978.13	21.67

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	35	98,949.84	1,31,596.52	58,376.35	44.40	32,646.68	33.00
Total	35	98,949.84	1,31,596.52	58,376.35	44.36	32,646.68	32.99

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	14	61,801.69	62,975.79	1.90	2	23,144.11	24,318.21	5.07
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	56	2,06,905.35	2,13,603.99	3.24	15	36,702.27	45,424.28	23.76
7	POWER	42	2,74,465.11	3,47,411.35	26.58	24	1,52,955.09	2,26,418.38	48.03
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	RAILWAYS	157	3,93,603.51	5,87,511.82	49.26	98	1,46,551.69	3,45,992.01	136.09
10	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.25	2,22,428.40	6.16	17	20,128.00	33,039.15	64.15
11	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	16	1,72,867.22	1,78,723.70	3.39	5	26,033.88	31,890.36	22.50
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		448	14,56,628.08	18,27,235.83	25.44	167	4,71,796.08	8,50,934.26	80.36

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun[^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	21	98,791.39	1,47,893.34	49.70	7	18,977.19	68,437.14	260.63
2	ARUNACHAL PRADESH	4	11,753.92	29,887.37	154.28	2	8,782.23	26,915.68	206.48
3	ASSAM	7	10,628.98	13,232.87	24.50	3	2,127.51	4,868.01	128.81
4	BIHAR	26	57,828.84	99,394.54	71.88	16	33,657.10	75,222.80	123.50
5	GUJARAT	18	46,707.74	52,415.93	12.22	3	13,264.36	18,972.55	43.03
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	14,146.19	24,256.72	71.47	2	6,886.58	16,997.11	146.82
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	1017.96
9	KARNATAKA	19	55,640.48	58,048.19	4.33	5	5,713.62	8,317.34	45.57
10	KERALA	10	32,670.86	35,455.35	8.52	4	12,448.08	15,256.61	22.56
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	8	28,044.20	36,348.78	29.61
12	MAHARASHTRA	51	1,54,156.84	1,65,652.44	7.46	17	33,504.13	45,771.60	36.61
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	181.17
14	MEGHALAYA	1	906.46	6,000.00	561.92	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	109.80
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	28.95
17	ODISHA	33	80,852.03	82,843.71	2.46	10	25,048.54	30,539.79	21.92
18	PUNJAB	3	3,627.54	4,765.00	31.36	1	1,388.34	2,525.80	81.93
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	3	14,015.71	20,158.75	43.83
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	26	99,661.58	1,15,832.79	16.23	11	33,622.33	50,490.54	50.17
22	UTTAR PRADESH	43	1,11,788.14	1,15,458.91	3.28	8	34,043.60	38,486.32	13.05
23	WEST BENGAL	23	40,606.18	51,315.85	26.37	10	17,240.88	27,981.59	62.30
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
25	DELHI	7	50,481.91	57,816.75	14.53	3	6,254.39	13,589.23	117.28
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	7	34,693.96	46,471.98	33.95
27	JHARKHAND	11	47,087.51	50,541.95	7.34	3	19,637.61	23,092.05	17.59
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	8,654.06	17,090.60	97.49
29	TELANGANA	6	19,991.02	22,068.26	10.39	2	2,378.60	4,455.84	87.33
30	MULTI STATE	59	2,87,449.36	3,88,159.91	35.04	31	96,384.96	1,98,077.01	105.51
Total		448	14,56,628.08	18,27,235.83	25.44	167	4,71,796.08	8,50,934.26	80.36

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	14	61,801.69	62,975.79	1.90	2	6,962.16	8,135.46	24 - 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	25,381.34	32,638.34	28.59	6	25,381.34	32,638.34	12 - 62
6	PETROLEUM	56	2,06,905.35	2,13,603.99	3.24	21	97,953.47	1,01,372.62	1 - 110
7	POWER	42	2,74,465.11	3,47,411.35	26.58	28	1,74,083.23	2,32,469.05	3 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
9	RAILWAYS	157	3,93,603.51	5,87,511.82	49.26	79	1,42,762.33	2,22,338.34	3 - 264
10	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.25	2,22,428.40	6.16	36	51,821.16	54,631.38	1 - 100
11	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	-
12	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
13	URBAN DEVELOPMENT	16	1,72,867.22	1,78,723.70	3.39	7	86,815.14	87,693.93	2 - 64
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		448	14,56,628.08	18,27,235.83	25.44	186	6,78,850.87	9,02,306.99	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,47,893.34	49.70	10	59,598.89	1,05,859.16	1 - 168
2	ARUNACHAL PRADESH	4	11,753.92	29,887.37	154.28	2	3,750.00	8,672.44	60 - 116
3	ASSAM	7	10,628.98	13,232.87	24.50	2	2,850.35	3,910.86	12 - 81
4	BIHAR	26	57,828.84	99,394.54	71.88	9	32,035.52	57,007.05	12 - 118
5	GUJARAT	18	46,707.74	52,415.93	12.22	5	26,057.77	31,659.26	2 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	2	4,637.00	5,817.00	5 - 100
7	HIMACHAL PRADESH	6	14,146.19	24,256.72	71.47	2	6,405.52	12,483.04	15 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	4	14,917.75	40,366.75	10 - 235
9	KARNATAKA	19	55,640.48	58,048.19	4.33	10	39,631.87	40,402.12	3 - 264
10	KERALA	10	32,670.86	35,455.35	8.52	5	15,319.19	16,854.06	8 - 33
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	7	20,977.06	26,426.55	6 - 26
12	MAHARASHTRA	51	1,54,156.84	1,65,652.44	7.46	23	86,794.35	91,538.51	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	33	80,852.03	82,843.71	2.46	16	40,474.91	42,466.58	3 - 177
18	PUNJAB	3	3,627.54	4,765.00	31.36	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	2	13,749.38	18,508.38	6 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	26	99,661.58	1,15,832.79	16.23	12	64,834.44	73,061.89	6 - 133
22	UTTAR PRADESH	43	1,11,788.14	1,15,458.91	3.28	12	34,676.06	37,350.72	2 - 40
23	WEST BENGAL	23	40,606.18	51,315.85	26.37	12	23,022.93	28,495.83	13 - 171
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
25	DELHI	7	50,481.91	57,816.75	14.53	2	2,613.73	2,986.52	17 - 31
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	7	37,249.02	48,139.42	3 - 62
27	JHARKHAND	11	47,087.51	50,541.95	7.34	4	18,278.97	19,076.44	9 - 32
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	23,343.06	31,505.53	15 - 114
29	TELANGANA	6	19,991.02	22,068.26	10.39	4	14,450.02	14,727.42	7 - 156
30	MULTI STATE	59	2,87,449.36	3,88,159.91	35.04	25	76,583.36	1,14,519.01	3 - 252
Total		448	14,56,628.08	18,27,235.83	25.44	186	6,78,850.87	9,02,306.99	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	4	77,000.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	14	62,974.99	62,975.79	0.00	2	8,135.46	8,135.46	24 - 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	25,381.34	32,638.34	28.59	0	0.00	0.00	-
6	PETROLEUM	56	2,12,784.23	2,13,603.99	0.39	9	62,618.93	62,753.40	1 - 110
7	POWER	42	2,99,643.06	3,47,411.35	15.94	13	57,950.43	80,829.55	3 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
9	RAILWAYS	157	4,97,230.57	5,87,511.82	18.16	63	1,53,236.38	1,77,436.08	3 - 264
10	ROAD TRANSPORT AND HIGHWAYS	143	2,10,654.96	2,22,428.40	5.59	36	51,821.16	54,631.38	1 - 100
11	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	-
12	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
13	URBAN DEVELOPMENT	16	1,73,169.31	1,78,723.70	3.21	6	75,395.14	76,273.93	13 - 64
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		448	16,03,805.07	18,27,235.83	13.93	136	5,12,109.54	6,23,087.67	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule RS.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	14	62,974.99	62,975.79	0.00	1	17,237.00	17,237.80	0.00
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	56	2,12,784.23	2,13,603.99	0.39	7	13,807.27	16,382.59	18.65
7	POWER	42	2,99,643.06	3,47,411.35	15.94	19	1,24,042.89	1,72,328.23	38.93
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	RAILWAYS	157	4,97,230.57	5,87,511.82	18.16	82	1,08,669.78	2,04,444.47	88.13
10	ROAD TRANSPORT AND HIGHWAYS	143	2,10,654.96	2,22,428.40	5.59	16	18,739.66	30,513.35	62.83
11	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	16	1,73,169.31	1,78,723.70	3.21	5	26,335.97	31,890.36	21.09
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		448	16,03,805.07	18,27,235.83	13.93	134	3,51,334.61	5,82,989.67	65.94

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	133- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	14	62,974.99	62,975.79	0.00	0	0.00	0.00	0- 0
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	0	0.00	0.00	0- 0
6	PETROLEUM	56	2,12,784.23	2,13,603.99	0.39	1	2,915.00	3,049.47	110- 110
7	POWER	42	2,99,643.06	3,47,411.35	15.94	7	37,653.50	60,532.62	12- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	RAILWAYS	157	4,97,230.57	5,87,511.82	18.16	30	42,250.72	68,217.50	9- 252
10	ROAD TRANSPORT AND HIGHWAYS	143	2,10,654.96	2,22,428.40	5.59	11	11,890.31	14,700.53	2- 100
11	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
13	URBAN DEVELOPMENT	16	1,73,169.31	1,78,723.70	3.21	2	6,401.00	7,279.79	17- 29
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		448	16,03,805.07	18,27,235.83	13.93	54	1,28,087.57	2,40,832.78	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	14	61,801.69	62,975.79	1.90	1	5,907.11	7,080.41	48- 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	62- 62
6	PETROLEUM	56	2,06,905.35	2,13,603.99	3.24	9	25,526.31	30,071.43	1- 110
7	POWER	42	2,74,465.11	3,47,411.35	26.58	20	1,31,034.29	1,89,420.11	12- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	RAILWAYS	157	3,93,603.51	5,87,511.82	49.26	45	64,927.28	1,48,484.94	3- 235
10	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.25	2,22,428.40	6.16	11	11,890.31	14,700.53	2- 100
11	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
13	URBAN DEVELOPMENT	16	1,72,867.22	1,78,723.70	3.39	2	6,401.00	7,279.79	17- 29
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		448	14,56,628.08	18,27,235.83	25.44	94	3,11,967.34	5,40,889.08	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,47,893.34	49.70	3	12,237.86	58,856.13	2 - 168
2	ARUNACHAL PRADESH	4	11,753.92	29,887.37	154.28	1	2,496.90	7,419.34	116 - 116
3	ASSAM	7	10,628.98	13,232.87	24.50	1	385.20	1,532.00	12 - 12
4	BIHAR	26	57,828.84	99,394.54	71.88	7	29,343.85	54,315.38	12 - 118
5	GUJARAT	18	46,707.74	52,415.93	12.22	2	12,288.74	17,890.23	12 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	100 - 100
7	HIMACHAL PRADESH	6	14,146.19	24,256.72	71.47	1	3,919.59	9,997.11	147 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	235 - 235
9	KARNATAKA	19	55,640.48	58,048.19	4.33	2	1,824.74	2,611.00	3 - 4
10	KERALA	10	32,670.86	35,455.35	8.52	3	10,882.08	12,440.99	15 - 32
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	5	16,734.90	22,184.39	6 - 26
12	MAHARASHTRA	51	1,54,156.84	1,65,652.44	7.46	10	18,663.53	24,179.56	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	33	80,852.03	82,843.71	2.46	9	22,712.87	28,204.11	3 - 177
18	PUNJAB	3	3,627.54	4,765.00	31.36	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	1	12,320.00	17,079.00	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	26	99,661.58	1,15,832.79	16.23	6	17,160.09	25,387.54	12 - 133
22	UTTAR PRADESH	43	1,11,788.14	1,15,458.91	3.28	3	11,862.61	14,686.28	5 - 40
23	WEST BENGAL	23	40,606.18	51,315.85	26.37	6	14,389.73	19,877.67	13 - 141
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
25	DELHI	7	50,481.91	57,816.75	14.53	1	1,219.21	1,592.00	17 - 17
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	5	32,792.00	43,984.42	9 - 62
27	JHARKHAND	11	47,087.51	50,541.95	7.34	1	14,366.58	15,164.05	27 - 27
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	3	7,127.06	15,289.53	76 - 114
29	TELANGANA	6	19,991.02	22,068.26	10.39	1	1,266.60	1,544.00	39 - 39
30	MULTI STATE	59	2,87,449.36	3,88,159.91	35.04	17	53,851.56	91,787.21	8 - 178
Total		448	14,56,628.08	18,27,235.83	25.44	94	3,11,967.34	5,40,889.08	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

<u>List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above</u> (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	NORTH URIMARI OCP (3.0 MTY)	12/2007	179.87	03/2012	179.87	07/2019	163.23
	<u>PETROLEUM</u>						
2	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	191.96	05/2015	191.96	07/2019	76.28
3	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	03/2015	3,957.00	12/2018	3,397.00	06/2019	2,707.26
4	REPLACEMENT OF KV SECTION OF KSPL Central Sector Projects	10/2014	279.00	08/2018	279.00	07/2019	200.05
5	PARADIP-RAIPUR- RANCHI PIPELINE	08/2009	1,793.00	12/2016	1,793.00	07/2019	1,788.86
	<u>POWER</u>						
6	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	330.00	11/2017	332.00	04/2019	331.46
	<u>RAILWAYS</u>						
7	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	04/2013	654.00	N.A.	700.00	03/2025	0.00
8	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR	04/2013	1,239.00	N.A.	1,239.00	03/2025	0.00
9	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	04/2013	400.00	N.A.	400.00	03/2025	0.00
10	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	04/2011	289.64	N.A.	760.00	N.A.	0.13
11	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	01/1991	1,013.45	12/2021	1,428.00	12/2021	0.01
12	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	04/1995	524.43	12/2021	939.00	12/2024	184.33
13	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	04/2013	876.00	N.A.	876.00	03/2025	0.00
14	MM FROM PANSKURA-GHATAL NL	04/2011	276.69	N.A.	426.00	03/2030	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
15	BHOPAL-BIORA (4L) OF NH-12 IN MP BOT (TOLL)	11/2011	704.26	05/2015	704.26	07/2019	5.21
	<u>STEEL</u>						

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
16	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	188.93	04/2015	188.93	N.A.	138.83
17	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	818.00	06/2020	818.00	06/2020	31.60
18	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	10/2016	488.40	03/2021	254.65
19	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	07/2015	465.85	07/2018	465.85	07/2019	390.25
20	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	4,749.00	09/2017	4,749.00	N.A.	110.95
	<u>TELECOMMUNICATIONS</u>						
21	MADHYA PRADESH ACCESS (LOT1) Central Sector Projects	08/2017	215.30	05/2018	219.60	07/2019	33.46

TABLE-26

<u>List of projects added Rs.150 Crore and above</u>					(July 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>CIVIL AVIATION</u>					
1	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2,467.00	2/2022	2,467.00	8/2022
2	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	951.28	10/2021	951.28	10/2021
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	233.38	4/2020	233.38	12/2020
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	1,383.00	9/2021	1,383.00	9/2021
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	358.89	4/2021	358.89	4/2021
6	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	264.99	11/2021	264.99	11/2021
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	3/2021	860.00	3/2021
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	353.27	9/2020	353.27	9/2020
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	338.93	6/2019	339.00	12/2019
10	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	539.20	10/2022	539.20	10/2022
11	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	219.91	3/2020	219.91	12/2020
12	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT	7/2018	323.19	9/2021	323.19	9/2021
	<u>COAL</u>					
13	SAONER I UG TO OC PHASE I	11/2016	162.10	3/2022	162.10	3/2022
14	UKNI DEEP OC	11/2018	318.14	3/2021	318.14	3/2021
15	GAURI DEEP OC	10/2016	164.96	3/2019	164.96	3/2019
16	BELLORA-NAIGAON DEEP OC	11/2018	252.71	3/2021	252.71	3/2021
17	VISHNUPURI UG TO OC MINE	7/2018	195.57	3/2025	195.57	3/2025
	<u>INFORMATION AND BROADCASTING</u>					
18	NATIONAL FILM HERITAGE MISSION	11/2014	597.41	/	597.41	-
19	FILM AND TELEVISION INSTITUTE ARUNACHAL	11/2016	204.32	2/2019	204.32	11/2019

<u>List of projects added Rs.150 Crore and above</u>					(July 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PRADESH</u>					
20	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	167.70	3/2020	167.70	3/2020
	<u>PETROLEUM</u>					
21	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	2,166.38	6/2022	2,166.38	6/2022
22	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	763.92	12/2020	763.92	12/2020
23	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK)	10/2018	156.67	3/2021	156.67	3/2021
24	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	371.00	9/2022	371.00	9/2022
25	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	854.00	12/2022	854.00	12/2022
	<u>RAILWAYS</u>					
26	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	393.98	3/2020	393.98	3/2020
27	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	380.60	4/2010	1,300.00	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
28	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	235.31	11/2020	235.31	11/2020
29	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	167.62	12/2020	167.62	12/2020
30	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	172.63	12/2020	172.63	12/2020
31	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	171.90	8/2020	171.90	8/2020
32	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	336.25	9/2019	336.25	9/2019
33	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	217.35	11/2020	217.35	11/2020
34	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	237.51	12/2022	237.51	12/2022
35	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO	8/2010	186.96	9/2014	305.61	12/2019

<u>List of projects added Rs.150 Crore and above</u>					(July 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	SUPPORT KALADAN MULTI MOD					
36	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	251.55	2/2015	251.55	2/2017

TABLE-27

Milestones (Cumulative due & achieved) Rs.150 Crore and above

Total	5377
Achieved up to month	2734

TABLE-28

<u>List of projects reporting additional delayed Rs. 150 Crore and above</u>							(July 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	KISTARAM OCP SCCL	242.29	164.04	03/2015	07/2019	03/2021	20
2	JALAGAM VENGALA RAO OCP-II SCCL	447.06	473.22	03/2015	09/2017	03/2021	42
	<u>FERTILISERS</u>						
3	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY RCF	197.79	209.44	11/2016	08/2019	09/2019	1
	<u>STEEL</u>						
4	COKE OVEN BATTERY-5 RINL	2,858.00	2,500.00	12/2017	09/2019	10/2019	1
5	CENTRAL DISPATCH YARD RINL	320.66	320.66	08/2018	07/2019	10/2019	3
6	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT SAIL	1,154.18	1,154.18	12/2017	06/2019	11/2019	5
7	INSTALLATION OF NEW HOT STRIP MILL AT RSP SAIL	3,127.30	3,127.30	04/2018	05/2019	11/2019	6
	<u>PETROLEUM</u>						
8	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY IOCL	822.66	822.66	11/2018	07/2019	08/2019	1
9	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE MANGALORE REFIN	135.00	170.70	03/2019	08/2019	09/2019	1
10	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT GAIL	286.42	286.42	08/2020	08/2020	09/2020	1
11	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV ONGC	3,660.71	3,740.05	04/2021	04/2021	05/2021	1
12	FIELD DEVELOPMENT OF NELP BLOCK KG- ONN-2003, NAGAYALANKA-KG ONGC	420.76	407.45	09/2018	07/2019	09/2019	2
13	HEERA REDEVELOPMENT - PHASE III ONGC	2,494.68	2,494.68	12/2021	12/2021	03/2022	3
14	BS-VI PROJECT AT PANIPAT REFINERY IOCL	3,529.00	3,529.00	07/2019	07/2019	12/2019	5
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS ONGC	2,059.63	2,059.63	03/2015	05/2019	12/2019	7

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	KOCHI SALEM LPG PIPELINE PROJECT BPCL	1,112.00	1,507.24	06/2019	06/2020	02/2022	20
	<u>POWER</u>						
17	EASTERN REGION STRENGTHENING SCHEME- XII PGCIL	522.29	546.36	11/2016	12/2019	03/2020	3
18	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR PGCIL	808.63	808.63	01/2018	12/2019	03/2020	3
19	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	07/2019	12/2021	29
20	BUXAR THERMAL POWER PLANT (1320 MW) SJVN	10,439.09	10,439.09	01/2024	07/2019	01/2024	54
	<u>RAILWAYS</u>						
21	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND SER	148.77	377.00	12/2016	09/2019	11/2019	2
22	RAIPUR - TITLAGARH - DOUBLING RVNL	1,402.02	1,100.00	03/2020	03/2020	06/2020	3
23	INDARA - DOHRIGHAT GAUGE CONVERSION. NER	213.00	213.35	04/2016	02/2020	06/2020	4
24	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING SER	258.20	358.68	12/2018	01/2020	06/2020	5
25	KATNI - SINGRAULI DOUBLING PROJECT WCR	1,763.93	1,763.93	03/2020	10/2021	03/2022	5
26	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	27,949.00	11/2002	12/2021	06/2022	6
27	KATNI GRADE SEPARATOR/BYE PASS WCR	582.13	1,247.64	03/2022	03/2022	09/2022	6
28	GEVRA ROAD PENDRA ROAD IRCON	2,288.00	4,970.11	03/2022	03/2022	12/2022	9
29	HAJIPUR - BACHAWARA ECR	678.54	678.54	03/2019	03/2020	02/2021	11
30	MANOHARABAD-KOTHPALL NEW LINE(SCR) SCR	1,160.48	1,160.48	03/2010	03/2022	03/2023	12
31	KADAPA-BANGALORE (NL), KADAPA- PENDLIMARRI PH-I SCR	2,132.77	2,132.77	03/2014	03/2023	03/2024	12
32	SAMBALPUR-TALCHER DOUBLING ECOR	1,111.99	1,539.28	02/2019	03/2021	03/2022	12
33	JAGDALPUR-KORAPUT DOUBLING ECOR	1,547.38	1,547.38	03/2022	03/2022	03/2023	12
34	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. ECOR	1,172.92	1,172.92	12/2018	03/2021	03/2022	12

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
35	SAMBALPUR - TITLAGARH - DOUBLING RVNL	948.04	1,500.00	03/2020	03/2020	03/2021	12
36	KATNI-BINA 3RD LINE (263 KM) WCR	2,478.23	2,478.23	03/2022	03/2022	03/2023	12
37	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE ECR	1,491.47	1,491.47	03/2020	10/2021	12/2022	14
38	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING SR	760.00	1,182.31	03/2020	03/2020	06/2021	15
39	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC ECR	548.00	785.87	03/2020	03/2020	03/2022	24
40	NADIKUDE-SRI KALAHASTI SCR	2,288.70	2,288.70	03/2021	03/2022	03/2024	24
41	BHADRAK - NERGUNDI 3RD LINE ECR	843.04	843.04	10/2020	03/2021	03/2023	24
42	KAZIPET-BALHRSHA SCR	2,063.03	2,063.03	03/2021	03/2021	03/2023	24
43	AUNRIHAR - JAUNPUR PATCH DOUBLING . NER	600.00	600.00	01/2022	01/2020	01/2022	24
44	KHURDA ROAD-BOLANGIR(NL)ECOR	2,923.13	3,798.80	03/2009	06/2021	12/2023	30
45	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) NCR	2,912.96	3,845.60	03/2022	03/2022	12/2024	33
46	KIRANDUL - JAGDALPUR DOUBLING ECR	1,160.00	1,160.83	03/2020	03/2020	03/2023	36
47	KORAPUT - SINGAPUR ROAD DOUBLING ECR	2,361.74	2,361.74	03/2022	03/2022	03/2025	36
48	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL IRCON	5,200.00	1,700.43	03/2020	03/2020	06/2023	39
49	BARDHAMAN-KATWA (GC) ER	1,106.62	1,091.59	12/2010	03/2020	03/2025	60
50	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL ER	595.51	769.40	03/2017	05/2010	03/2025	178
	ROAD TRANSPORT AND HIGHWAYS						
51	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 NHAI	199.81	385.13	04/2009	07/2019	08/2019	1
52	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 NHAI	1,387.11	1,387.11	11/2017	07/2019	08/2019	1
53	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) NHAI	726.67	598.13	04/2018	02/2020	03/2020	1


<u>List of projects reporting additional delayed Rs. 150 Crore and above</u>							(July 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
54	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T NHAI	804.97	804.97	06/2018	12/2019	01/2020	1
55	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM NHIDCL	284.09	284.09	04/2017	02/2021	03/2021	1
56	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 PWD	178.23	178.23	09/2018	07/2019	08/2019	1
57	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 NHAI	605.84	722.46	07/2018	12/2019	02/2020	2
58	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 PWD EPC	255.75	348.43	09/2017	09/2019	12/2019	3
59	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 NHAI	248.97	248.97	05/2019	08/2019	11/2019	3
60	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN NHAI	649.50	649.50	03/2019	12/2020	04/2021	4
61	FOUR LANING OF HOSPET - CHITRADURGA NHAI PPP (BOT)	1,388.00	1,388.00	08/2018	11/2019	03/2020	4
62	HARIDWAR DEHRADUN APPROVED LENGTH 69 NHAI	478.51	478.00	10/2013	07/2019	02/2020	7
63	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD MORTH	319.28	319.28	08/2017	08/2019	03/2020	7
64	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A PWD	373.82	373.82	09/2019	09/2019	05/2020	8
65	NAGPUR RING ROAD PACKAGE-1 NHAI	546.00	546.00	07/2019	07/2019	12/2020	17
66	NAGPUR RING ROAD PACKAGE-2 NHAI	591.66	591.66	07/2019	07/2019	12/2020	17
67	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI NHAI	400.25	400.25	03/2019	09/2019	02/2021	17
	<u>URBAN DEVELOPMENT</u>						
68	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB CPWD	430.00	430.00	05/2020	12/2020	01/2021	1
69	PUNE METRO RAIL PROJECT (PHASE 1) MMRC	11,420.00	11,420.00	11/2021	12/2021	01/2022	1
70	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB CPWD	294.00	294.00	04/2019	12/2019	02/2020	2

<u>List of projects reporting additional delayed Rs. 150 Crore and above</u>							(July 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
71	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA CPWD	156.57	156.57	08/2016	07/2019	10/2019	3
72	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR CPWD	790.79	800.00	06/2021	06/2021	03/2022	9
73	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD CPWD	209.84	209.84	03/2020	03/2020	05/2021	14


TABLE-29

<u>Sector wise analysis of projects Rs. 150 Crore and above</u>					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	770,00.00	80,348.00	45,577.74
CIVIL AVIATION	13	8,607.51	86,07.51	8,734.44	1,357.47
COAL	105	99,835.93	1,010,09.23	1,00,289.27	35,189.01
FERTILISERS	5	1,299.07	12,99.07	1,310.72	561.89
INFORMATION AND BROADCASTING	3	969.43	9,69.43	969.43	29.80
MINES	5	7,078.62	70,78.62	7,078.62	587.94
STEEL	9	26,228.23	262,28.23	33,485.23	22,898.68
PETROLEUM	151	2,46,407.34	2,529,83.09	2,53,901.92	88,700.73
POWER	74	2,87,196.40	3,123,74.35	3,60,575.39	2,13,724.90
HEAVY INDUSTRY	1	1,554.00	15,54.00	1,554.00	335.03
HEALTH AND FAMILY WELFARE	20	8,129.23	81,29.23	8,246.52	3,239.95
RAILWAYS	315	4,61,117.38	5,634,50.06	6,67,113.52	1,82,344.63
ROAD TRANSPORT AND HIGHWAYS	839	4,93,493.25	4,962,80.73	5,10,239.55	2,39,800.48
SHIPPING AND PORTS	8	10,757.29	104,28.79	11,199.74	3,046.68
TELECOMMUNICATIONS	4	16,095.23	161,03.53	27,333.53	9,135.56
URBAN DEVELOPMENT	63	1,86,663.06	1,872,05.75	1,92,886.88	84,370.55
WATER RESOURCES	2	10,384.61	103,84.61	55,782.44	16,450.19
DEFENCE PRODUCTION	2	453.64	4,54.00	453.64	220.22
Grand total	1623	19,33,390.22	20,81,540.23	23,21,502.84	9,47,571.45

Graphical Presentation of All Projects w.r.t. Original Schedule

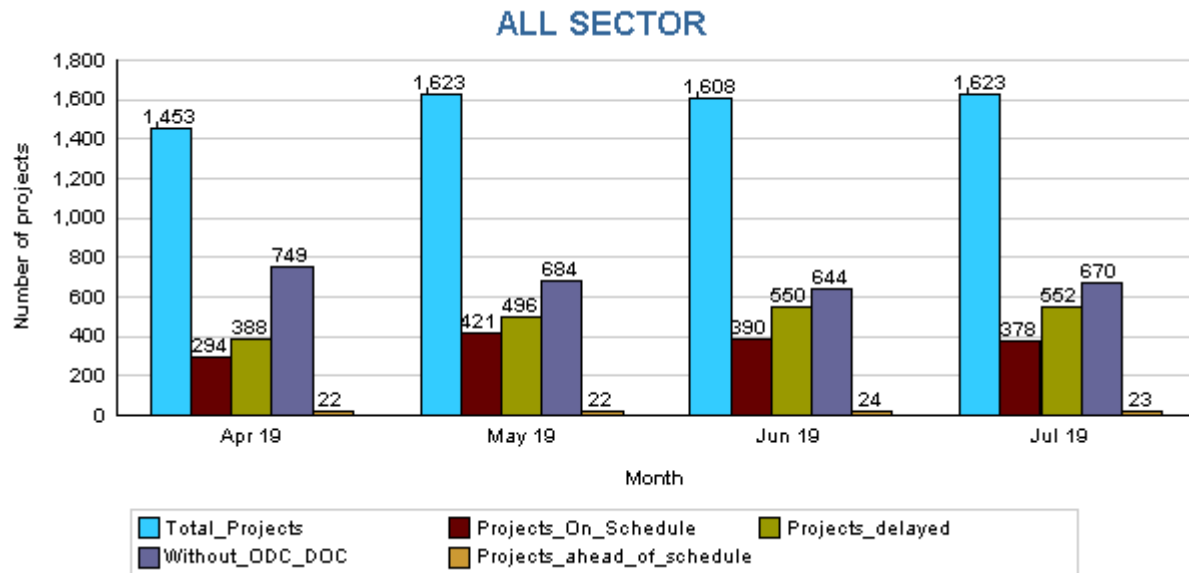


Break-up of 552 Delayed projects in July 2019

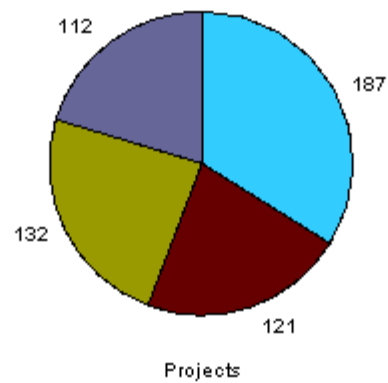


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

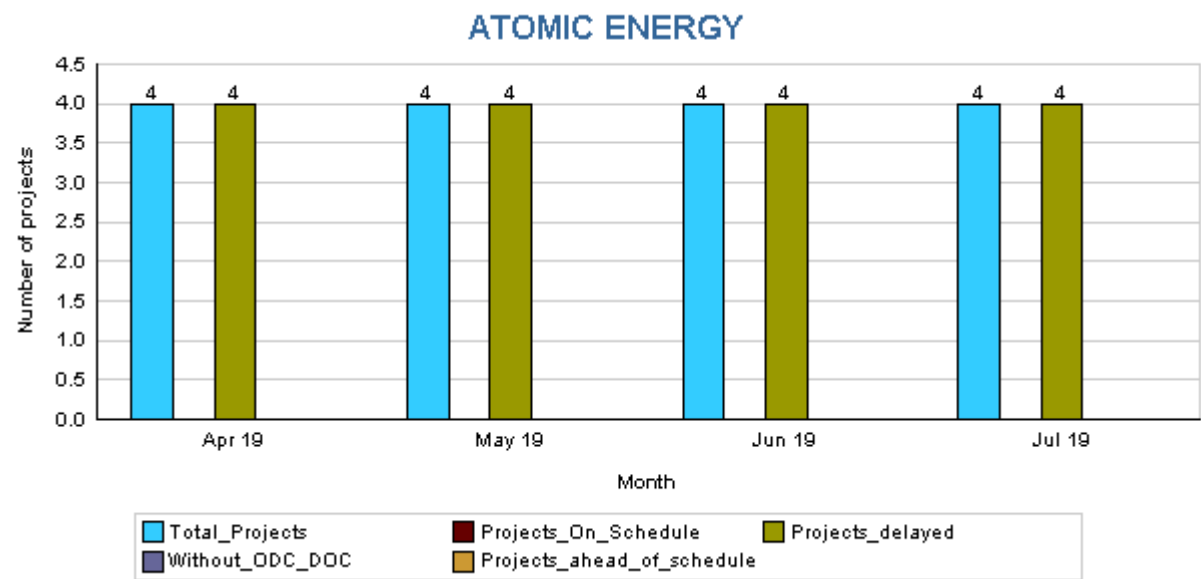


Break-up of 4 Delayed projects in July 2019

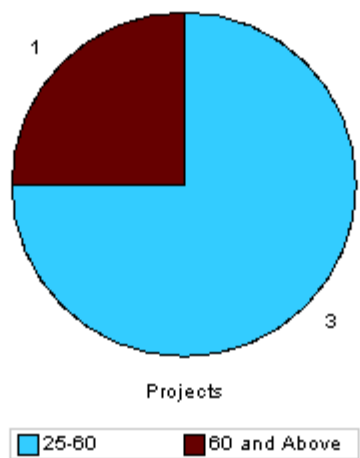


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

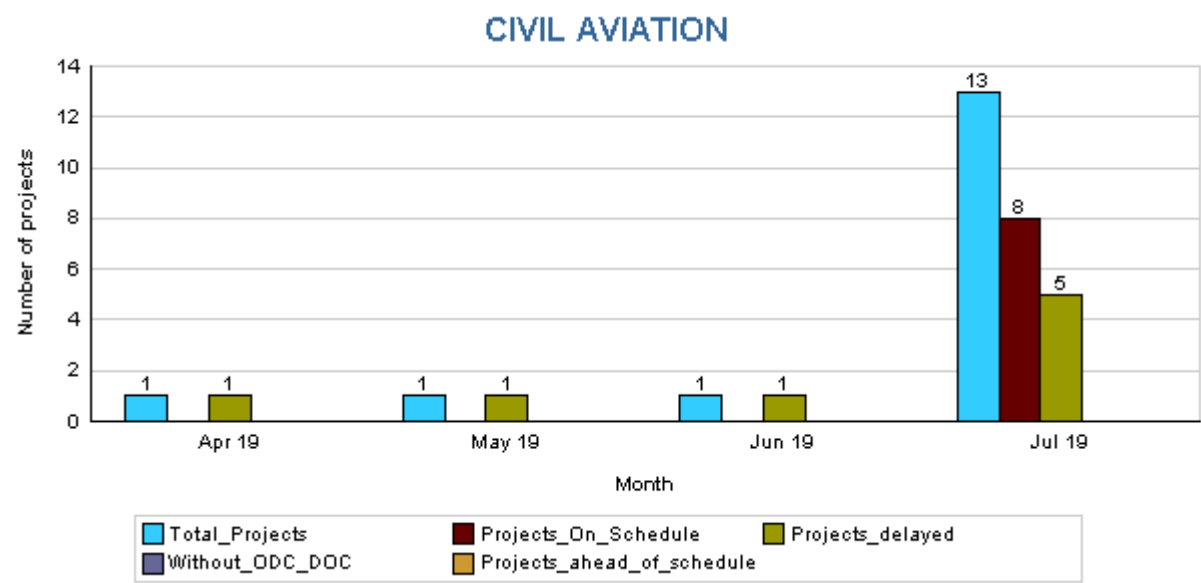


Break-up of 5 Delayed projects in July 2019

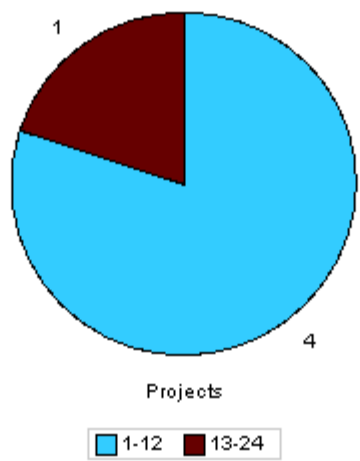


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

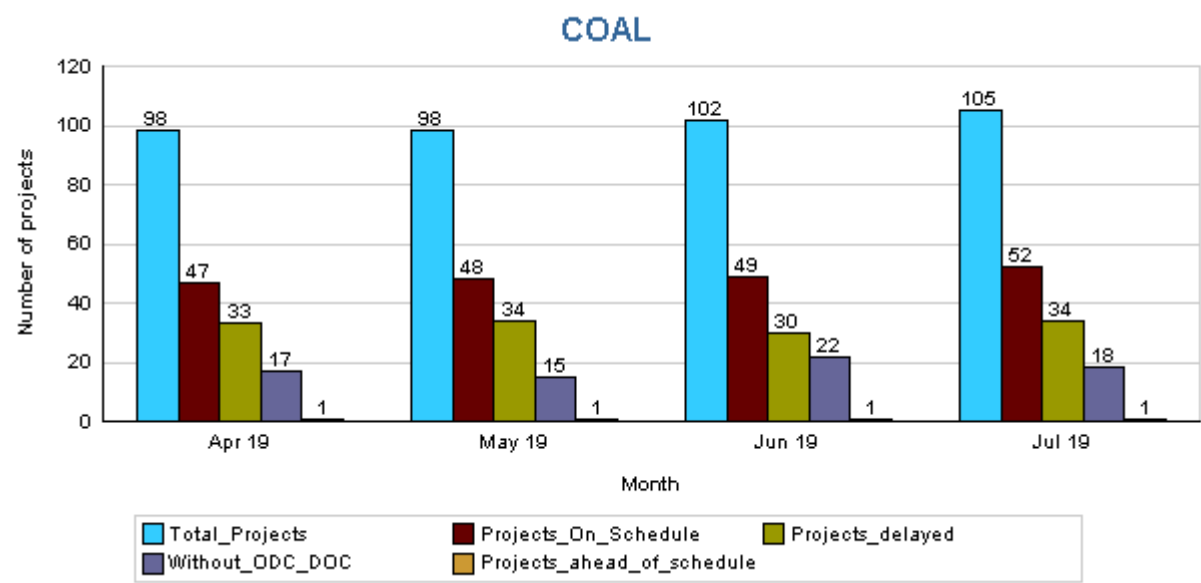


Break-up of 34 Delayed projects in July 2019

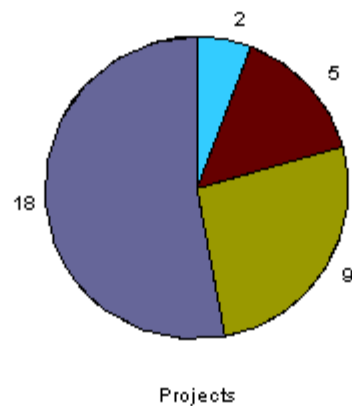


Delay in Months

1-12	13-24	25-60	60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

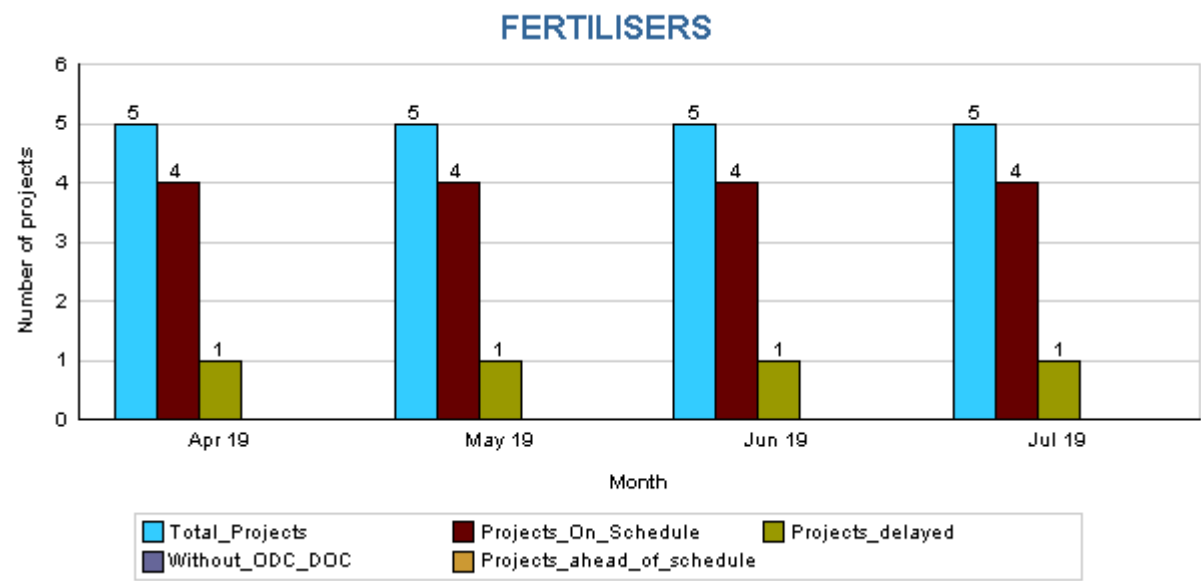


Break-up of 1 Delayed projects in July 2019



Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

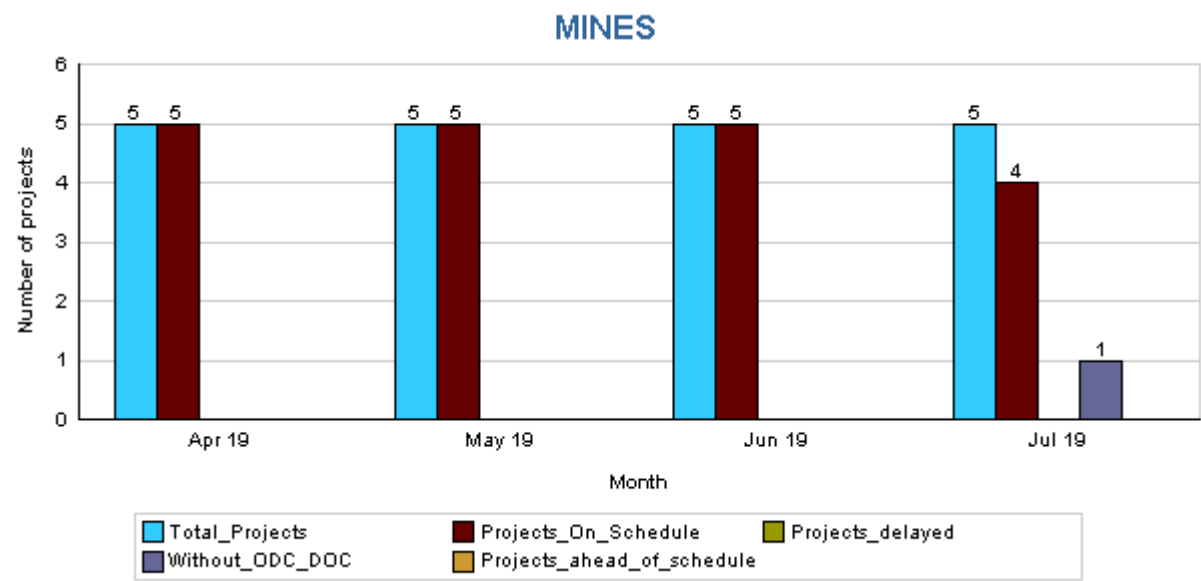


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

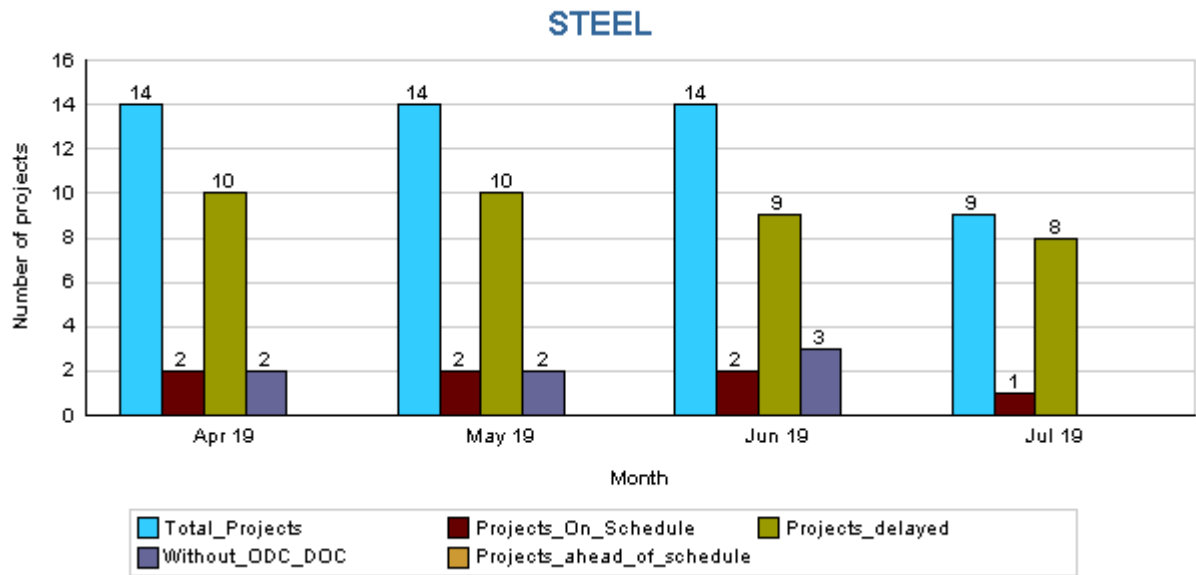


Break-up of 8 Delayed projects in July 2019

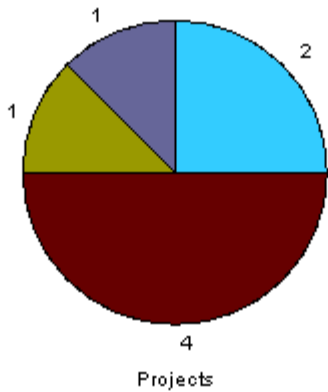


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

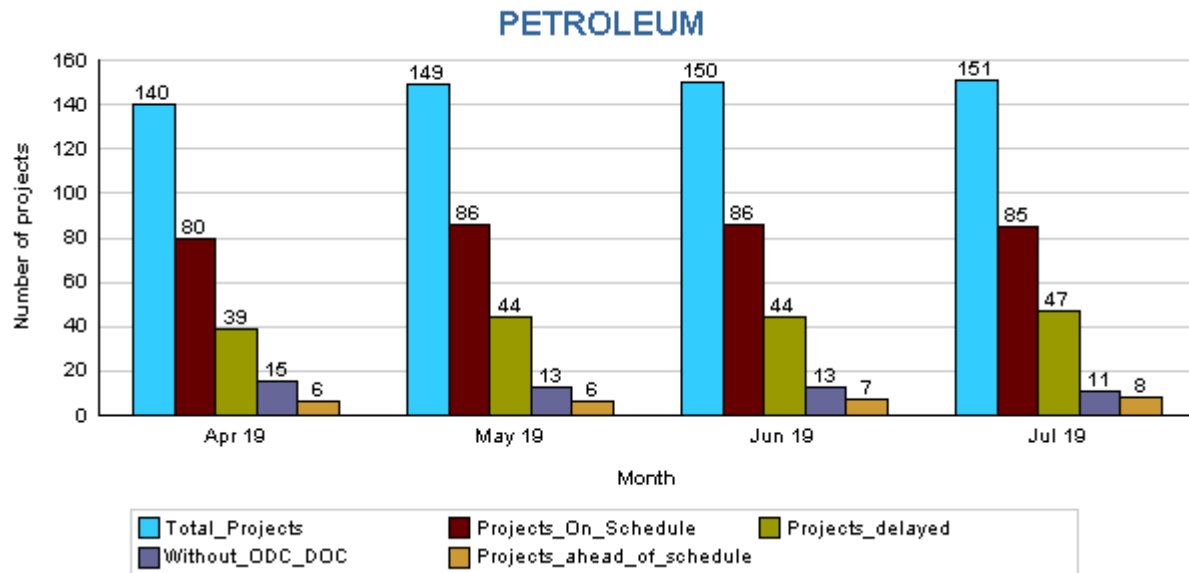


Break-up of 47 Delayed projects in July 2019

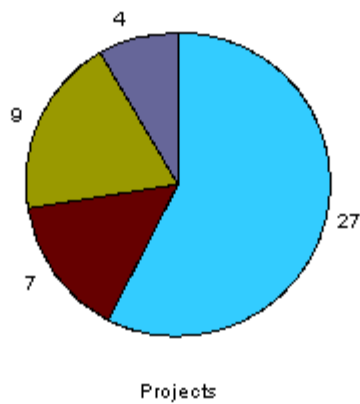


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

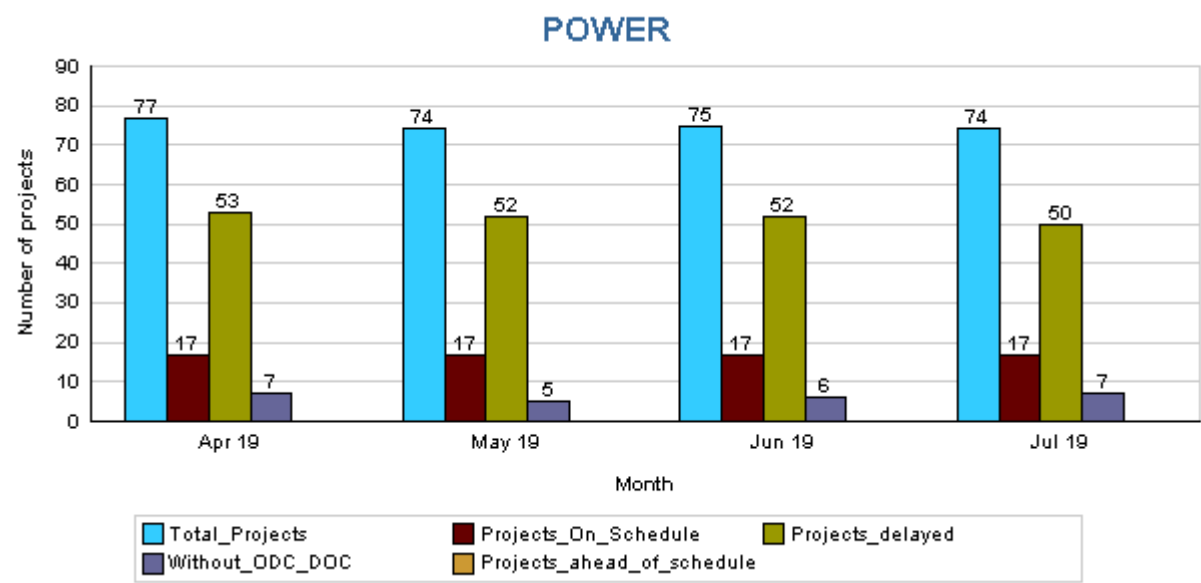


Break-up of 50 Delayed projects in July 2019

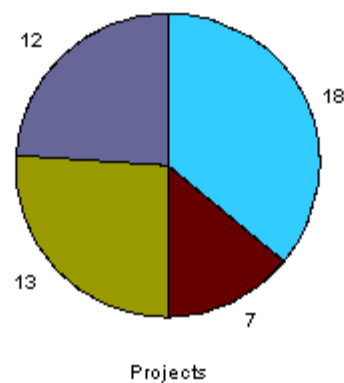

Delay in Months


1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

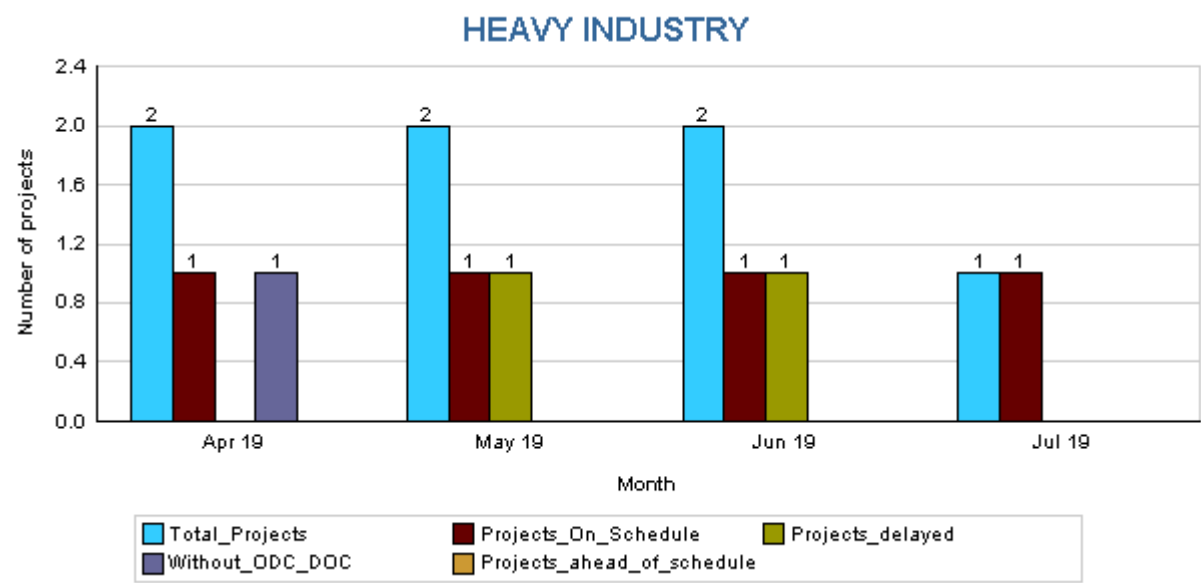


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

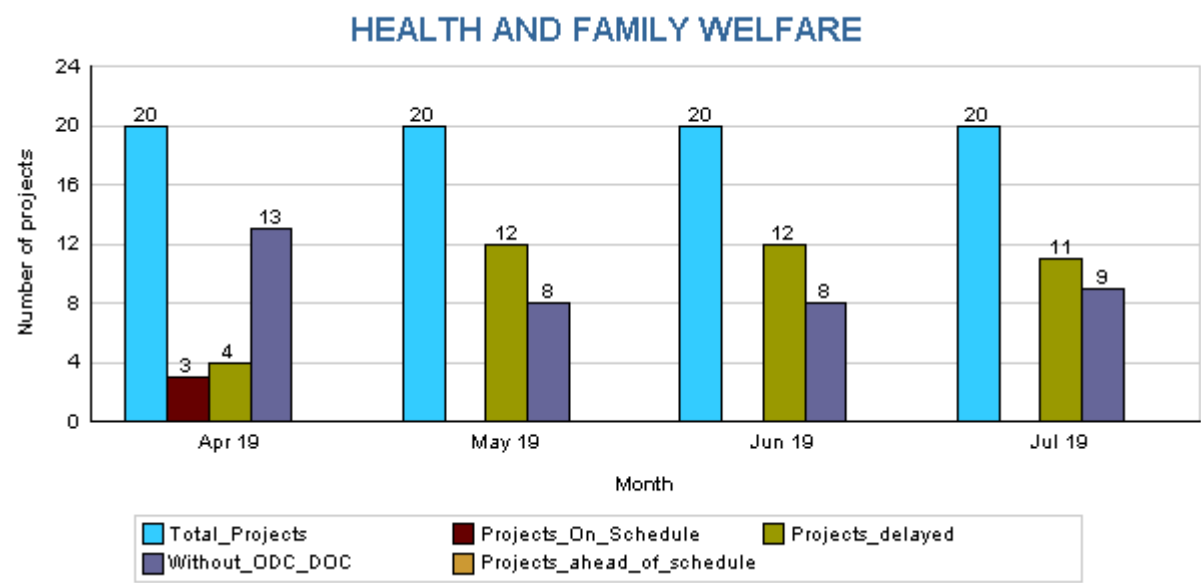


Break-up of 11 Delayed projects in July 2019

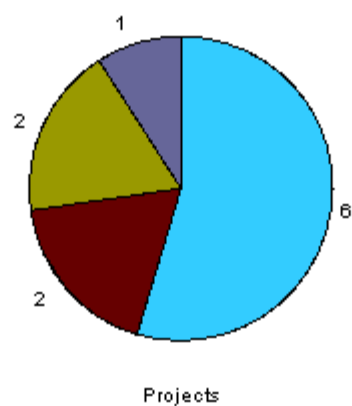


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	6	2	2	1

Graphical Presentation of All Projects w.r.t. Original Schedule

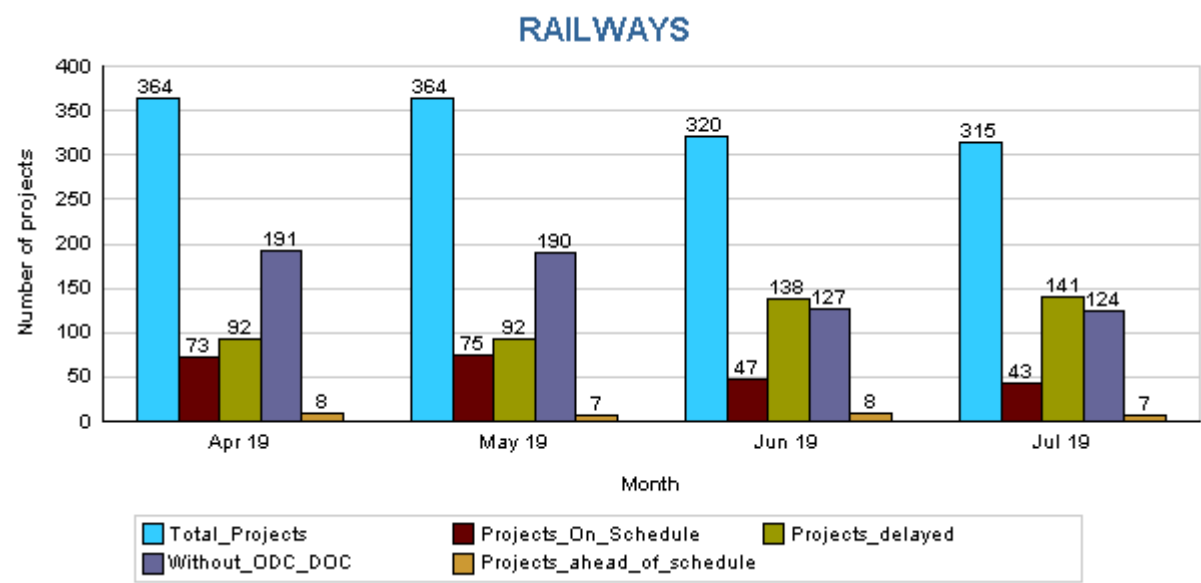


Break-up of 141 Delayed projects in July 2019

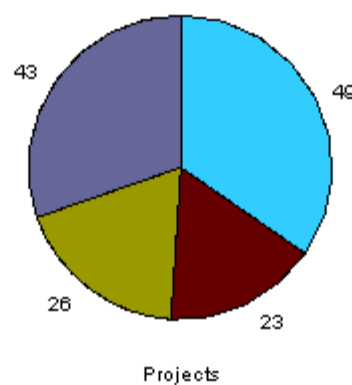


Delay in Months

Delay in Months	Count
1-12	49
13-24	23
25-60	26
60 and Above	43

Graphical Presentation of All Projects w.r.t. Original Schedule

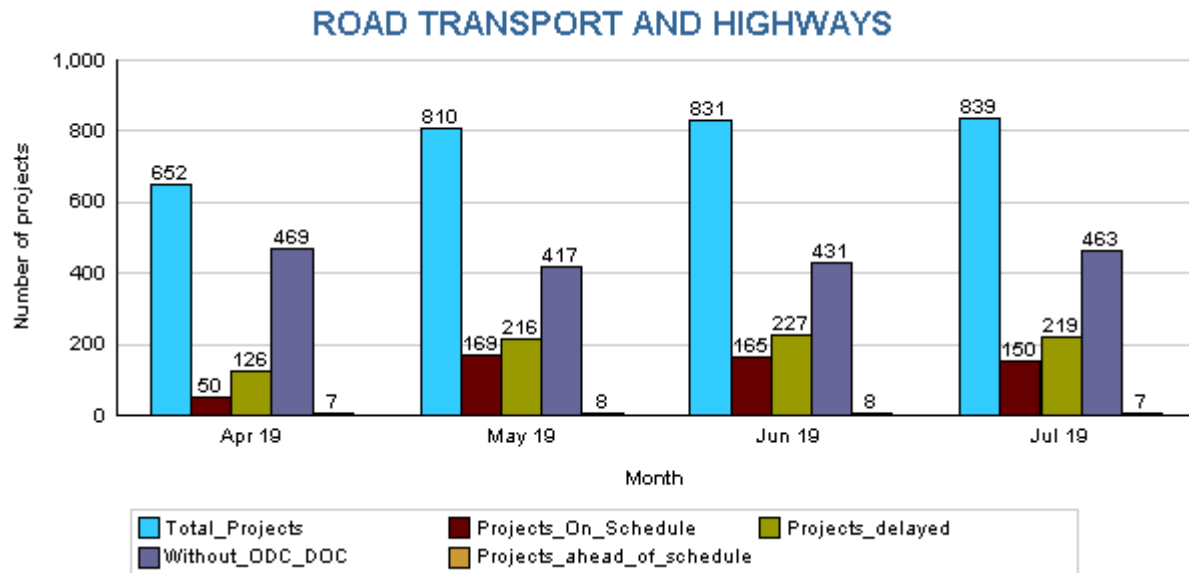


Break-up of 219 Delayed projects in July 2019

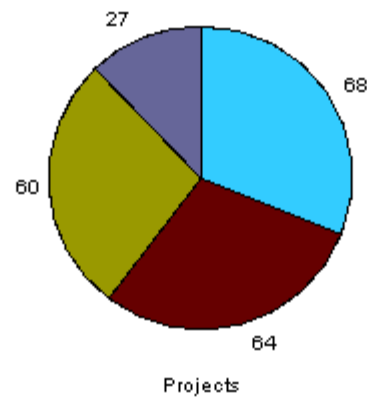


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

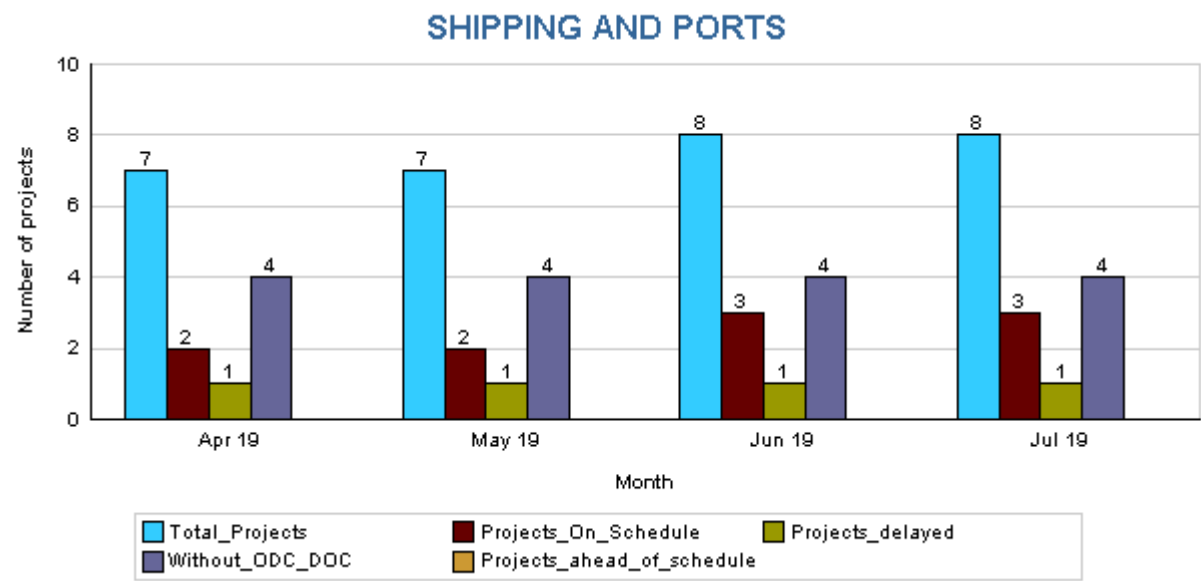


Break-up of 1 Delayed projects in July 2019




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

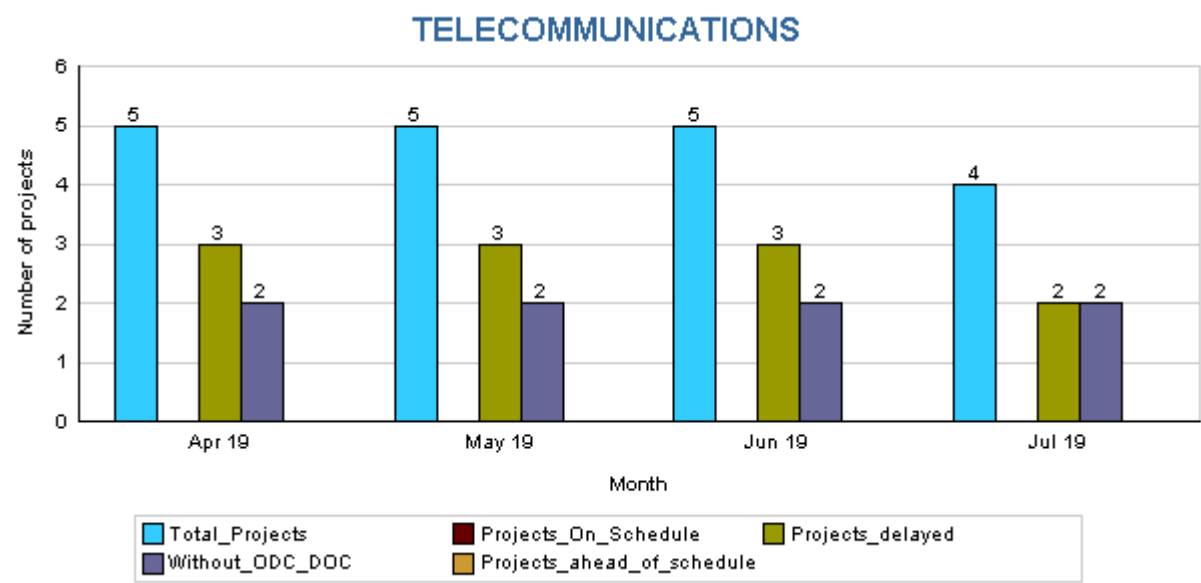


Break-up of 2 Delayed projects in July 2019

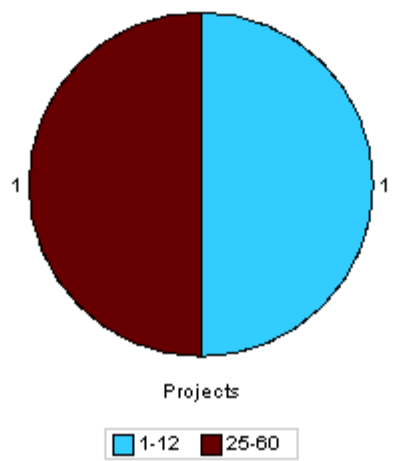


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

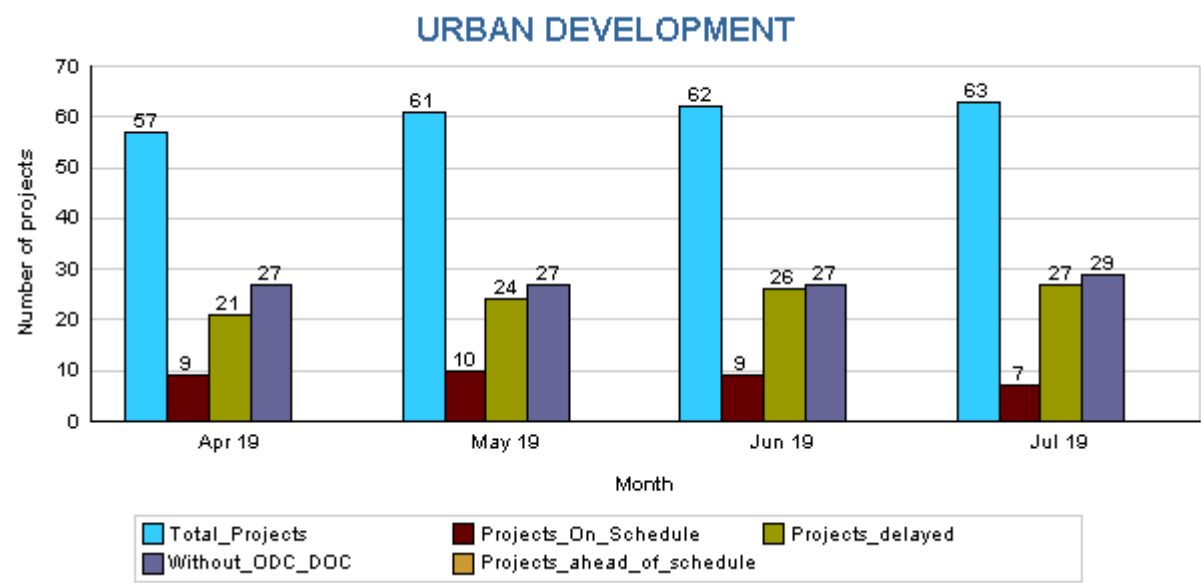


Break-up of 27 Delayed projects in July 2019

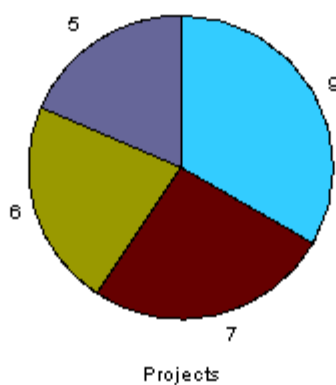


Delay in Months

1-12	13-24	25-60	60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

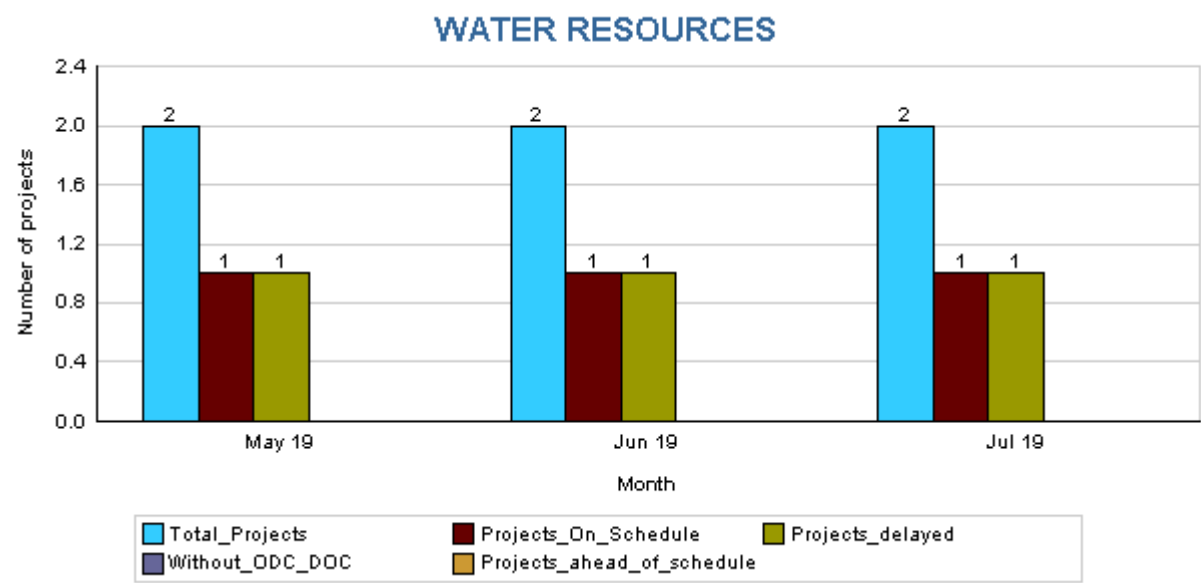


Break-up of 1 Delayed projects in July 2019



Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

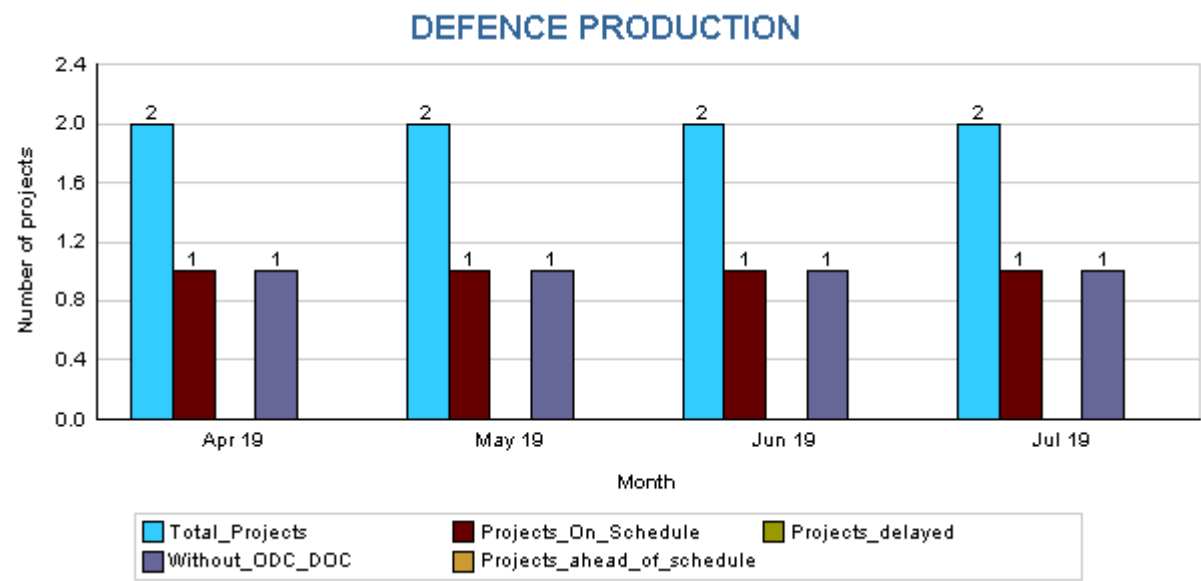

Delay in Months

TABLE-30

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	13,838.00	12/2015 -	06/2020	54(O) -	52/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 17,079.00	17,079.00	11,091.00	12/2016 -	12/2020	48(O) -	40/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	14,864.00	11/2020 -	11/2023	36(O) -	23/76
	Total		67,120.00 -	80,348.00	45,577.74				198/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021	0(O) -	0/0
7	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	539.20 -	539.20	25.64	10/2022 -	10/2022	0(O) -	0/0
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8(O) -	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	323.19 -	323.19	10.14	09/2021 -	09/2021	0(O) -	0/0
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	358.89 -	358.89	29.73	04/2021 -	04/2021	0(O) -	0/0
11	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6(O) -	0/0
12	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	71.55	10/2021 -	10/2021	0(O) -	0/0
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6(O) -	0/0
14	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021	0(O) -	0/0
15	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	353.27 -	353.27	114.29	09/2020 -	09/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL ,	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9(O) -	0/0
17	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI, WEST BENGAL ,	01/2019	264.99 -	264.99	.42	11/2021 -	11/2021	0(O) -	0/0
	Total		8,607.51 -	8,734.44	1,357.47				0/0
	COAL								
18	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,879.89	03/2023 -	03/2023	0(O) -	14/19
19	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,043.87	03/2023 -	03/2023	0(O) -	7/21
20	PELMA OCP(15.00MTY) - [N06000045]SECL, CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023	0(O) -	1/12
21	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH ,	09/2008	152.43 -	459.49	191.40	03/2015 -	03/2020	60(O) -	6/10
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH ,	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72(O) -	2/8
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH ,	12/2009	321.50 -	321.50	192.68	03/2014 -	03/2021	84(O) -	0/5
24	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH ,	11/2009	198.59 -	198.59	169.15	03/2016 -	-	-	7/9
25	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH ,	04/2012	258.56 -	258.56	177.65	03/2016 -	03/2020	48(O) -	4/7
26	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATISGARH ,	12/2013	610.63 -	610.63	92.47	03/2022 -	03/2022	0(O) -	2/10
27	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL, CHHATISGARH ,	05/2014	164.49 -	164.49	82.76	03/2020 -	03/2020	0(O) -	5/9
28	AMERA OC RCE - [N06000123]SECL, CHHATISGARH ,	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24(O) -	1/7
29	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH ,	07/2015	316.10 -	316.10	67.41	03/2020 -	03/2020	0(O) -	1/6
30	DURGAPUR OPENCAST PROJECT - [N06000136]SECL, CHHATISGARH ,	02/2015	916.24 -	916.24	4.02	03/2023 -	03/2023	0(O) -	1/11
31	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL, CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	1/5
32	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL, CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
33	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL, CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/1
34	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL, CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	1/1
35	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND ,	08/2008	706.40 -	706.40	354.48	07/2012 -	03/2022	116(O) -	5/6
36	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND ,	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120(O) -	4/6
37	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND ,	08/2008	264.68 -	264.68	179.87	03/2012 -	03/2021	108(O) -	5/6

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
38	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	362.47	03/2016 -	03/2021	60(O) -	5/6
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	89.82	03/2014 -	03/2021	84(O) -	6/6
40	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	-	-	4/7
41	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	371.19	04/2015 -	-	-	2/6
42	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	187.12	03/2020 -	03/2020	0(O) -	6/7
43	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.24	03/2021 -	03/2021	0(O) -	0/2
44	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
45	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	244.43	05/2014 -	03/2020	70(O) -	0/8
46	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	180.52	04/2014 -	11/2019	67(O) -	0/10
47	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	80.56	03/2022 -	03/2022	0(O) -	2/22
48	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	90.13	03/2024 -	03/2024	0(O) -	0/16
49	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021	-24(O) -	3/10
50	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/9
51	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	103.99	03/2021 -	03/2021	0(O) -	3/10
52	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	47.15	03/2021 -	03/2021	0(O) -	3/8
53	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/8
54	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	27.08	03/2023 -	03/2023	0(O) -	0/4
55	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	116.09	03/2021 -	03/2021	0(O) -	2/5
56	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	18.45	03/2022 -	03/2022	0(O) -	0/0
57	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	264.90	03/2021 -	03/2021	0(O) -	0/9
58	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022	0(O) -	0/9
59	SEMARIA OPENCAST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	0/5
60	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	.00	03/2025 -	03/2025	0(O) -	0/7
61	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	213.24	03/2020 -	03/2020	0(O) -	8/11
62	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020	0(O) -	3/8

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67	267.67	208.78	03/2018	-	-	7/7
64	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94	409.68	119.73	03/2023	03/2023	0(O)	7/11
65	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56	295.56	123.60	03/2019	-	-	10/13
66	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49	205.49	121.74	03/2020	03/2020	0(O)	6/10
67	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69	483.69	199.23	03/2021	03/2021	0(O)	2/6
68	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28	727.28	258.40	03/2025	03/2025	0(O)	5/13
69	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90	333.43	17.71	03/2023	03/2024	12(O)	3/10
70	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65	313.34	115.28	03/2021	03/2024	36(O)	3/6
71	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42	498.42	175.30	03/2020	03/2020	0(O)	2/6
72	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68	198.68	181.84	03/2019	-	-	2/9
73	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52	304.52	153.29	03/2019	-	-	2/8
74	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73	362.73	319.81	03/2020	03/2020	0(O)	0/0
75	SAONER I UG TO OC PHASE I - [N06000177]WCL,MAHARASHTRA ,	11/2016	162.10	162.10	50.56	03/2022	03/2022	0(O)	0/6
76	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14	318.14	149.87	03/2021	03/2021	0(O)	0/4
77	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71	252.71	.00	03/2021	03/2021	0(O)	0/3
78	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA ,	10/2016	164.96	164.96	89.94	03/2019	03/2019	-	0/3
79	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76	319.76	235.29	03/2022	03/2022	0(O)	0/3
80	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07	458.07	20.86	03/2022	03/2022	0(O)	1/12
81	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00	328.00	150.05	03/2021	03/2021	0(O)	1/6
82	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96	302.96	302.96	03/2010	03/2020	120(O)	10/10
83	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10	490.10	493.85	03/2017	03/2020	36(O)	11/12
84	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77	457.77	539.59	03/2013	03/2022	108(O)	8/9
85	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08	172.08	347.15	03/2010	03/2022	144(O)	3/4
86	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28	207.28	228.90	03/2012	03/2021	108(O)	5/7
87	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53	479.53	390.94	03/2013	03/2021	96(O)	6/9

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	196.26	03/2019 -	03/2022	36(O) -	2/9
89	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,547.80	03/2026 -	03/2026	0(O) -	7/15
90	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12(O) -	5/6
91	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	75.78	03/2018 -	03/2020	24(O) -	4/6
92	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	439.24	03/2021 -	03/2021	0(O) -	6/9
93	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	82.60	03/2027 -	03/2027	0(O) -	2/12
94	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,111.70	03/2029 -	03/2029	0(O) -	0/9
95	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	09/2019	0(O) -	0/0
96	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	12/2019	0(O) -	0/0
97	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,080.41	7,080.41	6,567.64	12/2015 -	12/2019	48(O) -	30/35
98	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 -	709.06	448.19	06/2015 -	09/2019	51(O) -	5/7
99	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	296.92	03/2012 -	03/2024	144(O) -	35/42
100	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
101	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132(O) -	0/2
102	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	154.15	03/2015 -	03/2020	60(O) -	30/31
103	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	170.60	03/2012 -	-	-	6/6
104	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	115.71	03/2015 -	03/2021	72(O) -	2/5
105	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	7.23	03/2015 -	03/2021	72(O) -	4/29
106	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72(O) -	8/13
107	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	134.09	06/2015 -	12/2015	-	35/36
108	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	92.60	07/2016 -	04/2017	-	24/28
109	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	186.91	03/2016 -	12/2016	-	38/39
110	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	78.46	03/2019 -	09/2017	-	15/18
111	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24(O) -	0/9
112	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020	0(O) -	5/17

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
113	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	54.00	03/2019 -	03/2021	24(O) -	1/11
114	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	144.07	- 04/2017	-	-	0/6
115	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA ,	08/2016	431.92 -	431.92	.00	- 03/2020	-	-	0/9
116	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA ,	02/2018	412.70 -	412.70	.00	- 03/2021	-	-	0/7
117	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	6,860.71	11/2021 -	11/2021	0(O) -	0/0
118	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	314.86	03/2022 -	03/2022	0(O) -	9/13
119	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	486.13	03/2018 -	03/2020	24(O) -	11/16
120	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/21
121	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	.00	03/2029 -	03/2029	0(O) -	0/22
122	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.00	03/2027 -	03/2027	0(O) -	0/27
	Total		99,835.93 -	1,00,289.27	35,189.01				507/1102
	<u>FERTILISERS</u>								
123	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	100.17	11/2019 -	11/2019	0(O) -	0/2
124	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 -	209.44	160.07	11/2016 -	09/2019	34(O) -	3/13
125	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	92.10	04/2020 -	04/2020	0(O) -	1/14
126	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	101.91	11/2019 -	11/2019	0(O) -	0/2
127	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	107.64	11/2019 -	11/2019	0(O) -	0/2
	Total		1,299.07 -	1,310.72	561.89				4/33
	<u>INFORMATION AND BROADCASTING</u>								
128	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH ,	11/2016	204.32 -	204.32	.00	02/2019 -	11/2019	9(O) -	0/0
129	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA ,	11/2014	597.41 -	597.41	29.80	-	-	-	0/0
130	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC,MAHARASHTRA ,	12/2016	167.70 -	167.70	.00	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		969.43 -	969.43	29.80				0/0
	<u>MINES</u>								
131	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	102.61	04/2021 04/2021	04/2021	0(O) 0	3/3
132	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	318.13	01/2020 01/2020	01/2020	0(O) 0	1/2
133	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020	0(O) -	2/2
134	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.30	04/2021 04/2021	04/2021	0(O) 0	1/1
135	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 -	166.62	134.98	06/2019 -	-	-	1/1
	Total		7,078.62 -	7,078.62	587.94				8/9
	<u>STEEL</u>								
136	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,292.76	12/2017 10/2019	10/2019	22(O) 1	5/6
137	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	206.91	08/2018 10/2019	10/2019	14(O) 3	2/4
138	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	23,140.00	15,811.82	05/2015 07/2020	07/2020	62(O) 0	64/86
139	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	431.27	10/2017 06/2020	06/2020	32(O) 0	0/2
140	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	927.19	12/2017 11/2019	11/2019	23(O) 5	1/2
141	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	99.71	06/2019 06/2020	06/2020	12(O) 0	0/1
142	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,970.60	04/2018 11/2019	11/2019	19(O) 6	3/3
143	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,155.53	09/2018 09/2019	09/2019	12(O) 0	4/5
144	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	2.89	09/2020 -	09/2020	0(O) -	0/4
	Total		26,228.23 -	33,485.23	22,898.68				79/113
	<u>PETROLEUM</u>								
145	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	5,541.02	07/2020 -	07/2020	0(O) -	81/111

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
146	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00	407.00	375.09	09/2019	09/2019	0(O)	24/27
147	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00	34,012.00	3,011.57	06/2020	08/2021	14(O)	15/20
148	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00	342.00	.00	03/2021	03/2021	0(O)	0/0
149	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00	247.00	.00	03/2021	03/2021	0(O)	0/0
150	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76	407.45	224.89	09/2018 09/2019	09/2019	12(O) 2	3/5
151	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58	384.58	81.56	04/2021	04/2020	-12(O)	0/0
152	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00	466.00	77.27	04/2021	07/2021	3(O)	0/0
153	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00	355.00	14.07	04/2022	02/2023	10(O)	0/0
154	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20	316.20	14.78	10/2021	10/2021	0(O)	0/0
155	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20	580.20	33.91	02/2021	02/2021	0(O)	0/16
156	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15	2,378.86	2,147.00	03/2013 12/2019	12/2019	81(O) 0	6/15
157	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 345.92	345.92	145.60	01/2014	11/2019	70(O)	6/7
158	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00	423.00	250.31	08/2019	09/2019	1(O)	5/13
159	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00	2,582.00	1,526.40	11/2019	11/2019	0(O)	13/17
160	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 265.49	265.49	157.02	05/2020	05/2020	0(O)	4/5
161	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00	350.00	2.06	01/2019	09/2019	8(O)	0/0
162	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00	1,222.00	531.40	09/2019	09/2019	0(O)	6/7
163	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91	682.90	7.60	02/2020	02/2020	0(O)	1/14
164	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00	557.00	178.05	02/2020	02/2020	0(O)	1/5
165	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75	224.75	3.30	08/2020	08/2020	0(O)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
167	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]OCL, BIHAR ,	07/2015	822.66 -	822.66	822.02	11/2018 -	08/2019	9(O) -	8/8
168	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]OCL, BIHAR ,	05/2016	664.00 -	664.00	594.01	12/2020 -	02/2020	-10(O) -	4/5
169	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]OCL, BIHAR ,	09/2015	324.00 -	324.00	149.98	06/2020 -	03/2020	-3(O) -	3/4
170	LPG BP PROJECT MOTIHARI - [N16000317]OCL, BIHAR ,	05/2018	206.50 -	206.50	8.19	03/2021 -	03/2021	0(O) -	10/26
171	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]OCL, BIHAR ,	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020	0(O) -	2/2
172	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL, BIHAR ,	10/2017	359.25 -	359.25	61.78	10/2022 -	10/2022	0(O) -	0/0
173	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]OCL, BIHAR ,	07/2018	189.00 -	189.00	7.82	01/2021 -	01/2021	0(O) -	2/8
174	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]OCL, BIHAR ,	04/2018	522.00 -	522.00	142.12	03/2021 -	03/2021	0(O) -	0/0
175	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]OCL, BIHAR ,	06/2017	951.64 -	951.64	325.42	10/2019 -	10/2019	0(O) -	9/11
176	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL, CHHATTISGARH ,	12/2016	300.00 -	300.00	1.09	04/2021 -	-	-	0/0
177	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,783.74	05/2019 10/2019	10/2019	5(O) 0	13/14
178	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT ,	04/2016	327.78 -	200.00	140.90	04/2018 -	08/2019	16(O) -	18/20
179	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC, GUJARAT ,	02/2017	1,162.56 -	1,162.56	356.41	03/2026 -	03/2026	0(O) -	7/10
180	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]OCL, GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	108.00	07/2020 -	07/2020	0(O) -	10/10
181	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]OCL, GUJARAT ,	08/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020	0(O) -	1/1
182	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]OCL, GUJARAT ,	03/2018	3,380.00 -	3,380.00	1,872.71	09/2019 -	09/2019	0(O) -	7/9
183	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]OCL, GUJARAT ,	10/2017	906.00 -	906.00	85.08	02/2020 -	10/2020	8(O) -	4/8
184	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]OCL, GUJARAT ,	03/2018	588.20 -	588.20	.94	-	-	-	6/17
185	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL, GUJARAT ,	09/2018	225.54 -	225.54	.00	02/2021 -	02/2021	0(O) -	2/8
186	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]ONGC, GUJARAT ,	10/2018	156.67 -	156.67	.00	03/2021 -	03/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
187	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	63.55	11/2020 -	11/2020	0(O) -	18/46
188	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	7.75	02/2020 -	02/2020	0(O) -	3/6
189	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	1,562.10	07/2019 -	12/2019	5(O) -	7/9
190	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	142.67	08/2020 -	08/2020	0(O) -	3/6
191	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	13.11	01/2021 -	01/2021	0(O) -	0/0
192	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	14.12	02/2020 -	02/2020	0(O) -	3/4
193	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 -	286.42	1.00	08/2020 09/2020	09/2020	1(O) 1	6/16
194	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	.00	06/2021 -	06/2021	0(O) -	0/3
195	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	147.35	09/2019 -	06/2019	-	4/4
196	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 910.23	910.23	320.14	03/2023 03/2022	03/2022	-12(O) 0	6/10
197	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	06/2020	0(O) -	0/0
198	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	46.48	10/2022 -	10/2022	0(O) -	9/17
199	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	42.63	10/2022 -	10/2022	0(O) -	0/0
200	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
201	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	0(O) -	0/0
202	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	185.00	164.61	04/2019 06/2019	10/2018	-	8/8
203	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	154.03	03/2019 09/2019	09/2019	6(O) 1	11/11
204	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	726.57	12/2019 07/2020	07/2020	7(O) 0	8/9
205	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	621.00	68.27	03/2020 -	09/2020	6(O) -	2/3
206	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	.42	03/2021 -	03/2021	0(O) -	0/0
207	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	6.94	06/2022 -	06/2022	0(O) -	0/0
208	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
209	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	354.84	10/2017 -	-	-	39/52
210	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	3,518.66	08/2018 -	11/2019	15(O) -	0/20
211	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	944.42	02/2020 10/2020	10/2020	8(O) 0	0/20
212	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	495.00	06/2019 -	02/2022	32(O) -	0/0
213	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	15.04	03/2023 -	03/2023	0(O) -	0/0
214	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	22.66	06/2020 -	08/2020	2(O) -	0/0
215	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 -	1,683.06	1,285.65	05/2013 12/2019	12/2019	79(O) 0	4/8
216	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 -	2,059.63	1,908.01	03/2015 12/2019	12/2019	57(O) 7	14/18
217	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019	8(O) 0	8/9
218	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020	14(O) 0	4/5
219	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	4,323.32	12/2017 03/2020	03/2020	27(O) 0	4/5
220	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,192.66	04/2018 05/2020	05/2020	25(O) 0	13/15
221	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	917.26	08/2021 -	08/2021	0(O) -	4/5
222	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	335.52	02/2020 -	09/2019	-5(O) -	0/10
223	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	155.19	12/2019 -	12/2019	0(O) -	0/17
224	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	34.07	01/2021 -	04/2021	3(O) -	0/0
225	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	27.05	01/2021 -	10/2021	9(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
226	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	37.47	01/2021 -	01/2021	0(O) -	0/0
227	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	2,376.01	03/2020 -	03/2020	0(O) -	104/135
228	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 565.15	565.15	442.18	11/2019 03/2020	03/2020	4(O) 0	4/5
229	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 -	511.30	445.24	11/2019 -	11/2019	0(O) -	4/5
230	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 -	1,033.95	897.60	11/2019 -	11/2019	0(O) -	4/5
231	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,475.92	2,745.63	05/2021 12/2021	12/2021	7(O) 0	11/15
232	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	115.60	08/2020 -	08/2020	0(O) -	0/15
233	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	58.33	06/2020 -	06/2020	0(O) -	0/0
234	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	436.53	12/2019 -	12/2019	0(O) -	4/5
235	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,292.46	121.38	05/2021 -	05/2021	0(O) -	0/0
236	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 -	3,228.80	405.01	03/2022 -	03/2022	0(O) -	0/0
237	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1(O) -	0/0
238	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	05/2019	2,494.68 -	2,494.68	.00	12/2021 -	03/2022	3(O) -	0/0
239	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	763.92	.00	12/2020 -	12/2020	0(O) -	0/0
240	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	689.03	10/2014 08/2019	08/2019	58(O) 0	34/40
241	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33(O) -	2/15
242	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	806.13	12/2020 -	12/2020	0(O) -	4/5
243	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	1,697.02	12/2020 -	08/2020	-4(O) -	4/5
244	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	600.35	10/2019 -	10/2019	0(O) -	5/6
245	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	256.76	07/2018 -	10/2020	27(O) -	23/36

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
246	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00	1,879.00	1,438.13	06/2020	06/2020	0(O)	18/24
247	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00	406.00	83.34	10/2020	10/2020	0(O)	6/12
248	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66	571.66	158.44	12/2019	12/2019	0(O)	6/22
249	LAYING OF VIJAIPIUR-AURAIYA PIPELINE SECTION OF VIJAIPIUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40	2,000.00	1,256.25	12/2020	12/2020	0(O)	19/24
250	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00	2,433.00	1,395.00	12/2020	12/2020	0(O)	16/24
251	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00	3,437.00	1,256.48	12/2020	12/2020	0(O)	17/24
252	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00	3,049.47	2,371.62	12/2012	02/2022	110(O)	18/42
253	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00	2,677.00	717.33	03/2021	03/2021	0(O)	8/26
254	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00	500.00	.00	06/2017	-	-	0/0
255	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00	3,308.00	934.68	12/2021	12/2021	0(O)	10/20
256	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00	3,150.00	2,573.02	09/2017	07/2019	22(O)	6/6
257	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00	1,933.00	995.48	12/2020	12/2020	0(O)	18/24
258	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00	429.00	306.24	01/2019	12/2019	11(O)	6/6
259	LPG BP PROJECT KHRDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59	161.59	36.68	12/2019	12/2019	0(O)	17/26
260	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53	243.53	48.22	07/2022	07/2022	0(O)	0/0
261	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00	315.00	110.38	12/2021	12/2020	-12(O)	2/3
262	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20	182.20	27.01	07/2022	07/2022	0(O)	0/0
263	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00	5,654.00	242.10	10/2021	10/2021	0(O)	2/10
264	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00	750.00	34.73	12/2020	12/2020	0(O)	0/14
265	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50	1,297.50	8.85	10/2021	10/2021	0(O)	0/1
266	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30	462.30	.00	09/2021	09/2021	0(O)	0/0
267	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00	3,361.00	284.31	08/2021	08/2021	0(O)	2/11

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
268	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	.00	09/2022 -	09/2022	0(O) -	0/0
269	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
270	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	69.10	- -	03/2021	- -	5/26
271	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
272	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.00	11/2015 -	-	-	52/52
273	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56(O) -	0/0
274	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	390.52	380.85	03/2019 05/2020	05/2020	14(O) 0	4/5
275	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	454.65	12/2018 -	02/2021	26(O) -	4/5
276	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	12.28	06/2020 -	06/2020	0(O) -	4/5
277	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	909.85	12/2019 -	12/2019	0(O) -	0/0
278	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	109.41	08/2020 -	08/2020	0(O) -	0/0
279	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	26.83	10/2020 -	08/2021	10(O) -	0/0
280	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022	0(O) -	0/0
281	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	121.99	04/2022 -	04/2022	0(O) -	32/43
282	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	39.76	08/2021 -	11/2021	3(O) -	0/0
283	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	376.04	09/2019 -	09/2019	0(O) -	5/6
284	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	.71	08/2020 -	08/2020	0(O) -	1/1
285	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	15.01	12/2021 -	12/2021	0(O) -	2/3
286	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH ,	03/2014	204.00 -	204.00	132.24	09/2019 -	09/2019	0(O) -	0/6
287	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	13.19	12/2021 -	12/2021	0(O) -	0/0
288	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH ,	08/2016	154.84 -	154.84	114.80	11/2019 -	11/2019	0(O) -	37/40

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
289	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	38.51	02/2020 -	10/2020	8(O) -	18/26
290	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL ,	03/2015	694.00 1,097.54	1,097.54	693.14	10/2018 11/2019	11/2019	13(O) 0	0/15
291	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
292	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL, WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	171.48	12/2020 -	12/2020	0(O) -	12/24
293	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL ,	04/2017	163.02 -	163.02	44.00	04/2020 -	03/2021	11(O) -	17/26
294	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL, WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	1,569.01	09/2019 -	09/2019	0(O) -	10/11
295	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL, WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	108.51	09/2022 -	06/2021	-15(O) -	1/1
	Total		2,46,407.34 -	2,53,901.92	88,700.73				1027/1694
	POWER								
296	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,927.32	09/2010 -	-	-	0/0
297	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH ,	12/2004	2,496.90 7,419.34	7,419.34	7,494.35	12/2009 08/2019	08/2019	116(O) 0	30/30
298	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	16,249.55	10/2011 08/2021	08/2021	118(O) 0	28/47
299	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR ,	01/2007	5,353.00 -	9,996.59	7,840.42	07/2012 -	09/2020	98(O) -	12/25
300	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	13,670.00	05/2018 12/2021	12/2021	43(O) 29	34/45
301	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN, BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	564.81	01/2024 -	01/2024	0(O) -	16/19
302	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	12,229.51	10/2017 03/2020	03/2020	29(O) 0	35/41
303	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019	0(O) -	0/0
304	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL, DELHI ,	03/2015	1,394.52 -	1,394.52	405.65	05/2017 06/2019	12/2019	31(O) 0	4/9
305	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	92.78	09/2018 09/2019	09/2019	12(O) 0	0/0
306	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT ,	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3(O) -	0/0
307	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,997.11	7,522.82	09/2009 -	12/2021	147(O) -	3/5
308	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,152.85	04/2020 -	12/2023	44(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
309	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	9,044.25	06/2019 09/2019	09/2021	27(O) 0	22/23
310	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,268.00	10/2017 -	-	-	0/0
311	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	18,668.00	1,855.39	03/2023 -	03/2023	0(O) -	0/1
312	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10(O) -	0/0
313	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	12,027.37	01/2018 03/2020	03/2020	26(O) 0	39/42
314	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	8,306.06	01/2020 -	01/2020	0(O) -	32/39
315	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	299.55	09/2020 -	09/2020	0(O) -	9/16
316	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
317	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
318	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 12/2019	12/2019	86(O) 0	8/11
319	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022	103(O) 0	23/26
320	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019	63(O) 0	10/12
321	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 08/2019	08/2019	40(O) 0	8/12
322	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 374.63	374.63	210.72	04/2016 03/2017	12/2019	44(O) 0	0/0
323	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 -	546.36	465.21	11/2016 12/2019	03/2020	40(O) 3	8/12
324	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 5,151.37	5,151.37	3,115.72	03/2018 12/2019	12/2019	21(O) 0	9/12
325	EASTERN REGION STRENGTHENING SCHEME-IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 -	225.28	162.30	02/2016 04/2019	06/2019	-	16/17
326	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 -	340.88	251.33	03/2018 03/2019	07/2019	16(O) 0	1/3
327	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	548.30	10/2017 09/2019	09/2019	23(O) 0	0/5
328	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	190.80	07/2017 06/2019	08/2019	25(O) 0	3/5
329	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	81.97	03/2018 03/2018	08/2019	17(O) 0	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
330	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	513.85	01/2018 12/2019	03/2020	26(O) 3	0/0
331	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4(O) -	0/0
332	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019	0(O) -	0/0
333	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	392.96	03/2019 03/2019	07/2019	4(O) 0	0/0
334	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	185.94	06/2019 -	06/2019	-	0/0
335	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	187.60	11/2019 11/2019	11/2019	0(O) 0	0/0
336	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	266.03	01/2019 09/2019	09/2019	8(O) 0	0/0
337	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	407.79	04/2019 04/2019	07/2019	3(O) 0	0/0
338	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	116.76	02/2020 02/2020	02/2020	0(O) 0	0/0
339	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	153.70	02/2019 06/2019	08/2019	6(O) 0	0/0
340	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	117.15	06/2019 06/2019	10/2019	4(O) 0	0/0
341	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	52.63	12/2019 12/2019	12/2019	0(O) 0	0/0
342	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020	0(O) -	0/0
343	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	84.17	06/2019 -	07/2019	1(O) -	0/0
344	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12(O) -	0/0
345	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 12/2018	12/2020	24(O) 0	0/0
346	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,308.50	04/2019 -	07/2019	3(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
347	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020	0(O) -	0/0
348	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020	0(O) -	0/0
349	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5(O) -	0/0
350	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020	0(O) -	0/0
351	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	9,460.46	12/2018 06/2020	06/2020	18(O) 0	33/38
352	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	430.71	04/2019 04/2019	08/2019	4(O) 0	0/0
353	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	1,011.38	01/2019 -	07/2019	6(O) -	0/0
354	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	2,237.45	11/2008 06/2019	08/2019	129(O) 0	20/22
355	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2(O) -	0/0
356	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	5,231.15	11/2020 06/2021	06/2021	7(O) 0	23/23
357	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	6,334.35	07/2019 06/2020	06/2020	11(O) 0	33/35
358	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 -	294.60	295.73	02/2014 -	10/2019	68(O) -	7/8
359	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	9,703.00	02/2017 06/2020	06/2020	40(O) 0	33/40
360	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	509.30	09/2023 -	09/2023	0(O) -	0/0
361	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020	0(O) -	0/0
362	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	125.00	11/2020 -	11/2020	0(O) -	0/0
363	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 -	5,024.35	2,969.55	02/2016 -	06/2022	76(O) -	16/30
364	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,110.76	03/2013 12/2020	12/2020	93(O) 0	6/15
365	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,397.80	1,718.70	06/2013 -	12/2022	114(O) -	10/13
366	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	148.91	08/2017 -	-	-	0/15
367	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	236.30	12/2021 -	12/2021	0(O) -	3/32

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
368	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,592.34	473.97	09/2019 02/2022	02/2022	29(O) 0	5/9
369	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	287.52	04/2018 01/2020	01/2020	21(O) 0	0/0
	Total		2,87,196.40 -	3,60,575.39	2,13,724.90				580/778
	HEAVY INDUSTRY								
370	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019	0(O) -	0/0
	Total		1,554.00 -	1,554.00	335.03				0/0
	HEALTH AND FAMILY WELFARE								
371	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7(O) -	0/0
372	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	85.04	- -	02/2020	- -	0/0
373	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
374	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5(O) -	0/0
375	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83(O) -	0/0
376	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28(O) -	2/2
377	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27(O) -	3/5
378	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.65	54.94	- -	02/2020	- -	0/0
379	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	73.40	- -	05/2020	- -	0/0
380	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	508.29	03/2018 -	-	-	1/2
381	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7(O) -	0/0
382	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	112.97	- -	02/2020	- -	0/0
383	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16(O) -	0/0
384	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19(O) -	1/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
385	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2(O) -	0/0
386	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	99.26	- -	04/2020	- -	0/0
387	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2(O) -	0/0
388	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	241.39	09/2018 -	-	-	0/0
389	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12(O) -	0/0
390	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	112.82	- -	02/2020	- -	0/0
	Total		8,129.23 -	8,246.52	3,239.95				7/10
	<u>RAILWAYS</u>								
391	NANDYAL-YERRAGUNTALA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
392	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168(O) -	0/0
393	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
394	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	- -	-	-	1/1
395	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36(O) -	0/1
396	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	1,331.60	03/2020 -	03/2022	24(O) -	0/0
397	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
398	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12(O) -	0/0
399	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	837.66	12/2023 -	12/2023	0(O) -	0/0
400	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	3,382.95	325.64	03/2022 -	03/2022	0(O) -	0/0
401	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
402	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	7.38	03/2019 -	12/2020	21(O) -	0/0
403	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 1,532.00	1,532.00	606.82	03/2019 -	03/2020	12(O) -	0/0
404	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 728.00	728.00	691.97	03/2019 -	03/2020	12(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
405	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32	2,182.00	582.27	03/2022	03/2020	-24(O)	0/0
406	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96	2,136.01	455.80	03/2021	03/2021	0(O)	0/0
407	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73	1,156.41	1,028.71	03/2012	03/2020	96(O)	0/0
408	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87	589.15	303.96	-	03/2022	-	0/0
409	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65	2,066.77	1,403.38	-	03/2023	-	0/0
410	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41	516.02	389.29	03/2020	03/2020	0(O)	0/0
411	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92	339.00	200.00	-	-	-	0/0
412	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88	749.00	672.82	03/2012	03/2020	96(O)	0/0
413	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87	2,145.00	932.80	03/2019	03/2020	12(O)	0/0
414	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76	360.00	6.67	-	03/2022	-	0/0
415	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87	2,396.88	.40	-	03/2023	-	0/0
416	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57	2,626.98	.28	-	03/2024	-	0/0
417	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25	2,860.55	1.14	-	03/2024	-	0/0
418	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20	2,995.01	1.91	-	03/2024	-	0/0
419	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00	729.92	349.60	-	03/2021	-	0/0
420	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56	2,614.36	375.63	-	03/2022	-	0/0
421	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00	205.00	5.21	-	03/2024	-	0/0
422	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00	926.09	24.16	-	03/2024	-	0/0
423	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62	2,393.23	17.20	-	03/2024	-	0/0
424	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
425	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17	1,605.17	23.40	-	03/2023	-	0/0
426	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56	192.56	.39	-	03/2024	-	0/0
427	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30	281.30	.60	-	03/2024	-	0/0
428	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14	1,470.50	356.81	-	03/2021	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
429	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	785.87	457.46	03/2020 -	03/2022	24(O) -	0/0
430	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	400.17	378.41	- -	01/2020	- -	0/0
431	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 519.33	519.33	126.80	- -	02/2023	- -	0/0
432	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR ,	08/2010	400.00 -	400.00	.00	03/2014 -	-	-	0/0
433	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR ,	07/2004	599.63 674.00	674.00	.00	12/2007 -	-	-	0/0
434	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	390.91	03/2020 -	10/2021	19(O) -	0/1
435	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	424.98	03/2020 -	12/2022	33(O) -	1/1
436	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	541.07	07/2014 -	-	-	0/0
437	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	35.10	03/2021 -	03/2022	12(O) -	0/0
438	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	15.39	03/2021 -	03/2022	12(O) -	0/0
439	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	727.29	488.81	- -	09/2019	- -	0/0
440	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	1,483.14	815.41	- -	12/2021	- -	0/0
441	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 -	1,160.83	654.74	03/2020 -	03/2023	36(O) -	1/1
442	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,100.00	1,016.52	03/2020 -	06/2020	3(O) -	0/0
443	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
444	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 1,226.51	1,226.51	1,039.54	12/2019 10/2019	10/2019	-2(O) 0	0/0
445	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 1,973.66	1,973.66	129.54	03/2021 12/2021	12/2021	9(O) 0	0/1
446	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	619.50	03/2022 12/2022	12/2022	9(O) 9	0/1
447	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 12/2020	12/2020	27(O) 0	0/1
448	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	241.23	03/2020 -	03/2020	0(O) -	0/0
449	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	107.86	- -	03/2024	- -	0/0
450	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	79.53	- -	03/2023	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
451	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,215.34	1,310.23	1,363.06	03/2020 03/2021	03/2021	12(O) 0	0/0
452	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120(O) 0	0/0
453	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	404.70	03/2011 03/2017	03/2017	-	0/0
454	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	933.88	12/2021 -	12/2021	0(O) -	0/0
455	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	296.20	03/2021 -	03/2021	0(O) -	0/0
456	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	92.69	- 03/2021	03/2021	- 0	0/0
457	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36(O) 0	0/0
458	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	1,176.15	12/2021 -	12/2021	0(O) -	0/0
459	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,037.15	1,037.15	992.18	03/2021 03/2022	03/2022	12(O) 0	0/0
460	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	374.60	03/2021 03/2021	03/2021	0(O) 0	0/0
461	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9(O) -	0/0
462	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
463	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
464	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
465	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 809.07	809.07	616.90	03/2019 03/2020	03/2020	12(O) 0	0/0
466	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 663.29	663.29	163.85	03/2020 03/2021	03/2021	12(O) 0	0/0
467	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111(O) -	0/0
468	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	286.56	03/2019 -	03/2020	12(O) -	0/0
469	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	368.23	12/2026 -	12/2026	0(O) -	0/0
470	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	18,583.33	11/2002 -	06/2022	235(O) -	0/0
471	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,031.00	3,376.00	3,180.37	- -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
472	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	456.83	-	03/2021	-	0/0
473	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	231.84	12/2018 -	06/2020	18(O) -	0/0
474	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019	35(O) 2	0/0
475	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	332.04	03/2021 -	12/2021	9(O) -	0/0
476	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	159.07	03/2021 -	12/2020	-3(O) -	0/0
477	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	144.76	-	12/2024	-	0/0
478	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
479	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,801.01	44.36	-	12/2023	-	0/0
480	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93(O) -	0/1
481	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	-	12/2023	-	0/0
482	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
483	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.35	-	12/2023	-	0/0
484	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,571.99	03/2023 -	03/2023	0(O) -	0/1
485	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	-	12/2023	-	0/0
486	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72(O) -	0/0
487	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	-	12/2023	-	0/0
488	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93(O) -	0/0
489	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12(O) -	0/5
490	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	578.00	509.07	03/2020 -	03/2020	0(O) -	0/2
491	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36(O) -	0/0
492	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 2,815.62	2,815.62	263.99	-	-	-	0/0
493	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 252.96	252.96	8.50	-	-	-	0/0
494	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 189.24	189.24	6.72	-	-	-	0/0
495	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 1,431.90	1,431.90	67.54	- 06/2022	-	-	0/0
496	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 828.50	828.50	.08	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
497	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
498	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 2,909.99	2,909.99	1,027.12	03/2021 03/2023	03/2023	24(O) 0	0/14
499	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 1,413.76	1,413.76	1,324.64	- 10/2019	10/2019	- 0	0/0
500	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 3,338.15	3,860.40	1,676.43	03/2022 03/2023	03/2023	12(O) 0	0/0
501	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 1,763.93	1,763.93	624.49	03/2020 03/2022	03/2022	24(O) 5	1/1
502	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	1,009.30	12/2020 -	12/2020	0(O) -	0/0
503	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	367.59	03/2022 03/2023	03/2023	12(O) 12	0/10
504	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	154.63	03/2022 09/2022	09/2022	6(O) 6	0/1
505	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	150.61	03/2019 -	02/2020	11(O) -	0/0
506	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 737.72	1,300.44	646.68	02/2019 03/2020	06/2020	16(O) 0	0/1
507	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.00	1,370.00	276.86	12/2021 12/2021	12/2021	0(O) 0	0/0
508	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	86.45	06/2020 06/2021	06/2021	12(O) 0	0/0
509	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	2,980.41	1,403.52	03/2004 -	03/2021	204(O) -	0/0
510	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	3,712.50	2,291.50	03/2021 -	03/2022	12(O) -	0/0
511	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 918.53	918.53	277.61	03/2014 03/2021	03/2021	84(O) 0	0/0
512	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
513	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,205.35	03/2023 -	03/2023	0(O) -	0/0
514	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	792.89	297.30	03/2021 -	03/2022	12(O) -	0/0
515	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	305.00	267.36	03/2019 12/2019	12/2019	9(O) 0	0/0
516	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	220.34	03/2022 -	03/2024	24(O) -	0/0
517	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
518	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
519	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	-	-	0/0
520	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,272.19	271.39	03/2022 -	03/2023	12(O) -	0/0
521	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	145.69	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
522	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	511.35	03/2024 -	03/2022	-24(O) -	0/0
523	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	77.48	03/2023 -	03/2023	0(O) -	0/0
524	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	68.93	03/2022 -	03/2024	24(O) -	0/0
525	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	54.67	03/2023 -	03/2024	12(O) -	0/0
526	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	1,950.00	1,823.93	03/2020 -	03/2020	0(O) -	0/0
527	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
528	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 2,686.63	2,686.63	441.10	03/2023 03/2023	03/2023	0(O) 0	0/1
529	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	260.88	03/2019 -	12/2019	9(O) -	0/0
530	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
531	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
532	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 403.00	860.92	41.54	12/2021 03/2023	03/2023	15(O) 0	0/1
533	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 13,809.00	12,524.00	8,821.88	03/2011 -	03/2020	108(O) -	0/0
534	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.00	261.66	03/2021 -	03/2021	0(O) -	0/0
535	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 4,968.00	5,021.45	2,935.76	03/2014 03/2022	03/2022	96(O) 0	0/0
536	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 1,756.00	1,756.00	1,660.29	04/2020 12/2020	12/2020	8(O) 0	0/1
537	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140(O) -	0/0
538	MUNEERABAD-MAHABOBNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252(O) -	0/0
539	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023	178(O) 0	0/9
540	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 3,300.00	3,300.00	3,259.74	12/2008 -	03/2021	147(O) -	0/0
541	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024	133(O) -	0/0
542	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	770.08	277.14	12/2022 -	12/2022	0(O) -	0/0
543	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	106.55	12/2021 -	-	-	0/0
544	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	307.99	01/2019 -	01/2020	12(O) -	0/0
545	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	719.73	03/2022 03/2022	03/2022	0(O) 0	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
546	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	682.91	03/2022 03/2023	03/2023	12(O) 0	0/0
547	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,079.15	184.89	- -	-	-	0/1
548	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33(O) -	0/3
549	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	12/2022	- -	0/0
550	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	-	-	0/0
551	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.47	- -	03/2024	- -	0/0
552	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	2,496.67	.00	03/2019 -	-	-	0/0
553	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,300.00	2.28	- -	-	-	0/0
554	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 457.08	457.08	369.32	- -	-	-	0/0
555	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	68.14	03/2020 -	03/2020	0(O) -	0/0
556	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 373.87	394.28	272.88	- -	03/2021	- -	0/0
557	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	121.98	03/2020 -	03/2020	0(O) -	0/0
558	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
559	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9(O) -	0/0
560	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228(O) -	0/0
561	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	9.31	- -	03/2025	- -	0/0
562	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.73	- -	03/2025	- -	0/0
563	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	288.53	03/2022 -	03/2025	36(O) -	0/0
564	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	376.90	370.65	- -	03/2020	- -	0/0
565	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	471.81	454.23	- -	05/2019	-	0/0
566	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	433.31	03/2016 -	03/2025	108(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
567	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	102.27	03/2017 -	03/2025	96(O) -	0/0
568	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.42	- -	03/2025	- -	0/0
569	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	153.62	03/2016 -	03/2025	108(O) -	0/0
570	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	200.07	03/2017 -	03/2025	96(O) -	0/0
571	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.47	11/2018 -	03/2021	28(O) -	0/0
572	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.12	- -	03/2025	- -	0/0
573	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
574	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	693.80	424.02	03/2020 -	03/2020	0(O) -	0/0
575	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	226.22	226.22	- -	03/2021	- -	0/0
576	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
577	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
578	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
579	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
580	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	153.64	02/2012 -	03/2025	157(O) -	0/0
581	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	104.65	03/2014 -	03/2025	132(O) -	0/0
582	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	246.00	- -	03/2025	- -	0/0
583	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12(O) -	0/0
584	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	1,787.00	2.46	- -	-	-	1/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
585	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 791.39	800.00	512.67	-	03/2022	-	0/0
586	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	-	12/2023	-	0/0
587	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 -	2,062.20	825.58	-	03/2022	-	0/2
588	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 1,352.74	1,352.74	269.07	03/2020 03/2020	03/2020	0(O) 0	1/1
589	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120(O) -	1/1
590	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	252.18	-	03/2024	-	0/0
591	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	39.52	03/2020 -	04/2022	25(O) -	0/0
592	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	860.43	697.21	03/2020 -	03/2020	0(O) -	0/0
593	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24(O) -	0/0
594	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	678.54	446.51	03/2019 -	02/2021	23(O) -	0/38
595	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	-	-	-	0/0
596	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24(O) -	0/0
597	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	-	-	-	0/0
598	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	2,812.27	12/2023 -	12/2023	0(O) -	0/0
599	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
600	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023	0(O) -	0/0
601	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 781.00	855.00	834.59	03/2016 -	03/2021	60(O) -	0/0
602	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	3,000.00	759.42	03/2015 -	10/2021	79(O) -	0/0
603	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
604	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,798.80	1,354.80	03/2009 -	12/2023	177(O) -	0/0
605	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,729.78	12/2017 -	03/2020	27(O) -	0/0
606	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	1,202.70	861.32	02/2015 -	12/2021	82(O) -	0/0
607	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	386.28	03/2009 03/2009	12/2019	129(O) 0	1/1
608	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 -	1,928.07	624.68	06/2021 -	03/2023	21(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
609	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
610	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	879.96	02/2019 -	03/2022	37(O) -	0/0
611	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 -	843.04	125.30	10/2020 -	03/2023	29(O) -	0/0
612	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	224.63	03/2020 -	03/2020	0(O) -	0/0
613	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	320.30	03/2022 -	03/2023	12(O) -	0/0
614	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	148.96	03/2022 -	03/2025	36(O) -	0/0
615	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	116.91	11/2018 -	03/2021	28(O) -	0/0
616	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	349.23	12/2018 -	03/2022	39(O) -	0/0
617	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	494.27	03/2020 -	06/2020	3(O) -	0/0
618	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.68	546.57	12/2024 -	12/2024	0(O) -	0/0
619	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	1,500.00	1,249.76	03/2020 -	03/2021	12(O) -	0/0
620	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,120.00	992.67	03/2019 -	03/2021	24(O) -	0/0
621	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]JRCON,ODISHA ,	04/2016	5,200.00 1,700.43	1,700.43	48.00	03/2020 06/2023	06/2023	39(O) 39	0/0
622	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.89	- -	03/2024	- -	0/0
623	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	886.41	517.39	02/2019 -	12/2021	34(O) -	0/0
624	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	202.86	12/2019 -	06/2020	6(O) -	0/0
625	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	136.88	10/2018 -	10/2019	12(O) -	0/0
626	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
627	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
628	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	420.18	152.83	03/2020 -	06/2020	3(O) -	0/0
629	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	260.89	11/2019 -	05/2020	6(O) -	0/0
630	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 281.03	410.00	347.99	02/2019 -	12/2019	10(O) -	0/0
631	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.25	- -	-	-	0/0
632	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	438.08	03/2018 -	03/2020	24(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
633	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85	808.85	35.36	08/2022	09/2022	1(O)	0/0
634	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48	4,084.69	285.46	12/2015 06/2021	03/2020	51(O)	0/0
635	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98	980.00	669.21	03/2020	03/2021	12(O)	0/0
636	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74	734.01	445.91	06/2013	-	-	1/4
637	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69	2,072.50	1,386.59	02/2019	02/2020	12(O)	0/0
638	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40	900.00	62.50	-	-	-	0/0
639	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83	2,300.00	241.39	-	-	-	0/0
640	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84	1,105.00	3.34	02/2019	-	-	0/0
641	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00	1,500.00	.62	-	-	-	0/0
642	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68	556.64	303.72	-	-	-	0/0
643	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57	1,140.00	1.63	-	-	-	0/0
644	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41	450.00	151.50	-	03/2020	-	0/0
645	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 951.24	951.24	724.96	-	03/2020	-	0/0
646	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26	231.67	108.34	04/2014	03/2020	71(O)	0/0
647	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87	950.00	927.86	03/2005	-	-	0/0
648	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	268.31	03/2018	-	-	0/0
649	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00	1,567.00	.00	03/2024	03/2026	24(O)	0/0
650	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00	1,003.00	167.73	03/2022	03/2022	0(O)	0/0
651	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00	1,182.31	406.32	03/2020	06/2021	15(O)	0/0
652	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25	458.26	3.83	-	-	-	0/0
653	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48	1,160.48	288.38	03/2010	03/2023	156(O)	1/1
654	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68	816.55	682.17	03/2016	12/2020	57(O)	0/0
655	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00	2,911.84	.92	-	-	-	1/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
656	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR, TELANGANA ,	04/2013	723.00 997.09	997.09	.00	-	-	-	0/1
657	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES, TELANGANA ,	03/2015	636.38 -	636.38	281.85	03/2021 -	03/2021	0(O) -	3/3
658	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA ,	04/2015	773.94 -	773.94	364.69	12/2024 -	12/2024	0(O) -	0/0
659	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA ,	04/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022	0(O) -	0/0
660	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA ,	04/2012	569.63 569.63	650.00	45.24	03/2020 03/2020	12/2021	21(O) -10	2/3
661	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR, UTTAR PRADESH ,	04/1997	120.00 314.09	346.00	345.51	12/2008 03/2015	03/2015	-	0/0
662	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
663	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
664	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
665	UNCHAHAR-AMETHI - [N22000294]NR, UTTAR PRADESH ,	04/2012	1,229.00 -	1,230.00	103.17	- -	03/2023	- -	0/0
666	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
667	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER, UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	291.45	03/2022 -	12/2019	-27(O) -	0/0
668	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR, UTTAR PRADESH ,	04/2015	668.70 680.00	680.00	330.00	03/2020 03/2020	03/2020	0(O) 0	4/6
669	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH ,	04/2015	943.60 -	750.56	327.46	03/2022 -	12/2024	33(O) -	0/0
670	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH ,	04/2011	927.01 -	1,200.00	1,124.56	03/2019 -	03/2020	12(O) -	0/0
671	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	462.05	03/2023 -	12/2024	21(O) -	0/0
672	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	1,011.48	12/2020 -	03/2021	3(O) -	0/0
673	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	474.57	03/2020 -	03/2021	12(O) -	0/0
674	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH ,	08/2015	528.57 -	528.57	88.93	03/2019 -	12/2019	9(O) -	0/0
675	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH ,	04/2016	213.00 -	213.35	5.45	04/2016 -	06/2020	50(O) -	0/0
676	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER, UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
677	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER, UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
678	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
679	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	163.75	04/2017 -	01/2020	33(O) -	0/0
680	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
681	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	11.93	- -	-	-	0/0
682	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	600.00	15.03	01/2022 -	01/2022	0(O) -	0/0
683	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	3.12	12/2019 -	04/2021	16(O) -	0/0
684	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023	0(O) -	0/0
685	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	416.59	03/2021 03/2023	03/2021	0(O) 0	0/6
686	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
687	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	229.48	- -	06/2020	-	0/0
688	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,492.47	12/2024 -	03/2026	15(O) -	0/0
689	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12(O) -	0/0
690	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
691	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
692	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	862.50	03/2019 12/2009	03/2025	72(O) 0	0/0
693	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	827.99	12/2010 12/2017	03/2025	171(O) 60	7/7
694	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
695	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141(O) -	0/0
696	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,127.22	03/2016 -	03/2025	108(O) -	0/0
697	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	2,913.50	843.96	03/2016 -	03/2025	108(O) -	0/0
698	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
699	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	-	-	-	0/0
700	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	- 0	0/0
701	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.03	-	03/2025	-	0/0
702	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	148.03	-	09/2021	-	0/0
703	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	602.27 -	612.00	186.09	12/2021 -	03/2020	-21(O) -	0/0
704	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	-	-	0/0
705	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL ,	02/1999	380.60 -	1,300.00	1,087.60	04/2010 -	-	-	0/0
	Total		4,61,117.38 -	6,67,113.52	1,82,344.63				27/137
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
706	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4
707	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	21.11	12/2017 -	-	-	0/4
708	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	142.03	04/2017 -	-	-	3/4
709	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	17.23	10/2018 -	-	-	0/4
710	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	17.40	10/2018 -	-	-	0/4
711	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019	0(O) -	0/0
712	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019	0(O) -	0/0
713	AJANTHA TO BULDHANA - [N24001008]MORTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	82.81	07/2019 -	07/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
714	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	-	-	0/0
715	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65(O) -	0/0
716	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
717	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
718	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	143.44	10/2015 11/2019	11/2019	49(O) 0	2/4
719	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
720	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
721	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	21.73	11/2018 -	-	-	0/0
722	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
723	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	1.15	03/2020 -	11/2019	-4(O) -	0/0
724	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	687.88	03/2020 -	05/2020	2(O) -	0/0
725	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	20.54	06/2017 -	11/2019	29(O) -	0/0
726	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	176.29	- -	11/2019	- -	0/0
727	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	30.00	- -	07/2021	- -	0/0
728	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	70.71	- -	-	-	0/0
729	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	44.43	- -	07/2021	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
730	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62	1,532.62	.00	03/2021	04/2021	1(O)	0/0
731	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98	1,550.98	.00	-	07/2021	-	0/0
732	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09	565.09	.00	-	02/2021	-	0/0
733	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43	314.43	24.90	-	12/2020	-	0/0
734	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30	557.30	33.63	-	03/2020	-	0/0
735	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH ,	10/2015	333.21	333.21	256.29	12/2015 12/2019	12/2019	48(O) 0	2/3
736	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH ,	09/2016	372.68	372.68	179.43	02/2017 09/2019	09/2019	31(O) 0	2/4
737	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH ,	11/2016	378.24	378.24	187.63	01/2018 01/2020	01/2020	24(O) 0	3/4
738	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH ,	11/2016	290.15	290.15	69.42	05/2017 11/2019	11/2019	30(O) 0	1/4
739	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH ,	01/2017	319.28	319.28	101.28	08/2017 03/2020	03/2020	31(O) 7	1/4
740	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH ,	02/2017	429.43	429.43	181.17	11/2017 03/2020	11/2019	24(O) 0	3/4
741	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH ,	03/2018	228.32	228.32	26.78	08/2018 03/2020	03/2020	19(O) 0	1/4
742	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	84.47	08/2018 02/2020	02/2020	18(O) -6	0/3

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
743	REHABILITATION AND UPGRADE OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	60.76	08/2018 02/2020	02/2020	18(O) 0	2/4
744	REHABILITATION AND UPGRADE OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MORTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	297.12	138.68	07/2018 01/2020	01/2020	18(O) 0	3/4
745	REHABILITATION AND UPGRADE OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	269.70	11/2018 05/2020	05/2020	18(O) 0	1/4
746	REHABILITATION AND UPGRADE OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	401.90	05/2016 03/2020	03/2020	46(O) 0	2/4
747	REHABILITATION AND UPGRADE OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	103.64	08/2018 02/2020	02/2020	18(O) 0	2/4
748	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	301.70	01/2017 12/2019	12/2019	35(O) 0	3/4
749	REHABILITATION AND UPGRADE OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	160.20	05/2016 08/2019	08/2019	39(O) 0	2/4
750	REHABILITATION UPGRADE OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MORTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	144.95	08/2016 12/2019	12/2019	40(O) 0	0/4
751	REHABILITATION AND UPGRADE OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	208.09	09/2016 12/2019	12/2019	39(O) 0	2/4
752	REHABILITATION AND UPGRADE OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	180.38	08/2017 03/2020	08/2019	24(O) 0	2/4
753	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	43.79	09/2017 03/2020	09/2019	24(O) 0	0/4
754	REHABILITATION AND UPGRADE OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	177.36	01/2018 01/2020	01/2020	24(O) 0	1/4
755	REHABILITATION AND UPGRADE OF EEPURPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214(NH2 - [N24000971]MORTH,ANDHRA PRADESH ,	08/2016	574.19 -	574.19	456.98	07/2017 07/2019	07/2019	24(O) 0	3/4
756	REHABILITATION & UPGRADE OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
757	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD, ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	-	0/0
758	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD, ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
759	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD, ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 389.45	389.45	275.19	05/2012 06/2018	-	-	0/0
760	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL, ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	174.80	05/2018 -	08/2019	15(O) -	3/4
761	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL, ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	197.77	01/2019 -	-	-	4/4
762	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL, ARUNACHAL PRADESH , EPC	07/2015	197.16 197.16	197.16	66.17	10/2018 09/2015	09/2018	-	1/4
763	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	240.21	06/2018 -	03/2020	21(O) -	1/3
764	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	90.29	11/2016 -	-	-	2/4
765	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	98.37	- -	09/2020	- -	0/4
766	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL, ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36(O) -	2/4
767	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL - [N24000618]NHIDCL, ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	126.58	- -	12/2020	- -	2/4
768	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	17.42	01/2017 -	01/2020	36(O) -	2/4
769	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60(O) -	1/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
770	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	46.85	04/2017 03/2018	03/2021	47(O) 1	1/4
771	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	37.30	04/2017 -	-	-	1/4
772	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	48.16	04/2017 -	-	-	1/4
773	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	56.15	04/2017 -	-	-	1/4
774	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 168.32	168.32	28.67	04/2017 02/2018	02/2021	46(O) 0	1/4
775	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46(O) 0	0/4
776	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 216.71	216.71	15.77	04/2017 02/2018	02/2021	46(O) 0	0/4
777	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 167.28	167.28	18.70	04/2017 02/2018	02/2021	46(O) 0	0/1
778	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	24.14	04/2017 -	-	-	1/4
779	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
780	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	72.97	- -	-	-	0/0
781	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	154.14	- -	-	-	0/0
782	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH ,	05/2016	259.52 -	259.52	143.01	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
783	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	125.96	- -	-	-	0/0
784	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	30.88	- -	-	-	0/0
785	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 175.06	175.06	.00	- 04/2019	04/2022	- 0	0/0
786	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 176.12	176.12	.00	- 04/2019	04/2022	- 0	0/0
787	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH ,	02/2017	199.02 199.02	199.02	9.65	- 02/2018	02/2021	- 0	0/0
788	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH ,	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	- 0	0/0
789	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 -	210.50	114.37	- -	-	-	0/0
790	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH ,	07/2015	189.91 -	189.91	.00	- -	-	-	0/4
791	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	108.75	- -	-	-	3/4
792	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
793	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	280.00	472.00	02/2009 -	-	-	0/0
794	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	319.96	04/2009 -	08/2019	124(O) -	0/0
795	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	-	-	0/0
796	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	-	-	0/0
797	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	224.28	03/2008 -	09/2019	138(O) -	0/0
798	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019	136(O) -	0/0
799	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019	140(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
800	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019	-	0/0
801	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0
802	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019	112(O) -	0/0
803	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	120.86	05/2018 -	-	-	2/4
804	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	6.27	06/2018 -	-	-	0/4
805	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	6.62	06/2018 -	-	-	0/4
806	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	304.28	01/2019 -	-	-	2/4
807	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	61.74	11/2018 -	-	-	4/4
808	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	356.31	11/2018 -	-	-	2/4
809	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	201.56	05/2017 -	-	-	0/0
810	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	344.32	02/2011 -	-	-	0/0
811	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 307.47	307.47	239.76	02/2018 -	-	-	0/0
812	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	26.00	12/2018 -	-	-	1/4
813	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	61.74	06/2018 -	-	-	1/2
814	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	50.39	- -	-	-	1/4
815	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	15.27	12/2018 -	-	-	0/4
816	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	48.09	01/2016 -	-	-	1/4
817	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	.00	01/2016 -	-	-	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
818	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	292.24	01/2016 -	-	-	2/3
819	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	54.31	- -	06/2020	- -	0/4
820	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]PWD,ASSAM ,	09/2018	160.00 -	160.00	.50	09/2021 -	09/2021	0(O) -	0/0
821	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70(O) -	0/0
822	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	885.47	02/2013 -	-	-	0/0
823	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	329.40	05/2013 -	-	-	0/0
824	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
825	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
826	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	843.67	07/2013 -	-	-	0/0
827	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	566.60	11/2013 -	-	-	0/0
828	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	780.77	152.37	- -	-	-	0/0
829	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	278.45	08/2016 -	-	-	0/0
830	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	323.60	10/2016 -	-	-	0/0
831	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
832	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	214.34	04/2019 -	-	-	0/0
833	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	384.48	- -	01/2020	-	0/0
834	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24(O) -	0/0
835	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	131.71	- -	10/2020	-	0/0
836	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	113.26	- -	12/2019	-	0/0
837	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6(O) -	0/0
838	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
839	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	579.78	-	-	-	0/0
840	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	417.09	04/2018 -	-	-	0/0
841	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	-	-	-	0/0
842	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	369.77	113.67	-	-	-	0/0
843	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
844	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	596.44	07/2016 -	-	-	0/0
845	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
846	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	93.11	05/2016 -	-	-	0/0
847	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
848	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	267.22	05/2016 -	-	-	0/0
849	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	753.03	10/2016 -	-	-	0/0
850	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
851	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	280.00	11/2015 -	-	-	0/0
852	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	-	-	0/0
853	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	719.20	12/2016 -	-	-	0/0
854	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
855	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	05/2021	14(O) -	0/0
856	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54(O) -	0/0
857	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
858	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
859	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
860	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
861	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	.00	- -	-	-	0/0
862	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD,BIHAR ,	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019	0(O) -	0/0
863	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR ,	03/2018	153.24 -	153.24	2.06	- -	-	-	0/0
864	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR ,	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52(O) -	0/0
865	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	178.85	- -	-	-	0/0
866	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.70	12/2015 -	-	-	0/0
867	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	387.97	05/2018 10/2019	10/2019	17(O) 0	0/0
868	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 08/2018	08/2018	-	0/0
869	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 598.13	598.13	394.83	04/2018 03/2020	03/2020	23(O) 1	0/0
870	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	.00	- 03/2021	03/2021	- 0	0/0
871	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) _NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	-	-	0/0
872	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
873	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	153.33	- -	-	-	0/4
874	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	91.39	- -	-	-	2/4
875	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	290.59	219.47	- -	-	-	3/4
876	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	262.25	- -	-	-	0/0
877	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	259.46	- -	-	-	0/0
878	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	191.63	- -	-	-	0/0
879	PATRADEVI TO KARASWADA 4L - [N24001004]MORTH,GOA ,	03/2017	634.32 634.32	634.32	108.33	05/2020 -	05/2020	0(O) -	1/4
880	KARASWADA TO BAMBOLIM - [N24001005]MORTH,GOA ,	03/2017	852.67 852.67	852.67	108.04	12/2019 -	12/2019	0(O) -	1/4
881	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,187.21	09/2012 -	-	-	2/3
882	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	-	-	0/0
883	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-	-	0/3
884	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0
885	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	435.25	- -	08/2019	- -	0/0
886	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	140.44	- -	10/2019	- -	0/0
887	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	321.67	- -	09/2019	- -	0/0
888	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	357.12	- -	08/2019	- -	0/0
889	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	-	-	0/0
890	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	364.56	208.94	- -	12/2019	- -	0/0
891	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	75.08	- -	01/2020	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
892	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	262.83	- -	09/2019	- -	0/0
893	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	- -	0/0
894	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2(O) -	0/0
895	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	11/2019	25(O) -	0/0
896	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,052.21	1,080.00	- -	01/2021	- -	0/0
897	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	- -	01/2021	- -	0/0
898	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	.00	- -	07/2021	- -	0/0
899	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
900	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]PWD, GUJARAT ,	03/2016	223.67 -	223.67	112.81	02/2017 -	-	-	4/4
901	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD, GUJARAT , EPC	03/2016	208.34 -	208.34	112.87	02/2016 -	-	-	0/4
902	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD, GUJARAT , EPC	12/2017	867.97 -	867.97	90.63	11/2018 -	-	-	0/1
903	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE - [N24000923]PWD, GUJARAT , EPC	03/2018	464.07 399.35	464.07	14.17	11/2018 -	-	-	0/1
904	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD, GUJARAT , EPC	10/2018	400.76 386.19	400.76	4.45	05/2019 -	-	-	0/0
905	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD, GUJARAT , EPC	08/2017	962.43 887.21	962.43	45.70	03/2018 -	-	-	0/1
906	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118(O) -	0/0
907	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020	100(O) -	0/0
908	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
909	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	417.86	06/2016 -	08/2019	38(O) -	0/0
910	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28	448.92	07/2018 -	07/2019	12(O) -	0/0
911	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	971.24	04/2019 -	-	-	0/0
912	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
913	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6(O) -	0/0
914	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	1,004.67	.00	05/2019 -	-	-	0/0
915	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	480.73	03/2020 -	09/2019	-6(O) -	0/0
916	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	.00	- -	-	-	0/0
917	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	.00	- -	03/2020	- -	0/0
918	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	.00	- -	03/2020	- -	0/0
919	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	634.70	.00	- -	-	-	0/0
920	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	795.50	.00	- -	-	-	0/0
921	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	.00	- -	03/2020	- -	0/0
922	REHABILITATION AND UPGADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	.00	- -	06/2020	- -	0/0
923	REDESIGNING REHABILITATION AND UPGADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	.00	- -	03/2020	- -	0/0
924	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA ,	01/2017	247.25 -	247.25	144.00	03/2019 03/2020	09/2019	6(O) 0	0/0
925	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA ,	01/2017	276.01 -	276.01	180.95	03/2019 07/2019	07/2019	4(O) 0	0/0
926	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-	-	0/0
927	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	452.30	03/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
928	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	256.25	02/2019 -	06/2019	-	0/0
929	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	234.67	- -	09/2020	- -	0/0
930	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	07/2020	- -	0/0
931	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	179.17	- -	11/2019	- -	0/0
932	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15(O) -	0/0
933	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	.00	- -	05/2021	- -	0/0
934	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,580.88	07/2015 -	-	-	0/0
935	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
936	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
937	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,075.87	06/2014 -	-	-	0/0
938	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	301.68	06/2019 -	12/2020	18(O) -	0/0
939	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,154.18	12/2018 -	10/2019	10(O) -	0/0
940	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	305.75	- -	01/2021	- -	0/0
941	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	30.43	08/2018 -	-	-	1/4
942	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	.00	11/2018 -	-	-	0/4
943	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	.00	07/2019 -	07/2019	0(O) -	0/0
944	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
945	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	728.62	03/2019 -	07/2019	4(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
946	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	219.61	- -	12/2019	- -	0/0
947	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17(O) -	0/0
948	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	117.09	03/2020 -	09/2019	-6(O) -	0/0
949	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	7.21	03/2020 -	06/2019	-	0/0
950	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
951	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0
952	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- -	-	-	0/0
953	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD,JHARKHAND ,	03/2018	212.99 -	212.99	59.56	06/2020 -	06/2020	0(O) -	0/0
954	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18(O) -	3/3
955	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
956	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
957	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	453.95	09/2017 -	12/2019	27(O) -	0/0
958	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
959	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52(O) -	0/0
960	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,119.56	08/2018 -	03/2020	19(O) -	0/0
961	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20(O) -	0/0
962	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	16.09	03/2019 -	11/2020	20(O) -	0/0
963	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
964	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	608.81	04/2020 -	04/2020	0(O) -	0/0
965	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	254.96	03/2019 -	06/2020	15(O) -	0/0
966	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	803.81	08/2019 -	12/2020	16(O) -	0/0
967	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	551.42	03/2020 -	07/2020	4(O) -	0/0
968	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	604.76	03/2020 -	06/2020	3(O) -	0/0
969	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	.00	-	-	-	0/0
970	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	1,995.34	.00	-	11/2021	-	0/0
971	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,177.80	.00	-	-	-	0/0
972	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
973	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
974	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]PWD,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0
975	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
976	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
977	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHAARA SECTION - [N24001159]PWD,KARNATAKA ,	01/2018	159.70 -	159.70	21.16	07/2018 -	-	-	0/0
978	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
979	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
980	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA ,	03/2018	325.86 -	325.86	62.54	10/2018 -	-	-	0/0
981	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
982	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
983	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
984	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
985	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
986	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24(O) -	0/0
987	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
988	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24(O) -	0/0
989	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
990	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88(O) -	0/0
991	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27(O) -	0/0
992	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	788.62	- -	10/2019	- -	0/0
993	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	402.47	06/2018 -	01/2020	19(O) -	0/0
994	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	256.47	09/2017 -	06/2020	33(O) -	0/0
995	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,424.77	.00	- -	-	-	0/0
996	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
997	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/0
998	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
999	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	178.32	- -	03/2020	- -	0/0
1000	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020	36(O) -	0/0
1001	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1002	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54(O) -	0/0
1003	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	.00	04/2015 -	08/2019	52(O) -	0/0
1004	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	564.36	- -	-	-	0/0
1005	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	492.23	- -	-	-	0/0
1006	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	207.68	01/2020 -	01/2020	0(O) -	0/0
1007	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	412.39	02/2020 -	02/2020	0(O) -	0/0
1008	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	588.21	- -	06/2019	-	0/0
1009	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1010	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	-	-	0/0
1011	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	586.36	- -	06/2019	-	0/0
1012	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	-	0/0
1013	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADHYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	237.15	08/2017 -	02/2020	30(O) -	0/0
1014	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	100.96	01/2019 -	03/2019	-	0/0
1015	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1016	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1017	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	.00	09/2017 -	-	-	0/0
1018	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	- -	-	-	0/0
1019	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	.00	- -	08/2020	-	0/0
1020	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	- -	-	-	0/0
1021	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH ,	03/2018	162.56 -	162.56	66.95	03/2018 -	12/2019	21(O) -	0/0
1022	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH ,	03/2018	166.21 -	166.21	17.10	08/2018 -	06/2020	22(O) -	0/0
1023	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH ,	02/2018	169.63 -	169.63	7.10	03/2018 -	07/2020	28(O) -	0/0
1024	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH ,	11/2017	235.91 -	235.91	83.40	02/2018 -	11/2019	21(O) -	0/0
1025	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH ,	11/2017	184.62 -	184.62	54.49	02/2018 -	11/2019	21(O) -	0/0
1026	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH ,	03/2018	191.21 -	191.21	68.26	11/2019 -	11/2019	0(O) -	0/0
1027	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH ,	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39(O) -	0/0
1028	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH ,	03/2018	214.69 -	214.69	15.22	03/2018 -	11/2019	20(O) -	0/0
1029	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH ,	03/2018	217.22 -	217.22	12.39	08/2018 -	06/2020	22(O) -	0/0
1030	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH ,	03/2018	233.04 -	233.04	93.96	03/2018 -	11/2019	20(O) -	0/0
1031	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH ,	11/2017	249.05 -	249.05	100.10	07/2018 -	01/2020	18(O) -	0/0
1032	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH ,	11/2017	254.17 -	254.17	117.16	02/2018 -	11/2019	21(O) -	0/0
1033	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH ,	02/2018	279.44 -	279.44	53.59	03/2018 -	04/2020	25(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1034	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH ,	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10(O) -	0/0
1035	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH ,	01/2017	373.82 -	373.82	116.33	09/2019 -	05/2020	8(O) -	0/0
1036	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH ,	01/2016	809.16 -	809.16	198.65	07/2018 -	02/2020	19(O) -	0/0
1037	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH ,	03/2016	877.79 -	877.79	383.94	06/2019 -	11/2019	5(O) -	0/0
1038	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH ,	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	11(O) -	0/0
1039	ANJANGAON TO MAH/MP BORDER - [N24001007]MORTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	173.80	06/2019 -	-	-	0/4
1040	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH ,	11/2017	392.33 -	392.33	224.94	03/2018 -	11/2019	20(O) -	0/0
1041	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019	76(O) -	0/0
1042	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	750.38	06/2014 -	03/2020	69(O) -	0/0
1043	WIDENING OF KHED-SINAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1044	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	52.00	-	-	-	0/4
1045	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1046	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	259.50	-	-	-	3/4
1047	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	-	-	-	0/0
1048	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	-	-	-	0/0
1049	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	83.11	-	-	-	0/0
1050	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	.00	05/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1051	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA ,	09/2015	414.51 -	414.00	529.62	05/2018 -	06/2020	25(O) -	0/0
1052	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	05/2018 -	06/2020	25(O) -	0/0
1053	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1054	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA ,	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31(O) -	0/0
1055	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA ,	12/2015	649.50 -	649.50	129.48	03/2019 -	04/2021	25(O) -	0/0
1056	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA ,	08/2015	505.00 -	505.00	347.91	05/2018 -	05/2020	24(O) -	0/0
1057	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019	24(O) -	0/0
1058	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	708.62	11/2016 -	05/2020	42(O) -	0/0
1059	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA ,	09/2005	168.00 -	168.00	226.24	06/2006 -	-	-	0/0
1060	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	3,424.19	01/2018 -	-	-	0/0
1061	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1062	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA ,	03/2016	197.69 -	197.69	22.27	07/2018 -	-	-	0/0
1063	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA ,	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17(O) 17	0/0
1064	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA ,	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17(O) 17	0/0
1065	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD, MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	726.85	- -	-	-	0/0
1066	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD, MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	- -	-	-	0/0
1067	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	.00	- -	07/2021	- -	0/0
1068	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	07/2021	- -	0/0
1069	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1070	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA ,	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8(O) -	0/0
1071	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA ,	11/2016	290.73 -	290.73	174.12	- -	05/2019	-	0/0
1072	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA ,	01/2017	244.90 -	244.90	219.09	05/2019 -	09/2019	4(O) -	0/0
1073	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA ,	02/2017	904.16 -	904.16	607.37	02/2020 -	05/2020	3(O) -	0/0
1074	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	02/2020	-1(O) -	0/0
1075	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1076	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2(O) -	0/0
1077	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5(O) -	0/0
1078	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	480.96	03/2017 -	11/2020	44(O) -	0/0
1079	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA ,	03/2017	296.19 -	254.00	248.60	03/2020 -	09/2019	-6(O) -	0/0
1080	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5(O) -	0/0
1081	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA ,	12/2017	404.94 448.18	404.94	90.86	- -	10/2020	- -	0/0
1082	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA ,	01/2018	607.00 -	607.00	55.06	- -	08/2021	- -	0/0
1083	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA ,	01/2018	621.00 -	621.00	212.24	- -	04/2021	- -	0/0
1084	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI, MAHARASHTRA , EPC	03/2018	291.53 -	291.53	29.25	- -	11/2020	- -	0/0
1085	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI, MAHARASHTRA , EPC	03/2018	289.21 -	289.21	19.78	- -	11/2020	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1086	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	14.11	- -	07/2021	- -	0/0
1087	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	642.13	288.84	- -	12/2020	- -	0/0
1088	SARSAM TO KOTHARI - [N24001002]MORTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	64.01	07/2019 -	07/2019	0(O) -	0/4
1089	AKOLA TO AKOT - [N24001003]MORTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	37.05	06/2019 -	-	-	0/4
1090	AKOT TO ANJANGAON - [N24001006]MORTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	111.98	06/2019 -	-	-	0/4
1091	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	101.79	05/2019 -	12/2019	7(O) -	0/0
1092	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	136.43	05/2019 -	12/2019	7(O) -	0/4
1093	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	184.08	05/2019 -	-	-	0/4
1094	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	260.00	06/2019 -	10/2019	4(O) -	0/4
1095	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	84.00	06/2019 -	06/2020	12(O) -	0/0
1096	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	184.75	06/2019 -	12/2019	6(O) -	0/0
1097	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	156.29	06/2019 -	12/2019	6(O) -	0/0
1098	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	231.90	06/2019 -	-	-	0/0
1099	DAHEGAON TO KUHI - [N24001017]MORTH,MAHARASHTRA ,	01/2017	228.89 228.89	228.89	115.00	06/2019 -	-	-	3/4
1100	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	690.60	06/2019 -	-	-	0/0
1101	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	243.34	06/2019 -	08/2019	2(O) -	0/4
1102	AMDHI TO SAONER - [N24001021]MORTH,MAHARASHTRA ,	01/2017	396.91 396.91	396.91	247.48	06/2019 -	08/2019	2(O) -	3/4
1103	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA ,	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12(O) -	1/4
1104	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	149.81	06/2019 -	12/2019	6(O) -	0/4
1105	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA ,	01/2017	457.52 457.52	457.52	202.31	07/2019 -	07/2020	12(O) -	2/4
1106	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA ,	01/2017	355.17 355.17	355.17	141.87	07/2019 -	12/2019	5(O) -	3/4
1107	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA ,	01/2017	376.19 376.19	376.19	23.03	05/2019 -	05/2020	12(O) -	1/4
1108	SHAHPUR PATGAON SECTION I - [N24001027]MORTH,MAHARASHTRA ,	01/2018	150.79 150.79	150.79	21.42	12/2019 -	12/2019	0(O) -	1/4
1109	PATGAON KHOPOLI SECTION I - [N24001028]MORTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	15.57	12/2019 -	12/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1110	AHMADPUR TO PIMPLA - [N24001029]MORTH,MAHARASHTRA ,	01/2017	422.38 422.38	422.38	148.58	08/2019 -	08/2019	0(O) -	2/4
1111	PIMPLA TO MANJARSUMBHA - [N24001030]MORTH,MAHARASHTRA ,	01/2017	595.77 595.77	595.77	118.44	08/2019 -	08/2019	0(O) -	2/4
1112	MANJUSUMBA TO CHUMBALI - [N24001031]MORTH,MAHARASHTRA ,	01/2017	228.54 228.54	228.54	92.30	08/2019 -	08/2019	0(O) -	2/4
1113	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	155.78	05/2019 -	05/2020	12(O) -	0/4
1114	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MORTH,MAHARASHTRA ,	01/2017	486.19 486.19	486.19	210.29	07/2019 -	07/2019	0(O) -	2/4
1115	PARTUR TO MAJALGAON - [N24001034]MORTH,MAHARASHTRA ,	01/2017	420.57 420.57	420.57	157.39	07/2019 -	07/2019	0(O) -	2/4
1116	MANSAR TO SALAIKHURD - [N24001035]MORTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	102.13	12/2019 -	12/2019	0(O) -	0/4
1117	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	310.33	07/2019 -	07/2019	0(O) -	0/0
1118	KAIJ TO KUSALAM - [N24001037]MORTH,MAHARASHTRA ,	01/2017	554.78 554.78	554.78	157.90	07/2019 -	07/2019	0(O) -	2/4
1119	MAHAD TO RAIGAD FORT - [N24001038]MORTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	7.34	05/2020 -	05/2020	0(O) -	0/4
1120	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA ,	01/2017	356.66 356.66	356.66	24.88	- -	-	-	0/4
1121	JAHIRABAD TO LATUR - [N24001040]MORTH,MAHARASHTRA ,	01/2017	461.96 461.96	461.96	127.43	11/2019 -	11/2019	0(O) -	2/4
1122	SHIROD SHAHPURER TO NANDED - [N24001041]MORTH,MAHARASHTRA ,	01/2017	211.34 211.34	211.34	100.83	07/2019 -	07/2019	0(O) -	2/4
1123	SALAIKHURD TO TIRORA - [N24001042]MORTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019	0(O) -	0/4
1124	NILAJPHATA TO BHANDARA - [N24001043]MORTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020	0(O) -	0/4
1125	KALMAB TO RALEGAON - [N24001044]MORTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	294.91	06/2019 -	-	-	0/4
1126	JALGAON TO BHADGAON - [N24001045]MORTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	106.59	11/2019 -	11/2019	0(O) -	0/4
1127	RALEGAON TO RAMTIRTH - [N24001046]MORTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	106.69	07/2019 -	07/2019	0(O) -	0/4
1128	BHADGAON TO CHALISGAON - [N24001047]MORTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	150.00	11/2019 -	11/2019	0(O) -	0/0
1129	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	85.51	07/2019 -	07/2019	0(O) -	0/0
1130	KARAD TO VITA - [N24001049]MORTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	66.04	12/2019 -	12/2019	0(O) -	0/4
1131	VITA TO NAGAJ - [N24001050]MORTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019	0(O) -	0/4
1132	NALDURG TO AKKALKOT - [N24001051]MORTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	224.39	12/2019 -	12/2019	0(O) -	0/4
1133	SANGOLA TO JATH - [N24001052]MORTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	62.15	12/2019 -	12/2019	0(O) -	0/4
1134	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	73.97	06/2019 -	06/2020	12(O) -	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1135	TASGAON TO SHIRDHON - [N24001054]MORTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	93.73	11/2019 -	11/2019	0(O) -	0/4
1136	HELWAK TO KARAD - [N24001055]MORTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	111.40	07/2019 -	07/2019	0(O) -	0/4
1137	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	224.01	07/2019 -	07/2019	0(O) -	0/0
1138	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	12.00	06/2019 -	06/2020	12(O) -	0/4
1139	KARWANDI TO RAJURI - [N24001058]MORTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	85.47	12/2019 -	12/2019	0(O) -	0/4
1140	SHIVUR TO YEOLA - [N24001059]MORTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	7.45	12/2019 -	12/2019	0(O) -	0/4
1141	PALPHATA TO PHULAMBARI - [N24001060]MORTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	50.23	12/2019 -	12/2019	0(O) -	0/4
1142	CHIKALI TO DHAD - [N24001061]MORTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	21.00	12/2019 -	12/2019	0(O) -	0/4
1143	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MORTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	58.66	12/2019 -	12/2019	0(O) -	0/4
1144	WADIGODRI TO DHANGRIPIPRI - [N24001063]MORTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	57.23	02/2020 -	02/2020	0(O) -	0/4
1145	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MORTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	58.77	02/2020 -	02/2020	0(O) -	0/4
1146	PARBHANI TO GANGKHED - [N24001065]MORTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	23.85	12/2019 -	12/2019	0(O) -	0/4
1147	LATUR TO PANGAON - [N24001066]MORTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	85.48	12/2019 -	12/2019	0(O) -	0/4
1148	OMREGA TO AUSA - [N24001067]MORTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	72.24	12/2019 -	12/2019	0(O) -	0/4
1149	WASHIM TO DASTAPUR - [N24001068]MORTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	25.45	12/2019 -	12/2019	0(O) -	1/4
1150	NANDED TO JALKOT - [N24001069]MORTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	55.50	09/2019 -	09/2019	0(O) -	1/4
1151	DASTAPUR TO KARANJA - [N24001070]MORTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	89.15	12/2019 -	12/2019	0(O) -	2/4
1152	JALKOT TO TOGRI - [N24001071]MORTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020	0(O) -	0/4
1153	KHERDA TO NAGZARI - [N24001072]MORTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	66.50	12/2019 -	12/2019	0(O) -	0/4
1154	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020	0(O) -	0/0
1155	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	65.20	12/2019 -	12/2019	0(O) -	0/0
1156	OSMANNAGAR TO KUNDAL - [N24001075]MORTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	44.02	08/2020 -	08/2020	0(O) -	0/4
1157	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	106.46	12/2019 -	12/2019	0(O) -	0/0
1158	KUNDAL TO WAZAR - [N24001077]MORTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	97.75	12/2019 -	12/2019	0(O) -	2/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1159	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	13.50	12/2019 -	12/2019	0(O) -	0/0
1160	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MORTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	64.97	06/2020 -	06/2020	0(O) -	1/4
1161	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	15.50	12/2019 -	12/2019	0(O) -	0/0
1162	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MORTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	36.30	12/2019 -	12/2019	0(O) -	1/4
1163	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	21.42	12/2019 -	12/2019	0(O) -	0/0
1164	CHIKLI TO TAKARKHED - [N24001083]MORTH,MAHARASHTRA ,	03/2018	393.10 393.10	393.10	111.97	12/2019 -	12/2019	0(O) -	2/4
1165	PAHUR TO BODHWAD - [N24001084]MORTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	34.23	05/2020 -	05/2020	0(O) -	0/4
1166	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	67.26	06/2019 -	12/2019	6(O) -	0/4
1167	BODHWAD TO STATE BORDER - [N24001086]MORTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	96.95	07/2019 -	07/2019	0(O) -	0/4
1168	MANGRUPHIR TO MAHAN - [N24001087]MORTH,MAHARASHTRA ,	03/2018	222.13 222.13	222.13	23.36	11/2019 -	11/2019	0(O) -	0/4
1169	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	45.69	12/2019 -	12/2019	0(O) -	0/0
1170	MALEGAON TO RISOD - [N24001089]MORTH,MAHARASHTRA ,	02/2018	303.24 303.24	303.24	93.97	12/2019 -	12/2019	0(O) -	0/4
1171	KOLDE TO KHETIYA - [N24001090]MORTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	175.93	07/2019 -	07/2019	0(O) -	0/4
1172	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIKA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019	0(O) -	0/0
1173	SATARA TO MHASWAD - [N24001092]MORTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	203.42	07/2019 -	07/2019	0(O) -	0/4
1174	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	16.32	12/2019 -	12/2019	0(O) -	0/0
1175	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	15.94	03/2019 -	12/2019	9(O) -	0/0
1176	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	179.77	- -	-	-	0/0
1177	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	23.71	03/2019 -	12/2019	9(O) -	0/0
1178	SELDOH TO PANVAR - [N24001097]MORTH,MAHARASHTRA ,	07/2018	404.33 404.33	404.33	14.19	05/2020 -	05/2020	0(O) -	0/4
1179	WARDHA TO HINGAGHAT - [N24001098]MORTH,MAHARASHTRA ,	01/2018	216.90 216.90	216.90	20.00	12/2019 -	12/2019	0(O) -	1/4
1180	MHASWAD TO TEMBHURNI - [N24001099]MORTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	151.71	07/2019 -	07/2019	0(O) -	0/4
1181	AHMEDNAGAR TO BARAMATI - [N24001100]MORTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	331.50	08/2019 -	08/2019	0(O) -	0/4
1182	KURUDWADI TO PANDHARPUR - [N24001101]MORTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	148.17	07/2019 -	07/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1183	PANDHARPUR TO SANGOLA - [N24001102]MORTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	07/2019	0(O) -	0/4
1184	SARAD VANI PIMPALGAON - [N24001103]MORTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	103.63	07/2019 -	07/2019	0(O) -	0/4
1185	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12(O) -	2/4
1186	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	156.72	03/2019 -	-	-	0/4
1187	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	.00	03/2018 -	12/2019	21(O) -	0/4
1188	PANCHARAL TO MANDANGHAR - [N24001107]MORTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020	0(O) -	0/4
1189	CHALISGAON TO NANDGAON - [N24001108]MORTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	68.89	12/2019 -	12/2019	0(O) -	0/4
1190	KUSUMBA TO MALEGAON - [N24001109]MORTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	58.02	12/2019 -	12/2019	0(O) -	0/4
1191	BAMNI TO NAVAEGAON - [N24001110]MORTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	76.29	04/2020 -	04/2020	0(O) -	1/4
1192	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	23.73	04/2019 -	04/2020	12(O) -	0/4
1193	NASRATPUR TO BARASGAON - [N24001112]MORTH,MAHARASHTRA ,	07/2016	406.54 406.54	406.54	142.00	09/2019 -	09/2019	0(O) -	2/4
1194	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	24.00	09/2018 -	04/2021	31(O) -	0/4
1195	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA ,	01/2017	1,202.52 1,202.52	1,202.52	652.90	12/2019 -	03/2020	3(O) -	1/4
1196	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA ,	01/2017	1,598.47 1,598.47	1,598.47	746.91	11/2019 -	03/2020	4(O) -	1/4
1197	GADCHIROLI TO MUL - [N24001116]MORTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	159.31	06/2019 -	-	-	2/4
1198	MUL TO CHANDRAPUR - [N24001117]MORTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019	0(O) -	1/4
1199	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA ,	01/2017	362.96 362.96	362.96	29.83	06/2019 -	11/2019	5(O) -	0/4
1200	NAGBHID TO ARMORI - [N24001119]MORTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	203.91	07/2019 -	07/2019	0(O) -	0/4
1201	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	130.85	02/2019 -	02/2020	12(O) -	0/4
1202	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	83.81	11/2018 -	11/2019	12(O) -	0/4
1203	PAITHAN TO SHIRUR - [N24001122]MORTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	118.00	06/2019 -	-	-	0/4
1204	SHIRUR TO KHARDA - [N24001123]MORTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	147.79	06/2019 -	-	-	0/4
1205	AURANGABAD TO SILLOD - [N24001124]MORTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	91.30	06/2019 -	-	-	0/4
1206	SILLOD TO FARDAPUR - [N24001125]MORTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	44.03	06/2019 -	-	-	0/4
1207	FARDAPUR TO JALGAON - [N24001126]MORTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	66.10	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1208	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	280.69	06/2019 -	-	-	0/0
1209	BHOKAR TO SARSAM - [N24001128]MORTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	155.64	07/2019 -	07/2019	0(O) -	0/4
1210	BHOGAN KHURD TO KASHEDI - [N24001132]MORTH,MAHARASHTRA ,	09/2017	743.21 743.21	743.21	52.87	06/2021 -	06/2021	0(O) -	1/4
1211	PARSHURAM GHAT TO ARAWALI - [N24001133]MORTH,MAHARASHTRA ,	04/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019	-1(O) -	1/4
1212	KANTE TO WAKED - [N24001134]MORTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.02	1,230.02	567.61	11/2019 -	11/2019	0(O) -	1/4
1213	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	618.00	02/2019 -	-	-	0/0
1214	TALGAON TO KALMATH - [N24001136]MORTH,MAHARASHTRA ,	10/2016	904.70 904.70	904.70	604.05	03/2020 -	03/2020	0(O) -	2/4
1215	KALMATH TO ZARAP - [N24001137]MORTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.13	1,338.13	959.51	03/2020 -	03/2020	0(O) -	3/5
1216	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA ,	02/2017	205.72 205.72	205.72	26.42	06/2019 -	06/2020	12(O) -	1/4
1217	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA ,	02/2018	355.99 355.99	355.99	95.97	12/2019 -	12/2019	0(O) -	0/0
1218	WARDHA TO ARVI - [N24001150]MORTH,MAHARASHTRA ,	02/2018	313.58 313.58	313.58	4.86	04/2020 -	04/2020	0(O) -	0/4
1219	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	119.56	10/2018 -	10/2021	36(O) -	1/4
1220	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]PWD,MANIPUR ,	10/2016	235.31 -	235.31	74.49	11/2020 -	11/2020	0(O) -	0/0
1221	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	475.02	05/2018 -	09/2019	16(O) -	0/0
1222	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	27.90	- -	09/2021	- -	0/4
1223	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	42.66	05/2019 -	07/2019	2(O) -	0/0
1224	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019	105(O) -	0/0
1225	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110(O) -	0/0
1226	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	296.28	10/2010 -	06/2020	116(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1227	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	.00	09/2019 -	09/2019	0(O) -	0/0
1228	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	.00	09/2019 -	09/2019	0(O) -	0/0
1229	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	.00	09/2019 -	09/2019	0(O) -	0/0
1230	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	.00	09/2019 -	09/2019	0(O) -	0/0
1231	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	.00	09/2019 -	09/2019	0(O) -	0/0
1232	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	.00	09/2019 -	09/2019	0(O) -	0/0
1233	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	.00	09/2019 -	09/2019	0(O) -	0/0
1234	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	.00	09/2019 -	09/2019	0(O) -	0/0
1235	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM ,	08/2010	186.96 -	305.61	269.07	09/2014 -	12/2019	63(O) -	0/0
1236	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128(O) -	0/0
1237	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	303.71	08/2011 -	-	-	2/2
1238	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1239	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69(O) -	0/0
1240	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81(O) -	0/0
1241	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-	-	0/0
1242	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1243	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,275.00	-	02/2020	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1244	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,294.47	.00	- -	-	-	0/0
1245	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	998.70	.00	- -	-	-	0/0
1246	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1247	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	187.25	08/2016 -	08/2019	36(O) -	0/4
1248	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	229.11	08/2016 -	08/2019	36(O) -	0/4
1249	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	153.61	08/2016 -	08/2019	36(O) -	0/4
1250	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	112.38	04/2017 -	-	-	1/4
1251	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	116.06	09/2018 -	-	-	0/4
1252	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	-	-	0/0
1253	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	.00	09/2018 -	-	-	0/0
1254	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 -	-	-	0/4
1255	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	-	-	0/0
1256	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	4.38	09/2018 -	-	-	0/2
1257	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	2.11	09/2018 -	-	-	0/2
1258	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	9.21	09/2018 -	-	-	0/2

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1259	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	6.75	09/2018 -	-	-	0/2
1260	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	3.27	09/2018 -	-	-	0/2
1261	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	6.86	09/2018 -	-	-	1/2
1262	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	-	-	1/2
1263	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/0
1264	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/0
1265	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]PWD,NAGALAND ,	10/2016	167.62 -	167.62	34.89	12/2020 -	12/2020	0(O) -	0/0
1266	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]PWD,NAGALAND ,	10/2016	172.63 -	172.63	35.30	12/2020 -	12/2020	0(O) -	0/0
1267	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]PWD,NAGALAND ,	11/2016	336.25 -	336.25	44.91	09/2019 -	09/2019	0(O) -	0/0
1268	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]PWD,NAGALAND ,	03/2017	217.35 -	217.35	33.02	11/2020 -	11/2020	0(O) -	0/0
1269	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]PWD,NAGALAND ,	03/2019	237.51 -	237.51	.00	12/2022 -	12/2022	0(O) -	0/0
1270	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,930.61	09/2014 -	-	-	0/0
1271	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,864.34	06/2014 -	-	-	0/0
1272	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1273	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	268.01	10/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1274	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1275	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1276	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	.00	- -	04/2020	-	0/0
1277	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	- -	11/2019	-	0/0
1278	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22(O) -	0/0
1279	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52(O) -	0/0
1280	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	.00	- -	07/2019	-	0/0
1281	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	.00	08/2019 -	08/2019	0(O) -	0/0
1282	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	468.18	- -	07/2020	-	0/0
1283	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43(O) -	0/0
1284	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1285	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1286	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.31	137.43	10/2017 -	-	-	0/0
1287	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	268.27	05/2016 -	-	-	0/0
1288	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1289	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1290	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1291	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	221.91	03/2020 -	03/2021	12(O) -	0/0
1292	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 -	11/2020	40(O) -	0/0
1293	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	34.36	- -	07/2020	- -	0/0
1294	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	- -	-	-	0/0
1295	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	.00	- -	05/2020	- -	0/0
1296	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	.00	- -	05/2020	- -	0/0
1297	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1298	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	.00	- -	08/2021	- -	0/0
1299	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	08/2021	- -	0/0
1300	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	29.45	- -	03/2020	- -	0/0
1301	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1302	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1303	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	06/2021	- -	0/0
1304	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	.00	- -	04/2021	- -	0/0
1305	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1306	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1307	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1308	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1309	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1310	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1311	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1312	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIP IN ODISHA - [N24000918]MORTH,ODISHA ,	07/2013	251.92 -	251.92	225.98	10/2015 -	-	-	0/0
1313	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIP IN ODISHA - [N24000919]MORTH,ODISHA ,	07/2013	265.35 -	265.35	247.56	10/2015 -	-	-	0/0
1314	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA - [N24000924]MORTH,ODISHA ,	03/2015	229.29 -	229.29	163.40	11/2015 -	-	-	0/0
1315	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	666.72	- 09/2019	-	-	0/0
1316	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	1,086.49	- -	-	-	0/0
1317	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	904.82	722.92	- 12/2019	-	-	0/0
1318	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.09	- -	03/2020	-	0/0
1319	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019	24(O) 0	0/0
1320	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	642.01	- -	-	-	0/0
1321	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019	0(O) 0	0/0
1322	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	1,004.18	- -	04/2020	-	0/0
1323	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	76.83	03/2020 -	04/2020	1(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1324	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	261.76	40.89	- -	01/2021	- -	0/0
1325	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	37.68	- -	-	-	0/0
1326	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	9.03	- -	01/2020	-	0/0
1327	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB ,	03/2018	322.48 -	322.48	48.73	07/2020 -	07/2020	0(O) -	0/0
1328	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB ,	03/2018	173.24 -	173.24	10.97	06/2020 -	06/2020	0(O) -	0/0
1329	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD,PUNJAB ,	03/2018	293.10 -	293.10	10.26	08/2020 -	08/2020	0(O) -	0/0
1330	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB ,	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019	0(O) -	0/0
1331	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]PWD,PUNJAB ,	03/2018	170.57 -	170.57	46.23	11/2020 -	11/2020	0(O) -	0/0
1332	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1333	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1334	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1335	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1336	REHABILITATION AND UPGADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1337	REHABILITATION AND UPGADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1338	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1339	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.00	06/2018 -	07/2019	13(O) -	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1340	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	297.72	09/2016 -	-	-	0/0
1341	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	605.33	10/2017 -	-	-	0/0
1342	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	-	-	0/0
1343	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	834.75	04/2018 -	-	-	0/0
1344	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1345	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70(O) -	0/4
1346	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1347	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	257.52	- -	-	-	0/0
1348	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGLAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3(O) -	0/0
1349	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5(O) -	0/0
1350	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	09/2019	3(O) -	0/0
1351	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	661.85	- -	11/2019	- -	0/0
1352	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1353	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	206.14	01/2019 -	-	-	0/0
1354	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	174.79	- -	05/2020	- -	0/0
1355	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	886.00	- -	12/2019	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1356	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1357	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	670.00	04/2020 -	11/2019	-5(O) -	0/0
1358	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	329.90	10/2017 -	11/2020	37(O) -	0/0
1359	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	12/2020	- -	0/0
1360	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	242.53	- -	09/2020	- -	0/0
1361	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1362	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	73.00	- -	-	-	0/0
1363	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	.00	- -	-	-	0/0
1364	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	121.47	- -	-	-	0/0
1365	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD,RAJASTHAN ,	11/2017	187.82 -	187.82	45.29	04/2018 -	-	-	1/4
1366	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD,RAJASTHAN ,	10/2014	382.81 -	382.81	333.27	01/2015 -	-	-	3/4
1367	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD,RAJASTHAN ,	01/2017	179.32 -	179.32	93.64	11/2017 -	-	-	2/4
1368	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD,RAJASTHAN ,	03/2016	155.77 -	155.77	97.42	09/2016 -	-	-	3/4
1369	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD,RAJASTHAN ,	01/2012	378.07 478.73	478.73	188.98	01/2014 -	-	-	1/4
1370	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD,RAJASTHAN ,	10/2012	511.21 -	511.21	814.79	10/2013 -	-	-	3/4
1371	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD,RAJASTHAN ,	03/2009	501.00 671.54	671.54	659.98	09/2013 -	-	-	3/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1372	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD,RAJASTHAN ,	11/2017	163.95 -	163.95	51.40	04/2018 -	-	-	3/4
1373	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD,RAJASTHAN ,	02/2018	370.30 -	370.30	176.00	06/2018 -	-	-	1/4
1374	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD,RAJASTHAN ,	02/2018	341.79 -	341.79	97.97	05/2018 -	-	-	1/4
1375	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD,RAJASTHAN ,	12/2015	621.43 -	621.43	405.10	10/2016 -	-	-	3/4
1376	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD,RAJASTHAN ,	01/2017	163.54 -	163.54	84.68	07/2017 -	-	-	2/4
1377	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76(O) -	0/0
1378	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 203.26	166.27	132.27	08/2013 -	-	-	0/0
1379	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82(O) 0	0/0
1380	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	388.00	78.33	10/2017 -	-	-	1/4
1381	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	78.78	11/2017 -	-	-	1/4
1382	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	77.39	- -	-	-	0/0
1383	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	30.70	11/2017 -	-	-	1/4
1384	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1385	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,330.29	12/2013 -	-	-	0/0
1386	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	326.23	06/2013 -	-	-	0/0
1387	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	-	-	0/0
1388	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1389	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1390	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1391	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1392	CONSTRUCTION OF PAVED SHOULDERS INCULding STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1393	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	966.02	11/2017 -	08/2019	21(O) -	0/0
1394	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	96.48	12/2017 -	08/2019	20(O) -	0/0
1395	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1396	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	627.66	07/2008 -	-	-	0/0
1397	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	304.69	08/2018 -	03/2020	19(O) -	0/0
1398	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	431.21	07/2018 -	05/2020	22(O) -	0/0
1399	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	69.68	03/2020 -	03/2020	0(O) -	0/0
1400	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	405.31	07/2016 -	05/2020	46(O) -	0/0
1401	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	.00	08/2017 -	09/2020	37(O) -	0/0
1402	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	95.96	09/2017 -	11/2019	26(O) -	0/0
1403	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	.00	09/2017 -	08/2020	35(O) -	0/0
1404	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	92.44	- -	03/2020	- -	0/0
1405	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	- -	02/2021	- -	0/0
1406	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	36.14	- -	11/2020	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1407	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	59.22	- -	11/2020	-	0/0
1408	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	633.55	.00	- -	-	-	0/0
1409	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,016.92	.00	- -	04/2021	-	0/0
1410	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,065.96	.00	- -	-	-	0/0
1411	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019	39(O) -	0/0
1412	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1413	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	.00	02/2017 -	-	-	0/1
1414	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	.00	01/2017 -	-	-	0/0
1415	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	691.30	11/2018 -	07/2019	8(O) -	0/0
1416	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1417	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	.00	- -	-	-	0/0
1418	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	.00	- -	-	-	0/0
1419	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	.00	- -	-	-	0/0
1420	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1421	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA ,	10/2016	298.32 -	298.32	62.22	02/2019 -	12/2019	10(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1422	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA ,	10/2016	248.83 -	248.83	79.02	03/2019 -	12/2019	9(O) -	0/0
1423	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA ,	01/2017	244.54 -	244.54	122.31	05/2019 -	07/2019	2(O) -	0/0
1424	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]PWD,TELANGANA ,	01/2017	196.52 -	196.52	92.88	10/2019 -	10/2019	0(O) -	0/0
1425	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]PWD,TELANGANA ,	01/2017	283.00 -	283.00	121.47	12/2019 -	12/2019	0(O) -	0/0
1426	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA ,	01/2017	359.27 -	359.27	200.24	05/2019 -	08/2019	3(O) -	0/0
1427	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA ,	01/2017	300.00 -	300.00	83.83	05/2019 -	12/2019	7(O) -	0/0
1428	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]PWD,TELANGANA ,	01/2018	283.15 -	283.15	32.04	05/2020 -	05/2020	0(O) -	0/0
1429	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD,TELANGANA ,	01/2018	230.03 -	230.03	80.71	12/2019 -	12/2019	0(O) -	0/0
1430	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD,TELANGANA ,	02/2018	206.13 -	206.13	94.93	06/2020 -	06/2020	0(O) -	0/0
1431	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD,TELANGANA ,	02/2018	294.13 -	294.13	23.54	11/2019 -	11/2019	0(O) -	0/0
1432	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD,TELANGANA ,	02/2018	220.28 -	220.28	7.40	11/2019 -	11/2019	0(O) -	0/0
1433	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]PWD,TELANGANA ,	02/2018	426.52 -	426.52	134.38	04/2020 -	04/2020	0(O) -	0/0
1434	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD,TELANGANA ,	03/2018	322.81 -	322.81	.34	09/2020 -	09/2020	0(O) -	0/0
1435	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD,TELANGANA ,	03/2018	626.76 -	626.76	46.62	07/2020 -	07/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1436	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD,TELANGANA ,	01/2017	605.08 -	605.08	213.00	10/2019 -	10/2019	0(O) -	0/0
1437	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA ,	03/2018	192.67 -	192.67	.00	07/2019 -	07/2019	0(O) -	0/0
1438	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA ,	01/2019	193.19 -	193.19	.00	- -	-	-	0/0
1439	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	297.12	03/2018 12/2019	-	-	3/4
1440	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]PWD,TRIPURA ,	10/2016	171.90 -	171.90	14.17	08/2020 -	08/2020	0(O) -	0/0
1441	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1442	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1443	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	459.07	01/2014 -	-	-	0/0
1444	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-	-	0/0
1445	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1446	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1447	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	433.68	01/2016 -	-	-	0/0
1448	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	232.93	09/2016 -	11/2018	-	0/0
1449	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	207.94	01/2016 -	-	-	0/0
1450	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	633.24	01/2016 -	-	-	0/0
1451	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019	29(O) -	0/0
1452	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2017 -	-	-	0/0
1453	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	839.63	03/2018 -	-	-	0/0
1454	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1455	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1456	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1457	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1458	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1459	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1460	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	86.63	08/2015 -	09/2019	49(O) -	0/0
1461	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	623.53	- -	-	-	0/0
1462	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	988.72	06/2019 -	-	-	0/0
1463	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	632.21	04/2019 -	-	-	0/0
1464	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	92.37	- -	-	-	0/0
1465	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1466	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	276.87	04/2019 -	-	-	0/0
1467	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	532.53	04/2019 -	-	-	0/0
1468	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	938.03	- -	02/2020	- -	0/0
1469	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	21.46	- -	07/2020	- -	0/0
1470	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	278.92	- -	04/2020	- -	0/0
1471	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7(O) -	0/0
1472	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	433.62	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1473	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1474	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8(O) -	0/0
1475	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5(O) -	0/0
1476	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2(O) -	0/0
1477	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020	0(O) -	0/0
1478	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	410.09	- -	05/2020	-	0/0
1479	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1480	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1481	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1482	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1483	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1484	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0
1485	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	-	-	0/0
1486	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0
1487	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1488	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	1,025.80	46.29	- -	-	-	0/0
1489	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	1,115.28	113.90	- -	-	-	0/0
1490	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	.00	- -	-	-	0/0
1491	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	.00	- -	-	-	0/0
1492	REHABILITATION AND UPGADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH ,	03/2016	208.50 -	208.50	102.98	11/2019 -	11/2019	0(O) -	0/0
1493	REHABILITATION AND UPGADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	67.87	03/2020 -	03/2020	0(O) -	0/0
1494	REHABILITATION AND UPGADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	125.09	09/2019 -	09/2019	0(O) -	0/0
1495	REHABILITATION AND UPGADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	171.00	01/2020 -	01/2020	0(O) -	0/0
1496	REHABILITATION AND UPGADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	132.45	10/2018 -	07/2019	9(O) -	0/0
1497	REHABILITATION AND UPGADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.00	454.41	03/2017 -	07/2019	28(O) -	0/0
1498	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	86.63	08/2015 -	07/2019	47(O) -	0/0
1499	REHABILITATION AND UPGADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH ,	03/2016	249.50 -	249.50	190.10	05/2019 -	-	-	0/0
1500	REHABILITATION AND UPGADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD,UTTAR PRADESH ,	10/2016	239.63 -	239.63	197.77	02/2019 -	-	-	0/0
1501	REHABILITATION AND UPGADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH ,	03/2016	599.34 -	599.34	376.71	01/2020 -	01/2020	0(O) -	0/0
1502	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	409.17	10/2013 -	02/2020	76(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1503	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	278.01	- -	10/2019	- -	0/0
1504	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	610.71	- -	02/2020	- -	0/0
1505	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 -	02/2020	19(O) -	0/0
1506	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	8.68	05/2018 -	-	-	0/4
1507	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	75.19	06/2018 -	-	-	1/4
1508	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	76.48	05/2018 -	-	-	1/4
1509	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019	0(O) -	0/0
1510	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019	0(O) -	0/0
1511	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019	0(O) -	0/0
1512	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6(O) -	0/0
1513	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019	0(O) -	0/0
1514	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019	0(O) -	0/0
1515	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019	0(O) -	0/0
1516	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	02/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1517	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	- -	-	-	0/0
1518	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1519	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1520	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	92.26	07/2018 -	-	-	0/5
1521	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24(O) -	0/0
1522	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76(O) -	0/0
1523	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82(O) -	0/0
1524	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63(O) -	0/0
1525	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71(O) -	0/0
1526	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1527	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
1528	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18(O) -	0/0
1529	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	3,059.39	- -	06/2019	-	0/0
1530	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13(O) -	0/0
1531	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13(O) -	0/0
1532	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	28.21	06/2018 -	-	-	0/0
1533	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0
1534	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL ,	08/2014	600.87 720.97	720.97	636.67	11/2017 05/2019	05/2019	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1535	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]PWD, WEST BENGAL ,	08/2014	823.20 937.76	937.76	703.86	11/2017 06/2019	06/2019	-	0/0
1536	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL ,	03/2016	271.17 291.20	291.20	79.43	11/2018 11/2019	11/2019	12(O) 0	0/0
1537	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD, WEST BENGAL ,	01/2017	396.86 396.86	396.86	179.31	09/2019 -	-	-	0/0
1538	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD, WEST BENGAL ,	03/2017	202.69 202.69	202.69	93.60	11/2019 -	-	-	0/0
1539	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19 - [N24000880]PWD, WEST BENGAL ,	02/2018	426.18 426.18	426.18	217.82	09/2020 -	-	-	0/0
1540	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD, WEST BENGAL ,	02/2018	218.70 218.70	218.70	18.22	11/2020 -	-	-	0/0
1541	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]PWD, WEST BENGAL ,	03/2018	254.30 254.30	254.30	20.09	10/2020 -	10/2020	0(O) -	0/0
1542	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL ,	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24(O) -	0/0
1543	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24(O) -	0/0
1544	REHABILITATION AND UPGADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD, WEST BENGAL ,	04/2014	279.70 398.52	398.52	314.63	08/2017 07/2019	07/2019	23(O) 0	0/0
	Total		4,93,493.25 -	5,10,239.55	2,39,800.48				208/901
	SHIPPING AND PORTS								
1545	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL, KERALA ,	07/2016	1,799.00 -	1,799.00	21.00	05/2021 -	05/2021	0(O) -	0/0
1546	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL, KERALA ,	05/2016	970.00 -	970.00	109.97	05/2020 -	05/2020	0(O) -	0/0
1547	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1548	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE ,	01/2018	4,200.00 -	4,200.00	1,256.55	03/2023 -	03/2023	0(O) -	0/0
1549	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1550	ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
1551	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	275.98	275.58	12/2017 -	-	-	1/1
1552	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU ,	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29(O) -	0/0
	Total		10,757.29 -	11,199.74	3,046.68				1/1
	<u>TELECOMMUNICATIONS</u>								
1553	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	367.03	06/2017 -	-	-	0/0
1554	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 240.10	240.10	117.63	10/2018 09/2019	09/2019	11(O) 0	0/0
1555	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58(O) -	0/0
1556	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,095.23 -	27,333.53	9,135.56				0/70
	<u>URBAN DEVELOPMENT</u>								
1557	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1558	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	169.16	163.98	03/2017 -	-	-	4/5
1559	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1560	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5(O) -	0/7
1561	IRRIGATION WORK OF BAGMATI - [N12000108]HSCCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1562	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	69.60	06/2017 -	10/2020	40(O) -	0/0
1563	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,763.15	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1564	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	313.93	10/2019 -	03/2021	17(O) -	0/7
1565	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	703.90	12/2015 -	-	-	0/0
1566	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019	0(O) -	3/7
1567	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	42.30	04/2019 -	06/2020	14(O) -	0/2
1568	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	-	-	-	0/0
1569	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	47.30	05/2020 -	05/2020	0(O) -	0/0
1570	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	146.45	06/2019 -	-	-	0/0
1571	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	10.36	-	12/2020	-	0/0
1572	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	- 0	0/0
1573	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	23.00	04/2018 -	-	-	0/0
1574	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019	0(O) -	0/0
1575	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	.00	-	-	-	0/0
1576	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	-	-	-	0/0
1577	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	10,773.00	5,854.77	12/2018 -	07/2020	19(O) -	0/0
1578	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59(O) -	2/8
1579	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1580	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1581	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1582	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1583	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	80.08	03/2016 -	09/2020	54(O) -	1/6
1584	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1585	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1586	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1587	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	62.56	02/2020 -	09/2020	7(O) -	0/0
1588	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	86.04	10/2012 -	03/2020	89(O) -	1/6
1589	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29(O) -	0/0
1590	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 -	03/2020	0(O) -	2/7
1591	BHOPAL METRO RAIL - [N28000124]MPMRL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023	0(O) -	0/0
1592	INDORE METRO RAIL - [N28000125]MPMRL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023	0(O) -	0/0
1593	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	205.00	156.21	03/2012 -	-	-	17/20
1594	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	5,989.97	03/2018 -	12/2019	21(O) -	0/0
1595	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1596	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	29.51	07/2020 09/2020	09/2020	2(O) 0	3/14
1597	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	2,642.09	11/2021 01/2022	01/2022	2(O) 1	0/0
1598	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67(O) -	0/10
1599	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0
1600	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	800.00	2.56	06/2021 -	03/2022	9(O) -	0/0
1601	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	488.28	422.79	05/2017 -	09/2019	28(O) -	8/12
1602	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	193.89	04/2019 -	02/2020	10(O) -	4/8

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1603	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	60.28	05/2020 -	01/2021	8(O) -	1/5
1604	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1605	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 559.47	559.47	326.38	07/2019 12/2019	12/2019	5(O) 0	0/0
1606	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-	-	12/24
1607	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	127.69	10/2019 -	03/2020	5(O) -	1/6
1608	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/2
1609	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	12.00	- -	11/2021	- -	0/0
1610	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	35.79	03/2020 02/2017	05/2021	14(O) 14	0/5
1611	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1612	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1613	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1614	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1615	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020	0(O) -	0/0
1616	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1617	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1618	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38(O) -	10/16
1619	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	126.07	04/2018 -	07/2019	15(O) -	5/6
	Total		1,86,663.06 -	1,92,886.88	84,370.55				74/183

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>WATER RESOURCES</u>								
1620	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15(O) -	0/19
1621	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	12/2019	0(O) -	0/0
	Total		10,384.61 -	55,782.44	16,450.19				0/19
	<u>DEFENCE PRODUCTION</u>								
1622	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	167.69	138.39	05/2018 03/2019	-	-	7/10
1623	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	285.95	81.83	08/2020 -	08/2020	0(O) -	7/16
	Total		453.64 -	453.64	220.22				14/26
	Grand Total		19,33,390.22	23,21,502.84	9,47,571.45				2734/5377


Summary of projects in the Flash Report for the month of July, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1608
Number of Projects completed/dropped/frozen in Current Month	21
	0
Number of Projects Added in Current Month	36
Number of Projects in Current Month	1623

Brief Analysis

Project Status with respect to Original Schedule: Out of 1623 projects, 23 projects are ahead of schedule, 378 projects are on schedule 552 projects are delayed. 508 projects do not have fixed dates of commissioning. 162 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

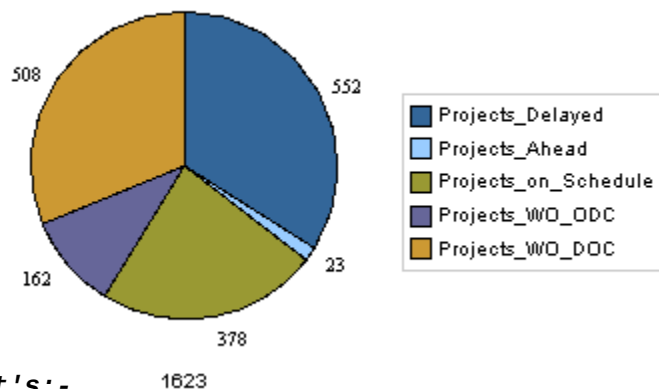


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1623 projects when sanctioned, was of the order of Rs. 1933390.22 crore but this was subsequently revised to Rs. 2321502.84 crore implying a cost overrun of 20.1%. The expenditure incurred on these projects till July, 2019 is Rs. 947571.45 crore, which is 40.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

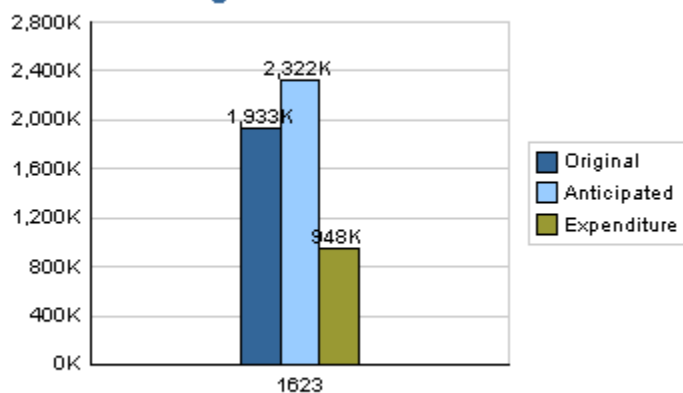

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

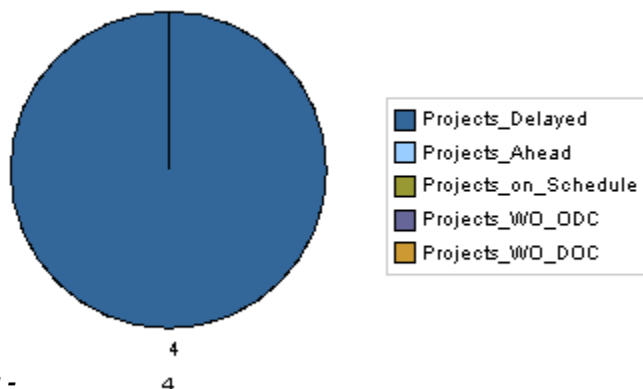

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till July, 2019 is Rs. 45577.74 crore, which is 56.7% of the anticipated cost of the projects.

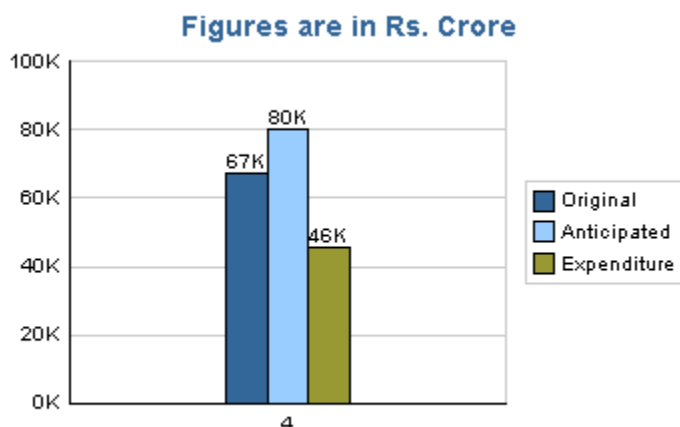

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	13
Number of Projects On Schedule	8
Number of Projects Delayed	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 8 projects are on schedule 5 projects are delayed.

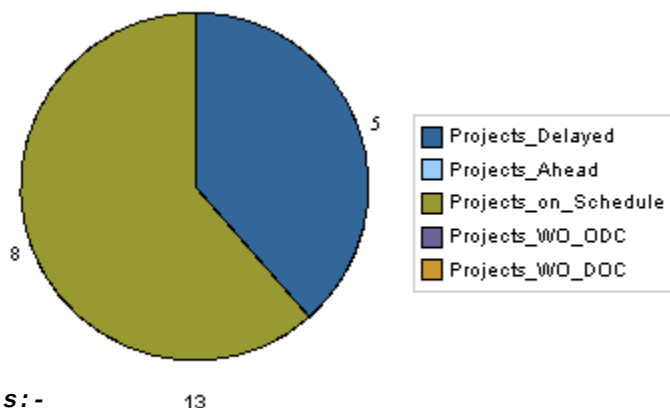


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 8607.51 crore but this was subsequently anticipated to Rs. 8734.44 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till July, 2019 is Rs. 1357.47 crore, which is 15.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

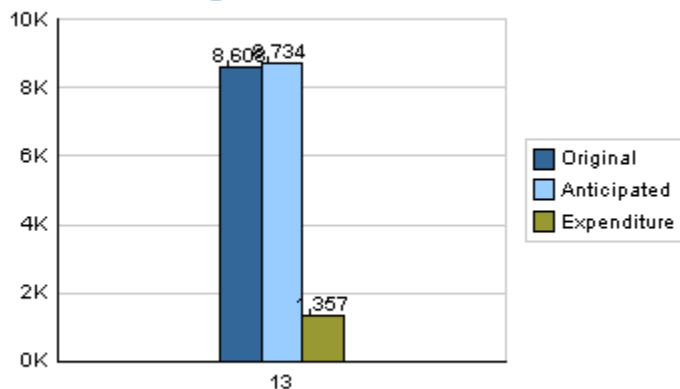

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	105
Number of Projects On Schedule	52
Number of Projects Delayed	34
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	16

Brief Analysis

Project Status with respect to Original Schedule: Out of 105 projects, 1 project is ahead of schedule, 52 projects are on schedule 34 projects are delayed. 16 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

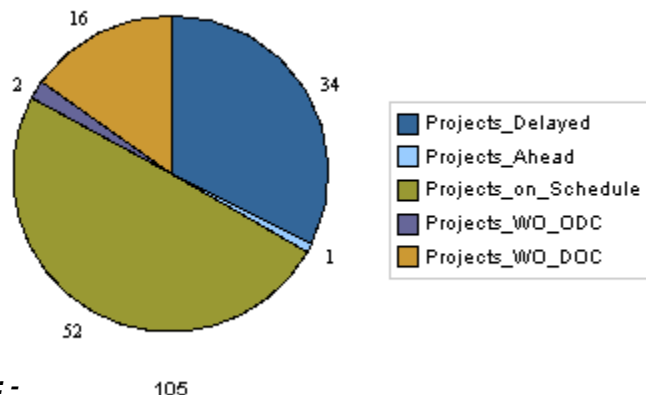


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 105 projects when sanctioned, was of the order of Rs. 99835.93 crore but this was subsequently anticipated to Rs. 100289.27 crore implying a cost overrun of .5%. The expenditure incurred on these projects till July, 2019 is Rs. 35189.01 crore, which is 35.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

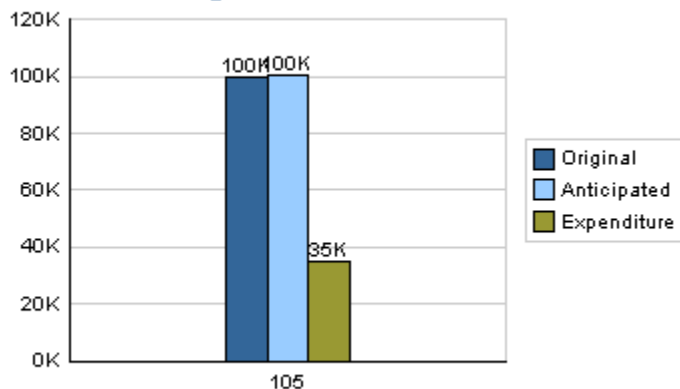

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	5
Number of Projects On Schedule	4
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project is delayed.

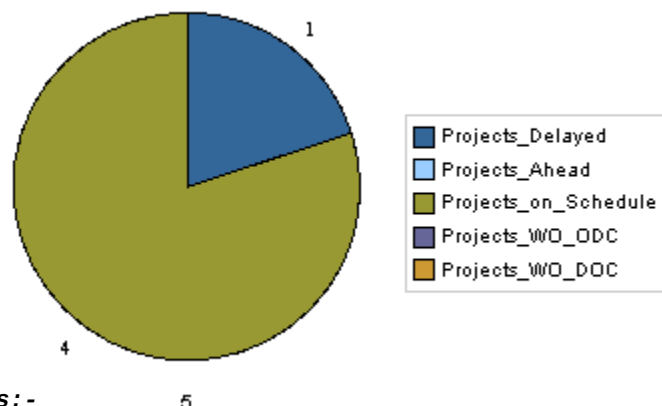


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1299.07 crore but this was subsequently anticipated to Rs. 1310.72 crore implying a cost overrun of .9%. The expenditure incurred on these projects till July, 2019 is Rs. 561.89 crore, which is 42.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

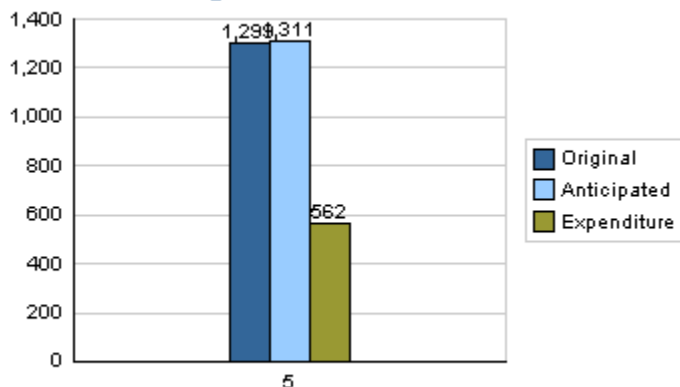

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	5
Number of Projects On Schedule	4

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project does not have fixed dates of commissioning.

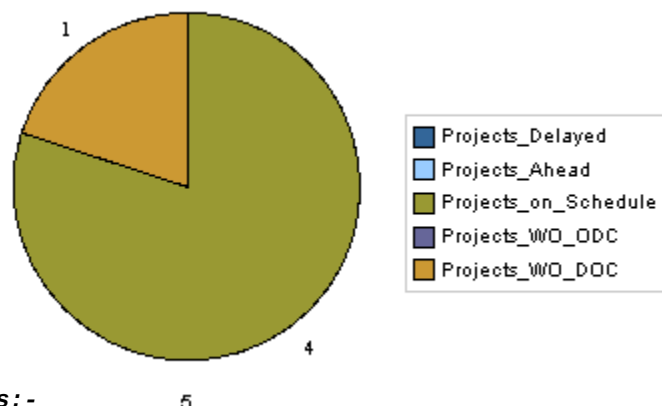


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore The expenditure incurred on these projects till July, 2019 is Rs. 587.94 crore, which is 8.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

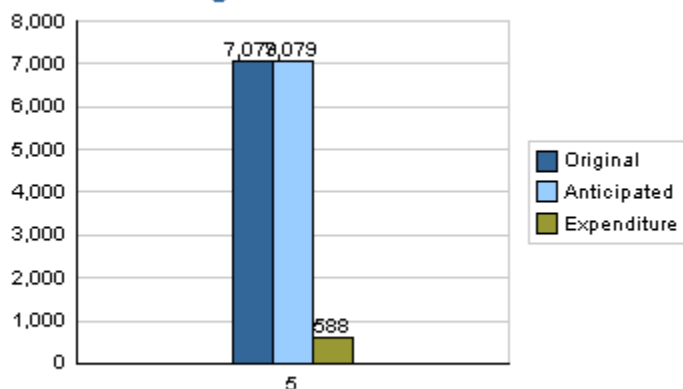

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 8 projects are delayed.

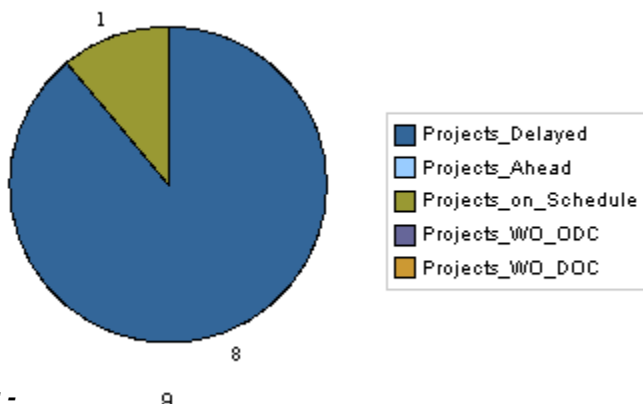


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 26228.23 crore but this was subsequently anticipated to Rs. 33485.23 crore implying a cost overrun of 27.7%. The expenditure incurred on these projects till July, 2019 is Rs. 22898.68 crore, which is 68.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

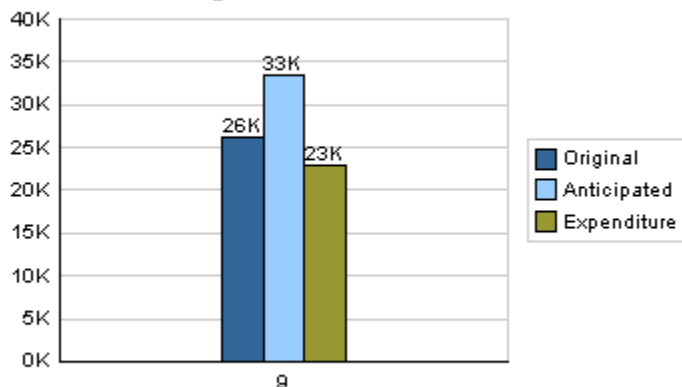

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	151
Number of Projects On Schedule	85
Number of Projects Delayed	47
Number of Projects Ahead	8
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 151 projects, 8 projects are ahead of schedule, 85 projects are on schedule 47 projects are delayed. 10 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

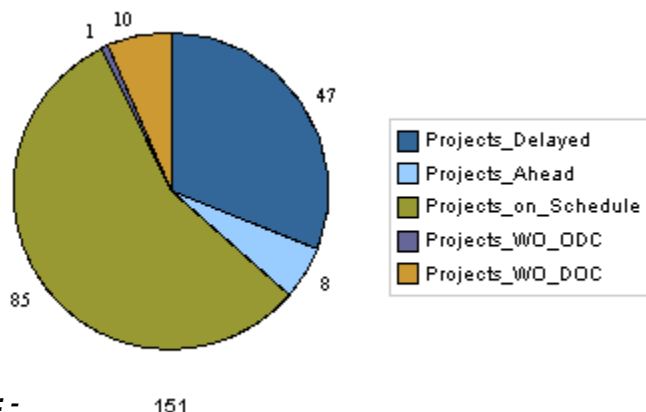


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 151 projects when sanctioned, was of the order of Rs. 246407.34 crore but this was subsequently anticipated to Rs. 253901.92 crore implying a cost overrun of 3%. The expenditure incurred on these projects till July, 2019 is Rs. 88700.73 crore, which is 34.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

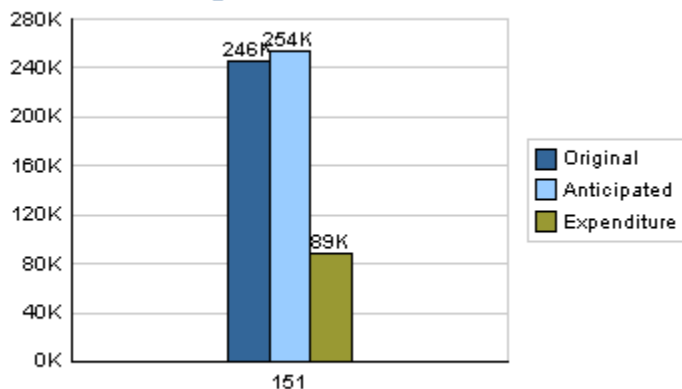

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	74
Number of Projects On Schedule	17
Number of Projects Delayed	50

Number of Projects Without Date Of Commissioning	7
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 74 projects, 17 projects are on schedule 50 projects are delayed. 7 projects do not have fixed dates of commissioning.

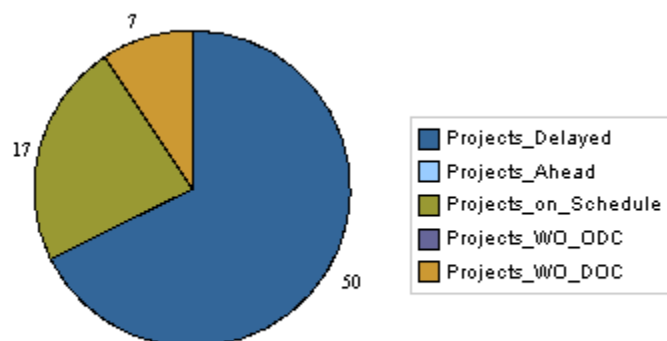


Total No Of Project's:- 74

Investment Scenario

Total original cost of implementation of 74 projects when sanctioned, was of the order of Rs. 287196.4 crore but this was subsequently anticipated to Rs. 360575.39 crore implying a cost overrun of 25.6%. The expenditure incurred on these projects till July, 2019 is Rs. 213724.9 crore, which is 59.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

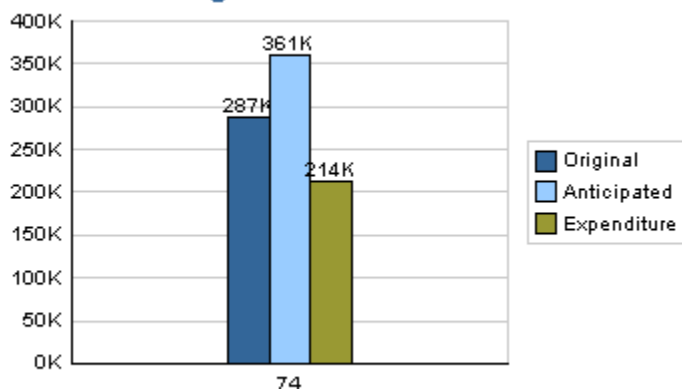

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1554 crore but this was subsequently anticipated to Rs. 1554 crore. The expenditure incurred on these projects till July, 2019 is Rs. 335.03 crore, which is 21.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

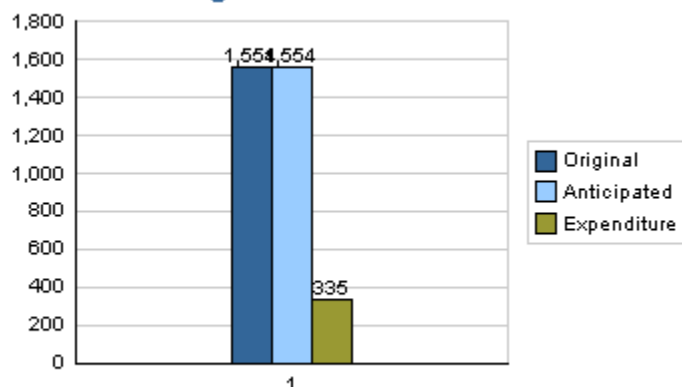

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	20
Number of Projects Delayed	11
Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 11 projects are delayed. 3 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

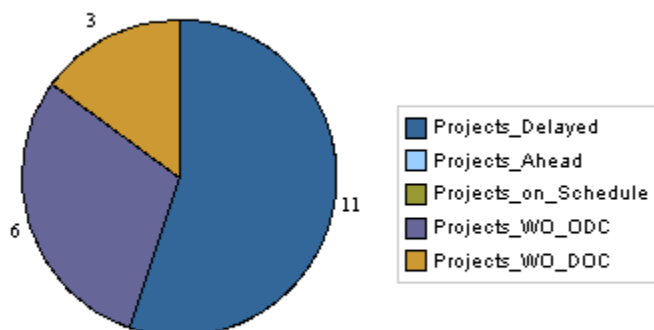


Total No Of Project's:-

20

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 8129.23 crore but this was subsequently anticipated to Rs. 8246.52 crore implying a cost overrun of 1.4%. The expenditure incurred on these projects till July, 2019 is Rs. 3239.95 crore, which is 39.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

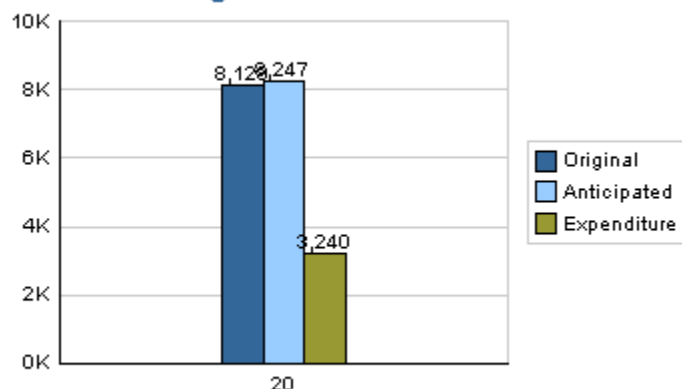

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	315
Number of Projects On Schedule	43
Number of Projects Delayed	141
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	59
Number of Projects Without Date Of Commissioning	65

Brief Analysis

Project Status with respect to Original Schedule: Out of 315 projects, 7 projects are ahead of schedule, 43 projects are on schedule 141 projects are delayed. 65 projects do not have fixed dates of commissioning. 59 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

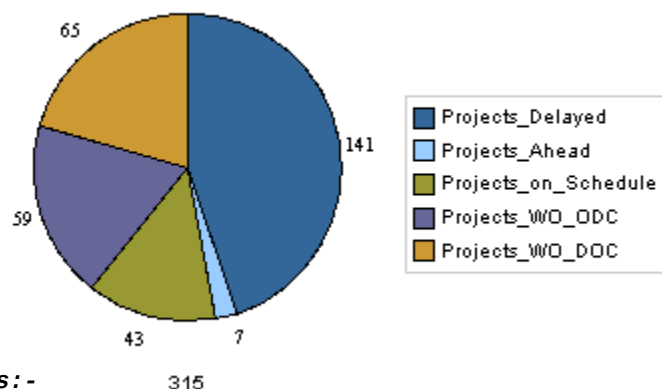


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 315 projects when sanctioned, was of the order of Rs. 461117.38 crore but this was subsequently anticipated to Rs. 667113.52 crore implying a cost overrun of 44.7%. The expenditure incurred on these projects till July, 2019 is Rs. 182344.63 crore, which is 27.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

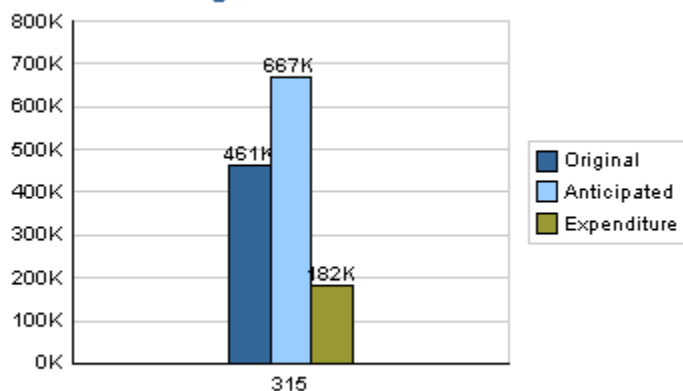

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	839
Number of Projects On Schedule	150
Number of Projects Delayed	219
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	91
Number of Projects Without Date Of Commissioning	372

Brief Analysis

Project Status with respect to Original Schedule: Out of 839 projects, 7 projects are ahead of schedule, 150 projects are on schedule 219 projects are delayed. 372 projects do not have fixed dates of commissioning. 91 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

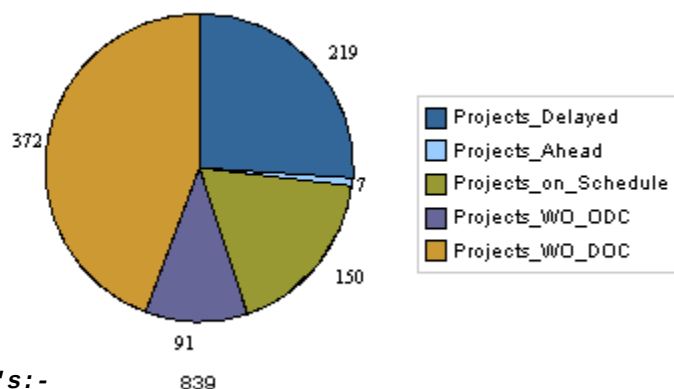

Investment Scenario

Total original cost of implementation of 839 projects when sanctioned, was of the order of Rs. 493493.25 crore but this was subsequently anticipated to Rs. 510239.55 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till July, 2019 is Rs. 239800.48 crore, which is 47% of the anticipated cost of the projects.

Figures are in Rs. Crore

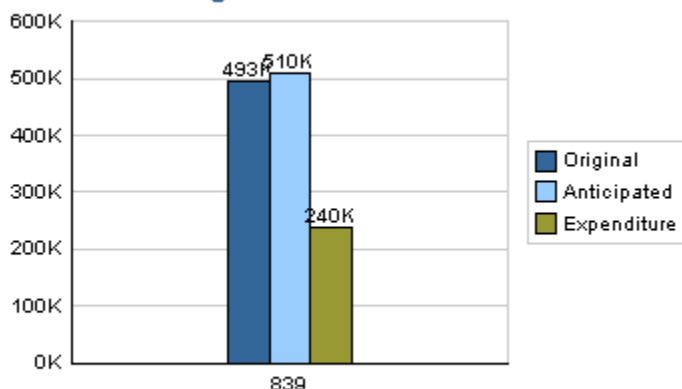

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	3
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule 1 project is delayed. 4 projects do not have fixed dates of commissioning.

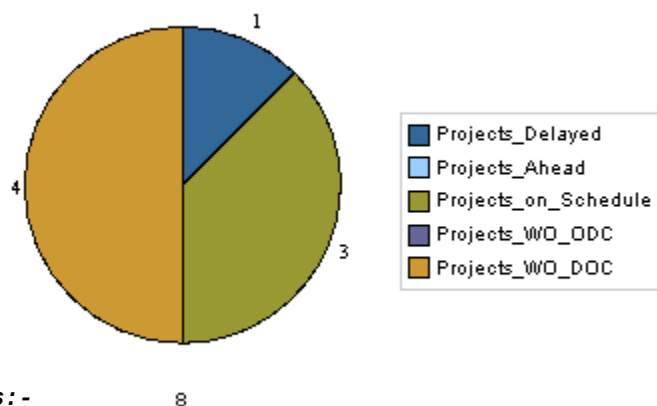


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 10757.29 crore but this was subsequently anticipated to Rs. 11199.74 crore implying a cost overrun of 4.1%. The expenditure incurred on these projects till July, 2019 is Rs. 3046.68 crore, which is 27.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

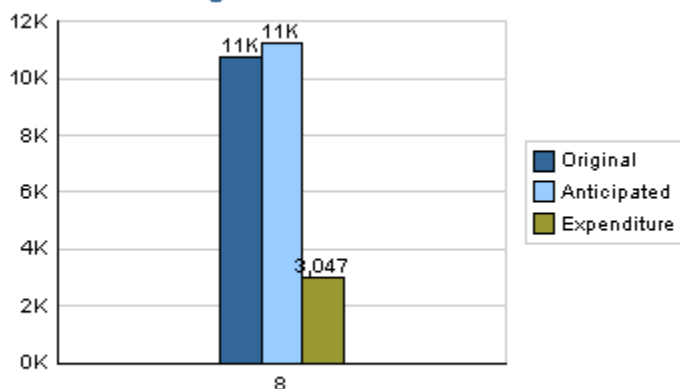

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	4
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

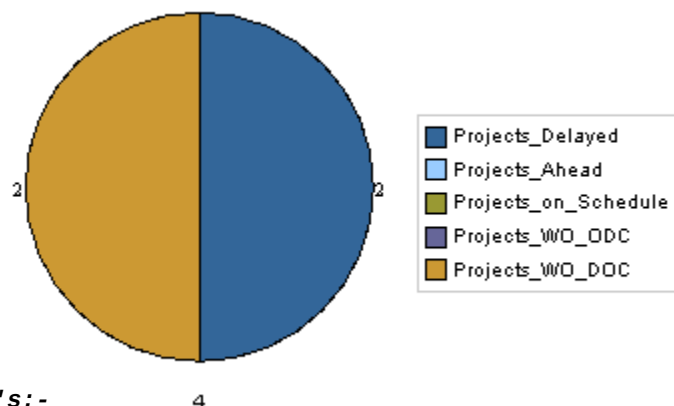


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 16095.23 crore but this was subsequently anticipated to Rs. 27333.53 crore implying a cost overrun of 69.8%. The expenditure incurred on these projects till July, 2019 is Rs. 9135.56 crore, which is 33.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

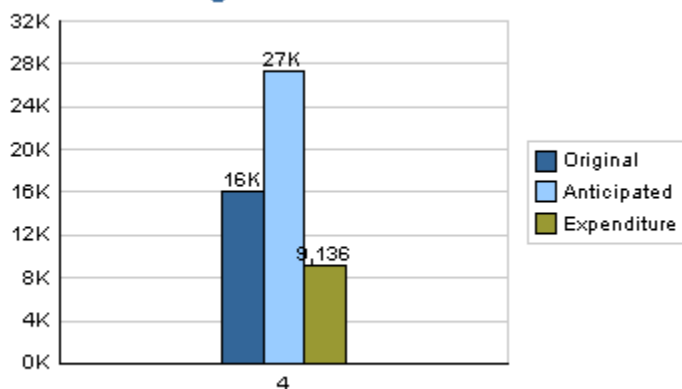

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	63
Number of Projects On Schedule	7
Number of Projects Delayed	27

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	26

Brief Analysis

Project Status with respect to Original Schedule: Out of 63 projects, 7 projects are on schedule 27 projects are delayed. 26 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

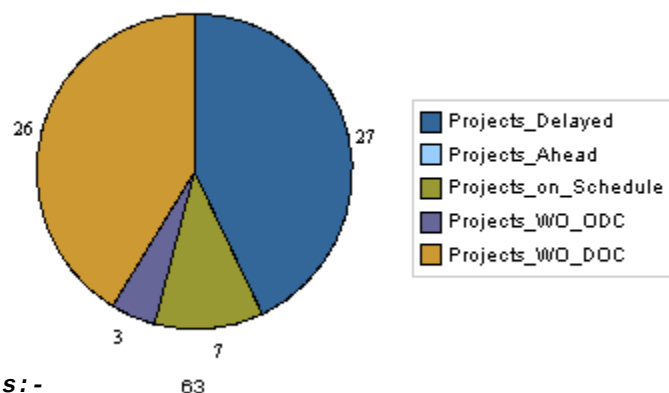


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 63 projects when sanctioned, was of the order of Rs. 186663.06 crore but this was subsequently anticipated to Rs. 192886.88 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till July, 2019 is Rs. 84370.55 crore, which is 43.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

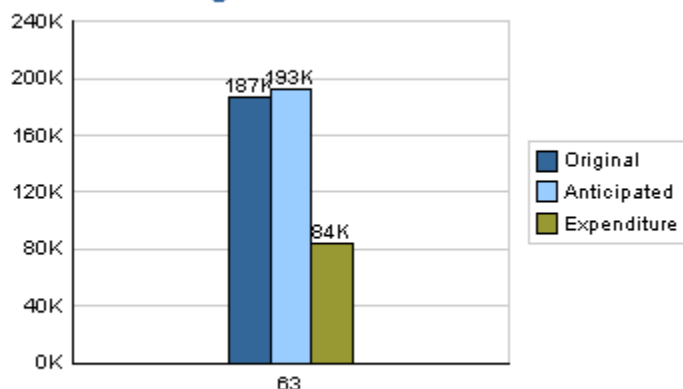

Sector wise current status of projects on the Flash Report


WATER RESOURCES

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

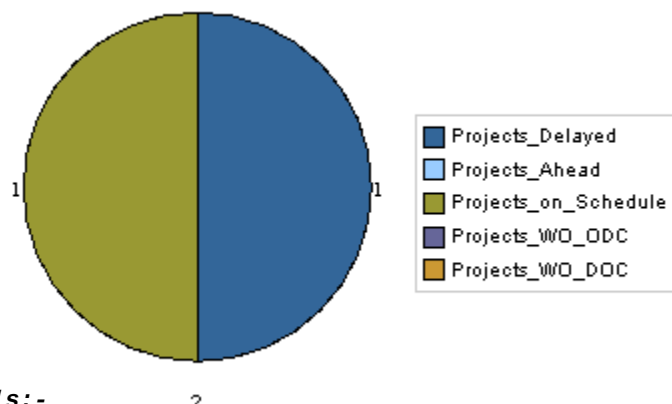


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 10384.61 crore but this was subsequently anticipated to Rs. 55782.44 crore implying a cost overrun of 437.2%. The expenditure incurred on these projects till July, 2019 is Rs. 16450.19 crore, which is 29.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

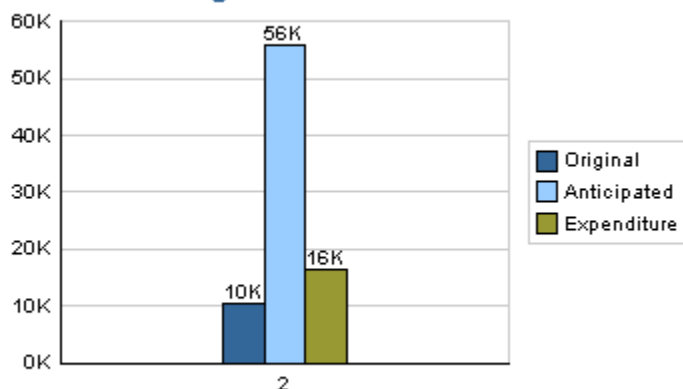

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.




Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 453.64 crore The expenditure incurred on these projects till July, 2019 is Rs. 220.22 crore, which is 48.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

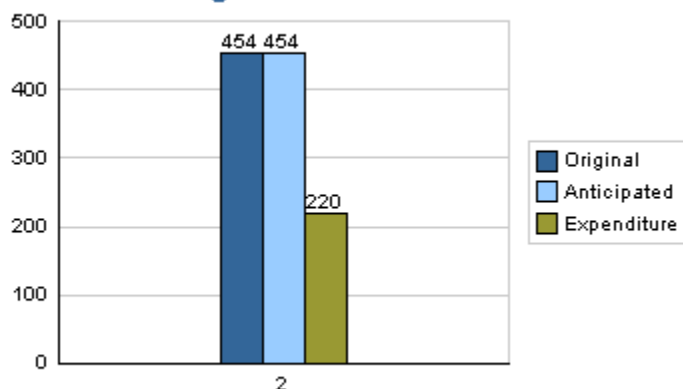

Annexure - I
STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (JULY 2019)
 (All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,786.01	2,893.59	414.94
2	ANDHRA PRADESH	76	1,20,064.65	1,69,040.57	42,700.81
3	ARUNACHAL PRADESH	38	19,572.19	38,023.5	21,473.61
4	ASSAM	47	25,166.52	29,070.62	13,674.47
5	BIHAR	93	87,682.2	1,32,726.3	61,129.22
6	CHHATISGARH	35	73,823.69	85,478.21	43,106.31
7	D & N HAVELI	1	6,086.08	5,842.31	4,783.74
8	DELHI	24	55,715.65	63,190.88	41,665.29
9	GOA	12	5,779.51	5,789.94	1,978.16
10	GUJARAT	55	64,314.47	70,750.56	44,403.18
11	HARYANA	32	22,390.13	23,907.66	11,287.46
12	HIMACHAL PRADESH	12	16,702.17	26,812.7	12,013.91
13	JAMMU AND KASHMIR	13	24,646.76	50,095.76	32,575.92
14	JHARKHAND	45	60,234.46	64,107.45	25,802.14
15	KARNATAKA	65	74,513.97	77,491.82	17,956.1
16	KERALA	22	39,078.6	41,891.46	13,763.23
17	MADHYA PRADESH	74	84,134.46	91,226.06	40,852.75
18	MAHARASHTRA	261	2,37,745.85	2,46,454.54	95,703.83
19	MANIPUR	5	6,002.36	14,012.39	9,067.93
20	MEGHALAYA	6	2,760.77	7,854.31	980.58
21	MIZORAM	13	7,757.62	11,189.69	4,545.2
22	MULTI STATE	131	3,17,640.98	4,23,586.25	1,31,487.99
23	NAGALAND	26	14,842.43	15,515.91	1,738.53
24	ODISHA	97	1,06,511.4	1,08,955.39	42,384.76
25	PUNJAB	27	13,539.35	15,093.54	8,779.44
26	RAJASTHAN	62	47,167.18	54,596.11	31,986.19
27	SIKKIM	9	3,476.73	6,308.8	1,065.18
28	TAMIL NADU	69	1,19,531.37	1,37,822.56	64,970.52
29	TELANGANA	57	40,255.16	43,275.56	12,367.58
30	TRIPURA	7	1,977.29	2,139.55	1,089.91
31	UTTAR PRADESH	107	1,39,916.34	1,44,181.28	61,639.09
32	UTTARAKHAND	31	35,661.33	44,552.75	14,108.04
33	WEST BENGAL	62	55,912.54	67,624.82	36,075.44
TOTAL		1,623	19,33,390.22	23,21,502.84	9,47,571.45

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021
	Total		3,492.00 -	6,840.00	5,784.74		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
2	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022
3	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	228.90	03/2012 -	03/2021
4	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022
5	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	493.85	03/2017 -	03/2020
	<u>Singareni Colliers Company Limited</u>						
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	296.92	03/2012 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
7	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	191.40	03/2015 -	03/2020
	Total		1,728.69 -	2,235.58	2,097.81		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
8	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	523.00	508.29	03/2018 -	-
	Total		505.58 -	523.00	508.29		
	<u>PETROLEUM</u>						
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>						
10	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,285.65	05/2013 12/2019	12/2019
	Total		1,854.79 -	3,376.06	2,835.50		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
11	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	9/2002	3,919.59 -	9,997.11	7,522.82	09/2009 -	12/2021
12	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	9/2003	6,285.33 -	19,496.34	10,927.32	09/2010 -	-
	<u>National Thermal Power Corporation</u>						
13	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	12,027.37	01/2018 03/2020	03/2020
14	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,229.51	10/2017 03/2020	03/2020
15	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	1/2007	5,353.00 -	9,996.59	7,840.42	07/2012 -	09/2020
	<u>North East Electric Power Corporation</u>						
16	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,419.34	7,494.35	12/2009 08/2019	08/2019
	<u>Power Grid Corporation Of India Limited</u>						
17	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022
18	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019
19	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [N180100258]	5/2005	1,779.29 -	2,187.32	2,237.45	11/2008 06/2019	08/2019
	<u>Thdc India Limited</u>						
20	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	5/2011	195.42 -	294.60	295.73	02/2014 -	10/2019
21	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	5,024.35	2,969.55	02/2016 -	06/2022
	Total		56,788.76 -	95,379.95	76,889.10		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
22	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	305.00	267.36	03/2019 12/2019	12/2019
23	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [N220100181]	2/1997	2,271.50 -	3,712.50	2,291.50	03/2021 -	03/2022
	<u>East Central Railways</u>						
24	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [N220100222]	3/1999	1,033.07 -	3,376.00	3,180.37	- -	03/2021
25	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [N220100303]	4/2003	528.65 -	2,066.77	1,403.38	- -	03/2023
26	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	815.41	- -	12/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
27	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	4/1998	180.82 -	727.29	488.81	-	09/2019
28	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	559.91	541.07	07/2014 -	-
29	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	400.17	378.41	-	01/2020
30	SAKRI-HASANPUR ROAD (NL) - [N22000171]	4/1999	325.00 -	729.92	349.60	-	03/2021
31	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	4/1997	162.87 -	589.15	303.96	-	03/2022
32	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	324.73 -	1,156.41	1,028.71	03/2012 -	03/2020
33	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	4/1996	477.88 283.95	749.00	672.82	03/2012 -	03/2020
	<u>East Coast Railway</u>						
34	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	224.63	03/2020 -	03/2020
	<u>Eastern Railways</u>						
35	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	4/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024
36	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	376.90	370.65	-	03/2020
37	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	471.81	454.23	-	05/2019
38	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	226.22	226.22	-	03/2021
39	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	252.18	-	03/2024
40	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]	4/2011	166.89 -	166.89	246.00	-	03/2025
	<u>Metropolitan Rapid Transport Projects</u>						
41	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
42	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	<u>North Central Railway</u>						
43	ETAWAH-MAINPURI (NL),NCR - [220100318]	4/1997	120.00 -	346.00	345.51	12/2008 03/2015	03/2015
	<u>North East Frontier Railway</u>						
44	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,871.00	1,082.01	-	-
45	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	2/1999	380.60 -	1,300.00	1,087.60	04/2010 -	-
	<u>North Eastern Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
46	HATHUA-BHATNI (N L) (NER) - [N220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	12/2022
47	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	307.99	01/2019 -	01/2020
	<u>North Western Railway</u>						
48	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	260.89	11/2019 -	05/2020
49	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	410.00	347.99	02/2019 -	12/2019
	<u>Northern Railway</u>						
50	HARIDWAR-LAKSAR - [N22000289]	4/2012	219.83 -	346.63	229.48	- -	06/2020
51	NANGALDAM-TALWARA(NL),NR - [N220100188]	3/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024
52	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	855.00	834.59	03/2016 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
53	HARIDASPUR-PARADEEP(NL) - [N220100285]	4/1996	1,185.64 -	1,844.47	1,729.78	12/2017 -	03/2020
54	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,120.00	992.67	03/2019 -	03/2021
55	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	682.17	03/2016 -	12/2020
56	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,200.00	1,124.56	03/2019 -	03/2020
57	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,500.00	1,249.76	03/2020 -	03/2021
58	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,950.00	1,823.93	03/2020 -	03/2020
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327]	4/2000	133.41 207.00	385.00	386.28	03/2009 03/2009	12/2019
	<u>South Central Railway</u>						
60	NANDYAL-YERRAGUNTALA(NL),SCR - [N220100192]	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
	<u>South Eastern Railway</u>						
61	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019
	<u>Southern Railway</u>						
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'- AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020
63	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	4/1999	198.68 -	556.64	303.72	- -	-
64	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]	9/1995	303.98 -	980.00	669.21	03/2020 -	03/2021
65	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
66	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444	2/1999	257.00 257.00	257.00	268.31	03/2018 -	-
67	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	2/1996	268.87 -	950.00	927.86	03/2005 -	-
	<u>West Central Railway</u>						
68	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	9/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023
	<u>Western Railway</u>						
69	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	202.35	404.70	03/2011 03/2017	03/2017
70	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,310.23	1,363.06	03/2020 03/2021	03/2021
	Total		26,653.84 -	64,146.23	45,783.30		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
71	BHANDARA TO GHOTITOK - [N24001018	1/2017	392.83 393.00	392.83	690.60	06/2019 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
72	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	197.77	01/2019 -	-
	<u>National Highways Authority Of India</u>						
73	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	280.00	472.00	02/2009 -	-
74	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
75	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	839.63	03/2018 -	-
76	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	834.75	04/2018 -	-
77	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432	9/2015	414.51 -	414.00	529.62	05/2018 -	06/2020
78	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	556.02	08/2016 -	-
79	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	605.33	10/2017 -	-
80	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367	4/2014	495.78 -	495.78	633.24	01/2016 -	-
81	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	351.34	433.68	01/2016 -	-
82	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	843.67	07/2013 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
83	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	2/2018	1,052.21 -	1,052.21	1,080.00	- -	01/2021
84	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020
85	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	02/2020
86	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,275.00	- -	02/2020
87	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	627.66	07/2008 -	-
88	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	1,665.00	3,059.39	- -	06/2019
89	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
90	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	3,424.19	01/2018 -	-
91	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
92	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
93	NAGPUR - KONDHALI - [N24000472	9/2005	168.00 -	168.00	226.24	06/2006 -	-
94	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
95	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460	12/2015	611.65 -	611.65	728.24	06/2016 -	-
96	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019
97	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	494.33	04/2014 -	-
98	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	768.73	03/2014 -	-
99	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019
100	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.52	10/2013 -	-
101	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	976.79	07/2013 -	-
102	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,330.29	12/2013 -	-
103	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
104	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	885.47	02/2013 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-
106	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-
107	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-
108	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	733.33	07/2014 -	06/2020
109	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	459.07	01/2014 -	-
110	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019
111	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,864.34	06/2014 -	-
112	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020
113	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019
114	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019
115	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,930.61	09/2014 -	-
116	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,075.87	06/2014 -	-
117	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	566.60	11/2013 -	-
118	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-
119	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	1,509.10	3,187.21	09/2012 -	-
120	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019
121	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-
122	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019
123	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019
124	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019
125	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	325.00	469.54	05/2013 -	-
126	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019
127	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
128	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]	2/2010	617.00 -	617.00	943.17	08/2012 -	12/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
129	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
130	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	340.12	07/2009 -	-
131	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	5/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020
132	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019
133	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	319.96	04/2009 -	08/2019
134	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-
135	NASHRI- CHANANI - [N24000162	5/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-
136	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	2,580.88	07/2015 -	-
137	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	167.64	268.94	11/2008 -	-
138	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	195.35	11/2008 -	-
	<u>National Highways Development Project</u>						
139	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019
140	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020
	<u>Public Works Dept Of State</u>						
141	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019
142	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	305.61	269.07	09/2014 -	12/2019
143	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389	11/2015	847.02 -	847.02	1,086.49	-	-
144	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	8/2010	195.04 -	377.99	296.28	10/2010 -	06/2020
145	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
146	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955	10/2012	511.21 -	511.21	814.79	10/2013 -	-
147	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
148	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	254.24	10/2010 -	12/2019
	Total		69,469.26 -	74,532.37	1,05,312.24		
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
149	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	275.98	275.58	12/2017 -	-
	<u>Mumbai Port Trust</u>						
150	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	1/2007	366.39 -	669.46	411.12	12/2010 -	-
	Total		610.89 -	945.44	686.70		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
151	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	23,140.00	15,811.82	05/2015 07/2020	07/2020
	Total		15,525.00 -	23,140.00	15,811.82		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
152	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	2/2014	388.00 -	488.28	422.79	05/2017 -	09/2019
153	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	169.16	163.98	03/2017 -	-
	<u>Chennai Metro Rail Ltd</u>						
154	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	2/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-
	<u>Hindustan Steelwork Construction Limited</u>						
155	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
156	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	3/2007	149.73 173.00	175.94	178.65	12/2015 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>						
157	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019
	Total		21,246.24 -	26,692.51	23,391.83		
	<u>WATER RESOURCES</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(July 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Polavaram Project Authority</u>						
158	POLAVARAM IRRIGATION PROJECT - [N30000002	2/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021
	Total		10,151.04 -	55,548.87	16,417.99		
	Grand Total		2,08,026.09	3,53,360.01	2,95,519.32		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs.150 Crore and above						(July 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021
	Total		1,186.64 -	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
2	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY [N16000260]	2/2016	554.00 -	554.00	335.52	02/2020 -	09/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,697.02	12/2020 -	08/2020
4	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	594.01	12/2020 -	02/2020
5	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	149.98	06/2020 -	03/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	110.38	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	108.51	09/2022 -	06/2021
8	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	81.56	04/2021 -	04/2020
	Total		8,274.58 -	9,275.58	3,076.98		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
9	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	511.35	03/2024 -	03/2022
	<u>East Central Railways</u>						
10	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	159.07	03/2021 -	12/2020
	<u>North Central Railway</u>						
11	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00	2,001.00	416.59	03/2021 03/2023	03/2021
	<u>North East Frontier Railway</u>						
12	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48	4,084.69	285.46	12/2015 06/2021	03/2020

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	186.09	12/2021 -	03/2020
14	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	582.27	03/2022 -	03/2020
	<u>North Eastern Railway</u>						
15	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	291.45	03/2022 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.19	12/2025 -	03/2025
	Total		12,169.97 -	14,874.59	2,432.47		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
17	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]	2/2017	429.43	429.43	181.17	11/2017 03/2020	11/2019
18	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]	11/2016	376.25	376.25	180.38	08/2017 03/2020	08/2019
19	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]	1/2017	263.45	263.45	43.79	09/2017 03/2020	09/2019
20	PARSHURAM GHAT TO ARAWALI - [N24001133]	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
	<u>National Highways Authority Of India</u>						
21	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019
22	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019
23	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02	157.49	-	03/2020 -	02/2020
24	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19	254.00	248.60	03/2020 -	09/2019
25	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79	552.90	480.73	03/2020 -	09/2019
26	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32	503.10	1.15	03/2020 -	11/2019
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50	172.16	117.09	03/2020 -	09/2019
28	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	670.00	04/2020 -	11/2019
	<u>Public Works Dept Of State</u>						
29	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]	1/2017	247.25 -	247.25	144.00	03/2019 03/2020	09/2019

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		7,025.97	8,105.40	4,767.56		
	Grand Total		28,657.16	32,459.39	10,394.56		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs.150 Crore and above						(July 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
2	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
4	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
5	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AIRPORT - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
6	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
7	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	0.42	11/2021 -	11/2021
8	CCS INTERNATIONAL AIRPORT, LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
	Total		5,033.68 -	5,033.82	694.83		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	187.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
11	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
12	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	314.86	03/2022 -	03/2022
14	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	80.56	03/2022 -	03/2022
15	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.13	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
16	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
	<u>Mahanadi Coal Fields Limited</u>						
17	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	439.24	03/2021 -	03/2021
18	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,111.70	03/2029 -	03/2029
19	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,547.80	03/2026 -	03/2026
20	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	82.60	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
21	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	6,860.71	11/2021 -	11/2021
22	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
23	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.88	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
24	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
25	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	264.90	03/2021 -	03/2021
26	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
27	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
28	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	116.09	03/2021 -	03/2021
29	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.08	03/2023 -	03/2023
30	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,043.87	03/2023 -	03/2023
31	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.02	03/2023 -	03/2023
32	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
33	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
34	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,879.89	03/2023 -	03/2023
35	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023
36	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	82.76	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
37	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	92.47	03/2022 -	03/2022
38	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
39	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
40	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
41	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	67.41	03/2020 -	03/2020
42	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
43	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.15	03/2021 -	03/2021
44	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	103.99	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
45	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	-	03/2025 -	03/2025
46	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
47	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020
48	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
49	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	235.29	03/2022 -	03/2022
50	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	149.87	03/2021 -	03/2021
51	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	150.05	03/2021 -	03/2021
52	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
53	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	-	03/2021 -	03/2021
54	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	50.56	03/2022 -	03/2022
55	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.81	03/2020 -	03/2020
56	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	18.45	03/2022 -	03/2022
57	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	119.73	03/2023 -	03/2023
58	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	199.23	03/2021 -	03/2021
59	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	175.30	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
60	AMALGAMATED YEKONA-I YEKONA-II - [N06000132	8/2015	727.28 -	727.28	258.40	03/2025 -	03/2025
	Total		72,911.73 -	73,134.27	19,269.29		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
61	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	285.95	81.83	08/2020 -	08/2020
	Total		285.95 -	285.95	81.83		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
62	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL [N08000016	1/2018	239.81 -	239.81	107.64	11/2019 -	11/2019
63	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA [N08000015	1/2018	218.83 -	218.83	101.91	11/2019 -	11/2019
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT [N08000014	1/2018	215.92 -	215.92	100.17	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
65	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY [N08000018	4/2018	426.72 -	426.72	92.10	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	401.82		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
66	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>INFORMATION AND BROADCASTING</u>						
	<u>National Building Construcion Corporation Ltd</u>						
67	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003	12/2016	167.70 -	167.70	-	03/2020 -	03/2020
	Total		167.70 -	167.70	.00		
	<u>MINES</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Aluminum Company Limited (Nalco)</u>						
68	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	318.13	01/2020 01/2020	01/2020
69	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
70	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	0.30	04/2021 04/2021	04/2021
71	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	102.61	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	452.96		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
72	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20 -	580.20	33.91	02/2021 -	02/2021
73	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	155.19	12/2019 -	12/2019
74	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	115.60	08/2020 -	08/2020
75	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	13.19	12/2021 -	12/2021
76	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	15.04	03/2023 -	03/2023
77	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
78	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	0.42	03/2021 -	03/2021
	<u>Chennai Petroleum Corporation Limited</u>						
79	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	909.85	12/2019 -	12/2019
80	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	109.41	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
81	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	46.48	10/2022 -	10/2022
82	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	121.99	04/2022 -	04/2022
83	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	48.22	07/2022 -	07/2022
84	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
85	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	-	02/2021 -	02/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	42.63	10/2022 -	10/2022
87	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	995.48	12/2020 -	12/2020
88	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	61.78	10/2022 -	10/2022
89	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	171.48	12/2020 -	12/2020
90	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,256.48	12/2020 -	12/2020
91	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	27.01	07/2022 -	07/2022
92	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,395.00	12/2020 -	12/2020
93	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	934.68	12/2021 -	12/2021
94	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,256.25	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						
95	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	717.33	03/2021 -	03/2021
96	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	6.94	06/2022 -	06/2022
97	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,438.13	06/2020 -	06/2020
98	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	63.55	11/2020 -	11/2020
99	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
100	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
101	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
102	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	114.80	11/2019 -	11/2019
103	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,376.01	03/2020 -	03/2020
104	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	375.09	09/2019 -	09/2019
105	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	5,541.02	07/2020 -	07/2020
	<u>Indian Oil Corporation Limited</u>						
106	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	600.35	10/2019 -	10/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	242.10	10/2021 -	10/2021
108	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,569.01	09/2019 -	09/2019
109	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	15.01	12/2021 -	12/2021
110	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
111	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	178.05	02/2020 -	02/2020
112	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
113	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
114	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
115	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	142.67	08/2020 -	08/2020
116	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	7.75	02/2020 -	02/2020
117	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	8.85	10/2021 -	10/2021
118	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPEL - [N16000276]	5/2016	261.00 -	261.00	37.47	01/2021 -	01/2021
119	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
120	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	376.04	09/2019 -	09/2019
121	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	0.71	08/2020 -	08/2020
122	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	325.42	10/2019 -	10/2019
123	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	14.12	02/2020 -	02/2020
124	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
125	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
126	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,872.71	09/2019 -	09/2019
127	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	36.68	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
128	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	108.00	07/2020 -	07/2020
129	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	12.28	06/2020 -	06/2020
130	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
131	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
132	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	7.82	01/2021 -	01/2021
133	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	142.12	03/2021 -	03/2021
134	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,526.40	11/2019 -	11/2019
135	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020
136	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
137	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	13.11	01/2021 -	01/2021
138	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	806.13	12/2020 -	12/2020
139	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	917.26	08/2021 -	08/2021
140	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	284.31	08/2021 -	08/2021
141	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	132.24	09/2019 -	09/2019
142	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	8.19	03/2021 -	03/2021
143	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	531.40	09/2019 -	09/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
144	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	405.01	03/2022 -	03/2022
145	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]	10/2018	156.67 -	156.67	-	03/2021 -	03/2021
146	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	157.02	05/2020 -	05/2020
147	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	356.41	03/2026 -	03/2026
148	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	445.24	11/2019 -	11/2019
149	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	897.60	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
150	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	121.38	05/2021 -	05/2021
151	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	-	12/2020 -	12/2020
152	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	436.53	12/2019 -	12/2019
	<u>Oil India Limited</u>						
153	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	158.44	12/2019 -	12/2019
154	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	3.30	08/2020 -	08/2020
155	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	83.34	10/2020 -	10/2020
156	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	682.90	7.60	02/2020 -	02/2020
	Total		1,20,634.00 -	1,22,128.47	32,134.92		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
157	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
158	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
159	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	1,855.39	03/2023 -	03/2023
160	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	8,306.06	01/2020 -	01/2020
161	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019
	<u>Power Grid Corporation Of India Limited</u>						
162	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	116.76	02/2020 02/2020	02/2020
163	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020
164	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020
165	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020
166	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	187.60	11/2019 11/2019	11/2019
167	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	52.63	12/2019 12/2019	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
168	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019
169	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247	2/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020
	<u>Satluj Jal Vidyut Nigam Limited</u>						
170	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194	3/2019	10,439.09 -	10,439.09	564.81	01/2024 -	01/2024
171	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	648.33	236.30	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
172	KHURJA SUPER THERMAL POWER PROJECT - [N18000272	3/2019	11,089.42 -	11,089.42	509.30	09/2023 -	09/2023
173	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	1,587.16	299.55	09/2020 -	09/2020
	Total		83,212.44 -	83,973.74	26,924.86		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
174	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	145.69	03/2023 -	03/2023
175	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
176	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	77.48	03/2023 -	03/2023
177	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,205.35	03/2023 -	03/2023
178	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
179	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
180	KOSI BRIDGE (NL), ECR - [220100304	4/2002	499.41 -	516.02	389.29	03/2020 -	03/2020
	<u>East Coast Railway</u>						
181	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	3/2012	155.81 -	238.03	224.63	03/2020 -	03/2020
182	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	3,382.95	325.64	03/2022 -	03/2022
	<u>Eastern Railways</u>						
183	HANSDIHA-GODDA NL - [N22000236	4/2011	542.18 -	693.80	424.02	03/2020 -	03/2020
	<u>North Central Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
184	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 03/2020	03/2020
185	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
186	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	416.59	03/2021 03/2023	03/2021
	<u>North East Frontier Railway</u>						
187	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	455.80	03/2021 -	03/2021
188	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.14	03/2020 -	03/2020
189	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.66	03/2021 -	03/2021
190	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.98	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
191	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	15.03	01/2022 -	01/2022
192	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	12/2022
193	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>Northern Railway</u>						
194	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
195	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	2,812.27	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
196	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]	2/2016	393.98 -	393.98	241.23	03/2020 -	03/2020
197	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
198	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,571.99	03/2023 -	03/2023
199	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	1,009.30	12/2020 -	12/2020
200	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	837.66	12/2023 -	12/2023
201	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	933.88	12/2021 -	12/2021
202	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.68	546.57	12/2024 -	12/2024
203	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	1,176.15	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
204	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	368.23	12/2026 -	12/2026
205	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	296.20	03/2021 -	03/2021
206	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,950.00	1,823.93	03/2020 -	03/2020
207	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	364.69	12/2024 -	12/2024
	<u>South Central Railway</u>						
208	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	1,352.74	269.07	03/2020 03/2020	03/2020
209	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
	<u>South East Central Railway</u>						
210	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	276.86	12/2021 12/2021	12/2021
211	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	441.10	03/2023 03/2023	03/2023
	<u>South Western Railway</u>						
212	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
213	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
	<u>Southern Railway</u>						
214	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>Western Railway</u>						
215	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	719.73	03/2022 03/2022	03/2022
216	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	374.60	03/2021 03/2021	03/2021
	Total		1,88,107.03 -	2,42,091.91	43,184.17		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
217	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
218	AHMADPUR TO PIMPLA - [N24001029]	1/2017	422.38 -	422.38	148.58	08/2019 -	08/2019
219	BHOKAR TO SARSAM - [N24001128]	2/2017	295.09 -	295.99	155.64	07/2019 -	07/2019
220	SARAD VANI PIMPALGAON - [N24001103]	1/2017	250.46 -	250.46	103.63	07/2019 -	07/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
221	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
222	JALGAON TO BHADGAON - [N24001045	1/2018	307.54 308.00	307.54	106.59	11/2019 -	11/2019
223	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	64.97	06/2020 -	06/2020
224	OMREGA TO AUSA - [N24001067	3/2018	272.04 272.00	272.04	72.24	12/2019 -	12/2019
225	MAHAD TO RAIGAD FORT - [N24001038	7/2018	237.40 -	237.40	7.34	05/2020 -	05/2020
226	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
227	KUSUMBA TO MALEGAON - [N24001109	3/2018	243.45 244.00	243.45	58.02	12/2019 -	12/2019
228	CHALISGAON TO NANDGAON - [N24001108	3/2018	206.97 207.00	206.97	68.89	12/2019 -	12/2019
229	BHOGAN KHURD TO KASHEDI - [N24001132	9/2017	743.21 743.00	743.21	52.87	06/2021 -	06/2021
230	BHADGAON TO CHALISGAON - [N24001047	1/2018	259.55 260.00	259.55	150.00	11/2019 -	11/2019
231	KOTHARI TO DHANORA - [N24001073	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
232	NILAJPHATA TO BHANDARA - [N24001043	1/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020
233	KARWANDI TO RAJURI - [N24001058	3/2018	276.95 277.00	276.95	85.47	12/2019 -	12/2019
234	MANGRUPHIR TO MAHAN - [N24001087	3/2018	222.13 222.00	222.13	23.36	11/2019 -	11/2019
235	LATUR TO PANGAON - [N24001066	3/2018	336.47 336.00	336.47	85.48	12/2019 -	12/2019
236	PARBHANI TO GANGKHED - [N24001065	3/2018	238.19 238.00	238.19	23.85	12/2019 -	12/2019
237	KOLDE TO KHETIYA - [N24001090	1/2017	509.18 -	509.18	175.93	07/2019 -	07/2019
238	WASHIM TO DASTAPUR - [N24001068	3/2018	165.51 -	165.51	25.45	12/2019 -	12/2019
239	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	2/2017	422.02 422.00	422.02	224.01	07/2019 -	07/2019
240	PANDHARPUR TO SANGOLA - [N24001102	7/2017	218.38 -	218.38	168.75	07/2019 -	07/2019
241	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
242	CHIKLI TO TAKARKHED - [N24001083	3/2018	393.10 393.00	393.10	111.97	12/2019 -	12/2019
243	VITA TO NAGAJ - [N24001050	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
244	RALEGAON TO RAMTIRTH - [N24001046]	1/2017	210.81 -	210.81	106.69	07/2019 -	07/2019
245	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	76.29	04/2020 -	04/2020
246	MEHKAR TO AJISPUR - [N24001048]	1/2017	232.77 -	232.77	85.51	07/2019 -	07/2019
247	CHIKALI TO DHAD - [N24001061]	3/2018	189.46 189.00	189.46	21.00	12/2019 -	12/2019
248	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	95.97	12/2019 -	12/2019
249	KARASWADA TO BAMBOLIM - [N24001005]	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019
250	PARTUR TO MAJALGAON - [N24001034]	1/2017	420.57 -	420.57	157.39	07/2019 -	07/2019
251	KAIJ TO KUSALAM - [N24001037]	1/2017	554.78 -	554.78	157.90	07/2019 -	07/2019
252	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	44.02	08/2020 -	08/2020
253	NANDED TO JALKOT - [N24001069]	12/2017	456.93 457.00	456.93	55.50	09/2019 -	09/2019
254	PUNE TO MALE VILLAGE - [N24001078]	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
255	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020
256	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]	3/2018	294.87 295.00	294.87	36.30	12/2019 -	12/2019
257	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
258	PATGAON KHOPOLI SECTION I - [N24001028]	1/2018	170.00 -	170.00	15.57	12/2019 -	12/2019
259	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
260	SARSAM TO KOTHARI - [N24001002]	2/2016	545.64 -	545.64	64.01	07/2019 -	07/2019
261	SATARA TO MHASWAD - [N24001092]	1/2017	653.46 -	653.46	203.42	07/2019 -	07/2019
262	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]	3/2018	249.29 -	249.29	65.20	12/2019 -	12/2019
263	NAGBHID TO ARMORI - [N24001119]	9/2016	269.05 -	269.05	203.91	07/2019 -	07/2019
264	WADIGODRI TO DHANGRIPIMPRI - [N24001063]	3/2018	194.23 194.00	194.23	57.23	02/2020 -	02/2020
265	MANJUSUMBA TO CHUMBALI - [N24001031]	1/2017	228.54 -	228.54	92.30	08/2019 -	08/2019
266	PAHUR TO BODHWAD - [N24001084]	1/2017	244.93 -	244.93	34.23	05/2020 -	05/2020
267	DEULGAON SAKARSHA TO MEHKAR - [N24001076]	3/2018	219.91 -	219.91	106.46	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
268	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
269	KUNDRA TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	97.75	12/2019 -	12/2019
270	TASGAON TO SHIRDHON - [N24001054]	1/2017	195.64 196.00	195.64	93.73	11/2019 -	11/2019
271	AHMEDNAGAR TO BARAMATI - [N24001100]	1/2017	955.40 -	955.40	331.50	08/2019 -	08/2019
272	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
273	SANGOLA TO JATH - [N24001052]	1/2018	257.38 257.00	257.38	62.15	12/2019 -	12/2019
274	SALAIKHURD TO TIRORA - [N24001042]	1/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019
275	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	3/2018	336.21 336.00	336.21	58.66	12/2019 -	12/2019
276	MALEGAON TO RISOD - [N24001089]	2/2018	303.24 303.00	303.24	93.97	12/2019 -	12/2019
277	HELWAK TO KARAD - [N24001055]	2/2017	416.99 -	416.99	111.40	07/2019 -	07/2019
278	MUL TO CHANDRAPUR - [N24001117]	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019
279	ARNI TO NAIGAINBANDI - [N24001093]	12/2017	309.94 310.00	309.94	16.32	12/2019 -	12/2019
280	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	89.15	12/2019 -	12/2019
281	KURUDWADI TO PANDHARPUR - [N24001101]	1/2017	307.63 -	307.63	148.17	07/2019 -	07/2019
282	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
283	AJANTHA TO BULDHANA - [N24001008]	2/2017	401.00 401.00	401.00	82.81	07/2019 -	07/2019
284	SHAHAPUR PATGAON SECTION I - [N24001027]	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
285	SELDOH TO PANVAR - [N24001097]	7/2018	404.33 404.00	404.33	14.19	05/2020 -	05/2020
286	PATRADEVI TO KARASWADA 4L - [N24001004]	3/2017	634.32 -	634.32	108.33	05/2020 -	05/2020
287	NASRATPUR TO BARASGAON - [N24001112]	7/2016	406.54 407.00	406.54	142.00	09/2019 -	09/2019
288	JAHIRABAD TO LATUR - [N24001040]	1/2017	461.96 -	461.96	127.43	11/2019 -	11/2019
289	MANSAR TO SALAIKHURD - [N24001035]	1/2018	418.36 -	418.36	102.13	12/2019 -	12/2019
290	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	4.86	04/2020 -	04/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
291	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIKA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
292	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
293	SHIVUR TO YEOLA - [N24001059]	3/2018	181.08 -	181.08	7.45	12/2019 -	12/2019
294	MHASWAD TO TEMBHURNI - [N24001099]	1/2017	488.60 -	488.60	151.71	07/2019 -	07/2019
295	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]	1/2017	486.19 -	486.19	210.29	07/2019 -	07/2019
296	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	3/2018	217.14 217.00	217.14	58.77	02/2020 -	02/2020
297	PIMPLA TO MANJARUMBHA - [N24001030]	1/2017	595.77 -	595.77	118.44	08/2019 -	08/2019
298	JALGAON TO NANDURA - [N24001088]	3/2018	177.84 177.00	177.84	45.69	12/2019 -	12/2019
299	SHIROD SHAHPURER TO NANDED - [N24001041]	1/2017	211.34 -	211.34	100.83	07/2019 -	07/2019
300	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
301	BODHWAD TO STATE BORDER - [N24001086]	1/2017	178.26 -	178.26	96.95	07/2019 -	07/2019
302	NALDURG TO AKKALKOT - [N24001051]	2/2018	274.50 275.00	274.50	224.39	12/2019 -	12/2019
303	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
304	MAJALGAON TO KAIJ - [N24001036]	1/2017	413.99 -	413.99	310.33	07/2019 -	07/2019
305	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
306	JALKOT TO TOGRI - [N24001071]	7/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020
307	KARAD TO VITA - [N24001049]	1/2018	344.85 245.00	344.85	66.04	12/2019 -	12/2019
308	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	567.61	11/2019 -	11/2019
309	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	66.50	12/2019 -	12/2019
310	PALPHATA TO PHULAMBARI - [N24001060]	3/2018	227.19 227.00	227.19	50.23	12/2019 -	12/2019
311	WARDHA TO HINGAGHAT - [N24001098]	1/2018	216.90 217.00	216.90	20.00	12/2019 -	12/2019
312	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
313	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
314	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
315	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
316	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868	3/2018	253.44 -	253.44	-	07/2019 -	07/2019
317	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
318	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
319	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
320	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
322	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
323	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	69.68	03/2020 -	03/2020
324	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
325	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	608.81	04/2020 -	04/2020
326	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
327	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	2,525.80	1,449.00	09/2019 03/2020	09/2019
328	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020
	<u>National Highways Development Project</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
329	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	957.54 -	957.54	412.39	02/2020 -	02/2020
330	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	207.68	01/2020 -	01/2020
	Public Works Dept Of State						
331	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020
332	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
333	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
334	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983	1/2017	196.52 -	196.52	92.88	10/2019 -	10/2019
335	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	32.04	05/2020 -	05/2020
336	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175	10/2016	167.62 -	167.62	34.89	12/2020 -	12/2020
337	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	67.87	03/2020 -	03/2020
338	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
339	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	121.47	12/2019 -	12/2019
340	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	134.38	04/2020 -	04/2020
341	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	59.56	06/2020 -	06/2020
342	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	0.34	09/2020 -	09/2020
343	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	7.40	11/2019 -	11/2019
344	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
345	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	376.71	01/2020 -	01/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
346	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	74.49	11/2020 -	11/2020
347	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	336.25	44.91	09/2019 -	09/2019
348	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	46.62	07/2020 -	07/2020
349	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996	1/2017	605.08 -	605.08	213.00	10/2019 -	10/2019
350	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942	3/2016	208.50 -	208.50	102.98	11/2019 -	11/2019
351	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	20.09	10/2020 -	10/2020
352	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	0.50	09/2021 -	09/2021
353	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	94.93	06/2020 -	06/2020
354	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176	10/2016	172.63 -	172.63	35.30	12/2020 -	12/2020
355	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	80.71	12/2019 -	12/2019
356	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910	3/2018	170.57 -	170.57	46.23	11/2020 -	11/2020
357	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	125.09	09/2019 -	09/2019
358	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177	10/2016	171.90 -	171.90	14.17	08/2020 -	08/2020
359	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997	3/2018	192.67 -	192.67	-	07/2019 -	07/2019
360	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	171.00	01/2020 -	01/2020
361	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
362	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	23.54	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
363	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019
364	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]	3/2017	217.35 -	217.35	33.02	11/2020 -	11/2020
365	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
366	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]	3/2018	191.21 -	191.21	68.26	11/2019 -	11/2019
	Total		60,375.44 -	62,177.15	17,433.30		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
367	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	21.00	05/2021 -	05/2021
368	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	109.97	05/2020 -	05/2020
	<u>Inland Waterways Authority Of India</u>						
369	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	4,200.00	1,256.55	03/2023 -	03/2023
	Total		6,969.00 -	6,969.00	1,387.52		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
370	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	2.89	09/2020 -	09/2020
	Total		263.36 -	263.36	2.89		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
371	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
372	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019
373	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	47.30	05/2020 -	05/2020
374	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
375	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023
376	INDORE METRO RAIL - [N28000125	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023
	<u>National Building Construcion Corporation Ltd</u>						
377	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	Total		19,538.67 -	19,713.90	3,438.71		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
378	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA [N30000001	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Total		233.57 -	233.57	32.20		
	Grand Total		5,67,299.85	6,25,740.12	1,45,774.33		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

Costing Rs.150 Crore and above							
						(July 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63
	Total		27,271.00 -	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 -	860.00	03/2021 -	03/2021	.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
7	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
10	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
11	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	09/2017	11.42
12	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093 <u>South-Eastern Coal Fields Limited</u>	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
14	JAGANNATHPOR OCP(3.00MTY) - [N06000075 <u>Western Coal Fields Limited</u>	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
15	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
16	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
17	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		25,725.94 -	28,037.55			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
18	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
19	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
20	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
21	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
22	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	10/2018 -	11/2019	58.15
23	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33
24	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
25	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
26	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
27	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	08/2019	133.50
28	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
29	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	09/2015	4,199.00 -	5,060.00	03/2020 -	03/2020	20.50
	<u>Indian Oil Corporation Limited</u>						
30	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
31	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	12/2020 -	12/2020	66.09
32	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	08/2020	43.82
33	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
35	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	09/2019	26.44
36	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
37	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45
38	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
39	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
40	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	03/2023 -	03/2022	10.56
41	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	265.49	05/2020 -	05/2020	6.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
42	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48
43	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
44	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71
45	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17
	<u>Oil India Limited</u>						
46	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
47	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	02/2020	25.55
	Total		42,112.82 -	52,074.16			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
49	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
50	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
51	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
52	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	12/2020	96.99
53	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	06/2020	9.64
54	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55
55	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
56	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75
57	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	12/2021	33.47
58	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
59	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16
60	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55
61	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
62	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
63	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>						
64	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,419.34	12/2009 06/2016	08/2019	197.14
	<u>Power Grid Corporation Of India Limited</u>						
65	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
66	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
67	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	08/2019	38.61
68	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
69	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	06/2019	14.60
70	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	07/2019	26.82
71	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	08/2019	27.92
72	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17
73	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [N180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	08/2019	22.93
74	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
75	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Thdc India Limited</u>						
76	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75
77	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
78	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		1,54,828.95	2,28,724.99			
			-				
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
79	3RD LINE BETWEEN BHUSAVAL-JALGAON - [N22000247	04/2011	184.06	305.00	03/2019	12/2019	65.71
			-		-		
80	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	2,271.50	3,712.50	03/2021	03/2022	63.44
			-		-		
81	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00	5,341.68	03/2024	03/2024	120.28
			-		-		
82	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	02/2016	2,750.00	3,438.51	03/2024	-	25.04
			-		-		
83	DAUND - MANMAD (236 KM) - [N22000360	02/2016	1,876.00	2,081.27	03/2023	03/2023	10.94
			-		-		
	<u>Container Corporation Of India</u>						
84	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50	235.00	03/2019	12/2020	.21
			-		-		
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
85	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346	10/2006	11,589.00	28,181.00	-	-	143.17
			30,357.00		-		
86	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00	51,101.00	03/2020	03/2020	207.99
			51,101.00		-		
	<u>East Central Railways</u>						
87	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	03/1999	1,033.07	3,376.00	-	03/2021	226.79
			-		-		
88	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	528.65	2,066.77	-	03/2023	290.95
			-		-		
89	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88	749.00	03/2012	03/2020	56.73
			283.95		-		
90	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	04/1997	324.73	1,156.41	03/2012	03/2020	256.11
			-		-		
91	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87	589.15	-	03/2022	261.73
			-		-		
92	KOSI BRIDGE (NL), ECR - [220100304	04/2002	499.41	516.02	03/2020	03/2020	3.33
			-		-		
93	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00	519.33	-	02/2023	36.67
			-		-		
94	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344	07/2004	599.63	674.00	12/2007	-	12.40
			674.00		-		
95	ARA-BHABHUA ROAD (NL) - [N22000166	04/2008	633.87	2,396.88	-	03/2023	278.13
			-		-		
96	NAWADA-LAXMIPUR (NL) - [N22000167	04/2008	620.57	2,626.98	-	03/2024	323.32
			-		-		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
97	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	03/2024	542.46
98	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	03/2024	32.26
99	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15
100	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	- -	03/2021	124.59
101	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	- -	03/2022	590.61
102	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	03/2024	338.91
103	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	03/2024	252.66
104	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) [N22000180]	04/2004	372.14 -	1,470.50	- -	03/2021	295.15
105	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2022	43.41
106	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	400.17	- -	01/2020	87.86
107	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
108	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
109	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
110	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	727.29	- -	09/2019	302.22
111	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	12/2021	350.27
	<u>East Coast Railway</u>						
112	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
113	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	12/2023	29.96
114	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
115	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07
116	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
117	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
						(July 2019)	
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
118	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
119	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22
120	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80
121	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46
122	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2020	27.96
123	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	226.22	- -	03/2021	28.68
124	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
125	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01
126	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25
127	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15
128	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82
129	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	09/2021	6.48
130	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08
131	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30
132	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19
133	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
134	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	376.90	- -	03/2020	30.71
135	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	471.81	- -	05/2019	80.51
136	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
137	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20
	<u>Indian Railway Construction Company Limited</u>						
138	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
	<u>Metropolitan Rapid Transport Projects</u>						
139	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
140	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57
141	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	-	48.06
142	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
143	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	03/2015	188.33
144	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
145	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	03/2020	1.69
	<u>North East Frontier Railway</u>						
146	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
147	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80
148	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,300.00	12/2008 -	03/2021	179.62
149	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,524.00	03/2011 -	03/2020	181.17
150	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
151	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
152	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
153	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2022	7.86
154	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
						(July 2019)	
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
155	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,496.67	03/2019 -	-	38.86
156	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2022	71.62
157	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11
158	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
159	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
160	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2021	63.25
161	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
162	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
163	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	728.00	03/2019 -	03/2020	131.85
164	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
165	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
166	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,300.00	04/2010 -	-	241.57
	<u>North Eastern Railway</u>						
167	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
168	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08	12/2022 -	12/2022	234.77
169	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
170	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
171	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	-	267.13
172	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
173	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
174	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16
175	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
176	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
177	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	12/2021	116.16
178	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
179	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64
180	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
181	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15	- -	-	95.85
182	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47
183	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
184	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
185	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35
186	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	12/2019	69.36
	<u>Northern Railway</u>						
187	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	03/2024	25.87
188	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
189	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00	- -	03/2022	137.45
190	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	06/2020	57.68
191	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
192	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67
193	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	06/2022	1,017.96
194	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
195	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	855.00	03/2016 -	03/2021	36.80
	<u>Rail Vikas Nigam Ltd.</u>						
196	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
197	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	188.58
198	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
199	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
200	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
201	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
202	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
203	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
204	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
205	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
206	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00	03/2020 -	03/2020	173.31
207	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
208	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22
209	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						
210	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
211	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
212	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
213	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
214	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
215	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
216	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	1,352.74	03/2020 -	03/2020	92.07

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
217	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
218	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
219	KONDAPALLI-KOTHAGUEDEM - [N22000364]	04/2013	723.00 -	997.09	- -	-	37.91
220	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
	<u>South East Central Railway</u>						
221	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	- -	10/2019	268.37
222	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.00	04/2020 -	12/2020	243.06
223	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
224	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94
225	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95
226	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	12/2019 -	10/2019	40.65
227	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	1,973.66	03/2021 -	12/2021	.03
	<u>South Eastern Railway</u>						
228	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
229	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	11/2019	153.41
230	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	-	131.89
231	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	-	54.99
232	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
233	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	12/2018 -	06/2020	38.92
234	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	03/2020 -	06/2020	35.38
235	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	<u>South Western Railway</u>						
236	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
237	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
238	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
239	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
240	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
241	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
242	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98
243	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
244	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
245	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
246	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80
247	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
248	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	- -	-	339.33
249	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
250	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
251	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
252	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
253	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
254	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	951.24	- -	03/2020	2.07
255	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
256	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
257	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	-	253.33
258	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
259	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35
260	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
261	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32
	<u>Western Railway</u>						
262	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18
263	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	03/2011 -	03/2017	72.42
264	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06
265	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
266	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
267	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70
	Total		1,78,097.92 -	3,95,346.58			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
268	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	- -	-	3.72
	<u>Ministry Of Road Transport And Highways</u>						
269	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	- -	-	58.68
270	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
271	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
272	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382	01/1991	675.00 -	780.77	- -	-	15.67
273	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	08/2016 -	-	14.02
274	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42
275	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26
276	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643	12/2013	319.80 320.00	320.00	05/2016 -	-	.06
277	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02
278	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
279	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
280	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31
281	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.00	03/2017 -	-	46.45
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
282	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
	<u>National Highways Authority Of India</u>						
283	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	08/2019	92.75
284	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
285	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
286	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
287	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2020	106.50
288	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
289	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	12/2019	21.90
290	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
291	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
292	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	12/2017 -	12/2019	66.88
293	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	2,525.80	09/2019 -	09/2019	81.93
294	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
295	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25
296	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
297	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
298	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
299	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
300	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
301	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
302	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
303	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
304	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
305	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	09/2019	4.02
306	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
307	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
308	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
309	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
310	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	-	03/2021	22.44
	<u>National Highways Development Project</u>						
311	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	08/2019	46.51
312	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
	<u>Public Works Dept Of State</u>						
313	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
314	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
315	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
316	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	05/2012 -	-	88.11
317	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65
318	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
319	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	36.24
320	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	-	-	1.75
321	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06
322	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
323	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	02/2018 -	-	40.84
324	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
325	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67
326	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871	08/2014	600.87 720.97	720.97	11/2017 -	05/2019	19.99
327	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	11/2017 -	06/2019	13.92
328	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39
329	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51
330	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18
331	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	08/2017 -	07/2019	42.48
332	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954	01/2012	378.07 -	478.73	01/2014 -	-	26.62
333	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956	03/2009	501.00 -	671.54	09/2013 -	-	34.04
334	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46
	Total		37,589.35 -	55,162.90			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
335	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88
	<u>Mumbai Port Trust</u>						
336	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	-	82.72
	<u>Port Trust</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
337	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00 -	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
338	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	23,140.00 -	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
339	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	01/2018	231.80 -	240.10	10/2018 -	09/2019	3.58
	<u>Department Of Telecommunication</u>						
340	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,565.80 -	24,904.10			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
341	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROHAR AT ROHAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85
342	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2021	30.58
343	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	06/2014	157.84 -	169.16	03/2017 -	-	7.17
344	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57
345	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
346	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	12/2019	1.85
347	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	01/2019	790.79 -	800.00	06/2021 -	03/2022	1.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Chennai Metro Rail Ltd</u>						
348	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
349	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
350	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
351	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
352	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Kochi Metro Rail Corporation Ltd</u>						
353	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
354	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		29,058.09 -	35,281.91			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
355	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		5,37,474.24	9,43,308.81			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	13,838.00	12/2015 -	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	11,091.00	12/2016 -	12/2020	48	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	14,864.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	45,577.74					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6	.02	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	0	
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9	0	
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	0	
	Total		3,573.83 -	3,700.62	662.64					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
10	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	180.52	04/2014 -	11/2019	67	0	
11	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	244.43	05/2014 -	03/2020	70	0	
	<u>Central Coal Fields Limited</u>									
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120	0	
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	179.87	03/2012 -	03/2021	108	0	
14	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	362.47	03/2016 -	03/2021	60	0	
15	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.82	03/2014 -	03/2021	84	0	
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	354.48	07/2012 -	03/2022	116	0	
	<u>Eastern Coal Fields Limited</u>									
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	486.13	03/2018 -	03/2020	24	0	
	<u>Mahanadi Coal Fields Limited</u>									
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	0	
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	493.85	03/2017 -	03/2020	36	0	
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12	0	
21	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	75.78	03/2018 -	03/2020	24	0	
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	228.90	03/2012 -	03/2021	108	0	
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	390.94	03/2013 -	03/2021	96	0	
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022	108	0	
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022	144	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA <u>Neyveli Lignite Corporation</u>	05/2014	479.15 -	479.15	196.26	03/2019 -	03/2022	36	0	
27	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	709.06	448.19	06/2015 -	09/2019	51	-51.37	Due to unavailability of land, it was not possible to increase OB removal to the extent of 47.5 MM3 per annum as envisaged in Mining Plan to get 7.0 MTPA lignite exposures. Hence, it is required to keep Mine 1A expansion to 7.0 MTPA on hold till land is acquired and required OB removal capacity is attained. Land acquisition process was delayed due to lack of clarity about payment of compensation in the State land acquisition rules consequent to enactment of Acquisition, Rehabilitation and Resettlement Act, 2013 (Central Act 30 of 2013) and Land Acquisition Rehabilitation and resettlement (Amendment) Act 2015.
28	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU <u>Singareni Colliers Company Limited</u>	06/2011	5,907.11 7,080.41	7,080.41	6,567.64	12/2015 -	12/2019	48	19.86	
29	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.15	03/2015 -	03/2020	60	0	
30	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	0	
31	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	115.71	03/2015 -	03/2021	72	-32.3	
32	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	7.23	03/2015 -	03/2021	72	114.6	
33	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	5.85	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
34	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	54.00	03/2019 -	03/2021	24	0	
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132	16.86	
36	SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	296.92	03/2012 -	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
37	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	459.49	191.40	03/2015 -	03/2020	60	201.44	
38	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72	0	
39	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	177.65	03/2016 -	03/2020	48	0	
40	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24	0	
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	192.68	03/2014 -	03/2021	84	0	
	<u>Western Coal Fields Limited</u>									
42	ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA	08/2015	288.90 -	333.43	17.71	03/2023 -	03/2024	12	15.41	
43	KAMPTEE DEEP OC MINE - [N06000141]WCL, MAHARASHTRA	11/2015	277.65 -	313.34	115.28	03/2021 -	03/2024	36	12.85	
	Total		18,387.03 -	19,603.41	13,518.40					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA	10/2014	197.79 -	209.44	160.07	11/2016 -	09/2019	34	5.89	
	Total		197.79 -	209.44	160.07					
	<u>INFORMATION AND BROADCASTING</u>									
	<u>Central Public Works Department</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
45	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	0	
	Total		204.32 -	204.32	.00					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
46	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	23,140.00	15,811.82	05/2015 07/2020	07/2020	62	49.05	
	<u>Rastriya Ispat Nigam Limited</u>									
47	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,155.53	09/2018 09/2019	09/2019	12	0	No
48	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,292.76	12/2017 10/2019	10/2019	22	-12.53	No
49	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	206.91	08/2018 10/2019	10/2019	14	0	No
	<u>Steel Authority Of India Limited (SAIL)</u>									
50	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,970.60	04/2018 11/2019	11/2019	19	0	
51	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	927.19	12/2017 11/2019	11/2019	23	0	
52	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	431.27	10/2017 06/2020	06/2020	32	0	
53	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	99.71	06/2019 06/2020	06/2020	12	0	
	Total		25,964.87 -	33,221.87	22,895.79					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
54	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 1,097.54	1,097.54	693.14	10/2018 11/2019	11/2019	13	58.15	
55	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	3,518.66	08/2018 -	11/2019	15	14.33	
56	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 3,288.96	3,288.96	944.42	02/2020 10/2020	10/2020	8	-7.3	
57	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	0	
58	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	495.00	06/2019 -	02/2022	32	35.54	
	<u>Gas Authority Of India Limited</u>									
59	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	140.90	04/2018 -	08/2019	16	-38.98	
60	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 -	286.42	1.00	08/2020 09/2020	09/2020	1	0	
61	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,371.62	12/2012 -	02/2022	110	4.61	
	<u>Hindustan Petroleum Corporation Limited</u>									
62	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	689.03	10/2014 08/2019	08/2019	58	133.5	
	<u>Indian Oil Corporation Limited</u>									
63	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	2,573.02	09/2017 06/2019	07/2019	22	0	
64	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	08/2019	9	0	
65	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	250.31	08/2019 -	09/2019	1	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
66	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	306.24	01/2019 -	12/2019	11	0	
67	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	1,562.10	07/2019 -	12/2019	5	0	
68	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	22.66	06/2020 -	08/2020	2	0	
69	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	256.76	07/2018 -	10/2020	27	0	
70	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	38.51	02/2020 -	10/2020	8	0	
71	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	85.08	02/2020 -	10/2020	8	0	
72	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	454.65	12/2018 -	02/2021	26	33.98	
73	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	163.02	44.00	04/2020 -	03/2021	11	0	
74	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	34.07	01/2021 -	04/2021	3	0	
75	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	77.27	04/2021 -	07/2021	3	0	
76	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	26.83	10/2020 -	08/2021	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
77	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	27.05	01/2021 -	10/2021	9	0	
78	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	39.76	08/2021 -	11/2021	3	0	
79	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.07	04/2022 -	02/2023	10	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
80	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 170.70	170.70	154.03	03/2019 09/2019	09/2019	6	26.44	
81	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	726.57	12/2019 07/2020	07/2020	7	0	
82	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	68.27	03/2020 -	09/2020	6	6.88	
	<u>Oil & Natural Gas Corporation Limited</u>									
83	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 -	407.45	224.89	09/2018 09/2019	09/2019	12	-3.16	
84	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,783.74	05/2019 10/2019	10/2019	5	-4.01	
85	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	145.60	01/2014 -	11/2019	70	70.45	
86	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81	-3.5	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
87	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	1,683.06	1,285.65	05/2013 12/2019	12/2019	79	95.3	
88	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,059.63	1,908.01	03/2015 12/2019	12/2019	57	0	
89	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019	8	-12.72	
90	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	4,619.94	4,323.32	12/2017 03/2020	03/2020	27	0	
91	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 565.15	565.15	442.18	11/2019 03/2020	03/2020	4	3.48	
92	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020	14	0	
93	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,192.66	04/2018 05/2020	05/2020	25	1.77	
94	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	390.52	380.85	03/2019 05/2020	05/2020	14	-40	
95	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1	2.17	
96	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	3,011.57	06/2020 -	08/2021	14	0	
97	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 -	4,475.92	2,745.63	05/2021 12/2021	12/2021	7	11.71	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
98	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	-	12/2021 -	03/2022	3	0	
	<u>Oil India Limited</u>									
99	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	
100	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33	24.47	
	Total		1,08,790.72 -	1,12,546.03	47,382.44					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
101	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,152.85	04/2020 -	12/2023	44	0	
	<u>National Hydro-Electric Power Corporation</u>									
102	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,522.82	09/2009 -	12/2021	147	155.05	
	<u>National Thermal Power Corporation</u>									
103	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	12,229.51	10/2017 03/2020	03/2020	29	7.55	
104	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	12,027.37	01/2018 03/2020	03/2020	26	10.55	
105	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	6,334.35	07/2019 06/2020	06/2020	11	0	
106	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	9,460.46	12/2018 06/2020	06/2020	18	9.64	
107	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	9,703.00	02/2017 06/2020	06/2020	40	24.87	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
108	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	9,996.59	7,840.42	07/2012 -	09/2020	98	86.75	
109	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,110.76	03/2013 12/2020	12/2020	93	96.99	
110	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	5,231.15	11/2020 06/2021	06/2021	7	0	
111	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	16,249.55	10/2011 08/2021	08/2021	118	145.16	
112	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,044.25	06/2019 09/2019	09/2021	27	5.55	
113	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	13,670.00	05/2018 12/2021	12/2021	43	33.47	
114	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	473.97	09/2019 02/2022	02/2022	29	15.23	
	<u>North East Electric Power Corporation</u>									
115	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,419.34	7,419.34	7,494.35	12/2009 08/2019	08/2019	116	197.14	
	<u>Power Grid Corporation Of India Limited</u>									
116	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	340.88	251.33	03/2018 03/2019	07/2019	16	26.82	
117	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	1,429.38	1,011.38	01/2019 -	07/2019	6	0	
118	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	562.25	392.96	03/2019 03/2019	07/2019	4	0	
119	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	407.79	04/2019 04/2019	07/2019	3	0	
120	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	84.17	06/2019 -	07/2019	1	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
121	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,308.50	04/2019 -	07/2019	3	0	
122	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,237.45	11/2008 06/2019	08/2019	129	22.93	
123	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 08/2019	08/2019	40	38.61	
124	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	190.80	07/2017 06/2019	08/2019	25	27.92	
125	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	81.97	03/2018 03/2018	08/2019	17	0	
126	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	430.71	04/2019 04/2019	08/2019	4	0	
127	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	153.70	02/2019 06/2019	08/2019	6	0	
128	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019	63	31.17	
129	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	548.30	10/2017 09/2019	09/2019	23	0	
130	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4	0	
131	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	266.03	01/2019 09/2019	09/2019	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
132	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	92.78	09/2018 09/2019	09/2019	12	0	
133	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2	0	
134	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3	0	
135	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	117.15	06/2019 06/2019	10/2019	4	0	
136	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 12/2019	12/2019	86	5.14	
137	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	210.72	04/2016 03/2017	12/2019	44	0	
138	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 5,151.37	5,151.37	3,115.72	03/2018 12/2019	12/2019	21	0	
139	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	405.65	05/2017 06/2019	12/2019	31	0	
140	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12	90.82	
141	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10	0	
142	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	287.52	04/2018 01/2020	01/2020	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
143	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	0	
144	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	465.21	11/2016 12/2019	03/2020	40	4.61	
145	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	513.85	01/2018 12/2019	03/2020	26	0	
146	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 12/2018	12/2020	24	34.61	
147	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022	103	32.24	
	<u>Thdc India Limited</u>									
148	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	295.73	02/2014 -	10/2019	68	50.75	1-Following Statutory clearances are required: a- Firefighting – Pending with Deputy Director Uttar Pradesh Fire Service, Kanpur b-Electrical Safety- - Pending with Electrical Safety Officer Vidyut Suraksha Nideshalay Kanpur Region, GoUP. 2-Permission for River Diversion & water availability.- Pending with Principal Secretary(Energy) GoUP.
149	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	2,969.55	02/2016 -	06/2022	76	203.22	Renewal of lease for 3.0 Ha. land at Asena Quarry and transfer of additional 05 Ha. Forest land and permission for mining are pending. It needs to be expedited.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
150	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	4,397.80	1,718.70	06/2013	12/2022	114	76.51	1) There have been frequent hindrances by local villagers since mobilization of works in Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Still regular support of Distt. Administration is required for smooth and unobstructed execution of the project works. 2) Approval of Gadi quarry and crusher plant is pending with District Administration/ GoUK.
	Total		1,82,985.40	2,41,775.27	1,66,805.57					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>HII Infra Tech Services Limited</u>									
151	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00	785.00	244.66	04/2020	06/2020	2	0	
152	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00	703.00	184.93	06/2020	08/2020	2	0	
153	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00	875.00	39.27	05/2021	10/2021	5	0	
	<u>Hospital Services Consultancy Corporation</u>									
154	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19	272.19	140.58	03/2019	10/2019	7	0	
	<u>Hospital Services Consultancy Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
155	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27	0	
156	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	0	
157	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	0	
158	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	0	
159	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	0	
160	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	0	
161	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	24.1	
	Total		4,693.67 -	4,793.45	1,838.34					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
162	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	305.00	267.36	03/2019 12/2019	12/2019	9	65.71	
163	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,291.50	03/2021 -	03/2022	12	63.44	
164	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	792.89	297.30	03/2021 -	03/2022	12	0	
165	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	271.39	03/2022 -	03/2023	12	0	
166	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	220.34	03/2022 -	03/2024	24	0	
167	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	68.93	03/2022 -	03/2024	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
168	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	54.67	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									
169	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	260.88	03/2019 -	12/2019	9	0	
170	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	0	
171	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	150.61	03/2019 -	02/2020	11	0	
172	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	438.08	03/2018 -	03/2020	24	0	
173	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	286.56	03/2019 -	03/2020	12	0	
174	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	7.38	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
175	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	88.93	03/2019 -	12/2019	9	0	
176	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,156.41	1,028.71	03/2012 -	03/2020	96	256.11	
177	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	672.82	03/2012 -	03/2020	96	56.73	
178	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	446.51	03/2019 -	02/2021	23	0	
179	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	474.57	03/2020 -	03/2021	12	0	
180	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	390.91	03/2020 -	10/2021	19	0	
181	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	785.87	457.46	03/2020 -	03/2022	24	43.41	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
182	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	35.10	03/2021 -	03/2022	12	63.37	
183	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	15.39	03/2021 -	03/2022	12	62.06	
184	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	424.98	03/2020 -	12/2022	33	0	
	<u>East Coast Railway</u>									
185	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	116.91	11/2018 -	03/2021	28	15.45	
186	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	879.96	02/2019 -	03/2022	37	38.43	
187	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	349.23	12/2018 -	03/2022	39	0	
188	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	624.68	06/2021 -	03/2023	21	137.8	
189	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	125.30	10/2020 -	03/2023	29	0	
190	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	654.74	03/2020 -	03/2023	36	.07	
191	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	320.30	03/2022 -	03/2023	12	0	
192	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,354.80	03/2009 -	12/2023	177	29.96	
193	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	148.96	03/2022 -	03/2025	36	0	
	<u>Eastern Railways</u>									
194	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.47	11/2018 -	03/2021	28	0	
195	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024	133	134.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
196	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	862.50	03/2019 12/2009	03/2025	72	36.22	1. Acquisition of land in stretch of 7.008 KM between Kamarpukur and Mayanapur and pending over of 13.342 KM stretch possession to Railway. 2. Villagers of Vill. Bhabadighi, Hooghly District, are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non availability of land
197	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	827.99	12/2010 12/2017	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 232.99 Cr. for their balance share towards project Katwa- BWN G.C.
198	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects.
199	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	2,137.81	288.53	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 158.50 Crs. as share of expenditure incurred in this project..

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
200	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52	995.10	433.31	03/2016	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 For Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to religious structures in alignment and Amghata to Nabadwipghat work is held up due to 41 nos. of un authorized crossings.
201	CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51	769.40	102.27	03/2017	03/2025	96	29.2	Suri – Prantik New Line (33.90 km). The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
202	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28	266.32	153.62	03/2016	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
203	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17	296.43	200.07	03/2017	03/2025	96	-18.82	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non availability of land.
204	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54	494.59	32.00	03/2005	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bakrahat (9.75 Km) New line-- Work could not be started due to non availability of land

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
205	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	153.64	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
206	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	104.65	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
207	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
208	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 12/2020	12/2020	27	0	
209	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	619.50	03/2022 12/2022	12/2022	9	117.23	
210	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 1,700.43	1,700.43	48.00	03/2020 06/2023	06/2023	39	-67.3	
	<u>Metropolitan Rapid Transport Projects</u>									
211	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,403.52	03/2004 -	03/2021	204	501.57	
212	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 918.53	918.53	277.61	03/2014 03/2021	03/2021	84	-82.67	
213	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>North Central Railway</u>									
214	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	32.02	
	<u>North East Frontier Railway</u>									
215	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12	106.51	
216	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	8,821.88	03/2011 -	03/2020	108	181.17	
217	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 1,532.00	1,532.00	606.82	03/2019 -	03/2020	12	297.72	
218	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12	302.54	
219	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 728.00	728.00	691.97	03/2019 -	03/2020	12	131.85	
220	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 3,300.00	3,300.00	3,259.74	12/2008 -	03/2021	147	179.62	
221	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	3,000.00	759.42	03/2015 -	10/2021	79	28.95	
222	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	569.63 569.63	650.00	45.24	03/2020 03/2020	12/2021	21	14.11	
223	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 4,968.00	5,021.45	2,935.76	03/2014 03/2022	03/2022	96	109.8	
224	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	285.46	12/2015 06/2021	03/2020	51	204.95	
	<u>North Eastern Railway</u>									
225	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	307.99	01/2019 -	01/2020	12	61.8	
226	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER, UTTAR PRADESH	04/2017	622.50 427.00	426.74	163.75	04/2017 -	01/2020	33	-31.45	
227	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	213.35	5.45	04/2016 -	06/2020	50	.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
228	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	3.12	12/2019 -	04/2021	16	-12.65	
229	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
230	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
	<u>North Western Railway</u>									
231	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	136.88	10/2018 -	10/2019	12	24.47	
232	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	347.99	02/2019 -	12/2019	10	69.36	
233	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	244.02	260.89	11/2019 -	05/2020	6	14.35	
234	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	202.86	12/2019 -	06/2020	6	41.64	
235	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	152.83	03/2020 -	06/2020	3	0	
236	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	517.39	02/2019 -	12/2021	34	116.16	
237	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	39.52	03/2020 -	04/2022	25	14.33	
238	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	35.36	08/2022 -	09/2022	1	0	
	<u>Northern Railway</u>									
239	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	141.81	
240	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	855.00	834.59	03/2016 -	03/2021	60	36.8	
241	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	18,583.33	11/2002 -	06/2022	235	1017.96	
242	NANGALDAM-TALWARA(NL), NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140	346.67	
	<u>Rail Vikas Nigam Ltd.</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
243	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	385.00	386.28	03/2009 03/2009	12/2019	129	188.58	
244	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	1,185.64 -	1,844.47	1,729.78	12/2017 -	03/2020	27	55.57	
245	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,124.56	03/2019 -	03/2020	12	29.45	
246	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,016.52	03/2020 -	06/2020	3	-21.54	
247	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	682.17	03/2016 -	12/2020	57	29.06	
248	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	1,500.00	1,249.76	03/2020 -	03/2021	12	58.22	
249	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,120.00	992.67	03/2019 -	03/2021	24	18.78	
250	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,011.48	12/2020 -	03/2021	3	0	
251	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	1,202.70	861.32	02/2015 -	12/2021	82	0	
252	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,331.60	03/2020 -	03/2022	24	0	
253	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	750.56	327.46	03/2022 -	12/2024	33	-20.46	
254	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	462.05	03/2023 -	12/2024	21	0	
255	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,127.22	03/2016 -	03/2025	108	7.78	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
256	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	843.96	03/2016 -	03/2025	108	0	
257	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	18.95	
258	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,492.47	12/2024 -	03/2026	15	0	
	<u>South Central Railway</u>									
259	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252	0	
260	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	102.85	
261	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	0	
262	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	0	
263	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	0	
264	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	18.47	
265	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	0	
266	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	0	
	<u>South East Central Railway</u>									
267	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR, MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	646.68	02/2019 03/2020	06/2020	16	121.94	
268	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	511.86 1,756.00	1,756.00	1,660.29	04/2020 12/2020	12/2020	8	243.06	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
269	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR, CHHATISGARH	04/2015	1,973.00 1,973.66	1,973.66	129.54	03/2021 12/2021	12/2021	9	.03	
270	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR, MAHARASHTRA	06/2018	229.00 403.00	860.92	41.54	12/2021 03/2023	03/2023	15	275.95	
	<u>South Eastern Railway</u>									
271	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019	35	153.41	
272	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 358.68	358.68	231.84	12/2018 -	06/2020	18	38.92	
273	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA	11/2015	969.83 1,312.96	1,312.96	494.27	03/2020 -	06/2020	3	35.38	
274	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER, JHARKHAND	03/2016	1,724.20 -	1,724.20	332.04	03/2021 -	12/2021	9	0	
	<u>South Western Railway</u>									
275	KADUR CHIKMAGALUR SAKLIESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	37.96	
276	HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-1.38	
277	HOTGI-KUDGI-GADAG - [N22000333]SWR, MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	15.84	
278	BAGALKOT-KUDACHI NL - [N22000258]SWR, KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	0	
279	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	0	
280	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	
281	SHIMOGA-HARIHAR NL - [N22000278]SWR, KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
282	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	0	
	<u>Southern Railway</u>									
283	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR, MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	1391.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
284	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	185.98	
285	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	23.72	
286	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	222.39	
287	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	55.57	
288	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									
289	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 1,763.93	1,763.93	624.49	03/2020 03/2022	03/2022	24	0	
290	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	154.63	03/2022 09/2022	09/2022	6	114.32	
291	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023	178	2360.35	
292	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 2,909.99	2,909.99	1,027.12	03/2021 03/2023	03/2023	24	585.35	
293	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	367.59	03/2022 03/2023	03/2023	12	0	
	<u>Western Railway</u>									
294	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	809.07	616.90	03/2019 03/2020	03/2020	12	46.7	
295	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	1,310.23	1,363.06	03/2020 03/2021	03/2021	12	57.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
296	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	663.29	163.85	03/2020 03/2021	03/2021	12	-4.13	
297	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	86.45	06/2020 06/2021	06/2021	12	-13.76	
298	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120	1.06	
299	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36	167.87	
300	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	1,037.15	992.18	03/2021 03/2022	03/2022	12	0	
301	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,338.15	3,860.40	1,676.43	03/2022 03/2023	03/2023	12	10.18	
302	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	682.91	03/2022 03/2023	03/2023	12	0	
	Total		1,75,159.00 -	2,56,812.50	1,08,007.49					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
303	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	621.43	387.00	06/2018 -	07/2019	13	0	
304	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.00	454.41	03/2017 -	07/2019	28	46.45	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
305	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 - [N24000971]MORTH,ANDHRA PRADESH	08/2016	574.19 -	574.19	456.98	07/2017 07/2019	07/2019	24	0	
306	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH	01/2016	386.09 -	386.09	160.20	05/2016 08/2019	08/2019	39	0	
307	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	180.38	08/2017 03/2020	08/2019	24	0	
308	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA	01/2017	463.62 664.00	463.62	243.34	06/2019 -	08/2019	2	0	
309	AMD I TO SAONER - [N24001021]MORTH,MAHARASHTRA	01/2017	396.91 396.91	396.91	247.48	06/2019 -	08/2019	2	0	
310	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	86.63	08/2015 -	09/2019	49	0	
311	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH	09/2016	372.68 -	372.68	179.43	02/2017 09/2019	09/2019	31	0	
312	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	43.79	09/2017 03/2020	09/2019	24	0	
313	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	260.00	06/2019 -	10/2019	4	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
314	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	.02	
315	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH	11/2016	290.15 -	290.15	69.42	05/2017 11/2019	11/2019	30	0	
316	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	181.17	11/2017 03/2020	11/2019	24	0	
317	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	29.83	06/2019 -	11/2019	5	0	
318	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	83.81	11/2018 -	11/2019	12	0	
319	WIDENING AND STRENGTHENING OF EXISTING SLIL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	.26	
320	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	0	
321	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH	10/2015	333.21 -	333.21	256.29	12/2015 12/2019	12/2019	48	0	
322	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	301.70	01/2017 12/2019	12/2019	35	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
323	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MORTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	144.95	08/2016 12/2019	12/2019	40	0	
324	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	208.09	09/2016 12/2019	12/2019	39	0	
325	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	101.79	05/2019 -	12/2019	7	0	
326	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	136.43	05/2019 -	12/2019	7	0	
327	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	184.75	06/2019 -	12/2019	6	0	
328	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	156.29	06/2019 -	12/2019	6	0	
329	NAGAJ TO VAIJAPUR - [N24001023]MORTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	149.81	06/2019 -	12/2019	6	0	
330	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA	01/2017	355.17 355.17	355.17	141.87	07/2019 -	12/2019	5	0	
331	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	67.26	06/2019 -	12/2019	6	0	
332	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	15.94	03/2019 -	12/2019	9	0	
333	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	23.71	03/2019 -	12/2019	9	0	
334	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
335	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-11.07	
336	REHABILITATION AND UPGRADE OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH	11/2016	378.24 -	378.24	187.63	01/2018 01/2020	01/2020	24	0	
337	REHABILITATION AND UPGRADE OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (-) [N24000938]MORTH,ANDHRA PRADESH	03/2018	297.12 294.00	297.12	138.68	07/2018 01/2020	01/2020	18	0	
338	REHABILITATION AND UPGRADE OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	177.36	01/2018 01/2020	01/2020	24	0	
339	REHABILITATION AND UPGRADE OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH	03/2018	244.95 245.00	244.95	84.47	08/2018 02/2020	02/2020	18	0	
340	REHABILITATION AND UPGRADE OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	60.76	08/2018 02/2020	02/2020	18	0	
341	REHABILITATION AND UPGRADE OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	103.64	08/2018 02/2020	02/2020	18	0	
342	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	130.85	02/2019 -	02/2020	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
343	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	101.28	08/2017 03/2020	03/2020	31	0	
344	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	26.78	08/2018 03/2020	03/2020	19	0	
345	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	401.90	05/2016 03/2020	03/2020	46	0	
346	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	652.90	12/2019 -	03/2020	3	0	
347	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	746.91	11/2019 -	03/2020	4	0	
348	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	23.73	04/2019 -	04/2020	12	0	
349	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	269.70	11/2018 05/2020	05/2020	18	0	
350	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	23.03	05/2019 -	05/2020	12	0	
351	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	155.78	05/2019 -	05/2020	12	0	
352	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	84.00	06/2019 -	06/2020	12	0	
353	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	73.97	06/2019 -	06/2020	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
354	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	12.00	06/2019 -	06/2020	12	0	
355	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	0	
356	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	26.42	06/2019 -	06/2020	12	0	
357	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	202.31	07/2019 -	07/2020	12	0	
358	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12	0	
359	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	24.00	09/2018 -	04/2021	31	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
360	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	42.66	05/2019 -	07/2019	2	0	
361	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	194.11	174.80	05/2018 -	08/2019	15	0	
362	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	187.25	08/2016 -	08/2019	36	0	
363	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	229.11	08/2016 -	08/2019	36	0	
364	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	153.61	08/2016 -	08/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
365	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36	0	
366	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	17.42	01/2017 -	01/2020	36	11.57	
367	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	240.21	06/2018 -	03/2020	21	0	
368	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	28.67	04/2017 02/2018	02/2021	46	0	
369	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46	0	
370	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	15.77	04/2017 02/2018	02/2021	46	0	
371	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	18.70	04/2017 02/2018	02/2021	46	0	
372	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	46.85	04/2017 03/2018	03/2021	47	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
373	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	457.77	119.56	10/2018 -	10/2021	36	-11.55	
374	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60	0	
	<u>National Highways Authority Of India</u>									
375	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019	76	0	
376	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	574.28	448.92	07/2018 -	07/2019	12	0	
377	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019	24	0	
378	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	1,423.96	691.30	11/2018 -	07/2019	8	0	
379	4-LANNING OF MAHULIA BAHARAGORA-JHWB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 -	997.15	728.62	03/2019 -	07/2019	4	0	
380	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	319.96	04/2009 -	08/2019	124	92.75	
381	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019	112	0	
382	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	1,387.11	966.02	11/2017 -	08/2019	21	0	
383	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	08/2019	20	0	
384	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	417.86	06/2016 -	08/2019	38	0	
385	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	09/2019	138	-28.84	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
386	TWO LANNING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	475.02	05/2018 -	09/2019	16	0	
387	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	0	
388	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	0	
389	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13	0	
390	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	219.09	05/2019 -	09/2019	4	0	
391	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019	136	0	
392	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	0	
393	FOUR LANNING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,154.18	12/2018 -	10/2019	10	0	
394	FOUR LANNING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	387.97	05/2018 10/2019	10/2019	17	0	
395	TWO LANNING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	0	
396	FOUR LANNING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
397	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7	0	
398	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6	0	
399	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8	0	
400	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	20.54	06/2017 -	11/2019	29	0	
401	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	0	
402	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	95.96	09/2017 -	11/2019	26	0	
403	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019	140	10.58	
404	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	0	
405	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	0	
406	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	0	
407	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	0	
408	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	0	
409	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
410	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019	39	21.9	
411	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	453.95	09/2017 -	12/2019	27	0	
412	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	0	
413	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019	24	66.88	
414	CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	0	
415	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	402.47	06/2018 -	01/2020	19	0	
416	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17	0	
417	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	0	
418	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	02/2020	76	-11	
419	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 -	02/2020	19	19.25	
420	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	0	
421	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020	100	106.5	
422	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	750.38	06/2014 -	03/2020	69	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
423	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,119.56	08/2018 -	03/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
424	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 598.13	598.13	394.83	04/2018 03/2020	03/2020	23	-17.69	The CALA, Raipur had submitted proposal of additional 3A area for 12.6814 Ha (missing Khasra/plot no.) . 3A notification was published in Gazette on 04.07.2018 but CALA, Raipur did not provide revenue/ Khasra map to NHAI inspite of repeated request. In 680m length work was held up due to non-payment of land compensation to land owners, so NHAI has processed the 3D notification for 2.561Ha private land considering urgency at project site without revenue khasra map plan and balance 3D for area 10.1204 Ha was kept in hold due to non-receipt of Revenue Khasra map plan from CALA, Raipur. 3D of 2.561 Ha. land was published on 24.08.2018 . In spite of repeated request to CALA, Raipur has not submitted revenue Khasra map plan showing 12.6814Ha land so the 3A notification dated 04.07.2018 balance area 10.1204Ha has lapsed on 03.07.2019. Some land owners (which land 3A was published on 04.07.2018 but 3D not published due to want of revenue Khasra map plan) have filed writ petition in Bilaspur High Court and Court passed order that land compensation should be paid to land owners within 09 months from the date of order after duly verification of land proposed in the acquisition. The land acquisition map showing RoW width for 25 villages are still not submitted by SDM Raipur & SDM Simga due to which 3A for balance 10.1204Ha of land could not be processed.
					41					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
425	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	304.69	08/2018 -	03/2020	19	0	
426	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	0	
427	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	76.83	03/2020 -	04/2020	1	.23	
428	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	347.91	05/2018 -	05/2020	24	0	
429	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	708.62	11/2016 -	05/2020	42	0	
430	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	431.21	07/2018 -	05/2020	22	0	
431	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	607.37	02/2020 -	05/2020	3	0	
432	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	3.4	
433	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FROM - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
434	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	687.88	03/2020 -	05/2020	2	13.97	
435	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	405.31	07/2016 -	05/2020	46	0	
436	4-LANING OF BRAHAMPUR- FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	0	
437	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	0	
438	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	529.62	05/2018 -	06/2020	25	-12	
439	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	06/2020	25	0	
440	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	1,167.42	254.96	03/2019 -	06/2020	15	0	
441	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	604.76	03/2020 -	06/2020	3	44.39	
442	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	256.47	09/2017 -	06/2020	33	0	
443	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	551.42	03/2020 -	07/2020	4	41.54	
444	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
445	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	10.58	
446	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	5.56	
447	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	5.7	
448	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	0	
449	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	-	09/2017 -	08/2020	35	0	
450	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	-	08/2017 -	09/2020	37	0	
451	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	0	
452	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	16.09	03/2019 -	11/2020	20	0	
453	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	0	
454	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	480.96	03/2017 -	11/2020	44	1.06	
455	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
456	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	329.90	10/2017 -	11/2020	37	0	
457	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31	0	
458	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	0	
459	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	301.68	06/2019 -	12/2020	18	0	
460	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17	0	
461	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17	0	
462	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	950.69	803.81	08/2019 -	12/2020	16	0	
463	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	0	
464	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	221.91	03/2020 -	03/2021	12	10.24	
465	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	129.48	03/2019 -	04/2021	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
466	FOUR LANE OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,532.62	-	03/2021 -	04/2021	1	0	
467	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-3.27	
468	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	0	
469	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	0	
	<u>National Highways Development Project</u>									
470	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019	29	46.51	
471	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	410.72	-	04/2015 -	08/2019	52	0	
472	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020	36	77.26	
	<u>Public Works Dept Of State</u>									
473	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	244.54	122.31	05/2019 -	07/2019	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
474	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	07/2019	9	0	
475	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	86.63	08/2015 -	07/2019	47	0	
476	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.52	398.52	314.63	08/2017 07/2019	07/2019	23	42.48	
477	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	276.01	180.95	03/2019 07/2019	07/2019	4	0	
478	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70	0	
479	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	11	0	
480	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	359.27	200.24	05/2019 -	08/2019	3	0	
481	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24	0	
482	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
483	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	247.25	144.00	03/2019 03/2020	09/2019	6	0	
484	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	143.44	10/2015 11/2019	11/2019	49	0	
485	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL	03/2016	271.17 291.20	291.20	79.43	11/2018 11/2019	11/2019	12	7.39	
486	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	83.40	02/2018 -	11/2019	21	0	
487	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	54.49	02/2018 -	11/2019	21	0	
488	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	15.22	03/2018 -	11/2019	20	0	
489	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	93.96	03/2018 -	11/2019	20	0	
490	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	117.16	02/2018 -	11/2019	21	0	
491	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
492	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	383.94	06/2019 -	11/2019	5	0	
493	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	224.94	03/2018 -	11/2019	20	0	
494	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	36.24	
495	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019	105	58.98	
496	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	69.3	
497	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76	0	
498	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	47.65	
499	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	0	
500	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	66.95	03/2018 -	12/2019	21	0	
501	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	62.22	02/2019 -	12/2019	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
502	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	79.02	03/2019 -	12/2019	9	0	
503	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	83.83	05/2019 -	12/2019	7	0	
504	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	0	
505	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	305.61	269.07	09/2014 -	12/2019	63	63.46	
506	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	100.10	07/2018 -	01/2020	18	0	
507	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	237.15	08/2017 -	02/2020	30	0	
508	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	198.65	07/2018 -	02/2020	19	0	
509	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54	0	
510	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	53.59	03/2018 -	04/2020	25	0	
511	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	373.82	116.33	09/2019 -	05/2020	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
512	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	0	
513	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	296.28	10/2010 -	06/2020	116	93.8	
514	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	17.10	08/2018 -	06/2020	22	0	
515	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39	0	
516	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	12.39	08/2018 -	06/2020	22	0	
517	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	7.10	03/2018 -	07/2020	28	0	
518	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	0	
519	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	
520	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	33.51	
521	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	11.18	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		1,27,865.13	1,33,024.22	79,842.51					
	<u>SHIPPING AND PORTS</u>									
	<u>Kamarajar Port Limited</u>									
522	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-57.02	
	Total		600.00 -	257.90	1.45					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
523	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	240.10	117.63	10/2018 09/2019	09/2019	11	3.58	
	<u>Department Of Telecommunication</u>									
524	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	84.97	
	Total		13,565.80 -	24,904.10	8,514.63					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
525	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	5,854.77	12/2018 -	07/2020	19	0	
	<u>Bangalore Metro Rail Corporation Limited</u>									
526	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									
527	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	126.07	04/2018 -	07/2019	15	0	
528	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
529	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	488.28	422.79	05/2017 -	09/2019	28	25.85	
530	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38	0	
531	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59	0	
532	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
533	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	326.38	07/2019 12/2019	12/2019	5	1.85	
534	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	193.89	04/2019 -	02/2020	10	0	
535	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	86.04	10/2012 -	03/2020	89	0	
536	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	127.69	10/2019 -	03/2020	5	0	
537	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	42.30	04/2019 -	06/2020	14	0	
538	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	80.08	03/2016 -	09/2020	54	0	
539	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	62.56	02/2020 -	09/2020	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
						Date of Commissioning (Month/Year)				(July 2019)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
540	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	29.51	07/2020 09/2020	09/2020	2	0	
541	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	0	
542	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	69.60	06/2017 -	10/2020	40	.57	
543	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	60.28	05/2020 -	01/2021	8	0	
544	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	313.93	10/2019 -	03/2021	17	30.58	
545	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 02/2017	05/2021	14	0	
546	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	800.00	2.56	06/2021 -	03/2022	9	1.16	
	<u>Hindustan Steelwork Construction Limited</u>									
547	IRRIGATION WORK OF BAGMATI - [N12000108]HISCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
548	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	9.76	
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
549	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11,420.00	2,642.09	11/2021 01/2022	01/2022	2	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(July 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
550	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
551	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	8,680.00	5,989.97	03/2018 -	12/2019	21	0	
	Total		93,270.17 -	94,423.16	23,295.63					
	<u>WATER RESOURCES</u>									
	<u>Polavaram Project Authority</u>									
552	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	447.22	
	Total		10,151.04 -	55,548.87	16,417.99					
	Grand Total		8,32,528.77	10,61,373.16	5,34,920.69					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

Costing Rs.150 Crore and above								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88	133
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63	48
	Total		27,271.00 -	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02	6
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		653.54 -	780.33				
	<u>COAL</u>							
	<u>Neyveli Lignite Corporation</u>							
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86	48
	<u>Singareni Colliers Company Limited</u>							
7	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
9	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85	72
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
13	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
	Total		7,903.91 -	9,947.65				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
14	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89	34
	Total		197.79 -	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
15	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10	83
	Total		414.11 -	513.89				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
16	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	10/2018 -	11/2019	58.15	13
17	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	06/2019 -	02/2022	35.54	32
18	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33	15
	<u>Gas Authority Of India Limited</u>							
19	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61	110
	<u>Hindustan Petroleum Corporation Limited</u>							
20	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	10/2014 -	08/2019	133.50	58
	<u>Indian Oil Corporation Limited</u>							
21	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98	26
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
22	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE [N16000256	10/2015	135.00 171.00	170.70	03/2019 -	09/2019	26.44	6

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
23	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88	6
	<u>Oil & Natural Gas Corporation Limited</u>							
24	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45	70
25	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48	4
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30	79
27	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77	25
28	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17	1
29	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71	7
	<u>Oil India Limited</u>							
30	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47	33
	Total		27,653.77 -	32,936.44				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
31	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06	147
	<u>National Thermal Power Corporation</u>							
32	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23	29
33	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	12/2020	96.99	93
34	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75	98
35	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87	40
36	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55	29
37	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55	26
38	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	06/2020	9.64	18

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55	27
40	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	12/2021	33.47	43
41	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16	118
	<u>North East Electric Power Corporation</u>							
42	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,419.34	12/2009 06/2016	08/2019	197.14	116
	<u>Power Grid Corporation Of India Limited</u>							
43	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	08/2019	27.92	25
44	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	07/2019	26.82	16
45	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61	40
46	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17	63
47	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	08/2019	38.61	40
48	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	08/2019	22.93	129
49	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14	86
50	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61	24
51	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82	12
52	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24	103
	<u>Thdc India Limited</u>							
53	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75	68
54	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51	114
55	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22	76
	Total		1,32,711.57 -	1,91,501.44				
	<u>RAILWAYS</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Central Railways</u>							
56	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71	9
57	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44	12
	<u>Container Corporation Of India</u>							
58	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							
59	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73	96
60	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2022	43.41	24
61	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11	96
62	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
63	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
	<u>East Coast Railway</u>							
64	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45	28
65	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07	36
66	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43	37
67	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
68	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	12/2023	29.96	177
	<u>Eastern Railways</u>							
69	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
70	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE- PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
71	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
72	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
74	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
75	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
76	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
77	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
78	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23	9
	<u>Metropolitan Rapid Transport Projects</u>							
79	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57	204
80	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>							
81	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
82	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
83	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11	21
84	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	728.00	03/2019 -	03/2020	131.85	12
85	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
86	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
87	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95	79
88	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	3,300.00	12/2008 -	03/2021	179.62	147
89	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95	51
90	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
91	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,524.00	03/2011 -	03/2020	181.17	108
	<u>North Eastern Railway</u>							
92	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16	50
93	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80	12
	<u>North Western Railway</u>							
94	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35	6
95	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47	12
96	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64	6
97	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	12/2019	69.36	10
98	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33	25
99	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	12/2021	116.16	34
	<u>Northern Railway</u>							
100	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81	111
101	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	855.00	03/2016 -	03/2021	36.80	60
102	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67	140
103	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	06/2022	1,017.96	235
	<u>Rail Vikas Nigam Ltd.</u>							
104	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	188.58	129
105	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
106	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78	24
107	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45	12
108	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22	12
109	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57	27
110	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
111	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98	4,259.48	03/2016	03/2025	7.78	108
	<u>South Central Railway</u>							
112	KOTLAPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20	2,120.16	03/2009	03/2023	102.85	168
113	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95	2,200.00	03/2023	03/2024	18.47	12
	<u>South East Central Railway</u>							
114	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	860.92	12/2021	03/2023	275.95	15
115	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93	1,300.44	02/2019	06/2020	121.94	16
116	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86	1,756.00	04/2020	12/2020	243.06	8
117	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00	1,973.66	03/2021	12/2021	.03	9
	<u>South Eastern Railway</u>							
118	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20	358.68	12/2018	06/2020	38.92	18
119	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77	377.00	12/2016	11/2019	153.41	35
120	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83	1,312.96	03/2020	06/2020	35.38	3
	<u>South Western Railway</u>							
121	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78	889.52	03/2017	03/2020	37.96	36
122	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59	1,870.41	03/2019	03/2021	15.84	24
	<u>Southern Railway</u>							
123	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26	231.67	04/2014	03/2020	23.72	71
124	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98	980.00	03/2020	03/2021	222.39	12
125	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00	1,182.31	03/2020	06/2021	55.57	15
126	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70	1,800.00	03/2019	12/2019	1,391.30	9
127	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]	09/2007	724.69	2,072.50	02/2019	02/2020	185.98	12
	<u>West Central Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
128	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32	6
129	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
130	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
131	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06	120
132	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70	12
133	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
134	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91	12
135	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18	12
	Total		78,571.46 -	1,69,181.44				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways</u>							
136	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02	41
137	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26	43
138	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.00	03/2017 -	-	46.45	28
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
139	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
140	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58	140
141	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	08/2019	92.75	124
142	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25	19

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
143	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	12/2017 -	12/2019	66.88	24
144	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
145	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
146	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
147	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
148	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
149	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54	4
150	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
151	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
152	REHABILITATION AND UPGRADEMENT BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24	12
153	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
154	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	12/2019	21.90	39
155	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2020	106.50	100
<u>National Highways Development Project</u>								
156	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	08/2019	46.51	29
157	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26	36
<u>Public Works Dept Of State</u>								
158	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
159	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18	24
160	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65	82
161	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39	12
162	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46	63
163	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30	110
164	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	36.24	27
165	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80	116
166	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	08/2017 -	07/2019	42.48	23
167	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98	105
	Total		18,583.06 -	24,035.87				
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
168	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05	62
	Total		15,525.00 -	23,140.00				
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
169	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	01/2018	231.80 -	240.10	10/2018 -	09/2019	3.58	11
	<u>Department Of Telecommunication</u>							
170	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58
	Total		13,565.80 -	24,904.10				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above								
(July 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
171	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
172	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85	28
173	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57	40
174	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	559.47	07/2019 -	12/2019	1.85	5
175	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126	01/2019	790.79 -	800.00	06/2021 -	03/2022	1.16	9
176	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2021	30.58	17
	<u>Kochi Metro Rail Corporation Ltd</u>							
177	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77	29
	Total		8,739.54 -	9,892.53				
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
178	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22	15
	Total		10,151.04 -	55,548.87				
	Grand Total		3,41,941.59	5,83,091.00				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs.150 Crore and above					
				(July 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-
2	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	-
3	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Singareni Colliers Company Limited</u>				
4	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	06/2015 -	12/2015
5	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	03/2016 -	12/2016
6	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	07/2016 -	04/2017
7	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	03/2019 -	09/2017
8	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
9	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 -	-
10	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	- 04/2017	-
	<u>South-Eastern Coal Fields Limited</u>				
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	03/2016 -	-
	<u>Western Coal Fields Limited</u>				
12	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA	10/2016	164.96 -	03/2019 -	03/2019
13	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	03/2018 -	-
14	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
15	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
16	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
	Total		6,505.91 -		
	<u>INFORMATION AND BROADCASTING</u>				
	<u>National Film Archive Of India</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
17	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA	11/2014	597.41 -	- -	-
	Total		597.41 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
18	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 -	06/2019 -	-
	Total		166.62 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
19	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
20	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
21	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	-
	<u>Indian Oil Corporation Limited</u>				
22	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH	02/2016	151.00 -	09/2019 -	06/2019
23	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	10/2017 -	-
24	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	- -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>				
26	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA	05/2015	224.00 207.00	04/2019 06/2019	10/2018
	<u>Oil India Limited</u>				
27	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		7,654.97 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
30	LOKTAK D/S HEP(NHPC) - [180100078]NHPC, MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
31	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
32	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
33	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
	<u>Power Grid Corporation Of India Limited</u>				
34	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL, MULTI STATE	02/2014	196.58 -	02/2016 04/2019	06/2019
35	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL, MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019
	Total		20,998.56 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
36	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-
37	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	03/2018 -	-
38	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	-
	Total		925.15 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
39	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
40	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
41	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
42	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
43	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
44	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR	07/2004	599.63 674.00	12/2007 -	-
45	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>Eastern Railways</u>				
46	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				
47	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
48	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
49	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 -	-
50	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
51	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 314.09	12/2008 03/2015	03/2015
	<u>North East Frontier Railway</u>				
52	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	-
53	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-
54	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
55	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
	<u>North Eastern Railway</u>				
56	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
57	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
58	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	-
59	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
60	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
61	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
62	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-
	<u>North Western Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
64	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
65	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
66	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
67	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
68	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
69	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
70	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
71	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
72	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
73	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
74	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
75	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 997.09	- -	-
76	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South Eastern Railway</u>				
77	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
78	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR	08/2010	400.00 -	03/2014 -	-
79	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
80	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
81	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	-
82	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-
	<u>Southern Railway</u>				
83	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
84	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
85	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
86	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
87	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
88	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
89	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
90	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-
91	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-
92	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
93	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-
94	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-
95	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
96	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
97	ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
98	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017
99	GANDHINAGAR REDEVELOPMENT OF STATION ALOGLWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
100	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
101	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
102	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
103	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		57,102.22 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Dept Of Road Transport & Highways</u>				
104	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
105	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
106	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
107	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
108	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
109	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
110	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
111	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
112	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
113	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
114	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
115	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
116	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
117	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
118	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
119	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
120	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
121	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
122	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
123	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
124	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
125	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-
126	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
127	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
128	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
129	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
130	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
131	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
132	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
133	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
134	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
135	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
136	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
137	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
138	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
139	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
140	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
141	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
142	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
143	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
144	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-
145	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-
146	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
147	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
148	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-
149	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-
150	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA	03/2016	165.06 -	12/2016 -	-
151	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA	08/2016	287.70 -	02/2017 -	-
152	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA	09/2016	295.67 -	02/2017 -	-
153	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA	12/2016	223.50 -	08/2018 -	-
154	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA	12/2016	206.88 -	04/2018 -	-
155	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA	03/2018	214.23 -	08/2018 -	-
156	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA	03/2018	199.16 -	08/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA - [N24000918]MORTH,ODISHA	07/2013	251.92 -	10/2015 -	-
158	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA - [N24000919]MORTH,ODISHA	07/2013	265.35 -	10/2015 -	-
159	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA - [N24000924]MORTH,ODISHA	03/2015	229.29 -	11/2015 -	-
160	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR	09/2018	1,478.40 -	- -	-
161	AKOLA TO AKOT - [N24001003]MORTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
162	AKOT TO ANJANGAON - [N24001006]MORTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
163	ANJANGAON TO MAH/MP BORDER - [N24001007]MORTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
164	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
165	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
166	DAHEGAON TO KUHI - [N24001017]MORTH,MAHARASHTRA	01/2017	228.89 228.89	06/2019 -	-
167	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
168	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA	01/2017	356.66 356.66	- -	-
169	KALMAB TO RALEGAON - [N24001044]MORTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
170	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-
171	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
172	GADCHIROLI TO MUL - [N24001116]MORTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
173	PAITHAN TO SHIRUR - [N24001122]MORTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
174	SHIRUR TO KHARDA - [N24001123]MORTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
175	AURANGABAD TO SILLOD - [N24001124]MORTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
176	SILLOD TO FARDAPUR - [N24001125]MORTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
177	FARDAPUR TO JALGAON - [N24001126]MORTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
178	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
179	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
180	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
181	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	-
182	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	-
183	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	06/2018 -	-
184	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
185	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
186	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
187	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
188	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 12/2019	-
189	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
190	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
191	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
192	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
193	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	-
194	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
195	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
196	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
197	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
198	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
199	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
200	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
201	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
202	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
203	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
204	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
205	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
206	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
207	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
208	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
209	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
210	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
211	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-
212	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-
213	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
214	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
215	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
216	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
217	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
218	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
219	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
220	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
221	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
222	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-
223	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
224	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
225	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
226	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
227	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
228	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
229	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
230	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866])NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
232	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
233	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
234	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
235	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-
236	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
237	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
238	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-
239	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
240	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
241	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	-
<u>National Highways Authority Of India</u>					
242	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018
243	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	11/2018
244	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	03/2019
245	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	05/2019
246	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
247	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2019
248	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	06/2019

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
249	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	06/2019
250	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	06/2019
251	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019
252	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	06/2019
253	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
254	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
255	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
256	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
257	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
258	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
259	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
260	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
261	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
262	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	-
263	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
264	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
265	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
266	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
267	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
268	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
269	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
270	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-
271	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
272	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
273	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
274	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
275	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
276	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
277	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
278	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
279	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
280	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
281	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
282	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
283	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
284	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
285	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
286	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
287	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
288	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
289	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
290	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
291	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-
292	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
293	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
294	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
295	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
296	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
297	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
298	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
299	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
300	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-
301	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
302	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
303	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-
304	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-
305	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
306	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
307	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
308	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
309	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
310	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
311	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
312	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
313	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
314	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
315	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
316	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-
317	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
318	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
319	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
320	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
321	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
322	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
323	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
324	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
325	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
326	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-
327	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
328	MEERUT-BULANDSHAHAR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-
329	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
330	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
331	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
332	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
333	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-
334	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-
335	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
336	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
337	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-
338	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-
339	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-
340	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI, KARNATAKA	05/2014	720.69 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
341	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	-
342	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
343	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-
344	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
345	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
346	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
347	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
348	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
349	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
350	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
351	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
352	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
353	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
354	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
355	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
356	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
357	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
358	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
359	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
360	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
361	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
362	REHABILITATION AND UPGRADE OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
363	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
364	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
365	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
366	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
367	FOR REHABILITATION AND UPGRADE FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
368	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
369	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-
370	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
371	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
372	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
373	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-
374	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
375	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
376	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
377	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
378	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	-
379	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
380	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI, UTTAR PRADESH	02/2018	972.77 -	- -	-
381	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI, ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
382	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI, BIHAR	03/2018	496.20 -	- -	-
383	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-
384	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
385	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
386	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
387	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-
388	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-
389	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-
390	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
391	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- -	-
392	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-
393	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	- -	-
394	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
395	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-
396	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
397	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-
<u>National Highways Development Project</u>					
398	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
399	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-
400	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
401	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
<u>Public Works Dept Of State</u>					
402	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017
403	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
404	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
405	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
406	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	-
407	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-
408	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
409	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
410	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
411	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
412	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
413	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
414	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
415	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
416	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 06/2018	-
417	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 203.26	08/2013 -	-
418	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
419	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
420	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
421	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
422	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
423	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
424	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
425	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 307.47	02/2018 -	-
426	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-
427	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
428	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
429	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
430	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
431	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
432	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
433	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
434	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-
435	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-
436	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
437	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	-
438	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	-
439	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]PWD,GUJARAT	03/2016	223.67 -	02/2017 -	-
440	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD,GUJARAT	03/2016	208.34 -	02/2016 -	-
441	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD,GUJARAT	12/2017	867.97 -	11/2018 -	-
442	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE - [N24000923]PWD,GUJARAT	03/2018	464.07 399.35	11/2018 -	-
443	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 386.19	05/2019 -	-
444	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD,GUJARAT	08/2017	962.43 887.21	03/2018 -	-
445	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
446	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD,RAJASTHAN	10/2014	382.81 -	01/2015 -	-
447	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD,RAJASTHAN	01/2017	179.32 -	11/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
448	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD,RAJASTHAN	03/2016	155.77 -	09/2016 -	-
449	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD,RAJASTHAN	01/2012	378.07 478.73	01/2014 -	-
450	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD,RAJASTHAN	10/2012	511.21 -	10/2013 -	-
451	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD,RAJASTHAN	03/2009	501.00 671.54	09/2013 -	-
452	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD,RAJASTHAN	11/2017	163.95 -	04/2018 -	-
453	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
454	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
455	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD,RAJASTHAN	12/2015	621.43 -	10/2016 -	-
456	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD,RAJASTHAN	01/2017	163.54 -	07/2017 -	-
457	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA	01/2019	193.19 -	- -	-
458	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR	03/2018	153.24 -	- -	-
459	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	-
460	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
461	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA	08/2016	367.44 -	01/2017 -	-
462	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA	08/2016	175.20 -	01/2017 -	-
463	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	-
464	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
465	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA	03/2018	159.97 -	06/2019 -	-
466	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	-
467	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	-
468	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	-
469	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	-
470	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	-
471	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	-
472	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	-
473	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	-
474	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	-
475	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	-
	Total		2,26,047.40 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
476	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.00	12/2017 -	-
	<u>Mumbai Port Trust</u>				
477	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	-
	<u>Port Trust</u>				
478	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
479	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		3,188.29 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
480	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
481	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
482	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	-
483	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
484	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
485	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	-
486	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
487	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	- -	-
	<u>Chennai Metro Rail Ltd</u>				
488	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
489	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
490	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
491	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
492	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
493	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
494	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
495	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	09/2017 -	-
496	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL, ANDHRA PRADESH	07/2014	232.00 -	- -	-
497	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	- -	-
498	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN	05/2015	189.00 -	03/2017 -	-
499	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL, JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
500	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL, JHARKHAND	12/2007	200.00 -	03/2018 -	-
501	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	12/2016 -	-
502	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL, JHARKHAND	04/2013	170.00 -	04/2018 -	-
503	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
504	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Lucknow Metro Rail Corporation Limited</u>				
505	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Maharashtra Metro Rail Corporation Ltd.</u>				
506	DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>National Building Construction Corporation Ltd</u>				
507	REDEVELOPMENT OF GPRA COLONY AT NAUJOJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-
	Total		72,691.45 -		
	<u>DEFENCE PRODUCTION</u>				
	<u>Goa Shipyard Limited</u>				
508	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA	12/2016	167.69 168.00	05/2018 03/2019	-
	Total		167.69 -		
	Grand Total		3,98,575.10		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs.150 Crore and above									
								(July 2019)	
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	RAMPURAM SHAFT BLOCK - [N06000174]SCCL, TELANGANA	08/2016	431.92 -	431.92	-	- 03/2020	-	-	0/9
2	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL, TELANGANA	02/2018	412.70 -	412.70	-	- 03/2021	-	-	0/7
	Total		844.62 -	844.62	.00				0/16
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
3	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80 -	229.80	69.10	- -	03/2021	-	5/26
	Total		229.80 -	229.80	69.10				5/26
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation</u>								
4	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	601.02	85.04	- -	02/2020	-	0/0
5	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	582.99	112.97	- -	02/2020	-	0/0
6	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99	112.82	- -	02/2020	-	0/0
7	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	268.84	99.26	- -	04/2020	-	0/0
8	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	249.01	73.40	- -	05/2020	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>								
9	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	156.65	54.94	- -	02/2020	-	0/0
	Total		2,510.41 -	2,510.50	538.43				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
10	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]EJR, BIHAR	04/1998	180.82 -	727.29	488.81	- -	09/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
11	HAJIPUR-RAMDALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	400.17	378.41	- -	01/2020	-	0/0
12	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,031.00	3,376.00	3,180.37	- -	03/2021	-	0/0
13	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	459.91	456.83	- -	03/2021	-	0/0
14	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 -	729.92	349.60	- -	03/2021	-	0/0
15	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	356.81	- -	03/2021	-	0/0
16	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	1,483.14	815.41	- -	12/2021	-	0/0
17	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	589.15	303.96	- -	03/2022	-	0/0
18	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	2,614.36	375.63	- -	03/2022	-	0/0
19	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	126.80	- -	02/2023	-	0/0
20	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	2,066.77	1,403.38	- -	03/2023	-	0/0
21	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	2,396.88	.40	- -	03/2023	-	0/0
22	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	23.40	- 03/2023	03/2023	0(R3)	0/0
23	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	2,626.98	.28	- -	03/2024	-	0/0
24	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	2,860.55	1.14	- -	03/2024	-	0/0
25	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	549.75	15.47	- -	03/2024	-	0/0
26	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	1.91	- -	03/2024	-	0/0
27	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.21	- -	03/2024	-	0/0
28	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	926.09	24.16	- -	03/2024	-	0/0
29	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	2,393.23	17.20	- -	03/2024	-	0/0
30	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
31	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	.39	- -	03/2024	-	0/0
32	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	.60	- -	03/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Eastern Railways</u>								
33	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	376.90	370.65	- -	03/2020	-	0/0
34	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	226.22	226.22	- -	03/2021	-	0/0
35	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	148.03	- -	09/2021	-	0/0
36	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	252.18	- -	03/2024	-	0/0
37	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	9.31	- -	03/2025	-	0/0
38	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	10.73	- -	03/2025	-	0/0
39	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.42	- -	03/2025	-	0/0
40	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.12	- -	03/2025	-	0/0
41	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
42	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	- -	03/2025	-	0/0
43	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	- -	03/2025	-	0/0
44	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	246.00	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
45	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North Central Railway</u>								
46	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	19.07	- -	12/2022	-	0/0
	<u>North East Frontier Railway</u>								
47	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 373.87	394.28	272.88	- -	03/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
48	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.67	- 03/2022	03/2022	0(R3)	0/0
49	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	0(R3)	0/0
	<u>Northern Railway</u>								
50	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	346.63	229.48	- -	06/2020	-	0/0
51	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	800.00	512.67	- -	03/2022	-	0/0
52	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	79.53	- -	03/2023	-	0/0
53	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,230.00	103.17	- -	03/2023	-	0/0
54	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	197.17	107.86	- -	03/2024	-	0/0
55	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	205.22	1.89	- -	03/2024	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
56	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	2,062.30 -	2,062.20	825.58	- -	03/2022	-	0/2
	<u>South East Central Railway</u>								
57	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,413.76	1,413.76	1,324.64	- 10/2019	10/2019	0(R3)	0/0
	<u>South Western Railway</u>								
58	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,801.01	44.36	- -	12/2023	-	0/0
59	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	12/2023	-	0/0
60	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	12/2023	-	0/0
61	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.35	- -	12/2023	-	0/0
62	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
63	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	12/2023	-	0/0
64	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	2,135.00	144.76	- -	12/2024	-	0/0
	<u>Southern Railway</u>								
65	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	151.50	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
66	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 951.24	951.24	724.96	- -	03/2020	-	0/0
67	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	1,431.90	67.54	- 06/2022	-	-	0/0
	<u>Western Railway</u>								
68	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	92.69	- 03/2021	03/2021	0(R3)	0/0
	Total		31,047.64 -	55,799.70	14,554.56				0/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
69	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	54.31	- -	06/2020	-	0/4
70	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	98.37	- -	09/2020	-	0/4
71	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	434.06	126.58	- -	12/2020	-	2/4
72	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	9.65	- 02/2018	02/2021	36(R3)	0/0
73	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	36(R3)	0/0
74	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	27.90	- -	09/2021	-	0/4
75	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	-	- 04/2019	04/2022	36(R3)	0/0
76	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	-	- 04/2019	04/2022	36(R3)	0/0
	<u>National Highways Authority Of India</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
77	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	-	-	07/2019	-	0/0
78	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	435.25	-	08/2019	-	0/0
79	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	357.12	-	08/2019	-	0/0
80	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	321.67	-	09/2019	-	0/0
81	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	417.19	262.83	-	09/2019	-	0/0
82	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	788.62	-	10/2019	-	0/0
83	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	278.01	-	10/2019	-	0/0
84	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	834.64	140.44	-	10/2019	-	0/0
85	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	-	-	11/2019	-	0/0
86	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	688.70	661.85	-	11/2019	-	0/0
87	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	447.75	179.17	-	11/2019	-	0/0
88	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	328.67	176.29	-	11/2019	-	0/0
89	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,167.45	113.26	-	12/2019	-	0/0
90	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	364.56	208.94	-	12/2019	-	0/0
91	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	458.03	219.61	-	12/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,100.19	886.00	- -	12/2019	-	0/0
93	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
94	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	814.04	384.48	- -	01/2020	-	0/0
95	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	75.08	- -	01/2020	-	0/0
96	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	196.05	9.03	- -	01/2020	-	0/0
97	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	1,443.00	610.71	- -	02/2020	-	0/0
98	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	938.03	- -	02/2020	-	0/0
99	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,275.00	- -	02/2020	-	0/0
100	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	453.09	- -	03/2020	-	0/0
101	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	92.44	- -	03/2020	-	0/0
102	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	29.45	- -	03/2020	-	0/0
103	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	557.30	33.63	- -	03/2020	-	0/0
104	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	275.12	-	- -	03/2020	-	0/0
105	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	307.79	-	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
106	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	198.05	-	-	03/2020	-	0/0
107	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	551.58	-	-	03/2020	-	0/0
108	4 LANNING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	-	-	04/2020	-	0/0
109	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	278.92	-	04/2020	-	0/0
110	4 LANNING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	1,169.61	1,004.18	-	04/2020	-	0/0
111	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	174.79	-	05/2020	-	0/0
112	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	1,232.21	410.09	-	05/2020	-	0/0
113	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	-	-	05/2020	-	0/0
114	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	-	-	05/2020	-	0/0
115	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	181.78	-	-	06/2020	-	0/0
116	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	21.46	-	07/2020	-	0/0
117	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	-	-	07/2020	-	0/0
118	REHABILITATION AND UPGRADATION TO FOUR LANNING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	468.18	-	07/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
119	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	34.36	- -	07/2020	-	0/0
120	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
121	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	960.24	-	- -	08/2020	-	0/0
122	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	234.67	- -	09/2020	-	0/0
123	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	1,103.88	242.53	- -	09/2020	-	0/0
124	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	131.71	- -	10/2020	-	0/0
125	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	404.94	90.86	- -	10/2020	-	0/0
126	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	36.14	- -	11/2020	-	0/0
127	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	59.22	- -	11/2020	-	0/0
128	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	29.25	- -	11/2020	-	0/0
129	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	19.78	- -	11/2020	-	0/0
130	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	-	- -	12/2020	-	0/0
131	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	24.90	- -	12/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
132	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA	03/2018	642.13 -	642.13	288.84	- -	12/2020	-	0/0
133	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
134	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 -	1,471.75	305.75	- -	01/2021	-	0/0
135	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB	02/2018	261.76 -	261.76	40.89	- -	01/2021	-	0/0
136	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	1,052.21	1,080.00	- -	01/2021	-	0/0
137	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	2,702.05	-	- -	01/2021	-	0/0
138	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI, TAMIL NADU	02/2018	1,166.26 -	1,166.26	-	- -	02/2021	-	0/0
139	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	565.09	-	- -	02/2021	-	0/0
140	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	1,261.05	-	- 03/2021	03/2021	0(R3)	0/0
141	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA	01/2018	621.00 -	621.00	212.24	- -	04/2021	-	0/0
142	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI, TAMIL NADU	03/2018	1,016.92 -	1,016.92	-	- -	04/2021	-	0/0
143	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA	03/2018	806.11 -	806.11	-	- -	04/2021	-	0/0
144	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 -	478.74	-	- -	05/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
145	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	-	- -	06/2021	-	0/0
146	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,071.61	-	- -	07/2021	-	0/0
147	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,064.88	-	- -	07/2021	-	0/0
148	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	30.00	- -	07/2021	-	0/0
149	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	44.43	- -	07/2021	-	0/0
150	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	-	- -	07/2021	-	0/0
151	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	-	- -	07/2021	-	0/0
152	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	14.11	- -	07/2021	-	0/0
153	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	55.06	- -	08/2021	-	0/0
154	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	-	- -	08/2021	-	0/0
155	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	-	- -	08/2021	-	0/0
156	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	1,995.34	-	- -	11/2021	-	0/0
National Highways Development Project									
157	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	390.51	178.32	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Public Works Dept Of State</u>								
158	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	766.36	666.72	- 09/2019	-	-	0/0
159	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	904.82	722.92	- 12/2019	-	-	0/0
	Total		75,331.32 -	75,577.99	17,749.29				2/16
	<u>URBAN DEVELOPMENT</u>								
	<u>Central Public Works Department</u>								
160	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	10.36	- -	12/2020	-	0/0
161	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	7(R3)	0/0
162	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	348.77	12.00	- -	11/2021	-	0/0
	Total		1,162.77 -	1,162.77	34.92				0/0
	Grand Total		1,11,126.56	1,36,125.38	32,946.30				7/60

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs.150 Crore and Above						
(July 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	06/2019 -	12/2019	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
3	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	353.27 -	09/2020 -	09/2020	0/0
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	04/2020 -	12/2020	0/0
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	03/2020 -	12/2020	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	859.86 -	03/2021 -	03/2021	0/0
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	358.89 -	04/2021 -	04/2021	0/0
8	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2021	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR	07/2018	323.19 -	09/2021 -	09/2021	0/0
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	10/2021 -	10/2021	0/0
11	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	264.99 -	11/2021 -	11/2021	0/0
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	02/2022 -	08/2022	0/0
13	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	539.20 -	10/2022 -	10/2022	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
14	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
15	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
16	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Western Coal Fields Limited</u>					
17	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>INFORMATION AND BROADCASTING</u>					
	<u>Central Public Works Department</u>					
19	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	02/2019 -	11/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
20	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC,MAHARASHTRA	12/2016	167.70 -	03/2020 -	03/2020	0/0
	<u>National Film Archive Of India</u>					
21	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA	11/2014	597.41 -	- -	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
22	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	03/2021 -	03/2021	0/0
23	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	10/2021	0/0
24	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH	12/2017	1,524.06 -	12/2021 -	12/2021	0/0
25	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
26	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
27	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
28	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
29	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
30	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 -	07/2022 -	07/2022	0/0
31	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20 -	07/2022 -	07/2022	0/0
32	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0
33	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45 -	10/2022 -	10/2022	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
34	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	06/2020 -	06/2020	0/0
35	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	06/2020 -	06/2020	0/0
36	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA	06/2019	2,166.38 -	06/2022 -	06/2022	0/0
37	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA	12/2018	854.00 -	12/2022 -	12/2022	0/0
38	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	-	0/0
	<u>Indian Oil Corporation Limited</u>					
39	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2020	0/0
40	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
41	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	08/2020	0/0
42	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
43	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
44	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	01/2021 -	01/2021	0/0
45	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
46	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
47	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 -	03/2021	0/0
48	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
49	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
50	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
51	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	09/2021 -	09/2021	0/0
52	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
53	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
54	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
55	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	04/2022	0/0
56	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 -	09/2022 -	09/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
57	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
	<u>Indian Strategic Petroleum Reserves Ltd</u>					
58	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
59	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	12/2020 -	12/2020	0/0
60	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]ONGC,GUJARAT	10/2018	156.67 -	03/2021 -	03/2021	0/0
61	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	05/2021 -	05/2021	0/0
62	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	04/2021 -	05/2021	0/0
63	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 -	03/2022 -	03/2022	0/0
64	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	12/2021 -	03/2022	0/0
	<u>Oil India Limited</u>					
65	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
66	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	08/2020	0/0
67	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
68	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	12/2023	0/0
	<u>National Hydro-Electric Power Corporation</u>					
69	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
70	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
71	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
72	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	09/2020	0/0
73	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	11/2020	0/0
74	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
75	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
76	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	07/2019	0/0
77	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 03/2019	07/2019	0/0
78	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 04/2019	07/2019	0/0
79	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	07/2019	0/0
80	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	07/2019	0/0
81	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 03/2018	08/2019	0/0
82	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 04/2019	08/2019	0/0
83	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 06/2019	08/2019	0/0
84	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	09/2019	0/0
85	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 09/2019	09/2019	0/0
86	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 09/2019	09/2019	0/0
87	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	09/2019	0/0
88	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPF AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 -	09/2019	0/0
89	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 06/2019	10/2019	0/0
90	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
91	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 11/2019	11/2019	0/0
92	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	04/2016 03/2017	12/2019	0/0
93	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 12/2019	12/2019	0/0
94	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
95	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	12/2019	0/0
96	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 01/2020	01/2020	0/0
97	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 02/2020	02/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
98	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
99	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	02/2020	0/0
100	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 12/2019	03/2020	0/0
101	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
102	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
103	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
104	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 12/2018	12/2020	0/0
	<u>Thdc India Limited</u>					
105	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	09/2023 -	09/2023	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
106	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	09/2019	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
107	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	06/2020	0/0
108	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	08/2020	0/0
109	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	10/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					
110	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	10/2019	0/0
111	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	02/2020	0/0
112	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	02/2020	0/0
113	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	02/2020	0/0
114	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
115	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2020	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
116	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	09/2019	0/0
117	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	10/2019	0/0
118	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	02/2020	0/0
119	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2020	0/0
120	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	10/2020	0/0
121	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
122	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	-	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
123	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 12/2019	12/2019	0/0
124	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2022	0/0
125	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2022	0/0
126	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2022	0/0
127	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
128	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
129	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2023	0/0
130	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
131	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
132	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
133	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
134	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
135	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
136	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-	0/0
	<u>Container Corporation Of India</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
137	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2019	0/0
138	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
139	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	02/2020	0/0
140	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020	0/0
141	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2020	0/0
142	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
143	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
144	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
145	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
146	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
<u>East Central Railways</u>						
147	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	09/2019	0/0
148	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
149	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	01/2020	0/0
150	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	03/2012 -	03/2020	0/0
151	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	03/2020	0/0
152	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	03/2012 -	03/2020	0/0
153	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
154	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,031.00	- -	03/2021	0/0
155	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	03/2021	0/0
156	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
157	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2021	0/0
158	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
159	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	- -	12/2021	0/0
160	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	03/2022	0/0
161	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
162	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	03/2020 -	03/2022	0/0
163	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2022	0/0
164	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	03/2021 -	03/2022	0/0
165	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	- -	02/2023	0/0
166	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
167	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	03/2023	0/0
168	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- 03/2023	03/2023	0/0
169	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	03/2024	0/0
170	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	03/2024	0/0
171	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	03/2024	0/0
172	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
173	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	03/2024	0/0
174	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	03/2024	0/0
175	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	03/2024	0/0
176	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
177	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	03/2024	0/0
178	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	03/2024	0/0
179	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
180	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR	07/2004	599.63 674.00	12/2007 -	-	0/0
181	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
	<u>East Coast Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
182	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2020	0/0
183	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2021	0/0
184	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	03/2022	0/0
185	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	03/2022	0/0
186	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2022	0/0
187	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	03/2023	0/0
188	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 -	03/2023	0/0
189	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 -	03/2023	0/0
190	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	12/2023	0/0
191	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 -	03/2025	0/0
<u>Eastern Railways</u>						
192	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
193	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2020	0/0
194	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2020	0/0
195	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
196	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2021	0/0
197	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	09/2021	0/0
198	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
199	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
200	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
201	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
202	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
203	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
204	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
205	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
206	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
207	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
208	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
209	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
210	BARIAPUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
211	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
212	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
213	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
214	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
215	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
216	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
217	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
218	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
	<u>Indian Railway Construction Company Limited</u>					
219	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 1,700.43	03/2020 06/2023	06/2023	0/0
	<u>Kolkata Metro Rail Corporation Limited</u>					
220	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
221	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2021	0/0
222	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 918.53	03/2014 03/2021	03/2021	0/0
223	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
224	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
225	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
226	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
227	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	12/2022	0/0
228	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 314.09	12/2008 03/2015	03/2015	0/0
229	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
	<u>North East Frontier Railway</u>					
230	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	03/2020	0/0
231	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 13,809.00	03/2011 -	03/2020	0/0
232	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 1,532.00	03/2019 -	03/2020	0/0
233	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,145.00	03/2019 -	03/2020	0/0
234	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
235	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
236	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 728.00	03/2019 -	03/2020	0/0
237	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
238	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
239	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 3,300.00	12/2008 -	03/2021	0/0
240	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
241	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 373.87	- -	03/2021	0/0
242	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
243	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	03/2015 -	10/2021	0/0
244	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 4,968.00	03/2014 03/2022	03/2022	0/0
245	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- 03/2022	03/2022	0/0
246	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- 03/2022	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
247	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	-	0/0
248	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
249	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
250	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
251	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 06/2021	03/2020	0/0
<u>North Eastern Railway</u>						
252	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019	0/0
253	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2020	0/0
254	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	01/2020	0/0
255	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	06/2020	0/0
256	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
257	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
258	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2022	0/0
259	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
260	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
261	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
262	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
263	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
264	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	-	0/0
265	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
266	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
267	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
268	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
<u>North Western Railway</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Antici Pated	
1	2	3	4	5	6	7
269	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2019	0/0
270	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	02/2019 -	12/2019	0/0
271	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	05/2020	0/0
272	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2020	0/0
273	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2020	0/0
274	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	12/2021	0/0
275	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
276	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0
277	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
278	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
279	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	06/2020	0/0
280	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	03/2021	0/0
281	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	03/2016 -	03/2021	0/0
282	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	- -	03/2022	0/0
283	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	06/2022	0/0
284	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	03/2023	0/0
285	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
286	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
287	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0
288	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
289	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
	<u>National High Speed Rail Corporation Limited</u>					
290	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Rail India Technical And Economic Service</u>					
291	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES, CHHATISGARH	02/2016	393.98 -	03/2020 -	03/2020	0/0
292	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES, MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
293	HARIDASPUR-PARADEEP (NL) - [220100285]RVNL, ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
294	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
295	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL, MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2020	0/0
296	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	03/2020 -	06/2020	0/0
297	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	03/2016 -	12/2020	0/0
298	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2020	0/0
299	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
300	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	03/2020 -	03/2021	0/0
301	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
302	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
303	SUKINDA ROAD - ANGUL (NL) (ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	02/2015 -	12/2021	0/0
304	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
305	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2021	0/0
306	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
307	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
308	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
309	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
310	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
311	VIZIANAGARAM - SAMBALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	12/2024 -	12/2024	0/0
312	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
313	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
314	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
315	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
316	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2026	0/0
317	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2026	0/0
<u>Railway Electrification</u>						
318	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
319	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2021	0/0
320	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
321	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2023	0/0
322	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2023	0/0
323	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2023	0/0
324	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
325	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
326	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA	07/1998	458.25 -	- -	-	0/0
327	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
328	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
329	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 1,413.76	- 10/2019	10/2019	0/0
330	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR, CHHATISGARH	04/2008	872.00 1,226.51	12/2019 10/2019	10/2019	0/0
331	ANUPPUR-KATNI - [N22000485]SECR, MADHYA PRADESH	04/2015	1,370.00 1,370.00	12/2021 12/2021	12/2021	0/0
<u>South Eastern Railway</u>						
332	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 11/2019	11/2019	0/0
333	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 358.68	12/2018 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
334	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 -	06/2020	0/0
335	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2021	0/0
336	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
337	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR	08/2010	400.00 -	03/2014 -	-	0/0
338	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
339	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
340	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	-	0/0
341	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-	0/0
<u>South Western Railway</u>						
342	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	03/2020	0/0
343	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	03/2020	0/0
344	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	03/2021	0/0
345	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
346	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
347	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
348	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
349	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
350	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
351	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
352	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
353	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
354	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
355	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	12/2024	0/0
<u>Southern Railway</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
356	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2019	0/0
357	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2020	0/0
358	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
359	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 951.24	- -	03/2020	0/0
360	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
361	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2021	0/0
362	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2021	0/0
363	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
364	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
365	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-	0/0
366	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
367	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
368	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
369	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
370	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
371	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
372	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-	0/0
373	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-	0/0
374	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
375	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-	0/0
376	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	- 06/2022	-	0/0
377	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-	0/0
378	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
379	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
380	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
	<u>Western Railway</u>					
381	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017	0/0
382	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	03/2019 03/2020	03/2020	0/0
383	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	03/2020 03/2021	03/2021	0/0
384	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2021	03/2021	0/0
385	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 03/2021	03/2021	0/0
386	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	03/2020 03/2021	03/2021	0/0
387	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 06/2021	06/2021	0/0
388	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	03/2012 03/2022	03/2022	0/0
389	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2022	03/2022	0/0
390	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	03/2019 03/2022	03/2022	0/0
391	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	03/2021 03/2022	03/2022	0/0
392	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,338.15	03/2022 03/2023	03/2023	0/0
393	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
394	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
395	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
396	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
397	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
398	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
399	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
400	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	07/2019	0/0
401	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	07/2019	0/0
402	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019	0/0
403	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	09/2019	0/0
404	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	11/2019	0/0
405	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
406	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
407	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
408	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
409	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	11/2019	0/0
410	BHADGAON TO CHALISGAON - [N24001047]MORTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	11/2019	0/0
411	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	12/2019	0/0
412	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
413	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
414	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
415	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2019	0/0
416	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	12/2019	0/0
417	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	12/2019	0/0
418	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2019	0/0
419	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	12/2019	0/0
420	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
421	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	12/2019	0/0
422	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	12/2019	0/0
423	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	12/2019	0/0
424	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	12/2019	0/0
425	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	12/2019	0/0
426	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	12/2019	0/0
427	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2019	0/0
428	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	12/2019	0/0
429	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2019	0/0
430	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA	02/2018	355.99 355.99	12/2019 -	12/2019	0/0
431	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
432	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
433	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	06/2020	0/0
434	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	08/2020	0/0
435	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
436	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
437	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
438	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
439	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
440	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
441	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
442	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
443	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
444	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
445	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
446	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
447	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
448	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
449	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
450	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
451	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
452	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
453	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
454	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
455	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
456	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
457	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
458	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
459	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
460	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
461	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
462	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
463	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
464	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
465	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
466	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
467	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH, BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
468	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH, BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
469	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH, BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
470	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH, ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
471	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH, ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
472	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH, ODISHA	03/2015	226.31 226.00	10/2017 -	-	0/0
473	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH, ODISHA	12/2013	319.80 320.00	05/2016 -	-	0/0
474	REHABILITATION AND UPGRADE OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH, ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
475	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
476	REHABILITATION AND UPGRADE OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH, UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
477	REHABILITATION AND UPGRADE OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH, UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
478	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26 - [N24000911]MORTH, ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
479	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA - [N24000912]MORTH, ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
480	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH, ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
481	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH, ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
482	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH, ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
483	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH, ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
484	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH, ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
485	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA - [N24000918]MORTH, ODISHA	07/2013	251.92 -	10/2015 -	-	0/0
486	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA - [N24000919]MORTH, ODISHA	07/2013	265.35 -	10/2015 -	-	0/0
487	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA - [N24000924]MORTH, ODISHA	03/2015	229.29 -	11/2015 -	-	0/0
488	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING REHABILITATION AND - [N24000943]MORTH, BIHAR	09/2018	1,478.40 -	- -	-	0/0
489	MORSHI TO MAH/MP BORDER - [N24001016]MORTH, MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
490	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
491	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
492	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
493	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
494	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	07/2019	0/0
495	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	07/2019	0/0
496	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019	0/0
497	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019	0/0
498	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019	0/0
499	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019	0/0
500	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019	0/0
501	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019	0/0
502	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019	0/0
503	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019	0/0
504	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	- 02/2018	02/2021	0/0
505	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	- 02/2018	02/2021	0/0
506	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	- 04/2019	04/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
507	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	- 04/2019	04/2022	0/0
508	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0
509	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-	0/0
510	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-	0/0
511	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-	0/0
512	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-	0/0
513	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-	0/0
514	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
515	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
516	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
517	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-	0/0
518	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
519	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
520	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	-	0/0
National Highways Authority Of India						
521	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018	0/0
522	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	11/2018	0/0
523	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	03/2019	0/0
524	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	05/2019	0/0
525	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
526	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2019	0/0
527	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	06/2019	0/0
528	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
529	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	06/2019	0/0
530	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019	0/0
531	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI, JHARKHAND	03/2017	239.68 -	03/2020 -	06/2019	0/0
532	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	07/2019	0/0
533	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	07/2019	0/0
534	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	07/2019	0/0
535	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	11/2018 -	07/2019	0/0
536	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 -	03/2019 -	07/2019	0/0
537	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	07/2019	0/0
538	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	04/2009 -	08/2019	0/0
539	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	04/2010 -	08/2019	0/0
540	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	08/2019	0/0
541	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	08/2019	0/0
542	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	08/2019	0/0
543	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	08/2019	0/0
544	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	08/2019	0/0
545	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0
546	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	03/2008 -	09/2019	0/0
547	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	09/2019	0/0
548	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
549	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
550	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
551	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 2,525.80	09/2019 03/2020	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
552	FOUR LANNING OF CHICHA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	09/2019	0/0
553	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
554	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	05/2019 -	09/2019	0/0
555	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	03/2020 -	09/2019	0/0
556	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA	03/2017	639.79 -	03/2020 -	09/2019	0/0
557	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI, JHARKHAND	03/2017	165.50 -	03/2020 -	09/2019	0/0
558	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	06/2008 -	10/2019	0/0
559	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	10/2019	0/0
560	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- -	10/2019	0/0
561	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	10/2019	0/0
562	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 10/2019	10/2019	0/0
563	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	10/2019	0/0
564	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	10/2019	0/0
565	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	10/2019	0/0
566	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	- -	11/2019	0/0
567	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	11/2019	0/0
568	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	11/2019	0/0
569	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019	0/0
570	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	05/2019 -	11/2019	0/0
571	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	03/2019 -	11/2019	0/0
572	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	11/2019	0/0
573	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI, ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	11/2019	0/0
574	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	04/2020 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
575	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	11/2019	0/0
576	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT	10/2017	232.49 -	10/2017 -	11/2019	0/0
577	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI, TAMIL NADU	09/2017	244.27 -	09/2017 -	11/2019	0/0
578	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	11/2019	0/0
579	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2019	0/0
580	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019	0/0
581	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2019	0/0
582	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2019	0/0
583	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2019	0/0
584	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2019	0/0
585	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	12/2019	0/0
586	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	12/2019	0/0
587	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	12/2019	0/0
588	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	12/2017 06/2020	12/2019	0/0
589	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
590	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	12/2019	0/0
591	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	12/2019	0/0
592	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	12/2019	0/0
593	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	- -	12/2019	0/0
594	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2020	0/0
595	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	01/2020	0/0
596	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	01/2020	0/0
597	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	01/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
598	FOUR LANE OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	01/2020	0/0
599	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	01/2020	0/0
600	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	01/2020	0/0
601	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	02/2020	0/0
602	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
603	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	02/2020	0/0
604	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
605	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	02/2020	0/0
606	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	02/2020	0/0
607	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2020	0/0
608	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2020	0/0
609	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2020	0/0
610	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2020	0/0
611	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	03/2020	0/0
612	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 598.13	04/2018 03/2020	03/2020	0/0
613	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2020	0/0
614	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
615	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
616	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
617	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
618	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2020	0/0
619	REHABILITATION AND UPGRADEATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	03/2020	0/0
620	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
621	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	03/2020	0/0
622	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	03/2020	0/0
623	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	03/2020	0/0
624	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	03/2020	0/0
625	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	04/2020	0/0
626	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
627	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
628	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	04/2020	0/0
629	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
630	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
631	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	05/2020	0/0
632	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATAKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	05/2020	0/0
633	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	05/2020	0/0
634	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	05/2020	0/0
635	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	05/2020	0/0
636	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
637	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	05/2020	0/0
638	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
639	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	05/2020	0/0
640	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	05/2020	0/0
641	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	05/2020	0/0
642	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	05/2020	0/0
643	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
644	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	06/2020	0/0
645	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 -	06/2020	0/0
646	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	05/2018 -	06/2020	0/0
647	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42 -	03/2019 -	06/2020	0/0
648	SIX LANNING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI, KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
649	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI, KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
650	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA	03/2018	181.78 -	- -	06/2020	0/0
651	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
652	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
653	REHABILITATION AND UPGRADATION TO FOUR LANNING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	07/2020	0/0
654	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI, KARNATAKA	03/2017	831.58 -	03/2020 -	07/2020	0/0
655	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA	12/2017	686.65 -	- -	07/2020	0/0
656	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	08/2020	0/0
657	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI, RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
658	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	08/2020	0/0
659	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
660	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
661	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	06/2020 -	08/2020	0/0
662	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI, TAMIL NADU	09/2017	1,227.87 -	09/2017 -	08/2020	0/0
663	FOUR LANNING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI, MADHYA PRADESH	01/2018	960.24 -	- -	08/2020	0/0
664	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI, HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
665	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI, TAMIL NADU	08/2017	1,176.37 -	08/2017 -	09/2020	0/0
666	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
667	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0
668	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	- -	10/2020	0/0
669	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	11/2020	0/0
670	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
671	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020	0/0
672	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
673	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	11/2020	0/0
674	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
675	FOUR LANINIG OF CHETTikulAM TO NATHAM SECTION OF NH-785 FROM CHETTikulUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	11/2020	0/0
676	FOUR LANING OF MADURAI- CHETTikulAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTikulAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	11/2020	0/0
677	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	11/2020	0/0
678	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	11/2020	0/0
679	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	12/2020	0/0
680	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
681	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
682	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 12/2020	12/2020	0/0
683	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 12/2020	12/2020	0/0
684	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	12/2020	0/0
685	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2020	0/0
686	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	12/2020	0/0
687	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	12/2020	0/0
688	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	01/2021	0/0
689	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	01/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
690	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	01/2021	0/0
691	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021	0/0
692	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	01/2021	0/0
693	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
694	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	02/2021	0/0
695	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
696	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2021	0/0
697	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- 03/2021	03/2021	0/0
698	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 -	04/2021	0/0
699	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	04/2021	0/0
700	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 -	04/2021	0/0
701	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	04/2021	0/0
702	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
703	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
704	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	05/2021	0/0
705	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
706	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	07/2021	0/0
707	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	07/2021	0/0
708	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
709	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	07/2021	0/0
710	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	07/2021	0/0
711	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
712	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
713	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	08/2021	0/0
714	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
715	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	08/2021	0/0
716	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
717	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
718	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
719	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
720	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
721	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
722	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
723	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
724	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
725	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
726	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	-	0/0
727	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
728	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
729	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
730	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
731	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
732	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
733	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
734	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
735	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
736	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
737	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
738	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
739	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
740	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
741	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
742	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
743	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
744	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
745	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
746	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
747	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
748	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
749	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
750	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
751	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
752	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
753	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
754	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
755	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
756	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
757	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
758	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
759	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
760	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-	0/0
761	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
762	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-	0/0
763	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
764	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
765	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
766	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-	0/0
767	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
768	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0
769	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
770	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
771	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
772	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
773	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
774	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
775	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-	0/0
776	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
777	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
778	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
779	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
780	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
781	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
782	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
783	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
784	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-	0/0
785	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
786	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0
787	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-	0/0
788	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-	0/0
789	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
790	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
791	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-	0/0
792	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
793	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
794	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
795	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
796	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
797	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
798	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-	0/0
799	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
800	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
801	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
802	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
803	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	-	0/0
804	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
805	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-	0/0
806	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
807	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
808	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
809	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
810	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
811	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
812	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
813	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
814	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
815	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
816	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
817	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
818	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
819	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
820	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
821	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
822	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
823	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
824	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
825	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
826	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
827	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
828	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
829	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
830	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
831	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
832	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
833	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
834	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
835	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-	0/0
836	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
837	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
838	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
839	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
840	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
841	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
842	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
843	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
844	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
845	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
846	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
847	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
848	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
849	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
850	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
851	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
852	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
853	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	-	0/0
854	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
855	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-	0/0
856	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
857	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-	0/0
858	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
859	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-	0/0
<u>National Highways Development Project</u>						
860	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	08/2019	0/0
861	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	08/2019	0/0
862	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	01/2020 -	01/2020	0/0
863	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	02/2020	0/0
864	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	03/2020	0/0
865	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2020	0/0
866	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
<u>Public Works Dept Of State</u>						
867	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	05/2019 -	07/2019	0/0
868	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	07/2019	0/0
869	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	07/2019	0/0
870	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017	0/0
871	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
872	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
873	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD, WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019	0/0
874	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD, HARYANA	01/2017	276.01 -	03/2019 07/2019	07/2019	0/0
875	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD, TELANGANA	03/2018	192.67 -	07/2019 -	07/2019	0/0
876	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD, MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019	0/0
877	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD, TELANGANA	01/2017	359.27 -	05/2019 -	08/2019	0/0
878	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD, KARNATAKA	01/2017	291.49 -	08/2017 -	08/2019	0/0
879	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA	12/2011	159.39 -	11/2017 -	09/2019	0/0
880	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD, HARYANA	01/2017	247.25 -	03/2019 03/2020	09/2019	0/0
881	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD, UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	09/2019	0/0
882	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]PWD, NAGALAND	11/2016	336.25 -	09/2019 -	09/2019	0/0
883	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD, PUNJAB	10/2017	1,069.59 -	10/2019 -	10/2019	0/0
884	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]PWD, TELANGANA	01/2017	196.52 -	10/2019 -	10/2019	0/0
885	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD, TELANGANA	01/2017	605.08 -	10/2019 -	10/2019	0/0
886	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD, BIHAR	11/2016	230.34 -	10/2019 -	10/2019	0/0
887	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL	03/2016	271.17 291.20	11/2018 11/2019	11/2019	0/0
888	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD, MADHYA PRADESH	11/2017	235.91 -	02/2018 -	11/2019	0/0
889	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD, MADHYA PRADESH	11/2017	184.62 -	02/2018 -	11/2019	0/0
890	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD, MADHYA PRADESH	03/2018	191.21 -	11/2019 -	11/2019	0/0
891	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD, MADHYA PRADESH	03/2018	214.69 -	03/2018 -	11/2019	0/0
892	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD, MADHYA PRADESH	03/2018	233.04 -	03/2018 -	11/2019	0/0
893	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD, MADHYA PRADESH	11/2017	254.17 -	02/2018 -	11/2019	0/0
894	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD, MADHYA PRADESH	09/2016	287.34 -	01/2019 -	11/2019	0/0
895	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD, MADHYA PRADESH	03/2016	877.79 -	06/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
896	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	11/2019	0/0
897	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD,TELANGANA	02/2018	294.13 -	11/2019 -	11/2019	0/0
898	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD,TELANGANA	02/2018	220.28 -	11/2019 -	11/2019	0/0
899	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	03/2018 -	11/2019	0/0
900	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	12/2019	0/0
901	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	12/2019	0/0
902	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	12/2019	0/0
903	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	08/2013 -	12/2019	0/0
904	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	02/2013 09/2017	12/2019	0/0
905	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	12/2019	0/0
906	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	12/2019	0/0
907	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	02/2019 -	12/2019	0/0
908	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	03/2019 -	12/2019	0/0
909	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]PWD,TELANGANA	01/2017	283.00 -	12/2019 -	12/2019	0/0
910	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	05/2019 -	12/2019	0/0
911	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD,TELANGANA	01/2018	230.03 -	12/2019 -	12/2019	0/0
912	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	02/2014 -	12/2019	0/0
913	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	09/2014 -	12/2019	0/0
914	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	01/2020	0/0
915	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	01/2020	0/0
916	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	01/2020	0/0
917	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	02/2020	0/0
918	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	02/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
919	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	03/2020	0/0
920	REHABILITATION AND UPGADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	03/2020	0/0
921	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	04/2020	0/0
922	REHABILITATION AND UPGADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]PWD,TELANGANA	02/2018	426.52 -	04/2020 -	04/2020	0/0
923	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	05/2020	0/0
924	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]PWD,TELANGANA	01/2018	283.15 -	05/2020 -	05/2020	0/0
925	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	05/2018 -	05/2020	0/0
926	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	06/2020	0/0
927	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	06/2020	0/0
928	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	06/2020	0/0
929	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	08/2018 -	06/2020	0/0
930	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB	03/2018	173.24 -	06/2020 -	06/2020	0/0
931	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD,TELANGANA	02/2018	206.13 -	06/2020 -	06/2020	0/0
932	REHABILITATION AND UPGADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD,JHARKHAND	03/2018	212.99 -	06/2020 -	06/2020	0/0
933	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	07/2020	0/0
934	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB	03/2018	322.48 -	07/2020 -	07/2020	0/0
935	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD,TELANGANA	03/2018	626.76 -	07/2020 -	07/2020	0/0
936	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD,PUNJAB	03/2018	293.10 -	08/2020 -	08/2020	0/0
937	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
938	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
939	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]PWD,TRIPURA	10/2016	171.90 -	08/2020 -	08/2020	0/0
940	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD,TELANGANA	03/2018	322.81 -	09/2020 -	09/2020	0/0
941	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]PWD,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
942	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]PWD,PUNJAB	03/2018	170.57 -	11/2020 -	11/2020	0/0
943	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]PWD,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
944	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]PWD,NAGALAND	03/2017	217.35 -	11/2020 -	11/2020	0/0
945	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	08/2016 -	12/2020	0/0
946	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]PWD,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020	0/0
947	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]PWD,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020	0/0
948	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
949	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27 213.97	08/2019 -	08/2021	0/0
950	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 263.26	08/2019 -	08/2021	0/0
951	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]PWD,ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
952	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]PWD,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
953	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
954	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
955	REHABILITATION AND UPGADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
956	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
957	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
958	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 06/2018	-	0/0
959	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 203.26	08/2013 -	-	0/0
960	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
961	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
962	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
963	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- 09/2019	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
964	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
965	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- 12/2019	-	0/0
966	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
967	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
968	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
969	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 307.47	02/2018 -	-	0/0
970	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-	0/0
971	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
972	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
973	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
974	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
975	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
976	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
977	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
978	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-	0/0
979	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-	0/0
980	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-	0/0
981	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	-	0/0
982	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	-	0/0
983	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 386.19	05/2019 -	-	0/0
984	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA	01/2019	193.19 -	- -	-	0/0
985	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR	03/2018	153.24 -	- -	-	0/0
986	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
987	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-	0/0
988	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
989	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
990	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
991	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
992	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
993	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
994	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
995	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
996	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
997	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
998	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
999	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
1000	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
1001	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
1002	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Cochin Shipyard Ltd</u>					
1003	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL,KERALA	05/2016	970.00 -	05/2020 -	05/2020	0/0
1004	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL,KERALA	07/2016	1,799.00 -	05/2021 -	05/2021	0/0
	<u>Inland Waterways Authority Of India</u>					
1005	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	4,200.00 -	03/2023 -	03/2023	0/0
	<u>Kamarajar Port Limited</u>					
1006	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Mumbai Port Trust</u>					
1007	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	-	0/0
	<u>Port Trust</u>					
1008	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
1009	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
1010	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	10/2018 09/2019	09/2019	0/0
	<u>Department Of Telecommunication</u>					
1011	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
1012	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
1013	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12/2018 -	07/2020	0/0
	<u>Bangalore Metro Rail Corporation Limited</u>					
1014	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
1015	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
1016	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	11/2019	0/0
1017	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	07/2019 12/2019	12/2019	0/0
1018	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	03/2020	0/0
1019	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
1020	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 -	09/2020	0/0
1021	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1022	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	12/2020	0/0
1023	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- 08/2020	03/2021	0/0
1024	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	11/2021	0/0
1025	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	06/2021 -	03/2022	0/0
1026	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
1027	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	-	0/0
1028	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-	0/0
1029	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	- -	-	0/0
	<u>Hindustan Steelwork Construction Limited</u>					
1030	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1031	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1032	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
1033	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1034	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
1035	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1036	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
1037	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1038	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
1039	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1040	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1041	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1042	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0
1043	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1044	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(July 2019)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1045	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1046	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1047	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1048	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC, MAHARASHTRA	12/2016	11,420.00 -	11/2021 01/2022	01/2022	0/0
1049	DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1050	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1051	BHOPAL METRO RAIL - [N28000124]MPMRCL, MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1052	INDORE METRO RAIL - [N28000125]MPMRCL, MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1053	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Building Construction Corporation Ltd</u>					
1054	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1055	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB, MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2019	0/0
	Total		11,63,156.35 -			0/0
	Grand Total		11,63,156.35			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(July 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021
	Total		1,186.64 -	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
2	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	335.52	02/2020 -	09/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,697.02	12/2020 -	08/2020
4	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL [N16000252]	5/2016	664.00 -	664.00	594.01	12/2020 -	02/2020
5	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	149.98	06/2020 -	03/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY [N16000308]	8/2017	315.00 -	315.00	110.38	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	108.51	09/2022 -	06/2021
8	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	81.56	04/2021 -	04/2020
	Total		8,274.58 -	9,275.58	3,076.98		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
9	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	511.35	03/2024 -	03/2022
	<u>East Central Railways</u>						
10	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	159.07	03/2021 -	12/2020
	<u>North Central Railway</u>						
11	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00	2,001.00	416.59	03/2021 03/2023	03/2021
	<u>North East Frontier Railway</u>						

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
12	SEVOK RANGPO, NEFR - [N22000102	4/2008	1,339.48	4,084.69	285.46	12/2015 06/2021	03/2020
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390	4/2016	602.27 -	612.00	186.09	12/2021 -	03/2020
14	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	4/2015	2,232.32 -	2,182.00	582.27	03/2022 -	03/2020
	<u>North Eastern Railway</u>						
15	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42 -	1,295.42	291.45	03/2022 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
16	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
	Total		12,169.97 -	14,874.59	2,432.47		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
17	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43	429.43	181.17	11/2017 03/2020	11/2019
18	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968	11/2016	376.25	376.25	180.38	08/2017 03/2020	08/2019
19	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI- DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45	263.45	43.79	09/2017 03/2020	09/2019
20	PARSHURAM GHAT TO ARAWALI - [N24001133	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
	<u>National Highways Authority Of India</u>						
21	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 746.43	746.43	596.50	12/2017 06/2020	12/2019
22	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019
23	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02	157.49	-	03/2020 -	02/2020
24	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19	254.00	248.60	03/2020 -	09/2019
25	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79	552.90	480.73	03/2020 -	09/2019
26	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32	503.10	1.15	03/2020 -	11/2019
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50	172.16	117.09	03/2020 -	09/2019

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
28	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00	894.00	670.00	04/2020 -	11/2019
	<u>Public Works Dept Of State</u>						
29	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904	1/2017	247.25 -	247.25	144.00	03/2019 03/2020	09/2019
	Total		7,025.97 -	8,105.40	4,767.56		
	Grand Total		28,657.16	32,459.39	10,394.56		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs.150 Crore and above						(July 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
2	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
3	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
4	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
5	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	.42	11/2021 -	11/2021
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
	Total		5,033.68 -	5,033.82	694.83		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	187.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
11	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	314.86	03/2022 -	03/2022
12	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	80.56	03/2022 -	03/2022
13	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.13	03/2024 -	03/2024
15	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
16	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
	<u>Mahanadi Coal Fields Limited</u>						
17	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,547.80	03/2026 -	03/2026
18	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	439.24	03/2021 -	03/2021
19	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,111.70	03/2029 -	03/2029
20	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	82.60	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
21	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.88	09/2019 -	09/2019
22	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	6,860.71	11/2021 -	11/2021
23	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
24	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	264.90	03/2021 -	03/2021
25	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
26	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
27	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
28	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023
29	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	92.47	03/2022 -	03/2022
30	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	82.76	03/2020 -	03/2020
31	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
32	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
33	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
34	VIJAY WEST OPENCASE PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
35	AMADAND OPENCASE EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	116.09	03/2021 -	03/2021
36	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,879.89	03/2023 -	03/2023
37	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,043.87	03/2023 -	03/2023
38	DURGAPUR OPENCASE PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.02	03/2023 -	03/2023
39	AMGAON OPENCASE PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	67.41	03/2020 -	03/2020
40	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
41	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.15	03/2021 -	03/2021
42	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	103.99	03/2021 -	03/2021
43	MADANNAGAR OPENCASE PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
44	MALACHUA OPENCASE PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.08	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
45	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	175.30	03/2020 -	03/2020
46	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020
47	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	150.05	03/2021 -	03/2021
48	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
49	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	235.29	03/2022 -	03/2022
50	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	18.45	03/2022 -	03/2022
51	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
52	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	258.40	03/2025 -	03/2025
53	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	199.23	03/2021 -	03/2021
54	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
55	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	409.68	119.73	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
56	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	-	03/2021 -	03/2021
57	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	149.87	03/2021 -	03/2021
58	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	-	03/2025 -	03/2025
59	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	50.56	03/2022 -	03/2022
60	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.81	03/2020 -	03/2020
	Total		72,911.73 -	73,134.27	19,269.29		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
61	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	81.83	08/2020 -	08/2020
	Total		285.95 -	285.95	81.83		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
62	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	100.17	11/2019 -	11/2019
63	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	107.64	11/2019 -	11/2019
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	101.91	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
65	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	92.10	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	401.82		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
66	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>INFORMATION AND BROADCASTING</u>						
	<u>National Building Construcion Corporation Ltd</u>						
67	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]	12/2016	167.70 -	167.70	-	03/2020 -	03/2020
	Total		167.70 -	167.70	.00		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
68	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	102.61	04/2021 04/2021	04/2021
69	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	318.13	01/2020 01/2020	01/2020
70	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
71	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	.30	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	452.96		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
72	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	1,097.54	693.14	10/2018 11/2019	11/2019
73	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	944.42	02/2020 10/2020	10/2020
74	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
75	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	.42	03/2021 -	03/2021
76	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	13.19	12/2021 -	12/2021
77	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20 -	580.20	33.91	02/2021 -	02/2021
78	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	15.04	03/2023 -	03/2023
79	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	115.60	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
80	MMPL PIPELINE REROUTING PROJECT - [N16000261] <u>Chennai Petroleum Corporation Limited</u>	4/2013	449.58 -	449.58	155.19	12/2019 -	12/2019
81	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	909.85	12/2019 -	12/2019
82	RE-LIQUIFIED NATURAL GAS - [N16000301] <u>Gas Authority Of India Limited</u>	8/2017	421.00 -	421.00	109.41	08/2020 -	08/2020
83	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
84	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	1.00	08/2020 09/2020	09/2020
85	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	-	02/2021 -	02/2021
86	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	934.68	12/2021 -	12/2021
87	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	42.63	10/2022 -	10/2022
88	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	46.48	10/2022 -	10/2022
89	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	27.01	07/2022 -	07/2022
90	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	61.78	10/2022 -	10/2022
91	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	48.22	07/2022 -	07/2022
92	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	995.48	12/2020 -	12/2020
93	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,256.48	12/2020 -	12/2020
94	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	171.48	12/2020 -	12/2020
95	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	121.99	04/2022 -	04/2022
96	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,395.00	12/2020 -	12/2020
97	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,256.25	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						
98	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	689.03	10/2014 08/2019	08/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
100	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	6.94	06/2022 -	06/2022
101	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	114.80	11/2019 -	11/2019
102	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
103	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
104	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	63.55	11/2020 -	11/2020
105	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	717.33	03/2021 -	03/2021
106	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,376.01	03/2020 -	03/2020
107	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	375.09	09/2019 -	09/2019
108	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,438.13	06/2020 -	06/2020
109	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	5,541.02	07/2020 -	07/2020
	<u>Indian Oil Corporation Limited</u>						
110	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
111	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
112	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	917.26	08/2021 -	08/2021
113	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
114	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
115	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
116	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	284.31	08/2021 -	08/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
117	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
118	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	132.24	09/2019 -	09/2019
119	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	14.12	02/2020 -	02/2020
120	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	13.11	01/2021 -	01/2021
121	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
122	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
123	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	325.42	10/2019 -	10/2019
124	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	8.85	10/2021 -	10/2021
125	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	142.12	03/2021 -	03/2021
126	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	142.67	08/2020 -	08/2020
127	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	178.05	02/2020 -	02/2020
128	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	242.10	10/2021 -	10/2021
129	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	7.82	01/2021 -	01/2021
130	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	15.01	12/2021 -	12/2021
131	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020
132	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	.71	08/2020 -	08/2020
133	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,569.01	09/2019 -	09/2019
134	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	7.75	02/2020 -	02/2020
135	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	531.40	09/2019 -	09/2019
136	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	8.19	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
137	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,872.71	09/2019 -	09/2019
138	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
139	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	376.04	09/2019 -	09/2019
140	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	12.28	06/2020 -	06/2020
141	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	108.00	07/2020 -	07/2020
142	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	36.68	12/2019 -	12/2019
143	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	37.47	01/2021 -	01/2021
144	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
145	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	600.35	10/2019 -	10/2019
146	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,526.40	11/2019 -	11/2019
147	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	806.13	12/2020 -	12/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
148	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	154.03	03/2019 09/2019	09/2019
149	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	726.57	12/2019 07/2020	07/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
150	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019
151	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]	10/2018	156.67 -	156.67	-	03/2021 -	03/2021
152	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	-	12/2020 -	12/2020
153	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	405.01	03/2022 -	03/2022
154	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	121.38	05/2021 -	05/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]	11/2015	650.82 -	390.52	380.85	03/2019 05/2020	05/2020
156	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	320.14	03/2023 03/2022	03/2022
157	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,192.66	04/2018 05/2020	05/2020
158	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,323.32	12/2017 03/2020	03/2020
159	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,059.63	1,908.01	03/2015 12/2019	12/2019
160	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,285.65	05/2013 12/2019	12/2019
161	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020
162	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,783.74	05/2019 10/2019	10/2019
163	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	436.53	12/2019 -	12/2019
164	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,475.92	2,745.63	05/2021 12/2021	12/2021
165	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	897.60	11/2019 -	11/2019
166	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	445.24	11/2019 -	11/2019
167	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	565.15	442.18	11/2019 03/2020	03/2020
168	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	407.45	224.89	09/2018 09/2019	09/2019
169	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	356.41	03/2026 -	03/2026
170	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	157.02	05/2020 -	05/2020
171	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019
Oil India Limited							
172	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	83.34	10/2020 -	10/2020
173	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	3.30	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
174	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	682.90	7.60	02/2020 -	02/2020
175	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	158.44	12/2019 -	12/2019
	Total		1,61,801.02 -	1,64,201.56	63,086.76		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
176	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	12,027.37	01/2018 03/2020	03/2020
177	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,110.76	03/2013 12/2020	12/2020
178	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,592.34	473.97	09/2019 02/2022	02/2022
179	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	17,304.00	13,670.00	05/2018 12/2021	12/2021
180	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	9,460.46	12/2018 06/2020	06/2020
181	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	6,334.35	07/2019 06/2020	06/2020
182	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	9,703.00	02/2017 06/2020	06/2020
183	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	1,855.39	03/2023 -	03/2023
184	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
185	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
186	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019
187	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	5,231.15	11/2020 06/2021	06/2021
188	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	8,306.06	01/2020 -	01/2020
189	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,229.51	10/2017 03/2020	03/2020
190	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	16,249.55	10/2011 08/2021	08/2021
	<u>North East Electric Power Corporation</u>						
191	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,419.34	7,494.35	12/2009 08/2019	08/2019
	<u>Power Grid Corporation Of India Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
192	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 12/2019	12/2019
193	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	3,115.72	03/2018 12/2019	12/2019
194	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019
195	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020
196	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020
197	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	92.78	09/2018 09/2019	09/2019
198	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020
199	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020
200	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	52.63	12/2019 12/2019	12/2019
201	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	116.76	02/2020 02/2020	02/2020
202	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	266.03	01/2019 09/2019	09/2019
203	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	187.60	11/2019 11/2019	11/2019
204	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	287.52	04/2018 01/2020	01/2020
205	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022
206	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019
207	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	548.30	10/2017 09/2019	09/2019
208	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 08/2019	08/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
209	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	564.81	01/2024 -	01/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
210	NAITWAR MORI HEP - [N18000265 <u>Thdc India Limited</u>	10/2017	648.33 -	648.33	236.30	12/2021 -	12/2021
211	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	1,587.16	299.55	09/2020 -	09/2020
212	KHURJA SUPER THERMAL POWER PROJECT - [N18000272	3/2019	11,089.42 -	11,089.42	509.30	09/2023 -	09/2023
	Total		2,02,150.59 -	2,38,162.53	1,47,381.36		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
213	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,205.35	03/2023 -	03/2023
214	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	305.00	267.36	03/2019 12/2019	12/2019
215	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	77.48	03/2023 -	03/2023
216	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	145.69	03/2023 -	03/2023
217	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
218	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
219	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
220	KOSI BRIDGE (NL), ECR - [220100304	4/2002	499.41 -	516.02	389.29	03/2020 -	03/2020
221	ARARIA-SUPAUL (NL) - [N22000177	4/2008	1,605.17 -	1,605.17	23.40	- 03/2023	03/2023
	<u>East Coast Railway</u>						
222	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	3/2012	155.81 -	238.03	224.63	03/2020 -	03/2020
223	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	3,382.95	325.64	03/2022 -	03/2022
	<u>Eastern Railways</u>						
224	HANSDIHA-GODDA NL - [N22000236 <u>Indian Railway Construction Company Limited</u>	4/2011	542.18 -	693.80	424.02	03/2020 -	03/2020
225	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418	4/2016	5,200.00 -	1,700.43	48.00	03/2020 06/2023	06/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
226	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	4/2013	3,055.00 -	3,055.00	1,729.64	09/2018 12/2020	12/2020
227	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,970.11	619.50	03/2022 12/2022	12/2022
	<u>Metropolitan Rapid Transport Projects</u>						
228	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	918.53	277.61	03/2014 03/2021	03/2021
	<u>North Central Railway</u>						
229	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 03/2020	03/2020
230	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
231	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	5,021.45	2,935.76	03/2014 03/2022	03/2022
232	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	455.80	03/2021 -	03/2021
233	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.98	03/2020 -	03/2020
234	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.14	03/2020 -	03/2020
235	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	4/2008	333.76 -	360.00	6.67	- 03/2022	03/2022
236	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	4/2010	221.42 -	380.00	38.18	- 03/2022	03/2022
237	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.66	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
238	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	12/2022
239	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
240	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	15.03	01/2022 -	01/2022
	<u>Northern Railway</u>						
241	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
242	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	2,812.27	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
243	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
244	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498	2/2016	393.98 -	393.98	241.23	03/2020 -	03/2020
	<u>Rail Vikas Nigam Ltd.</u>						
245	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99 -	7,000.00	368.23	12/2026 -	12/2026
246	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00 -	2,900.00	1,571.99	03/2023 -	03/2023
247	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,485.85	1,009.30	12/2020 -	12/2020
248	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	1/1991	2,335.67 -	2,335.68	546.57	12/2024 -	12/2024
249	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	1,950.00	1,823.93	03/2020 -	03/2020
250	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	773.94 -	773.94	364.69	12/2024 -	12/2024
251	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.67	837.66	12/2023 -	12/2023
252	PALANPUR-SAMAKHAYALI (DL) - [N22000144	4/2013	1,548.66 -	1,548.66	1,176.15	12/2021 -	12/2021
253	DHASA-JETALSAR (GC) - [N22000141	4/2012	644.38 -	644.38	296.20	03/2021 -	03/2021
254	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,082.32	933.88	12/2021 -	12/2021
	<u>South Central Railway</u>						
255	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	4/2010	704.31 -	1,352.74	269.07	03/2020 03/2020	03/2020
256	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
	<u>South East Central Railway</u>						
257	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	4/2005	383.79 -	1,413.76	1,324.64	- 10/2019	10/2019
258	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,908.51 -	2,686.63	441.10	03/2023 03/2023	03/2023
259	GONDIA-JABALPUR(GC),(SECR) - [220100186	2/1997	511.86 -	1,756.00	1,660.29	04/2020 12/2020	12/2020
260	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	6/2018	229.00 -	860.92	41.54	12/2021 03/2023	03/2023
261	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	4/2015	1,973.00 -	1,973.66	129.54	03/2021 12/2021	12/2021
262	ANUPPUR-KATNI - [N22000485	4/2015	1,370.00 -	1,370.00	276.86	12/2021 12/2021	12/2021
263	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	4/2008	872.00 -	1,226.51	1,039.54	12/2019 10/2019	10/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>South Eastern Railway</u>						
264	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019
	<u>South Western Railway</u>						
265	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
266	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
	<u>Southern Railway</u>						
267	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>West Central Railway</u>						
268	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,027.12	03/2021 03/2023	03/2023
269	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023
270	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,247.64	154.63	03/2022 09/2022	09/2022
271	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	367.59	03/2022 03/2023	03/2023
272	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	1,763.93	624.49	03/2020 03/2022	03/2022
	<u>Western Railway</u>						
273	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	3,860.40	1,676.43	03/2022 03/2023	03/2023
274	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	321.62	125.76	03/2012 03/2022	03/2022
275	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	682.91	03/2022 03/2023	03/2023
276	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	92.69	- 03/2021	03/2021
277	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	719.73	03/2022 03/2022	03/2022
278	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,310.23	1,363.06	03/2020 03/2021	03/2021
279	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	858.96	534.00	03/2019 03/2022	03/2022
280	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,037.15	992.18	03/2021 03/2022	03/2022
281	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494]	4/2017	691.84 -	663.29	163.85	03/2020 03/2021	03/2021
282	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	86.45	06/2020 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
283	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	2/1991	551.51 -	809.07	616.90	03/2019 03/2020	03/2020
284	SURENDRA NAGAR RAJKOT - [N22000392	4/2015	1,002.39 -	1,002.39	374.60	03/2021 03/2021	03/2021
	Total		2,26,738.85 -	2,92,456.10	63,427.31		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
285	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
286	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
287	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
288	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
289	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
290	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
291	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	3/2018	297.12 294.00	297.12	138.68	07/2018 01/2020	01/2020
292	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	3/2018	289.67 290.00	289.67	60.76	08/2018 02/2020	02/2020
293	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936	3/2018	244.95 245.00	244.95	84.47	08/2018 02/2020	02/2020
294	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	26.78	08/2018 03/2020	03/2020
295	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932	1/2017	319.28 -	319.28	101.28	08/2017 03/2020	03/2020
296	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931	11/2016	290.15 -	290.15	69.42	05/2017 11/2019	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
297	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]	11/2016	378.24 -	378.24	187.63	01/2018 01/2020	01/2020
298	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]	9/2016	372.68 -	372.68	179.43	02/2017 09/2019	09/2019
299	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	333.21	256.29	12/2015 12/2019	12/2019
300	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]	1/2017	576.48 -	576.48	177.36	01/2018 01/2020	01/2020
301	REHABILITATION AND UPGRADATION OF EEPURPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 - [N24000971]	8/2016	574.19 -	574.19	456.98	07/2017 07/2019	07/2019
302	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]	1/2016	348.95 -	348.95	144.95	08/2016 12/2019	12/2019
303	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]	3/2016	444.84 -	444.84	208.09	09/2016 12/2019	12/2019
304	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]	1/2016	386.09 -	386.09	160.20	05/2016 08/2019	08/2019
305	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]	8/2016	350.61 -	350.61	301.70	01/2017 12/2019	12/2019
306	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]	1/2018	418.03 -	418.03	103.64	08/2018 02/2020	02/2020
307	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09 995.00	995.09	401.90	05/2016 03/2020	03/2020
308	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	3/2018	504.19 504.00	504.19	269.70	11/2018 05/2020	05/2020
309	SHIROD SHAHPURER TO NANDED - [N24001041]	1/2017	211.34 -	211.34	100.83	07/2019 -	07/2019
310	MAHAD TO RAIGAD FORT - [N24001038]	7/2018	237.40 -	237.40	7.34	05/2020 -	05/2020
311	JAHIRABAD TO LATUR - [N24001040]	1/2017	461.96 -	461.96	127.43	11/2019 -	11/2019
312	KAIJ TO KUSALAM - [N24001037]	1/2017	554.78 -	554.78	157.90	07/2019 -	07/2019
313	MANSAR TO SALAIKHURD - [N24001035]	1/2018	418.36 -	418.36	102.13	12/2019 -	12/2019
314	MAJALGAON TO KAIJ - [N24001036]	1/2017	413.99 -	413.99	310.33	07/2019 -	07/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
315	PARTUR TO MAJALGAON - [N24001034	1/2017	420.57 -	420.57	157.39	07/2019 -	07/2019
316	MANTHA TALUKAS BORDER TO PARTUR - [N24001033	1/2017	486.19 -	486.19	210.29	07/2019 -	07/2019
317	MANJUSUMBA TO CHUMBALI - [N24001031	1/2017	228.54 -	228.54	92.30	08/2019 -	08/2019
318	NANDED TO JALKOT - [N24001069	12/2017	456.93 457.00	456.93	55.50	09/2019 -	09/2019
319	WASHIM TO DASTAPUR - [N24001068	3/2018	165.51 -	165.51	25.45	12/2019 -	12/2019
320	OMREGA TO AUSA - [N24001067	3/2018	272.04 272.00	272.04	72.24	12/2019 -	12/2019
321	LATUR TO PANGAON - [N24001066	3/2018	336.47 336.00	336.47	85.48	12/2019 -	12/2019
322	PARBHANI TO GANGKHED - [N24001065	3/2018	238.19 238.00	238.19	23.85	12/2019 -	12/2019
323	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	3/2018	217.14 217.00	217.14	58.77	02/2020 -	02/2020
324	WADIGODRI TO DHANGRIPIMPRI - [N24001063	3/2018	194.23 194.00	194.23	57.23	02/2020 -	02/2020
325	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	3/2018	336.21 336.00	336.21	58.66	12/2019 -	12/2019
326	CHIKALI TO DHAD - [N24001061	3/2018	189.46 189.00	189.46	21.00	12/2019 -	12/2019
327	PALPHATA TO PHULAMBARI - [N24001060	3/2018	227.19 227.00	227.19	50.23	12/2019 -	12/2019
328	SHIVUR TO YEOLA - [N24001059	3/2018	181.08 -	181.08	7.45	12/2019 -	12/2019
329	KARWANDI TO RAJURI - [N24001058	3/2018	276.95 277.00	276.95	85.47	12/2019 -	12/2019
330	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	2/2017	422.02 422.00	422.02	224.01	07/2019 -	07/2019
331	HELWAK TO KARAD - [N24001055	2/2017	416.99 -	416.99	111.40	07/2019 -	07/2019
332	TASGAON TO SHIRDHON - [N24001054	1/2017	195.64 196.00	195.64	93.73	11/2019 -	11/2019
333	SANGOLA TO JATH - [N24001052	1/2018	257.38 257.00	257.38	62.15	12/2019 -	12/2019
334	NALDURG TO AKKALKOT - [N24001051	2/2018	274.50 275.00	274.50	224.39	12/2019 -	12/2019
335	VITA TO NAGAJ - [N24001050	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019
336	KARAD TO VITA - [N24001049	1/2018	344.85 245.00	344.85	66.04	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
337	MEHKAR TO AJISPUR - [N24001048]	1/2017	232.77 -	232.77	85.51	07/2019 -	07/2019
338	BHADGAON TO CHALISGAON - [N24001047]	1/2018	259.55 260.00	259.55	150.00	11/2019 -	11/2019
339	RALEGAON TO RAMTIRTH - [N24001046]	1/2017	210.81 -	210.81	106.69	07/2019 -	07/2019
340	JALGAON TO BHADGAON - [N24001045]	1/2018	307.54 308.00	307.54	106.59	11/2019 -	11/2019
341	NILAJPHATA TO BHANDARA - [N24001043]	1/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020
342	SALAIKHURD TO TIRORA - [N24001042]	1/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019
343	PIMPLA TO MANJARSUMBHA - [N24001030]	1/2017	595.77 -	595.77	118.44	08/2019 -	08/2019
344	AHMADPUR TO PIMPLA - [N24001029]	1/2017	422.38 -	422.38	148.58	08/2019 -	08/2019
345	PATGAON KHOPOLI SECTION I - [N24001028]	1/2018	170.00 -	170.00	15.57	12/2019 -	12/2019
346	SHAHAPUR PATGAON SECTION I - [N24001027]	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
347	AJANTHA TO BULDHANA - [N24001008]	2/2017	401.00 401.00	401.00	82.81	07/2019 -	07/2019
348	KARASWADA TO BAMBOLIM - [N24001005]	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019
349	PATRADEVI TO KARASWADA 4L - [N24001004]	3/2017	634.32 -	634.32	108.33	05/2020 -	05/2020
350	SARSAM TO KOTHARI - [N24001002]	2/2016	545.64 -	545.64	64.01	07/2019 -	07/2019
351	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	4.86	04/2020 -	04/2020
352	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	95.97	12/2019 -	12/2019
353	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
354	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
355	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	567.61	11/2019 -	11/2019
356	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	52.87	06/2021 -	06/2021
357	BHOKAR TO SARSAM - [N24001128]	2/2017	295.09 -	295.99	155.64	07/2019 -	07/2019
358	NAGBHID TO ARMORI - [N24001119]	9/2016	269.05 -	269.05	203.91	07/2019 -	07/2019
359	MUL TO CHANDRAPUR - [N24001117]	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
360	NASRATPUR TO BARASGAON - [N24001112]	7/2016	406.54 407.00	406.54	142.00	09/2019 -	09/2019
361	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	76.29	04/2020 -	04/2020
362	KUSUMBA TO MALEGAON - [N24001109]	3/2018	243.45 244.00	243.45	58.02	12/2019 -	12/2019
363	CHALISGAON TO NANDGAON - [N24001108]	3/2018	206.97 207.00	206.97	68.89	12/2019 -	12/2019
364	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020
365	SARAD VANI PIMPALGAON - [N24001103]	1/2017	250.46 -	250.46	103.63	07/2019 -	07/2019
366	PANDHARPUR TO SANGOLA - [N24001102]	7/2017	218.38 -	218.38	168.75	07/2019 -	07/2019
367	KURUDWADI TO PANDHARPUR - [N24001101]	1/2017	307.63 -	307.63	148.17	07/2019 -	07/2019
368	AHMEDNAGAR TO BARAMATI - [N24001100]	1/2017	955.40 -	955.40	331.50	08/2019 -	08/2019
369	MHASWAD TO TEMBHURNI - [N24001099]	1/2017	488.60 -	488.60	151.71	07/2019 -	07/2019
370	WARDHA TO HINGAGHAT - [N24001098]	1/2018	216.90 217.00	216.90	20.00	12/2019 -	12/2019
371	SELDOH TO PANVAR - [N24001097]	7/2018	404.33 404.00	404.33	14.19	05/2020 -	05/2020
372	ARNI TO NAIGAINBANDI - [N24001093]	12/2017	309.94 310.00	309.94	16.32	12/2019 -	12/2019
373	SATARA TO MHASWAD - [N24001092]	1/2017	653.46 -	653.46	203.42	07/2019 -	07/2019
374	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
375	KOLDE TO KHETIYA - [N24001090]	1/2017	509.18 -	509.18	175.93	07/2019 -	07/2019
376	MALEGAON TO RISOD - [N24001089]	2/2018	303.24 303.00	303.24	93.97	12/2019 -	12/2019
377	JALGAON TO NANDURA - [N24001088]	3/2018	177.84 177.00	177.84	45.69	12/2019 -	12/2019
378	BODHWAD TO STATE BORDER - [N24001086]	1/2017	178.26 -	178.26	96.95	07/2019 -	07/2019
379	MANGRUPHIR TO MAHAN - [N24001087]	3/2018	222.13 222.00	222.13	23.36	11/2019 -	11/2019
380	PAHUR TO BODHWAD - [N24001084]	1/2017	244.93 -	244.93	34.23	05/2020 -	05/2020
381	CHIKLI TO TAKARKHED - [N24001083]	3/2018	393.10 393.00	393.10	111.97	12/2019 -	12/2019
382	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
383	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]	3/2018	294.87 295.00	294.87	36.30	12/2019 -	12/2019
384	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
385	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	64.97	06/2020 -	06/2020
386	PUNE TO MALE VILLAGE - [N24001078]	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
387	DEULGAON SAKARSHA TO MEHKAR - [N24001076]	3/2018	219.91 -	219.91	106.46	12/2019 -	12/2019
388	KUNDRAL TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	97.75	12/2019 -	12/2019
389	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]	3/2018	249.29 -	249.29	65.20	12/2019 -	12/2019
390	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	44.02	08/2020 -	08/2020
391	KOTHARI TO DHANORA - [N24001073]	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
392	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	66.50	12/2019 -	12/2019
393	JALKOT TO TOGRI - [N24001071]	7/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020
394	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	89.15	12/2019 -	12/2019
395	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
396	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
397	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
398	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
399	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
400	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
401	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82 -	537.82	-	09/2019 -	09/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
402	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
403	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868	3/2018	253.44 -	253.44	-	07/2019 -	07/2019
404	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
405	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
406	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
407	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
National Highways Authority Of India							
408	FOUR LANNING OF SIMGA - SARAGAON - [N24000495	12/2015	596.67 -	596.67	387.97	05/2018 10/2019	10/2019
409	FOUR / SIX LANNING OF RAIPUR - SIMGA (PKG-1) - [N24000510	12/2015	726.67 -	598.13	394.83	04/2018 03/2020	03/2020
410	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020
411	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
412	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
413	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	3/2018	1,029.96 -	1,261.05	-	- 03/2021	03/2021
414	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020
415	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
416	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	69.68	03/2020 -	03/2020
417	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	608.81	04/2020 -	04/2020
418	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020
National Highways Development Project							

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
419	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 [N24000475]	11/2015	628.45 -	628.45	207.68	01/2020 -	01/2020
420	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 [N24000478]	12/2015	957.54 -	957.54	412.39	02/2020 -	02/2020
	<u>Public Works Dept Of State</u>						
421	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]	3/2015	271.45 -	271.45	143.44	10/2015 11/2019	11/2019
422	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C [N24000999]	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019
423	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]	3/2018	192.67 -	192.67	-	07/2019 -	07/2019
424	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR) - [N24000996]	1/2017	605.08 -	605.08	213.00	10/2019 -	10/2019
425	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]	1/2017	196.52 -	196.52	92.88	10/2019 -	10/2019
426	REHABILITATION AND UPGRADATION OF HARPALPUR-SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]	3/2016	208.50 -	208.50	102.98	11/2019 -	11/2019
427	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
428	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
429	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]	3/2018	170.57 -	170.57	46.23	11/2020 -	11/2020
430	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
431	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) [N24000908]	1/2017	276.01 -	276.01	180.95	03/2019 07/2019	07/2019
432	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020
433	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
434	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]	3/2018	626.76 -	626.76	46.62	07/2020 -	07/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
435	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	.34	09/2020 -	09/2020
436	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	134.38	04/2020 -	04/2020
437	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	7.40	11/2019 -	11/2019
438	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	23.54	11/2019 -	11/2019
439	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	94.93	06/2020 -	06/2020
440	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	80.71	12/2019 -	12/2019
441	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	32.04	05/2020 -	05/2020
442	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	121.47	12/2019 -	12/2019
443	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176	10/2016	172.63 -	172.63	35.30	12/2020 -	12/2020
444	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175	10/2016	167.62 -	167.62	34.89	12/2020 -	12/2020
445	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	74.49	11/2020 -	11/2020
446	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	.50	09/2021 -	09/2021
447	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	376.71	01/2020 -	01/2020
448	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	171.00	01/2020 -	01/2020
449	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	125.09	09/2019 -	09/2019
450	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	67.87	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
451	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]	3/2018	212.99 -	212.99	59.56	06/2020 -	06/2020
452	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
453	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]	3/2017	217.35 -	217.35	33.02	11/2020 -	11/2020
454	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]	11/2016	336.25 -	336.25	44.91	09/2019 -	09/2019
455	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]	10/2016	171.90 -	171.90	14.17	08/2020 -	08/2020
456	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
457	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]	4/2014	279.70 398.22	398.52	314.63	08/2017 07/2019	07/2019
458	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]	3/2018	191.21 -	191.21	68.26	11/2019 -	11/2019
459	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]	3/2018	254.30 -	254.30	20.09	10/2020 -	10/2020
460	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	3/2016	271.17 291.20	291.20	79.43	11/2018 11/2019	11/2019
	Total		70,928.48 -	71,834.13	21,395.04		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
461	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	21.00	05/2021 -	05/2021
462	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	109.97	05/2020 -	05/2020
	<u>Inland Waterways Authority Of India</u>						
463	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	4,200.00	1,256.55	03/2023 -	03/2023
	Total		6,969.00 -	6,969.00	1,387.52		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
464	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	15,811.82	05/2015 07/2020	07/2020
	<u>Rastriya Ispat Nigam Limited</u>						
465	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	1,155.53	09/2018 09/2019	09/2019
466	CENTRAL DISPATCH YARD - [N12000119]	8/2015	320.66 -	320.66	206.91	08/2018 10/2019	10/2019
467	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,500.00	1,292.76	12/2017 10/2019	10/2019
	<u>Steel Authority Of India Limited (Sail)</u>						
468	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	2,970.60	04/2018 11/2019	11/2019
469	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	99.71	06/2019 06/2020	06/2020
470	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	431.27	10/2017 06/2020	06/2020
471	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	927.19	12/2017 11/2019	11/2019
472	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	2.89	09/2020 -	09/2020
	Total		26,228.23 -	33,485.23	22,898.68		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
473	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	240.10	117.63	10/2018 09/2019	09/2019
	Total		231.80 -	240.10	117.63		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
474	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	47.30	05/2020 -	05/2020
475	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
476	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
477	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	326.38	07/2019 12/2019	12/2019
478	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]	1/2018	223.37 -	223.37	29.51	07/2020 09/2020	09/2020
479	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
	<u>Maharastra Metro Rail Corporation Ltd.</u>						
480	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	2,642.09	11/2021 01/2022	01/2022
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
481	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023
482	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023
	<u>National Building Construcion Corporation Ltd</u>						
483	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	Total		31,731.35 -	31,916.74	6,436.69		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
484	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Total		233.57 -	233.57	32.20		
	Grand Total		8,14,979.23	9,27,687.98	3,47,398.95		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs.150 Crore and above							
						(July 2019)	
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	Total		3,492.00 -	6,840.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 -	860.00	03/2021 -	03/2021	.02
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
8	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	09/2017	11.42
9	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
13	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
14	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		19,818.83 -	20,957.14			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
16	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45
18	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
19	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
21	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
22	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
24	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
25	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
26	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
27	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
28	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71
	<u>Oil India Limited</u>						
29	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
30	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
31	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	02/2020	25.55
	Total		16,950.80 -	20,051.58			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
32	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
34	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
35	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	06/2020	9.64
36	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55
37	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
38	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
39	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87
40	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55
41	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
42	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
43	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
44	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
45	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
46	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	08/2019	38.61
47	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
48	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	06/2019	14.60
49	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	07/2019	26.82
50	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	08/2019	27.92
51	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17
52	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
53	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Thdc India Limited</u>						
54	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75
55	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
56	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,25,916.71 -	1,74,634.84			
	<u>RAILWAYS</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Central Railways</u>						
57	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	184.06	305.00	03/2019	12/2019	65.71
58	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	2,271.50	3,712.50	03/2021	03/2022	63.44
59	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00	5,341.68	03/2024	03/2024	120.28
60	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	02/2016	2,750.00	3,438.51	03/2024	-	25.04
61	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	02/2015	3,627.47 3,627.00	3,627.47	03/2024	03/2022	.01
62	DAUND - MANMAD (236 KM) - [N22000360	02/2016	1,876.00	2,081.27	03/2023	03/2023	10.94
	<u>Container Corporation Of India</u>						
63	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50	235.00	03/2019	12/2020	.21
	<u>East Central Railways</u>						
64	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	03/1999	1,033.07	3,376.00	-	03/2021	226.79
65	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	528.65	2,066.77	-	03/2023	290.95
66	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	749.00	03/2012	03/2020	163.78
67	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	04/1997	324.73	1,156.41	03/2012	03/2020	256.11
68	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87	589.15	-	03/2022	261.73
69	KOSI BRIDGE (NL), ECR - [220100304	04/2002	499.41	516.02	03/2020	03/2020	3.33
70	ARA-BHABHUA ROAD (NL) - [N22000166	04/2008	633.87	2,396.88	-	03/2023	278.13
71	NAWADA-LAXMIPUR (NL) - [N22000167	04/2008	620.57	2,626.98	-	03/2024	323.32
72	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168	04/2008	445.25	2,860.55	-	03/2024	542.46
73	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67	549.75	-	03/2024	32.26
74	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20	2,995.01	-	03/2024	818.15
75	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00	729.92	-	03/2021	124.59
76	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56	2,614.36	-	03/2022	590.61
77	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00	926.09	-	03/2024	338.91

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	03/2024	252.66
79	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2022	43.41
80	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	400.17	- -	01/2020	87.86
81	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
82	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
83	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
84	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	727.29	- -	09/2019	302.22
85	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	12/2021	350.27
<u>East Coast Railway</u>							
86	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
87	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	12/2023	29.96
88	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
89	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07
90	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
91	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
92	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
<u>Eastern Railways</u>							
93	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22
94	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80
95	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46
96	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2020	27.96
97	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	226.22	- -	03/2021	28.68

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
99	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01
100	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25
101	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15
102	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82
103	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	09/2021	6.48
104	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08
105	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30
106	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19
107	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
108	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	376.90	- -	03/2020	30.71
109	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	471.81	- -	05/2019	80.51
110	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75
111	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
112	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
<u>Metropolitan Rapid Transport Projects</u>							
113	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
114	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57
115	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	-	48.06

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
116	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
117	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	03/2015	188.33
118	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>						
119	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
120	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80
121	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
122	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2022	7.86
123	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95
124	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,496.67	03/2019 -	-	38.86
125	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2022	71.62
126	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11
127	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
128	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
129	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2021	63.25
130	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
131	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
132	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
133	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
134	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60 -	1,300.00	04/2010 -	-	241.57
	<u>North Eastern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
135	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	-	-	60.34
136	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08	12/2022 -	12/2022	234.77
137	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
138	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
139	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	-	267.13
140	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
141	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
142	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16
143	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91
144	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
145	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	12/2021	116.16
146	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
147	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64
148	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
149	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15	- -	-	95.85
150	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47
151	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
152	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
153	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35
154	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	12/2019	69.36
	<u>Northern Railway</u>						
155	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	03/2024	25.87

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
156	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
157	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00	- -	03/2022	137.45
158	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	06/2020	57.68
159	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
160	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67
161	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
162	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	855.00	03/2016 -	03/2021	36.80
	<u>Rail Vikas Nigam Ltd.</u>						
163	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
164	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	85.99
165	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
166	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
167	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
168	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
169	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
170	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
171	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
172	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
173	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00	03/2020 -	03/2020	173.31
174	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
175	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22
176	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Railway Electrification</u>						
177	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
178	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
179	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	-	-	161.86
180	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
181	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	-	-	93.56
182	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	-	-	92.93
183	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
184	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	1,723.00	03/2000 -	03/2021	1,72,200.00
185	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	-	-	.00
	<u>South East Central Railway</u>						
186	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94
187	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95
	<u>South Eastern Railway</u>						
188	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
189	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	11/2019	153.41
190	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	-	-	131.89
191	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	-	54.99
192	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
193	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	<u>South Western Railway</u>						
194	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	-	12/2023	24.09
195	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	12/2023	57.65

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
196	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	-	12/2023	14.14
197	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	-	12/2023	12.38
198	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
199	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
200	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98
201	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	-	-	295.78
202	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	-	-	294.63
203	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
204	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
205	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	-	-	339.33
206	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	-	-	78.78
207	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	-	-	180.17
208	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	-	-	295.05
209	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	-	03/2020	173.71
210	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
211	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
212	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	-	253.33
213	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
214	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
	<u>Western Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
215	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18
216	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	202.35	03/2011 -	03/2017	2.74
217	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
218	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,30,811.66 -	2,47,117.96			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
219	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	- -	-	3.72
	<u>Ministry Of Road Transport And Highways</u>						
220	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	- -	-	9.23
221	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
222	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]	01/1991	675.00 -	780.77	- -	-	15.67
223	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	08/2016 -	-	14.02
224	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 -	377.64	10/2016 -	-	5.42
225	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]	03/2015	226.31 226.00	226.31	10/2017 -	-	.14
226	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]	06/2016	157.30 157.00	157.30	06/2018 -	-	.19
227	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06
228	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
229	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00	297.12	07/2018 -	01/2020	1.06
230	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	05/2020	.04
231	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	03/2020	.01
232	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	12/2019	.10
233	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	12/2019	.03
234	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.15
235	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	10/2019	.01
236	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	06/2020	.02
237	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	12/2019	.05
238	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	12/2019	40.76
239	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	12/2019	.15
240	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00
241	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	06/2020	.05
242	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	12/2019	.08
243	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	12/2019	.24
244	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	12/2019	.06
245	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	02/2020	.12
246	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	02/2020	.06
247	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	12/2019	.08
248	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	12/2019	.14
249	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	12/2019	.01

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
250	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00	301.38	08/2020 -	08/2020	.13
251	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00	344.25	08/2020 -	08/2020	.07
252	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00	225.25	12/2019 -	12/2019	.11
253	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	06/2020 -	06/2020	.01
254	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00	177.84	12/2019 -	12/2019	.47
255	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00	536.65	12/2019 -	12/2019	50.74
256	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00	244.04	03/2019 -	12/2019	.02
257	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00	264.41	03/2019 -	12/2019	.16
258	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00	381.08	05/2020 -	05/2020	26.19
259	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	07/2019 -	-	.31
	<u>National Highways Authority Of India</u>						
260	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	08/2019	92.75
261	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
262	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
263	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
264	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2020	106.50
265	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58
266	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	12/2019	21.90
267	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
268	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
269	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
270	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
271	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
272	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
273	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
274	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
275	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
276	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
277	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
278	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
279	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
280	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	09/2019	4.02
281	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
282	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
283	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
284	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
285	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	-	03/2021	22.44
<u>National Highways Development Project</u>							
286	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	08/2019	46.51
287	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
<u>Public Works Dept Of State</u>							

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
288	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
289	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
290	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
291	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	.12
292	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75
293	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06
294	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21
295	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
296	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67
297	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923	03/2018	464.07 -	464.07	11/2018 -	-	.00
298	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925	10/2018	400.76 -	400.76	05/2019 -	-	.00
299	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926	08/2017	962.43 -	962.43	03/2018 -	-	.00
300	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	09/2019	.07
301	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	01/2020	.13
302	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46
	Total		43,298.25 -	58,003.76			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
303	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	6.97
	<u>Mumbai Port Trust</u>						
304	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	-	82.72
	<u>Port Trust</u>						
305	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
306	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
307	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
308	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85
309	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2021	30.58
310	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	06/2014	157.84 -	169.16	03/2017 -	-	7.17
311	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.60

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(July 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
312	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR [N28000126]	01/2019	790.79 -	800.00	06/2021 -	03/2022	1.16
	<u>Chennai Metro Rail Ltd</u>						
313	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
314	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
315	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Kochi Metro Rail Corporation Ltd</u>						
316	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
317	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		28,016.42 -	34,022.73			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
318	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		4,10,863.04	6,69,569.63			

List of Delayed Projects w.r.t. Latest Schedule

Annexure -XIV

Costing Rs.150 Crore and above									
								(July 2019)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	13,838.00	12/2015 -	06/2020	54	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	11,091.00	12/2016 -	12/2020	48	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	14,864.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	45,577.74				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	-
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9	-
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	-
	Total		3,573.83 -	3,700.62	662.64				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
10	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	180.52	04/2014 -	11/2019	67	-
11	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	244.43	05/2014 -	03/2020	70	-
	<u>Central Coal Fields Limited</u>								
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	179.87	03/2012 -	03/2021	108	-
14	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	362.47	03/2016 -	03/2021	60	-
15	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.82	03/2014 -	03/2021	84	-
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	354.48	07/2012 -	03/2022	116	-
	<u>Eastern Coal Fields Limited</u>								
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	486.13	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	-
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	493.85	03/2017 -	03/2020	36	-
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N060000114]MCL,ODISHA	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12	-
21	KULDA EXPN OC. (5.00 MTY) - [N060000115]MCL,ODISHA	06/2014	289.03 -	289.03	75.78	03/2018 -	03/2020	24	-
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	228.90	03/2012 -	03/2021	108	-
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	390.94	03/2013 -	03/2021	96	-
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022	108	-
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022	144	-
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N060000112]MCL,ODISHA	05/2014	479.15 -	479.15	196.26	03/2019 -	03/2022	36	-
	<u>Neyveli Lignite Corporation</u>								
27	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N060000138]NLC,TAMIL NADU	04/2013	1,458.17 -	709.06	448.19	06/2015 -	09/2019	51	-
28	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N060000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,567.64	12/2015 -	12/2019	48	-
	<u>Singareni Colliers Company Limited</u>								
29	RKP OCP PHASE-I - [N060000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.15	03/2015 -	03/2020	60	-
30	KOYAGUDEM OPENCAST PROJECT - [N060000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	-
31	KISTARAM OCP - [N060000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	115.71	03/2015 -	03/2021	72	-
32	RCE OF INDARAM OCP(1.20 MTPA) - [N060000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	7.23	03/2015 -	03/2021	72	-
33	JALAGAM VENGALA RAO OCP-II - [N060000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	-
34	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N060000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	54.00	03/2019 -	03/2021	24	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132	-
36	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	296.92	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
37	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.49	191.40	03/2015 -	03/2020	60	-
38	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72	-
39	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	177.65	03/2016 -	03/2020	48	-
40	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24	-
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	192.68	03/2014 -	03/2021	84	-
	<u>Western Coal Fields Limited</u>								
42	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	17.71	03/2023 -	03/2024	12	-
43	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	115.28	03/2021 -	03/2024	36	-
	Total		18,387.03 -	19,603.41	13,518.40				
	<u>FERTILISERS</u>								
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	209.44	160.07	11/2016 -	09/2019	34	-
	Total		197.79 -	209.44	160.07				
	<u>INFORMATION AND BROADCASTING</u>								
	<u>Central Public Works Department</u>								
45	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	-
	Total		204.32 -	204.32	.00				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
46	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	3,518.66	08/2018 -	11/2019	15	-
47	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	-
48	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	495.00	06/2019 -	02/2022	32	-
	<u>Gas Authority Of India Limited</u>								

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
49	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	140.90	04/2018 -	08/2019	16	-
50	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,371.62	12/2012 -	02/2022	110	-
	<u>Indian Oil Corporation Limited</u>								
51	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	2,573.02	09/2017 06/2019	07/2019	22	1
52	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	08/2019	9	-
53	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	250.31	08/2019 -	09/2019	1	-
54	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	306.24	01/2019 -	12/2019	11	-
55	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	1,562.10	07/2019 -	12/2019	5	-
56	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	22.66	06/2020 -	08/2020	2	-
57	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	256.76	07/2018 -	10/2020	27	-
58	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	38.51	02/2020 -	10/2020	8	-
59	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	85.08	02/2020 -	10/2020	8	-
60	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	454.65	12/2018 -	02/2021	26	-
61	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	44.00	04/2020 -	03/2021	11	-
62	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	34.07	01/2021 -	04/2021	3	-
63	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	77.27	04/2021 -	07/2021	3	-
64	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	26.83	10/2020 -	08/2021	10	-
65	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	27.05	01/2021 -	10/2021	9	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
66	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	39.76	08/2021 -	11/2021	3	-
67	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.07	04/2022 -	02/2023	10	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
68	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	68.27	03/2020 -	09/2020	6	-
	<u>Oil & Natural Gas Corporation Limited</u>								
69	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	145.60	01/2014 -	11/2019	70	-
70	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1	-
71	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	3,011.57	06/2020 -	08/2021	14	-
72	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	-	12/2021 -	03/2022	3	-
	<u>Oil India Limited</u>								
73	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
74	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33	-
	Total		68,446.97 -	71,383.17	16,750.74				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
75	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,152.85	04/2020 -	12/2023	44	-
	<u>National Hydro-Electric Power Corporation</u>								
76	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,522.82	09/2009 -	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
77	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	9,996.59	7,840.42	07/2012 -	09/2020	98	-
78	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,044.25	06/2019 09/2019	09/2021	27	24
	<u>Power Grid Corporation Of India Limited</u>								
79	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	340.88	251.33	03/2018 03/2019	07/2019	16	4
80	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	1,429.38	1,011.38	01/2019 -	07/2019	6	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
81	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	562.25	392.96	03/2019 03/2019	07/2019	4	4
82	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	407.79	04/2019 04/2019	07/2019	3	3
83	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	84.17	06/2019 -	07/2019	1	-
84	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,308.50	04/2019 -	07/2019	3	-
85	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,237.45	11/2008 06/2019	08/2019	129	2
86	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	190.80	07/2017 06/2019	08/2019	25	2
87	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	81.97	03/2018 03/2018	08/2019	17	17
88	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	430.71	04/2019 04/2019	08/2019	4	4
89	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	153.70	02/2019 06/2019	08/2019	6	2
90	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4	-
91	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2	-
92	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3	-
93	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	117.15	06/2019 06/2019	10/2019	4	4
94	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	210.72	04/2016 03/2017	12/2019	44	33
95	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	405.65	05/2017 06/2019	12/2019	31	6
96	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
97	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10	-
98	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	-
99	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	465.21	11/2016 12/2019	03/2020	40	3
100	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTRIC - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	513.85	01/2018 12/2019	03/2020	26	3
101	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 12/2018	12/2020	24	24
	<u>Thdc India Limited</u>								
102	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	295.73	02/2014 -	10/2019	68	-
103	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	2,969.55	02/2016 -	06/2022	76	-
104	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,718.70	06/2013 -	12/2022	114	-
	Total		64,047.25 -	87,586.48	46,349.07				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>HII Infra Tech Services Limited</u>								
105	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2	-
106	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2	-
107	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5	-
	<u>Hospital Services Consultancy Corporation</u>								
108	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
109	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27	-
110	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	-
111	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	-
112	NEIGRIHMS SHILLONG MEGHALAYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
113	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	-
114	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	-
115	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	-
	Total		4,693.67 -	4,793.45	1,838.34				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
116	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,291.50	03/2021 -	03/2022	12	-
117	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	792.89	297.30	03/2021 -	03/2022	12	-
118	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	1,272.19	271.39	03/2022 -	03/2023	12	-
119	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	540.02	220.34	03/2022 -	03/2024	24	-
120	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR, MAHARASHTRA	02/2016	1,035.16 -	1,035.16	68.93	03/2022 -	03/2024	24	-
121	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR, MAHARASHTRA	02/2016	637.95 -	637.95	54.67	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
122	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	305.00	260.88	03/2019 -	12/2019	9	-
123	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	-
124	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	174.00	150.61	03/2019 -	02/2020	11	-
125	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	493.17	438.08	03/2018 -	03/2020	24	-
126	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	346.32	286.56	03/2019 -	03/2020	12	-
127	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	235.00	7.38	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
128	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	88.93	03/2019 -	12/2019	9	-
129	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 -	1,156.41	1,028.71	03/2012 -	03/2020	96	-
130	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	477.88 283.95	749.00	672.82	03/2012 -	03/2020	96	-
131	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	678.54 678.54	678.54	446.51	03/2019 -	02/2021	23	-
132	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	474.57	03/2020 -	03/2021	12	-
133	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR, BIHAR	12/2015	1,200.20 1,200.20	1,200.20	390.91	03/2020 -	10/2021	19	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
134	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	785.87	457.46	03/2020 -	03/2022	24	-
135	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	35.10	03/2021 -	03/2022	12	-
136	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	15.39	03/2021 -	03/2022	12	-
137	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	424.98	03/2020 -	12/2022	33	-
<u>East Coast Railway</u>									
138	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	116.91	11/2018 -	03/2021	28	-
139	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	879.96	02/2019 -	03/2022	37	-
140	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	349.23	12/2018 -	03/2022	39	-
141	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	624.68	06/2021 -	03/2023	21	-
142	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	125.30	10/2020 -	03/2023	29	-
143	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	654.74	03/2020 -	03/2023	36	-
144	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	320.30	03/2022 -	03/2023	12	-
145	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,354.80	03/2009 -	12/2023	177	-
146	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	148.96	03/2022 -	03/2025	36	-
<u>Eastern Railways</u>									
147	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.47	11/2018 -	03/2021	28	-
148	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.72	02/2013 -	03/2024	133	-
149	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	862.50	03/2019 12/2009	03/2025	72	183
150	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	827.99	12/2010 12/2017	03/2025	171	87
151	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228	-
152	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	288.53	03/2022 -	03/2025	36	-
153	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	433.31	03/2016 -	03/2025	108	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
154	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	102.27	03/2017 -	03/2025	96	-
155	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	153.62	03/2016 -	03/2025	108	-
156	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	200.07	03/2017 -	03/2025	96	-
157	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
158	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	153.64	02/2012 -	03/2025	157	-
159	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	104.65	03/2014 -	03/2025	132	-
160	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Metropolitan Rapid Transport Projects</u>								
161	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,403.52	03/2004 -	03/2021	204	-
162	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
	<u>North Central Railway</u>								
163	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
164	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12	-
165	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	8,821.88	03/2011 -	03/2020	108	-
166	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	1,532.00	606.82	03/2019 -	03/2020	12	-
167	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12	-
168	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	728.00	691.97	03/2019 -	03/2020	12	-
169	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	3,300.00	3,259.74	12/2008 -	03/2021	147	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
170	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	3,000.00	759.42	03/2015 -	10/2021	79	-
171	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 569.63	650.00	45.24	03/2020 03/2020	12/2021	21	21
	<u>North Eastern Railway</u>								
172	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	307.99	01/2019 -	01/2020	12	-
173	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	163.75	04/2017 -	01/2020	33	-
174	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	5.45	04/2016 -	06/2020	50	-
175	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	3.12	12/2019 -	04/2021	16	-
176	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
177	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
178	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	136.88	10/2018 -	10/2019	12	-
179	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	347.99	02/2019 -	12/2019	10	-
180	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	244.02	260.89	11/2019 -	05/2020	6	-
181	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	202.86	12/2019 -	06/2020	6	-
182	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	152.83	03/2020 -	06/2020	3	-
183	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	517.39	02/2019 -	12/2021	34	-
184	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	39.52	03/2020 -	04/2022	25	-
185	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	35.36	08/2022 -	09/2022	1	-
	<u>Northern Railway</u>								
186	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	-
187	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	855.00	834.59	03/2016 -	03/2021	60	-
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	18,583.33	11/2002 -	06/2022	235	-
189	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140	-
	<u>Rail Vikas Nigam Ltd.</u>								
190	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	386.28	03/2009 03/2009	12/2019	129	129

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
191	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,729.78	12/2017 -	03/2020	27	-
192	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,124.56	03/2019 -	03/2020	12	-
193	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,016.52	03/2020 -	06/2020	3	-
194	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	682.17	03/2016 -	12/2020	57	-
195	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,249.76	03/2020 -	03/2021	12	-
196	BANASPAANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	992.67	03/2019 -	03/2021	24	-
197	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,011.48	12/2020 -	03/2021	3	-
198	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	861.32	02/2015 -	12/2021	82	-
199	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,331.60	03/2020 -	03/2022	24	-
200	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	327.46	03/2022 -	12/2024	33	-
201	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	462.05	03/2023 -	12/2024	21	-
202	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,127.22	03/2016 -	03/2025	108	-
203	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.50	843.96	03/2016 -	03/2025	108	-
204	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
205	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,492.47	12/2024 -	03/2026	15	-
<u>South Central Railway</u>									
206	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252	-
207	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	-
208	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	-
209	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	-
210	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
211	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	-
212	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	-
213	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	-
	<u>South East Central Railway</u>								
214	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	646.68	02/2019 03/2020	06/2020	16	3
	<u>South Eastern Railway</u>								
215	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	231.84	12/2018 -	06/2020	18	-
216	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	494.27	03/2020 -	06/2020	3	-
217	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	332.04	03/2021 -	12/2021	9	-
	<u>South Western Railway</u>								
218	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	-
219	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-
220	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	-
221	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	-
222	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	-
223	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-
224	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
225	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	-
	<u>Southern Railway</u>								
226	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	-
227	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	-
228	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	-
229	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	-
230	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
231	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	Total		1,37,446.94 -	2,06,192.16	89,587.42				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
232	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	621.43	387.00	06/2018 -	07/2019	13	-
233	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.00	454.41	03/2017 -	07/2019	28	-
234	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA	01/2017	463.62 664.00	463.62	243.34	06/2019 -	08/2019	2	-
235	AMD I TO SAONER - [N24001021]MORTH,MAHARASHTRA	01/2017	396.91 396.91	396.91	247.48	06/2019 -	08/2019	2	-
236	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	86.63	08/2015 -	09/2019	49	-
237	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	260.00	06/2019 -	10/2019	4	-
238	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	-
239	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	29.83	06/2019 -	11/2019	5	-
240	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	83.81	11/2018 -	11/2019	12	-
241	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	-
242	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	-
243	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	101.79	05/2019 -	12/2019	7	-
244	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	136.43	05/2019 -	12/2019	7	-
245	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	184.75	06/2019 -	12/2019	6	-
246	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	156.29	06/2019 -	12/2019	6	-
247	NAGAJ TO VAJAPUR - [N24001023]MORTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	149.81	06/2019 -	12/2019	6	-
248	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA	01/2017	355.17 355.17	355.17	141.87	07/2019 -	12/2019	5	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
249	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	67.26	06/2019 -	12/2019	6	-
250	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	15.94	03/2019 -	12/2019	9	-
251	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	23.71	03/2019 -	12/2019	9	-
252	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	-
253	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-
254	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	130.85	02/2019 -	02/2020	12	-
255	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	652.90	12/2019 -	03/2020	3	-
256	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	746.91	11/2019 -	03/2020	4	-
257	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	23.73	04/2019 -	04/2020	12	-
258	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	23.03	05/2019 -	05/2020	12	-
259	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	155.78	05/2019 -	05/2020	12	-
260	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	84.00	06/2019 -	06/2020	12	-
261	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	73.97	06/2019 -	06/2020	12	-
262	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	12.00	06/2019 -	06/2020	12	-
263	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	-
264	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	26.42	06/2019 -	06/2020	12	-
265	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	202.31	07/2019 -	07/2020	12	-
266	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12	-
267	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	24.00	09/2018 -	04/2021	31	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
268	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	42.66	05/2019 -	07/2019	2	-
269	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	194.11	174.80	05/2018 -	08/2019	15	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
270	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	187.25	08/2016 -	08/2019	36	-
271	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	229.11	08/2016 -	08/2019	36	-
272	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	153.61	08/2016 -	08/2019	36	-
273	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36	-
274	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	17.42	01/2017 -	01/2020	36	-
275	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	240.21	06/2018 -	03/2020	21	-
276	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	28.67	04/2017 02/2018	02/2021	46	36
277	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46	36
278	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	15.77	04/2017 02/2018	02/2021	46	36
279	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	18.70	04/2017 02/2018	02/2021	46	36
280	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	9.65	- 02/2018	02/2021	-	36
281	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	-	36
282	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	46.85	04/2017 03/2018	03/2021	47	36
283	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	119.56	10/2018 -	10/2021	36	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
284	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60	-
285	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	-	- 04/2019	04/2022	-	36
286	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	-	- 04/2019	04/2022	-	36
	<u>National Highways Authority Of India</u>								
287	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019	76	-
288	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	574.28	448.92	07/2018 -	07/2019	12	-
289	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019	24	-
290	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	691.30	11/2018 -	07/2019	8	-
291	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	728.62	03/2019 -	07/2019	4	-
292	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	319.96	04/2009 -	08/2019	124	-
293	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019	112	-
294	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	966.02	11/2017 -	08/2019	21	-
295	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	08/2019	20	-
296	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	417.86	06/2016 -	08/2019	38	-
297	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	09/2019	138	-
298	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	475.02	05/2018 -	09/2019	16	-
299	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	-
300	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000)TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	-
301	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
302	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	219.09	05/2019 -	09/2019	4	-
303	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019	136	-
304	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	-
305	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,154.18	12/2018 -	10/2019	10	-
306	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	-
307	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	-
308	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7	-
309	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6	-
310	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8	-
311	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	20.54	06/2017 -	11/2019	29	-
312	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	-
313	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	95.96	09/2017 -	11/2019	26	-
314	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019	140	-
315	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	-
316	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	-
317	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	-
318	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	-
319	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	-
320	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
321	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019	39	-
322	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	453.95	09/2017 -	12/2019	27	-
323	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	-
324	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	-
325	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	402.47	06/2018 -	01/2020	19	-
326	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17	-
327	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	-
328	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	02/2020	76	-
329	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 -	02/2020	19	-
330	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	-
331	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020	100	-
332	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	750.38	06/2014 -	03/2020	69	-
333	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,119.56	08/2018 -	03/2020	19	-
334	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	304.69	08/2018 -	03/2020	19	-
335	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	-
336	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	76.83	03/2020 -	04/2020	1	-
337	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	347.91	05/2018 -	05/2020	24	-
338	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	708.62	11/2016 -	05/2020	42	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
339	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	431.21	07/2018 -	05/2020	22	-
340	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	607.37	02/2020 -	05/2020	3	-
341	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	-
342	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2	-
343	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	687.88	03/2020 -	05/2020	2	-
344	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	405.31	07/2016 -	05/2020	46	-
345	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	-
346	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	-
347	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	529.62	05/2018 -	06/2020	25	-
348	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	06/2020	25	-
349	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	1,167.42	254.96	03/2019 -	06/2020	15	-
350	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	604.76	03/2020 -	06/2020	3	-
351	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	256.47	09/2017 -	06/2020	33	-
352	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	551.42	03/2020 -	07/2020	4	-
353	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	-
354	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	-
355	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
356	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	-
357	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	-
358	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	-	09/2017 -	08/2020	35	-
359	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	-	08/2017 -	09/2020	37	-
360	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	-
361	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	16.09	03/2019 -	11/2020	20	-
362	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	-
363	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	480.96	03/2017 -	11/2020	44	-
364	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	-
365	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	329.90	10/2017 -	11/2020	37	-
366	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31	-
367	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	-
368	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	301.68	06/2019 -	12/2020	18	-
369	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	950.69	803.81	08/2019 -	12/2020	16	-
370	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	-
371	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	221.91	03/2020 -	03/2021	12	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
372	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	129.48	03/2019 -	04/2021	25	-
373	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,532.62	-	03/2021 -	04/2021	1	-
374	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-
375	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	-
376	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	-
<u>National Highways Development Project</u>									
377	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019	29	-
378	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	410.72	-	04/2015 -	08/2019	52	-
379	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020	36	-
<u>Public Works Dept Of State</u>									
380	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	244.54	122.31	05/2019 -	07/2019	2	-
381	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	07/2019	9	-
382	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	86.63	08/2015 -	07/2019	47	-
383	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70	-
384	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	11	-
385	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	359.27	200.24	05/2019 -	08/2019	3	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
386	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24	-
387	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	-
388	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	83.40	02/2018 -	11/2019	21	-
389	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	54.49	02/2018 -	11/2019	21	-
390	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	15.22	03/2018 -	11/2019	20	-
391	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	93.96	03/2018 -	11/2019	20	-
392	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	117.16	02/2018 -	11/2019	21	-
393	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	-
394	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	383.94	06/2019 -	11/2019	5	-
395	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	224.94	03/2018 -	11/2019	20	-
396	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	-
397	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019	105	-
398	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	-
399	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76	-
400	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	27

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
401	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	-
402	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	66.95	03/2018 -	12/2019	21	-
403	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	62.22	02/2019 -	12/2019	10	-
404	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	79.02	03/2019 -	12/2019	9	-
405	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	83.83	05/2019 -	12/2019	7	-
406	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	-
407	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	305.61	269.07	09/2014 -	12/2019	63	-
408	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	100.10	07/2018 -	01/2020	18	-
409	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	237.15	08/2017 -	02/2020	30	-
410	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	198.65	07/2018 -	02/2020	19	-
411	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54	-
412	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	53.59	03/2018 -	04/2020	25	-
413	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	373.82	116.33	09/2019 -	05/2020	8	-
414	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	-
415	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	296.28	10/2010 -	06/2020	116	-
416	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	17.10	08/2018 -	06/2020	22	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
417	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39	-
418	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	12.39	08/2018 -	06/2020	22	-
419	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	7.10	03/2018 -	07/2020	28	-
420	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	-
421	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
422	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	-
423	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	-
	Total		1,15,925.12 -	1,20,774.76	73,301.77				
	<u>SHIPPING AND PORTS</u>								
	<u>Kamarajar Port Limited</u>								
424	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-
	Total		600.00 -	257.90	1.45				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
425	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
426	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	5,854.77	12/2018 -	07/2020	19	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
427	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Central Public Works Department</u>								
428	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL	10/2014	162.88 -	162.88	126.07	04/2018 -	07/2019	15	-
429	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD, ANDHRA PRADESH	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5	-
430	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB	02/2014	388.00 -	488.28	422.79	05/2017 -	09/2019	28	-
431	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38	-
432	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59	-
433	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
434	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD, PUNJAB	08/2016	294.00 -	294.00	193.89	04/2019 -	02/2020	10	-
435	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	86.04	10/2012 -	03/2020	89	-
436	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD, TAMIL NADU	12/2015	209.00 -	209.00	127.69	10/2019 -	03/2020	5	-
437	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD, DELHI	06/2015	197.33 -	197.33	42.30	04/2019 -	06/2020	14	-
438	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	80.08	03/2016 -	09/2020	54	-
439	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA	12/2016	246.31 -	246.31	62.56	02/2020 -	09/2020	7	-
440	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	-
441	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR	02/2016	496.18 496.00	498.99	69.60	06/2017 -	10/2020	40	-
442	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD, PUNJAB	01/2018	430.00 -	430.00	60.28	05/2020 -	01/2021	8	-
443	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES (CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	1,592.00	313.93	10/2019 -	03/2021	17	-
444	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD, DELHI	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	-	7

Costing Rs.150 Crore and above

(July 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
445	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 02/2017	05/2021	14	51
446	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	800.00	2.56	06/2021 -	03/2022	9	-
	<u>Hindustan Steelwork Construction Limited</u>								
447	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
448	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
449	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	<u>Nagpur Metro Rail Corporation Ltd</u>								
450	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	5,989.97	03/2018 -	12/2019	21	-
	Total		81,469.49 -	82,612.32	20,310.21				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
451	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	-
	Total		10,151.04 -	55,548.87	16,417.99				
	Grand Total		5,85,597.45	7,57,878.90	3,32,872.84				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	06/2019	12/2019	338.93	6
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	12/2020	219.91	9
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT	AAI	11/2016	04/2020	12/2020	233.38	8
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	08/2022	2467	6

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
10	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2021	413.84	24
11	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2020	258.56	48
12	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
13	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
14	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	48
15	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2020	302.96	120
16	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2021	510.85	60
17	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2022	457.77	108
18	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
19	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
20	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2021	479.53	96
22	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2020	209.78	60
23	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2022	172.08	144
24	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2020	426.79	24
25	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
26	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2022	706.4	116
27	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
28	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2021	163.51	120
29	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2021	264.68	108
30	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2021	162.46	84
31	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
32	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
33	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
34	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
35	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
36	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
37	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2022	479.15	36
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2020	337.66	12
39	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
40	AMERA OC RCE	SECL	02/2015	03/2018	03/2020	335.97	24
41	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	03/2020	289.45	70
42	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2019	269.82	67
43	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	09/2019	197.79	34

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
45	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	09/2019	363.99	16
46	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	09/2019	204.44	28
47	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	08/2019	293.65	27
48	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	09/2019	152.95	19
49	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	03/2020	355.15	12
50	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	10/2019	274.19	7
51	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	10/2019	272.19	7
52	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	10/2020	414.11	83

INFORMATION AND BROADCASTING

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	CPWD	11/2016	02/2019	11/2019	204.32	9

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
54	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
55	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
56	FIELD DEVELOPMENT OF NBP BLOCK KG-ONN-2003, NAGAYALANKA-KG	ONGC	04/2017	09/2018	09/2019	420.76	12
57	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
58	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	12/2019	6068.8	8
59	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
61	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	79
62	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	MANGALORE REFI	10/2015	03/2019	09/2019	135	6
63	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	07/2020	1810	7
64	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
65	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
66	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	12/2019	429	11
67	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	7
68	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	03/2021	163.02	11
69	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2020	906	8
70	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
71	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2020	4619.94	27
72	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2020	3190.69	25
73	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2020	160.1	8
74	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
75	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	09/2020	581	6
76	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	12/2019	2465.15	81
77	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	12/2019	352.56	33
78	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	07/2019	3150	22
79	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
80	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	58
81	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	11/2019	694	13
82	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
83	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	08/2019	327.78	16
84	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	10/2021	678	56
85	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2020	650.82	14
86	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
87	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	IOCL	07/2015	11/2018	08/2019	822.66	9
88	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497	26
89	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
90	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	24
91	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2020	808.63	26
92	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	09/2019	175.64	12
93	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	12/2019	445.89	10
94	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	12964.6	43
95	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	40
96	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
97	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	86
98	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	11638.55	26
99	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
100	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	40
101	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2019	374.63	44
102	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2020	522.29	40
103	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	12/2019	5151.37	21
105	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	14366.58	27
106	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
107	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	PGCIL	01/2015	03/2018	07/2019	268.8	16
108	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
109	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	08/2019	203.28	25
110	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	08/2019	197.4	17
111	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2019	1394.52	31
112	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	10/2019	195.42	68
113	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353	98
114	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	12/2023	8112.12	44
115	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	06/2020	9188.98	11
116	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	06/2020	12532.44	18
117	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	114
118	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	08/2019	2496.9	116
119	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657	76
120	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	63
121	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	08/2019	1779.29	129
122	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	118
123	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	11846	29
124	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	06/2021	10598.98	7
125	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	01/2020	454.11	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
126	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	PGCIL	07/2016	01/2019	07/2019	1429.38	6
127	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
128	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	08/2019	322.3	6
129	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	09/2019	408.46	8

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
130	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	03/2021	691.84	12
131	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288	9
132	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
133	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
134	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	06/2020	213	50
135	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
136	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
137	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
138	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
139	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
140	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
141	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229	15
142	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2021	1973	9
143	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
144	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	03/2026	16216	15
145	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	12
146	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
147	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
148	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	6
149	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
150	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	06/2023	5200	39
151	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
152	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
153	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
154	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2022	1491.47	33
155	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2022	1763.93	24
156	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
157	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
158	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
159	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
160	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
161	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
162	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
163	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
164	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
165	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
166	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.6	24
167	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
168	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	129
169	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
170	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	12
171	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
172	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	96
173	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
174	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2023	1160.48	156
175	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
176	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
177	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
178	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
179	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28
180	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	12
181	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
182	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
183	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
184	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
185	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	9
186	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
187	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
188	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
189	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287	111
190	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
191	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
192	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2132.77	120

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
193	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
194	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
195	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.5	12
196	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	204
197	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
198	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	96
199	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	147
200	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2023	2923.13	177
201	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	108
202	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
203	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
204	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
205	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2021	5300	84
206	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
207	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	12/2021	410.08	34
208	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140
209	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	06/2022	2500	235
210	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
211	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
212	MUNEERABAD-MAHABOOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2021	1723	252
213	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	8
214	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
215	TIRUCHIRAPPALI-NAGORE- KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2021	303.98	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
216	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2022	318.24	120
217	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	12
218	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
219	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
220	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2023	843.04	29
221	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
222	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	11/2019	148.77	35
223	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
224	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
225	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
226	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	02/2021	678.54	23
227	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	6
228	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
229	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
230	VIRANGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	03/2022	1037.15	12
231	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
232	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	10/2019	236.93	12
233	AJMER-BANGURGRAM	NWR	04/2011	11/2019	05/2020	213.39	6
234	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	12/2019	242.09	10
235	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2020	258.2	18
236	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
237	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	63
238	JAYNAGAR-BIJALPURA INCLUDING	ECR	04/2009	03/2020	03/2022	548	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC						
239	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	12/2021	569.63	21
240	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314	12
241	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
242	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2019	120.7	9
243	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
244	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
245	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
246	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
247	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2025	2361.74	36
248	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	28
249	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2022	1172.92	39
250	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2023	2063.03	24
251	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
252	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
253	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
254	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2020	493.17	24
255	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	12/2019	305	9
256	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2020	346.32	12
257	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	02/2020	174	11
258	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
259	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	16
260	TRANSMISSION LINE BETWEEN CHENNAI- HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
261	MADURAI - MANIYACHI - TUTICORIN (160	SR	02/2015	03/2020	06/2021	760	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM) DOUBLING						
262	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	12
263	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2020	3055	27
264	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	06/2021	700	12
265	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625	60

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
266	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	12/2019	186.96	63
267	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	PWD	11/2017	03/2018	11/2019	392.33	20
268	REHABILITATION AND UPGRADE OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	07/2019	445.89	28
269	PARLI PIMPLA DAHIGUDA	MORTH	02/2017	06/2019	06/2020	205.72	12
270	NAIGAONBANDI TO MANGRULPIR	MORTH	12/2017	03/2019	12/2019	244.04	9
271	TALEGAON TO GONAPUR	MORTH	01/2018	03/2019	12/2019	264.41	9
272	MALEWADA TO CHIMUR	MORTH	10/2016	06/2019	06/2020	322.55	12
273	PEN TO KHOPOLI	MORTH	03/2018	03/2018	12/2019	301.39	21
274	KOLHA TO NASRATPUR	MORTH	04/2016	04/2019	04/2020	281.78	12
275	BARASGAON TO RAHATEE	MORTH	07/2016	09/2018	04/2021	289.11	31
276	AKKALKOT TO DHUDHNI	MORTH	04/2016	02/2019	02/2020	211.42	12
277	NASHIK TO PETH	MORTH	12/2015	11/2018	11/2019	289.6	12
278	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	MORTH	08/2016	12/2017	12/2019	234.88	24
279	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	PWD	10/2016	02/2019	12/2019	298.32	10
280	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	PWD	10/2016	03/2019	12/2019	248.83	9
281	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	PWD	01/2017	05/2019	12/2019	300	7
282	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40	PWD	05/2014	08/2016	12/2020	199.98	52

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	OF NH-104 IN BIHAR UNDER EPC						
283	KHAMGAON TO SHEGAON	MORTH	02/2017	05/2019	12/2019	203.21	7
284	SHEGAON TO DEORI PHATA	MORTH	02/2017	05/2019	12/2019	373.1	7
285	DIGRAS DARWAH KARANJA	MORTH	01/2017	06/2019	06/2020	391.06	12
286	NANDGAON TO MORSHI	MORTH	01/2017	06/2019	12/2019	385.87	6
287	MORSHI TO ACHALPUR	MORTH	01/2017	06/2019	12/2019	341.16	6
288	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MORTH	02/2017	11/2017	11/2019	429.43	24
289	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MORTH	03/2018	08/2018	03/2020	228.32	19
290	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	MORTH	03/2018	08/2018	02/2020	244.95	18
291	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MORTH	03/2018	08/2018	02/2020	289.67	18
292	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	MORTH	03/2018	07/2018	01/2020	297.12	18
293	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	MORTH	03/2018	11/2018	05/2020	504.19	18
294	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 0	MORTH	03/2016	05/2016	03/2020	995.09	46
295	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	PWD	09/2016	09/2018	08/2019	178.23	11
296	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MORTH	01/2018	08/2018	02/2020	418.03	18
297	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	105
298	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	110
299	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	PWD	01/2013	02/2013	12/2019	182.28	82
300	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	116
301	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	05/2020	641.17	46
302	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
303	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	09/2020	1176.37	37
304	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	11/2020	476.56	40

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
305	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	11/2019	648.33	29
306	JUNAGADH BYPASS	NHAI	10/2017	10/2017	11/2019	232.49	25
307	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	01/2020	639.97	27
308	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	11/2020	964.17	37
309	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
310	4-LANNING OF OTTANCHATRAM BYPASS	NHAI	09/2017	09/2017	11/2019	244.27	26
311	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	08/2020	1227.87	35
312	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH	PWD	03/2015	10/2015	11/2019	271.45	49
313	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	NHIDCL	03/2015	05/2018	08/2019	194.11	15
314	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	03/2020	394	21
315	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	MORTH	12/2015	06/2018	07/2019	621.43	13
316	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	12/2019	255.75	27
317	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	08/2019	445.89	29
318	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	36
319	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	09/2019	164.54	49
320	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	PWD	03/2015	08/2017	02/2020	511.83	30
321	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	PWD	12/2011	11/2017	09/2019	159.39	22
322	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	12/2019	191.08	52
323	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	03/2020	954.43	54
324	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	08/2019	410.72	52
325	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	PWD	09/2012	10/2013	08/2019	511	70
326	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	08/2020	604	128
327	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	06/2020	702.16	71

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
328	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	03/2020	486	118
329	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108	100
330	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2019	617	88
331	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	07/2019	1724.55	76
332	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	12/2019	1266.6	39
333	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
334	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	10/2019	1535	65
335	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
336	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2019	1078.84	76
337	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2020	998.79	82
338	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2019	1396.18	63
339	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	07/2019	972.5	24
340	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	05/2020	923.04	42
341	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
342	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	03/2020	1388	19
343	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	08/2019	199.81	124
344	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	PWD	04/2013	08/2013	12/2019	151.59	76
345	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	09/2019	245	138
346	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	08/2019	217.61	112
347	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2019	208	140
348	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	10/2019	225	136
349	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	12/2019	946	18
350	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	02/2020	478.51	76

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
351	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2020	942.69	69
352	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	12/2019	709	27
353	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	08/2019	1387.11	21
354	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	08/2019	563.92	20
355	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	06/2020	414.51	25
356	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2020	531.13	25
357	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	12/2020	593.26	31
358	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	04/2021	649.5	25
359	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	08/2019	602.95	38
360	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	07/2019	574.28	12
361	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	05/2020	505	24
362	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	12/2019	1083	18
363	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
364	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	07/2019	1423.96	8
365	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	10/2019	2136.97	10
366	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	10/2019	596.67	17
367	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
368	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	24
369	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	03/2020	726.67	23
370	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	09/2019	479.2	16
371	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6
372	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	11/2020	701.4	20
373	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	11/2018	12/2019	229.37	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
374	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
375	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2020	707.82	19
376	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	05/2020	641.17	22
377	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2020	546	17
378	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2020	591.66	17
379	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	01/2020	804.97	19
380	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	01/2020	323.72	17
381	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	06/2020	1167.42	15
382	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
383	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	NHAI	08/2016	05/2019	11/2019	248.97	6
384	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	NHIDCL	04/2016	10/2016	10/2019	198	36
385	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	NHAI	09/2016	08/2018	09/2019	767.03	13
386	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16
387	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	02/2021	400.25	23
388	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	11/2019	446.17	8
389	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	19
390	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	MORTH	03/2014	05/2016	12/2019	191.5	43
391	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	MORTH	08/2013	06/2016	11/2019	171.96	41
392	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
393	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
394	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
395	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
396	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
397	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
398	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
399	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	02/2021	168.32	46
400	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
401	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	02/2021	216.71	46
402	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46
403	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
404	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
405	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
406	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
407	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	PWD	01/2017	03/2017	06/2020	205.05	39
408	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	07/2019	279.7	23
409	UPGRADATION OF PAWAT-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	214.69	20
410	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	217.22	22
411	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	233.04	20
412	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	PWD	11/2017	07/2018	01/2020	249.05	18
413	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	254.17	21
414	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	PWD	02/2018	03/2018	04/2020	279.44	25
415	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	PWD	09/2016	01/2019	11/2019	287.34	10
416	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MORTH	06/2017	06/2019	12/2019	282.08	6
417	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
418	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	PWD	03/2018	03/2018	12/2019	162.56	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
419	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	166.21	22
420	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	PWD	03/2016	11/2018	11/2019	271.17	12
421	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	PWD	02/2018	03/2018	07/2020	169.63	28
422	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	PWD	11/2017	02/2018	11/2019	235.91	21
423	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	184.62	21
424	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	PWD	03/2016	08/2019	08/2021	160.27	24
425	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	PWD	06/2016	08/2019	08/2021	236.78	24
426	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	PWD	01/2017	09/2019	05/2020	373.82	8
427	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	PWD	01/2016	07/2018	02/2020	809.16	19
428	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	PWD	01/2017	03/2019	09/2019	247.25	6
429	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	MORTH	10/2015	12/2015	12/2019	333.21	48
430	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	MORTH	09/2016	02/2017	09/2019	372.68	31
431	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	MORTH	11/2016	01/2018	01/2020	378.24	24
432	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MORTH	11/2016	05/2017	11/2019	290.15	30
433	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MORTH	01/2017	08/2017	03/2020	319.28	31
434	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MORTH	08/2016	01/2017	12/2019	350.61	35
435	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	MORTH	01/2016	05/2016	08/2019	386.09	39
436	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	MORTH	03/2016	09/2016	12/2019	444.84	39
437	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MORTH	01/2016	08/2016	12/2019	348.95	40
438	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MORTH	11/2016	08/2017	08/2019	376.25	24
439	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MORTH	01/2017	09/2017	09/2019	263.45	24
440	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2	MORTH	08/2016	07/2017	07/2019	574.19	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
441	REHABILITATION AND UPGRADE OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MORTH	01/2017	01/2018	01/2020	576.48	24
442	WADI TO ASOLA	MORTH	01/2017	09/2019	09/2020	363.82	12
443	NAGAJ TO VAIJAPUR	MORTH	01/2017	06/2019	12/2019	376.72	6
444	MANGAON TO DIGHI PORT	MORTH	01/2017	07/2019	07/2020	457.52	12
445	WAKAN PALI KHOPOLI	MORTH	01/2017	05/2019	05/2020	376.19	12
446	DEORI TO AMGAON	MORTH	01/2017	05/2019	05/2020	409.62	12
447	KARAD TO TAGAON	MORTH	01/2017	06/2019	06/2020	537.81	12
448	KARAD PATAN CHIPLUN GUHAGAR	MORTH	02/2017	06/2019	06/2020	407.19	12
449	TAKARKHED TO JALNA	MORTH	09/2017	06/2019	12/2019	417.9	6
450	REHABILITATION AND UPGRADE OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	PWD	10/2016	10/2018	07/2019	176.94	9
451	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	PWD	05/2013	08/2015	07/2019	164.54	47
452	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	PWD	11/2010	02/2014	12/2019	197.37	70
453	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	PWD	02/2017	05/2019	05/2021	157.32	24
454	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	PWD	01/2017	08/2017	08/2019	291.49	24
455	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	PWD	05/2018	05/2018	05/2020	171.6	24

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
456	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
457	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	10/2019	320.66	14
458	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	15525	62
459	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	11/2019	3127.3	19
460	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
461	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2019	1154.18	23
462	FORGED WHEEL PLANT	RINL	04/2014	09/2018	09/2019	1682.85	12
463	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2019	2858	22
464	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
465	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
466	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	BSNL	01/2018	10/2018	09/2019	231.8	11

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
467	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	CPWD	01/2019	06/2021	03/2022	790.79	9
468	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
469	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2020	216.69	67
470	NSG AT KOLKATA	CPWD	10/2014	04/2018	07/2019	162.88	15
471	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
472	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
473	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2020	197.33	14
474	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	09/2019	388	28
475	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	10/2019	156.57	38
476	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2019	270.83	59
477	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2020	171.86	54
478	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	17
479	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2020	165.23	89

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
480	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
481	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
482	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
483	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	02/2020	294	10
484	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2020	496.18	40
485	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
486	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
487	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	01/2021	430	8
488	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	07/2020	10773	19

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
489	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	10151.04	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7080.41	1173.3
7	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
8	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
9	BHANEAGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	345.92	142.98
13	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
14	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	4006.83	4475.92	469.09
15	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	3049.47	134.47
16	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
17	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
18	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	694	1097.54	403.54
20	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
21	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
22	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	682.9	138.99
23	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1683.06	821.27
24	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
25	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9997.11	6077.52
27	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	12865.92	1227.37
28	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
30	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
31	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6880.36	1769.03
32	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9072.36	4317.94
33	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
34	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7419.34	4922.44
36	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4397.8	1906.22
37	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
38	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
39	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	9996.59	4643.59
40	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1592.34	210.5

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15164.05	797.47
42	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13740.53	1208.09
43	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
44	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
45	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
46	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
48	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
49	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	5024.35	3367.35
50	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
51	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
52	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3376	2342.93
53	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
54	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
55	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
56	HATHUA-BHATNI (N L) (NER)	NER	04/2005	12/2022	230.03	770.08	540.05
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	749	271.12
59	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.77	1538.12
60	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5021.45	2627.98
61	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
62	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
63	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
64	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
65	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
66	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
67	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
68	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
69	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	800	463.09
70	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
71	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	694	407
72	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
73	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
74	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
75	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4079.15	1996.4
76	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
77	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
78	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
79	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
80	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
81	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
82	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
83	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	410.08	886.41	476.33
84	SAKRI-NIRMALI AND JHANJHARPUR-	ECR	04/2004	N.A.	372.14	1470.5	1098.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)						
85	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
86	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
87	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	2614.36	2235.8
88	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	729.92	404.92
89	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
90	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
91	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	ECR	04/2008	N.A.	445.25	2860.55	2415.3
92	NAWADA-LAXMIPUR (NL)	ECR	04/2008	N.A.	620.57	2626.98	2006.41
93	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	809.07	257.56
94	KADUR CHIKMAGALUR SAKLIESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
95	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
96	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	860.92	631.92
97	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
98	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	727.29	546.47
99	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
100	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
101	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
102	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
103	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
104	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
105	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
106	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1300.44	714.51
108	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
109	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
110	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
111	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1500	551.96
112	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	1950	1236.52
113	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1200	272.99
114	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
115	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
116	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	2136.01	1265.05
117	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
118	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	2499.71	3382.95	883.24
119	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
120	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
121	KONDAPALLI-KOTHAGUDEM	SCR	04/2013	N.A.	723	997.09	274.09
122	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
123	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
124	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
125	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
126	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
127	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	471.81	210.43
128	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
129	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
131	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3
132	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
133	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	728	414
134	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
135	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
136	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
137	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
138	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
139	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
140	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
141	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
142	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
143	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
144	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
145	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2300	1776.48
146	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
147	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2496.67	698.67
148	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	400.17	187.16
149	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	785.87	237.87
150	ARA-BHABHUA ROAD (NL)	ECR	04/2008	N.A.	633.87	2396.88	1763.01
151	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
152	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
154	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	410	167.91
155	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
156	AJMER-KOTA (NASIRABAD- JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
157	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
158	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
159	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	3000	673.48
160	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
161	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
162	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
163	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12524	8069.83
164	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3798.8	875.67
165	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	1180.19	3300	2119.81
166	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA- JAIN	NFR	02/1999	04/2010	380.6	1300	919.4
167	JALANDHAR-PATHANKOT- JAMMU TAWI	NR	03/2002	03/2016	625	855	230
168	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
169	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
170	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
171	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
172	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
173	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
174	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
175	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1310.23	480.49

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
176	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	980	676.02
177	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
178	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756	1244.14
179	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
181	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
183	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2010	1560
184	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	589.15	426.28
185	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1156.41	831.68
186	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
187	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
188	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
189	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773
190	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
191	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	1352.74	648.43
192	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	305	120.94
193	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
194	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	693.8	151.62
195	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
196	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	3860.4	356.71
197	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
198	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	346	226

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
199	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
200	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
201	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
202	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
203	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
204	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
205	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
206	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	PWD	03/2012	05/2012	207.03	389.45	182.42
207	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
208	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	186.96	305.61	118.65
209	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653	207.11
210	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	PWD	03/2009	09/2013	501	671.54	170.54
211	NAGAUR-BIKANER OF NH-11 (2L+PS) UNDER PPP.	PWD	01/2012	01/2014	378.07	478.73	100.66
212	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	279.7	398.52	118.82
213	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	PWD	08/2014	11/2017	823.2	937.76	114.56
214	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	PWD	08/2014	11/2017	600.87	720.97	120.1
215	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
216	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
217	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
218	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
219	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
220	SIX LANNING OF RANASTALAM-ANANDAPURAM	NHAI	03/2017	03/2020	1041.62	1187.1	145.48

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	SECTION OF NH-16 FROM KM 634.000 TO KM 681.000						
221	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
222	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
223	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
224	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
225	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2525.8	1137.46
226	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
227	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
228	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	195.04	377.99	182.95
229	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	PWD	11/2010	02/2011	470.2	630.36	160.16
230	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	497.05	881.05	384
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	MORTH	01/1991	N.A.	675	780.77	105.77
232	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	445.89	653.29	207.4
233	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
234	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	193.69	327.92	134.23
235	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	624.41	992.67	368.26
236	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
237	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
238	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	23140	7615

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2019)

TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
241	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
242	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79
243	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
244	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
245	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
246	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	5687.79	506
247	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	388	488.28	100.28
WATER RESOURCES							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
248	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	1,2320.00	1,7079.00	4759	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6840.00	3348	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	7080.41	1173.3	48
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144
8	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
10	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	4475.92	469.09	7
11	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497.00	6025.00	1528	26
12	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	723.40	413.59	58
13	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	11/2019	694.00	1097.54	403.54	13
14	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT	BPCL	11/2014	08/2018	11/2019	4588.29	5245.96	657.67	15

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	KOCHI REFINERY								
15	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	3049.47	134.47	110
16	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	345.92	142.98	70
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	1683.06	821.27	79

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
18	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	6880.36	1769.03	24
19	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	1,1846.00	1,2739.82	893.82	29
20	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	2,1312.11	12619.1	118
21	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9072.36	4317.94	12
22	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	08/2019	1779.29	2187.32	408.03	129
23	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	4397.80	1906.22	114
24	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	5071.94	247.82	86
25	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	1,1638.55	1,2865.92	1227.37	26
26	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,4719.10	3588.91	103
27	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	1891.41	526.89	40
28	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	5867.38	2888.9	93
29	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	06/2020	1,2532.44	1,3740.53	1208.09	18
30	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	1,4366.58	1,5164.05	797.47	27

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	1592.34	210.5	29
32	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353.00	9996.59	4643.59	98
33	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	1,2964.60	1,7304.00	4339.4	43
34	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	1,2176.28	2425.39	40
35	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9997.11	6077.52	147
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	08/2019	2496.90	7419.34	4922.44	116
37	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657.00	5024.35	3367.35	76
38	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	639.46	151.97	63

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
39	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625.00	855.00	230	60
40	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288.00	4970.11	2682.11	9
41	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
42	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	809.07	257.56	12
43	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229.00	860.92	631.92	15
44	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
45	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	810.02	108.41	28
46	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1200.00	272.99	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	1500.00	551.96	12
48	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	1120.00	177.05	24
49	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	1247.64	665.51	6
50	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
51	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	1300.44	714.51	16
52	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760.00	1182.31	422.31	15
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	1,2524.00	8069.83	108
54	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
55	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
56	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	3000.00	673.48	79
57	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
58	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	12/2021	410.08	886.41	476.33	34
59	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450.00	2010.00	1560	140
60	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	06/2022	2500.00	2,7949.00	25449	235
61	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
62	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
63	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
65	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
66	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
67	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
68	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	385.00	251.59	129
69	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	1928.07	1117.29	21
70	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	2072.50	1347.81	12
71	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	5021.45	2627.98	96
72	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	749.00	271.12	96
73	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	3860.40	356.71	12
74	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
75	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	305.00	120.94	9
76	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12
77	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287.00	694.00	407	111
78	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.50	3712.50	1441	12
79	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	2980.41	2484.97	204
80	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
81	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1156.41	831.68	96
82	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	3300.00	2119.81	147
83	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2023	2923.13	3798.80	875.67	177
84	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
85	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	1756.00	1244.14	8
86	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2021	303.98	980.00	676.02	12
87	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	1310.23	480.49	12
88	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
89	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	11/2019	148.77	377.00	228.23	35
90	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
91	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
92	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	12/2019	242.09	410.00	167.91	10
93	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2020	258.20	358.68	100.48	18
94	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548.00	785.87	237.87	24
95	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314.00	728.00	414	12
96	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
97	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2019	120.70	1800.00	1679.3	9
98	LAKSHMIKANTAPUR-NAMKHANA	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
99	SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
100	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
101	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
102	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	348.55	102.47	6
103	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
104	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
105	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	12/2019	186.96	305.61	118.65	63
106	REHABILITATION AND UPGRADEATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	07/2019	445.89	653.00	207.11	28
107	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	12/2019	1266.60	1544.00	277.4	39
108	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	992.67	368.26	105
109	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	327.92	134.23	110
110	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	377.99	182.95	116
111	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	08/2019	445.89	653.29	207.4	29
112	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	881.05	384	36
113	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108.00	2288.00	1180	100
114	MAIBANG TO LUMDING (AS-25),	NHAI	12/2003	04/2009	08/2019	199.81	385.13	185.32	124

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	KM.83.400 TO KM.111.000								
115	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	746.43	299.14	24
116	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	1420.00	131.93	12
117	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	722.46	116.62	19
118	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	07/2019	279.70	398.52	118.82	23

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
119	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	1,5525.00	2,3140.00	7615	62

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
120	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
121	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
122	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	09/2019	388.00	488.28	100.28	28
123	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	1592.00	372.79	17
124	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	5687.79	506	29

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
125	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	1,0151.04	5,5548.87	45397.8	15

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs.150 Crore and above								
					Date of Commissioning (Month/Year)		(July 2019)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	-	.00	0
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	-	.00	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2020	.00	118
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	-	.00	0
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	-	.00	0
10	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
11	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
12	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	-	.00	0
13	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	08/2020	.00	128
14	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2019	.00	88
15	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
16	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	-	.00	0
18	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16	702.16	07/2014	06/2020	.00	71
19	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	12/2019	.00	81
20	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	11/2019	.00	5
21	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	-	.00	0
22	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	05/2020	.00	42
23	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	-	.00	0
24	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	07/2019	.00	24
25	4-LANING OF BRAHMAPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	06/2020	.00	82
26	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00	1,046.00	09/2013	-	.00	0
27	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	-	.00	0
28	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	12/2019	.00	76
29	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	-	.00	0
30	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	-	.00	0
31	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	-	.00	0
32	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	-	.00	0
33	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	-	.00	0
34	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	03/2020	.00	19
35	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	12/2019	.00	63
36	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0
37	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0
39	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	10/2019	.00	65
40	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	12/2019	21.90	39
41	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
42	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	06/2019	.00	5
43	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
44	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
45	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	-	.00	0
46	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	06/2019	.00	0
47	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
48	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
49	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	07/2019	.00	76
50	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
51	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	-	.00	0
52	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
53	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	-	.00	0
54	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
55	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	-	.00	0
56	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,159.00	06/2015	-	.00	0
57	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	03/2020	106.50	100
58	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	05/2019	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above

(July 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
60	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	12/2019	.00	69
61	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73	0
	Total		73,759.12 -	76,780.07				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
62	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88	0
	<u>Mumbai Port Trust</u>							
63	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	-	82.72	0
	Total		610.89 -	945.44				
	Grand Total		74,370.01	77,725.51				

State-Wise Central sector Project Detail's

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above					(As on 31.07.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	21.11 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [7/2019]	401.00 (401.00) [401.00]	82.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	142.03 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	17.23 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	17.40 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
10	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [2/2020]	601.02 (-) [601.02]	85.04 (0.00) [-]
11	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [10/2019]	272.19 (-) [272.19]	140.58 (0.00) [7]
	<u>Information And Broadcasting</u>				
12	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	2/2019 (-) [11/2019]	204.32 (-) [204.32]	0.00 (0.00) [9]
	<u>Petroleum</u>				
13	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
14	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-)	466.00 (-)	77.27 (0.00)

			[7/2021]	[466.00]	[3]
15	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2020]	384.58 (-) [384.58]	81.56 (0.00) [-12]
16	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [2/2021]	580.20 (-) [580.20]	33.91 (0.00) [0]
17	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (9/2019) [9/2019]	420.76 (-) [407.45]	224.89 (-13.31) [12]
18	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (-) [8/2021]	34,012.00 (-) [34,012.00]	3,011.57 (0.00) [14]
19	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	14.07 (0.00) [10]
20	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
21	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	14.78 (0.00) [0]
22	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	5,541.02 (0.00) [0]
23	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	375.09 (0.00) [0]
	<u>Railways</u>				
24	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
25	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
26	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
27	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (-) [3,631.00]	407.42 (0.00) [12]
28	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (-) [2,120.16]	412.87 (1,074.96) [168]
29	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (-) [3,382.95]	325.64 (883.24) [0]
30	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	7.38 (0.50) [21]
31	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
32	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,288.70]	667.03 (0.00) [36]
33	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
34	VIJAYAWADA-GUDUR	4/2015	12/2023 (-)	3,246.26 (-)	837.66 (302.41)

			[12/2023]	[3,548.67]	[0]
35	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	1,331.60 (0.00) [24]
	Road Transport And Highways				
36	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [11/2019]	328.67 (-) [328.67]	176.29 (0.00) [-]
37	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	70.71 (0.00) [0]
38	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [3/2020]	557.30 (-) [557.30]	33.63 (0.00) [-]
39	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (3/2020) [9/2019]	263.45 (-) [263.45]	43.79 (0.00) [24]
40	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (3/2020) [11/2019]	429.43 (-) [429.43]	181.17 (0.00) [24]
41	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [12/2020]	314.43 (-) [314.43]	24.90 (0.00) [-]
42	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (12/2019) [12/2019]	350.61 (-) [350.61]	301.70 (0.00) [35]
43	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
44	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]
45	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
46	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (12/2019) [12/2019]	333.21 (-) [333.21]	256.29 (0.00) [48]
47	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [4/2021]	1,532.62 (-) [1,532.62]	0.00 (0.00) [1]
48	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [11/2019]	648.33 (-) [648.33]	20.54 (0.00) [29]
49	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	21.73 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (1/2020) [1/2020]	576.48 (-) [576.48]	177.36 (0.00) [24]
51	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (12/2019) [12/2019]	348.95 (-) [348.95]	144.95 (0.00) [40]
52	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [2/2017]	251.55 (-) [251.55]	7.74 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (8/2019) [8/2019]	386.09 (-) [386.09]	160.20 (0.00) [39]
54	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO	8/2016	7/2017 (7/2019)	574.19 (-)	456.98 (0.00)

	254.500 OF NH214A(NH2		[7/2019]	[574.19]	[24]
55	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (11/2019) [11/2019]	290.15 (-) [290.15]	69.42 (0.00) [30]
56	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
57	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	0.00 (0.00) [-]
58	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (3/2020) [3/2020]	995.09 (995.00) [995.09]	401.90 (0.00) [46]
59	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (12/2019) [12/2019]	444.84 (-) [444.84]	208.09 (0.00) [39]
60	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (3/2020) [8/2019]	376.25 (-) [376.25]	180.38 (0.00) [24]
61	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (1/2020) [1/2020]	297.12 (294.00) [297.12]	138.68 (0.00) [18]
62	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (2/2020) [2/2020]	289.67 (290.00) [289.67]	60.76 (0.00) [18]
63	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (5/2020) [5/2020]	504.19 (504.00) [504.19]	269.70 (0.00) [18]
64	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (11/2019) [11/2019]	271.45 (-) [271.45]	143.44 (0.00) [49]
65	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (3/2020) [3/2020]	319.28 (-) [319.28]	101.28 (0.00) [31]
66	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [11/2019]	648.32 (-) [503.10]	1.15 (-145.22) [-4]
67	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (2/2020) [2/2020]	244.95 (245.00) [244.95]	84.47 (0.00) [18]
68	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (9/2019) [9/2019]	372.68 (-) [372.68]	179.43 (0.00) [31]
69	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2020) [3/2020]	228.32 (-) [228.32]	26.78 (0.00) [19]
70	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (2/2020) [2/2020]	418.03 (-) [418.03]	103.64 (0.00) [18]
71	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (1/2020) [1/2020]	378.24 (-) [378.24]	187.63 (0.00) [24]
72	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [7/2021]	1,959.00 (-) [1,959.00]	44.43 (0.00) [-]
73	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [7/2021]	1,323.15 (-) [1,323.15]	30.00 (0.00) [-]
74	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [7/2021]	1,550.98 (-) [1,550.98]	0.00 (0.00) [-]

75	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [10/2019]	1,535.00 (-) [1,535.00]	3,220.15 (0.00) [65]
76	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	687.88 (145.48) [2]
77	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.52 (0.00) [0]
78	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
79	CENTRAL DISPATCH YARD	8/2015	8/2018 (10/2019) [10/2019]	320.66 (-) [320.66]	206.91 (0.00) [14]
80	COKE OVEN BATTERY-5	12/2011	12/2017 (10/2019) [10/2019]	2,858.00 (-) [2,500.00]	1,292.76 (-358.00) [22]
	<u>Urban Development</u>				
81	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [8/2019]	206.58 (-) [206.58]	82.23 (0.00) [5]
82	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
83	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [169.16]	163.98 (11.32) [0]
84	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>Water Resources</u>				
85	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (-) [6/2021]	10,151.04 (-) [55,548.87]	16,417.99 (45,397.83) [15]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
86	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (8/2019) [8/2019]	2,496.90 (7,419.34) [7,419.34]	7,494.35 (4,922.44) [116]
87	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,927.32 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
88	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	108.75 (0.00) [0]
89	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	240.21 (0.00) [21]
90	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	174.80 (0.00) [15]
91	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
92	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [0/0]	210.50 (-) [210.50]	114.37 (0.00) [0]
93	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM	1/2016	11/2016	183.65	90.29

	583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450		(-) [0/0]	(-) [183.65]	(0.00) [0]
94	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/	189.91	0.00
			(-) [0/0]	(-) [189.91]	(0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/	259.52	143.01
			(-) [0/0]	(-) [259.52]	(0.00) [0]
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/	200.44	72.97
			(-) [0/0]	(-) [200.44]	(0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/	568.92	125.96
			(-) [0/0]	(-) [568.92]	(0.00) [0]
98	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/	188.78	30.88
			(-) [0/0]	(-) [188.78]	(0.00) [0]
99	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017	138.93	17.42
			(-) [1/2020]	(155.00) [155.00]	(16.07) [36]
100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	98.37
			(-) [9/2020]	(-) [245.79]	(0.00) [-]
101	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016	198.00	195.67
			(-) [10/2019]	(-) [198.00]	(0.00) [36]
102	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018	197.16	66.17
			(9/2015) [9/2018]	(197.16) [197.16]	(0.00) [0]
103	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	154.14
			(-) [0/0]	(-) [1,718.59]	(0.00) [0]
104	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017	1,253.10	211.21
			(-) [3/2022]	(-) [1,253.10]	(0.00) [60]
105	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017	167.28	18.70
			(2/2018) [2/2021]	(167.28) [167.28]	(0.00) [46]
106	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017	216.71	15.77
			(2/2018) [2/2021]	(216.71) [216.71]	(0.00) [46]
107	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
108	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	126.58
			(-) [12/2020]	(-) [434.06]	(0.00) [-]
109	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	46.85
			(3/2018) [3/2021]	(284.09) [284.09]	(0.00) [47]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	37.30
			(-) [0/0]	(-) [195.23]	(0.00) [0]
111	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	48.16
			(-) [0/0]	(-) [203.36]	(0.00) [0]
112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	56.15
			(-) [0/0]	(-) [194.66]	(0.00) [0]
113	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA)	1/2017	4/2017	198.22	24.14
			(-)	(-)	(0.00)

	TO KM.		[0/0]	[198.22]	[0]
114	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (389.45) [389.45]	275.19 (182.42) [0]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	13.73 (0.00) [46]
116	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	28.67 (0.00) [46]
117	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
118	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
119	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
120	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	0.00 (0.00) [-]
121	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	0.00 (0.00) [-]
122	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	9.65 (0.00) [-]
123	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	6.19 (0.00) [-]
	ASSAM				
	Civil Aviation				
124	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	Health And Family Welfare				
125	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
126	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	Petroleum				
127	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
128	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	178.05 (0.00) [0]
129	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	531.40 (0.00) [0]
130	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	3.30 (0.00) [0]
131	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
132	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-)	202.94 (345.92)	145.60 (142.98)

			[11/2019]	[345.92]	[70]
133	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	250.31 (0.00) [1]
134	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [682.90]	7.60 (138.99) [0]
135	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,526.40 (0.00) [0]
136	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	157.02 (15.64) [0]
137	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
138	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	691.97 (414.00) [12]
139	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	582.27 (-50.32) [-24]
140	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	455.80 (1,265.05) [0]
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	606.82 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
142	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	201.56 (0.00) [0]
143	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
144	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
145	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	61.74 (0.00) [0]
146	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	50.39 (0.00) [0]
147	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	356.31 (0.00) [0]
148	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	15.27 (0.00) [0]
149	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
150	453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	6.27 (0.00) [0]
151	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	48.09 (0.00) [0]
152	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010	217.61	451.15

			(-) [8/2019]	(-) [217.61]	(0.00) [112]
153	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
154	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.68 (7.98) [0]
155	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	304.28 (0.00) [0]
156	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	61.74 (0.00) [0]
157	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	54.31 (0.00) [-]
158	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	6.62 (0.00) [0]
159	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	292.24 (0.00) [0]
160	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	120.86 (0.00) [0]
161	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [280.00]	472.00 (0.00) [0]
162	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
163	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
164	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [8/2019]	199.81 (-) [385.13]	319.96 (185.32) [124]
165	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [167.64]	268.94 (0.00) [0]
166	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2019]	208.00 (-) [230.00]	337.08 (22.00) [140]
167	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	326.35 (0.00) [136]
168	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [9/2019]	245.00 (-) [174.34]	224.28 (-70.66) [138]
169	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (307.47) [307.47]	239.76 (89.16) [0]
170	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
171	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	539.20 (-) [539.20]	25.64 (0.00) [0]

	<u>Petroleum</u>				
172	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	594.01 (0.00) [-10]
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	61.78 (0.00) [0]
174	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	142.12 (0.00) [0]
175	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	9.49 (0.00) [0]
176	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [8/2019]	822.66 (-) [822.66]	822.02 (0.00) [9]
177	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (-) [10/2019]	951.64 (-) [951.64]	325.42 (0.00) [0]
178	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	7.82 (0.00) [0]
179	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	8.19 (0.00) [0]
180	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [3/2020]	324.00 (-) [324.00]	149.98 (0.00) [-3]
	<u>Power</u>				
181	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (8/2021) [8/2021]	8,692.97 (21,312.11) [21,312.11]	16,249.55 (12,619.14) [118]
182	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (-) [9/2020]	5,353.00 (-) [9,996.59]	7,840.42 (4,643.59) [98]
183	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	564.81 (0.00) [0]
184	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (12/2021) [12/2021]	12,964.60 (17,304.00) [17,304.00]	13,670.00 (4,339.40) [43]
	<u>Railways</u>				
185	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [3/2023]	633.87 (-) [2,396.88]	0.40 (1,763.01) [-]
186	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (-) [1,605.17]	23.40 (0.00) [-]
187	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	1.91 (2,668.81) [-]
188	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	378.56 (-) [2,614.36]	375.63 (2,235.80) [-]
189	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR	7/2004	12/2007 (-) [0/0]	599.63 (674.00) [674.00]	0.00 (74.37) [0]
190	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12)	8/2010	3/2014 (-) [0/0]	400.00 (-) [400.00]	0.00 (0.00) [0]
191	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/	406.92	200.00

			(-) [0/0]	(-) [339.00]	(-67.92) [0]
192	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-) [3/2024]	(-) [205.00]	(0.00) [-]
193	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/	329.39	815.41
			(-) [12/2021]	(-) [1,483.14]	(1,153.75) [-]
194	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	1.14
			(-) [3/2024]	(-) [2,860.55]	(2,415.30) [-]
195	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	378.41
			(-) [1/2020]	(-) [400.17]	(187.16) [-]
196	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	1,403.38
			(-) [3/2023]	(-) [2,066.77]	(1,538.12) [-]
197	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	1,028.71
			(-) [3/2020]	(-) [1,156.41]	(831.68) [96]
198	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	457.46
			(-) [3/2022]	(-) [785.87]	(237.87) [24]
199	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	303.96
			(-) [3/2022]	(-) [589.15]	(426.28) [-]
200	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.67
			(3/2022) [3/2022]	(-) [360.00]	(26.24) [-]
201	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	390.91
			(-) [10/2021]	(1,200.20) [1,200.20]	(0.00) [19]
202	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	389.29
			(-) [3/2020]	(-) [516.02]	(16.61) [0]
203	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.39
			(-) [3/2024]	(-) [192.56]	(0.00) [-]
204	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	672.82
			(-) [3/2020]	(283.95) [749.00]	(271.12) [96]
205	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	24.16
			(-) [3/2024]	(-) [926.09]	(715.09) [-]
206	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	4/2016	3/2021	731.64	15.39
			(-) [3/2022]	(-) [1,185.73]	(454.09) [12]
207	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.60
			(-) [3/2024]	(-) [281.30]	(0.00) [-]
208	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.53
			(-) [3/2024]	(-) [228.05]	(0.00) [-]
209	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	541.07
			(-) [0/0]	(-) [559.91]	(227.76) [0]
210	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.28
			(-) [3/2024]	(-) [2,626.98]	(2,006.41) [-]
211	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	932.80
			(-)	(2,145.00)	(1,612.13)

			[3/2020]	[2,145.00]	[12]
212	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (-) [9/2019]	180.82 (-) [727.29]	488.81 (546.47) [-]
213	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [12/2022]	1,491.47 (-) [1,491.47]	424.98 (0.00) [33]
214	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [3/2022]	744.04 (-) [1,215.54]	35.10 (471.50) [12]
215	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (-) [729.92]	349.60 (404.92) [-]
216	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2021]	372.14 (1,470.50) [1,470.50]	356.81 (1,098.36) [-]
217	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [2/2023]	380.00 (519.33) [519.33]	126.80 (139.33) [-]
218	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [3/2024]	678.62 (-) [2,393.23]	17.20 (1,714.61) [-]
	<u>Road Transport And Highways</u>				
219	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013 (-) [0/0]	351.54 (-) [351.54]	329.40 (0.00) [0]
220	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [0/0]	511.54 (-) [511.54]	566.60 (0.00) [0]
221	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
222	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [0/0]	575.00 (-) [575.00]	843.67 (0.00) [0]
223	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	77.43 (0.00) [0]
224	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	0.00 (0.00) [0]
225	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015 (-) [0/0]	288.24 (-) [288.24]	280.00 (0.00) [0]
226	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (-) [0/0]	2,598.00 (-) [2,598.00]	0.00 (0.00) [0]
227	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	0.00 (-7.71) [14]
228	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [496.20]	0.00 (0.00) [0]
229	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [683.83]	596.44 (0.00) [0]
230	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
231	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -	2/2016	5/2016 (-)	553.30 (-)	267.22 (0.00)

	LANE WITH P		[0/0]	[553.30]	[0]
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	93.11 (0.00) [0]
233	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	113.26 (0.00) [-]
234	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [10/2020]	642.41 (-) [642.41]	131.71 (0.00) [-]
235	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [4/2020]	322.09 (-) [322.09]	77.53 (0.00) [24]
236	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	753.03 (0.00) [0]
237	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [814.04]	384.48 (0.00) [-]
238	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
239	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	214.34 (0.00) [0]
240	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
241	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	885.47 (0.00) [0]
242	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	719.20 (0.00) [0]
243	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
244	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
245	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	113.67 (50.09) [0]
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
248	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	278.45 (39.60) [0]
249	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	323.60 (19.42) [0]
250	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [780.77]	152.37 (105.77) [0]
251	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]

252	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
253	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	102.51 (0.00) [54]
254	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	2.06 (0.00) [0]
255	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
256	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [10/2019]	399.54 (-) [399.54]	195.59 (0.00) [6]
257	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [854.80]	579.78 (0.00) [0]
258	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [516.13]	417.09 (0.00) [0]
259	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
260	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	153.43 (0.00) [52]
261	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [10/2019]	230.34 (-) [230.34]	178.39 (0.00) [0]
	<u>Urban Development</u>				
262	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [10/2020]	496.18 (496.00) [498.99]	69.60 (2.81) [40]
263	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
264	AMERA OC RCE	2/2015	3/2018 (-) [3/2020]	335.97 (-) [335.97]	51.25 (0.00) [24]
265	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	67.41 (0.00) [0]
266	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016 (-) [0/0]	198.59 (-) [198.59]	169.15 (0.00) [0]
267	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2020]	258.56 (-) [258.56]	177.65 (0.00) [48]
268	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	82.76 (0.00) [0]
269	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	92.47 (0.00) [0]
270	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	4.02 (0.00) [0]
271	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023	11,816.40	2,879.89

			(-) [3/2023]	(-) [11,816.40]	(0.00) [0]
272	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (-) [3/2020]	152.43 (-) [459.49]	191.40 (307.06) [60]
273	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
274	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	2.88 (0.00) [72]
275	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,043.87 (0.00) [0]
276	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
277	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
278	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	192.68 (0.00) [84]
279	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.42 (0.00) [0]
280	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
281	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [0/0]	300.00 (-) [300.00]	1.09 (0.00) [0]
	<u>Power</u>				
282	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (3/2020) [3/2020]	11,846.00 (-) [12,739.82]	12,229.51 (893.82) [29]
283	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,610.00 (0.00) [0]
	<u>Railways</u>				
284	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (10/2019) [10/2019]	872.00 (1,226.51) [1,226.51]	1,039.54 (354.51) [-2]
285	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [3/2020]	393.98 (-) [393.98]	241.23 (0.00) [0]
286	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (12/2022) [12/2022]	2,288.00 (-) [4,970.11]	619.50 (2,682.11) [9]
287	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2021) [12/2021]	1,973.00 (1,973.66) [1,973.66]	129.54 (0.66) [9]
288	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (12/2020) [12/2020]	3,055.00 (-) [3,055.00]	1,729.64 (0.00) [27]
289	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2023]	1,160.00 (-) [1,160.83]	654.74 (0.83) [36]
290	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-)	207.00 (-)	153.83 (0.00)

			[0/0]	[207.00]	[0]
291	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [6/2020]	1,402.02 (-) [1,100.00]	1,016.52 (-302.02) [3]
	<u>Road Transport And Highways</u>				
292	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (3/2021) [3/2021]	1,029.96 (-) [1,261.05]	0.00 (231.09) [-]
293	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (3/2020) [3/2020]	726.67 (598.13) [598.13]	394.83 (-128.54) [23]
294	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (8/2018) [8/2018]	509.13 (-) [509.13]	412.66 (0.00) [0]
295	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (10/2019) [10/2019]	596.67 (-) [596.67]	387.97 (0.00) [17]
296	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	178.85 (0.00) [0]
297	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	447.70 (0.00) [0]
	<u>Steel</u>				
298	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2020) [7/2020]	15,525.00 (-) [23,140.00]	15,811.82 (7,615.00) [62]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
299	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,783.74 (-243.77) [5]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
300	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [12/2020]	233.38 (-) [233.38]	84.73 (0.00) [8]
	<u>Health And Family Welfare</u>				
301	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [9/2019]	204.44 (-) [204.44]	188.00 (0.00) [28]
302	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [8/2019]	293.65 (-) [293.65]	290.71 (0.00) [27]
303	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [2/2020]	156.56 (-) [156.65]	54.94 (0.09) [-]
304	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [10/2020]	414.11 (-) [513.89]	147.00 (99.78) [83]
	<u>Heavy Industry</u>				
305	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [9/2019]	1,554.00 (-) [1,554.00]	335.03 (0.00) [0]
	<u>Power</u>				
306	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (6/2019) [12/2019]	1,394.52 (-) [1,394.52]	405.65 (0.00) [31]
	<u>Railways</u>				
307	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-)	295.68 (-)	79.53 (0.00)

			[3/2023]	[295.68]	[-]
308	GRADE SEPERATOR AT DAYABASTI	4/1999	/	156.65	107.86
			(-)	(-)	(40.52)
			[3/2024]	[197.17]	[-]
	<u>Road Transport And Highways</u>				
309	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/	771.18	261.77
			(-)	(-)	(6,786.82)
			[0/0]	[7,558.00]	[0]
	<u>Telecommunications</u>				
310	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017	418.26	367.03
			(-)	(-)	(0.00)
			[0/0]	[418.26]	[0]
	<u>Urban Development</u>				
311	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019	197.33	42.30
			(-)	(-)	(0.00)
			[6/2020]	[197.33]	[14]
312	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	/	218.72	0.00
			(-)	(-)	(0.00)
			[0/0]	[218.72]	[0]
313	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015	884.30	703.90
			(-)	(-)	(0.00)
			[0/0]	[884.30]	[0]
314	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019	271.90	33.56
			(-)	(-)	(0.00)
			[11/2019]	[271.90]	[0]
315	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019	188.00	146.45
			(-)	(-)	(0.00)
			[0/0]	[188.00]	[0]
316	DELHI MRTS PHASE-III	9/2011	3/2016	38,585.00	34,763.15
			(-)	(-)	(0.00)
			[0/0]	[38,585.00]	[0]
317	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	1,219.21	313.93
			(-)	(-)	(372.79)
			[3/2021]	[1,592.00]	[17]
318	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020	238.56	47.30
			(-)	(-)	(0.00)
			[5/2020]	[238.56]	[0]
319	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019	4,264.00	3,246.53
			(-)	(-)	(175.23)
			[11/2019]	[4,439.23]	[0]
320	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/	392.00	12.56
			(8/2020)	(-)	(0.00)
			[3/2021]	[392.00]	[-]
321	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/	422.00	10.36
			(-)	(-)	(0.00)
			[12/2020]	[422.00]	[-]
322	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/	2,694.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,694.00]	[0]
323	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018	248.20	23.00
			(-)	(-)	(0.00)
			[0/0]	[248.20]	[0]
	<u>GOA</u>				
	<u>Defence Production</u>				
324	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020	285.95	81.83
			(-)	(286.00)	(0.00)
			[8/2020]	[285.95]	[0]
325	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018	167.69	138.39
			(3/2019)	(168.00)	(0.00)
			[0/0]	[167.69]	[0]
	<u>Health And Family Welfare</u>				

326	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/	249.01	73.40
			(-)	(-)	(0.00)
			[5/2020]	[249.01]	[-]
	<u>Road Transport And Highways</u>				
327	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/	280.16	219.47
			(-)	(-)	(10.43)
			[0/0]	[290.59]	[0]
328	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/	184.05	91.39
			(-)	(-)	(0.00)
			[0/0]	[184.05]	[0]
329	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/	936.40	262.25
			(-)	(-)	(0.00)
			[0/0]	[936.40]	[0]
330	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/	298.33	153.33
			(-)	(-)	(0.00)
			[0/0]	[298.33]	[0]
331	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018	297.00	290.64
			(-)	(-)	(0.00)
			[0/0]	[297.00]	[0]
332	KARASWADA TO BAMBOLIM	3/2017	12/2019	852.67	108.04
			(-)	(852.67)	(0.00)
			[12/2019]	[852.67]	[0]
333	PATRADEVI TO KARASWADA 4L	3/2017	5/2020	634.32	108.33
			(-)	(634.32)	(0.00)
			[5/2020]	[634.32]	[0]
334	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/	773.98	259.46
			(-)	(-)	(0.00)
			[0/0]	[773.98]	[0]
335	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/	819.95	191.63
			(-)	(-)	(0.00)
			[0/0]	[819.95]	[0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
336	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11,459.00	13,838.00
			(-)	(16,580.00)	(5,121.00)
			[6/2020]	[16,580.00]	[54]
	<u>Petroleum</u>				
337	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/	588.20	0.94
			(-)	(-)	(0.00)
			[0/0]	[588.20]	[0]
338	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019	3,380.00	1,872.71
			(-)	(-)	(0.00)
			[9/2019]	[3,380.00]	[0]
339	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018	327.78	140.90
			(-)	(-)	(-127.78)
			[8/2019]	[200.00]	[16]
340	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020	1,342.00	6.30
			(-)	(-)	(0.00)
			[8/2020]	[1,342.00]	[0]
341	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020	906.00	85.08
			(-)	(-)	(0.00)
			[10/2020]	[906.00]	[8]
342	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK)	10/2018	3/2021	156.67	0.00
			(-)	(-)	(0.00)
			[3/2021]	[156.67]	[0]
343	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020	208.35	108.00
			(-)	(-)	(0.00)
			[7/2020]	[208.35]	[0]
344	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026	1,162.56	356.41
			(-)	(-)	(0.00)
			[3/2026]	[1,162.56]	[0]

345	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [2/2021]	225.54 (-) [225.54]	0.00 (0.00) [0]
	<u>Power</u>				
346	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [9/2019]	193.14 (-) [193.14]	72.38 (0.00) [3]
347	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (9/2019) [9/2019]	175.64 (-) [175.64]	92.78 (0.00) [12]
	<u>Railways</u>				
348	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	933.88 (106.70) [0]
349	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2021) [3/2021]	829.74 (1,215.34) [1,310.23]	1,363.06 (480.49) [12]
350	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (3/2017) [3/2017]	117.36 (196.95) [202.35]	404.70 (84.99) [0]
351	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (3/2020) [3/2020]	551.51 (809.07) [809.07]	616.90 (257.56) [12]
352	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2022) [3/2022]	318.24 (321.62) [321.62]	125.76 (3.38) [120]
353	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (3/2021) [3/2021]	691.84 (663.29) [663.29]	163.85 (-28.55) [12]
354	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	296.20 (0.00) [0]
355	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
356	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2021) [3/2021]	844.10 (844.10) [844.10]	92.69 (0.00) [-]
357	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	222.83 (0.00) [9]
358	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
359	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2021]	1,548.66 (-) [1,548.66]	1,176.15 (0.00) [0]
360	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2022) [3/2022]	320.66 (858.56) [858.96]	534.00 (538.30) [36]
361	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2021) [3/2021]	1,002.39 (1,002.39) [1,002.39]	374.60 (0.00) [0]
362	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (3/2022) [3/2022]	1,037.15 (1,037.15) [1,037.15]	992.18 (0.00) [12]
363	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	<u>Road Transport And Highways</u>				
364	2-LANE WITH PAVED SHOULDERS OF GADU-	12/2016	/	417.19	262.83

	PORBANDER SECTION		(-) [9/2019]	(-) [417.19]	(0.00) [-]
365	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/	829.97	75.08
			(-) [1/2020]	(-) [829.97]	(0.00) [-]
366	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020	1,958.88	1,116.85
			(-) [8/2020]	(-) [1,958.88]	(0.00) [2]
367	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015	2,125.24	4,659.71
			(-) [0/0]	(-) [2,125.24]	(0.00) [0]
368	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/	364.56	208.94
			(-) [12/2019]	(-) [364.56]	(0.00) [-]
369	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/	1,161.39	0.00
			(-) [0/0]	(-) [1,161.39]	(0.00) [0]
370	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/	1,437.64	0.00
			(-) [7/2021]	(-) [1,437.64]	(0.00) [-]
371	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/	2,702.05	0.00
			(-) [1/2021]	(-) [2,702.05]	(0.00) [-]
372	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019	400.76	4.45
			(-) [0/0]	(386.19) [400.76]	(0.00) [0]
373	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018	962.43	45.70
			(-) [0/0]	(887.21) [962.43]	(0.00) [0]
374	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018	867.97	90.63
			(-) [0/0]	(-) [867.97]	(0.00) [0]
375	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/	998.18	435.25
			(-) [8/2019]	(-) [998.18]	(0.00) [-]
376	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/	723.64	321.67
			(-) [9/2019]	(-) [723.64]	(0.00) [-]
377	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/	834.64	140.44
			(-) [10/2019]	(-) [834.64]	(0.00) [-]
378	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/	763.08	357.12
			(-) [8/2019]	(-) [763.08]	(0.00) [-]
379	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012	1,509.10	3,187.21
			(-) [0/0]	(-) [1,509.10]	(0.00) [0]
380	JUNAGADH BYPASS	10/2017	10/2017	232.49	0.00
			(-) [11/2019]	(-) [232.49]	(0.00) [25]
381	KANDLA - MUNDRA PORT	1/2011	7/2013	953.88	976.79
			(-) [0/0]	(-) [953.88]	(0.00) [0]
382	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/	1,052.21	1,080.00
			(-) [1/2021]	(-) [1,052.21]	(0.00) [-]
383	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/	1,251.11	1,084.26
			(-) [1/2021]	(-) [1,251.11]	(0.00) [-]
384	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG	5/2016	/	425.60	0.00
			(-)	(-)	(0.00)

	TERM REME		[0/0]	[425.60]	[0]
385	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [0/0]	464.07 (399.35) [464.07]	14.17 (0.00) [0]
386	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON	3/2016	2/2016 (-) [0/0]	208.34 (-) [208.34]	112.87 (0.00) [0]
387	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
388	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE	3/2016	2/2017 (-) [0/0]	223.67 (-) [223.67]	112.81 (0.00) [0]
	<u>Urban Development</u>				
389	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [7/2020]	10,773.00 (-) [10,773.00]	5,854.77 (0.00) [19]
390	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
391	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	100.17 (0.00) [0]
	<u>Health And Family Welfare</u>				
392	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [0/0]	505.58 (-) [523.00]	508.29 (17.42) [0]
	<u>Petroleum</u>				
393	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (-) [1/2021]	909.00 (-) [909.00]	13.11 (0.00) [0]
394	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [12/2019]	3,529.00 (-) [3,529.00]	1,562.10 (0.00) [5]
395	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	7.75 (0.00) [0]
396	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	63.55 (0.00) [0]
397	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (-) [2/2020]	598.00 (-) [598.00]	14.12 (0.00) [0]
398	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (-) [6/2021]	278.60 (-) [278.60]	0.00 (0.00) [0]
399	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	142.67 (0.00) [0]
400	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (9/2020) [9/2020]	286.42 (-) [286.42]	1.00 (0.00) [1]
	<u>Railways</u>				
401	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2020]	346.32 (-) [346.32]	286.56 (0.00) [12]
402	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [3/2021]	287.00 (-) [694.00]	220.42 (407.00) [111]

	Road Transport And Highways				
403	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [8/2019]	602.95 (-) [602.95]	417.86 (0.00) [38]
404	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [7/2019]	574.28 (-) [574.28]	448.92 (0.00) [12]
405	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [9/2019]	639.79 (-) [552.90]	480.73 (-86.89) [-6]
406	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [0/0]	2,128.72 (-) [2,128.72]	971.24 (0.00) [0]
407	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (7/2019) [7/2019]	276.01 (-) [276.01]	180.95 (0.00) [4]
408	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (3/2020) [9/2019]	247.25 (-) [247.25]	144.00 (0.00) [6]
409	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [11/2019]	248.97 (-) [248.97]	241.69 (0.00) [6]
410	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [0/0]	1,484.30 (-) [1,484.30]	0.00 (0.00) [0]
411	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [0/0]	1,004.67 (-) [1,004.67]	0.00 (0.00) [0]
412	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [118]
413	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
414	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
415	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [3/2020]	1,108.00 (-) [2,288.00]	3,978.72 (1,180.00) [100]
416	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [3/2020]	551.58 (-) [551.58]	0.00 (0.00) [-]
417	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [3/2020]	275.12 (-) [275.12]	0.00 (0.00) [-]
418	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI	3/2018	/ (-) [3/2020]	307.79 (-) [307.79]	0.00 (0.00) [-]
419	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [6/2020]	181.78 (-) [181.78]	0.00 (0.00) [-]
420	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [3/2020]	198.05 (-) [198.05]	0.00 (0.00) [-]
421	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [0/0]	795.50 (-) [795.50]	0.00 (0.00) [0]
422	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [0/0]	634.70 (-) [634.70]	0.00 (0.00) [0]

	HIMACHAL PRADESH				
	<u>Petroleum</u>				
423	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019 (-) [6/2019]	151.00 (-) [151.00]	147.35 (0.00) [0]
	<u>Power</u>				
424	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2021]	3,919.59 (-) [9,997.11]	7,522.82 (6,077.52) [147]
	<u>Railways</u>				
425	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2026]	2,966.99 (-) [7,000.00]	368.23 (4,033.01) [0]
	<u>Road Transport And Highways</u>				
426	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [6/2019]	273.20 (-) [273.20]	256.25 (0.00) [0]
427	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	704.29 (0.00) [15]
428	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,948.92 (0.00) [0]
429	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [0/0]	934.46 (-) [934.46]	452.30 (0.00) [0]
430	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [5/2021]	478.74 (-) [478.74]	0.00 (0.00) [-]
431	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [7/2020]	1,273.71 (-) [1,273.71]	0.00 (0.00) [-]
432	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [11/2019]	447.75 (-) [447.75]	179.17 (0.00) [-]
433	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (-) [1,583.18]	234.67 (0.00) [-]
	<u>Urban Development</u>				
434	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [10/2019]	270.83 (-) [270.83]	199.91 (0.00) [59]
	<u>JAMMU AND KASHMIR</u>				
	<u>Civil Aviation</u>				
435	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [9/2021]	323.19 (-) [323.19]	10.14 (0.00) [0]
	<u>Power</u>				
436	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [12/2023]	8,112.12 (-) [8,112.12]	1,152.85 (0.00) [44]
	<u>Railways</u>				
437	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [6/2022]	2,500.00 (27,949.00) [27,949.00]	18,583.33 (25,449.00) [235]
	<u>Road Transport And Highways</u>				
438	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (-) [1,471.75]	305.75 (0.00) [-]
439	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-)	2,168.66 (-)	301.68 (0.00)

			[12/2020]	[2,168.66]	[18]
440	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [10/2019]	2,136.97 (-) [2,136.97]	1,154.18 (0.00) [10]
441	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]
442	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	3,986.82 (0.00) [0]
443	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [0/0]	1,987.00 (-) [1,987.00]	2,580.88 (0.00) [0]
444	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [0/0]	1,100.70 (-) [1,100.70]	2,075.87 (0.00) [0]
445	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [7/2019]	253.44 (-) [253.44]	0.00 (0.00) [0]
446	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	30.43 (0.00) [0]
447	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	0.00 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
448	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	187.12 (0.00) [0]
449	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	90.13 (0.00) [0]
450	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2021]	163.51 (-) [163.51]	106.41 (0.00) [120]
451	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	80.56 (0.00) [0]
452	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
453	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2021]	162.46 (-) [162.46]	89.82 (0.00) [84]
454	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [3/2020]	289.45 (-) [289.45]	244.43 (0.00) [70]
455	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2022]	706.40 (-) [706.40]	354.48 (0.00) [116]
456	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [0/0]	1,230.27 (-) [1,230.27]	371.19 (0.00) [0]
457	MURAIIDH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [0/0]	339.88 (-) [339.88]	12.08 (0.00) [0]
458	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.24 (0.00) [0]
459	PATHERDIH NLW WASHERY	10/2012	4/2014	269.82	180.52

			(-) [11/2019]	(-) [269.82]	(0.00) [67]
460	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2021]	510.85 (-) [510.85]	362.47 (0.00) [60]
461	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2021]	264.68 (-) [264.68]	179.87 (0.00) [108]
	<u>Petroleum</u>				
462	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	17.78 (0.00) [0]
463	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	42.63 (0.00) [0]
464	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	46.48 (0.00) [0]
465	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (910.23) [910.23]	320.14 (86.96) [-12]
	<u>Power</u>				
466	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (9/2019) [9/2021]	14,366.58 (-) [15,164.05]	9,044.25 (797.47) [27]
467	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,268.00 (314.04) [0]
468	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2023]	18,668.00 (-) [18,668.00]	1,855.39 (0.00) [0]
	<u>Railways</u>				
469	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2021]	1,724.20 (-) [1,724.20]	332.04 (0.00) [9]
470	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	159.07 (0.00) [-3]
471	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (3,031.00) [3,376.00]	3,180.37 (2,342.93) [-]
472	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2021]	459.91 (-) [459.91]	456.83 (0.00) [-]
473	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (-) [6/2020]	258.20 (358.68) [358.68]	231.84 (100.48) [18]
474	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (11/2019) [11/2019]	148.77 (-) [377.00]	174.82 (228.23) [35]
	<u>Road Transport And Highways</u>				
475	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [6/2019]	239.68 (-) [235.90]	7.21 (-3.78) [0]
476	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [9/2019]	165.50 (-) [172.16]	117.09 (6.66) [-6]
477	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [0/0]	1,005.08 (-) [1,005.08]	0.00 (0.00) [0]
478	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER	2/2016	3/2019	997.15	728.62

	SECTION		(-) [7/2019]	(-) [997.15]	(0.00) [4]
479	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/	273.46	0.00
			(-) [0/0]	(-) [273.46]	(0.00) [0]
480	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018	323.72	252.99
			(-) [1/2020]	(-) [323.72]	(0.00) [17]
481	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015	1,479.00	740.26
			(-) [0/0]	(-) [1,479.00]	(0.00) [0]
482	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020	212.99	59.56
			(-) [6/2020]	(-) [212.99]	(0.00) [0]
483	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/	1,155.16	0.00
			(-) [0/0]	(-) [1,155.16]	(0.00) [0]
484	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/	458.03	219.61
			(-) [12/2019]	(-) [458.03]	(0.00) [-]
	<u>Steel</u>				
485	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (11/2019) [11/2019]	1,154.18 (-) [1,154.18]	927.19 (0.00) [23]
486	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (6/2020) [6/2020]	1,034.01 (-) [1,034.01]	431.27 (0.00) [32]
487	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (6/2020) [6/2020]	262.87 (-) [262.87]	99.71 (0.00) [12]
	<u>Urban Development</u>				
488	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [9/2020]	171.86 (-) [171.86]	80.08 (0.00) [54]
489	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
490	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
491	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
492	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
493	BSVI UPGRADATION	9/2016	12/2019 (7/2020) [7/2020]	1,810.00 (1,810.00) [1,810.00]	726.57 (0.00) [7]
494	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (6/2019) [10/2018]	224.00 (207.00) [185.00]	164.61 (-39.00) [0]
495	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	38.34 (0.00) [0]
496	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	606.89 (93.00) [0]
497	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022	2,166.38	6.94

			(-) [6/2022]	(-) [2,166.38]	(0.00) [0]
498	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (9/2019) [9/2019]	135.00 (170.70) [170.70]	154.03 (35.70) [6]
499	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	0.42 (0.00) [0]
500	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [9/2020]	581.00 (-) [621.00]	68.27 (40.00) [6]
501	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
502	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [12/2019]	445.89 (-) [445.89]	272.00 (0.00) [10]
	<u>Railways</u>				
503	ARSIKERE-TUMKUR	3/2015	3/2020 (-) [3/2020]	578.00 (-) [578.00]	509.07 (0.00) [0]
504	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2023]	986.30 (-) [986.30]	297.70 (0.00) [93]
505	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
506	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [367.77]	0.00 (40.52) [-]
507	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [692.43]	0.00 (134.43) [-]
508	GADAG-WADI NL	4/2013	12/2018 (-) [12/2024]	2,841.84 (-) [2,841.84]	113.63 (0.00) [72]
509	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,900.00]	1,571.99 (773.00) [0]
510	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [3/2021]	1,156.94 (-) [1,140.93]	786.13 (-16.01) [12]
511	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [2,135.00]	144.76 (-180.00) [-]
512	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (-) [889.52]	438.39 (244.74) [36]
513	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	28.51 (0.00) [93]
514	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
515	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
516	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [1,801.01]	44.36 (0.00) [-]

517	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (-) [348.85]	0.35 (0.00) [-]
	Road Transport And Highways				
518	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (-) [6/2020]	1,167.42 (-) [1,167.42]	254.96 (0.00) [15]
519	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	0.00 (0.00) [0]
520	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [52]
521	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/ (-) [0/0]	720.69 (-) [720.69]	99.03 (0.00) [0]
522	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [11/2020]	701.40 (-) [701.40]	29.48 (0.00) [20]
523	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	16.09 (0.00) [20]
524	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]
525	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [5/2020]	171.60 (-) [171.60]	0.86 (0.00) [24]
526	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [3/2020]	1,388.00 (-) [1,388.00]	1,119.56 (0.00) [19]
527	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	608.81 (0.00) [0]
528	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [12/2019]	946.00 (-) [946.00]	818.53 (0.00) [18]
529	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	62.54 (0.00) [0]
530	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
531	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
532	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
533	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
534	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	604.76 (440.84) [3]
535	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [7/2020]	831.58 (-) [1,177.00]	551.42 (345.42) [4]
536	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,177.80]	0.00 (0.00) [0]

537	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [1,995.34]	0.00 (0.00) [-]
538	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
539	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
540	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [12/2019]	709.00 (-) [709.00]	453.95 (0.00) [27]
541	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [12/2020]	950.69 (-) [950.69]	803.81 (0.00) [16]
542	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
543	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
544	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
545	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
546	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [0/0]	191.60 (-) [191.60]	26.24 (0.00) [0]
547	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [8/2019]	291.49 (-) [291.49]	130.00 (0.00) [24]
548	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
549	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
550	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
551	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	21.16 (0.00) [0]
552	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
553	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
<u>Urban Development</u>					
554	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
555	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
556	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]

557	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [9/2020]	246.31 (-) [246.31]	62.56 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
558	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	495.00 (395.24) [32]
559	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [0/0]	607.06 (-) [714.25]	354.84 (107.19) [0]
560	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	944.42 (-24.04) [8]
561	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (-) [11/2019]	4,588.29 (5,245.96) [5,245.96]	3,518.66 (657.67) [15]
562	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	15.04 (0.00) [0]
	<u>Railways</u>				
563	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (2,815.62) [2,815.62]	263.99 (1,249.62) [0]
564	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (189.24) [189.24]	6.72 (0.00) [0]
565	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (252.96) [252.96]	8.50 (0.00) [0]
566	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
567	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (6/2022) [0/0]	1,431.90 (1,431.90) [1,431.90]	67.54 (0.00) [0]
568	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (828.50) [828.50]	0.08 (-171.50) [0]
	<u>Road Transport And Highways</u>				
569	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [10/2019]	845.24 (-) [845.24]	788.62 (0.00) [-]
570	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [1/2020]	804.97 (-) [804.97]	402.47 (0.00) [19]
571	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,124.11]	256.47 (0.00) [33]
572	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,424.77]	0.00 (0.00) [0]
573	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [12/2019]	255.75 (348.00) [348.43]	290.12 (92.68) [27]
574	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [88]
	<u>Shipping And Ports</u>				
575	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	5/2016	5/2020 (-)	970.00 (-)	109.97 (0.00)

			[5/2020]	[970.00]	[0]
576	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA	7/2016	5/2021 (-) [5/2021]	1,799.00 (-) [1,799.00]	21.00 (0.00) [0]
	<u>Urban Development</u>				
577	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
578	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	86.04 (0.00) [89]
579	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [12/2019]	5,181.79 (-) [5,687.79]	5,188.00 (506.00) [29]
	<u>MADHYA PRADESH</u>				
	<u>Coal</u>				
580	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	116.09 (0.00) [0]
581	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
582	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
583	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2021]	1,186.64 (-) [203.82]	117.55 (-982.82) [-24]
584	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	18.45 (0.00) [0]
585	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	94.84 (0.00) [0]
586	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	264.90 (0.00) [0]
587	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	47.15 (0.00) [0]
588	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	27.08 (0.00) [0]
589	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	103.99 (0.00) [0]
590	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
591	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	0.00 (0.00) [0]
	<u>Petroleum</u>				
592	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [8/2020]	236.00 (-) [236.00]	22.66 (0.00) [2]
	<u>Power</u>				
593	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [1,587.16]	299.55 (-517.05) [0]
594	GADARWARA SUPER THERMAL POWER PROJECT	3/2013	1/2018	11,638.55	12,027.37

	STAGE-I		(3/2020) [3/2020]	(-) [12,865.92]	(1,227.37) [26]
595	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [1/2020]	9,870.51 (-) [11,148.86]	8,306.06 (1,278.35) [0]
	<u>Railways</u>				
596	ANUPPUR-KATNI	4/2015	12/2021 (12/2021) [12/2021]	1,370.00 (1,370.00) [1,370.00]	276.86 (0.00) [0]
597	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.85 (-) [1,485.85]	1,009.30 (0.00) [0]
598	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (10/2019) [10/2019]	383.79 (1,413.76) [1,413.76]	1,324.64 (1,029.97) [-]
599	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (3/2020) [6/2020]	585.93 (737.72) [1,300.44]	646.68 (714.51) [16]
600	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (6/2021) [6/2021]	700.00 (603.69) [603.69]	86.45 (-96.31) [12]
601	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (3/2022) [3/2022]	1,763.93 (1,763.93) [1,763.93]	624.49 (0.00) [24]
602	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (9/2022) [9/2022]	582.13 (1,247.64) [1,247.64]	154.63 (665.51) [6]
603	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (3/2023) [3/2023]	2,478.23 (-) [2,478.23]	367.59 (0.00) [12]
604	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [2/2020]	174.00 (-) [174.00]	150.61 (0.00) [11]
605	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2023) [3/2023]	424.60 (2,909.99) [2,909.99]	1,027.12 (2,485.39) [24]
606	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2023) [3/2023]	3,503.69 (3,338.15) [3,860.40]	1,676.43 (356.71) [12]
	<u>Road Transport And Highways</u>				
607	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [11/2019]	191.21 (-) [191.21]	68.26 (0.00) [0]
608	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (-) [1/2020]	249.05 (-) [249.05]	100.10 (0.00) [18]
609	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	173.80 (0.00) [0]
610	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	0.00 (0.00) [0]
611	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (-) [11/2019]	392.33 (-) [392.33]	224.94 (0.00) [20]
612	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [3/2019]	227.49 (-) [227.49]	100.96 (0.00) [0]
613	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]

614	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [0/0]	990.61 (-) [990.61]	0.00 (0.00) [0]
615	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
616	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2020]	390.51 (-) [390.51]	178.32 (0.00) [-]
617	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [6/2020]	205.05 (-) [205.05]	73.22 (0.00) [39]
618	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (-) [6/2019]	1,583.79 (-) [1,583.79]	1,568.11 (0.00) [0]
619	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [8/2020]	960.24 (-) [960.24]	0.00 (0.00) [-]
620	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	439.07 (0.00) [0]
621	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
622	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [6/2019]	928.83 (-) [928.83]	588.21 (0.00) [0]
623	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [0/0]	794.30 (-) [794.30]	492.23 (0.00) [0]
624	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [0/0]	795.76 (-) [795.76]	564.36 (0.00) [0]
625	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [6/2019]	810.22 (-) [810.22]	586.36 (0.00) [0]
626	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	274.24 (0.00) [27]
627	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	0.00 (0.00) [0]
628	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (-) [2/2020]	957.54 (-) [957.54]	412.39 (0.00) [0]
629	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [5/2020]	497.05 (-) [881.05]	507.45 (384.00) [36]
630	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
631	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,342.77 (0.00) [0]
632	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (-) [1/2020]	628.45 (-) [628.45]	207.68 (0.00) [0]
633	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [8/2019]	410.72 (-) [410.72]	0.00 (0.00) [52]
634	REHABILITATION AND UP-GRADATION OF EXISTING	2/2018	3/2018	169.63	7.10

	INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA		(-) [7/2020]	(-) [169.63]	(0.00) [28]
635	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [8/2019]	178.23 (-) [178.23]	114.16 (0.00) [11]
636	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (-) [11/2019]	287.34 (-) [287.34]	148.65 (0.00) [10]
637	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [11/2019]	877.79 (-) [877.79]	383.94 (0.00) [5]
638	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (-) [11/2019]	235.91 (-) [235.91]	83.40 (0.00) [21]
639	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [2/2020]	809.16 (-) [809.16]	198.65 (0.00) [19]
640	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
641	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [3/2020]	954.43 (-) [954.43]	298.00 (0.00) [54]
642	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [2/2020]	511.83 (-) [511.83]	237.15 (0.00) [30]
643	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	254.17 (-) [254.17]	117.16 (0.00) [21]
644	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	233.04 (-) [233.04]	93.96 (0.00) [20]
645	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [4/2020]	279.44 (-) [279.44]	53.59 (0.00) [25]
646	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	166.21 (-) [166.21]	17.10 (0.00) [22]
647	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	184.62 (-) [184.62]	54.49 (0.00) [21]
648	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	214.69 (-) [214.69]	15.22 (0.00) [20]
649	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	217.22 (-) [217.22]	12.39 (0.00) [22]
650	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [12/2019]	162.56 (-) [162.56]	66.95 (0.00) [21]
651	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [5/2020]	373.82 (-) [373.82]	116.33 (0.00) [8]
	<u>Urban Development</u>				
652	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	34.12 (0.00) [0]
653	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	42.62 (0.00) [0]
	<u>MAHARASHTRA</u>				

	Civil Aviation				
654	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	358.89 (-) [358.89]	29.73 (0.00) [0]
	Coal				
655	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	17.71 (44.53) [12]
656	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	181.84 (0.00) [0]
657	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	199.23 (0.00) [0]
658	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	258.40 (0.00) [0]
659	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [3/2021]	252.71 (-) [252.71]	0.00 (0.00) [0]
660	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	119.73 (221.74) [0]
661	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [0/0]	304.52 (-) [304.52]	153.29 (0.00) [0]
662	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	413.13 (0.00) [0]
663	GAURI DEEP OC	10/2016	3/2019 (-) [3/2019]	164.96 (-) [164.96]	89.94 (0.00) [0]
664	GOKUL	11/2014	3/2018 (-) [0/0]	267.67 (-) [267.67]	208.78 (0.00) [0]
665	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2024]	277.65 (-) [313.34]	115.28 (35.69) [36]
666	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	319.81 (0.00) [0]
667	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	175.30 (0.00) [0]
668	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [0/0]	295.56 (-) [295.56]	123.60 (0.00) [0]
669	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	213.24 (0.00) [0]
670	SAONER I UG TO OC PHASE I	11/2016	3/2022 (-) [3/2022]	162.10 (-) [162.10]	50.56 (0.00) [0]
671	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	121.74 (0.00) [0]
672	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	318.14 (-) [318.14]	149.87 (0.00) [0]
	Fertilisers				
673	GAS TURBINE GENERATOR AND HEAT RECOVERY	4/2018	4/2020	426.72	92.10

	STEAM GENERATOR PROJECT AT RCF TROMBAY		(-) [4/2020]	(-) [426.72]	(0.00) [0]
674	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (-) [9/2019]	197.79 (-) [209.44]	160.07 (11.65) [34]
	<u>Health And Family Welfare</u>				
675	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [2/2020]	582.99 (-) [582.99]	112.97 (0.00) [-]
676	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [10/2019]	274.19 (-) [274.19]	169.93 (0.00) [7]
	<u>Information And Broadcasting</u>				
677	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	3/2020 (-) [3/2020]	167.70 (-) [167.70]	0.00 (0.00) [0]
678	NATIONAL FILM HERITAGE MISSION	11/2014	/ (-) [0/0]	597.41 (-) [597.41]	29.80 (0.00) [0]
	<u>Petroleum</u>				
679	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	58.33 (0.00) [0]
680	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (-) [11/2019]	968.61 (-) [1,033.95]	897.60 (65.34) [0]
681	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	37.47 (0.00) [0]
682	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	34.07 (0.00) [3]
683	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	27.05 (0.00) [9]
684	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2019) [12/2019]	861.79 (-) [1,683.06]	1,285.65 (821.27) [79]
685	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (3/2020) [3/2020]	546.15 (565.15) [565.15]	442.18 (19.00) [4]
686	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (-) [11/2019]	511.30 (-) [511.30]	445.24 (0.00) [0]
687	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,292.46]	121.38 (0.00) [0]
688	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (12/2021) [12/2021]	4,006.83 (-) [4,475.92]	2,745.63 (469.09) [7]
689	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (-) [4,619.94]	4,323.32 (0.00) [27]
690	HEERA REDEVELOPMENT - PHASE III	5/2019	12/2021 (-) [3/2022]	2,494.68 (-) [2,494.68]	0.00 (0.00) [3]
691	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [9/2019]	554.00 (-) [554.00]	335.52 (0.00) [-5]
692	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019)	2,059.63 (-)	1,908.01 (0.00)

			[12/2019]	[2,059.63]	[57]
693	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	917.26 (0.00) [0]
694	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2020) [5/2020]	3,190.69 (-) [3,247.19]	2,192.66 (56.50) [25]
695	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	155.19 (0.00) [0]
696	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (-) [3/2022]	3,228.80 (-) [3,228.80]	405.01 (0.00) [0]
697	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (12/2019) [12/2019]	6,068.80 (-) [5,296.93]	4,758.62 (-771.87) [8]
698	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	2/2019	4/2021 (-) [5/2021]	3,660.71 (3,740.05) [3,740.05]	126.66 (79.34) [1]
699	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [3/2020]	4,199.00 (5,060.00) [5,060.00]	2,376.01 (861.00) [0]
700	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	2,230.96 (0.00) [14]
701	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (-) [12/2020]	763.92 (-) [763.92]	0.00 (0.00) [0]
702	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	436.53 (0.00) [0]
703	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	115.60 (0.00) [0]
	<u>Power</u>				
704	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
	<u>Railways</u>				
705	3RD LINE BETWEEN BHUSAVAL-JALGAON	4/2011	3/2019 (12/2019) [12/2019]	184.06 (199.12) [305.00]	267.36 (120.94) [9]
706	AHMEDNAGAR-PARLI VAJINATH(NL) CR	2/1997	3/2021 (-) [3/2022]	2,271.50 (-) [3,712.50]	2,291.50 (1,441.00) [12]
707	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2021]	495.44 (1,781.98) [2,980.41]	1,403.52 (2,484.97) [204]
708	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	77.48 (205.27) [0]
709	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	713.48 (-) [1,950.00]	1,823.93 (1,236.52) [0]
710	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
711	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
712	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023	2,449.91	145.69

			(-) [3/2023]	(-) [2,449.91]	(0.00) [0]
713	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2022]	792.89 (-) [792.89]	297.30 (0.00) [12]
714	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	68.93 (0.00) [24]
715	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2019]	305.00 (-) [305.00]	260.88 (0.00) [9]
716	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
717	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (3/2021) [3/2021]	5,300.00 (918.53) [918.53]	277.61 (-4,381.47) [84]
718	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2022]	3,627.47 (3,627.00) [3,627.47]	511.35 (0.00) [-24]
719	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
720	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (3/2023) [3/2023]	1,908.51 (2,686.63) [2,686.63]	441.10 (778.12) [0]
721	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
722	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
723	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
724	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (3/2023) [3/2023]	229.00 (403.00) [860.92]	41.54 (631.92) [15]
725	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	54.67 (0.00) [12]
726	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,272.19]	271.39 (0.00) [12]
727	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,205.35 (0.00) [0]
728	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	220.34 (0.00) [24]
	<u>Road Transport And Highways</u>				
729	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	0.00 (0.00) [0]
730	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
731	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [7/2019]	972.50 (-) [972.50]	1,497.56 (0.00) [24]
732	4-LANING FROM AURANGABAD TO KARODI (KM 290.200	1/2018	/	607.00	55.06

	TO 320.104)		(-) [8/2021]	(-) [607.00]	(0.00) [-]
733	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/	621.00	212.24
			(-) [4/2021]	(-) [621.00]	(0.00) [-]
734	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016	923.04	708.62
			(-) [5/2020]	(-) [923.04]	(0.00) [42]
735	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020	744.64	0.00
			(-) [3/2020]	(-) [982.00]	(237.36) [0]
736	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/	1,071.61	0.00
			(-) [7/2021]	(-) [1,071.61]	(0.00) [-]
737	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019	446.17	38.95
			(-) [11/2019]	(-) [446.17]	(0.00) [8]
738	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020	1,098.06	1,082.97
			(-) [8/2020]	(-) [1,160.64]	(62.58) [5]
739	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/	1,142.62	726.85
			(-) [0/0]	(-) [1,142.62]	(0.00) [0]
740	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/	1,101.58	0.00
			(-) [0/0]	(-) [1,101.58]	(0.00) [0]
741	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019	400.25	64.89
			(-) [2/2021]	(-) [400.25]	(0.00) [23]
742	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/	1,064.88	0.00
			(-) [7/2021]	(-) [1,064.88]	(0.00) [-]
743	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017	1,059.73	480.96
			(-) [11/2020]	(-) [1,071.00]	(11.27) [44]
744	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020	1,030.44	1,027.16
			(-) [5/2020]	(-) [1,065.51]	(35.07) [2]
745	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020	988.34	1,094.73
			(-) [8/2020]	(-) [1,043.28]	(54.94) [5]
746	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018	505.00	347.91
			(-) [5/2020]	(-) [505.00]	(0.00) [24]
747	AHMADPUR TO PIMPLA	1/2017	8/2019	422.38	148.58
			(-) [8/2019]	(422.38) [422.38]	(0.00) [0]
748	AHMEDNAGAR TO BARAMATI	1/2017	8/2019	955.40	331.50
			(-) [8/2019]	(-) [955.40]	(0.00) [0]
749	AKKALKOT TO DHUDHNI	4/2016	2/2019	211.42	130.85
			(-) [2/2020]	(-) [211.42]	(0.00) [12]
750	AKOLA TO AKOT	1/2017	6/2019	313.95	37.05
			(-) [0/0]	(-) [313.95]	(0.00) [0]
751	AKOT TO ANJANGAON	1/2017	6/2019	245.77	111.98
			(-) [0/0]	(246.00) [245.77]	(0.00) [0]
752	AMD I TO SAONER	1/2017	6/2019	396.91	247.48
			(-)	(396.91)	(0.00)

			[8/2019]	[396.91]	[2]
753	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2020]	426.06 (426.00) [426.06]	64.97 (0.00) [0]
754	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [12/2019]	309.94 (310.00) [309.94]	16.32 (0.00) [0]
755	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	91.30 (0.00) [0]
756	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	22.27 (0.00) [0]
757	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [4/2020]	241.69 (242.00) [241.69]	76.29 (0.00) [0]
758	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	24.00 (0.00) [31]
759	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [11/2019]	259.55 (260.00) [259.55]	150.00 (0.00) [0]
760	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	690.60 (0.00) [0]
761	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2021]	743.21 (743.21) [743.21]	52.87 (0.00) [0]
762	BHOKAR TO SARSAM	2/2017	7/2019 (-) [7/2019]	295.09 (-) [295.99]	155.64 (0.90) [0]
763	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [7/2019]	178.26 (-) [178.26]	96.95 (0.00) [0]
764	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [12/2019]	206.97 (207.00) [206.97]	68.89 (0.00) [0]
765	CHIKALI TO DHAD	3/2018	12/2019 (-) [12/2019]	189.46 (189.00) [189.46]	21.00 (0.00) [0]
766	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [10/2019]	548.03 (548.00) [548.03]	260.00 (0.00) [4]
767	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2019]	393.10 (393.10) [393.10]	111.97 (0.00) [0]
768	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	156.72 (0.00) [0]
769	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	14.11 (0.00) [-]
770	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (-) [4/2021]	649.50 (-) [649.50]	129.48 (0.00) [25]
771	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [11/2020]	291.53 (-) [291.53]	29.25 (0.00) [-]
772	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [9/2019]	244.90 (-) [244.90]	219.09 (0.00) [4]

773	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [11/2020]	289.21 (-) [289.21]	19.78 (0.00) [-]
774	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (-) [12/2020]	593.26 (-) [593.26]	484.48 (0.00) [31]
775	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
776	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [6/2020]	531.13 (-) [531.13]	163.10 (0.00) [25]
777	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	52.00 (0.00) [0]
778	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
779	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [2/2020]	247.02 (-) [157.49]	0.00 (-89.53) [-1]
780	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (-) [6/2020]	414.51 (-) [414.00]	529.62 (-0.51) [25]
781	DAHEGAON TO KUHI	1/2017	6/2019 (-) [0/0]	228.89 (228.89) [228.89]	115.00 (0.00) [0]
782	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [12/2019]	182.63 (-) [182.63]	89.15 (0.00) [0]
783	DEORI TO AMGAON	1/2017	5/2019 (-) [5/2020]	409.62 (410.00) [409.62]	155.78 (0.00) [12]
784	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	106.46 (0.00) [0]
785	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [9/2019]	296.19 (-) [254.00]	248.60 (-42.19) [-6]
786	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [12/2019]	336.21 (336.00) [336.21]	58.66 (0.00) [0]
787	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [2/2020]	217.14 (217.00) [217.14]	58.77 (0.00) [0]
788	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [6/2020]	391.06 (391.00) [391.06]	84.00 (0.00) [12]
789	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	66.10 (0.00) [0]
790	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
791	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [642.13]	288.84 (0.00) [-]
792	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [0/0]	1,871.34 (-) [1,871.34]	3,424.19 (0.00) [0]
793	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020	904.16	607.37

			(-) [5/2020]	(-) [904.16]	(0.00) [3]
794	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	159.31 (0.00) [0]
795	HELWAK TO KARAD	2/2017	7/2019 (-) [7/2019]	416.99 (-) [416.99]	111.40 (0.00) [0]
796	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [12/2019]	294.87 (295.00) [294.87]	36.30 (0.00) [0]
797	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [12/2019]	355.17 (355.17) [355.17]	141.87 (0.00) [5]
798	INDAPUR TO VADPALE	1/2017	12/2019 (-) [3/2020]	1,202.52 (1,202.52) [1,202.52]	652.90 (0.00) [3]
799	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [11/2019]	461.96 (461.96) [461.96]	127.43 (0.00) [0]
800	JALGAON TO BHADGAON	1/2018	11/2019 (-) [11/2019]	307.54 (308.00) [307.54]	106.59 (0.00) [0]
801	JALGAON TO NANDURA	3/2018	12/2019 (-) [12/2019]	177.84 (177.00) [177.84]	45.69 (0.00) [0]
802	JALKOT TO TOGRI	7/2018	8/2020 (-) [8/2020]	299.92 (300.00) [299.92]	4.20 (0.00) [0]
803	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (356.66) [356.66]	24.88 (0.00) [0]
804	KAIJ TO KUSALAM	1/2017	7/2019 (-) [7/2019]	554.78 (554.78) [554.78]	157.90 (0.00) [0]
805	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	294.91 (0.00) [0]
806	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (1,338.13) [1,338.13]	959.51 (0.00) [0]
807	KANTE TO WAKED	3/2016	11/2019 (-) [11/2019]	1,230.02 (1,230.02) [1,230.02]	567.61 (0.00) [0]
808	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [6/2020]	407.19 (407.00) [407.19]	12.00 (0.00) [12]
809	KARAD TO TAGAON	1/2017	6/2019 (-) [6/2020]	537.81 (538.00) [537.81]	73.97 (0.00) [12]
810	KARAD TO VITA	1/2018	12/2019 (-) [12/2019]	344.85 (245.00) [344.85]	66.04 (0.00) [0]
811	KARWANDI TO RAJURI	3/2018	12/2019 (-) [12/2019]	276.95 (277.00) [276.95]	85.47 (0.00) [0]
812	KATOL TO WARUD	1/2017	6/2019 (-) [8/2019]	463.62 (664.00) [463.62]	243.34 (0.00) [2]
813	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-)	249.29 (-)	65.20 (0.00)

			[12/2019]	[249.29]	[0]
814	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [12/2019]	203.21 (203.00) [203.21]	101.79 (0.00) [7]
815	KHERDA TO NAGZARI	3/2018	12/2019 (-) [12/2019]	181.30 (-) [181.30]	66.50 (0.00) [0]
816	KOLDE TO KHETIYA	1/2017	7/2019 (-) [7/2019]	509.18 (-) [509.18]	175.93 (0.00) [0]
817	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [4/2020]	281.78 (282.00) [281.78]	23.73 (0.00) [12]
818	KOTHARI TO DHANORA	9/2018	8/2020 (-) [8/2020]	301.38 (301.00) [301.38]	41.00 (0.00) [0]
819	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	280.69 (0.00) [0]
820	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [12/2019]	225.25 (225.00) [225.25]	97.75 (0.00) [0]
821	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [7/2019]	307.63 (-) [307.63]	148.17 (0.00) [0]
822	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [12/2019]	243.45 (244.00) [243.45]	58.02 (0.00) [0]
823	LATUR TO PANGAON	3/2018	12/2019 (-) [12/2019]	336.47 (336.00) [336.47]	85.48 (0.00) [0]
824	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [5/2020]	237.40 (-) [237.40]	7.34 (0.00) [0]
825	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [7/2019]	413.99 (-) [413.99]	310.33 (0.00) [0]
826	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [12/2019]	256.15 (-) [256.15]	15.50 (0.00) [0]
827	MALEGAON TO RISOD	2/2018	12/2019 (-) [12/2019]	303.24 (303.24) [303.24]	93.97 (0.00) [0]
828	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2020]	322.55 (-) [322.55]	156.91 (0.00) [12]
829	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [7/2020]	457.52 (457.52) [457.52]	202.31 (0.00) [12]
830	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [11/2019]	222.13 (222.13) [222.13]	23.36 (0.00) [0]
831	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [8/2019]	228.54 (228.54) [228.54]	92.30 (0.00) [0]
832	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [12/2019]	418.36 (-) [418.36]	102.13 (0.00) [0]
833	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [7/2019]	486.19 (486.19) [486.19]	210.29 (0.00) [0]

834	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [7/2019]	232.77 (-) [232.77]	85.51 (0.00) [0]
835	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	184.08 (0.00) [0]
836	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [7/2019]	488.60 (-) [488.60]	151.71 (0.00) [0]
837	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2019]	341.16 (341.00) [341.16]	156.29 (0.00) [6]
838	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	231.90 (0.00) [0]
839	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [7/2019]	162.34 (-) [162.34]	32.80 (0.00) [0]
840	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [12/2019]	376.72 (377.00) [376.72]	149.81 (0.00) [6]
841	NAGBHID TO ARMORI	9/2016	7/2019 (-) [7/2019]	269.05 (-) [269.05]	203.91 (0.00) [0]
842	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	226.24 (0.00) [0]
843	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (12/2020) [12/2020]	546.00 (-) [546.00]	269.67 (0.00) [17]
844	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (12/2020) [12/2020]	591.66 (-) [591.66]	310.56 (0.00) [17]
845	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2019]	244.04 (244.00) [244.04]	15.94 (0.00) [9]
846	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2019]	274.50 (275.00) [274.50]	224.39 (0.00) [0]
847	NANDED TO JALKOT	12/2017	9/2019 (-) [9/2019]	456.93 (457.00) [456.93]	55.50 (0.00) [0]
848	NANDGAON TO MORSHI	1/2017	6/2019 (-) [12/2019]	385.87 (386.00) [385.87]	184.75 (0.00) [6]
849	NASHIK TO PETH	12/2015	11/2018 (-) [11/2019]	289.60 (-) [289.60]	83.81 (0.00) [12]
850	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [9/2019]	406.54 (406.54) [406.54]	142.00 (0.00) [0]
851	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [5/2020]	420.63 (421.00) [420.63]	17.60 (0.00) [0]
852	OMREGA TO AUSA	3/2018	12/2019 (-) [12/2019]	272.04 (272.00) [272.04]	72.24 (0.00) [0]
853	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [8/2020]	344.25 (344.00) [344.25]	44.02 (0.00) [0]
854	PAHUR TO BODHWAD	1/2017	5/2020	244.93	34.23

			(-) [5/2020]	(-) [244.93]	(0.00) [0]
855	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	118.00 (0.00) [0]
856	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [12/2019]	227.19 (227.00) [227.19]	50.23 (0.00) [0]
857	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [5/2020]	381.08 (302.00) [381.08]	13.00 (0.00) [0]
858	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [7/2019]	218.38 (-) [218.38]	168.75 (0.00) [0]
859	PANVEL-INDAPUR	12/2011	6/2014 (-) [3/2020]	942.69 (-) [942.69]	750.38 (0.00) [69]
860	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [12/2019]	238.19 (238.00) [238.19]	23.85 (0.00) [0]
861	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2020]	205.72 (205.72) [205.72]	26.42 (0.00) [12]
862	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [11/2019]	983.14 (983.14) [983.14]	655.15 (0.00) [-1]
863	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [7/2019]	420.57 (420.57) [420.57]	157.39 (0.00) [0]
864	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [12/2019]	170.00 (-) [170.00]	15.57 (0.00) [0]
865	PEN TO KHOPOLI	3/2018	3/2018 (-) [12/2019]	301.39 (302.00) [301.39]	0.00 (0.00) [21]
866	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [8/2019]	595.77 (595.77) [595.77]	118.44 (0.00) [0]
867	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [12/2019]	223.46 (-) [223.46]	21.42 (0.00) [0]
868	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [12/2019]	228.31 (-) [228.31]	13.50 (0.00) [0]
869	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [7/2019]	1,724.55 (-) [1,724.55]	2,346.01 (0.00) [76]
870	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [7/2019]	210.81 (-) [210.81]	106.69 (0.00) [0]
871	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	259.50 (0.00) [0]
872	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	83.11 (0.00) [0]
873	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (-) [12/2019]	536.65 (356.00) [536.65]	42.25 (0.00) [0]
874	RISOD TO HINGOLI	2/2018	12/2019 (-)	355.99 (355.99)	95.97 (0.00)

			[12/2019]	[355.99]	[0]
875	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [11/2019]	362.96 (362.96) [362.96]	29.83 (0.00) [5]
876	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [12/2019]	415.25 (415.25) [415.25]	82.22 (0.00) [0]
877	SANGOLA TO JATH	1/2018	12/2019 (-) [12/2019]	257.38 (257.00) [257.38]	62.15 (0.00) [0]
878	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [7/2019]	250.46 (-) [250.46]	103.63 (0.00) [0]
879	SARSAM TO KOTHARI	2/2016	7/2019 (-) [7/2019]	545.64 (-) [545.64]	64.01 (0.00) [0]
880	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	179.77 (0.00) [0]
881	SATARA TO MHASWAD	1/2017	7/2019 (-) [7/2019]	653.46 (-) [653.46]	203.42 (0.00) [0]
882	SELDOH TO PANVAR	7/2018	5/2020 (-) [5/2020]	404.33 (404.33) [404.33]	14.19 (0.00) [0]
883	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [12/2019]	150.79 (150.79) [150.79]	21.42 (0.00) [0]
884	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [12/2019]	373.10 (373.00) [373.10]	136.43 (0.00) [7]
885	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [7/2019]	211.34 (211.34) [211.34]	100.83 (0.00) [0]
886	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	147.79 (0.00) [0]
887	SHIVUR TO YEOLA	3/2018	12/2019 (-) [12/2019]	181.08 (-) [181.08]	7.45 (0.00) [0]
888	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	44.03 (0.00) [0]
889	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (448.18) [404.94]	90.86 (0.00) [-]
890	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE	11/2016	/ (-) [5/2019]	290.73 (-) [290.73]	174.12 (0.00) [0]
891	TAKARKHED TO JALNA	9/2017	6/2019 (-) [12/2019]	417.90 (418.00) [417.90]	67.26 (0.00) [6]
892	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [12/2019]	264.41 (264.00) [264.41]	23.71 (0.00) [9]
893	TALGAON TO KALMATH	10/2016	3/2020 (-) [3/2020]	904.70 (904.70) [904.70]	604.05 (0.00) [0]
894	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [11/2019]	195.64 (196.00) [195.64]	93.73 (0.00) [0]

895	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [7/2019]	422.02 (422.00) [422.02]	224.01 (0.00) [0]
896	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [3/2020]	1,598.47 (1,598.47) [1,598.47]	746.91 (0.00) [4]
897	VITA TO NAGAJ	3/2018	12/2019 (-) [12/2019]	304.58 (305.00) [304.58]	9.16 (0.00) [0]
898	WADI TO ASOLA	1/2017	9/2019 (-) [9/2020]	363.82 (363.82) [363.82]	92.10 (0.00) [12]
899	WADIGODRI TO DHANGRIPIPRI	3/2018	2/2020 (-) [2/2020]	194.23 (194.00) [194.23]	57.23 (0.00) [0]
900	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [5/2020]	376.19 (376.19) [376.19]	23.03 (0.00) [12]
901	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	618.00 (0.00) [0]
902	WARDHA TO ARVI	2/2018	4/2020 (-) [4/2020]	313.58 (313.58) [313.58]	4.86 (0.00) [0]
903	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [12/2019]	216.90 (216.90) [216.90]	20.00 (0.00) [0]
904	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [12/2019]	165.51 (-) [165.51]	25.45 (0.00) [0]
905	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
906	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Shipping And Ports</u>				
907	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	1/2007	12/2010 (-) [0/0]	366.39 (-) [669.46]	411.12 (303.07) [0]
	<u>Telecommunications</u>				
908	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (9/2019) [9/2019]	231.80 (240.10) [240.10]	117.63 (8.30) [11]
	<u>Urban Development</u>				
909	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2020) [9/2020]	223.37 (-) [223.37]	29.51 (0.00) [2]
910	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
911	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	5,989.97 (0.00) [21]
912	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (1/2022) [1/2022]	11,420.00 (-) [11,420.00]	2,642.09 (0.00) [2]
913	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	6/2010	3/2012 (-) [0/0]	205.00 (-) [205.00]	156.21 (0.00) [0]
	<u>Water Resources</u>				

914	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2019]	233.57 (-) [233.57]	32.20 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
915	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
916	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (13,809.00) [12,524.00]	8,821.88 (8,069.83) [108]
	<u>Road Transport And Highways</u>				
917	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	74.49 (0.00) [0]
918	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	119.56 (-59.80) [36]
	<u>Urban Development</u>				
919	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
920	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
921	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.66 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
922	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [7/2019]	306.28 (-) [306.28]	42.66 (0.00) [2]
923	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [9/2019]	479.20 (-) [479.20]	475.02 (0.00) [16]
924	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	<u>Urban Development</u>				
925	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
926	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	2,935.76 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
927	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	296.28 (182.95) [116]
928	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	269.07 (118.65) [63]
929	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]

930	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
931	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
932	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
933	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
934	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
935	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
936	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
937	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
938	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	789.85 (368.26) [105]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
939	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	20.86 (0.00) [0]
940	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	150.05 (0.00) [0]
941	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	235.29 (0.00) [0]
	<u>Petroleum</u>				
942	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
943	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (3,027.90) [3,027.90]	806.13 (1,204.90) [0]
944	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	158.44 (0.00) [0]
945	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	934.68 (0.00) [0]
946	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,256.48 (0.00) [0]
947	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,395.00 (0.00) [0]
948	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	717.33 (0.00) [0]
949	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH	2/2015	10/2019	890.00	600.35

	AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE		(-) [10/2019]	(-) [887.00]	(-3.00) [0]
950	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (-) [2/2022]	2,915.00 (2,915.00) [3,049.47]	2,371.62 (134.47) [110]
951	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [12/2020]	2,881.40 (-) [2,000.00]	1,256.25 (-881.40) [0]
952	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,438.13 (0.00) [0]
953	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	1,697.02 (1,017.00) [-4]
954	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (-) [10/2020]	690.00 (-) [690.00]	256.76 (0.00) [27]
955	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	83.34 (0.00) [0]
956	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [12/2019]	352.56 (-) [438.84]	230.43 (86.28) [33]
957	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (8/2019) [8/2019]	309.81 (723.40) [723.40]	689.03 (413.59) [58]
	<u>Power</u>				
958	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [2/2020]	198.49 (-) [198.49]	83.31 (0.00) [5]
959	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2019]	4,754.42 (-) [9,072.36]	1,211.92 (4,317.94) [12]
960	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	38.90 (0.00) [0]
961	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (4/2019) [6/2019]	196.58 (-) [225.28]	162.30 (28.70) [0]
962	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (8/2019) [8/2019]	1,364.52 (-) [1,891.41]	1,259.05 (526.89) [40]
963	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (12/2019) [3/2020]	522.29 (-) [546.36]	465.21 (24.07) [40]
964	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	1,399.20 (0.00) [0]
965	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (6/2019) [10/2019]	235.53 (-) [235.53]	117.15 (0.00) [4]
966	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (6/2019) [8/2019]	322.30 (-) [322.30]	153.70 (0.00) [6]
967	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (3/2018) [8/2019]	197.40 (-) [197.40]	81.97 (0.00) [17]
968	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [9/2019]	3,519.59 (-) [3,519.59]	2,431.00 (0.00) [4]
969	HVDC BIPOLE LINK BETWEEN WESTERN REGION	2/2017	4/2020	5,070.13	2,516.66

	(RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR		(-) [4/2020]	(-) [5,070.13]	(0.00) [0]
970	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	7,922.74 (0.00) [0]
971	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	933.96 (0.00) [0]
972	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	185.94 (0.00) [0]
973	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (12/2018) [12/2020]	5,111.33 (-) [6,880.36]	1,367.68 (1,769.03) [24]
974	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (-) [14,719.10]	12,804.46 (3,588.91) [103]
975	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (11/2019) [11/2019]	283.72 (-) [283.72]	187.60 (0.00) [0]
976	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (3/2019) [7/2019]	562.25 (-) [562.25]	392.96 (0.00) [4]
977	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [7/2019]	3,654.00 (-) [3,654.00]	3,308.50 (0.00) [3]
978	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (4/2019) [7/2019]	608.24 (-) [608.24]	407.79 (0.00) [3]
979	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [8/2019]	203.28 (-) [260.03]	190.80 (56.75) [25]
980	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (12/2019) [12/2019]	379.95 (-) [379.95]	52.63 (0.00) [0]
981	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-) [7/2019]	337.75 (-) [337.75]	84.17 (0.00) [1]
982	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (9/2019) [9/2019]	487.49 (-) [639.46]	540.12 (151.97) [63]
983	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2019) [12/2019]	4,824.12 (-) [5,071.94]	4,558.05 (247.82) [86]
984	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	3/2018 (3/2019) [7/2019]	268.80 (-) [340.88]	251.33 (72.08) [16]
985	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [9/2019]	871.62 (-) [871.62]	548.30 (0.00) [23]
986	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (9/2019) [9/2019]	408.46 (-) [408.46]	266.03 (0.00) [8]
987	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (12/2019) [12/2019]	5,151.37 (5,151.37) [5,151.37]	3,115.72 (0.00) [21]
988	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (12/2019) [3/2020]	808.63 (-) [808.63]	513.85 (0.00) [26]
989	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (3/2017)	374.63 (374.63)	210.72 (0.00)

			[12/2019]	[374.63]	[44]
990	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (2/2020) [2/2020]	195.05 (-) [195.05]	116.76 (0.00) [0]
	<u>Railways</u>				
991	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	2,812.27 (0.00) [0]
992	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2020]	288.35 (-) [376.90]	370.65 (88.55) [-]
993	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.12 (-200.00) [-]
994	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (1,352.74) [1,352.74]	269.07 (648.43) [0]
995	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [1,787.00]	2.46 (863.77) [0]
996	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2021]	175.80 (-) [226.22]	226.22 (50.42) [-]
997	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	233.84 (1,211.86) [0]
998	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
999	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,300.00]	2.28 (1,776.48) [0]
1000	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	307.99 (182.31) [12]
1001	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [0/0]	243.78 (-) [895.00]	106.55 (651.22) [0]
1002	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	102.27 (173.89) [96]
1003	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2022) [3/2022]	1,347.26 (1,347.26) [1,347.26]	719.73 (0.00) [0]
1004	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	682.91 (0.00) [12]
1005	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [296.43]	200.07 (-68.74) [96]
1006	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2022]	336.91 (791.39) [800.00]	512.67 (463.09) [-]
1007	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	637.72 (818.35) [133]
1008	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [12/2022]	2,030.50 (-) [2,030.50]	19.07 (0.00) [-]
1009	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-)	651.00 (-)	7.96 (358.00)

			[0/0]	[1,009.00]	[0]
1010	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/	11,589.00	0.00
			(-)	(30,357.00)	(16,592.00)
			[0/0]	[28,181.00]	[0]
1011	GAYA-CHATRA (NL)	4/2008	/	415.67	15.47
			(-)	(-)	(134.08)
			[3/2024]	[549.75]	[-]
1012	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020	511.86	1,660.29
			(12/2020)	(1,756.00)	(1,244.14)
			[12/2020]	[1,756.00]	[8]
1013	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/	636.38	0.00
			(-)	(-)	(0.00)
			[0/0]	[636.38]	[0]
1014	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022	2,912.96	137.90
			(-)	(-)	(932.64)
			[12/2024]	[3,845.60]	[33]
1015	HAJIPUR - BACHAWARA	5/2015	3/2019	678.54	446.51
			(-)	(678.54)	(0.00)
			[2/2021]	[678.54]	[23]
1016	HANSDIHA-GODDA NL	4/2011	3/2020	542.18	424.02
			(-)	(-)	(151.62)
			[3/2020]	[693.80]	[0]
1017	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/	172.03	10.73
			(-)	(-)	(88.07)
			[3/2025]	[260.10]	[-]
1018	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022	230.03	277.14
			(-)	(-)	(540.05)
			[12/2022]	[770.08]	[0]
1019	HOTGI-KUDGI-GADAG	3/2015	3/2019	1,614.59	914.00
			(-)	(-)	(255.82)
			[3/2021]	[1,870.41]	[24]
1020	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018	157.94	51.47
			(-)	(-)	(0.00)
			[3/2021]	[157.94]	[28]
1021	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	246.00
			(-)	(-)	(0.00)
			[3/2025]	[166.89]	[-]
1022	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016	625.00	834.59
			(-)	(781.00)	(230.00)
			[3/2021]	[855.00]	[60]
1023	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014	2,132.77	331.17
			(-)	(-)	(0.00)
			[3/2024]	[2,132.77]	[120]
1024	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016	923.52	433.31
			(-)	(-)	(71.58)
			[3/2025]	[995.10]	[108]
1025	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/	174.56	71.42
			(-)	(-)	(0.00)
			[3/2025]	[174.56]	[-]
1026	KAZIPET-BALHRSHA	4/2015	3/2021	2,063.03	675.97
			(-)	(-)	(0.00)
			[3/2023]	[2,063.03]	[24]
1027	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023	1,856.95	252.81
			(-)	(-)	(343.05)
			[3/2024]	[2,200.00]	[12]
1028	KURUPPANTHARA-CHINGAVANAM	4/2007	/	270.14	369.32
			(-)	(457.08)	(186.94)
			[0/0]	[457.08]	[0]
1029	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006	406.99	148.43
			(-)	(-)	(138.71)
			[3/2025]	[545.70]	[228]

1030	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (3/2023) [3/2023]	247.66 (-) [6,093.31]	1,835.18 (5,845.65) [178]
1031	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	104.65 (0.00) [132]
1032	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2019]	120.70 (-) [1,800.00]	170.47 (1,679.30) [9]
1033	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	153.64 (180.72) [157]
1034	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	252.18 (59.77) [-]
1035	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2021]	1,723.00 (1.00) [1,723.00]	1,368.46 (0.00) [252]
1036	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	121.98 (246.16) [0]
1037	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (-) [2,010.00]	654.07 (1,560.00) [140]
1038	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	32.00 (0.05) [240]
1039	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	68.14 (228.78) [0]
1040	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [3/2021]	241.52 (373.87) [394.28]	272.88 (152.76) [-]
1041	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [0/0]	1,798.00 (-) [2,496.67]	0.00 (698.67) [0]
1042	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1043	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2021]	1,180.19 (3,300.00) [3,300.00]	3,259.74 (2,119.81) [147]
1044	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	39.52 (85.99) [25]
1045	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [471.81]	454.23 (210.43) [0]
1046	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	288.53 (1,221.83) [36]
1047	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1048	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,079.15]	184.89 (1,996.40) [0]
1049	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	2,062.30 (-) [2,062.20]	825.58 (-0.10) [-]
1050	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-	4/2000	/	297.47	52.09

	MINAKHAN VIA GHATAKPUR NL		(-) [3/2025]	(-) [298.22]	(0.75) [-]
1051	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	153.62 (-10.96) [108]
1052	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
1053	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	9.31 (811.34) [-]
1054	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1055	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1056	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [3/2020]	860.43 (-) [860.43]	697.21 (0.00) [0]
	<u>Road Transport And Highways</u>				
1057	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1058	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	3,070.11 (1,016.78) [0]
1059	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
1060	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,294.47]	0.00 (0.00) [0]
1061	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [998.70]	0.00 (0.00) [0]
1062	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [8/2020]	604.00 (-) [604.00]	423.83 (0.00) [128]
1063	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [12/2019]	754.00 (-) [754.00]	1,363.43 (0.00) [81]
1064	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	1,275.00 (0.00) [-]
1065	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	303.71 (0.00) [0]
1066	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2019]	2,848.00 (-) [2,848.00]	1,159.10 (0.00) [69]
	<u>Shipping And Ports</u>				
1067	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	4,200.00 (-) [4,200.00]	1,256.55 (0.00) [0]
	<u>Telecommunications</u>				
1068	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	8,397.00 (11,330.00) [58]
1069	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-)	2,111.17 (-)	253.90 (-100.00)

			[0/0]	[2,011.17]	[0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1070	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1071	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [3,000.00]	759.42 (673.48) [79]
	<u>Road Transport And Highways</u>				
1072	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
1073	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
1074	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	3.27 (0.00) [0]
1075	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	116.06 (0.00) [0]
1076	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
1077	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	33.02 (0.00) [0]
1078	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	112.38 (0.00) [0]
1079	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
1080	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	4.38 (0.00) [0]
1081	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	2.11 (0.00) [0]
1082	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	6.86 (0.00) [0]
1083	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
1084	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
1085	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
1086	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	6.75 (0.00) [0]
1087	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	9.21 (0.00) [0]
1088	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	187.25 (0.00) [36]

1089	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	229.11 (0.00) [36]
1090	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	153.61 (0.00) [36]
1091	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (-) [336.25]	44.91 (0.00) [0]
1092	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	34.89 (0.00) [0]
1093	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	35.30 (0.00) [0]
1094	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1095	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1096	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	228.90 (0.00) [108]
1097	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2022]	172.08 (-) [172.08]	347.15 (0.00) [144]
1098	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2022]	479.15 (-) [479.15]	196.26 (0.00) [36]
1099	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	493.85 (0.00) [36]
1100	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	439.24 (0.00) [0]
1101	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2021]	479.53 (-) [479.53]	390.94 (0.00) [96]
1102	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	82.60 (0.00) [0]
1103	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2020]	337.66 (-) [337.66]	183.98 (0.00) [12]
1104	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2022]	457.77 (-) [457.77]	539.59 (0.00) [108]
1105	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	75.78 (0.00) [24]
1106	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2020]	302.96 (-) [302.96]	302.96 (0.00) [120]
1107	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,111.70 (0.00) [0]
1108	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-)	3,756.36 (-)	1,547.80 (0.00)

			[3/2026]	[3,756.36]	[0]
	<u>Mines</u>				
1109	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	102.61 (0.00) [0]
1110	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	31.92 (0.00) [0]
1111	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.30 (0.00) [0]
1112	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	318.13 (0.00) [0]
	<u>Petroleum</u>				
1113	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	34.73 (0.00) [0]
1114	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	0.00 (0.00) [0]
1115	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2020]	315.00 (-) [315.00]	110.38 (0.00) [-12]
1116	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	48.22 (0.00) [0]
1117	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	27.01 (0.00) [0]
1118	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	995.48 (0.00) [0]
1119	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	242.10 (0.00) [0]
1120	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	284.31 (0.00) [0]
1121	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [12/2019]	429.00 (-) [429.00]	306.24 (0.00) [11]
1122	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (-) [9/2022]	371.00 (-) [371.00]	0.00 (0.00) [0]
1123	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	36.68 (0.00) [0]
1124	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	8.85 (0.00) [0]
1125	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (6/2019) [7/2019]	3,150.00 (-) [3,150.00]	2,573.02 (0.00) [22]
	<u>Power</u>				
1126	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (6/2020) [6/2020]	12,532.44 (-) [13,740.53]	9,460.46 (1,208.09) [18]
1127	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (4/2019) [8/2019]	844.64 (-) [844.64]	430.71 (0.00) [4]

	<u>Railways</u>				
1128	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [1,120.00]	992.67 (177.05) [24]
1129	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2023]	843.04 (-) [843.04]	125.30 (0.00) [29]
1130	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2022]	1,172.92 (-) [1,172.92]	349.23 (0.00) [39]
1131	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
1132	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (6/2023) [6/2023]	5,200.00 (1,700.43) [1,700.43]	48.00 (-3,499.57) [39]
1133	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,729.78 (658.83) [27]
1134	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2023]	1,547.38 (1,547.38) [1,547.38]	320.30 (0.00) [12]
1135	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2021]	701.61 (-) [810.02]	116.91 (108.41) [28]
1136	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2019]	133.41 (207.00) [385.00]	386.28 (251.59) [129]
1137	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [12/2023]	2,923.13 (-) [3,798.80]	1,354.80 (875.67) [177]
1138	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2025]	2,361.74 (2,361.74) [2,361.74]	148.96 (0.00) [36]
1139	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [6/2020]	969.83 (1,312.96) [1,312.96]	494.27 (343.13) [3]
1140	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2020]	155.81 (-) [238.03]	224.63 (82.22) [0]
1141	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2021]	948.04 (-) [1,500.00]	1,249.76 (551.96) [12]
1142	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2022]	1,111.99 (-) [1,539.28]	879.96 (427.29) [37]
1143	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (-) [1,202.70]	861.32 (0.00) [82]
1144	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2023]	810.78 (-) [1,928.07]	624.68 (1,117.29) [21]
1145	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (-) [2,335.68]	546.57 (0.01) [0]
	<u>Road Transport And Highways</u>				
1146	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [4/2020]	1,282.94 (-) [1,282.94]	0.00 (0.00) [-]
1147	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42	9/2016	8/2019 (-)	2,510.04 (-)	0.00 (0.00)

	(NEW NH-55 IN THE S		[8/2019]	[2,510.04]	[0]
1148	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/	752.28	0.00
			(-)	(-)	(0.00)
			[11/2019]	[752.28]	[-]
1149	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016	319.80	268.27
			(-)	(320.00)	(0.20)
			[0/0]	[320.00]	[0]
1150	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016	319.80	268.01
			(-)	(-)	(0.00)
			[0/0]	[319.80]	[0]
1151	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/	1,069.65	0.00
			(-)	(-)	(0.00)
			[7/2019]	[1,069.65]	[-]
1152	PANIKHOLI-RIMOLI	3/2012	9/2014	1,410.00	1,930.61
			(-)	(-)	(0.00)
			[0/0]	[1,410.00]	[0]
1153	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/	1,008.96	468.18
			(-)	(-)	(0.00)
			[7/2020]	[1,008.96]	[-]
1154	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/	564.66	0.00
			(-)	(-)	(0.00)
			[8/2021]	[564.66]	[-]
1155	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017	476.56	0.00
			(-)	(-)	(0.00)
			[11/2020]	[476.56]	[40]
1156	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/	633.68	0.00
			(-)	(-)	(0.00)
			[0/0]	[633.68]	[0]
1157	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/	953.09	0.00
			(-)	(-)	(0.00)
			[5/2020]	[953.09]	[-]
1158	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/	668.86	0.00
			(-)	(-)	(0.00)
			[5/2020]	[668.86]	[-]
1159	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/	614.48	0.00
			(-)	(-)	(0.00)
			[8/2021]	[614.48]	[-]
1160	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017	342.05	258.91
			(-)	(-)	(0.00)
			[0/0]	[342.05]	[0]
1161	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/	1,522.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,522.00]	[0]
1162	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/	503.88	0.00
			(-)	(-)	(0.00)
			[6/2021]	[503.88]	[-]
1163	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020	1,288.07	221.91
			(-)	(-)	(131.93)
			[3/2021]	[1,420.00]	[12]
1164	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/	686.65	34.36
			(-)	(-)	(0.00)
			[7/2020]	[686.65]	[-]
1165	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/	686.65	29.45
			(-)	(-)	(0.00)
			[3/2020]	[686.65]	[-]
1166	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/	417.51	0.00
			(-)	(-)	(0.00)
			[0/0]	[417.51]	[0]
1167	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017	342.05	258.91
			(-)	(342.00)	(-0.05)
			[0/0]	[342.00]	[0]

1168	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [0/0]	999.00 (-) [999.00]	0.00 (0.00) [0]
1169	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [11/2019]	171.96 (172.00) [172.00]	88.30 (0.04) [41]
1170	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1171	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1172	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,864.34 (0.00) [0]
1173	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	0.00 (0.00) [-]
1174	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [12/2019]	191.50 (192.00) [192.00]	136.19 (0.50) [43]
1175	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1176	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1177	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1178	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [9/2019]	159.39 (-) [159.39]	210.29 (0.00) [22]
1179	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [12/2019]	191.08 (-) [191.08]	99.98 (0.00) [52]
1180	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	3/2015	10/2017 (-) [0/0]	226.31 (226.00) [226.31]	137.43 (0.00) [0]
1181	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA	3/2015	11/2015 (-) [0/0]	229.29 (-) [229.29]	163.40 (0.00) [0]
1182	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA	7/2013	10/2015 (-) [0/0]	251.92 (-) [251.92]	225.98 (0.00) [0]
1183	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA	7/2013	10/2015 (-) [0/0]	265.35 (-) [265.35]	247.56 (0.00) [0]
1184	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1185	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1186	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1187	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1188	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN	3/2018	8/2018	199.16	25.63

	THE STATE OF ODISHA		(-) [0/0]	(-) [199.16]	(0.00) [0]
1189	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1190	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	<u>Steel</u>				
1191	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (11/2019) [11/2019]	3,127.30 (-) [3,127.30]	2,970.60 (0.00) [19]
	<u>Urban Development</u>				
1192	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	6/2021 (-) [3/2022]	790.79 (-) [800.00]	2.56 (9.21) [9]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1193	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	101.91 (0.00) [0]
1194	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	107.64 (0.00) [0]
	<u>Health And Family Welfare</u>				
1195	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [8/2020]	703.00 (-) [703.00]	184.93 (0.00) [2]
1196	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [9/2019]	152.95 (-) [152.95]	118.23 (0.00) [19]
	<u>Railways</u>				
1197	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [205.22]	1.89 (0.00) [-]
	<u>Road Transport And Highways</u>				
1198	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (-) [1,169.61]	1,004.18 (0.00) [-]
1199	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	1,086.49 (0.00) [0]
1200	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (12/2019) [0/0]	889.24 (-) [904.82]	722.92 (15.58) [0]
1201	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (3/2020) [9/2019]	1,388.34 (2,525.80) [2,525.80]	1,449.00 (1,137.46) [0]
1202	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [4/2020]	754.54 (-) [756.27]	76.83 (1.73) [1]
1203	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (9/2019) [0/0]	766.36 (-) [766.36]	666.72 (0.00) [0]
1204	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (6/2020) [12/2019]	447.29 (746.43) [746.43]	596.50 (299.14) [24]
1205	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [1/2021]	261.76 (-) [261.76]	40.89 (0.00) [-]
1206	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	453.09

			(-) [3/2020]	(-) [479.00]	(0.00) [-]
1207	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [10/2019]	1,069.59 (-) [1,069.59]	629.87 (0.00) [0]
1208	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [1/2020]	196.05 (-) [196.05]	9.03 (0.00) [-]
1209	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (-) [199.90]	37.68 (0.00) [0]
1210	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [11/2020]	170.57 (-) [170.57]	46.23 (0.00) [0]
1211	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020 (-) [6/2020]	173.24 (-) [173.24]	10.97 (0.00) [0]
1212	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020 (-) [7/2020]	322.48 (-) [322.48]	48.73 (0.00) [0]
1213	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1214	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1215	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [8/2020]	293.10 (-) [293.10]	10.26 (0.00) [0]
1216	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	642.01 (0.00) [0]
	<u>Urban Development</u>				
1217	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (-) [9/2019]	388.00 (-) [488.28]	422.79 (100.28) [28]
1218	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [1/2021]	430.00 (-) [430.00]	60.28 (0.00) [8]
1219	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [2/2020]	294.00 (-) [294.00]	193.89 (0.00) [10]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1220	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2020]	12,320.00 (17,079.00) [17,079.00]	11,091.00 (4,759.00) [48]
	<u>Coal</u>				
1221	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	175.30 (0.00) [0]
1222	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Petroleum</u>				
1223	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1224	LPG BP PROJECT JODHPUR	3/2018	/ (-) [3/2021]	229.80 (-) [229.80]	69.10 (0.00) [-]

	<u>Power</u>				
1225	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (-) [7/2019]	1,429.38 (-) [1,429.38]	1,011.38 (0.00) [6]
	<u>Railways</u>				
1226	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/	873.71	4.25
			(-) [0/0]	(-) [1,980.21]	(1,106.50) [0]
1227	AJMER-BANGURGRAM	4/2011	11/2019 (-) [5/2020]	213.39 (-) [244.02]	260.89 (30.63) [6]
1228	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/	822.00	0.00
			(-) [0/0]	(-) [1,099.54]	(277.54) [0]
1229	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [12/2019]	242.09 (281.03) [410.00]	347.99 (167.91) [10]
1230	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2020]	246.08 (-) [348.55]	202.86 (102.47) [6]
1231	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [12/2021]	410.08 (780.98) [886.41]	517.39 (476.33) [34]
1232	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	35.36 (0.00) [1]
1233	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2020]	420.18 (-) [420.18]	152.83 (0.00) [3]
1234	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	438.08 (0.00) [24]
1235	PUSHKAR-MERTA	4/2013	/	323.00	0.00
			(-) [0/0]	(-) [432.22]	(109.22) [0]
1236	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [10/2019]	236.93 (-) [294.90]	136.88 (57.97) [12]
	<u>Road Transport And Highways</u>				
1237	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	605.33 (0.00) [0]
1238	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [0/0]	320.30 (-) [320.30]	206.14 (0.00) [0]
1239	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [0/0]	530.07 (-) [530.07]	556.02 (0.00) [0]
1240	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/	688.70	661.85
			(-) [11/2019]	(-) [688.70]	(0.00) [-]
1241	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/	1,031.95	367.00
			(-) [8/2020]	(-) [1,031.95]	(0.00) [-]
1242	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [0/0]	822.90 (-) [822.90]	834.75 (0.00) [0]
1243	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP.	10/2012	10/2013 (-) [0/0]	511.21 (-) [511.21]	814.79 (0.00) [0]
1244	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH	3/2018	/	1,158.35	121.47

	PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM		(-) [0/0]	(-) [1,158.35]	(0.00) [0]
1245	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC.	12/2015	10/2016 (-) [0/0]	621.43 (-) [621.43]	405.10 (0.00) [0]
1246	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE.	3/2016	9/2016 (-) [0/0]	155.77 (-) [155.77]	97.42 (0.00) [0]
1247	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [0/0]	163.95 (-) [163.95]	51.40 (0.00) [0]
1248	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	73.00 (0.00) [0]
1249	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1250	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	3/2009	9/2013 (-) [0/0]	501.00 (671.54) [671.54]	659.98 (170.54) [0]
1251	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [12/2020]	1,308.73 (-) [1,308.73]	0.00 (0.00) [-]
1252	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	216.17 (0.00) [5]
1253	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	0.00 (0.00) [3]
1254	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [11/2020]	964.17 (-) [964.17]	329.90 (0.00) [37]
1255	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1256	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP.	1/2012	1/2014 (-) [0/0]	378.07 (478.73) [478.73]	188.98 (100.66) [0]
1257	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC.	10/2014	1/2015 (-) [0/0]	382.81 (-) [382.81]	333.27 (0.00) [0]
1258	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [8/2019]	511.00 (-) [511.00]	492.00 (0.00) [70]
1259	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	2,323.04 (0.00) [0]
1260	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1261	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1262	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [12/2019]	1,100.19 (-) [1,100.19]	886.00 (0.00) [-]
1263	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	174.79 (0.00) [-]
1264	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-)	894.00 (-)	670.00 (0.00)

			[11/2019]	[894.00]	[-5]
1265	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (-) [0/0]	425.19 (-) [425.19]	297.72 (0.00) [0]
1266	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [0/0]	275.90 (-) [275.90]	257.52 (0.00) [0]
1267	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1268	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	571.06 (0.00) [3]
1269	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE	1/2017	7/2017 (-) [0/0]	163.54 (-) [163.54]	84.68 (0.00) [0]
1270	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN	1/2017	11/2017 (-) [0/0]	179.32 (-) [179.32]	93.64 (0.00) [0]
1271	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	0.00 (0.00) [0]
1272	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	176.00 (0.00) [0]
1273	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	242.53 (0.00) [-]
1274	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	97.97 (0.00) [0]
1275	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1276	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	224.68 (0.00) [0]
1277	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1278	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [7/2019]	621.43 (-) [621.43]	387.00 (0.00) [13]
1279	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	45.29 (0.00) [0]
	<u>Urban Development</u>				
1280	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [0/0]	189.00 (-) [189.00]	0.00 (0.00) [0]
1281	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (12/2019) [12/2019]	549.31 (559.47) [559.47]	326.38 (10.16) [5]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1282	SEVOK RANGPO, NEFR	4/2008	12/2015 (6/2021) [3/2020]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
1283	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (9/2017)	182.28 (269.14)	185.49 (86.86)

			[12/2019]	[269.14]	[82]
1284	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [76]
1285	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (203.26) [166.27]	132.27 (0.00) [0]
1286	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
1287	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	30.70 (0.00) [0]
1288	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	78.78 (0.00) [0]
1289	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1290	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [388.00]	78.33 (0.00) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1291	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	14,864.00 (0.00) [36]
1292	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2021]	3,492.00 (-) [6,840.00]	5,784.74 (3,348.00) [133]
	<u>Civil Aviation</u>				
1293	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [8/2022]	2,467.00 (-) [2,467.00]	213.17 (0.00) [6]
1294	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [10/2021]	951.28 (-) [951.28]	71.55 (0.00) [0]
	<u>Coal</u>				
1295	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [9/2019]	1,458.17 (-) [709.06]	448.19 (-749.11) [51]
1296	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [12/2019]	5,907.11 (7,080.41) [7,080.41]	6,567.64 (1,173.30) [48]
	<u>Mines</u>				
1297	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (-) [0/0]	166.62 (-) [166.62]	134.98 (0.00) [0]
	<u>Petroleum</u>				
1298	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	12.28 (0.00) [0]
1299	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	909.85 (0.00) [0]
1300	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	26.83 (0.00) [10]
1301	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2021]	4,497.00 (6,025.00) [6,025.00]	454.65 (1,528.00) [26]

1302	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1303	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2020) [5/2020]	650.82 (-) [390.52]	380.85 (-260.30) [14]
1304	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [10/2021]	678.00 (-) [678.00]	5.57 (0.00) [56]
1305	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	109.41 (0.00) [0]
1306	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.00 (0.00) [0]
	Power				
1307	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (6/2019) [8/2019]	1,779.29 (2,187.32) [2,187.32]	2,237.45 (408.03) [129]
1308	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [9/2019]	186.17 (-) [186.17]	103.12 (0.00) [2]
	Railways				
1309	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [257.00]	268.31 (0.00) [0]
1310	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1311	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (-) [3/2020]	931.98 (951.24) [951.24]	724.96 (19.26) [-]
1312	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	303.72 (357.96) [0]
1313	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1314	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [0/0]	495.74 (-) [734.01]	445.91 (238.27) [0]
1315	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2021]	760.00 (-) [1,182.31]	406.32 (422.31) [15]
1316	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	151.50 (285.59) [-]
1317	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [3/2022]	1,700.00 (-) [1,003.00]	167.73 (-697.00) [0]
1318	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2020]	724.69 (-) [2,072.50]	1,386.59 (1,347.81) [12]
1319	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	108.34 (44.41) [71]
1320	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]
1321	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-)	268.87 (-)	927.86 (681.13)

			[0/0]	[950.00]	[0]
1322	TIDIVANAM-NAGARI (NL)	9/2006	/	582.83	241.39
			(-)	(-)	(1,717.17)
			[0/0]	[2,300.00]	[0]
1323	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/	227.40	62.50
			(-)	(-)	(672.60)
			[0/0]	[900.00]	[0]
1324	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020	303.98	669.21
			(-)	(-)	(676.02)
			[3/2021]	[980.00]	[12]
1325	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024	1,567.00	0.00
			(-)	(-)	(0.00)
			[3/2026]	[1,567.00]	[24]
	Road Transport And Highways				
1326	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013	485.00	406.68
			(-)	(-)	(0.00)
			[0/0]	[485.00]	[0]
1327	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014	624.00	350.79
			(-)	(-)	(0.00)
			[0/0]	[624.00]	[0]
1328	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017	244.27	95.96
			(-)	(-)	(0.00)
			[11/2019]	[244.27]	[26]
1329	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017	1,227.87	0.00
			(-)	(-)	(0.00)
			[8/2020]	[1,227.87]	[35]
1330	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015	258.97	0.00
			(-)	(-)	(9.95)
			[0/0]	[268.92]	[0]
1331	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015	154.14	0.00
			(-)	(-)	(0.00)
			[0/0]	[154.14]	[0]
1332	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013	600.00	326.23
			(-)	(-)	(0.00)
			[0/0]	[600.00]	[0]
1333	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/	1,016.92	0.00
			(-)	(-)	(0.00)
			[4/2021]	[1,016.92]	[-]
1334	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017	1,387.11	966.02
			(-)	(-)	(0.00)
			[8/2019]	[1,387.11]	[21]
1335	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/	628.71	59.22
			(-)	(-)	(0.00)
			[11/2020]	[628.71]	[-]
1336	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/	2,065.96	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,065.96]	[0]
1337	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/	1,166.26	0.00
			(-)	(-)	(0.00)
			[2/2021]	[1,166.26]	[-]
1338	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016	641.17	405.31
			(-)	(-)	(0.00)
			[5/2020]	[641.17]	[46]
1339	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/	505.35	36.14
			(-)	(-)	(0.00)
			[11/2020]	[505.35]	[-]
1340	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017	1,176.37	0.00
			(-)	(-)	(0.00)
			[9/2020]	[1,176.37]	[37]
1341	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER	2/2016	8/2018	707.82	304.69
			(-)	(-)	(0.00)

	NHDP-PH		[3/2020]	[707.82]	[19]
1342	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	69.68 (0.00) [0]
1343	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [5/2020]	641.17 (-) [641.17]	431.21 (0.00) [22]
1344	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1345	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2020]	379.90 (-) [379.90]	92.44 (0.00) [-]
1346	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,330.29 (0.00) [0]
1347	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1348	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	627.66 (0.00) [0]
1349	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [0/0]	374.00 (-) [374.00]	237.00 (0.00) [0]
1350	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [633.55]	0.00 (0.00) [0]
1351	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [8/2019]	563.92 (-) [563.92]	96.48 (0.00) [20]
	<u>Shipping And Ports</u>				
1352	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017 (-) [5/2020]	600.00 (258.00) [257.90]	1.45 (-342.10) [29]
1353	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017 (-) [0/0]	244.50 (258.00) [275.98]	275.58 (31.48) [0]
1354	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006 (-) [0/0]	150.00 (-) [600.00]	139.80 (450.00) [0]
1355	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008 (-) [0/0]	2,427.40 (-) [2,427.40]	831.21 (0.00) [0]
	<u>Urban Development</u>				
1356	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [3/2020]	209.00 (-) [209.00]	127.69 (0.00) [5]
1357	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1358	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.77 (4,458.00) [0]
1359	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [11/2021]	348.77 (-) [348.77]	12.00 (0.00) [-]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1360	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-)	477.65 (-)	2.11 (0.00)

			[3/2020]	[477.65]	[0]
1361	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2020]	426.79 (-) [426.79]	0.72 (0.00) [24]
1362	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2021]	447.06 (-) [473.22]	18.35 (26.16) [72]
1363	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1364	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2021]	413.84 (-) [413.84]	54.00 (0.00) [24]
1365	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [9/2017]	397.09 (-) [442.42]	78.46 (45.33) [0]
1366	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [4/2017]	417.33 (-) [384.32]	92.60 (-33.01) [0]
1367	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	115.71 (-78.25) [72]
1368	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	170.60 (0.00) [0]
1369	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	343.10 (70.65) [132]
1370	RAMPURAM SHAFT BLOCK	8/2016	/ (3/2020) [0/0]	431.92 (-) [431.92]	0.00 (0.00) [0]
1371	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	7.23 (186.52) [72]
1372	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [12/2016]	430.45 (-) [415.37]	186.91 (-15.08) [0]
1373	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [12/2015]	365.01 (-) [365.01]	134.09 (0.00) [0]
1374	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2020]	209.78 (-) [209.78]	154.15 (0.00) [60]
1375	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2024]	249.03 (-) [448.86]	296.92 (199.83) [144]
1376	SRAVANAPALLI OPENCAST PROJECT	2/2018	/ (3/2021) [0/0]	412.70 (-) [412.70]	0.00 (0.00) [0]
1377	SRP OC-II EXPANSION PROJECT	11/2016	/ (4/2017) [0/0]	272.73 (-) [272.73]	144.07 (0.00) [0]
	<u>Petroleum</u>				
1378	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [4/2022]	611.00 (-) [611.00]	1.68 (0.00) [0]
	<u>Power</u>				
1379	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (6/2021) [6/2021]	10,598.98 (-) [10,598.98]	5,231.15 (0.00) [7]
	<u>Railways</u>				

1380	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2020]	632.68 (-) [816.55]	682.17 (183.87) [57]
1381	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	281.85 (0.00) [0]
1382	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	723.00 (997.09) [997.09]	0.00 (274.09) [0]
1383	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-) [0/0]	458.25 (-) [458.26]	3.83 (0.01) [0]
1384	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	3.67 (65.24) [0]
1385	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2023]	1,160.48 (-) [1,160.48]	288.38 (0.00) [156]
1386	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1387	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	364.69 (0.00) [0]
	<u>Road Transport And Highways</u>				
1388	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [12/2019]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [39]
1389	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [5/2020]	283.15 (-) [283.15]	32.04 (0.00) [0]
1390	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [7/2020]	626.76 (-) [626.76]	46.62 (0.00) [0]
1391	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	0.00 (0.00) [0]
1392	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1393	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	0.00 (0.00) [0]
1394	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	0.00 (0.00) [0]
1395	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	0.00 (0.00) [0]
1396	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (-) [0/0]	828.29 (-) [828.29]	0.00 (0.00) [0]
1397	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (-) [7/2019]	1,423.96 (-) [1,423.96]	691.30 (0.00) [8]
1398	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [7/2019]	192.67 (-) [192.67]	0.00 (0.00) [0]
1399	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [10/2019]	605.08 (-) [605.08]	213.00 (0.00) [0]

1400	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [4/2020]	426.52 (-) [426.52]	134.38 (0.00) [0]
1401	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1402	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [11/2019]	294.13 (-) [294.13]	23.54 (0.00) [0]
1403	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [11/2019]	220.28 (-) [220.28]	7.40 (0.00) [0]
1404	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [9/2020]	322.81 (-) [322.81]	0.34 (0.00) [0]
1405	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [313.27]	0.00 (17.80) [0]
1406	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [12/2019]	248.83 (-) [248.83]	79.02 (0.00) [9]
1407	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [12/2019]	298.32 (-) [298.32]	62.22 (0.00) [10]
1408	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [12/2019]	230.03 (-) [230.03]	80.71 (0.00) [0]
1409	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [6/2020]	206.13 (-) [206.13]	94.93 (0.00) [0]
1410	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	0.00 (0.00) [0]
1411	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [10/2019]	196.52 (-) [196.52]	92.88 (0.00) [0]
1412	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019 (-) [12/2019]	283.00 (-) [283.00]	121.47 (0.00) [0]
1413	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [7/2019]	244.54 (-) [244.54]	122.31 (0.00) [2]
1414	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT	1/2017	5/2019 (-) [8/2019]	359.27 (-) [359.27]	200.24 (0.00) [3]
1415	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (-) [12/2019]	300.00 (-) [300.00]	83.83 (0.00) [7]
	<u>Urban Development</u>				
1416	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (2/2017) [5/2021]	209.84 (-) [209.84]	35.79 (0.00) [14]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1417	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [12/2019]	338.93 (-) [339.00]	213.50 (0.07) [6]
	<u>Railways</u>				
1418	AGARTALA-AKHAURA NL	4/2012	3/2020 (3/2020) [12/2021]	569.63 (569.63) [650.00]	45.24 (80.37) [21]

	Road Transport And Highways				
1419	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	297.12 (0.00) [0]
1420	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	14.17 (0.00) [0]
	Urban Development				
1421	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1422	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1423	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	UTTAR PRADESH				
	Civil Aviation				
1424	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2021]	1,383.00 (-) [1,383.00]	210.62 (0.00) [0]
	Coal				
1425	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	6,860.71 (0.80) [0]
	Health And Family Welfare				
1426	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [6/2020]	785.00 (-) [785.00]	244.66 (0.00) [2]
1427	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	99.26 (0.00) [-]
	Petroleum				
1428	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	9/2019 (-) [9/2019]	204.00 (-) [204.00]	132.24 (0.00) [0]
1429	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	15.01 (0.00) [0]
1430	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	376.04 (0.00) [0]
1431	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	121.99 (0.00) [0]
1432	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	0.71 (0.00) [0]
1433	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	13.19 (0.00) [0]
1434	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY	8/2016	11/2019 (-) [11/2019]	154.84 (-) [154.84]	114.80 (0.00) [0]
1435	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	39.76 (0.00) [3]
	Power				
1436	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-)	587.44 (-)	250.00 (0.00)

			[9/2020]	[587.44]	[0]
1437	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (-) [11/2020]	349.00 (-) [349.00]	125.00 (0.00) [0]
1438	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (-) [10/2019]	195.42 (-) [294.60]	295.73 (99.18) [68]
1439	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [9/2023]	11,089.42 (-) [11,089.42]	509.30 (0.00) [0]
1440	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [6/2020]	9,750.89 (-) [12,176.28]	9,703.00 (2,425.39) [40]
1441	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (6/2020) [6/2020]	9,188.98 (-) [9,188.98]	6,334.35 (0.00) [11]
	<u>Railways</u>				
1442	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1443	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2022]	600.00 (-) [600.00]	15.03 (0.00) [0]
1444	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1445	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	1,011.48 (0.00) [3]
1446	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	11.93 (111.84) [0]
1447	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1448	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1449	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (3/2015) [3/2015]	120.00 (314.09) [346.00]	345.51 (226.00) [0]
1450	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1451	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [6/2020]	213.00 (-) [213.35]	5.45 (0.35) [50]
1452	JHANSI BINA DOUBLING	9/2016	3/2021 (3/2023) [3/2021]	2,001.00 (-) [2,001.00]	416.59 (0.00) [0]
1453	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	3.90 (0.00) [0]
1454	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1455	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [12/2019]	528.57 (-) [528.57]	88.93 (0.00) [9]
1456	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-)	927.01 (-)	1,124.56 (272.99)

			[3/2020]	[1,200.00]	[12]
1457	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (3/2020) [3/2020]	668.70 (680.00) [680.00]	330.00 (11.30) [0]
1458	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	462.05 (0.00) [21]
1459	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1460	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1461	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [1/2020]	622.50 (427.00) [426.74]	163.75 (-195.76) [33]
1462	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	474.57 (0.00) [12]
1463	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [12/2019]	1,295.42 (-) [1,295.42]	291.45 (0.00) [-27]
1464	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	3.12 (-149.01) [16]
1465	UNCHAHAH-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,230.00]	103.17 (1.00) [-]
1466	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [750.56]	327.46 (-193.04) [33]
	Road Transport And Highways				
1467	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [11/2018]	368.73 (-) [368.73]	232.93 (0.00) [0]
1468	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
1469	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	433.68 (0.00) [0]
1470	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	633.24 (0.00) [0]
1471	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [291.36]	459.07 (0.00) [0]
1472	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	207.94 (0.00) [0]
1473	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [11/2019]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [7]
1474	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,120.57]	0.00 (0.00) [0]
1475	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [2/2020]	1,668.00 (-) [1,668.00]	938.03 (0.00) [-]
1476	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-)	611.65 (-)	728.24 (0.00)

			[0/0]	[611.65]	[0]
1477	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/	1,408.00	21.46
			(-)	(-)	(0.00)
			[7/2020]	[1,408.00]	[-]
1478	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/	1,737.00	278.92
			(-)	(-)	(0.00)
			[4/2020]	[1,737.00]	[-]
1479	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/	1,404.50	92.37
			(-)	(-)	(0.00)
			[0/0]	[1,404.50]	[0]
1480	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]	3/2016	4/2019	1,587.49	276.87
			(-)	(-)	(0.00)
			[0/0]	[1,587.49]	[0]
1481	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/	1,396.74	227.26
			(-)	(-)	(0.00)
			[0/0]	[1,396.74]	[0]
1482	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019	1,657.20	2,345.00
			(-)	(-)	(0.00)
			[0/0]	[1,657.20]	[0]
1483	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020	2,064.99	1,653.62
			(-)	(-)	(382.01)
			[3/2020]	[2,447.00]	[0]
1484	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN)	12/2017	/	207.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[207.00]	[0]
1485	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019	676.73	632.21
			(-)	(-)	(0.00)
			[0/0]	[676.73]	[0]
1486	BAREILY-SITAPUR (NH-24)	3/2011	9/2013	1,046.00	805.19
			(-)	(-)	(0.00)
			[0/0]	[1,046.00]	[0]
1487	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/	972.77	0.00
			(-)	(-)	(0.00)
			[0/0]	[972.77]	[0]
1488	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/	534.55	433.62
			(-)	(-)	(0.00)
			[0/0]	[534.55]	[0]
1489	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/	305.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[305.00]	[0]
1490	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/	1,117.84	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,117.84]	[0]
1491	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/	450.68	397.62
			(-)	(-)	(0.00)
			[0/0]	[450.68]	[0]
1492	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016	282.41	155.53
			(-)	(-)	(0.00)
			[0/0]	[282.41]	[0]
1493	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019	1,081.57	988.72
			(-)	(-)	(0.00)
			[0/0]	[1,081.57]	[0]
1494	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/	1,232.21	410.09
			(-)	(-)	(0.00)
			[5/2020]	[1,232.21]	[-]
1495	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020	1,989.00	842.34
			(-)	(-)	(0.00)
			[5/2020]	[1,989.00]	[2]
1496	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018	785.78	839.63
			(-)	(-)	(0.00)
			[0/0]	[785.78]	[0]

1497	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	1,998.25 (0.00) [0]
1498	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	0.00 (0.00) [0]
1499	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	0.00 (0.00) [0]
1500	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [925.40]	0.00 (0.00) [0]
1501	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	549.07 (0.00) [0]
1502	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	464.05 (0.00) [0]
1503	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1504	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1505	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1506	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [11/2020]	1,373.28 (-) [1,373.28]	571.96 (0.00) [8]
1507	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [8/2020]	1,184.71 (-) [1,310.00]	563.15 (125.29) [5]
1508	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [0/0]	899.00 (-) [899.00]	532.53 (0.00) [0]
1509	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1510	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [683.24]	623.53 (0.00) [0]
1511	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [0/0]	326.99 (327.00) [326.99]	0.00 (0.00) [0]
1512	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [1,025.80]	46.29 (0.00) [0]
1513	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [1,115.28]	113.90 (0.00) [0]
1514	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	2/2019 (-) [0/0]	239.63 (-) [239.63]	197.77 (0.00) [0]
1515	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [11/2019]	208.50 (-) [208.50]	102.98 (0.00) [0]
1516	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [7/2019]	445.89 (653.00) [653.00]	454.41 (207.11) [28]
1517	REHABILITATION AND UPGRADATION OF PRATAPGARH-	3/2016	1/2020	599.34	376.71

	ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F		(-) [1/2020]	(-) [599.34]	(0.00) [0]
1518	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [0/0]	249.50 (-) [249.50]	190.10 (0.00) [0]
1519	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [9/2019]	215.16 (215.00) [215.16]	125.09 (0.00) [0]
1520	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [1/2020]	240.30 (240.00) [240.30]	171.00 (0.00) [0]
1521	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [3/2020]	218.94 (219.00) [218.94]	67.87 (0.00) [0]
1522	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [7/2019]	176.94 (177.00) [176.94]	132.45 (0.00) [9]
1523	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [8/2019]	445.89 (-) [653.29]	454.49 (207.40) [29]
1524	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1525	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1526	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [7/2019]	164.54 (165.00) [164.54]	86.63 (0.00) [47]
1527	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [9/2019]	164.54 (-) [164.54]	86.63 (0.00) [49]
	<u>Steel</u>				
1528	FORGED WHEEL PLANT	4/2014	9/2018 (9/2019) [9/2019]	1,682.85 (-) [1,682.85]	1,155.53 (0.00) [12]
	<u>Urban Development</u>				
1529	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	32.00 (0.00) [0]
1530	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1531	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2020]	353.27 (-) [353.27]	114.29 (0.00) [0]
	<u>Petroleum</u>				
1532	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [10/2020]	160.10 (-) [160.10]	38.51 (0.00) [8]
	<u>Power</u>				
1533	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	148.91 (274.07) [0]
1534	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	236.30 (0.00) [0]
1535	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020)	2,978.48 (5,867.38)	4,110.76 (2,888.90)

			[12/2020]	[5,867.38]	[93]
1536	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2022]	1,657.00 (-) [5,024.35]	2,969.55 (3,367.35) [76]
1537	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2022]	2,491.58 (-) [4,397.80]	1,718.70 (1,906.22) [114]
	<u>Railways</u>				
1538	HARIDWAR-LAKSAR	4/2012	/ (-) [6/2020]	219.83 (-) [346.63]	229.48 (126.80) [-]
1539	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1540	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2026]	16,216.00 (-) [16,216.00]	1,492.47 (0.00) [15]
	<u>Road Transport And Highways</u>				
1541	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	75.19 (0.00) [0]
1542	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	76.48 (0.00) [0]
1543	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [2/2020]	605.84 (-) [722.46]	722.46 (116.62) [19]
1544	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	610.71 (0.00) [-]
1545	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	8.68 (0.00) [0]
1546	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	92.26 (0.00) [0]
1547	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1548	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [10/2019]	720.00 (-) [720.00]	278.01 (0.00) [-]
1549	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [2/2020]	478.51 (-) [478.00]	409.17 (-0.51) [76]
1550	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	59.44 (0.00) [0]
1551	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [283.51]	126.38 (0.00) [0]
1552	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	62.79 (0.00) [0]
1553	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [12/2019]	282.08 (-) [282.08]	77.05 (0.00) [6]
1554	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	31.00 (0.00) [0]
1555	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT	2/2018	2/2020	418.88	88.00

	OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR		(-) [2/2020]	(-) [418.88]	(0.00) [0]
1556	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	144.27 (0.00) [0]
1557	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [12/2019]	234.88 (-) [208.89]	118.26 (-25.99) [24]
1558	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1559	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1560	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1561	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1562	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (-) [11/2021]	264.99 (-) [264.99]	0.42 (0.00) [0]
1563	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	1/2016	3/2020 (-) [12/2020]	219.91 (-) [219.91]	65.45 (0.00) [9]
	<u>Coal</u>				
1564	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	314.86 (0.00) [0]
1565	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.00 (0.00) [0]
1566	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1567	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	486.13 (0.00) [24]
1568	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.00 (0.00) [0]
	<u>Health And Family Welfare</u>				
1569	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [0/0]	244.00 (-) [244.00]	241.39 (0.00) [0]
1570	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [2/2020]	651.99 (-) [651.99]	112.82 (0.00) [-]
1571	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2020]	355.15 (-) [355.15]	148.84 (0.00) [12]
	<u>Petroleum</u>				
1572	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,696.00]	108.51 (-16.00) [-15]
1573	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-)	2,934.40 (-)	1,569.01 (0.00)

			[9/2019]	[2,934.40]	[0]
1574	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	171.48 (0.00) [0]
1575	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1576	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (11/2019) [11/2019]	694.00 (1,097.54) [1,097.54]	693.14 (403.54) [13]
1577	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [3/2021]	163.02 (-) [163.02]	44.00 (0.00) [11]
	<u>Power</u>				
1578	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (1/2020) [1/2020]	454.11 (-) [454.11]	287.52 (0.00) [21]
1579	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,592.34]	473.97 (210.50) [29]
	<u>Railways</u>				
1580	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [0/0]	1,027.40 (-) [2,373.00]	485.04 (1,345.60) [0]
1581	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (12/2017) [3/2025]	1,106.62 (-) [1,091.59]	827.99 (-15.03) [171]
1582	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [9/2021]	255.64 (-) [272.20]	148.03 (16.56) [-]
1583	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [0/0]	267.37 (-) [620.00]	40.99 (352.63) [0]
1584	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1585	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1586	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1587	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (3/2022) [3/2022]	221.42 (-) [380.00]	38.18 (158.58) [-]
1588	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (-) [614.00]	274.97 (316.68) [12]
1589	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,300.00]	1,087.60 (919.40) [0]
1590	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	186.09 (9.73) [-21]
1591	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.13 (435.44) [141]
1592	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [2,913.50]	843.96 (-0.01) [108]
1593	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY	4/2010	3/2016	2,397.72	197.20

	FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)		(-) [0/0]	(-) [2,397.72]	(0.00) [0]
1594	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,127.22 (307.50) [108]
1595	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	862.50 (430.57) [72]
1596	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
Road Transport And Highways					
1597	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [12/2019]	1,083.00 (-) [1,083.00]	26.64 (0.00) [18]
1598	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2020]	998.79 (-) [998.79]	1,775.04 (0.00) [82]
1599	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [12/2019]	1,078.84 (-) [1,078.84]	2,173.80 (0.00) [76]
1600	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [12/2019]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [63]
1601	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2020]	361.15 (-) [361.15]	144.71 (0.00) [-]
1602	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	28.21 (0.00) [0]
1603	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (11/2019) [11/2019]	271.17 (291.20) [291.20]	79.43 (20.03) [12]
1604	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [8/2021]	160.27 (213.97) [213.97]	20.11 (53.70) [24]
1605	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [12/2019]	229.37 (-) [229.37]	78.31 (0.00) [13]
1606	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [8/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [24]
1607	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [10/2020]	254.30 (254.30) [254.30]	20.09 (0.00) [0]
1608	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (-) [767.03]	502.91 (0.00) [13]
1609	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [6/2020]	702.16 (-) [702.16]	733.33 (0.00) [71]
1610	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	636.67 (120.10) [0]
1611	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	703.86 (114.56) [0]
1612	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,261.98]	0.00 (0.00) [0]
1613	REHABILITATION AND UPGRADATION OF PUNDIBARI TO	4/2014	8/2017	279.70	314.63

	BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7		(7/2019) [7/2019]	(398.52) [398.52]	(118.82) [23]
1614	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (-) [0/0]	396.86 (396.86) [396.86]	179.31 (0.00) [0]
1615	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1616	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [6/2019]	1,665.00 (-) [1,665.00]	3,059.39 (0.00) [0]
1617	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [0/0]	202.69 (202.69) [202.69]	93.60 (0.00) [0]
1618	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [0/0]	218.70 (218.70) [218.70]	18.22 (0.00) [0]
1619	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [0/0]	426.18 (426.18) [426.18]	217.82 (0.00) [0]
	<u>Steel</u>				
1620	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [9/2020]	263.36 (-) [263.36]	2.89 (0.00) [0]
	<u>Urban Development</u>				
1621	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [10/2019]	156.57 (-) [156.57]	156.13 (0.00) [38]
1622	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1623	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	126.07 (0.00) [15]
	Total			19,33,390.22 (4,47,897.68) [23,21,502.84]	9,47,571.45 (3,88,112.62)

North East Central Sector Project's Details

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (As on 31.07.2019)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	ARUNACHAL PRADESH				
	Power				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (8/2019) [8/2019]	2,496.90 (7,419.34) [7,419.34]	7,494.35 (4,922.44) [116]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,927.32 (13,211.01) [0]
	Road Transport And Highways				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	108.75 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	240.21 (0.00) [21]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	174.80 (0.00) [15]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
7	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [0/0]	210.50 (-) [210.50]	114.37 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	90.29 (0.00) [0]
9	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	0.00 (0.00) [0]
10	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	143.01 (0.00) [0]
11	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	72.97 (0.00) [0]
12	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	125.96 (0.00) [0]
13	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	30.88 (0.00) [0]
14	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	17.42 (16.07) [36]
15	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [9/2020]	245.79 (-) [245.79]	98.37 (0.00) [-]
16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM.	4/2016	10/2016	198.00	195.67

	37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.		(-) [10/2019]	(-) [198.00]	(0.00) [36]
17	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	66.17 (0.00) [0]
18	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	154.14 (0.00) [0]
19	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	211.21 (0.00) [60]
20	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (2/2018) [2/2021]	167.28 (167.28) [167.28]	18.70 (0.00) [46]
21	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (2/2018) [2/2021]	216.71 (216.71) [216.71]	15.77 (0.00) [46]
22	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
23	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [12/2020]	434.06 (-) [434.06]	126.58 (0.00) [-]
24	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	46.85 (0.00) [47]
25	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	37.30 (0.00) [0]
26	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	48.16 (0.00) [0]
27	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	56.15 (0.00) [0]
28	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	24.14 (0.00) [0]
29	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (389.45) [389.45]	275.19 (182.42) [0]
30	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	13.73 (0.00) [46]
31	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	28.67 (0.00) [46]
32	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
33	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
34	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
35	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	0.00 (0.00) [-]
36	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM	2/2017	/ (4/2019)	176.12 (176.12)	0.00 (0.00)

	35.1		[4/2022]	[176.12]	[-]
37	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D)	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	9.65 (0.00) [-]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D)	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	6.19 (0.00) [-]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
39	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	<u>Health And Family Welfare</u>				
40	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
41	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
42	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
43	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	178.05 (0.00) [0]
44	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	531.40 (0.00) [0]
45	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	3.30 (0.00) [0]
46	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
47	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (345.92) [345.92]	145.60 (142.98) [70]
48	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	250.31 (0.00) [1]
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [682.90]	7.60 (138.99) [0]
50	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,526.40 (0.00) [0]
51	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	157.02 (15.64) [0]
52	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
53	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	691.97 (414.00) [12]
54	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	582.27 (-50.32) [-24]
55	DIGARU-HOJAI (102 KM)	4/2015	3/2021	870.96	455.80

			(-) [3/2021]	(-) [2,136.01]	(1,265.05) [0]
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	606.82 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
57	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	201.56 (0.00) [0]
58	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
59	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
60	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	61.74 (0.00) [0]
61	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	50.39 (0.00) [0]
62	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	356.31 (0.00) [0]
63	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	15.27 (0.00) [0]
64	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
65	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	6.27 (0.00) [0]
66	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	48.09 (0.00) [0]
67	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [8/2019]	217.61 (-) [217.61]	451.15 (0.00) [112]
68	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
69	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.68 (7.98) [0]
70	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	304.28 (0.00) [0]
71	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	61.74 (0.00) [0]
72	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	54.31 (0.00) [-]
73	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	6.62 (0.00) [0]
74	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	292.24 (0.00) [0]
75	FOUR LANING OF NUMALIGARH TO JORHAT SECTION	5/2015	5/2018	454.89	120.86

	FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM		(-) [0/0]	(-) [454.89]	(0.00) [0]
76	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [280.00]	472.00 (0.00) [0]
77	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
78	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
79	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [8/2019]	199.81 (-) [385.13]	319.96 (185.32) [124]
80	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [167.64]	268.94 (0.00) [0]
81	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2019]	208.00 (-) [230.00]	337.08 (22.00) [140]
82	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	326.35 (0.00) [136]
83	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [9/2019]	245.00 (-) [174.34]	224.28 (-70.66) [138]
84	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (307.47) [307.47]	239.76 (89.16) [0]
85	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
86	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
87	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (13,809.00) [12,524.00]	8,821.88 (8,069.83) [108]
	<u>Road Transport And Highways</u>				
88	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	74.49 (0.00) [0]
89	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	119.56 (-59.80) [36]
	<u>Urban Development</u>				
90	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
91	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
92	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.66 (5,093.54) [0]

	<u>Road Transport And Highways</u>				
93	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [7/2019]	306.28 (-) [306.28]	42.66 (0.00) [2]
94	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [9/2019]	479.20 (-) [479.20]	475.02 (0.00) [16]
95	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	<u>Urban Development</u>				
96	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
97	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	2,935.76 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
98	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	296.28 (182.95) [116]
99	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	269.07 (118.65) [63]
100	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
101	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
102	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
103	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
104	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
105	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
106	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
107	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
108	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
109	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	789.85 (368.26) [105]
	<u>NAGALAND</u>				
	<u>Railways</u>				
110	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]

111	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [3,000.00]	759.42 (673.48) [79]
	Road Transport And Highways				
112	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	3.27 (0.00) [0]
115	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	116.06 (0.00) [0]
116	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
117	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	33.02 (0.00) [0]
118	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	112.38 (0.00) [0]
119	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
120	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	4.38 (0.00) [0]
121	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	2.11 (0.00) [0]
122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	6.86 (0.00) [0]
123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	6.75 (0.00) [0]
127	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	9.21 (0.00) [0]
128	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	187.25 (0.00) [36]
129	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	229.11 (0.00) [36]
130	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	153.61 (0.00) [36]

131	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (-) [336.25]	44.91 (0.00) [0]
132	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	34.89 (0.00) [0]
133	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	35.30 (0.00) [0]
134	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
135	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
136	SEVOK RANGPO, NEFR	4/2008	12/2015 (6/2021) [3/2020]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
137	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (9/2017) [12/2019]	182.28 (269.14) [269.14]	185.49 (86.86) [82]
138	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [76]
139	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (203.26) [166.27]	132.27 (0.00) [0]
140	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
141	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	30.70 (0.00) [0]
142	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	78.78 (0.00) [0]
143	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
144	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [388.00]	78.33 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
145	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [12/2019]	338.93 (-) [339.00]	213.50 (0.07) [6]
	<u>Railways</u>				
146	AGARTALA-AKHAURA NL	4/2012	3/2020 (3/2020) [12/2021]	569.63 (569.63) [650.00]	45.24 (80.37) [21]
	<u>Road Transport And Highways</u>				
147	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	297.12 (0.00) [0]
148	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	14.17 (0.00) [0]

	<u>Urban Development</u>				
149	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
150	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
151	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			81,555.91 (34,034.20) [1,24,114.77]	53,635.41 (42,558.86)
