

दलनह; {k= dh ifj;k t ukvk
CENTRAL SECTOR PROJECTS

**₹150 dj kM vkj vf/kd ykxr okyh
(₹ 150 Crore and above)**

**356oh ¶Yk'k fj ikV@356th Flash Report
t u] 2015@June, 2015**



Hkkjr ljdkj / Government of India

l kf[; dh vkj dk; Øe dk; kUo; u e=ky ;

Ministry of Statistics and Programme Implementation

**vk/kkjh ljpuk vkj ifj;k t uk i ck/ku i Hkkx
Infrastructure and Project Monitoring Division**

l jnkj i Vy Hkou] l ln ekx]

Sardar Patel Bhavan, Sansad Marg,

ub] fnYyh / New Delhi-110001

oc l kbV / Website- www.cspm.gov.in

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents	
	Pages
Executive Summary Hindi	1-22
Executive Summary English	23-39
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2014-2015	40-41
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2014-2015	42-42
Summary of projects	43-57
Graphical Presentation of All Projects	58-70
Sector wise Analysis of Projects	71-106
Sector wise Graph	107-118
Annexures	119-119
Status of central sector projects costing Rs.150 Crore and above	120-120
List of projects in which expenditure is more than approved cost	121-130
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	131-141
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	142-146
List of Projects habving cost overruns with respect to Anticipated/Cumulative ependiture	147-159
Details of Delayed Projects w.r.t. Original and Revised Schedule	160-189
Details of Projects Ahead of Schedule w.r.t. Original Schedule	190-190
Details of On Schedule Projects w.r.t. Original Schedule	191-197
Details of projects without milestones w.r.t. original schedule	198-220
Details of Projects Without Date of Commissioning	221-233
Details of projects without original Date of Commissioning	234-235
List of ongoing projects having cost overrun w.r.t. to revised schedule	236-245
List of Delayed Projects w.r.t. Latest Schedule	246-259
List of Projects Ahead of Schedule w.r.t. Latest Schedule	260-260
List of Projects on schedule w.r.t. Latest Schedule	261-269
Details Of Central Sector Projects Showing Time Overruns Of 6 Months And More	270-283
Details of Central Sector Projects Showing Cost Overruns Of More Than Rs. 100 Crore	284-292
Details Of Central Sector Projects Showing Time Overruns Of 6 Months and More and cost overruns of Rs. 100 Crore and above	293-297

कार्यकारी सारांश

1. जून, 2015 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 770 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जून 2015 के दौरान, 6 परियोजनाओं (इस्पात, विद्युत तथा रेलवे क्षेत्र प्रत्येक की 2 परियोजनाएं) के पूरा होने की सूचना दी गई है।
2. संदर्भाधीन माह के दौरान, 770 परियोजनाओं में से, 313 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ है तथा 38 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 38 परियोजनाओं में से, 17 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	रेलवे	296	34	4	3
2.	सड़क परिवहन एवं राजमार्ग	137	90	10	4
3.	विद्युत	110	58	1	0
4.	पेट्रोलियम	71	48	9	6
5.	कोयला	76	45	7	2
6.	शहरी विकास	30	13	0	0
7.	इस्पात	26	14	4	0
8.	नागर विमानन	7	3	1	0
9.	पोत परिवहन एवं पत्तन	7	1	0	0
10.	परमाणु ऊर्जा	4	4	1	1
11.	दूरसंचार	2	1	0	0
12.	उर्वरक	1	0	0	0
13.	खदान	1	0	0	0
14.	पेट्रोसायन	1	1	1	1
15.	भारी उद्योग	1	1	0	0
कुल		770	313	38	17

3. 770 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹ 10,67,193.26 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 12,75,501.50 करोड़ होने की संभावना है, जो ₹ 2,08,308.24 करोड़ (मूल लागत का 19.52%) की समग्र लागत वृद्धि को दर्शाता है। जून, 2015 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,57,866.01 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 43.74% है।

लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(30.06.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	लागत वृद्धि(%)
	परमाणु ऊर्जा				
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
2	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	31.12
	नागर विमानन				
3	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	15.77
4	विभिन्न हवाई अड्डों पर 56 सं.एयरफील्ड फायर टैंडर्स की आपूर्ति	10/2012	217.60	244.10	12.18
5	चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	8.19
	कोयला				
6	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
7	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	76.47
8	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	34.63
9	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
10	मनुगुरु ओसी परियोजना की आरएफआर	11/2012	430.45	486.27	12.97
	भारी उद्योग				
11	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
	पेट्रोरसायन				
12	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	80.08

पेट्रोलियम					
13	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	820.20
14	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	75.35
15	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
16	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
17	कोरबा में विपणन टीओपी	01/2011	141.86	219.08	54.43
विद्युत					
18	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
19	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	159.38
20	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	159.15
21	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी)	09/2003	6285.33	15300.00	143.42
22	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.68	139.35
रेलवे					
23	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
24	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
25	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
26	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
27	तिरुचिरापल्लई-नागोरे-करायकल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
सड़क परिवहन एवं राजमार्ग					
28	पानीपत-जालंधर छः लेन (96 किमी. से 387.1 किमी.)	05/2009	1108.00	2288.00	106.50
29	मैबंग से लुमडिंग (एस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
30	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	363.74	85.58
31	हरंगाजो से मैबंग किमी 164.08-190.587 एनएच-54	12/2003	212.00	386.10	82.12
32	मैबंग से लुमडिंग (एस-24), 111.000 किमी.	12/2003	155.04	280.13	80.68

	से 126.450 किमी.				
	पोत परिवहन एवं पत्तन				
33	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
34	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
35	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	51.92
36	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	18.89
	इस्पात				
37	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
38	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	41.41
	शहरी विकास				
39	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. पूर्ण रूप से लागतवृद्धि की अधिकतम वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार है:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30.06.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	4099.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविति,	09/2003	3492.00	5677.00	2185.00

	500 एमडब्ल्यूई)				
	नागर विमानन				
3	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	52.92
4	चंडीगढ़ अंतरराष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	37.00
5	विभिन्न हवाई अड्डों पर 56 सं.एयरफील्ड फायर टैंडरर्स की आपूर्ति	10/2012	217.60	244.10	26.50
	कोयला				
6	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	1698.20
7	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	1552.99
8	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
9	मनुगुरु ओसी परियोजना का आरएफआर	08/2008	469.78	706.40	236.62
10	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	48.00
	भारी उद्योग				
11	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
	पेट्रोसायन				
12	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	4372.91
	पेट्रोलियम				
13	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
14	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	3525.39
15	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
16	बेसिन क्षेत्र के समन्वित विकास	12/2012	3513.07	4619.94	1106.87
	विद्युत				
17	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	15300.00	9014.67

18	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
19	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	3979.44
20	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7818.68	3899.09
21	बाढ़ एसटीपीपी चरण-II	02/2008	7341.04	10852.46	3511.42
रेलवे					
22	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
23	जिरिबाम से इम्फाल (तुपुई)(एनएल)(एनईएफआर)	04/2003	727.56	6570.75	5843.19
24	लुमडिंग-सिलचर जिरिबाम, बदरपुर-बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
25	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
26	सीवोक रंगपो, एनईएफआर	04/2008	1339.48	4190.00	2850.52
सड़क परिवहन एवं राजमार्ग					
27	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
28	मैंबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
29	हरंगाजो से मैंबंग किमी.164.08-190.587 किमी. एनएच-54	12/2003	212.00	386.10	174.10
30	हरंगाजो से मैंबंग, एनएच-54	12/2003	196.00	363.74	167.74
31	मैंबंग से लुमडिंग (एएस-24), 111.000 किमी.से 126.450 किमी.	12/2003	155.04	280.13	125.09
पोत परिवहन एवं पत्तन					
32	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
33	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
34	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	232.00
35	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	127.55
इस्पात					

36	तरल इस्पात क्षमता के विस्तार 3 एमटी से 6.3 एमटी तक (आरआईएनएल)	10/2005	8692.00	12291.00	3599.00
37	सिंटर मंशौन -1 और 2का सुधार	12/2009	343.00	488.40	145.40
	शहरी विकास				
38	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 770 परियोजनाओं में से, 4 परियोजनाएं समय से पहले चल रही हैं, 125 समय पर तथा 313 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 278 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 30 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 298 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 313 विलंबित परियोजनाओं में से, 52 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 67 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 129 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 65 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30.06.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2008	10/2015	12/2001	82
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2010	09/2016	09/2003	72
3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	12/2015	10/2017	10/2009	22
4	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	12/2016	05/2018	10/2009	17
	नागर विमानन				

5	पाकयांग (सिक्किम) हवाई अड्डा में नए हवाई अड्डे का निर्माण	01/2011	06/2017	01/2009	77
6	नया अंतर्राष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2012	03/2015	05/2010	34
7	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	03/2014	05/2015	02/2010	14
8	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर निविदाओं की आपूर्ति	03/2015	09/2015	10/2012	6
9	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	03/2015	07/2015	02/2011	4
कोयला					
10	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	03/2010	03/2017	12/2007	84
11	कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड)	03/2010	03/2017	01/2005	84
12	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	06/2009	07/2015	10/2004	73
13	झंझरा आर-VI सीम पीएसएलडब्ल्यू	03/2011	03/2017	11/2006	72
14	गोपाल प्रसाद ओसीपी (15 एमटीवाई)	03/2015	03/2021	02/2008	72
भारी उद्योग					
15	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	09/2011	12/2017	04/2011	75
पेट्रोसायन					
16	असम गैस क्रैकर परियोजना	04/2012	09/2015	04/2006	41
पेट्रोलियम					
17	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2006	06/2015	04/2003	110
18	जगदीशपुर-हल्दिया पाइपलाइन परियोजना चरण-I	01/2013	12/2018	07/2009	71
19	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	06/2011	03/2016	12/2009	57
20	12 ऑफशोर आपूर्ति वेसल्सका निर्माण (ओएसवी)	09/2011	12/2015	06/2007	51
21	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	10/2011	01/2016	01/2006	51
विद्युत					
22	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/2006	10/2016	07/1998	123
23	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2009	12/2018	09/2002	111
24	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	12/2007	12/2015	03/2005	96

25	टेहरी पंढ भंडारण संयंत्र (1000 मेगावाट)	07/2010	05/2018	07/2006	94
26	कुंडनकुलमएपीपी ट्रांस प्रणाली (पीजीसीआईएल)	09/2008	03/2016	05/2005	90
रेलवे					
27	गोंदिया-जबलपुर (जीसी), (एसईसीआर)	03/1998	12/2019	02/1997	261
28	गुना-इटावा वाया शिवपुरी-ग्वालियर-भिंड (एनएल), (एनसीआर)	03/1994	03/2015	04/1986	252
29	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	11/2002	12/2018	03/1995	193
30	बांकुरा-दामोदर (जीसी) (एसईआर)	03/2005	12/2019	03/1998	177
31	तमलुक-दीघा लाइन दोहरीकरण, (एसईआर)	06/2005	12/2019	03/1984	174
सड़क परिवहन एवं राजमार्ग					
32	हरंगाजो से मैबंगकिमी. 164.08-190.587 किमी. एनएच-54	09/2007	04/2016	12/2003	103
33	आगरा-बाईपास(एनएस-1/यूपी-1), एनएच-2,3	09/2007	12/2015	12/2003	99
34	सोनापुर से गुवाहाटी(एएस-3)	03/2008	01/2016	12/2003	94
35	नलवाडी से बिजनी(एएस-7)	04/2008	01/2016	12/2003	93
36	सिल्वर-उदरबंद (फेज. II) एनएच-54, 309 किमी. से 275 किमी.	09/2007	03/2015	12/2003	90
पोत परिवहन एवं पत्तन					
37	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	12/2010	01/2016	01/2007	61
इस्पात					
38	आरएमएचपी में लौह अयस्क भंडारण की वृद्धि	09/2009	07/2015	07/2007	70
39	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2009	04/2015	10/2005	66
40	बोकारो इस्पात संयंत्र का विस्तार	12/2011	08/2015	05/2010	44
41	बेलाडिला लौह अयस्क परियोजना डिपोजिट -11 बी (एनएमडीसी)	12/2011	03/2015	01/2007	39
42	भिलाई इस्पात संयंत्र का विस्तार	03/2013	03/2016	08/2010	36
दूरसंचार					
43	टर्न की आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	09/2015	59

	शहरी विकास				
44	सैन्य एमओडी स्टेशन मामुन पंजाब में वैवाहिक परिसर का निर्माण	08/2007	03/2015	08/2005	91
45	आरएसवीवाई पटना के अंतर्गत बिहार राज्य में राज्य राजमार्गों का विकास	03/2010	10/2014	11/2006	55
46	नागपुर महाराष्ट्र में राष्ट्रीय फायर सर्विसेज कॉलेज का उन्नयन	03/2012	04/2015	06/2010	37
47	आईआईएसआर कोलकाता के लिए हरिन घंटा कल्याणी प.बं. में आवासीय सह अकादमिक परिसर	06/2012	06/2015	01/2009	36
48	प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	08/2014	06/2017	07/2012	34

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

6. अप्रैल, 2015 में इस मंत्रालय के प्रबोधन (मॉनीटर) पर 758 परियोजनाओं में से 231 परियोजनाओं के संबंध में लागतवृद्धि तथा 323 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है; जबकि जून, 2015 के दौरान 770 परियोजनाओं में से 229 परियोजनाओं के संबंध में लागतवृद्धि तथा 313 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है। अप्रैल, 2015 की तुलना में लागतवृद्धि की सूचना देने वाली परियोजनाओं की संख्या 30.47% से घटकर 29.74% हो गई है जबकि समयवृद्धि की सूचना देने वाली परियोजनाओं की संख्या घटकर 42.61% से 40.65% हो गई है।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं की उपलब्धियों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां

उपलब्धियों की सूची प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30.06.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम) हवाई अड्डा में नए हवाई अड्डे का निर्माण	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	गगन परियोजना	09/2008	626.00	626.00	514.70	06/2013	एन.आर.
कोयला							
6	मुराईदीह यूजी	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	उत्तरी तीसरा और दक्षिणी तीसरा विस्तार ओसीपी (6 एमटीवाई)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	अमेरा ओसी आरसीई	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	अमृतधारा ओसी परियोजना	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	बिजारी ओसी आरसीई (1.50 एमटीवाई)	05/2014	164.49	164.49	22.10	03/2020	03/2020
उर्वरक							
11	नई सीवेज ट्रीटमेंट	10/2014	197.79	197.79	13.09	11/2016	11/2016

	संयंत्र पैकेज, आरसीएफ ट्राम्बे						
	भारी उद्योग						
12	राष्ट्रीय ऑटोमोटिव टेस्टिंग आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
	खान						
13	मलजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
	पेट्रोलियम						
14	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	एक बहुदेशीय सहायता वेसेल्स का निर्माण	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	बी-173ए क्षेत्र की विकसित तेल वसूली	01/2012	352.49	352.49	115.81	03/2014	05/2016
	विद्युत						
19	बीआरबीसीएल- नबीनगर-जेवी	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	एनपीजीसीपीएल- नबीनगर-जेवी	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	यूआरटीडीएसएम चरण-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	दक्षिणी क्षेत्रकोसुदृढ बनानेकीयोजना-XXII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	किशनगंगा एचईपी के साथ जुड़ी पारेषण प्रणाली	01/2015	268.80	268.80	0.00	03/2018	03/2018
	रेलवे						

24	जिंद-सोनीपत (एनएल), एनआर	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	लिव्ड फिंगर के साथ-साथ रंगिया- मूरकौगस्लेक	01/2004	915.70	3700.00	3198.30	एन.आर.	03/2015
26	कालीकट-मैंगलोर (डीएल) (एसआर)	02/1996	240.00	579.37	599.40	एन.आर.	02/2012
27	अहमदनगर-पर्ली वैजनाथ (एनएल), सीआर	02/1997	514.68	2820.00	329.67	एन.आर.	एन.आर.
28	दौसा-गंगापुर सीटी (एनएल), एनडब्ल्यूआर	02/1997	410.08	410.08	294.70	एन.आर.	एन.आर.
सड़क परिवहन एवं राजमार्ग							
29	छपरा-हाजीपुर की चार लेनिंग	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	देवली-कोटा	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	जोरबट-बारापानी	01/2011	536.00	536.00	0.00	01/2014	एन.आर.
32	कांडला-मुंदरा पोर्ट	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	पीएस कानपुर कबरई की दो लेनिंग	01/2013	373.47	373.47	0.00	07/2014	एन.आर.
पोत परिवहन एवं पत्तन							
34	सिंगल प्वाइंट मूरिंग (एसपीएम) तथा एली की स्थापना करना	02/2011	830.00	621.53	0.00	05/2013	एन.आर.
35	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल संपर्क	03/2007	245.67	373.22	373.22	04/2009	एन.आर.
36	सेतुसमुद्रमशिपचैनल परियोजना	06/2005	2427.40	2427.40	831.23	10/2008	एन.आर.
37	मौजूदा बर्थ एन का संशोधन करना तथा सुदृढीकरण	06/2010	277.00	277.00	0.21	03/2012	एन.आर.
38	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	एन.आर.

	इस्पात						
39	गैस नेटवर्क बीएसएल	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	आरएसपी में नया एचएसएम	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	24.02	10/2016	10/2016
	दूरसंचार						
42	एनएफएस	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	रक्षा क्षेत्र के टेलीकॉम नेटवर्क आवश्यकता का निष्पादन	05/2006	1077.00	1077.00	0.00	03/2009	एन.आर.
44	असमटेलीकॉमसर्किल , चरण-V.I, 2जीऔर3जी	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	टर्नकीआधारपरबीएस एनएलमेंईआरपीकार्या न्वयन	10/2009	384.00	384.00	55.22	10/2010	09/2015
	शहरी विकास						
46	आईआईएसईआर कोलकाताके लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	एनआईटी कालीकट केरल के लिए मेगा होस्टल II कानिर्माण	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	आईआईटी हौज खास नई दिल्ली में लेक्चर थियेटर और लैब कॉम्प्लेक्स	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	प्लॉट संख्या सी-41-4 पर आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	बिहटा, पटना आईआईटी के कैम्पस के लिए	02/2012	171.10	171.10	0.00	09/2014	एन.आर.

आवासीय तथा अन्य परिसर						
--------------------------	--	--	--	--	--	--

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानों वाली शुरूआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30-06-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	0.00	18271.00
	नागर विमानन				
2	पाकयांग (सिक्किम) हवाई अड्डा में नए हवाई अड्डे का निर्माण	01/2009	309.46	0.00	338.82
	कोयला				
3	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3027.59	3207.92
	पेट्रोलियम				
4	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	5925.40
	विद्युत				
5	बाढ़ एसटीपीपी फेज-II	02/2008	7341.04	0.00	8631.00
6	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7687.18
7	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	5040.21

8	किशनगंगा एचईपी (3x110 मेवा)	01/2009	3642.04	0.00	3934.97
9	छत्तीसगढ़ में आईपीपीएस जेनरेशन परियोजनाओं के लिए डब्ल्यूआर के पश्चिमी भाग में पारेषण प्रणाली का सुदृढीकरण	11/2011	2127.51	0.00	2172.33
10	तीस्ता लो डैम एचईपी चरण-IV (4X40 मेवा) (एनएचपीसी)	09/2005	1061.38	0.00	1742.55
रेलवे					
11	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10658.34
12	लुमडिंग-सिल्चर-जिरिबम बदरपुर-बराईग्राम-कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	0.00	4734.45
13	दमदम-नावपारा और नावपारा-एनएससीपी एयरपोर्ट तक विस्तार के साथ टॉलीगंज-गरिया (एमटीपी)	03/2000	1049.69	3385.14	3541.20
14	बोगीबिल तथा लिंक लाइनों पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	1000.00	3410.06
15	लिंक फिंगर्स के साथ रंगिया-मुरकौंगसलेक एनईएफआर	01/2004	915.70	915.70	3198.30
सड़क परिवहन एवं राजमार्ग					
16	पानीपत-जालंधर छः लेनिंग (96 किमी. से 387.1 किमी.)	05/2009	1108.00	0.00	3466.00
17	नागपुर-बेतुल के चार लेनिंग	02/2011	2498.76	0.00	2786.00
18	सूरत-दहिसर (छः लेन) 263 किमी. से 502 किमी.	02/2009	1693.75	0.00	2762.00
19	गाजियाबाद-अलीगढ़एनएच-91	02/2011	1141.00	0.00	2445.00
20	मुरादाबाद-बरेली	04/2010	1267.00	0.00	2425.00
पोत परिवहन एवं पत्तन					
21	कोचीन पोर्ट्स के बल्लापाडम में आईसीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	0.00	373.22

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (पुरानी) परियोजनाओं(अधिकतम संख्या में पांच) की क्षेत्र-वार सूची(30.06.2015की स्थिति के अनुसार)

क्र. सं.	क्षेत्र/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	गगन परियोजना	09/2008	06/2013	एन.आर.	06/2013
2	वीएसआई हवाईअड्डे, पोर्ट ब्लेयर में नए एकीकृत टर्मिनल भवनका निर्माण	10/2013	एन.आर.	एन.आर.	एन.आर.
कोयला					
1	शांतिखानी लॉग वॉल परियोजना-एससीसीएल	10/2006	03/2012	एन.आर.	एन.आर.
2	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.आर.	एन.आर.
3	रामागुंडमओसी॥ विस्तार	12/2009	03/2012	एन.आर.	एन.आर.
4	मुराडडीहयूजी टर्न की परियोजना	02/2011	04/2014	एन.आर.	04/2014
5	कृष्णाशिला (एनसीएल) (4एमटीवाई)	06/2011	03/2013	एन.आर.	03/2014
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	एन.आर.	एन.आर.
पेट्रोलियम					
1	एन्नोर में नई विपणन टर्मिनल	11/2006	एन.आर.	एन.आर.	एन.आर.
2	बीपीसीआर/एचपीसीआर से उरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण के लिए पाइपलाइन	08/2009	08/2012	एन.आर.	एन.आर.
3	एन्नोर-त्रिची-मदुरैएलपीजी पाइपलाइन	05/2013	एन.आर.	एन.आर.	एन.आर.
विद्युत					
1	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2009	एन.आर.
2	कुंदनकुलम एपीपी ट्रांसप्रणाली (पीजीसीआईएल)	05/2005	09/2008	एन.आर.	03/2013
3	एसआर -XII की व्यवस्था का सुदृढीकरण	02/2010	06/2012	एन.आर.	एन.आर.

4	आंध्रप्रदेश भाग-ए1 के वैमा गिरीक्षेत्र में आईएसजीएसपरियोजनाओंसे जुड़ी सामान्य प्रणाली	03/2012	06/2014	एन.आर.	एन.आर.
रेलवे					
1	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.आर.	एन.आर.
2	गजोली-ईटाहर (एनएल), एनईएफआर सहित एकलाखी-बालुरघाट से नई बीजी रेलवे लाइन	04/1983	एन.आर.	एन.आर.	एन.आर.
3	तामलुकदीघा, लाइन दोहरीकरण (एसईआर)	03/1984	06/2005	07/2011	एन.आर.
4	नामखाना चंद्रनगर काकद्वीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एमएम	04/1987	एन.आर.	एन.आर.	एन.आर.
5	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	एन.आर.	03/2010	एन.आर.
सड़क परिवहन एवं राजमार्ग					
1	लखनऊ-रायबरेली	07/1999	07/2012	एन.आर.	09/2014
2	दीवापुरसे यूपी/बिहार सीमा (एलएमएनएचपी-9) एनएच-28, किमी.402-360.915	12/2003	10/2008	एन.आर.	एन.आर.
3	सिलिगुड़ी से इस्लामपुर (पश्चिम बंगाल-7)	12/2003	07/2008	एन.आर.	एन.आर.
4	नलबाड़ी से बिजनी (एस-8)	12/2003	06/2008	एन.आर.	एन.आर.
5	पिंपलगांव-नासिक-गोंडी, एनएच-3 (एनएचडीपी चरण III)	03/2005	07/2012	एन.आर.	07/2012
पोत परिवहन एवं पत्तन					
1	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	02/2011	एन.आर.	12/2012
2	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	11/2010	एन.आर.
3	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत करना	10/2005	10/2008	एन.आर.	एन.आर.
4	पारादीप बंदरगाह पर चैनल का सुदृढीकरण	12/2005	एन.आर.	01/2009	12/2010
5	कांडला में 13 और 14 कार्गो बर्थ का निर्माण	12/2005	03/2011	एन.आर.	03/2013
शहरी विकास					
1	सैन्य रक्षामंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय का निर्माण	08/2005	08/2007	एन.आर.	एन.आर.
2	बंगलोर मेट्रो रेल परियोजना	05/2006	06/2011	एन.आर.	03/2013
3	बांद्रा कुर्ली कॉम्प्लेक्स, मुंबई में आईडीबीआई के लिए कार्यालय भवन का निर्माण	11/2006	04/2009	एन.आर.	एन.आर.

4	एनआईटी कालीकट केरल के लिए मेगा हॉस्टल का निर्माण	01/2010	10/2012	एन.आर.	एन.आर.
5	आईआईटी हॉजखास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	एन.आर.	07/2012

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित तारीख को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

- i) **पेट्रोसायन क्षेत्र में,** 1 परियोजना 'असम गैस क्रैकर परियोजना, बीपीसीएल' में ईपीएमसी, मेसर्स ईआईएल द्वारा पर्याप्त और प्रभावी पर्यवेक्षण में कमी के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।
- ii) **परमाणु ऊर्जा क्षेत्र में,** सभी 4 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना 'कुडनकुलम एपीपी (एनपीसीआईएल)' में पूर्ववर्ती कार्यकलापों में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।
- iii) **नागर विमानन क्षेत्र में,** 7 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना 'चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डा (मोहाली) का विकास चरण-II, एएआई' में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।
- iv) **विद्युत क्षेत्र में,** 110 परियोजनाओं में से 58 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना 'डब्ल्यूआर तथा एनआर (लाइन बे तथा रिएक्टर प्रावधान) के लिए सामान्य प्रणाली का सुदृढीकरण, पीजीसीआईएल' में संबद्ध लाइन तैयार न होने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।
- v) **रेलवे क्षेत्र में,** 296 परियोजनाओं में से 34 परियोजनाएं विलंबित हैं। माह के दौरान, 4 परियोजनाओं के संबंध में 2-36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 4 परियोजनाओं में से, 3 परियोजनाएं मेगा परियोजनाएं हैं। परियोजना 'मुंगेर में रेल-सह सड़क पुल (एनएल),

ईसीआर' में भूमि अधिग्रहण संबंधी मामलों में विलंब के कारण 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'हावड़ा मैदान से साल्ट लेक तक पूर्वी पश्चिमी मेट्रो कोरिडोर, एमआरटीपी' में अंडरग्राउंड प्लेटफार्म के एलाइनमेंट परिवर्तन के लिए राज्य सरकार के प्रस्ताव के कारण 27 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'कानपुर-कासगंज-मथुरा (जीसी), एनईआर' में सामग्री संशोधन के रूप में शामिल गेज परिवर्तन के कारण 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'होसादुर्गा-चिकजजुर (28.89 किमी.), एसडब्ल्यूआर' में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) इस्पात क्षेत्र में, 26 परियोजनाओं में से 14 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 1-5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'आरएमएचपी में लौह अयस्क भंडारण की वृद्धि, आरआईएनएल' में निविदा को अंतिम रूप देने में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'आरएसपी के एसपीपी में अतिरिक्त हीट ट्रीटमेंट सुविधाओं की स्थापना, सेल' तथा 'कैपटिव विद्युत संयंत्र-2, आरआईएनएल' प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा परियोजना 'बीएसपी, भिलाई छत्तीसगढ़ में कोक ओवन बैटरी-9 का कोल्ड रिपेयर, सेल' में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vii) कोयला क्षेत्र में, 76 परियोजनाओं में से 45 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । इन 7 परियोजनाओं में से 2 परियोजनाएं मेगा परियोजनाएं हैं । परियोजना 'तूतीकोरिन थर्मल पावर परियोजना-2 X 500 मेवा. , एनएलसी' में ठेकेदार द्वारा अपर्याप्त संसाधनों के जुटाने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'टीपीएस-II विस्तार (1470 मेवा. से 1970 मेवा.), एनएलसी' तथा 'विंड पावर परियोजना, काङ्गुनीरकुलाम, तमिलनाडु, एनएलसी' में क्रमशः जांच स्वीकृति में विलंब तथा सिविल कार्यों में विलंब के कारण क्रमशः 1 तथा 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'मानिकपुर ओसी विस्तार (3.5 एमटीवाई), एसईसीएल' तथा 'बारूद ओसी विस्तार (आरसीई)-3 एमटीवाई, एसईसीएल' में क्रमशः भूमि अधिग्रहण तथा वन संबंधी भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'आरकेपी ओसीपी चरण-I, एससीसीएल' तथा 'आरजी ओसी-III विस्तार (चरण-II) परियोजना, एससीसीएल' में क्रमशः 1 तथा 12 माह के अतिरिक्त

विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

viii) पेट्रोलियम क्षेत्र में, 71 परियोजनाओं में से 48 परियोजनाएं विलंबित हैं । माह के दौरान, 9 परियोजनाओं के संबंध में 2-10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 9 परियोजनाओं में से 6 परियोजनाएं मेगा परियोजनाएं हैं । दो परियोजनाएं 'मुंबई रिफाइनरी में सीडीयू/वीडीयू का पुनर्स्थापन, बीपीसीएल' तथा 'माउण्डेड बुलेट परियोजना, सीपीसीएल' में क्रमशः निर्माण कार्यकलापों में धीमी प्रगति तथा एचटी पारेषण में रुकावट के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'मंगलौर में स्ट्रैटेजिक कच्चा तेल भंडारण परियोजना, आईएसपीआरएल' तथा 'पादुर में स्ट्रैटेजिक कच्चा तेल भंडारण परियोजना, आईएसपीआरएल' में क्रमशः केवर्न स्वीकृति जांच के दौरान हुई कठिनाई तथा भारी वर्षा के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'हल्दिया रिफाइनरी में डिस्टिलेट यील्ड विकास परियोजना (कोकर), आईओसीएल' तथा 'बरौनी रिफाइनरी के कोकर में कोक चैम्बर्स का प्रतिस्थापन, आईओसीएल' में निष्पादन पद्धति में परिवर्तन तथा मैकेनिकल कार्य के लिए फिर से निविदा जारी करने के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; एक परियोजना 'पारादीप में विपणन टर्मिनल, आईओसीएल' में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'नहरकटिया-बरौनी कच्चा तेल ट्रंक पाइपलाइन के कच्चा तेल पंप स्टेशनों का उन्नयन, ऑयल' तथा 'दमन विकास परियोजना, ओएनजीसी' में क्रमशः 4 तथा 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

ix) सड़क क्षेत्र में, 137 परियोजनाओं में से 90 परियोजनाएं विलंबित हैं । माह के दौरान, 10 परियोजनाओं के संबंध में अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 4 परियोजनाएं मेगा परियोजनाएं हैं । दो परियोजनाएं 'गुवाहाटी से नलबाड़ी (एएस-4), एनएचएआई' तथा 'नलबाड़ी से बिजनी (एएस-6), एनएचएआई' में भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'नलबाड़ी से बिजनी (एएस-7), एनएचएआई' तथा 'सोनपुर से गुवाहाटी (एएस-3), एनएचएआई' में भूमि अधिग्रहण में विलंब के कारण क्रमशः 9 तथा 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'कुंदपुर-सूरथकल व मंगलौर, एनएचएआई' तथा 'उड़ीसा-छत्तीसगढ़ सीमा की चार लेनिंग करना, एनएचएआई' प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'धरमतुल से सोनपुर, 205-183 किमी. (एएस-20) एनएचएआई' तथा 'सूरत-दहिसर (6 लेन), 263 किमी से 502 किमी, एनएचएआई' में क्रमशः 4 माह तथा 9 माह के अतिरिक्त विलंब की

सूचना प्राप्त हुई है; दो परियोजनाएं 'वलझापेट पूनामलाई 106.8 किमी से 13.8 किमी, एनएचएआई' तथा 'रांची-रर्गा-जमशेदपुर, एनएचएआई' में क्रमशः 16 माह तथा 18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

12. रेलवे मंत्रालय ने इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी चल रही परियोजनाओं के संबंध में मासिक स्थिति रिपोर्टों को प्रस्तुत करना बंद कर दिया है । अतः, उपलब्ध सूचना/आंकड़े (जनवरी 2015 की स्थिति के अनुसार) का उपयोग रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में किया गया है ।
13. दिनांक 30.06.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
14. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for June 2015 contains information on the status of the 770 Central Sector Infrastructure Projects costing ₹150 crore and above. During June 2015, 6 projects (2 projects each of Steel, Power and Railway sector) have reported completion.

2. During the reference month, out of 770 projects, 313 projects are delayed with respect to original schedule and 38 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 38 projects, 17 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	RAILWAYS	296	34	4	3
2	ROAD TRANSPORT AND HIGHWAYS	137	90	10	4
3	POWER	110	58	1	0
4	PETROLEUM	71	48	9	6
5	COAL	76	45	7	2
6	URBAN DEVELOPMENT	30	13	0	0
7	STEEL	26	14	4	0
8	CIVIL AVIATION	7	3	1	0
9	SHIPPING AND PORTS	7	1	0	0
10	ATOMIC ENERGY	4	4	1	1
11	TELECOMMUNICATIONS	2	1	0	0
12	FERTILISERS	1	0	0	0
13	MINES	1	0	0	0
14	PETROCHEMICALS	1	1	1	1
15	HEAVY INDUSTRIES	1	1	0	0
Total		770	313	38	17

3. Total original cost of implementation of the 770 projects was ₹10,67,193.26 crore and their anticipated completion cost is likely to be ₹12,75,501.50 crore, which reflects overall cost overruns of ₹2,08,308.24 crore (19.52 % of original cost). The expenditure incurred on these projects till June 2015 is ₹5,57,866.01 crore, which is 43.74% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost
Overruns (as on 30-6-2015)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
2	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	31.12
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	15.77
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	8.19
COAL					
6	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	76.47
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	34.63
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
10	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
HEAVY INDUSTRY					
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
12	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	80.08
PETROLEUM					
13	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	820.20
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	75.35
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
17	MARKETING TOP AT KORBA	01/2011	141.86	219.00	54.38
POWER					
18	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	159.38
20	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	159.15
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	143.42
22	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.68	139.35
RAILWAYS					
23	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
24	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
25	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
26	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
27	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
ROAD TRANSPORT AND HIGHWAYS					
28	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
29	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
30	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	363.74	85.58
31	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	212.00	386.10	82.12

32	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
SHIPPING AND PORTS					
33	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
34	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	51.92
36	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	18.89
STEEL					
37	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
38	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	41.41
URBAN DEVELOPMENT					
39	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 30-6-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs. In crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	4099.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	52.92
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	37.00
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	1698.20
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	1552.99
8	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
9	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	48.00
HEAVY INDUSTRY					
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
12	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	4372.91

	PETROLEUM				
13	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
14	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	3525.39
15	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
16	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	12/2012	3513.07	4619.94	1106.87
	POWER				
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	9014.67
18	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	3979.44
20	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7818.68	3899.09
21	BARH STPP STAGE -II	02/2008	7341.04	10852.46	3511.42
	RAILWAYS				
22	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
23	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
24	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
25	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
26	SEVOK RANGPO, NEFR	04/2008	1339.48	4190.00	2850.52
	ROAD TRANSPORT AND HIGHWAYS				
27	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
29	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	212.00	386.10	174.10
30	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	363.74	167.74
31	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
	SHIPPING AND PORTS				
32	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
33	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
34	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	232.00
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	127.55
	STEEL				
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	3599.00
37	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
	URBAN DEVELOPMENT				
38	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 770 projects, 4 projects are ahead of schedule, 125 are on schedule and 313 are delayed with respect to original schedule. However, the number of delayed projects decreases to 278 if delay is calculated on the basis of latest schedule of completion. Further, 30 projects have been sanctioned without original commissioning schedule date and for 298 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 313 delayed projects, 52 projects have overall delay in the range of 1 to 12 months, 67 projects have delay in the range of 13 to 24 months, 129 projects have delay in the range of 25 to 60 months and 65 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 30-6-2015)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2008	10/2015	12/2001	82
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2010	09/2016	09/2003	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	12/2015	10/2017	10/2009	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	12/2016	05/2018	10/2009	17
CIVIL AVIATION					
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2011	06/2017	01/2009	77
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2012	03/2015	05/2010	34
7	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	03/2014	05/2015	02/2010	14
8	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	03/2015	09/2015	10/2012	6
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	03/2015	07/2015	02/2011	4
COAL					
10	BALRAM OCP EXTENSION,MCL 8.00 MTY	03/2010	03/2017	12/2007	84
11	KULDA OCP (MAHANADI COALFIELDS LTD)	03/2010	03/2017	01/2005	84
12	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	06/2009	07/2015	10/2004	73
13	JHANJRA R-VI SEAM PSLW	03/2011	03/2017	11/2006	72
14	GOPAL PRASAD OCP (15MTY)	03/2015	03/2021	02/2008	72
HEAVY INDUSTRY					
15	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	09/2011	12/2017	04/2011	75

	PETROCHEMICALS				
16	ASSAM GAS CRACKER PROJECT	04/2012	09/2015	04/2006	41
	PETROLEUM				
17	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	04/2006	06/2015	04/2003	110
18	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	01/2013	12/2018	07/2009	71
19	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	06/2011	03/2016	12/2009	57
20	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	09/2011	12/2015	06/2007	51
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	10/2011	01/2016	01/2006	51
	POWER				
22	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/2006	10/2016	07/1998	123
23	PARBATI HEP (4X200 MW) (NHPC) II	09/2009	12/2018	09/2002	111
24	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	12/2007	12/2015	03/2005	96
25	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2010	05/2018	07/2006	94
26	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	09/2008	03/2016	05/2005	90
	RAILWAYS				
27	GONDIA-JABALPUR(GC),(SECR)	03/1998	12/2019	02/1997	261
28	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	03/1994	03/2015	04/1986	252
29	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	11/2002	12/2018	03/1995	193
30	BANKURA - DAMODAR (GC) (SER)	03/2005	12/2019	03/1998	177
31	TAMLUK DIGHA,LINE DOUBLING (SER)	06/2005	12/2019	03/1984	174
	ROAD TRANSPORT AND HIGHWAYS				
32	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	09/2007	04/2016	12/2003	103
33	AGRA-BYPASS(NS-1/UP-1), NH-2,3	09/2007	12/2015	12/2003	99
34	SONAPUR TO GUWAHTI (AS-3)	03/2008	01/2016	12/2003	94
35	NALBARI T BIJNI (AS-7)	04/2008	01/2016	12/2003	93
36	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	09/2007	03/2015	12/2003	90
	SHIPPING AND PORTS				
37	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	12/2010	01/2016	01/2007	61
	STEEL				
38	AUGMENTATION OF IRON ORE STORAGE IN RMHP	09/2009	07/2015	07/2007	70
39	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2009	04/2015	10/2005	66
40	EXPANSION OF BOKARO STEEL PLANT	12/2011	08/2015	05/2010	44
41	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC)	12/2011	03/2015	01/2007	39
42	EXPANSION OF BHILAI STEEL PLANT	03/2013	03/2016	08/2010	36

TELECOMMUNICATIONS					
43	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2010	09/2015	10/2009	59
URBAN DEVELOPMENT					
44	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2007	03/2015	08/2005	91
45	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	03/2010	10/2014	11/2006	55
46	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	03/2012	04/2015	06/2010	37
47	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	06/2012	06/2015	01/2009	36
48	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	08/2014	06/2017	07/2012	34

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during June 2015, out of 770 projects, 229 projects reported cost overruns and 313 projects reported time overruns. In comparison to April 2015, number of projects reporting cost overruns has gone down from 30.47% to 29.74% whereas projects reporting time overruns have decreased from 42.61% to 40.65%.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones is as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 30-6-2015)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	GAGAN PROJECT	09/2008	626.00	626.00	514.70	06/2013	N.R.
COAL							
6	MURAI DIHUG	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	AMERA OC RCE	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	AMRITDHARA OC PROJECT	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	BIJARI OC RCE (1.50 MTY)	05/2014	164.49	164.49	22.10	03/2020	03/2020
FERTILISERS							
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	197.79	13.09	11/2016	11/2016
HEAVY INDUSTRY							
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
13	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
PETROLEUM							

14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	IMPROVED OIL RECOVERY OF B-173A FIELD	01/2012	352.49	352.49	115.81	03/2014	05/2016
POWER							
19	BRBCL-NABINAGAR - JV	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	NPGCPL-NABINAGAR - JV	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	URTDSM PHASE-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAG A HEP	01/2015	268.80	268.80	0.00	03/2018	03/2018
RAILWAYS							
24	JIND-SONEPAT (NL),NR	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	RANGIA-MURKONGSELE K, (GC) ALONG WITH LINKED FINGER	01/2004	915.70	3700.00	3198.30	N.R.	03/2015
26	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	579.37	599.40	N.R.	02/2012
27	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	514.68	2820.00	329.67	N.R.	N.R.
28	DAUSA-GANGAPUR CITY(NL),NWR	02/1997	410.08	410.08	294.70	N.R.	N.R.
ROAD TRANSPORT AND HIGHWAYS							
29	4-LANNING OF CHAPRA-HAJIPUR	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	DEOLI-KOTA	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	JORBAT - BARAPANI	01/2011	536.00	536.00	0.00	01/2014	N.R.
32	KANDLA - MUNDRA PORT	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	2 LANING WITH PS KANPUR	01/2013	373.47	373.47	0.00	07/2014	N.R.

	KABRAI						
	SHIPPING AND PORTS						
34	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIE	02/2011	830.00	621.53	0.00	05/2013	N.R.
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	373.22	373.22	04/2009	N.R.
36	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	N.R.
37	MODIFICATION AND STRENGTHENING OF EXISTING BERTH N	06/2010	277.00	277.00	0.21	03/2012	N.R.
38	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE	10/2002	150.00	600.00	139.80	03/2006	N.R.
	STEEL						
39	GAS NETWORK BSL	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	NEW HSM AT RSP	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	24.02	10/2016	10/2016
	TELECOMMUNICATIONS						
42	NFS	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE	05/2006	1077.00	1077.00	0.00	03/2009	N.R.
44	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	55.22	10/2010	09/2015
	URBAN DEVELOPMENT						
46	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	C/O MEGA HOSTEL II FOR NIT CALICUT	01/2010	165.23	165.23	0.00	10/2012	09/2013

	KERALA						
48	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-4	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	171.10	0.00	09/2014	N.R.

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 30-6-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMMULATIVE EXPENDITURE (Rs. Crore)
	ATOMIC ENERGY				
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	0.00	18271.00
	CIVIL AVIATION				
2	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	338.82
	COAL				
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3027.59	3207.92
	PETROLEUM				
4	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	5925.40
	POWER				
5	BARH STPP STAGE -II	02/2008	7341.04	0.00	8631.00
6	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7687.18
7	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5040.21
8	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	3934.97
9	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	11/2011	2127.51	0.00	2172.33
10	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1742.55
	RAILWAYS				
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
12	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	0.00	4734.45

13	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1049.69	3385.14	3541.20
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	1000.00	3410.06
15	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	01/2004	915.70	915.70	3198.30
ROAD TRANSPORT AND HIGHWAYS					
16	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	0.00	3466.00
17	4 LANING OF NAGPUR-BETUL	02/2011	2498.76	0.00	2786.00
18	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2762.00
19	GHAZIABAD-ALIGARH NH-91	02/2011	1141.00	0.00	2445.00
20	MURADABAD-BAREILY	04/2010	1267.00	0.00	2425.00
SHIPPING AND PORTS					
21	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	0.00	373.22

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 30-6-2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURADIDH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.

3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013
3	SYSTEM STRENGTHENING -XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.
3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.
4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010
5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013
URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Petrochemical**, 1 project 'Assam Gas Cracker Project BCPL' has reported additional delay of 3 months due to lack of adequate and effective supervision by the EPMC, M/s EIL.
- ii) In the **Atomic Energy**, all 4 projects are delayed. During the month, 1 project 'Kudankulam APP (NPCIL)' has reported additional delay of 1 month due to delay of preceding activities.
- iii) In the **Civil Aviation**, out of 7 projects, 3 projects are delayed. During the month, 1 project 'Development of Chandigarh International Airport (Mohali) Ph – II, AAI' has reported additional delay of 2 months (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).
- iv) In the **Power Sector**, out of 110 projects, 58 projects are delayed. During the month, 1 project 'System Strengthening Common for WR and NR (Line Bays and Reactor Provision), PGCIL' has reported additional delay of 1 month because associated line is not ready (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).
- v) In the **Railways**, out of 296 projects, 34 projects are delayed. During the month, 4 projects have reported additional delay in the range of 2-36 months. Out of 4 projects, 3 projects are mega projects. The project 'Rail-cum-Road Bridge at Munger (NL), ECR' has reported additional delay of 10 months due to land acquisition issues; the project 'East West Metro Corridor From Howrah Maidan to Salt Lake, MRTTP' has reported additional delay of 27 months due to state government proposal for alignment change of underground platform; the project 'Kanpur-Kasganj-Mathura(GC), NER' has reported additional delay of 36 months due to gauge conversion added as material modification; the project 'Hosadurga - Chickjajur (28.89 KM) SWR' has reported additional delay of 2 months (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

- vi)** In the **Steel Sector**, out of 26 projects, 14 projects are delayed. During the month, 4 projects have reported additional delay in the range of 1-5 months. The project 'Augmentation of Iron Ore Storage in RMHP, RINL' has reported additional delay of 1 month due to delay in finalization of tender; two projects 'Installation of Additional Heat Treatment Facilities in SPP at RSP, SAIL' and 'Captive Power Plant-2 RINL' have reported additional delay of 1 month each and the project 'Cold Repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh, SAIL' has reported additional delay of 5 months (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).
- vii)** In the **Coal Sector**, out of 76 projects, 45 projects are delayed. During the month, 7 projects have reported additional delay in the range of 1-24 months. Out of 7 projects, 2 projects are mega projects. The project 'Tuticorin Thermal Power Project- 2X500 MW, NLC' has reported additional delay of 1 month due to inadequate mobilization by the contractor; two project 'TPS-II Expansion (1470 MW to 1970MW), NLC' and 'Wind Power Project, Kazhuneerkulam, Tamilnadu NLC' have reported additional delay of 1 month and 2 months respectively due to delay in acceptance in testing and delay in civil works respectively; two projects 'Manikpur OC Expansion (3.5 MTY), SECL' and 'Baroud OC Expansion (RCE)- 3MTY SECL' have reported additional delay of 24 months each due to delay in land acquisition and delay in forest land acquisition respectively; two projects 'RKP OCP Phase-I SCCL' and 'RG OC-III Extension (Phase - II) Project SCCL' have reported additional delay of 1 month and 12 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).
- viii)** In the **Petroleum Sector**, out of 71 projects, 48 projects are delayed. During the month, 9 projects have reported additional delays in the range of 2-10 months. Out of 9 projects, 6 projects are mega projects. Two projects 'Replacement of CDU/VDU at Mumbai Refinery, BPCL' and 'Mounded Bullet Project, CPCL' have reported additional delay of 2 months each due to slow progress in construction activities and hindrance in HT transmission respectively; two projects 'Strategic Crude Oil Storage Project at Mangalore, ISPRL' and 'Strategic Crude Oil Storage Project at Padur, ISPRL' have reported additional delay of 3 months each due difficulty during cavern acceptance testing and heavy rain respectively; two projects 'Distillate Yield Improvement Project (Coker) at Haldia Refinery, IOCL' and 'Replacement of Coke Chambers in Coker at Barauni Refinery, IOCL' have reported additional delay of 3 months each due to change in execution methodology and retendering of mechanical job;

one project 'Marketing Terminal at Paradeep IOCL' has reported additional delay of 3 months; two projects 'Upgradation of Crude Oil Pump Stations of Naharkatiya-Barauni Crude Oil Trunk Pipeline, OIL' and 'Daman Development Project, ONGC' have reported additional delay of 4 months and 10 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).


- ix) In the **Road Sector**, out of 137 projects, 90 projects are delayed. During the month, 10 projects are additional delay out of which 4 projects are mega projects. Two projects 'Guwhati to Nalbari (AS-4), NHAI' and 'Nalbari to Bijni (AS-6) NHAI' have reported additional delay of 4 months each due to land acquisition; two projects 'Nalbari to Bijni (AS-7), NHAI' and 'Sonapur to Guwahti (AS-3) NHAI' have reported additional delay of 9 months and 10 months respectively due to land acquisition; two projects 'Kundupur-Surathkal & Manglore, NHAI' and 'Four Laning of Orissa Chattishgarh Border, NHAI' have reported additional delay of 6 months each; two projects 'Dharamtul to Sonapur, km 205-183 (AS-20), NHAI' and 'Surat- Dahisar (6 Lane) km 263 to km 502, NHAI' have reported additional delay of 4 months and 9 months respectively; two projects 'Walajapet Poonamalee km 106.8 to km 13.8 NHAI' and 'Ranchi-Rarga-Jamsethpur, NHAI' have reported additional delay of 16 months and 18 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

12. Ministry of Railway has discontinued the practice of furnishing monthly status reports on all on-going projects being implemented by Railways to this Ministry. Therefore, the available information/data (as on January 2015) has been used in respect of all projects of Railways sector.
13. The status as on 30.06.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.
14. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	296	4
2	ROAD TRANSPORT AND HIGHWAYS	137	10
3	POWER	110	1
4	COAL	76	7
5	PETROLEUM	71	9
6	URBAN DEVELOPMENT	30	0
7	STEEL	26	4
8	CIVIL AVIATION	7	1
9	SHIPPING AND PORTS	7	0
10	ATOMIC ENERGY	4	1
11	TELECOMMUNICATIONS	2	0
12	FERTILISERS	1	0
13	MINES	1	0
14	PETROCHEMICALS	1	1
15	HEAVY INDUSTRY	1	0
	Total	770	38

Sectoral break up of on-going infrastructure projects

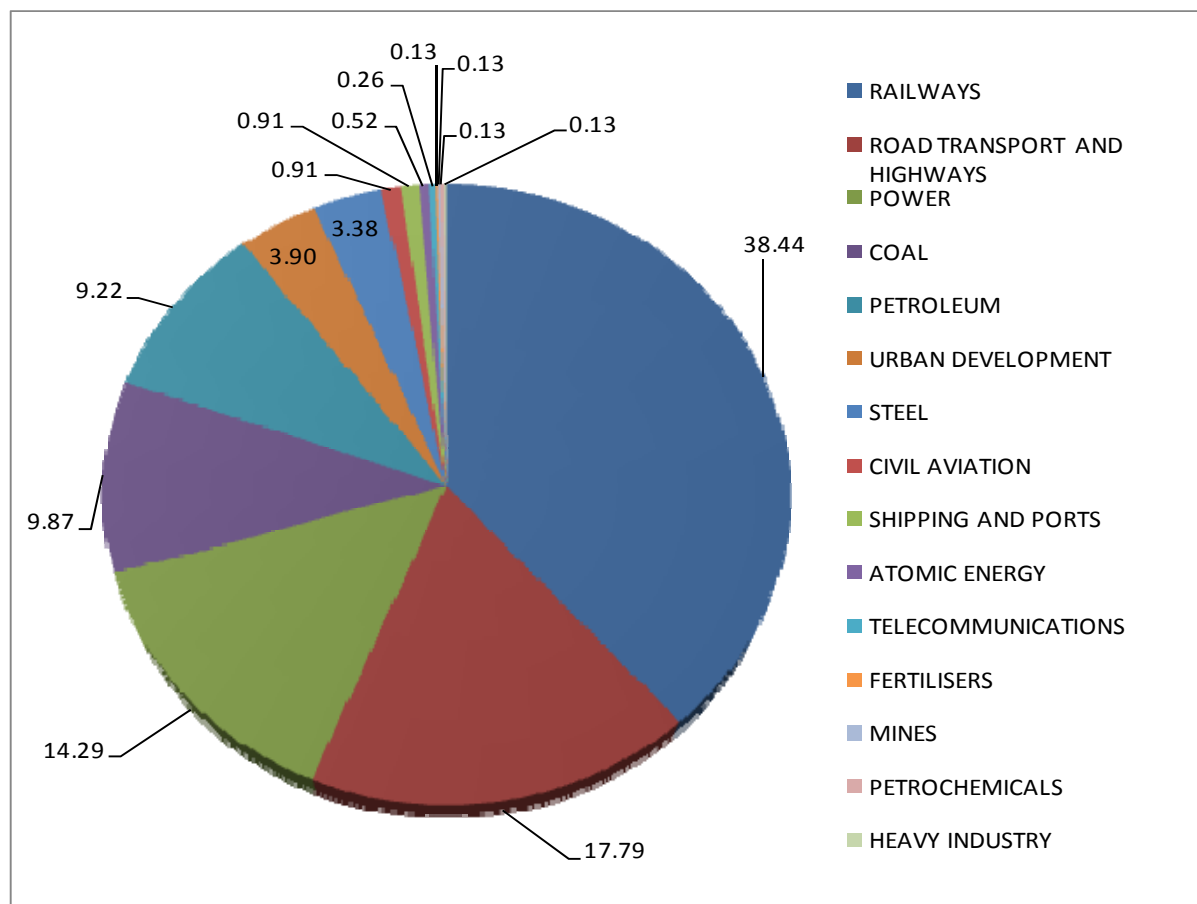

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May,2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
	June,2015			
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2015			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000170]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N24000127]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000127]	2,913.10	05/2016	13.86
	June,2015			
7	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000136]	2,913.10	05/2016	13.86
8	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N26000062]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
9	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N12000074]	1,077.00	03/2009	.00

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	766
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects elevated to the status of Major project during the Current Month	6
No of Projects added in Current Month	7
No of Projects in Current Month	770

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	313	4	125	30	298	770	40.65
Latest Approved (Date)	278	4	160	30	298	770	36.10

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	653	8,70,165.50	9,57,471.39	3,53,774.95	36.90	87,305.89	10.00
Project with Revision in Cost	117	2,62,568.19	3,18,030.11	2,04,091.06	64.20	55,461.92	21.10
Total	770	11,32,733.69	12,75,501.50	5,57,866.01	43.74	142767.81	12.60
Original Cost of All Projects							
Original Cost	770	10,67,193.26	12,75,501.50	5,57,866.01	43.74	2,08,308.24	19.52

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	313	556,724.61	672,225.19	405,468.90	60.30	115,500.58	20.70
Latest Approved (RCE)	280	532,759.93	595,547.97	375,325.34	63.00	62,788.04	11.80
Total	593	1,089,484.54	1,267,773.16	780,794.24	61.59	178288.62	16.36

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	40	59,537.81	75,247.11	58,039.23	77.10	15,709.30	26.40
Total	40	59,537.81	75,247.11	58,039.23	77.13	15709.3	26.39

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	37.71
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	3	1,005.21	1,121.63	11.58
3	COAL	76	59,478.01	63,381.17	6.56	6	8,208.23	12,579.39	53.25
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	26	61,866.16	65,580.56	6.00	2	9,035.00	12,779.40	41.44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	80.08
8	PETROLEUM	71	153,184.11	167,522.71	9.36	17	62,721.75	78,324.61	24.88
9	POWER	110	310,535.03	350,364.40	12.83	21	55,547.32	95,440.30	71.82
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS	296	171,881.41	297,255.34	72.94	161	85,637.72	212,427.62	148.05
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	102,199.30	2.15	10	3,146.62	5,322.13	69.14
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	4	1,990.06	3,102.68	55.91
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		770	1,067,193.26	1,275,501.50	19.52	229	257,528.52	469,314.58	82.24

Extent of cost overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	28	25,167.01	31,389.44	24.72	7	11,072.36	17,294.79	56.20
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	3	9,356.22	23,263.83	148.65
3	ASSAM	34	22,255.53	38,017.05	70.82	15	16,130.17	32,009.35	98.44
4	BIHAR	48	57,726.67	75,016.29	29.95	16	21,078.77	39,095.93	85.48
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	15.77
6	GUJARAT	29	36,037.34	36,616.51	1.61	4	1,202.26	2,117.22	76.10
7	HARYANA	9	4,659.81	6,630.43	42.29	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,966.47	10,785.67	117.17
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	34	66,982.20	81,944.97	22.34	17	13,700.79	28,669.59	109.26
11	KERALA	13	24,457.67	28,611.45	16.98	5	16,205.39	20,359.17	25.63
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	4	2,144.95	4,548.31	112.05
13	MAHARASHTRA	46	101,718.42	112,603.93	10.70	13	21,963.17	33,300.60	51.62
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	325.27
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	42	72,186.50	81,274.54	12.59	15	35,919.03	45,028.41	25.36
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	0.00
20	RAJASTHAN	30	27,857.57	27,913.04	0.20	6	2,574.16	3,142.63	22.08
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	42	68,208.56	85,860.44	25.88	20	30,028.23	47,680.11	58.78
23	TRIPURA	6	2,966.26	6,629.97	123.51	5	2,678.22	6,376.31	138.08
24	UTTAR PRADESH	29	35,842.78	38,740.53	8.08	8	2,088.15	5,034.16	141.08
25	WEST BENGAL	38	39,963.90	49,662.31	24.27	13	8,447.62	18,669.36	121.00
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	8.19
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
28	DELHI	12	50,903.45	50,903.45	0.00	0	0.00	0.00	0.00
29	CHHATISGARH	28	80,681.93	82,331.09	2.04	6	3,494.57	5,144.03	47.20
30	JHARKHAND	37	38,977.33	39,535.41	1.43	5	1,172.18	1,772.00	51.17
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,346.89	10,900.21	48.37
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
33	TELANGANA	21	9,410.62	12,235.26	30.02	6	1,903.46	4,728.10	148.40
34	MULTI STATE	187	207,744.19	236,422.65	13.80	41	23,230.13	52,118.64	124.36
Total		770	1,067,193.26	1,275,501.50	19.52	229	257,528.52	469,314.58	82.24

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	4	40,442.00	46,726.00	17 - 82
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	3	979.06	1,042.56	4 - 77
3	COAL	76	59,478.01	63,381.17	6.56	45	31,417.66	35,425.80	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	26	61,866.16	65,580.56	6.00	14	44,255.04	44,225.04	6 - 70
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41 - 41
8	PETROLEUM	71	153,184.11	167,522.71	9.36	48	100,568.95	112,167.48	2 - 110
9	POWER	110	310,535.03	350,364.40	12.83	58	144,924.18	172,160.60	3 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS	296	171,881.41	297,255.34	72.94	34	33,808.74	91,603.96	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	102,199.30	2.15	90	72,960.45	74,719.94	6 - 103
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	1	366.39	669.46	61 - 61
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	59 - 59
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	13	79,439.53	79,439.53	2 - 36
Total		770	1,067,193.26	1,275,501.50	19.52	313	556,724.61	672,225.19	

Extent of time overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	28	25,167.01	31,389.44	24.72	8	6,894.19	7,400.54	8 - 45
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	2	3,070.89	7,963.83	31 - 87
3	ASSAM	34	22,255.53	38,017.05	70.82	17	18,617.34	33,449.59	15 - 110
4	BIHAR	48	57,726.67	75,016.29	29.95	16	24,960.26	36,335.78	3 - 98
5	GOA	1	335.61	388.53	15.77	0	0.00	0.00	-
6	GUJARAT	29	36,037.34	36,616.51	1.61	11	25,362.68	25,285.99	14 - 48
7	HARYANA	9	4,659.81	6,630.43	42.29	3	2,244.00	3,424.00	28 - 62
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,190.42	8,089.51	11 - 111
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	6	13,202.50	32,123.18	10 - 193
10	KARNATAKA	34	66,982.20	81,944.97	22.34	7	4,716.71	5,776.36	12 - 96
11	KERALA	13	24,457.67	28,611.45	16.98	4	2,899.06	3,599.06	18 - 48
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	7	3,479.29	3,381.15	12 - 69
13	MAHARASHTRA	46	101,718.42	112,603.93	10.70	21	62,024.53	68,200.20	2 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	536.00	536.00	29 - 29
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	47 - 123
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	42	72,186.50	81,274.54	12.59	19	41,449.20	46,620.89	6 - 84
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	-
20	RAJASTHAN	30	27,857.57	27,913.04	0.20	9	18,877.57	18,431.29	15 - 84
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 77
22	TAMIL NADU	42	68,208.56	85,860.44	25.88	19	57,316.28	67,231.25	8 - 90
23	TRIPURA	6	2,966.26	6,629.97	123.51	4	2,417.39	5,379.59	25 - 108
24	UTTAR PRADESH	29	35,842.78	38,740.53	8.08	14	16,082.28	17,991.65	9 - 99
25	WEST BENGAL	38	39,963.90	49,662.31	24.27	16	22,674.01	26,706.94	3 - 177
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	4 - 4
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
28	DELHI	12	50,903.45	50,903.45	0.00	4	40,136.16	40,136.16	9 - 34
29	CHHATISGARH	28	80,681.93	82,331.09	2.04	15	55,943.90	56,425.95	9 - 72
30	JHARKHAND	37	38,977.33	39,535.41	1.43	20	12,723.06	13,155.85	2 - 138
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,605.06	11,048.24	35 - 94
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
33	TELANGANA	21	9,410.62	12,235.26	30.02	11	3,359.39	4,375.44	8 - 72
34	MULTI STATE	187	207,744.19	236,422.65	13.80	65	95,189.80	104,336.08	3 - 261
Total		770	1,067,193.26	1,275,501.50	19.52	313	556,724.61	672,225.19	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	17 - 82
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	3	979.06	1,042.56	4 - 77
3	COAL	76	59,478.01	63,381.17	6.56	43	25,170.67	29,178.81	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	26	61,866.16	65,580.56	6.00	13	28,730.04	28,700.04	6 - 70
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41 - 41
8	PETROLEUM	71	153,184.11	167,522.71	9.36	29	71,545.23	81,333.32	2 - 110
9	POWER	110	310,535.03	350,364.40	12.83	56	139,935.70	161,939.18	3 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS	296	171,881.41	297,255.34	72.94	31	27,333.74	79,079.96	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	102,199.30	2.15	83	71,530.72	73,198.26	6 - 103
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	1	366.39	669.46	61 - 61
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	59 - 59
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	13	79,439.53	79,439.53	2 - 36
Total		770	1,067,193.26	1,275,501.50	19.52	278	489,543.69	589,674.94	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	46,726.00	0.00	0	0.00	0.00	0.00
2	CIVIL AVIATION	7	2,636.56	2,715.98	3.01	2	553.21	632.63	14.36
3	COAL	76	62,985.69	63,381.17	0.63	3	3,657.71	4,261.99	16.52
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	26	65,465.16	65,580.56	0.18	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,833.52	10.24	1	8,920.00	9,833.52	10.24
8	PETROLEUM	71	165,066.76	167,522.71	1.49	4	15,877.91	18,583.61	17.04
9	POWER	110	333,473.69	350,364.40	5.07	5	17,399.92	34,290.63	97.07
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS	296	185,296.44	297,255.34	60.42	155	90,996.98	204,587.68	124.83
12	ROAD TRANSPORT AND HIGHWAYS	137	100,165.25	102,199.30	2.03	9	2,929.01	5,012.57	71.14
13	SHIPPING AND PORTS	7	5,827.53	6,428.61	10.31	3	1,623.67	2,433.22	49.86
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		770	1,132,733.69	1,275,501.50	12.60	185	150,414.41	295,560.55	96.50

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	1	3,492.00	5,677.00	72- 72
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	0	0.00	0.00	0- 0
3	COAL	76	59,478.01	63,381.17	6.56	2	6,935.32	10,186.51	40- 73
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	26	61,866.16	65,580.56	6.00	1	8,692.00	12,291.00	66- 66
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41- 41
8	PETROLEUM	71	153,184.11	167,522.71	9.36	7	37,617.12	48,353.39	12- 110
9	POWER	110	310,535.03	350,364.40	12.83	10	22,160.66	36,842.83	16- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	RAILWAYS	296	171,881.41	297,255.34	72.94	4	5,873.07	10,121.84	48- 174
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	102,199.30	2.15	2	425.61	517.56	69- 93
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		770	1067193.26	1275501.5	19.52	28	90656.39	133823.65	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	72- 82
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	2	669.60	733.10	4- 6
3	COAL	76	59,478.01	63,381.17	6.56	4	7,627.19	11,894.53	30- 73
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	26	61,866.16	65,580.56	6.00	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41- 41
8	PETROLEUM	71	153,184.11	167,522.71	9.36	12	41,085.22	53,891.47	12- 110
9	POWER	110	310,535.03	350,364.40	12.83	18	41,624.08	68,924.11	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	RAILWAYS	296	171,881.41	297,255.34	72.94	29	23,316.40	81,340.44	3- 261
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	102,199.30	2.15	7	2,511.77	4,295.87	60- 103
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	1	366.39	669.46	61- 61
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		770	1067193.26	1275501.5	19.52	77	141042.26	258356.8	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS	03/2013	2,913.10	05/2016	2,913.10	04/2018	13.86
2	IMPROVED OIL RECOVERY OF B-173A FIELD	01/2012	352.49	03/2014	352.49	05/2016	122.87
	<u>POWER</u>						
3	KOLDAM HEP (NTPC)	10/2002	4,527.15	04/2009	7,220.00	06/2015	6,622.00
4	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	09/2011	1,366.34	12/2013	1,606.38	06/2015	1,320.96
	<u>RAILWAYS</u>						
5	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	04/1997	863.23	N.A.	1,072.51	05/2015	888.87
6	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	01/2004	915.70	N.A.	3,700.00	05/2015	3,198.30
	<u>STEEL</u>						
7	EXPANSION OF DURGAPUR STEEL PLANT	08/2010	2,875.00	12/2012	2,875.00	06/2015	2,640.00
8	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES	11/2011	254.55	11/2013	254.55	06/2015	135.89
	<u>TELECOMMUNICATIONS</u>						
9	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES	05/2006	1,077.00	03/2009	1,077.00	N.A.	.00

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	CRU TO ISOMERIZATION (ISOM)	10/2011	725.00	11/2016	725.00	11/2016
2	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY	3/2014	238.50	3/2017	238.50	3/2017
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
3	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA	10/2013	677.79	4/2016	677.79	4/2016
4	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER	1/2014	177.32	1/2016	177.32	1/2016
5	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR	1/2014	158.04	12/2015	158.04	12/2015
6	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION	1/2014	368.15	1/2016	368.15	1/2016
7	2-LANING WITH PS BHILWARA-LODPURA SECTION	3/2014	240.10	3/2016	240.10	3/2016

Milestones (Cumulative due & achieved)


Total	3775
Achieved up to month	1775

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	09/2015	10/2015	1
	<u>CIVIL AVIATION</u>						
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II AAI	452.00	489.00	03/2015	05/2015	07/2015	2
	<u>COAL</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,583.77	06/2009	06/2015	07/2015	1
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,602.74	03/2012	06/2015	07/2015	1
5	RKP OCP PHASE-I SCCL	209.78	209.78	03/2015	03/2016	04/2016	1
6	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	06/2015	08/2015	2
7	RG OC -III EXTENSION (PHASE -II) PROJECT SCCL	365.01	365.01	06/2015	03/2016	03/2017	12
8	MANIKPUR OC EXPANSION (3.5 MTY) SECL	321.50	321.50	03/2014	03/2016	03/2018	24
9	BAROUD OC EXPANSION (RCE)- 3MTY SECL	258.56	258.56	03/2016	03/2016	03/2018	24
	<u>STEEL</u>						
10	AUGMENTATION OF IRON ORE STORAGE IN RMHP RINL	480.00	450.00	09/2009	06/2015	07/2015	1
11	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP SAIL	160.48	160.48	09/2014	06/2015	07/2015	1
12	CAPTIVE POWER PLANT - 2 RINL	677.00	677.00	09/2013	06/2015	07/2015	1
13	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH SAIL	332.65	332.65	08/2014	06/2015	11/2015	5
	<u>PETROCHEMICALS</u>						
14	ASSAM GAS CRACKER PROJECT BCPL	5,460.61	9,833.52	04/2012	06/2015	09/2015	3


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>PETROLEUM</u>						
15	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY BPCL	1,419.00	1,419.00	12/2014	06/2015	08/2015	2
16	MOUNDED BULLET PROJECT AT CPCL CPCL	279.00	279.00	12/2014	07/2015	09/2015	2
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE ISPRL	732.00	1,227.00	10/2011	10/2015	01/2016	3
18	MARKETING TERMINAL AT PARADEEP IOCL	199.75	239.73	07/2013	07/2015	10/2015	3
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR ISPRL	993.00	1,693.00	01/2012	10/2015	01/2016	3
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY IOCL	3,076.00	3,076.00	09/2017	09/2017	12/2017	3
21	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY IOCL	480.00	480.00	02/2016	02/2016	05/2016	3
22	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE OIL	871.35	1,200.00	03/2015	02/2016	06/2016	4
23	DAMAN DEVELOPMENT PROJECT ONGC	6,086.08	6,086.08	05/2019	05/2019	03/2020	10
	<u>POWER</u>						
24	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	06/2015	07/2015	1
	<u>RAILWAYS</u>						
25	HOSADURGA - CHICKAJAJUR (28.89 KM) SWR	203.40	203.40	N.A.	07/2015	09/2015	2
26	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	921.00	2,363.00	03/2009	12/2014	10/2015	10
27	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE MRTD	4,874.58	4,874.58	03/2016	03/2016	06/2018	27
28	KANPUR-KASGANJ-MATHURA(GC),NER	677.97	1,651.54	N.A.	03/2015	03/2018	36
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
29	GUWHATI TO NALBARI (AS-4) NHAI	175.96	175.96	04/2008	04/2015	08/2015	4
30	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	04/2015	08/2015	4

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
31	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	06/2015	10/2015	4
32	KUNDUPUR-SURATHKAL & MANGLORE NHAI	671.00	671.00	N.A.	06/2015	12/2015	6
33	FOUR LANING OF ORISSA CHATTISHGARH BORDER NHAI	1,232.00	1,232.00	08/2015	08/2015	02/2016	6
34	NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	04/2015	01/2016	9
35	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 NHAI	1,693.75	1,693.75	08/2011	12/2015	09/2016	9
36	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	03/2015	01/2016	10
37	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 NHAI	1,287.95	1,287.95	11/2015	11/2015	03/2017	16
38	RANCHI-RARGA-JAMSETHPUR NHAI	1,479.00	1,479.00	06/2015	06/2015	12/2016	18

Graphical Presentation of All Projects w.r.t. Original Schedule

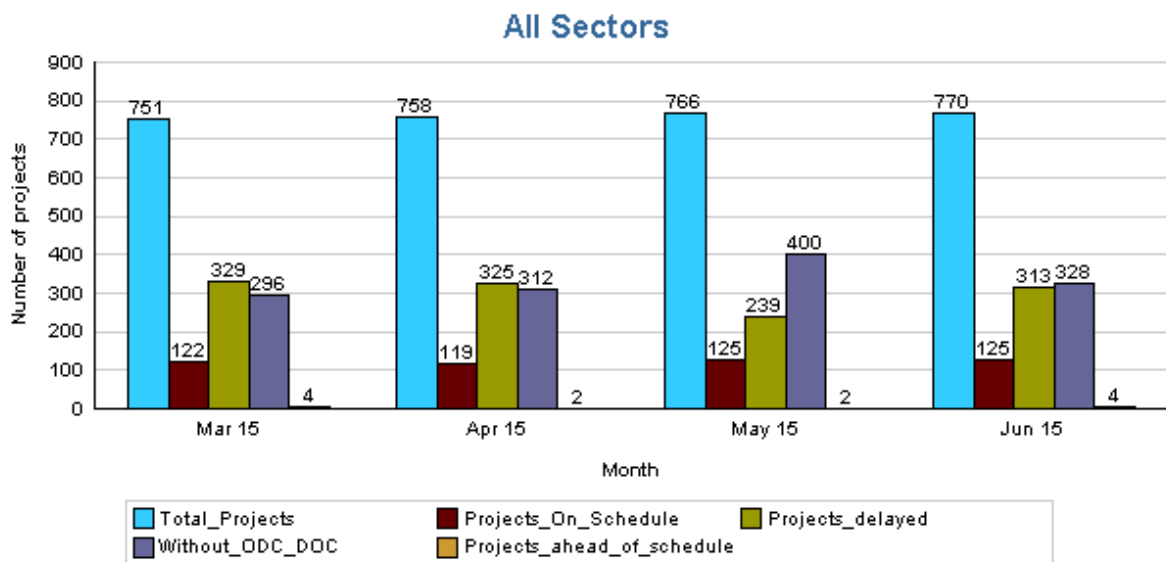


Break-up of 313 Delayed projects in June 2015

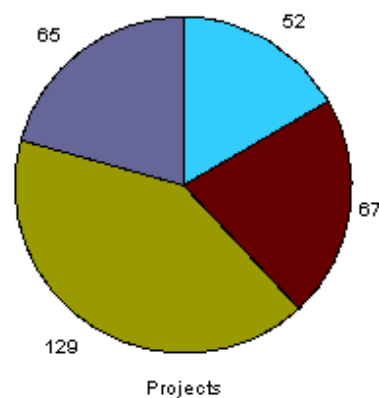


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of All Projects w.r.t. Revised Schedule

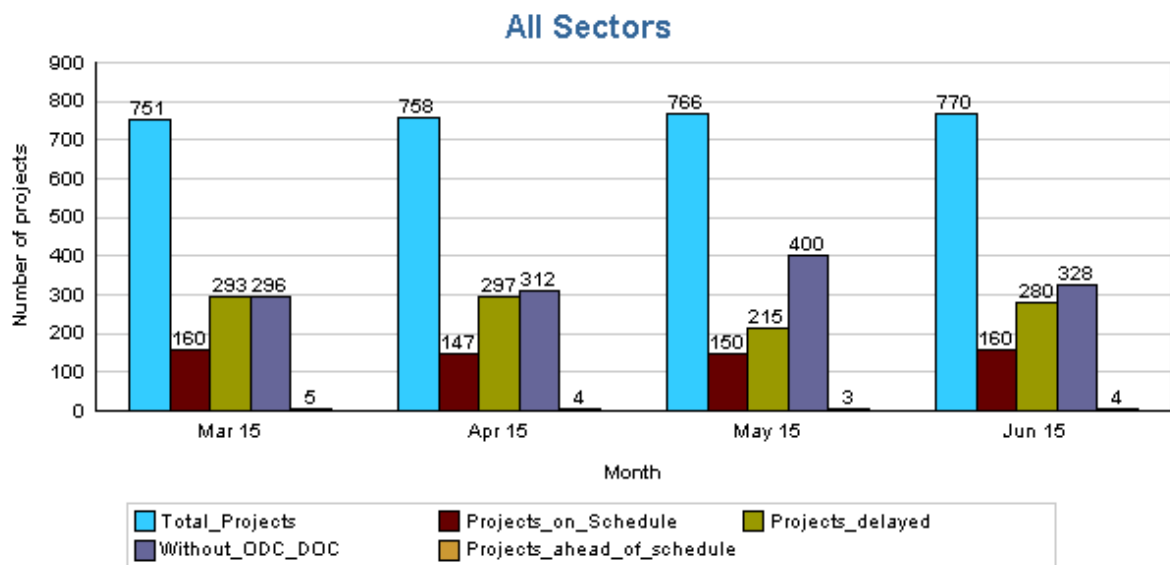


Break-up of 280 Delayed projects in June 2015

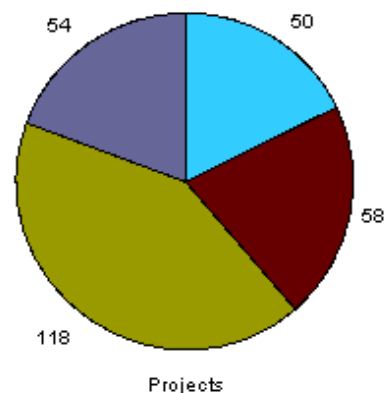


Delay in Months



Graphical Presentation of ATOMIC ENERGY Sector

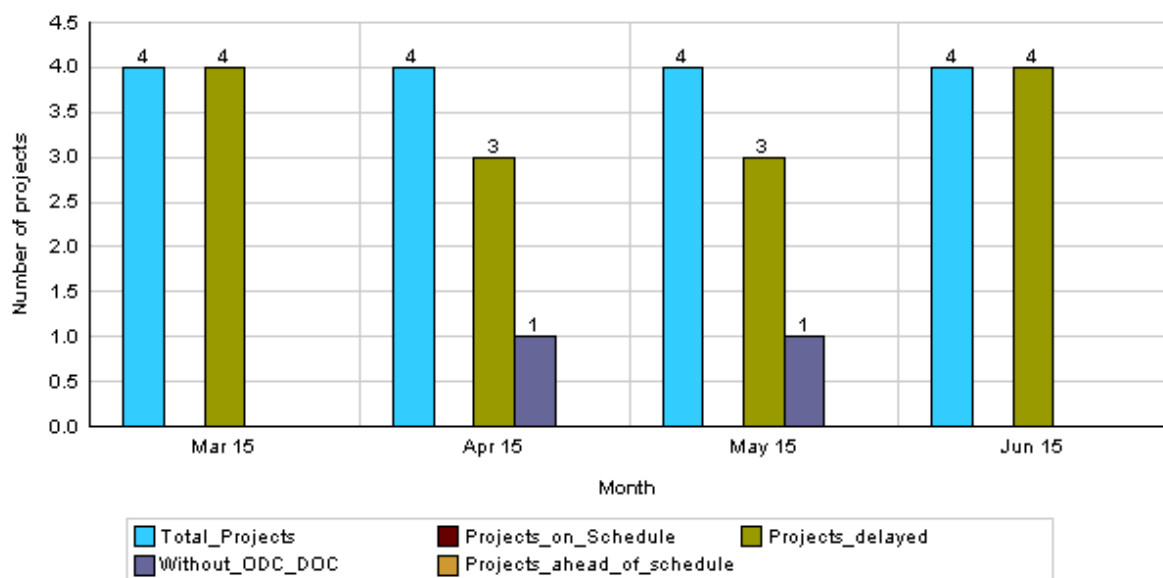


Break-up of 4 Delayed projects in June 2015

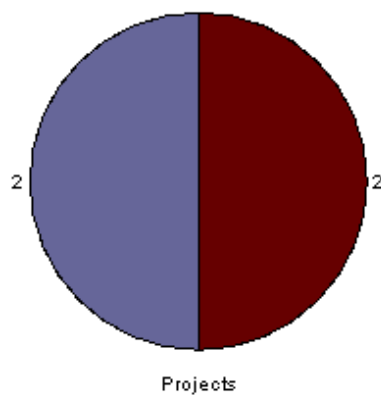


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

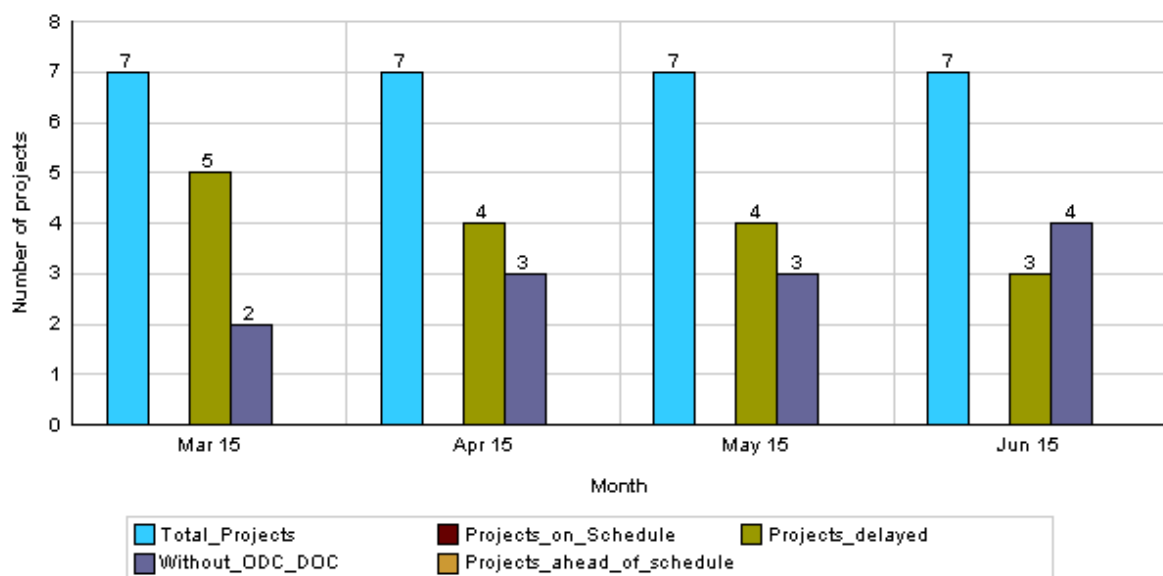


Break-up of 3 Delayed projects in June 2015

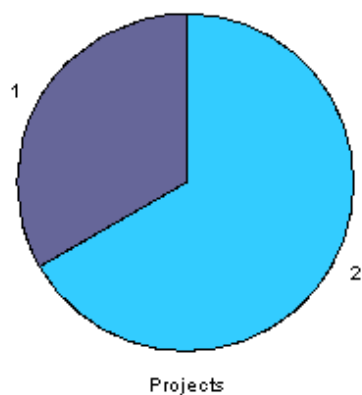


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of COAL Sector

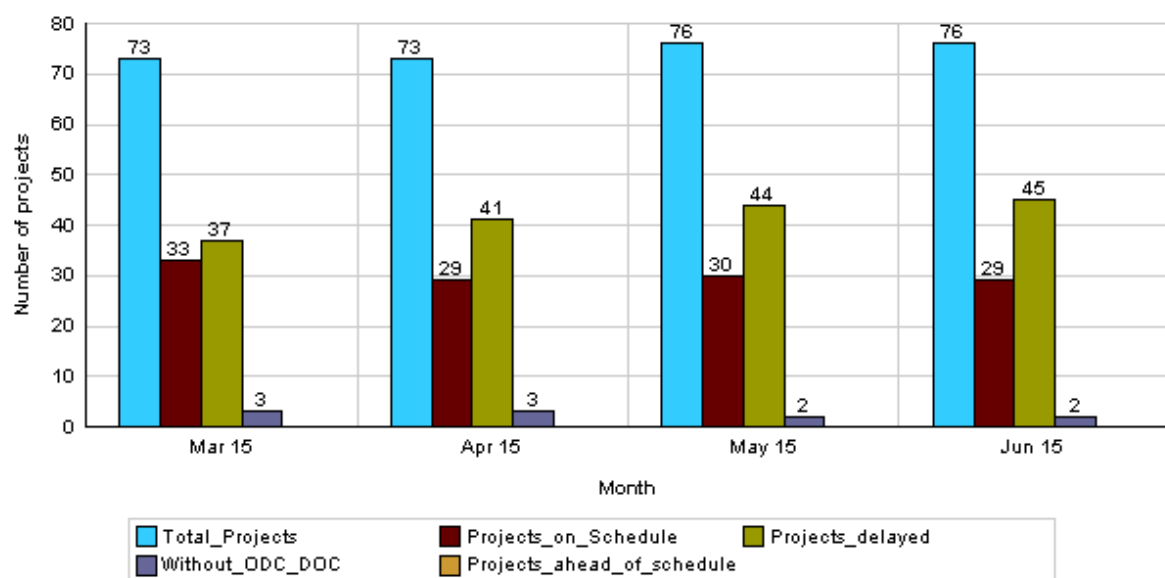


Break-up of 45 Delayed projects in June 2015

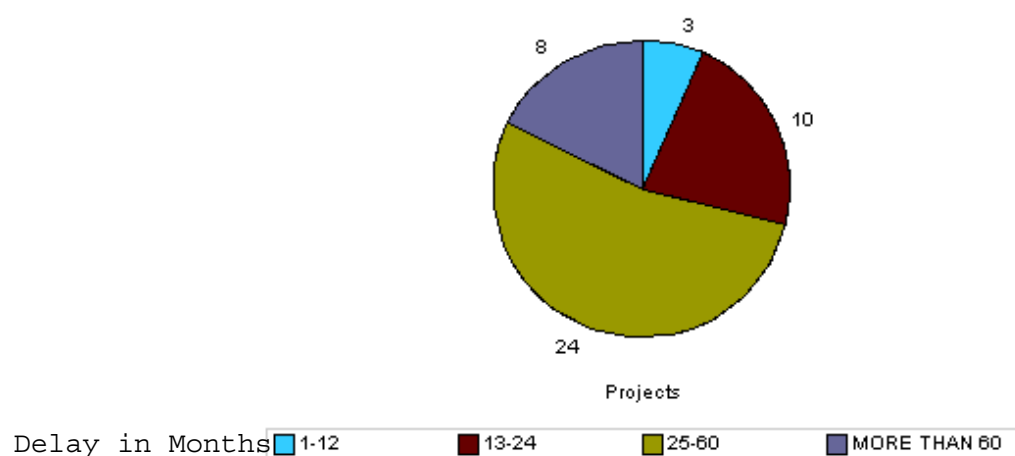

Graphical Presentation of STEEL Sector

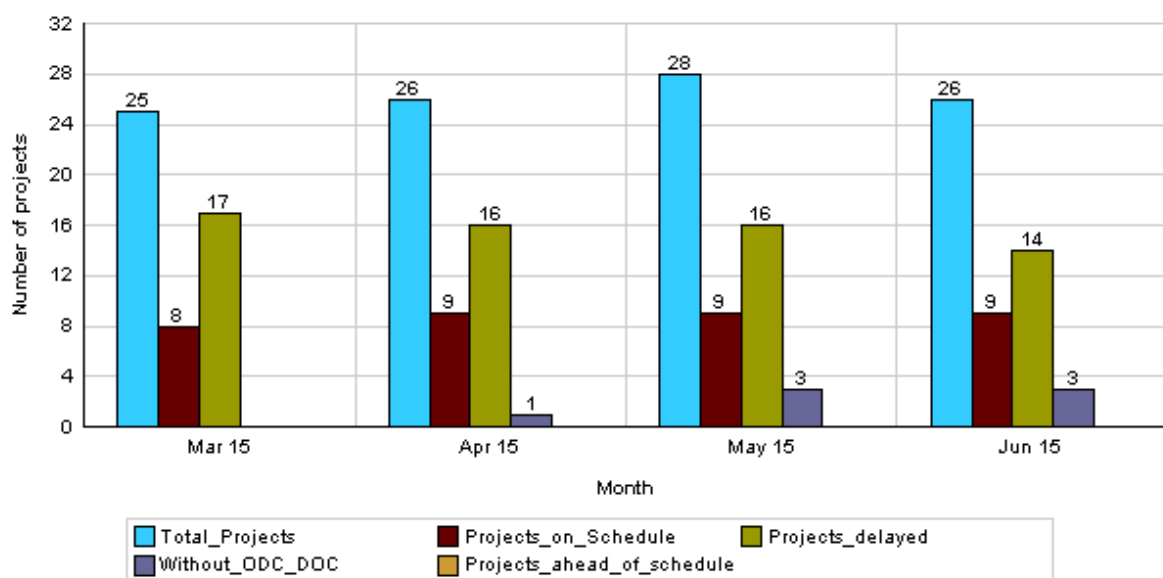


Break-up of 14 Delayed projects in June 2015

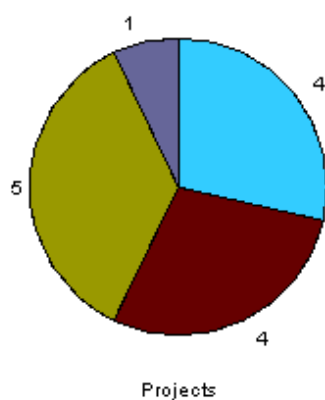


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

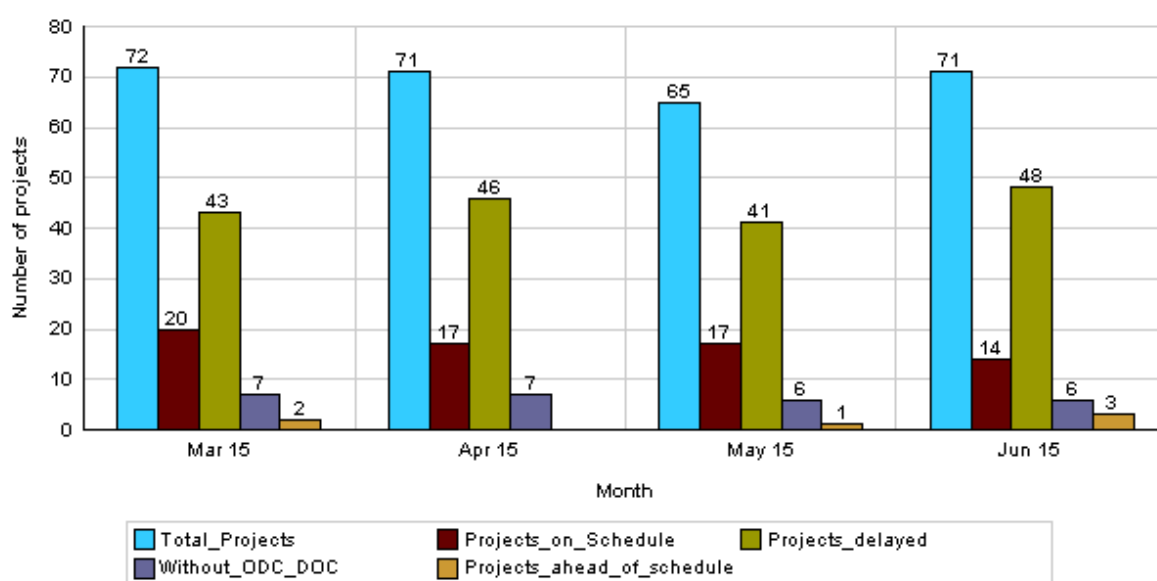


Break-up of 48 Delayed projects in June 2015

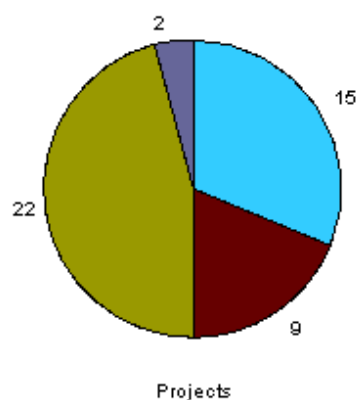


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of POWER Sector

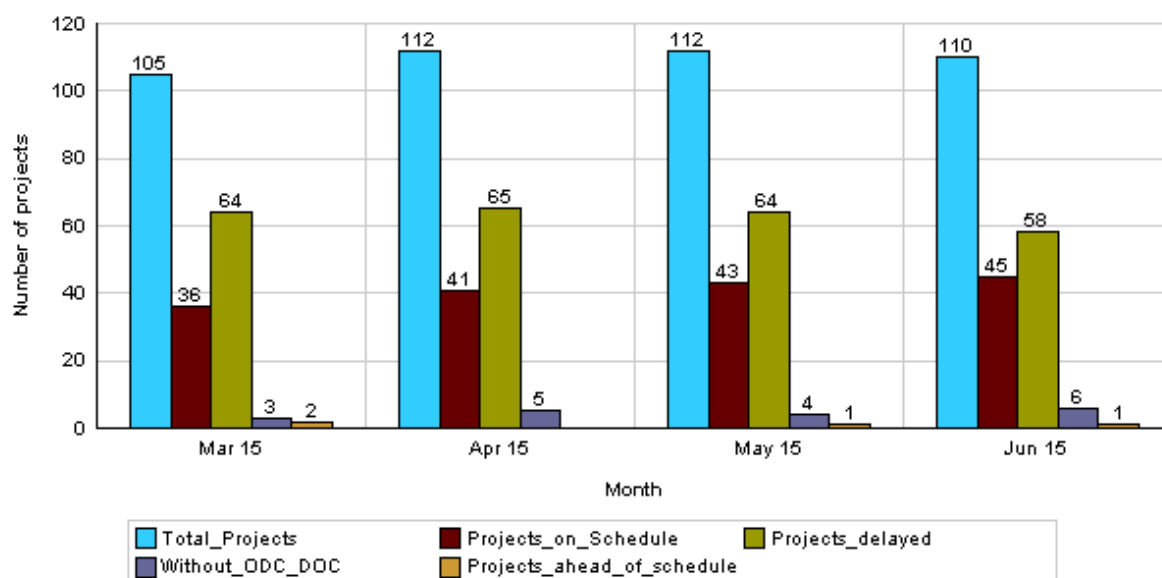


Break-up of 58 Delayed projects in June 2015

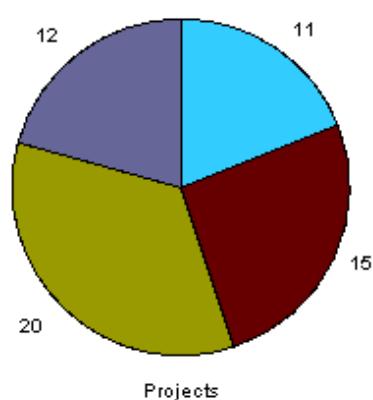


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

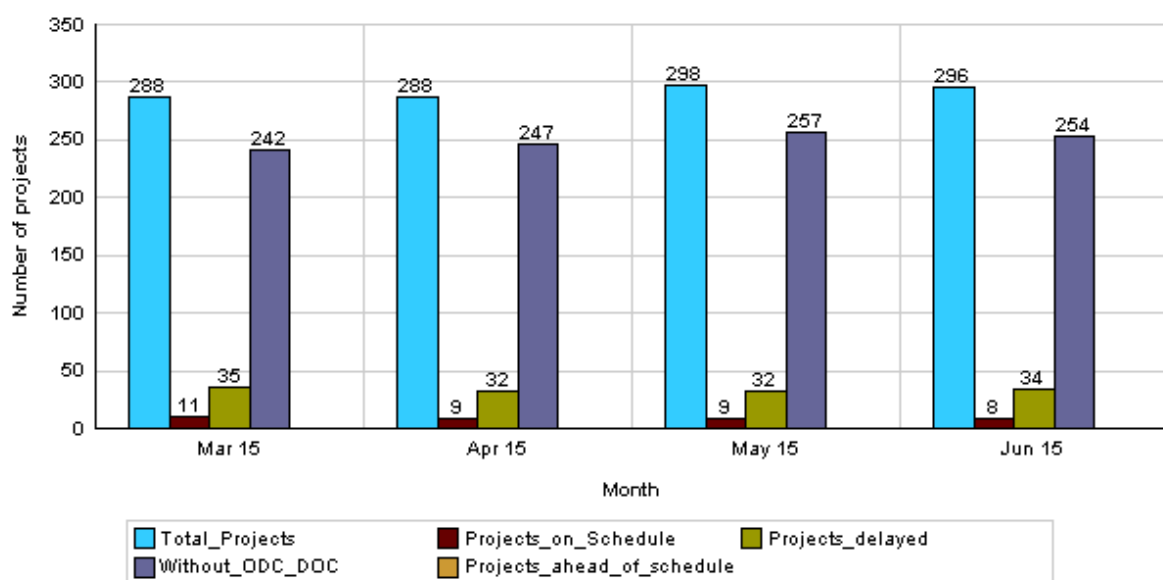


Break-up of 34 Delayed projects in June 2015

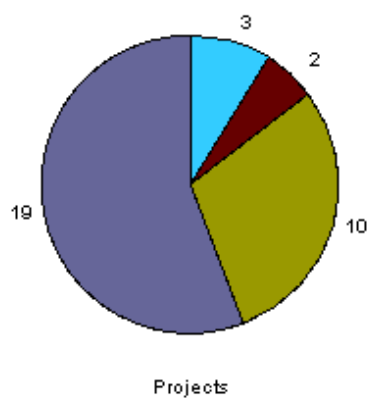


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60


Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

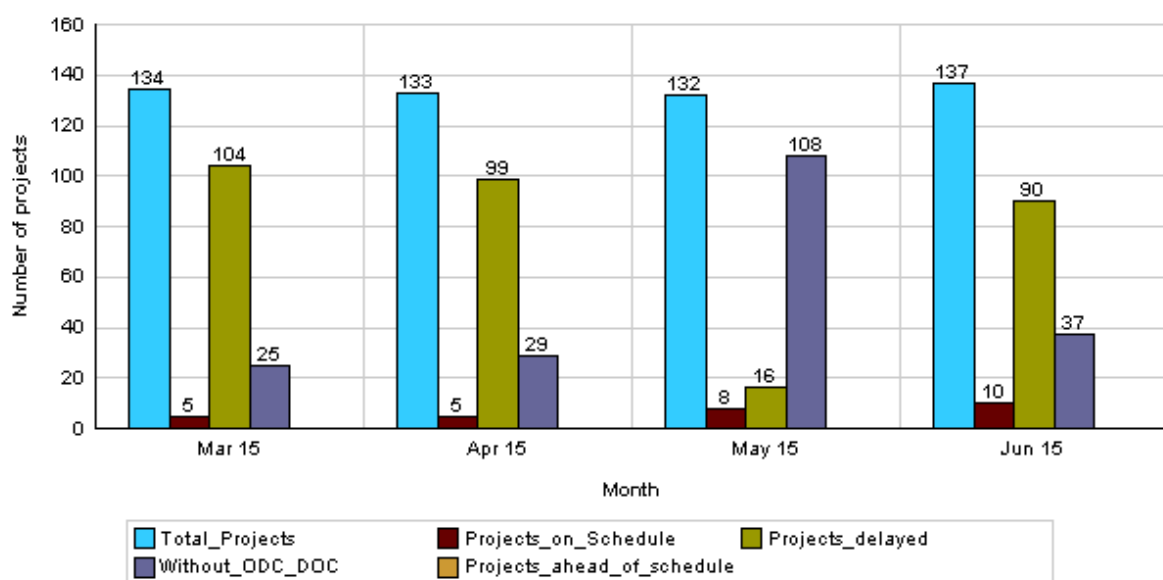


Break-up of 90 Delayed projects in June 2015

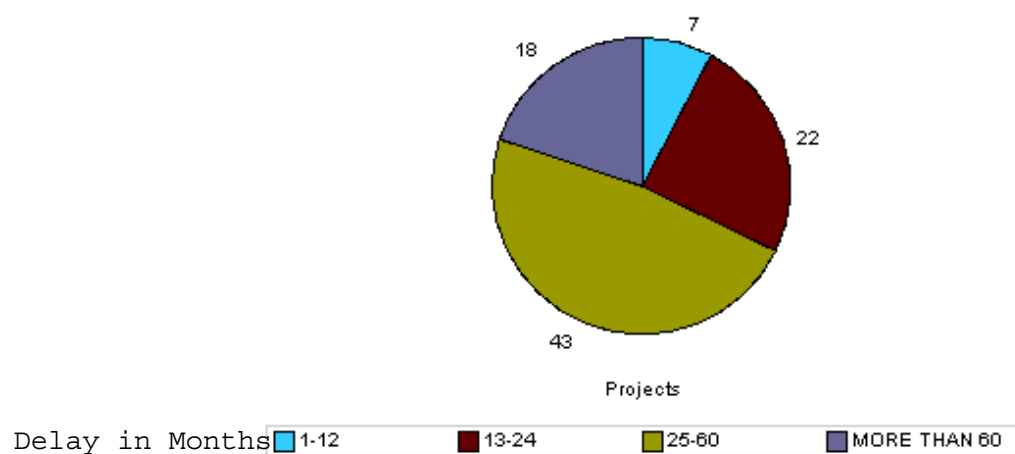


Graphical Presentation of SHIPPING AND PORTS Sector

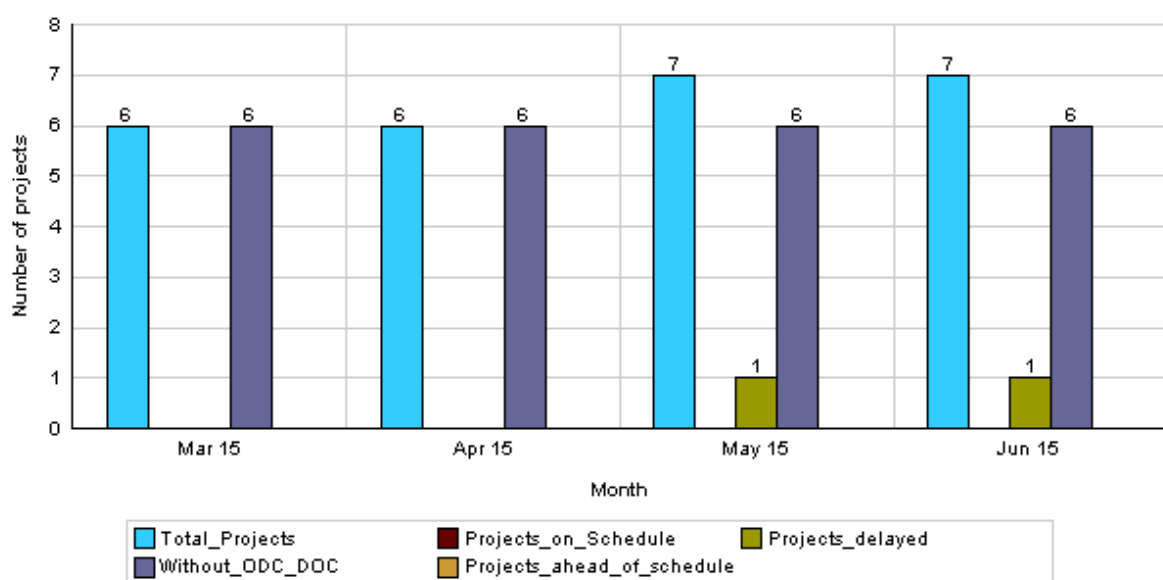


Break-up of 1 Delayed projects in June 2015




Graphical Presentation of TELECOMMUNICATIONS Sector

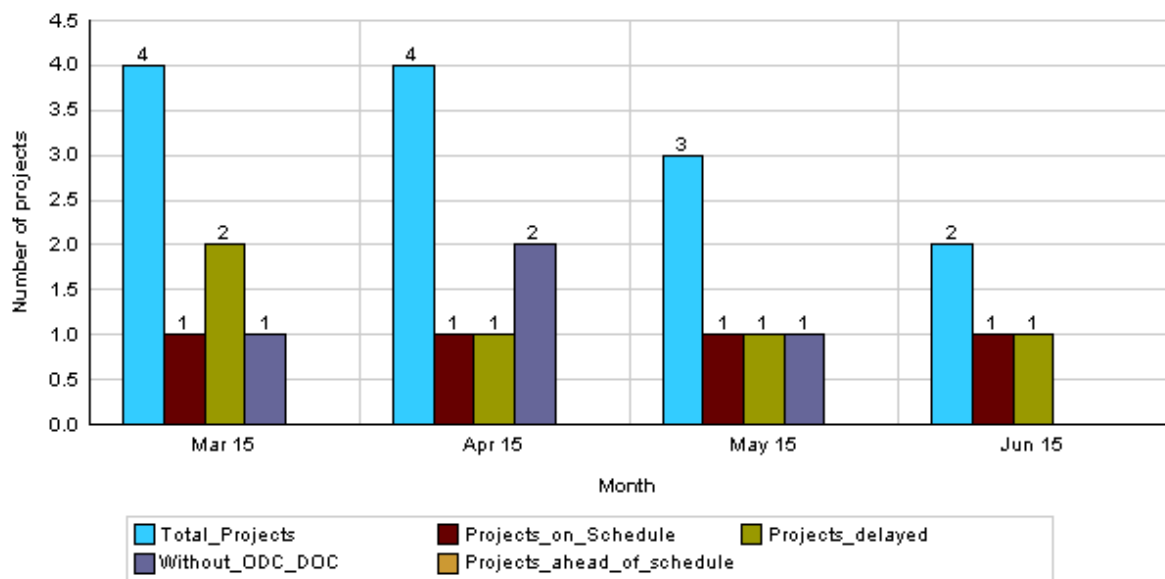


Break-up of 1 Delayed projects in June 2015

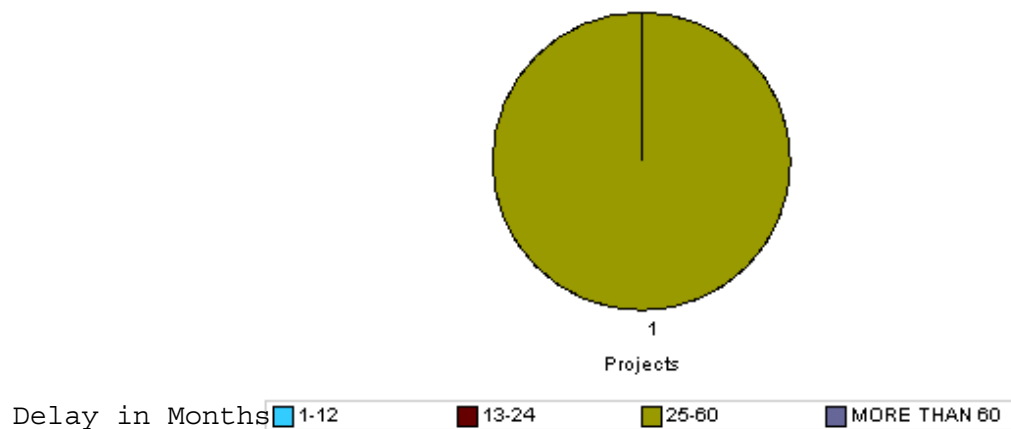

Graphical Presentation of URBAN DEVELOPMENT Sector

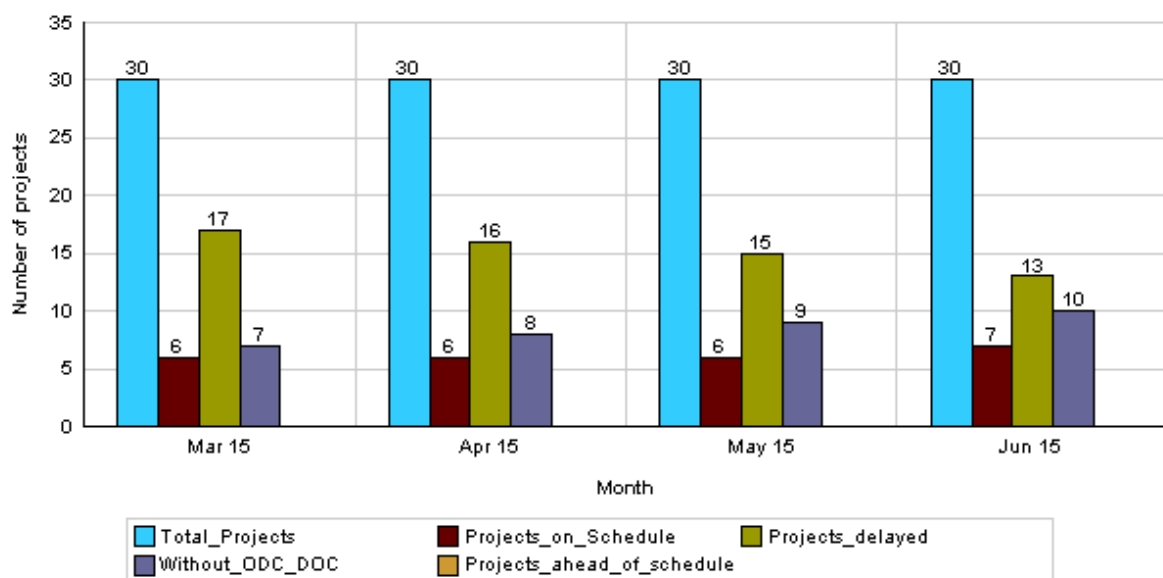

Break-up of 13 Delayed projects in June 2015

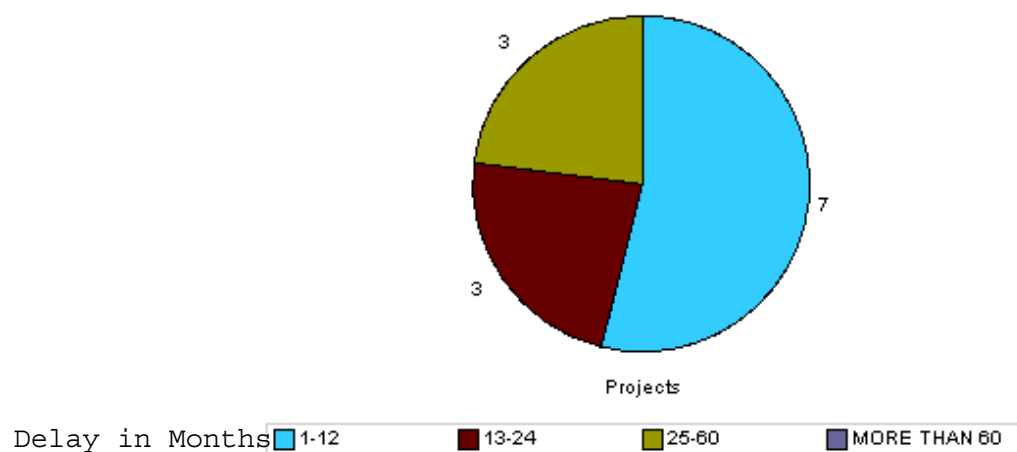

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	46,726.00	46,726.00	37,241.93
CIVIL AVIATION	7	2,599.56	2,636.56	2,715.98	1,675.78
COAL	76	59,478.01	62,985.69	63,381.17	22,383.50
FERTILISERS	1	197.79	197.79	197.79	21.94
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	26	61,866.16	65,465.16	65,580.56	42,179.65
PETROCHEMICALS	1	5,460.61	8,920.00	9,833.52	8,736.89
PETROLEUM	71	153,184.11	165,066.76	167,522.71	70,982.31
POWER	110	310,535.03	333,473.69	350,364.40	169,904.38
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
RAILWAYS	296	171,881.41	185,296.44	297,255.34	90,845.86
ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	100,165.25	102,199.30	89,186.97
SHIPPING AND PORTS	7	5,524.46	5,827.53	6,428.61	2,779.11
TELECOMMUNICATIONS	2	13,718.00	13,718.00	13,718.00	66.02
URBAN DEVELOPMENT	30	138,680.82	138,680.82	143,894.82	21,861.67
Grand total	770	1,067,193.26	1,132,733.69	1,275,501.50	557,866.01

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	6,853.00	12/2015 -	10/2017	22(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	20,713.00	12/2008 -	10/2015	82(O) -	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	5,006.93	09/2010 09/2016	09/2016	72(O) 0(R)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,669.00	12/2016 -	05/2018	17(O) -	4/69
	Total		40,442.00 -	46,726.00	37,241.93				60/329
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	355.88	01/2011 06/2016	06/2017	77(O) 12(R)	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	314.61	17.82	- 09/2018	09/2018	- 0(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61 -	388.53	301.94	05/2012 -	03/2015	-	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00 489.00	489.00	449.63	03/2015 -	07/2015	4(O) -	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28 -	344.28	66.94	03/2014 -	05/2015	-	0/0
10	GAGAN PROJECT - [N04000065]AAI, MULTI STATE	09/2008	626.00 -	626.00	483.53	06/2013 -	-	-	0/0
11	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	244.10	0.04	03/2015 -	09/2015	6(O) -	0/0
	Total		2,599.56 -	2,715.98	1,675.78				0/0
	<u>COAL</u>								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.58	03/2013 09/2012	09/2015	30(O) 36(R)	21/22
13	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	29.60	03/2018 -	03/2018	0(O) -	0/4
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	150.59 -	198.59	111.83	03/2016 -	03/2016	0(O) -	3/7
15	AMLOHRI EPR (NCL) (6 MTY, INCR.) - [N06000010]NCL, MADHYA PRADESH	12/2009	1,352.04 -	1,143.54	803.72	03/2016 -	03/2016	0(O) -	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL, JHARKHAND	02/2012	858.11 -	858.11	107.20	03/2020 -	03/2020	0(O) -	3/4

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
18	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	191.26	03/2012 -	03/2017	60(O) -	4/5
19	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 341.63	341.63	124.92	03/2011 -	03/2017	72(O) -	2/5
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	148.45	03/2010 -	03/2017	84(O) -	2/4
21	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	81.40	03/2016 -	03/2018	24(O) -	3/6
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	-	03/2019 -	03/2019	0(O) -	1/9
23	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	-	1/6
24	BHANEAGAN OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 -	187.94	37.92	03/2023 -	03/2023	0(O) -	5/21
25	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	208.60	03/2017 -	03/2017	0(O) -	11/11
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	76.43	03/2020 -	03/2020	0(O) -	1/6
27	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 535.10	535.10	379.04	03/2015 -	03/2016	12(O) -	0/3
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	0(O) -	1/7
29	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.60	03/2014 -	03/2016	24(O) -	7/9
30	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.92	03/2011 -	03/2016	60(O) -	0/3
31	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020	0(O) -	0/15
32	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,664.03	03/2014 -	03/2016	24(O) -	10/13
33	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	13.38	03/2021 -	03/2021	0(O) -	1/9
34	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,844.83	03/2014 -	03/2016	24(O) -	11/16
35	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	267.67	148.02	03/2018 -	03/2018	0(O) -	2/18
36	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	2/13
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	173.03	03/2013 -	03/2017	48(O) -	4/8
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	-	03/2019 -	03/2019	0(O) -	2/6
39	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60(O) -	1/7
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/13
41	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
42	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.18	225.39	03/2011 -	03/2017	72(O) -	7/15

Sector Wise Details

(June 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63	453.63	99.63	12/2012	03/2017	51(O)	11/44
44	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33	417.33	11.68	07/2016	03/2017	8(O)	6/28
45	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04	371.04	26.13	03/2021	03/2021	0(O)	0/6
46	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	175.03	03/2013	03/2017	48(O)	8/9
47	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35	988.35	43.93	04/2017	04/2017	0(O)	0/2
48	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	65.96	03/2014	03/2017	36(O)	2/4
49	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72(O)	1/7
50	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28	1,131.28	86.01	03/2018	03/2018	0(O)	0/4
51	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29	242.29	0.03	03/2015	03/2018	36(O)	0/5
52	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88	741.62	473.48	03/2013	03/2016	36(O)	0/2
53	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03	289.03	-	03/2018	03/2018	0(O)	1/5
54	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96	302.96	147.57	03/2010	03/2017	84(O)	8/10
55	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	08/2013	7,612.33	7,612.33	764.69	03/2023	03/2023	0(O)	1/17
56	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45	289.45	89.89	05/2014	04/2016	23(O)	0/8
57	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40	706.40	76.55	07/2012	03/2016	44(O)	1/3
58	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA	09/2014	266.23	266.23	85.62	03/2021	03/2021	0(O)	2/23
59	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50	321.50	206.52	03/2014	03/2018	48(O)	4/7
60	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19	181.19	36.60	03/2012	03/2016	48(O)	4/6
61	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27	1,230.27	42.39	04/2015	04/2019	48(O)	0/11
62	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88	339.88	9.97	04/2014	03/2016	23(O)	1/4
63	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56	295.56	52.16	03/2019	03/2019	0(O)	4/20
64	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11	5,907.11	965.20	12/2015	04/2018	28(O)	11/35
65	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40	259.40	21.42	03/2012	03/2016	48(O)	0/2
66	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52	555.52	3.52	03/2021	03/2021	0(O)	0/2
67	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87	179.87	81.52	03/2012	03/2017	60(O)	1/3

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	34.51	04/2014 -	04/2016	24(O) -	0/10
69	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH	11/2014	1,624.59 1,624.59	1,624.59	5.43	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
70	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA	09/2014	441.82 -	441.82	112.65	03/2020 -	03/2020	0(O) -	5/27
71	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	-	03/2013 -	03/2016	36(O) -	3/4
72	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	57.62	03/2014 -	03/2016	24(O) -	3/9
73	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	108.43	03/2021 -	03/2021	0(O) -	0/7
74	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	223.10	03/2016 -	03/2016	0(O) -	2/4
75	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.28	03/2012 -	03/2016	48(O) -	0/2
76	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2019	48(O) -	4/29
77	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 486.27	486.27	69.97	03/2016 -	03/2016	0(O) -	6/39
78	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21(O) -	4/51
79	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	77.47	03/2015 -	04/2016	13(O) -	8/31
80	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	71.72	03/2012 -	03/2018	72(O) -	27/42
81	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026	0(O) -	3/15
82	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	158.97	03/2018 -	03/2018	0(O) -	1/10
83	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
84	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	143.74	03/2012 -	03/2016	48(O) -	2/4
85	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,583.77	3,213.77	06/2009 03/2013	07/2015	73(O) 28(R)	23/23
86	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,277.83	03/2012 05/2014	07/2015	40(O) 14(R)	29/39
87	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	151.74	10/2014 -	08/2015	10(O) -	8/11
	Total		59,478.01 -	63,381.17	22,383.50				312/1004
	<u>FERTILISERS</u>								
88	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 197.79	197.79	21.94	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	197.79	21.94				0/0
	<u>MINES</u>								

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
89	EXPANSION OF MALANKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N1000007]HCL, MADHYA PRADESH	09/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	0(O) -	0/0
	Total		1,856.00 -	1,856.00	.00				0/0
	<u>STEEL</u>								
90	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	463.35	04/2013 09/2014	06/2015	26(O) 9(R)	18/19
91	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND	10/2013	245.67 -	245.67	40.89	05/2016 -	05/2016	0(O) -	1/3
92	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH	07/2011	974.76 -	974.76	128.09	07/2016 -	07/2016	0(O) -	1/2
93	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	387.59	05/2013 01/2015	08/2015	27(O) 7(R)	17/20
94	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL, JHARKHAND	03/2015	255.19 -	255.19	-	03/2018 -	03/2018	0(O) -	0/0
95	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	388.34	09/2009 05/2012	07/2015	70(O) 38(R)	1/1
96	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	607.17 -	607.17	391.51	12/2011 01/2015	03/2015	-	20/20
97	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	260.12	07/2015 -	03/2016	8(O) -	1/2
98	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00 -	677.00	522.58	09/2013 -	07/2015	22(O) -	0/1
99	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	199.46	08/2014 -	11/2015	15(O) -	4/5
100	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93 -	188.93	32.93	04/2015 -	04/2015	-	1/4
101	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,537.66	03/2013 -	03/2016	36(O) -	31/35
102	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,164.71	12/2011 -	08/2015	44(O) -	21/25
103	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [N120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,339.32	10/2009 10/2012	04/2015	-	69/70
104	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	158.95	10/2013 -	12/2015	26(O) -	2/6
105	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	132.35	09/2014 -	07/2015	10(O) -	1/3
106	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018	0(O) -	0/0
107	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017	0(O) -	0/0
108	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017	0(O) -	0/0

Sector Wise Details

(June 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	7,257.18	05/2015 12/2016	12/2016	19(O) 0(R)	17/81
110	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	249.80	06/2015 -	12/2015	6(O) -	3/4
111	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	192.84	12/2014 -	09/2015	9(O) -	1/3
112	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	25.02	10/2016 -	10/2016	0(O) -	0/0
113	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	152.00	07/2015 -	03/2017	20(O) -	0/1
114	TURBO BLOWER - 5 - [N12000092]RINL, ANDHRA PRADESH	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016	0(O) -	0/1
115	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	141.19	04/2016 -	04/2016	0(O) -	2/2
	Total		61,866.16 -	65,580.56	42,179.65				211/308
	<u>PETROCHEMICALS</u>								
116	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,736.89	04/2012 12/2013	09/2015	41(O) 21(R)	21/26
	Total		5,460.61 -	9,833.52	8,736.89				21/26
	<u>PETROLEUM</u>								
117	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39(O) 6(R)	0/1
118	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE	03/2014	2,476.82 -	2,476.82	67.33	12/2018 -	12/2018	0(O) -	3/9
119	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36(O) -	0/0
120	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48(O) -	0/0
121	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,777.84	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
122	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	316.02	08/2015 -	12/2015	4(O) -	0/12
123	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	1,823.00	-	- -	-	-	0/0
124	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL, ANDHRA PRADESH	07/2014	419.04 -	419.04	123.49	01/2017 -	06/2016	-7(O) -	0/0
125	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015	51(O) 0(R)	0/0
126	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 06/2015	06/2015	22(O) 0(R)	0/0
127	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	114.88	09/2012 12/2015	12/2015	39(O) 0(R)	0/5

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
128	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC, ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 -	06/2018	53(O) -	0/2
129	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC, MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39(O) 0(R)	0/0
130	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	885.75	05/2013 06/2014	12/2015	31(O) 18(R)	1/5
131	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL, MULTI STATE	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016	0(O) -	0/0
132	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	6,086.08	47.07	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
133	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,234.16	08/2015 -	12/2015	4(O) -	0/12
134	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	541.46	05/2014 05/2016	05/2016	24(O) 0(R)	0/21
135	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 06/2012	06/2015	110(O) 36(R)	5/5
136	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC, MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
137	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
138	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,436.51	01/2014 12/2015	12/2015	23(O) 0(R)	0/13
139	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 429.00	429.06	330.19	10/2014 10/2015	10/2015	12(O) 0(R)	0/0
140	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	96.08	09/2017 -	12/2017	3(O) -	0/0
141	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	711.00	6.52	- -	-	-	0/0
142	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC, MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,770.24	05/2015 05/2015	07/2015	2(O) 2(R)	0/17
143	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM	02/2014	163.88 -	163.88	21.93	07/2016 -	07/2016	0(O) -	2/6
144	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,204.41	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
145	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC, MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	335.37	02/2016 12/2017	12/2017	22(O) 0(R)	0/0
146	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2017	12(O) 12(R)	0/6
147	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	14,225.00 -	16,504.00	7,147.44	05/2016 -	05/2016	0(O) -	0/30
148	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	127.55	03/2014 05/2016	05/2016	26(O) 0(R)	0/3
149	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	3,957.00 -	3,957.00	5.70	01/2013 -	12/2018	71(O) -	0/0
150	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE	02/2015	890.00 -	890.00	0.05	- -	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
151	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00	2,915.00	1,345.03	12/2012	06/2015	30(O)	0/14
152	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06	607.06	57.94	01/2016	07/2017	18(O)	11/48
153	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00	838.08	481.49	11/2015	11/2016	12(O)	25/29
154	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75	239.73	190.20	07/2013	10/2015	27(O)	0/1
155	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86	219.00	141.77	09/2016	12/2015	-9(O)	0/12
156	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00	3,823.00	1,076.57	04/2015	12/2017	32(O)	0/0
157	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47	5,813.25	1,357.45	05/2017	05/2017	0(O)	6/16
158	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00	279.00	158.12	12/2014	09/2015	9(O)	57/58
159	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80	6,068.80	272.32	04/2019	03/2019	-1(O)	0/0
160	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87	257.87	5.37	11/2016	11/2016	0(O)	0/0
161	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83	171.83	-	-	-	-	0/0
162	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00	913.00	416.70	08/2015	06/2016	10(O)	0/0
163	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00	2,321.00	0.82	-	-	-	0/0
164	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00	690.00	-	07/2018	07/2018	0(O)	0/31
165	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00	34,555.00	29,273.28	11/2012	10/2015	35(O)	87/100
166	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00	1,793.00	1,146.48	09/2012	03/2016	42(O)	6/7
167	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50	238.50	1.07	03/2017	03/2017	0(O)	0/0
168	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25	160.16	57.16	07/2016	07/2016	0(O)	5/12
169	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00	3,150.00	98.95	09/2017	09/2017	0(O)	0/0
170	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00	215.66	-	06/2012	11/2015	41(O)	0/0
171	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50	686.58	449.51	04/2015	12/2015	8(O)	0/0
172	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00	1,419.00	1,171.43	12/2014	08/2015	8(O)	0/20
173	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00	480.00	37.49	02/2016	05/2016	3(O)	2/6
174	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36	3,110.36	699.72	11/2015	07/2016	8(O)	38/52

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
175	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	89.83	05/2015 -	12/2015	7(O) -	0/12
176	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016	0(O) 0(R)	0/0
177	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	1,066.43	11/2015 -	11/2015	0(O) -	18/24
178	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
179	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	970.98	10/2011 -	01/2016	51(O) -	0/0
180	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,404.06	01/2012 -	01/2016	48(O) -	0/0
181	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,079.05	10/2011 -	06/2015	44(O) -	0/0
182	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.44	04/2015 -	-	-	0/0
183	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	214.19	130.94	12/2016 -	12/2016	0(O) -	0/0
184	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	225.72	08/2012 06/2015	06/2015	34(O) 0(R)	1/1
185	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAJUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	273.36	03/2015 11/2015	06/2016	15(O) 7(R)	0/5
186	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	237.49	10/2014 10/2016	10/2016	24(O) 0(R)	26/40
187	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	280.86	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
	Total		153,184.11 -	167,522.71	70,982.31				311/700
	POWER								
188	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	315.66	12/2014 -	05/2015	-	9/17
189	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	1.00	05/2016 -	05/2016	0(O) -	0/6
190	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 10,852.46	10,852.46	8,664.00	10/2013 -	03/2015	-	20/20
191	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,899.00	01/2011 10/2014	03/2018	86(O) 41(R)	26/46
192	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,287.00	09/2011 -	03/2017	66(O) -	15/37
193	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,753.79	05/2014 -	06/2017	37(O) -	0/0
194	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	771.05	12/2015 -	03/2016	3(O) -	15/18

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
195	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGY PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13	1,940.13	1,813.96	09/2014	06/2016	21(O)	8/13
196	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24	1,909.24	765.33	06/2015	12/2015	6(O)	3/5
197	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44	206.44	43.97	06/2014	-	-	11/20
198	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20	514.20	142.20	06/2015	12/2015	6(O)	7/10
199	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52	1,394.52	-	05/2017	05/2017	0(O)	0/9
200	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33	780.33	-	07/2017	07/2017	0(O)	0/0
201	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44	12,532.44	1,639.00	08/2018	08/2018	0(O)	13/14
202	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42	195.42	27.73	02/2014	09/2017	43(O)	1/1
203	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58	196.58	1.00	02/2016	02/2016	0(O)	5/17
204	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80	1,272.80	1,110.83	11/2012	12/2016	49(O)	7/13
205	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52	1,364.52	236.94	04/2016	04/2016	0(O)	8/12
206	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29	522.29	24.80	11/2016	11/2016	0(O)	0/12
207	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63	198.63	75.53	09/2014	06/2016	21(O)	0/0
208	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40	197.40	-	04/2018	04/2018	0(O)	0/0
209	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87	1,961.87	1,713.45	05/2014	03/2016	22(O)	7/12
210	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12	3,363.12	651.00	12/2016	12/2016	0(O)	13/15
211	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55	11,638.55	3,246.00	09/2017	09/2017	0(O)	16/41
212	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30	1,479.30	16.30	04/2017	04/2017	0(O)	0/8
213	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61	3,705.61	-	04/2018	04/2018	0(O)	0/9

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
214	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	2.30	07/2016 -	07/2016	0(O) -	0/9
215	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017	0(O) -	0/0
216	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	474.07	10/2016 -	12/2015	-10(O) -	8/10
217	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	77.70	04/2018 -	04/2018	0(O) -	0/12
218	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	1,000.61	12/2007 12/2009	12/2015	96(O) 72(R)	4/7
219	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,892.98	12/2009 03/2017	03/2017	87(O) 0(R)	16/29
220	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,916.06	01/2013 -	03/2016	38(O) -	0/1
221	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,996.61	01/2016 -	11/2016	10(O) -	4/9
222	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	8,494.00	01/2017 -	01/2017	0(O) -	24/31
223	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,893.05	09/2008 03/2012	03/2016	90(O) 48(R)	20/22
224	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	4,295.00	06/2017 -	06/2017	0(O) -	19/39
225	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017	0(O) -	0/9
226	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,201.00	09/2016 -	09/2016	0(O) -	22/28
227	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9(O) -	0/1
228	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	2,106.00	02/2019 -	02/2019	0(O) -	5/5
229	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,005.30	08/2013 -	03/2016	31(O) -	11/26
230	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	46.40	06/2016 -	06/2016	0(O) -	8/18
231	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	485.72	07/2013 05/2015	11/2015	28(O) 6(R)	7/9
232	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	330.37	02/2012 -	03/2016	49(O) -	7/10
233	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	468.06	11/2011 -	03/2016	52(O) -	8/11
234	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	38.80	06/2016 -	06/2016	0(O) -	8/11
235	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,313.72	04/2013 -	03/2016	35(O) -	7/11
236	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	521.62	11/2014 -	12/2015	13(O) -	7/10
237	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	265.19	03/2016 -	03/2016	0(O) -	8/12

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	190.22	04/2015 -	09/2015	5(O) -	8/12
239	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	735.24	11/2012 -	03/2016	40(O) -	7/10
240	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	3,767.88	01/2018 -	01/2018	0(O) -	0/0
241	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0
242	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,109.77	09/2009 -	12/2018	111(O) -	8/14
243	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,007.62	08/2013 -	03/2016	31(O) -	28/38
244	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,381.84	111.00	09/2019 -	09/2019	0(O) -	3/3
245	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,974.00	11/2016 -	08/2017	9(O) -	20/24
246	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	2.00	08/2016 -	08/2016	0(O) -	0/4
247	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	63.10	12/2015 -	12/2015	0(O) -	5/8
248	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/3
249	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,737.41	09/2010 -	-	-	0/0
250	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH	03/2015	550.06 -	550.06	1.60	03/2018 -	03/2018	0(O) -	0/3
251	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	811.38	03/2015 -	09/2015	6(O) -	15/21
252	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	12.40	02/2017 -	02/2017	0(O) -	0/12
253	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	197.49	06/2012 -	-	-	1/4
254	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	198.64	03/2014 -	07/2015	16(O) -	5/7
255	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,214.43	08/2014 12/2015	03/2016	19(O) 3(R)	7/11
256	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,052.09	08/2012 -	03/2016	43(O) -	3/5
257	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	112.90	08/2016 -	08/2016	0(O) -	8/10
258	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	203.28	0.20	07/2017 -	07/2017	0(O) -	0/5
259	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,088.18	11/2014 -	09/2015	10(O) -	8/10

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
260	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,149.72	01/2015 -	03/2016	14(O) -	9/11
261	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE	12/2011	297.33 346.79	346.79	282.57	08/2014 06/2015	12/2015	16(O) 6(R)	8/10
262	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	487.49	374.72	06/2014 -	-	-	8/12
263	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	718.00	03/2019 -	03/2019	0(O) -	6/10
264	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,480.00	03/2013 -	12/2018	69(O) -	1/15
265	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,787.90	09/2009 -	06/2016	81(O) -	2/6
266	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL, UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,292.48	07/2010 02/2016	05/2018	94(O) 27(R)	6/21
267	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL, MULTI STATE	12/2011	2,422.66 -	2,422.66	1,941.66	08/2014 -	09/2015	13(O) -	8/14
268	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44 -	3,201.44	2,397.31	10/2014 -	03/2016	17(O) -	8/17
269	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 -	4,824.12	4,086.48	10/2012 -	03/2016	41(O) -	7/11
270	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL, GUJARAT	02/2014	378.71 -	378.71	70.90	10/2016 -	10/2016	0(O) -	8/11
271	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL, MULTI STATE	01/2015	268.80 -	268.80	0.80	03/2018 -	03/2018	0(O) -	0/3
272	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 -	1,927.16	1,510.47	10/2014 -	09/2015	11(O) -	11/15
273	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL, MULTI STATE	06/2014	400.47 -	400.47	6.40	04/2017 -	04/2017	0(O) -	0/3
274	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL, MULTI STATE	09/2013	1,575.30 -	1,575.30	322.10	05/2016 -	05/2016	0(O) -	8/13
275	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL, MULTI STATE	02/2010	2,144.00 -	2,144.00	2,156.70	12/2012 -	03/2016	39(O) -	7/23
276	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62 -	871.62	1.90	11/2017 -	11/2017	0(O) -	0/5
277	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL, ANDHRA PRADESH	08/2014	188.75 -	188.75	1.00	02/2017 -	02/2017	0(O) -	0/2
278	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	520.00	02/2014 -	09/2015	19(O) -	8/10
279	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,498.75	01/2015 -	03/2016	14(O) -	8/16

Sector Wise Details

(June 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
280	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	454.91	11/2013 -	12/2015	25(O) -	8/12
281	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,854.54	03/2013 06/2015	09/2015	30(O) 3(R)	8/11
282	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,825.87	03/2014 06/2015	08/2015	17(O) 2(R)	10/13
283	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,750.90	12/2013 -	09/2015	21(O) -	9/11
284	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	135.50	01/2013 -	09/2015	32(O) -	10/15
285	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,485.26	11/2013 -	12/2015	25(O) -	8/12
286	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH-PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	312.94	-	06/2016 -	06/2016	0(O) -	0/0
287	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,727.47	11/2012 -	07/2015	32(O) -	8/13
288	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,199.43	07/2014 -	03/2016	20(O) -	6/8
289	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	481.30	03/2018 -	03/2018	0(O) -	8/12
290	TRIPURA GAS BASED POWER PROJECT - [N18000071]NPEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	914.86	07/2013 -	08/2015	25(O) -	25/26
291	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NPEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	843.49	07/2006 12/2015	10/2016	123(O) 10(R)	5/13
292	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
293	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	05/2012	3,180.40 -	3,180.40	1,869.00	08/2015 -	08/2015	0(O) -	24/25
294	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	647.32	06/2013 12/2019	12/2019	78(O) 0(R)	2/8
295	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	3,662.02	28.80	05/2018 -	05/2018	0(O) -	0/5
296	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	520.99	09/2010 06/2013	03/2016	66(O) 33(R)	4/8
297	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,478.09	06/2015 -	03/2016	9(O) -	20/30
	Total		310,535.03 -	350,364.40	169,904.38				771/1339
	HEAVY INDUSTRY								

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
298	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	.00				0/0
	<u>RAILWAYS</u>								
299	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	60.84	03/2016 -	03/2016	0(O) -	0/0
300	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
301	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
302	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
303	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66(O) 51(R)	0/0
304	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
305	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
306	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
307	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	873.71	-	- -	-	-	0/0
308	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	23.63	- -	-	-	0/0
309	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
310	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
311	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
312	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	0.02	- -	-	-	0/0
313	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	129.14	- -	-	-	0/0
314	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
315	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
316	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.86	- -	-	-	0/0
317	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
318	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
319	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
320	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	-	-	-	0/0
321	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	960.00	-	-	-	-	0/0
322	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	-	-	-	0/0
323	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	76.08	-	-	-	0/0
324	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	100.76	-	-	-	0/0
325	BANDEL-BOINCHI 3RD LINE - [N22000221]JER,MULTI STATE	04/2011	288.35 -	288.35	9.60	-	-	-	0/0
326	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]JER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33(O) -	0/0
327	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	1,382.78	2.81	-	-	-	0/0
328	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]JNR,RAJASTHAN	04/2012	246.08 -	246.08	4.20	-	-	-	0/0
329	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
330	BARDHAMAN-KATWA (GC) - [N22000091]JER,WEST BENGAL	04/2007	1,106.62 -	1,106.62	244.99	12/2010 -	-	-	0/0
331	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]JER,MULTI STATE	04/2007	450.55 -	450.55	13.53	-	-	-	0/0
332	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]JER,WEST BENGAL	04/2012	255.64 -	255.64	-	-	-	-	0/0
333	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
334	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	337.50	0.21	-	-	-	0/0
335	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	923.23	1.01	-	-	-	0/0
336	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	837.33	1.15	-	-	-	0/0
337	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	760.00	0.09	-	-	-	0/0
338	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
339	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	-	-	-	0/0
340	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
341	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	94.11	-	-	-	0/0
342	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69(O) -	0/0
343	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
344	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20	326.20	1.68	-	-	-	0/0
345	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80	175.80	1.46	-	-	-	0/0
346	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37	434.00	35.90	-	-	-	0/0
347	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00	4,996.19	3,410.06	04/2008	06/2017	110(O) 39(R)	0/0
348	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00	579.37	599.40	-	02/2012	-	0/0
349	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90	230.00	68.67	03/2015	12/2016	21(O)	0/0
350	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14	328.14	0.30	-	-	-	0/0
351	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96	337.96	61.36	-	-	-	0/0
352	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00	951.24	619.87	-	03/2015	-	0/0
353	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72	222.95	112.40	-	-	-	0/0
354	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24	520.00	462.69	-	-	-	0/0
355	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52	1,200.00	2.07	-	-	-	0/0
356	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00	494.92	4.22	-	-	-	0/0
357	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07	378.56	111.71	-	-	-	0/0
358	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79	1,101.16	194.91	-	03/2017	-	0/0
359	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78	243.78	30.05	-	-	-	0/0
360	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	367.77	-	-	-	-	0/0
361	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	692.43	-	-	-	-	0/0
362	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91	595.91	89.60	-	-	-	0/0
363	CHOTTADEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26	1,347.26	164.55	-	-	-	0/0
364	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78	573.78	166.89	-	-	-	0/0
365	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00	1,242.25	1,005.81	03/2007	03/2016	108(O)	0/0
366	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68	556.64	268.56	-	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
367	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00	829.00	-	-	-	-	0/0
368	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13	225.00	193.37	-	10/2014	-	0/0
369	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04	1,640.04	187.84	-	-	-	0/0
370	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38	533.38	114.38	12/2011	-	-	0/0
371	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00	968.60	139.48	12/2012	-	-	0/0
372	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44	583.00	144.66	12/2015	03/2016	3(O)	0/0
373	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92	339.00	204.83	-	-	-	0/0
374	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44	296.44	4.55	-	-	-	0/0
375	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00	205.00	5.21	-	-	-	0/0
376	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08	410.08	297.44	-	-	-	0/0
377	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16	234.71	137.01	03/2015	03/2015	-	0/0
378	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00	1,239.00	-	-	-	-	0/0
379	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91	336.91	144.05	-	-	-	0/0
380	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09	607.09	561.14	12/2012	-	-	0/0
381	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59	376.59	4.58	-	-	-	0/0
382	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41	2,030.50	3.61	02/2019	02/2019	0(O)	0/0
383	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63	1,009.00	7.50	-	12/2019	-	0/0
384	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00	4,487.70	-	-	03/2020	-	0/0
385	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17	914.98	846.18	-	03/2016	-	0/0
386	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58	4,874.58	1,911.65	03/2016	06/2018	27(O)	0/0
387	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10	275.08	141.55	03/2012	03/2016	48(O)	0/0
388	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24	189.24	1.52	-	-	-	0/0
389	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57	603.22	1.64	-	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
390	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82(O) -	0/0
391	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, TAMIL NADU	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
392	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
393	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	1.89	- -	-	-	0/0
394	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
395	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	14.00	- -	-	-	0/0
396	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
397	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
398	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
399	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	177.01	02/2006 -	03/2016	121(O) -	0/0
400	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
401	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
402	GUDUR-DURGARA,JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
403	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0
404	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
405	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	179.32	37.80	- -	-	-	0/0
406	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
407	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
408	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	720.00	-	- -	-	-	0/0
409	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	367.17	17.19	- -	-	-	0/0
410	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	324.66	225.49	- -	-	-	0/0
411	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
412	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
413	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	266.35	- 09/2009	-	-	0/0
414	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	2.38	- -	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
415	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	1,092.98	-	-	-	0/0
416	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	172.58	-	-	-	0/0
417	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	94.65	03/2015 -	03/2015	-	0/0
418	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	-	-	-	0/0
419	HOSADURGA - CHICKKAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	153.29	-	09/2015	-	0/0
420	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	325.00	-	-	-	0/0
421	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	1,618.00	-	-	-	-	0/0
422	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	-	-	-	0/0
423	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	-	0/0
424	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	-	-	-	0/0
425	HUBLI- CHIKKAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	1,900.00	-	-	-	-	0/0
426	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	117.24	-	-	-	0/0
427	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
428	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.55	258.74	03/2014 -	-	-	0/0
429	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	143.62	-	-	-	0/0
430	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
431	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	1,043.56	819.19	03/2012 -	-	-	0/0
432	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	40.00	-	-	-	0/0
433	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	230.00	218.67	-	-	-	0/0
434	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
435	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
436	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.45	-	-	-	0/0
437	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	-	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
438	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
439	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0
440	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
441	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
442	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	1/1
443	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	800.66	- -	-	-	0/0
444	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
445	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
446	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	0(O) -	0/0
447	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	7.96	- -	-	-	0/0
448	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	541.00	160.25	- -	-	-	0/0
449	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	277.33	03/2009 03/2009	08/2014	-	0/0
450	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
451	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
452	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
453	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	682.31	- 03/2010	03/2010	-	0/0
454	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005 -	-	-	0/0
455	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	260.67	- -	-	-	0/0
456	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
457	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	323.26	03/2012 -	-	-	0/0
458	KOTLAPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
459	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
460	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
461	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
462	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
463	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0
464	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
465	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
466	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0
467	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
468	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
469	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.69	- -	-	-	0/0
470	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
471	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0
472	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
473	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
474	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
475	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	108.93	- -	-	-	0/0
476	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	498.37	03/2012 -	-	-	0/0
477	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
478	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	279.54	1.38	01/1999 -	-	-	0/0
479	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.82	- -	-	-	0/0
480	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	457.88	- -	-	-	0/0
481	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	7.50	- -	-	-	0/0
482	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	1,830.00	-	- -	-	-	0/0
483	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
484	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
485	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
486	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	-	-	-	0/0
487	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
488	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.69	-	-	-	0/0
489	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
490	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	-	03/2015	-	0/0
491	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	380.62	-	-	-	0/0
492	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	-	03/2018	-	0/0
493	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	-	-	-	0/0
494	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
495	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	-	-	-	0/0
496	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
497	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
498	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	-	-	-	-	0/0
499	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	-	-	-	0/0
500	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	-	03/2019	-	0/0
501	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	-	03/2017	-	0/0
502	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	-	03/2018	-	0/0
503	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
504	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	-	03/2017	-	0/0
505	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	-	03/2019	-	0/0
506	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	-	03/2019	-	0/0
507	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	-	03/2019	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
508	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
509	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0
510	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR, MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	- -	0/0
511	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
512	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
513	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.65	03/2014 -	03/2016	24(O) -	0/0
514	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.02	558.46	03/2016 -	03/2016	0(O) -	0/0
515	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(O) -	0/0
516	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	688.50	03/2016 -	03/2016	0(O) -	0/0
517	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	424.42	03/2008 06/2008	-	-	0/0
518	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
519	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
520	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	240.21	- -	01/2015	-	0/0
521	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
522	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	712.02	- -	02/2014	-	0/0
523	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	- -	03/2015	-	0/0
524	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	600.00	-	- -	-	-	0/0
525	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
526	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
527	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	-	0/0
528	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
529	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00	323.00	-	-	-	-	0/0
530	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	205.22	1.54	-	-	-	0/0
531	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94	1,030.00	800.90	01/1999	-	-	0/0
532	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00	1,122.00	889.95	-	-	-	0/6
533	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62	289.93	277.09	12/2007	-	-	0/0
534	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00	2,363.00	1,691.12	03/2009	10/2015	79(O) 34(R)	0/0
535	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16	288.00	305.47	02/2009	08/2014	-	0/0
536	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77	209.00	2.64	12/2016	12/2016	0(O)	0/0
537	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	913.48	457.67	-	-	-	0/0
538	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00	874.57	730.11	03/2013	09/2015	30(O)	0/0
539	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	-	03/2017	-	0/0
540	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07	335.00	230.67	06/2004	12/2015	138(O)	0/0
541	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97	288.97	0.82	-	-	-	0/0
542	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANI GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65	872.22	793.73	-	-	-	0/0
543	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75	3,500.00	54.23	-	-	-	0/0
544	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04	1,421.25	420.33	03/2012	-	-	0/0
545	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34	1,743.00	359.06	-	-	-	0/0
546	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00	400.00	-	-	-	-	0/0
547	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00	576.18	3.40	-	-	-	0/0
548	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10	714.10	65.93	04/2016	03/2017	11(O)	0/0
549	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44	193.44	53.01	-	-	-	0/0
550	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69	325.00	258.31	-	-	-	0/0
551	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14	355.81	294.07	-	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
552	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	230.21	03/2010 -	-	-	0/0
553	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	380.00	-	-	-	-	0/0
554	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	-	12/2016	-	0/0
555	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	-	-	-	0/0
556	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	-	-	-	0/0
557	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
558	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.94	-	-	-	0/0
559	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	239.32	17.17	-	-	-	0/0
560	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	-	-	-	0/0
561	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	-	-	-	0/0
562	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	-	-	-	0/0
563	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	-	-	-	0/0
564	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	113.50	02/2015 -	-	-	0/0
565	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	-	-	-	0/0
566	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	595.68	03/2014 -	-	-	0/0
567	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	160.80	-	-	-	0/0
568	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	1,428.00	466.36	06/2005 -	12/2019	174(O) 101(R)	0/0
569	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
570	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	-	-	-	0/0
571	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	-	-	-	0/0
572	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	-	-	-	0/0
573	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	0.41	-	-	-	0/0
574	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	-	-	-	0/0

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
575	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	-	-	-	0/0
576	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
577	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	-	-	-	0/0
578	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
579	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.32	-	-	-	0/0
580	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.47	-	-	-	0/0
581	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O)	0/0
582	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
583	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	-	-	-	0/0
584	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
585	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	-	-	-	0/0
586	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	-	-	-	0/0
587	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
588	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	-	-	-	0/0
589	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	-	-	-	0/0
590	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	-	-	-	0/0
591	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	-	-	-	0/0
592	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	-	-	-	0/0
593	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	-	-	-	0/0
594	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	-	-	-	-	0/0
	Total		171,881.41 -	297,255.34	90,845.86				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
595	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28(O)	0/0
596	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	65.26	10/2014 -	-	-	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
597	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	07/2015	12(O) -	0/0
598	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	07/2015	26(O) -	0/0
599	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2015	25(O) -	0/0
600	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	03/2016	23(O) -	0/0
601	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	07/2015	12(O) -	0/0
602	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	240.10	-	03/2016 -	03/2016	0(O) -	0/0
603	2-LANING WITH PS LAMBIA-JAIRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	2.67	12/2015 -	12/2015	0(O) -	0/0
604	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	177.32	86.65	01/2016 -	01/2016	0(O) -	0/0
605	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23(O) -	0/0
606	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
607	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20(O) -	0/0
608	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2016	23(O) -	0/0
609	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	160.20	05/2014 -	05/2014	-	0/0
610	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016	0(O) -	0/0
611	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	11/2015	14(O) -	0/3
612	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11(O) -	0/0
613	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	07/2015	25(O) -	0/3
614	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39(O) -	0/0
615	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	941.00	08/2013 -	08/2013	-	0/3
616	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
617	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19(O) -	0/0
618	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	07/2017	47(O) -	0/0
619	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36(O) -	0/0
620	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	05/2017	45(O) -	0/0
621	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015	0(O) -	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
622	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29(O) -	0/0
623	6-LANNING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	12/2015	15(O) -	0/0
624	AGRA-BYPASS (NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	12/2015	99(O) -	0/0
625	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015	0(O) -	0/3
626	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
627	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2016	39(O) -	0/0
628	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2017	34(O) -	0/0
629	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17(O) -	0/0
630	BELGAUM-DHARWAD (NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	438.00	-	-	-	2/2
631	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35(O) -	0/0
632	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	09/2015	25(O) -	0/0
633	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	237.80	275.00	06/2008 -	-	-	0/0
634	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00 -	195.00	231.20	06/2008 -	-	-	0/0
635	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00 -	230.00	233.00	06/2005 -	-	-	0/0
636	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
637	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84(O) -	0/0
638	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33(O) -	0/0
639	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56(O) -	0/0
640	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	07/2015	45(O) -	0/0
641	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31(O) -	0/0
642	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
643	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12(O) -	0/0
644	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	07/2015	62(O) -	0/0
645	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33(O) -	0/0
646	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	07/2015	25(O) -	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
647	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00	453.00	808.70	-	07/2015	-	1/1
648	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00	200.00	289.50	06/2008	05/2015	-	0/0
649	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00	160.00	197.60	05/2008 10/2015	10/2015	89(O) 0(R)	0/0
650	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45	232.45	317.50	09/2010	04/2016	67(O) -	0/0
651	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00	1,573.00	928.70	09/2015	09/2015	0(O) -	0/0
652	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94	332.94	550.30	09/2008	12/2015	87(O) -	0/0
653	FOUR LANNING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79	1,916.79	273.20	11/2016	11/2016	0(O) -	0/0
654	FOUR LANNING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00	1,232.00	590.90	08/2015	02/2016	6(O) -	0/0
655	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00	682.00	752.70	10/2013	11/2015	25(O) -	0/0
656	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00	201.66	191.80	09/2008	09/2015	84(O) -	0/0
657	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00	1,141.00	2,445.00	08/2013	08/2015	24(O) -	0/0
658	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10	1,509.10	2,686.00	09/2012	11/2015	38(O) -	2/3
659	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16	198.16	242.40	04/2008 08/2015	08/2015	88(O) 0(R)	0/0
660	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96	175.96	182.50	04/2008 08/2015	08/2015	88(O) 0(R)	0/0
661	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00	604.00	495.40	12/2009	12/2015	72(O) -	0/0
662	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00	361.00	301.80	02/2009	-	-	0/0
663	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00	363.74	242.80	07/2009	08/2015	73(O) -	0/0
664	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00	386.10	127.10	09/2007	04/2016	103(O) -	0/0
665	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00	478.00	328.70	10/2013	09/2016	35(O) -	0/0
666	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07	625.07	995.90	01/2013	05/2015	-	0/0
667	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00	946.00	737.50	-	-	-	3/3
668	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00	325.00	447.50	05/2013	-	-	0/0
669	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00	1,175.00	138.70	04/2013	12/2015	32(O) -	0/0
670	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81	267.81	564.50	02/2013	-	-	0/0

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
671	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06	792.06	1,983.00	12/2012	06/2015	30(O)	0/0
672	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76	1,813.76	1,173.00	07/2013	12/2015	29(O)	0/0
673	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00	536.00	759.90	01/2014	06/2016	29(O)	0/0
674	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88	953.88	942.90	07/2013	12/2015	29(O)	0/0
675	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00	795.00	1,133.00	05/2012	08/2015	39(O)	0/0
676	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00	250.39	285.30	10/2008	08/2015	82(O)	0/0
677	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16	702.16	726.40	07/2014	02/2017	31(O)	0/0
678	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00	671.00	1,273.00	-	12/2015	-	2/3
679	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90	635.90	-	07/2012	-	-	0/0
680	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04	280.13	114.80	11/2008	-	-	0/0
681	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81	385.13	83.98	04/2009	-	-	0/0
682	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64	167.64	45.43	11/2008	-	-	0/0
683	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00	200.00	141.80	04/2009	-	-	0/0
684	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00	1,267.00	2,425.00	06/2013	07/2015	25(O)	0/0
685	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00	754.00	593.50	03/2013	06/2016	39(O)	0/0
686	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72	264.72	299.20	06/2008	-	-	0/0
687	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	484.19	285.50	10/2014	03/2016	17(O)	0/0
688	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00	208.00	290.60	04/2008	01/2016	93(O)	0/0
689	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00	225.00	258.40	06/2008	08/2015	86(O)	0/0
690	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00	200.00	281.60	06/2008	-	-	0/0
691	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00	2,159.00	622.70	06/2015	05/2016	11(O)	0/0
692	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00	1,655.00	655.20	09/2013	09/2013	-	0/0
693	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00	557.00	932.30	02/2010	-	-	0/0
694	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00	586.00	237.60	01/2014	12/2016	35(O)	0/0
695	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	1,410.00	929.60	09/2014	06/2016	21(O)	0/0

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
696	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00	2,288.00	3,466.00	11/2011	11/2016	60(O)	0/0
697	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00	807.00	1,209.43	10/2014	10/2014	-	0/0
698	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69	942.69	286.80	06/2014	12/2015	18(O)	0/0
699	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00	574.00	991.70	03/2014	11/2015	20(O)	0/0
700	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30	671.30	632.70	02/2013	03/2016	37(O)	0/0
701	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00	940.00	1,601.00	07/2012	07/2012	-	0/0
702	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55	1,724.55	1,127.00	03/2013	-	-	0/0
703	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00	835.00	476.40	01/2014	11/2015	22(O)	0/0
704	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00	1,987.00	1,170.00	07/2015	06/2016	11(O)	0/0
705	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03	251.03	326.30	10/2008	01/2015	-	0/0
706	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00	1,479.00	368.60	06/2015	12/2016	18(O)	0/0
707	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51	333.51	271.60	09/2014	12/2015	15(O)	0/0
708	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00	650.00	1,178.00	11/2013	03/2016	28(O)	0/0
709	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39	805.39	842.20	03/2013	12/2015	33(O)	0/0
710	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00	909.00	982.90	05/2014	07/2015	14(O)	0/0
711	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47	154.57	228.30	09/2007	03/2015	-	0/0
712	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00	225.00	191.00	07/2008	-	-	0/0
713	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00	1,047.00	295.70	06/2014	03/2016	21(O)	0/0
714	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00	535.00	52.80	12/2013	09/2015	21(O)	0/0
715	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00	1,250.00	1,374.00	12/2013	12/2016	36(O)	0/0
716	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00	1,535.00	2,188.00	05/2014	02/2016	21(O)	0/0
717	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00	617.00	156.90	08/2012	03/2016	43(O)	0/0
718	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00	245.00	491.20	03/2008	01/2016	94(O) 0(R)	0/0

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
719	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70	1,100.70	323.00	06/2014	12/2015	18(O)	0/0
720	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75	1,693.75	2,762.00	08/2011	09/2016	61(O)	2/2
721	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00	567.00	1,388.00	11/2013	11/2013	-	0/0
722	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00	571.00	-	10/2013	03/2016	29(O)	0/0
723	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00	374.00	148.80	05/2013	12/2015	31(O)	0/0
724	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00	680.00	188.40	-	07/2014	-	2/2
725	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00	2,848.00	1,138.00	03/2014	04/2017	37(O)	0/0
726	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00	606.00	-	-	-	-	0/0
727	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45	193.45	66.11	11/2012	12/2016	49(O)	0/0
728	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95	1,287.95	540.40	11/2015	03/2017	16(O)	0/0
729	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15	368.15	27.32	01/2016	01/2016	0(O)	0/0
730	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20	1,348.20	588.40	02/2014	08/2016	30(O)	0/0
731	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17	1,123.17	-	-	-	-	0/0
	Total		100,051.30	102,199.30	89,186.97				14/28
	SHIPPING AND PORTS								
732	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00	1,460.00	1,049.37	12/2010	-	-	0/0
733	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39	669.46	407.32	12/2010	01/2016	61(O)	0/0
734	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00	600.00	139.80	03/2006	-	-	0/0
735	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00	277.00	0.21	03/2012	-	-	0/0
736	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67	373.22	351.18	04/2009	-	-	0/0
737	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40	2,427.40	831.23	10/2008	-	-	0/0
738	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00	621.53	-	05/2013	-	-	0/0

Sector Wise Details									
(June 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		5,524.46	6,428.61	2,779.11				0/0
	<u>TELECOMMUNICATIONS</u>								
739	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00	384.00	66.02	10/2010 08/2015	09/2015	59(O) 1(R)	0/0
740	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00	13,334.00	-	07/2015	07/2015	0(O) -	0/0
	Total		13,718.00	13,718.00	66.02				0/0
	<u>URBAN DEVELOPMENT</u>								
741	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86	171.86	-	03/2016	05/2016	2(O) -	0/0
742	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81	225.81	-	06/2012	06/2015	36(O) -	0/0
743	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00	11,609.00	2,267.57	06/2011	-	-	3/3
744	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14	26,405.14	-	02/2019	02/2019	0(O) -	0/0
745	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00	14,600.00	10,826.56	12/2015	08/2016	8(O) -	1/24
746	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	884.30	-	08/2014	06/2017	34(O) -	0/0
747	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87	188.87	5.79	12/2014	12/2016	24(O) -	0/0
748	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85	261.85	6.26	05/2013	11/2015	30(O) -	0/0
749	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01	405.01	-	12/2014	04/2016	16(O) -	0/0
750	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43	238.43	-	02/2015	08/2015	6(O) -	0/0
751	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24	191.24	-	08/2007	03/2015	-	0/0
752	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23	165.23	-	10/2012	09/2013	-	0/0
753	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00	315.00	3.11	06/2015	08/2015	2(O) -	0/0
754	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57	156.57	-	09/2015	12/2016	15(O) -	0/0
755	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84	157.84	-	03/2017	03/2017	0(O) -	0/0

Sector Wise Details									
(June 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
756	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00	38,585.00	8,110.85	03/2016	12/2016	9(O)	0/0
757	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89	2,727.89	-	03/2010	10/2014	-	0/0
758	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83	270.83	-	11/2014	10/2015	11(O)	0/0
759	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21	1,219.21	-	07/2017	07/2017	0(O)	0/0
760	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00	2,494.00	639.78	09/2014	05/2015	-	0/0
761	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79	5,181.79	-	07/2017	07/2017	0(O)	0/0
762	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90	162.90	-	07/2012	06/2014	-	0/0
763	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00	23,136.00	-	01/2015	12/2015	11(O)	0/0
764	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00	8,680.00	-	03/2018	03/2018	0(O)	0/0
765	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33	241.33	1.75	11/2014	12/2014	-	0/0
766	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00	4,264.00	-	11/2019	11/2019	0(O)	0/7
767	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90	246.90	-	-	-	-	0/0
768	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10	171.10	-	09/2014	-	-	0/0
769	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72	332.72	-	09/2016	09/2016	0(O)	0/0
770	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00	205.00	-	03/2012	04/2015	-	0/0
	Total		138,680.82	143,894.82	21,861.67				4/34
	Grand Total		1,067,193.26	1,275,501.50	557,866.01				1705/3775


Summary of projects in the Flash Report for the month of June, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	766
Number of Projects completed/dropped/frozen in Current Month	9
Number of Projects elevated to the status of Major project during the current month	6
Number of Projects Added in Current Month	7
Number of Projects in Current Month	770


Brief Analysis

Project Status with respect to Original Schedule: Out of 770 projects, 4 projects are ahead of schedule, 125 projects are on schedule 313 projects are delayed. 298 projects do not have fixed dates of commissioning. 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

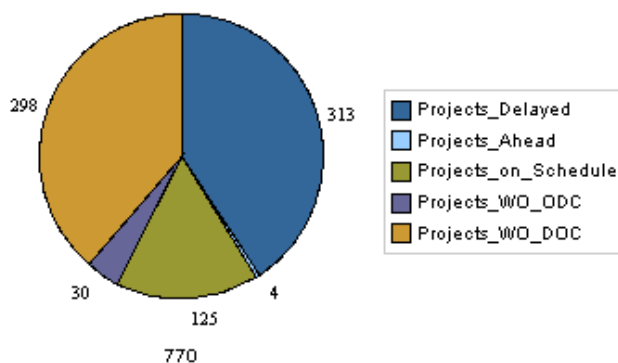

Investment Scenario

Total original cost of implementation of 770 projects when sanctioned, was of the order of Rs. 1067193.26 crore but this was subsequently revised to Rs. 1275501.5 crore implying a cost overrun of 19.5%. The expenditure incurred on these projects till June, 2015 is Rs. 557866.01 crore, which is 43.7% of the revised cost of the projects.

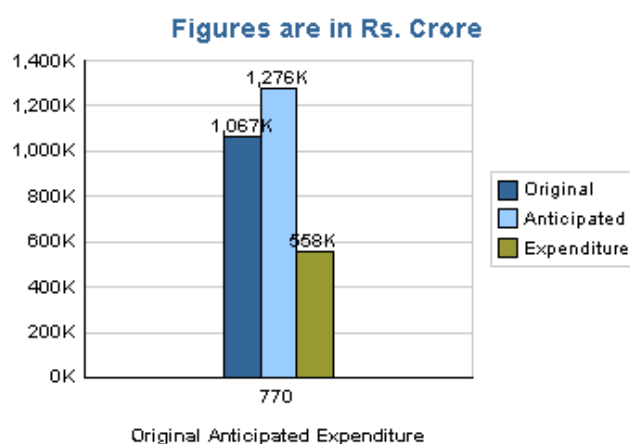

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

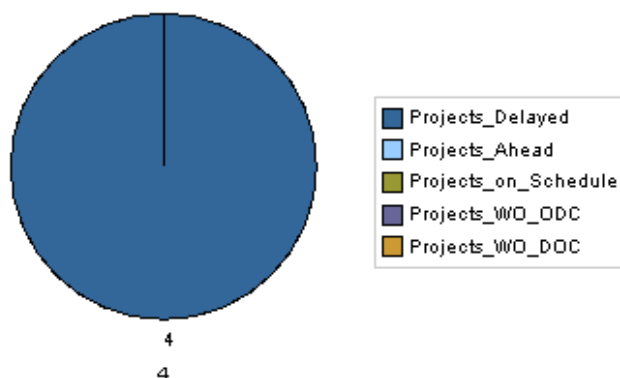

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till June, 2015 is Rs. 37241.93 crore, which is 79.7% of the revised cost of the projects.

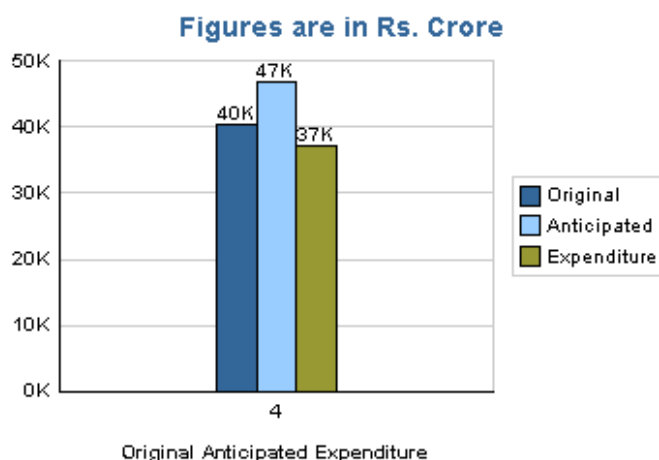

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	7
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 3 projects are delayed. 3 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

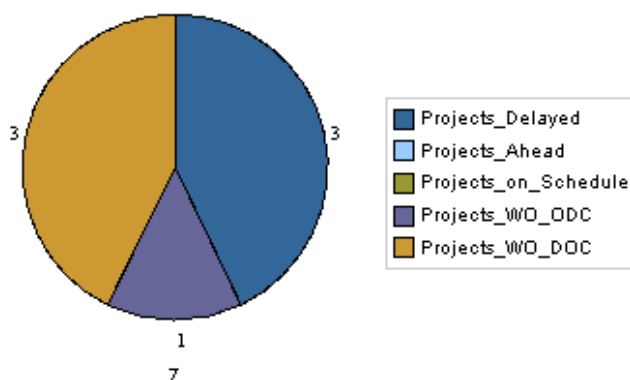

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2599.56 crore but this was subsequently anticipated to Rs. 2715.98 crore implying a cost overrun of 4.5%. The expenditure incurred on these projects till June, 2015 is Rs. 1675.78 crore, which is 61.7% of the revised cost of the projects.

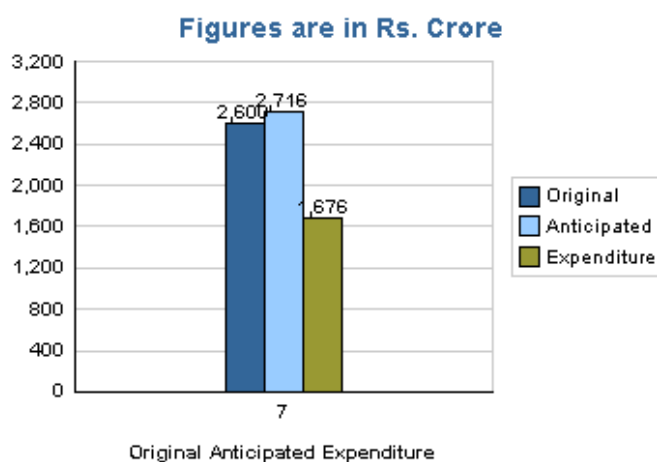

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	76
Number of Projects On Schedule	29
Number of Projects Delayed	45

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 76 projects, 29 projects are on schedule 45 projects are delayed. 2 projects do not have fixed dates of commissioning.

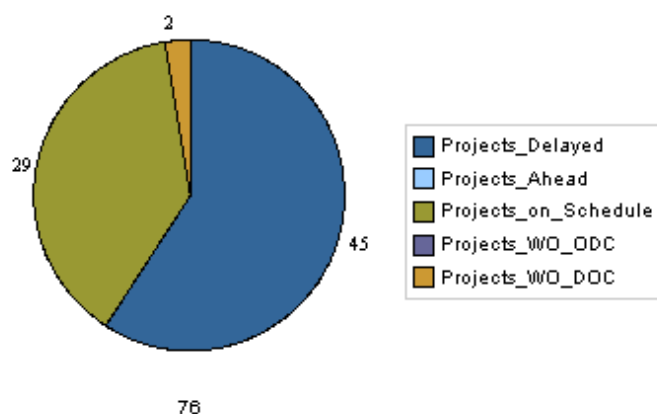

Investment Scenario

Total original cost of implementation of 76 projects when sanctioned, was of the order of Rs. 59478.01 crore but this was subsequently anticipated to Rs. 63381.17 crore implying a cost overrun of 6.6%. The expenditure incurred on these projects till June, 2015 is Rs. 22383.5 crore, which is 35.3% of the revised cost of the projects.

Figures are in Rs. Crore

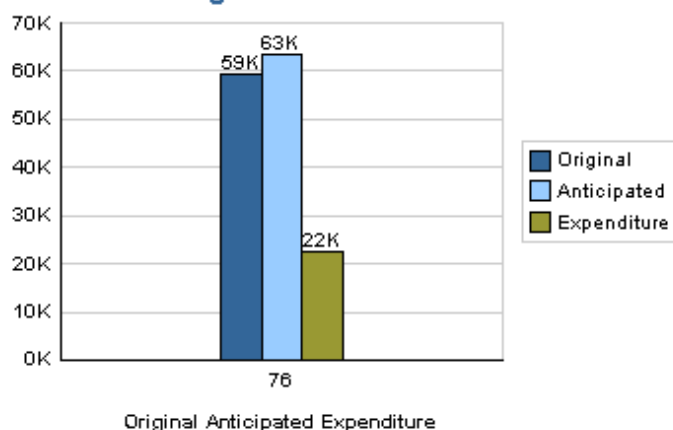

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	26
Number of Projects On Schedule	9
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 26 projects, 9 projects are on schedule 14 projects are delayed. 3 projects do not have fixed dates of commissioning.

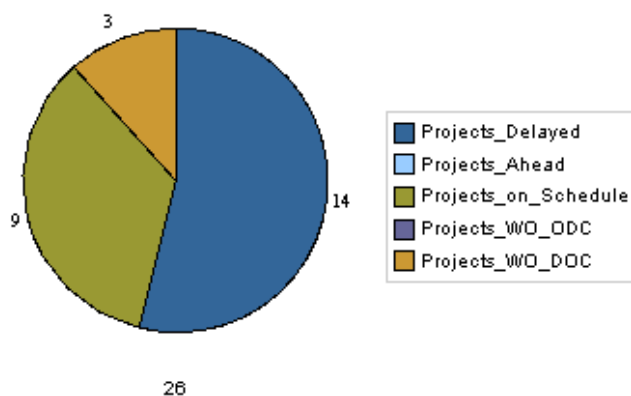

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 61866.16 crore but this was subsequently anticipated to Rs. 65580.56 crore implying a cost overrun of 6%. The expenditure incurred on these projects till June, 2015 is Rs. 42179.65 crore, which is 64.3% of the revised cost of the projects.

Figures are in Rs. Crore

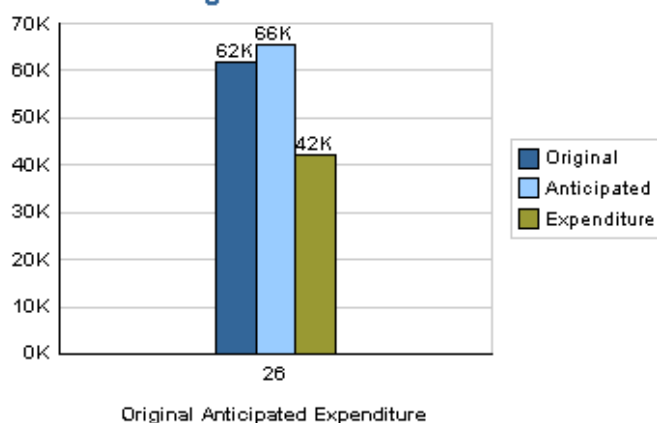

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	71
Number of Projects On Schedule	14
Number of Projects Delayed	48
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 71 projects, 3 projects are ahead of schedule, 14 projects are on schedule 48 projects are delayed. 6 projects do not have fixed dates of commissioning.

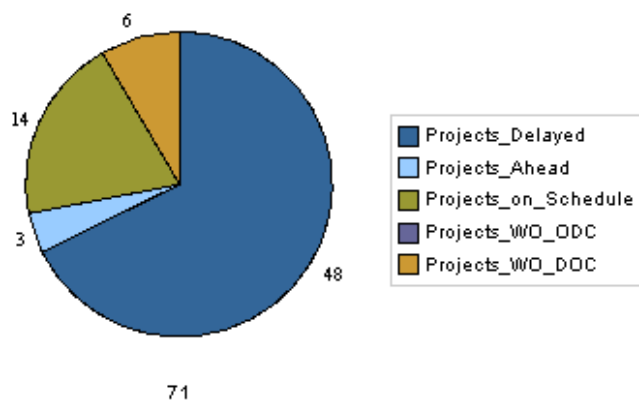

Investment Scenario

Total original cost of implementation of 71 projects when sanctioned, was of the order of Rs. 153184.11 crore but this was subsequently anticipated to Rs. 167522.71 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till June, 2015 is Rs. 70982.31 crore, which is 42.4% of the revised cost of the projects.

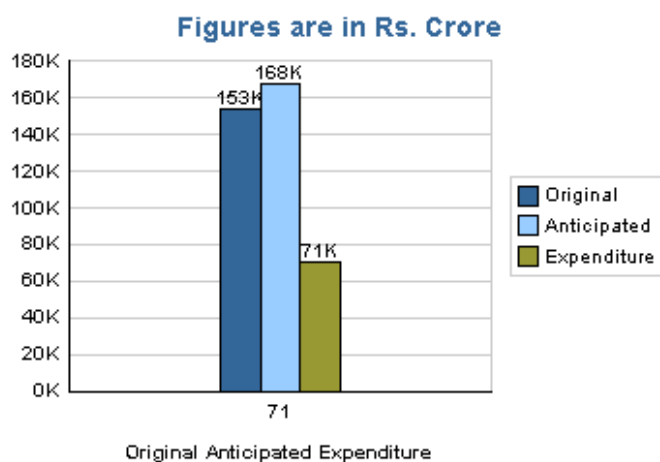

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	110
Number of Projects On Schedule	45
Number of Projects Delayed	58
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	6

Brief Analysis


Project Status with respect to Original Schedule: Out of 110 projects, 1 project is ahead of schedule, 45 projects are on schedule 58 projects are delayed. 6 projects do not have fixed dates of commissioning.

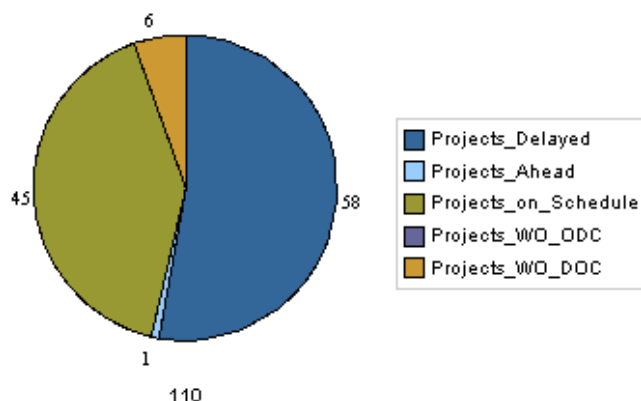

Investment Scenario

Total original cost of implementation of 110 projects when sanctioned, was of the order of Rs. 310535.03 crore but this was subsequently anticipated to Rs. 350364.4 crore implying a cost overrun of 12.8%. The expenditure incurred on these projects till June, 2015 is Rs. 169904.38 crore, which is 48.5% of the revised cost of the projects.

Figures are in Rs. Crore

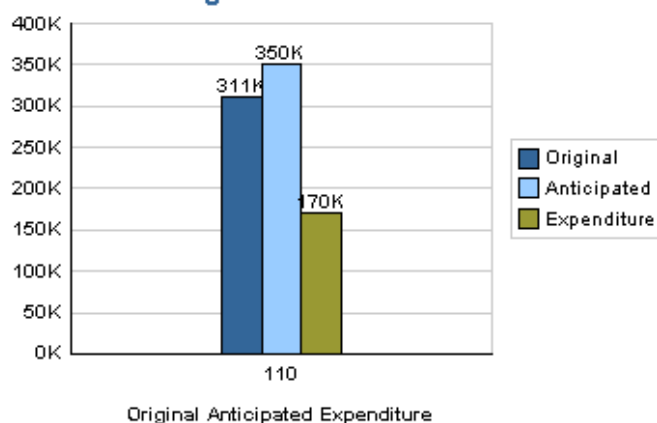

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	296
Number of Projects On Schedule	8
Number of Projects Delayed	34
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	227


Brief Analysis

Project Status with respect to Original Schedule: Out of 296 projects, 8 projects are on schedule 34 projects are delayed. 227 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

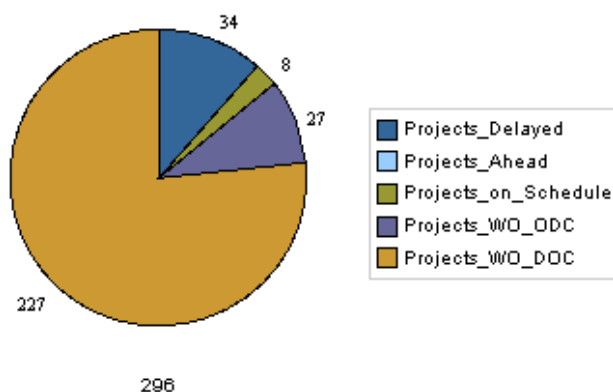

Investment Scenario

Total original cost of implementation of 296 projects when sanctioned, was of the order of Rs. 171881.41 crore but this was subsequently anticipated to Rs. 297255.34 crore implying a cost overrun of 72.9%. The expenditure incurred on these projects till June, 2015 is Rs. 90845.86 crore, which is 30.6% of the revised cost of the projects.

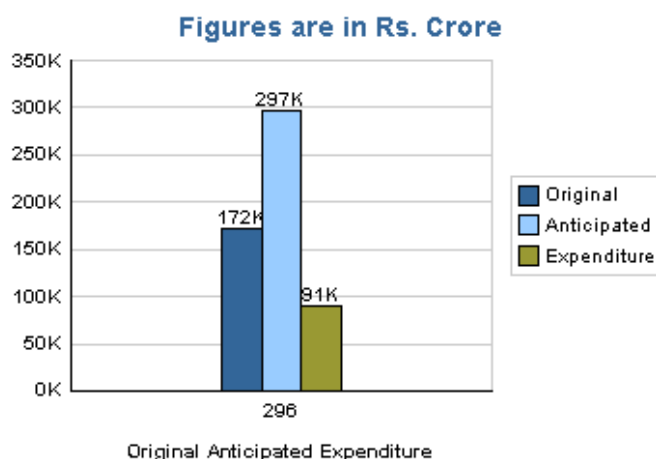

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHW

Current Status:

Number of Projects	137
Number of Projects On Schedule	10
Number of Projects Delayed	90
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	35


Brief Analysis

Project Status with respect to Original Schedule: Out of 137 projects, 10 projects are on schedule 90 projects are delayed. 35 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

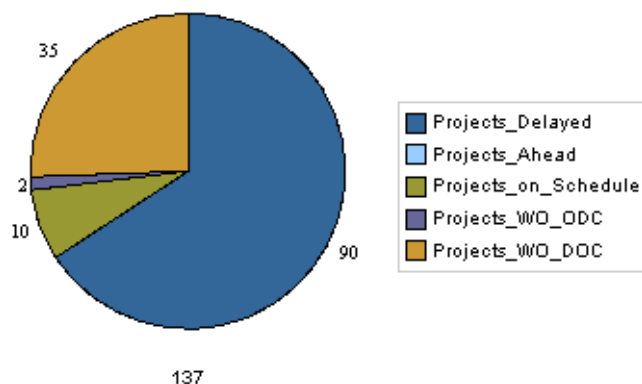

Investment Scenario

Total original cost of implementation of 137 projects when sanctioned, was of the order of Rs. 100051.3 crore but this was subsequently anticipated to Rs. 102199.3 crore implying a cost overrun of 2.1%. The expenditure incurred on these projects till June, 2015 is Rs. 89186.97 crore, which is 87.3% of the revised cost of the projects.

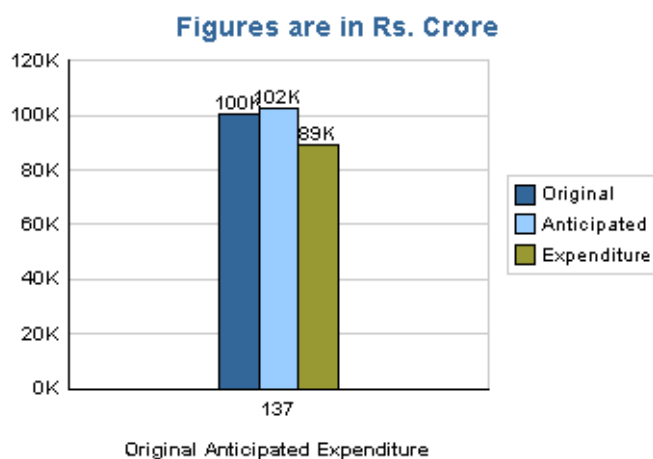

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	7
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 1 project is delayed. 6 projects do not have fixed dates of commissioning.

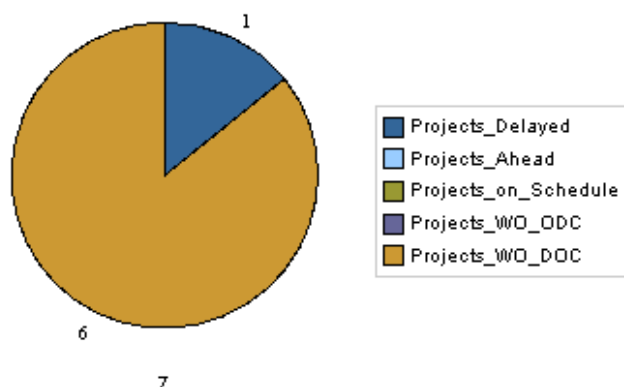

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 5524.46 crore but this was subsequently anticipated to Rs. 6428.61 crore implying a cost overrun of 16.4%. The expenditure incurred on these projects till June, 2015 is Rs. 2779.11 crore, which is 43.2% of the revised cost of the projects.

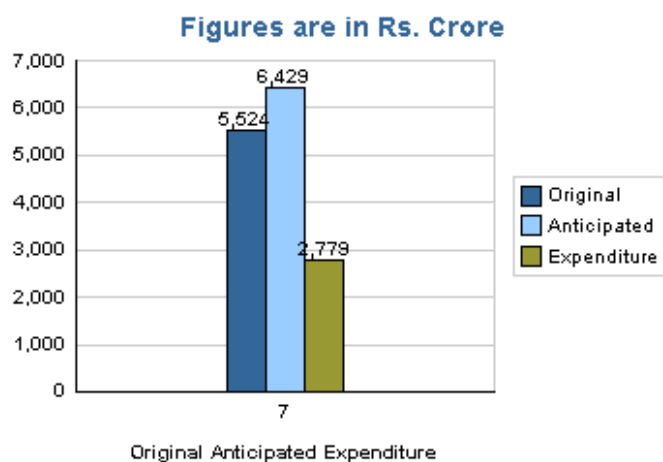

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.



Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 13718 crore but this was subsequently anticipated to Rs. 13718 crore. The expenditure incurred on these projects till June, 2015 is Rs. 66.02 crore, which is .5% of the revised cost of the projects.

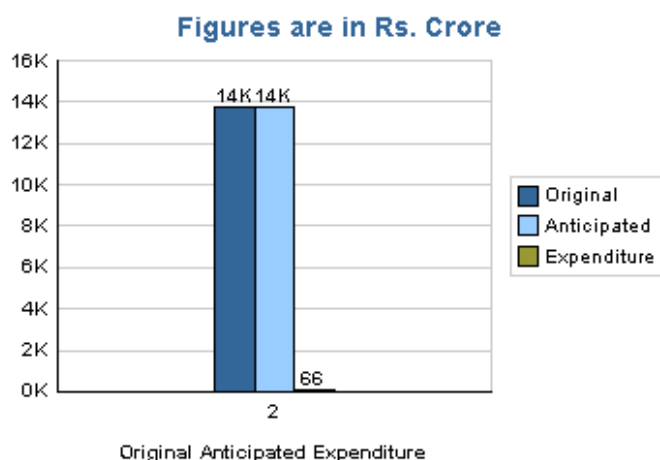

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	30
Number of Projects On Schedule	7
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	10
--	----


Brief Analysis

Project Status with respect to Original Schedule: Out of 30 projects, 7 projects are on schedule 13 projects are delayed. 10 projects do not have fixed dates of commissioning.

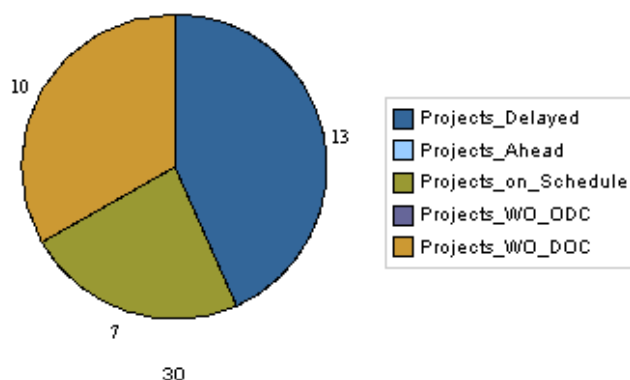

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 138680.82 crore but this was subsequently anticipated to Rs. 143894.82 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till June, 2015 is Rs. 21861.67 crore, which is 15.2% of the revised cost of the projects.

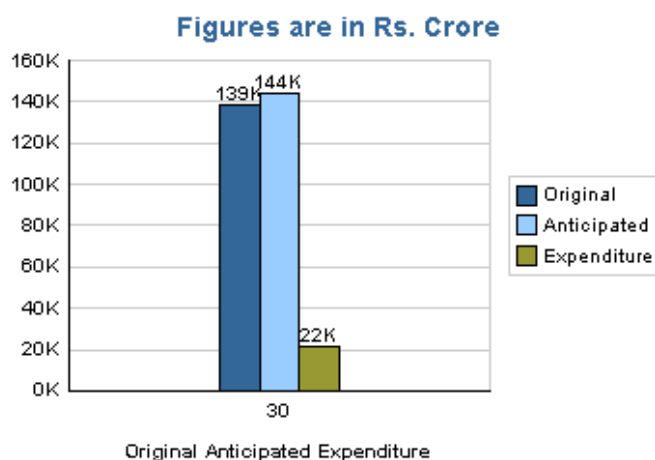

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE					
(All Cost /Expenditure in Rs. crore)					
S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	17.82
2	ANDHRA PRADESH	28	25,167.01	31,389.44	19,225.45
3	ARUNACHAL PRADESH	3	9,356.22	23,263.83	12,638.01
4	ASSAM	34	22,255.53	38,017.05	29,722.11
5	BIHAR	48	57,726.67	75,016.29	45,636.33
6	CHANDIGARH	1	452	489	449.63
7	CHHATISGARH	28	80,681.93	82,331.09	43,277.82
8	D & N HAVELI	1	6,086.08	6,086.08	47.07
9	DELHI	12	50,903.45	50,903.45	8,810.75
10	GOA	1	335.61	388.53	301.94
11	GUJARAT	29	36,037.34	36,616.51	20,931.88
12	HARYANA	9	4,659.81	6,630.43	7,382.50
13	HIMACHAL PRADESH	4	7,154.09	12,973.29	5,423.77
14	JAMMU AND KASHMIR	7	21,314.62	40,235.30	17,943.65
15	JHARKHAND	37	38,977.33	39,535.41	14,782.73
16	KARNATAKA	34	66,982.20	81,944.97	21,321.86
17	KERALA	13	24,457.67	28,611.45	11,055.32
18	MADHYA PRADESH	20	24,954.32	26,938.24	9,248.49
19	MAHARASHTRA	46	1,01,718.42	1,12,603.93	32,991.38
20	MANIPUR	1	727.56	6,570.75	2,787.99
21	MEGHALAYA	3	4,845.02	6,069.90	1,049.99
22	MIZORAM	2	988.06	4,201.96	1,042.80
23	MULTI STATE	187	2,07,744.19	2,36,422.65	85,360.03
24	NAGALAND	2	5,124	7,461.12	10.44
25	ODISHA	42	72,186.50	81,274.54	42,420.60
26	PUNJAB	3	792.5	765.46	110.47
27	RAJASTHAN	30	27,857.57	27,913.04	15,394.47
28	SIKKIM	2	1,648.94	4,499.46	444.44
29	TAMIL NADU	42	68,208.56	85,860.44	63,052.31
30	TELANGANA	21	9,410.62	12,235.26	3,027.36
31	TRIPURA	6	2,966.26	6,629.97	3,285.88
32	UTTAR PRADESH	29	35,842.78	38,740.53	15,816.33
33	UTTARAKHAND	6	9,351.89	12,905.21	4,895.88
34	WEST BENGAL	38	39,963.90	49,662.31	17,958.51
TOTAL		770	10,67,193.26	1,275,501.50	5,57,866.01

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	20,713
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2,030.78	3027.59	3,213.77
3	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,109.77
4	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,737.41
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,787.9
6	VIRAMGAM-BHILDI (WR) , GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	RAILWAYS	03/1995	2,500	3000	10,658.34
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	RAILWAYS	02/1997	295	-	1,092.98
12	KARUR-SALEM (NL) , SR	RAILWAYS	02/1997	155.55	-	800.66
13	NANDYAL-YERRAGUNTALA (NL) , SCR	RAILWAYS	03/1996	155.74	164.36	755.5
14	KANPUR-KASGANJ-MATHURA (GC) , NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06
16	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
17	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
18	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	819.19
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
21	KATIHAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
22	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
23	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
24	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
26	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
27	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53
28	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	301.84

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	639.77
30	RAJATGARH-BARANG (LD), ECR	RAILWAYS	04/1999	166.16	-	305.47
31	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
32	KOSI BRIDGE (NL), ECR	RAILWAYS	04/2002	322.95	-	323.26
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	RAILWAYS	04/2002	921	-	1,691.12
34	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,521.72
35	ETAWAH-MAINPURI (NL), NCR	RAILWAYS	04/1997	120	245.39	249.33
36	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	277.33
38	RAICHUR-GUNTAKAL (DL) (SCR)	RAILWAYS	04/2003	136.62	-	277.09
39	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	228.3
40	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	191.8
41	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	233
42	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	301.8

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	BIJNI TO ASSAM WB BORDER (NH-31.C) (1) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	231.2
44	BIJNI TO ASSAM /WB.BORDER (NH-31.C) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	275
45	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	550.3
46	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	285.3
47	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	326.3
48	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	355.88
49	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	3,996.61
50	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	POWER	02/2010	2,144	-	2,156.7
51	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	POWER	12/2010	2,743.19	-	2,750.9
52	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,199.43
53	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
54	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	793.71
55	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
56	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
58	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
59	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
60	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
61	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
62	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
63	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
64	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45
65	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
66	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	793.73
67	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	258.31
68	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
69	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
70	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
72	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
73	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
74	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
75	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
76	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62
77	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	800.9
78	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
79	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
80	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	182.5
81	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	299.2
82	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
83	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
84	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	258.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	290.6
86	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.6
87	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	289.5
88	HARANGAJO TO MAIBANG, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	196	-	242.8
89	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
90	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	317.5
91	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	667.1
92	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,601
93	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,686
94	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,133
95	CHENNAI-TADA (SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
96	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
97	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
98	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
100	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,388
101	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
102	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
103	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	901.6
104	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273
105	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	761.3
106	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
107	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	808.7
108	MURADABAD-BAREILLY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
109	4 LANNING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,786
110	INDORE-DEWAS (NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	447.5
111	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.6
112	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,392

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	941
114	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,178
115	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	2,445
116	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,374
117	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	842.2
118	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	759.9
119	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
120	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,188
121	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	776.4
122	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	991.7
123	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	408.1
124	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	835.6
125	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
126	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	633.3

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	982.9
128	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	564.5
129	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,922
130	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,610
131	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,934
132	KRISHNANAGAR-BERHAMPUR	ROAD TRANSPORT AND HIGHWAYS	02/2012	702.16	-	726.4
133	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2011	682	-	752.7
134	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	-	351.18

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(June 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	10/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	07/2015	8.19
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		1,005.21 -	1,121.63			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	07/2015	76.47
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	07/2015	34.63
9	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
11	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2016	12.97
	Total		8,208.23 -	12,579.39			
	<u>HEAVY INDUSTRY</u>						
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						

(June 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						
14	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
15	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2015	45.83
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
18	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
19	REWARI KANPUR PIPELINE PROJECT - [N16000145]	02/2012	1,210.64 -	1,446.34	11/2015 -	11/2015	19.47
20	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
21	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,178.35	10/2011 -	06/2015	75.35
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	01/2016	67.62
24	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	12/2017	31.51
25	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
26	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	10/2015	20.02
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	01/2016	70.49
28	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	219.00	09/2016 -	12/2015	54.38
29	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
30	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72
	Total		62,721.75 -	78,324.61			
	<u>POWER</u>						
31	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48

(June 2015)

(June 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	03/2017	159.38
34	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2018	73.65
35	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34
37	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
38	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
39	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
40	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10
41	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31
43	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15
44	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04 -	10,852.46	10/2013 -	03/2015	47.83
45	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35
46	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	09/2015	13.18
47	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	03/2011	2,569.25 -	3,105.51	03/2014 -	08/2015	20.87
48	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63
49	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.70	08/2014 -	03/2016	27.60
50	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
51	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52
	Total		55,547.32 -	95,440.30			
	<u>RAILWAYS</u>						
52	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
53	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06

(June 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
54	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
55	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
56	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
57	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
58	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
59	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
60	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
61	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91
62	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
63	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
64	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
65	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
66	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
67	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
68	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
69	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
70	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
71	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
72	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
73	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
74	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
75	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
76	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
77	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37

(June 2015)

(June 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
78	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
79	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
80	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
81	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
82	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
83	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
84	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
85	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
86	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
87	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
88	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
89	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
90	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
91	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
92	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
93	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
94	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
95	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
96	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
97	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
98	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
99	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
100	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49

(June 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
101	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16 -	- -	03/2017	186.92
102	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29 -	02/2015 -	-	346.59
103	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00 -	- -	10/2014	76.98
104	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00 -	03/2009 03/2009	08/2014	106.88
105	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80 -	- -	-	0.00
106	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93 -	12/2007 03/2010	-	112.22
107	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88 -	03/2012 -	-	43.54
108	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59 -	- -	-	109.11
109	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00 -	02/2006 -	03/2016	6.99
110	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11 -	03/2008 06/2008	-	50.35
111	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54 -	03/2010 -	-	18.66
112	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00 -	03/2010 -	12/2015	16.41
113	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	1,383.45 -	- -	-	242.28
114	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	914.98 -	- -	03/2016	166.63
115	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00 -	03/2011 -	-	185.29
116	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	490.00 -	- -	-	292.00
117	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	1,080.00 -	- -	-	136.84
118	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	496.24 -	- -	03/2017	148.12
119	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	827.73 -	- -	03/2019	175.91
120	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54 -	03/2010 -	03/2017	381.40
121	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04 -	03/2014 -	03/2019	50.68
122	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08 -	03/2012 -	03/2016	60.77
123	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00 -	06/2005 -	12/2019	385.76
124	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00 -	03/2014 -	03/2018	253.60

(June 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
125	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
126	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
127	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
128	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
129	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
130	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
131	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
132	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
133	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
134	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
135	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
136	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
137	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
138	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
139	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
140	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
141	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
142	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
143	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
144	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
145	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34

(June 2015)

(June 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
146	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
147	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
148	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
149	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
150	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
151	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
152	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
153	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
154	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
155	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
156	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
157	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
158	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
159	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
160	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
161	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
162	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
163	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
164	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
165	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
166	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
167	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
168	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00

(June 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
169	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
170	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
171	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
172	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
173	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
174	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
175	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
176	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
177	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
178	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
179	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJBHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
180	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
181	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
182	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
183	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
184	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
185	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
186	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
187	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
188	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
189	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
190	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
191	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
192	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76

(June 2015)

(June 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
193	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
194	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
195	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
196	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
197	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
198	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
199	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
200	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
201	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
202	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
203	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
204	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
205	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
206	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
207	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
208	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
209	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
210	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
211	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
212	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		85,637.72 -	212,427.62			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
213	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	09/2015	30.10
214	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93

(June 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
215	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
216	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
217	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2016	82.12
218	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	08/2015	85.58
219	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
220	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29
221	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	12/2015	33.70
222	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2016	106.50
	Total		3,146.62 -	5,322.13			
	<u>SHIPPING AND PORTS</u>						
223	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
224	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
225	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
226	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,990.06 -	3,102.68			
	<u>STEEL</u>						
227	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	04/2015	41.41
228	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		9,035.00 -	12,779.40			
	<u>URBAN DEVELOPMENT</u>						
229	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		257,528.52	469,314.58			

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	10/2015	31.12	82
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18	6
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	07/2015	8.19	4
	Total		669.60 -	733.10				
	<u>COAL</u>							
5	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50	30
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	07/2015	76.47	73
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	07/2015	34.63	40
	Total		7,627.19 -	11,894.53				
	<u>HEAVY INDUSTRY</u>							
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROCHEMICALS</u>							
10	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08	41
	Total		5,460.61 -	9,833.52				

(June 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>PETROLEUM</u>							
11	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	10/2015	20.02	27
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38	24
13	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110
14	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,178.35	10/2011 -	06/2015	75.35	44
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	01/2016	67.62	51
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2015	45.83	31
18	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72	15
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	01/2016	70.49	48
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
21	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	12/2017	31.51	22
22	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05	35
	Total		41,085.22 -	53,891.47				
	<u>POWER</u>							
23	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63	16
24	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
25	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35	25
26	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10	66
27	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15	31
28	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76	81
29	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94

(June 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
30	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	2,228.70	08/2014 -	03/2016	27.60	19
31	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34	90
32	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	09/2010	2,074.86 -	2,348.37	03/2013 -	09/2015	13.18	30
33	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31	78
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	03/2017	159.38	87
35	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096	03/2011	2,569.25 -	3,105.51	03/2014 -	08/2015	20.87	17
36	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69
37	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
38	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48	111
39	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
40	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2018	73.65	86
	Total		41,624.08 -	68,924.11				
	<u>RAILWAYS</u>							
41	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67	66
42	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
43	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49	82
44	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
45	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
46	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
47	KATAKHAL TO BHARABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
48	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	03/2016	6.99	121
49	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174

(June 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
50	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
51	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
52	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
53	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45	30
54	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
55	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
56	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
57	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
58	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
59	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
60	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
61	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
62	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
63	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
64	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57	79
65	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
66	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
67	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
68	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
69	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		23,316.40 -	81,340.44				
	ROAD TRANSPORT AND HIGHWAYS							

(June 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
70	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [N240106221	12/2003	155.00 -	201.66	09/2008 -	09/2015	30.10	84
71	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	08/2015	85.58	73
72	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2016	82.12	103
73	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
74	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29	84
75	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	12/2015	33.70	99
76	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2016	106.50	60
	Total		2,511.77 -	4,295.87				
	<u>SHIPPING AND PORTS</u>							
77	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72	61
	Total		366.39 -	669.46				
	Grand Total		141,042.26	258,356.80				

List of Projects having cost overrun with respect to Anticipated/Cumulative Expenditure

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
1	ATOMIC ENERGY	NPCIL	KUDANKULAM APP (NPCIL)	13,171.00	17,270.00	20,713.00	7,542.00
2	ATOMIC ENERGY	BHAVNI	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	3,492.00	5,677.00	5,006.93	2,185.00
3	CIVIL AVIATION	AAI	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	309.46	309.46	355.88	46.00
4	CIVIL AVIATION	AAI	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	217.60	244.10	0.04	27.00
5	CIVIL AVIATION	AAI	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	452.00	489.00	449.63	37.00
6	CIVIL AVIATION	AAI	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	335.61	388.53	301.94	53.00
7	COAL	NLC	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	2,030.78	3,583.77	3,213.77	1,553.00
8	COAL	NLC	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	4,904.54	6,602.74	6,277.83	1,698.00
9	COAL	SCCL	RFR OF MANUGURU OC PROJECT	430.45	486.27	69.97	56.00
10	COAL	SECL	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	150.59	198.59	111.83	48.00
11	COAL	SCCL	ADRIYALA SHAFT PROJECT	212.34	1,228.39	879.58	1,016.00
12	HEAVY INDUSTRY	HIPE	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	1,718.00	3,827.30	0.00	2,109.00
13	PETROCHEMICALS	BCPL	ASSAM GAS CRACKER PROJECT	5,460.61	9,833.52	8,736.89	4,373.00
14	PETROLEUM	ONGC	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	429.82	3,955.21	3,439.38	3,525.00
15	PETROLEUM	IOCL	PARADIP REFINERY PROJECT	29,777.00	34,555.00	29,273.28	4,778.00
16	PETROLEUM	ONGC	INTEGRATED DEVELOPMENT OF B-127 FIELDS	2,059.63	2,665.65	1,204.41	606.00
17	PETROLEUM	HPCL	REWARI KANPUR PIPELINE PROJECT	1,210.64	1,446.34	1,066.43	236.00
18	PETROLEUM	HPCL	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	309.81	462.79	237.49	153.00
19	PETROLEUM	OIL	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	871.35	1,200.00	273.36	329.00
20	PETROLEUM	ONGC	MH NORTH REDEVELOPMENT PHASE III	5,706.47	5,813.25	1,357.45	107.00
21	PETROLEUM	IOCL	MARKETING TOP AT KORBA	141.86	219.00	141.77	77.00
22	PETROLEUM	ISPRL	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	993.00	1,693.00	1,404.06	700.00
23	PETROLEUM	IOCL	MARKETING TERMINAL AT PARADEEP	199.75	239.73	190.20	40.00
24	PETROLEUM	OIL	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	352.56	450.55	10.60	98.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
25	PETROLEUM	ONGC	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	3,513.07	4,619.94	335.37	1,107.00
26	PETROLEUM	ISPRL	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	732.00	1,227.00	970.98	495.00
27	PETROLEUM	ISPRL	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	672.00	1,178.35	1,079.05	506.00
28	PETROLEUM	HPCL	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	666.00	838.08	481.49	172.00
29	PETROLEUM	BPCL	INTEGRATED REFINERY EXPANSION PROJECT	14,225.00	16,504.00	7,147.44	2,279.00
30	PETROLEUM	ONGC	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	861.79	1,256.72	885.75	395.00
31	POWER	NHPC	PARBATI HEP (4X200 MW) (NHPC) II	3,919.59	7,818.68	5,109.77	3,899.00
32	POWER	NHPC	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	1,061.38	1,929.15	1,787.90	868.00
33	POWER	PGCIL	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	1,779.29	2,159.07	1,893.05	380.00
34	POWER	NTPC	BARH STPP(3X660MW) NTPC	8,692.97	15,095.67	10,899.00	6,403.00
35	POWER	NHPC	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	6,285.33	15,300.00	7,737.41	9,015.00
36	POWER	NEEPC O	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW)	296.87	363.73	315.66	67.00
37	POWER	NEEPC O	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	368.72	1,381.71	843.49	1,013.00
38	POWER	PGCIL	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	1,746.65	2,228.70	1,214.43	482.00
39	POWER	PGCIL	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	297.33	346.79	282.57	49.00
40	POWER	PGCIL	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	2,127.51	2,127.51	2,199.43	72.00
41	POWER	PGCIL	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	2,569.25	3,105.51	2,825.87	536.00
42	POWER	PGCIL	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	2,743.19	2,743.19	2,750.90	8.00
43	POWER	PGCIL	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	2,074.86	2,348.37	1,854.54	274.00
44	POWER	PGCIL	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	2,144.00	2,144.00	2,156.70	13.00
45	POWER	NEEPC O	TRIPURA GAS BASED POWER PROJECT	421.01	1,007.68	914.86	587.00
46	POWER	NTPC	BARH STPP STAGE -II	7,341.04	10,852.46	8,664.00	3,511.00
47	POWER	NEEPC O	PARE HYDRO ELECTRIC PROJECT	573.99	1,487.49	1,007.62	914.00
48	POWER	THDCIL	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	3,745.08	647.32	1,254.00
49	POWER	NTPC	BONGAIGAON THERMAL POWER PROJECT	4,375.35	6,749.18	5,287.00	2,374.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
50	POWER	PGCIL	WESTERN REGION STRENGTHENING SCHEME-V	477.69	721.81	520.99	244.00
51	POWER	NHPC	KISHANGANGA HEP (3X110 MW)	3,642.04	5,497.72	3,996.61	1,856.00
52	POWER	NTPC	TAPOVAN-VISHNUGAD HEP (4X130MW)	2,978.48	3,846.30	2,480.00	868.00
53	POWER	THDCIL	TEHRI PUMPED STORAGE PLANT(1000MW)	1,657.00	2,978.86	1,292.48	1,322.00
54	POWER	NEEPC O	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	2,496.90	6,476.34	3,892.98	3,979.00
55	RAILWAYS	NCR	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	158.77	608.02	602.10	449.00
56	RAILWAYS	SCR	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	124.43	925.30	712.02	801.00
57	RAILWAYS	NR	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	2,500.00	19,565.00	10,658.34	17,065.00
58	RAILWAYS	RVNL	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	304.00	968.60	139.48	665.00
59	RAILWAYS	M RTP	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	495.44	1,781.98	440.08	1,287.00
60	RAILWAYS	SWR	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	295.00	1,289.92	1,092.98	995.00
61	RAILWAYS	NR	NANGALDAM-TALWARA(NL),NR	450.00	2,100.00	391.95	1,650.00
62	RAILWAYS	RE	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	171.10	275.08	141.55	104.00
63	RAILWAYS	M RTP	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	5,300.00	7,986.04	2,443.62	2,686.00
64	RAILWAYS	NR	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	325.00	1,564.54	420.71	1,240.00
65	RAILWAYS	NFR	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	300.00	827.73	53.52	528.00
66	RAILWAYS	NFR	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	200.00	496.24	213.72	296.00
67	RAILWAYS	SR	TIDIVANAM-NAGARI (NL)	456.00	1,080.00	194.61	624.00
68	RAILWAYS	SR	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	125.00	490.00	67.57	365.00
69	RAILWAYS	NFR	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	170.00	485.00	417.70	315.00
70	RAILWAYS	SR	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	343.17	914.98	846.18	572.00
71	RAILWAYS	SWR	CHIKBALLA-PUR-GOWRIBIDANUR NL	327.25	367.77	0.00	41.00
72	RAILWAYS	SWR	GADAG-WADI NL	1,117.00	1,922.00	1.89	805.00
73	RAILWAYS	SWR	TORANAGALLU-RANJITPURA DL	146.75	167.50	0.32	21.00
74	RAILWAYS	NR	HARIDWAR-LAKSAR	219.83	329.97	2.38	110.00
75	RAILWAYS	SWR	WHITE FIELD-KOLAR NL	341.05	348.85	0.34	8.00
76	RAILWAYS	SWR	RAYADURGA-TUMKUR NL	970.34	1,743.00	359.06	773.00
77	RAILWAYS	SWR	SHIMOGA-HARIHAR NL	562.74	832.47	0.94	270.00
78	RAILWAYS	SWR	SRINIVASA-PURA-MADANAPALLI NL	296.00	466.65	0.00	171.00
79	RAILWAYS	SWR	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	558.00	692.43	0.00	134.00
80	RAILWAYS	NR	BHANUPALI-BILASPUR BERI NL	1,046.88	2,966.99	40.80	1,920.00
81	RAILWAYS	NR	ROHTAK-MEHAM HANSI	287.00	576.18	3.40	289.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
82	RAILWAYS	SCR	AKOLA-KHANDWA GC AKOLA-AKOT	184.26	2,000.00	17.32	1,816.00
83	RAILWAYS	SWR	BAGALKOT-KUDACHI NL	377.93	986.30	100.76	608.00
84	RAILWAYS	SWR	MUNIRABAD (GINGERA) -RAICHUR NL	179.65	1,350.91	380.62	1,171.00
85	RAILWAYS	SWR	TUMKUR-CHITRADURGA-DAVENGERE NL	913.00	1,801.01	1.47	888.00
86	RAILWAYS	CR	PANVEL PEN DOUBLING	96.16	260.16	240.21	164.00
87	RAILWAYS	CR	PEN ROHA DOUBLING	98.74	203.00	227.84	129.00
88	RAILWAYS	CR	KALYAN-KASARA 3RD LINE	277.70	279.70	4.73	2.00
89	RAILWAYS	CR	WARDHA-NANDED MAHARASHTRA	499.30	2,501.05	84.11	2,002.00
90	RAILWAYS	SR	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	601.43	800.00	0.69	199.00
91	RAILWAYS	M RTP	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	632.68	816.55	60.84	184.00
92	RAILWAYS	NFR	LUMDING-HOJAI PATCH DOUBLING PROJECT	246.07	364.06	0.30	118.00
93	RAILWAYS	NFR	AMBARI FALAKATA TO NEW MAYNAGURI	312.12	453.10	134.79	141.00
94	RAILWAYS	NFR	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	523.17	1,653.55	1,040.11	1,130.00
95	RAILWAYS	NFR	MURKONGSELEK-PASIGHAT NL	165.82	435.58	0.56	270.00
96	RAILWAYS	NFR	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	241.52	394.28	233.46	153.00
97	RAILWAYS	NFR	NEW BG LINE FROM BALURGHAT TO HILLY NFR	242.22	679.57	40.41	437.00
98	RAILWAYS	NFR	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4,083.02	5,307.90	7.79	1,225.00
99	RAILWAYS	SR	CHENGANNUR-CHINGAVANAM	191.72	222.95	112.40	31.00
100	RAILWAYS	SR	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	247.00	951.24	619.87	704.00
101	RAILWAYS	SR	MADURAI-BODINAYAKKANUR	164.41	450.00	16.97	286.00
102	RAILWAYS	SR	ERODE-PALANI	288.57	603.22	1.64	315.00
103	RAILWAYS	NFR	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	283.55	288.81	11.74	5.00
104	RAILWAYS	NFR	NEW COOCHBEHAR TO SAMUKTALA	209.77	441.45	85.78	232.00
105	RAILWAYS	NFR	DIMAPUR-TIZIT NL	4,274.00	4,487.70	0.00	214.00
106	RAILWAYS	NFR	AGARTALA-AKHAURA NL	252.00	886.65	0.00	635.00
107	RAILWAYS	NFR	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	895.00	1,242.25	1,005.81	347.00
108	RAILWAYS	NFR	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	221.42	563.13	22.39	342.00
109	RAILWAYS	SR	KURUPPANTHARA-CHINGAVANAM	270.14	346.15	14.61	76.00
110	RAILWAYS	SR	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	822.39	1,280.83	1,031.83	458.00
111	RAILWAYS	SR	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	271.24	520.00	462.69	249.00
112	RAILWAYS	SR	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	198.68	556.64	268.56	358.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
113	RAILWAYS	SR	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	839.00	1,500.00	0.01	661.00
114	RAILWAYS	SR	CHENNAI-CUDDALORE VIA MAMALLAPURAM	523.52	1,200.00	2.07	676.00
115	RAILWAYS	SR	ATTIPPATTU-PUTTUR	446.87	528.00	2.96	81.00
116	RAILWAYS	NFR	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	1,798.00	1,887.90	0.00	90.00
117	RAILWAYS	ECR	HAJIPUR-RAMDAYALUNAGAR DOUBLING	213.01	367.17	17.19	154.00
118	RAILWAYS	ECR	MOTIHARI-SITAMARHI (NL)	211.00	926.09	4.41	715.00
119	RAILWAYS	ECOR	CHHAPRA-MUZAFFARPUR (NL)	285.07	378.56	111.71	93.00
120	RAILWAYS	ECOR	SAKRI-HASANPUR ROAD (NL)	175.69	325.00	258.31	149.00
121	RAILWAYS	SER	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	258.20	365.00	2.52	107.00
122	RAILWAYS	SER	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	309.44	583.00	144.66	274.00
123	RAILWAYS	SER	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	149.90	230.00	68.67	80.00
124	RAILWAYS	SER	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	289.64	760.00	0.09	470.00
125	RAILWAYS	SER	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	553.63	1,009.00	7.50	455.00
126	RAILWAYS	SER	BOWAICHANDI-ARAMBAGH	267.37	434.00	35.90	167.00
127	RAILWAYS	NCR	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	622.41	2,030.50	3.61	1,408.00
128	RAILWAYS	NWR	AJMER-BANGURGRAM	213.39	218.39	23.63	5.00
129	RAILWAYS	NWR	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	739.65	872.22	793.73	133.00
130	RAILWAYS	NWR	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	456.00	855.16	557.82	399.00
131	RAILWAYS	NWR	THIYAT HAMIRA-SANU	236.93	262.00	0.41	25.00
132	RAILWAYS	NCR	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	1,176.09	3,845.60	2.33	2,670.00
133	RAILWAYS	NWR	RATLAM-DUNGARPUR VIA BANSWARA (NL)	2,082.75	3,500.00	54.23	1,417.00
134	RAILWAYS	WR	VIRAMGAM-SAMAKHIALI (DL)	446.00	685.17	206.59	239.00
135	RAILWAYS	WR	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	320.66	913.48	457.67	593.00
136	RAILWAYS	NER	CHHAPRA-BALLIA UP	295.00	494.92	4.22	200.00
137	RAILWAYS	NFR	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	1,676.31	5,500.00	4,734.45	3,824.00
138	RAILWAYS	NFR	KATAKHAL TO BHAIRABI	227.90	331.40	182.22	104.00
139	RAILWAYS	WR	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	117.36	196.95	198.83	81.00
140	RAILWAYS	NFR	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	850.00	2,973.42	10.44	2,123.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
141	RAILWAYS	WR	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	318.24	321.62	2.91	3.00
142	RAILWAYS	WR	RATLAM-MHOW-KHANDWA-AKOLA (GC)	603.04	1,421.25	420.33	818.00
143	RAILWAYS	ER	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	207.52	207.52	223.44	16.00
144	RAILWAYS	SER	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	148.77	209.00	2.64	60.00
145	RAILWAYS	NER	GHAZIPUR - AUNRIHAR (40 KM)	182.92	197.73	0.00	15.00
146	RAILWAYS	ECOR	DELANG-PURI DOUBLING	165.16	234.71	137.01	70.00
147	RAILWAYS	ECOR	KIRANDUL - JAGDALPUR DOUBLING	826.57	1,143.60	189.12	317.00
148	RAILWAYS	ECOR	JHARSUGUDA-RENGALI DOUBLING	201.00	230.00	218.67	29.00
149	RAILWAYS	ECOR	SAMBALPUR-TALCHER DOUBLING	679.27	1,111.99	60.31	433.00
150	RAILWAYS	SER	MM FROM PANSKURA-GHATAL NL	276.69	426.00	0.00	149.00
151	RAILWAYS	SER	MM FROM BURAMARA-CHAKULIA	466.48	800.00	0.83	334.00
152	RAILWAYS	SR	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	460.94	1,030.00	800.90	569.00
153	RAILWAYS	NWR	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	516.23	516.23	595.68	79.00
154	RAILWAYS	RVNL	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	3,951.98	4,259.48	688.50	308.00
155	RAILWAYS	SWR	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	482.00	874.57	730.11	393.00
156	RAILWAYS	NFR	SEVOK RANGPO, NEFR	1,339.48	4,190.00	88.56	2,851.00
157	RAILWAYS	NFR	KISHANGANJ JALALGARH, NL, NEFR	282.92	565.13	2.80	282.00
158	RAILWAYS	NFR	BHAIRABI SAIRONG, NL, NEFR	619.34	2,820.25	199.31	2,201.00
159	RAILWAYS	NFR	AGARTALA SABROOM, NL, NEFR	813.34	2,876.00	823.83	2,063.00
160	RAILWAYS	SER	TAMLUK DIGHA, LINE DOUBLING (SER)	293.97	1,428.00	466.36	1,134.00
161	RAILWAYS	SR	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	404.19	1,383.45	457.88	979.00
162	RAILWAYS	RVNL	BHOPAL BINA 3D LINE DOUBLING	687.20	800.00	793.71	113.00
163	RAILWAYS	RVNL	SALKA ROAD -ANUPNAGAR LINE DOUBLING	324.90	385.54	230.21	61.00
164	RAILWAYS	RVNL	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	743.00	1,117.11	424.42	374.00
165	RAILWAYS	SER	GOELKERA-MANOHARPUR,(LD)(SER)	261.70	280.00	177.01	18.00
166	RAILWAYS	SCR	MANOHARABAD-KOTHPALL NEW LINE(SCR)	378.56	791.59	5.41	413.00
167	RAILWAYS	ECR	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	332.92	477.88	498.37	165.00
168	RAILWAYS	NR	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	625.30	847.75	835.14	222.00
169	RAILWAYS	ECR	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	162.87	541.00	160.25	378.00
170	RAILWAYS	SCR	GULBARGA-BIDAR,SCR(NL)	242.42	844.00	798.87	602.00
171	RAILWAYS	SR	ANGAMALI-SABARIMALA (N.L.)(SR)	550.00	1,566.00	137.40	1,016.00
172	RAILWAYS	NFR	KATIHAR - JOGBANI (GC)(NEFR)	492.98	1,727.27	743.74	1,234.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
173	RAILWAYS	NCR	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	108.00	432.72	436.85	329.00
174	RAILWAYS	ECR	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	501.69	1,043.56	819.19	542.00
175	RAILWAYS	WCR	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	247.66	1,630.97	488.76	1,383.00
176	RAILWAYS	SCR	MACHERLA-NALGONDA(NL)(SCR)	125.00	480.00	3.51	355.00
177	RAILWAYS	WCR	RAMGANJMUNDI-BHOPAL (NL),WCR	470.92	1,225.90	257.59	755.00
178	RAILWAYS	ECR	PATNA GANGA BRIDGE (NL), ECR	624.47	2,921.00	2,521.72	2,297.00
179	RAILWAYS	ECR	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	921.00	2,363.00	1,691.12	1,442.00
180	RAILWAYS	ECR	KOSI BRIDGE (NL), ECR	322.95	341.41	323.26	18.00
181	RAILWAYS	NFR	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	727.56	6,570.75	2,787.99	5,843.00
182	RAILWAYS	RVNL	RAJATGARH-BARANG(LD),ECOR	166.16	288.00	305.47	139.00
183	RAILWAYS	RVNL	HARIDASPUR-PARADEEP(NL)	301.64	1,185.64	266.35	884.00
184	RAILWAYS	ECOR	KHURDA ROAD-BOLANGIR(NL)ECOR	470.21	1,995.25	355.02	1,525.00
185	RAILWAYS	NR	JIND-SONEPAT (NL),NR	238.56	740.00	639.77	501.00
186	RAILWAYS	RVNL	RAICHUR-GUNTAKAL(DL)(SCR)	136.62	289.93	277.09	153.00
187	RAILWAYS	RVNL	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	133.41	276.00	277.33	144.00
188	RAILWAYS	RVNL	CUTTACK - BARANG (LD)	127.13	225.00	193.37	98.00
189	RAILWAYS	RVNL	SUKINDA ROAD - ANGUL (NL)(ECOR)	183.23	818.29	113.50	635.00
190	RAILWAYS	SECR	CHHINDWARA - NAGPUR (GC)(SECR)	383.79	1,101.16	194.91	717.00
191	RAILWAYS	NCR	ETAWAH-MAINPURI (NL),NCR	120.00	245.39	249.33	129.00
192	RAILWAYS	NER	MAHARAJGANJ-MASRAKH (NL) - NER	218.19	343.00	216.17	125.00
193	RAILWAYS	SER	BANKURA - DAMODAR (GC) (SER)	111.90	2,371.85	486.25	2,260.00
194	RAILWAYS	SWR	BANGLORE - SATYAMANGALAM (NL)(SWR)	138.00	1,382.78	2.81	1,245.00
195	RAILWAYS	SCR	GADWAL - RAICHUR (NL), SCR	92.63	270.00	301.84	209.00
196	RAILWAYS	M RTP	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	1,049.69	3,404.92	3,551.53	2,502.00
197	RAILWAYS	NFR	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	733.00	2,531.34	1,732.43	1,798.00
198	RAILWAYS	SCR	KOTLPALLI-NARASAPUR (NL) (SCR)	330.00	1,047.00	1.29	717.00
199	RAILWAYS	SR	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	280.00	1,122.00	889.95	842.00
200	RAILWAYS	SR	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	100.00	980.00	596.66	880.00
201	RAILWAYS	SER	RANCHI-LOHARDAGA(GC),SER	194.07	335.00	230.67	141.00
202	RAILWAYS	SER	HOWRAH-AMTA-CHAMPADANGA NL (SER)	393.46	1,026.00	181.48	633.00
203	RAILWAYS	SCR	MUNEERABAD-MAHABOBNAGAR(NL),SCR	218.24	645.00	309.19	427.00
204	RAILWAYS	NFR	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	1,500.00	4,996.19	3,410.06	3,496.00
205	RAILWAYS	NER	KANPUR-KASGANJ-MATHURA(GC),NER	677.97	1,651.54	1,621.40	974.00
206	RAILWAYS	SWR	HUBLI-ANKOLA(NL),SWR	227.00	2,135.00	117.24	1,908.00
207	RAILWAYS	SCR	NANDYAL-YERRAGUNTLA(NL),SCR	155.74	883.00	755.50	727.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
208	RAILWAYS	SR	KARUR-SALEM(NL),SR	155.55	800.00	800.66	645.00
209	RAILWAYS	SECR	GONDIA-JABALPUR(GC),(SECR)	386.30	1,544.40	590.26	1,158.00
210	RAILWAYS	CR	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	514.68	2,820.00	329.67	2,305.00
211	RAILWAYS	SR	CALICUT-MANGALORE (DL) (SR)	240.00	579.37	599.40	359.00
212	RAILWAYS	NFR	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	36.80	1,336.57	255.55	1,300.00
213	RAILWAYS	CR	AMRAVATI-NARKHER NL(CR)	663.01	725.00	586.75	62.00
214	RAILWAYS	WR	VIRAMGAM-BHILDI(WR),GC	155.66	548.01	201.26	392.00
215	ROAD TRANSPORT AND HIGHWAYS	NHAI	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	157.47	154.57	228.30	71.00
216	ROAD TRANSPORT AND HIGHWAYS	NHAI	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	237.80	237.80	275.00	37.00
217	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	682.00	682.00	752.70	71.00
218	ROAD TRANSPORT AND HIGHWAYS	NHAI	KRISHNANAGAR-BERHAMPUR	702.16	702.16	726.40	24.00
219	ROAD TRANSPORT AND HIGHWAYS	NHAI	6-LANING OF DHANKUNI-KHARAGPUR SECTION	1,396.18	1,396.18	1,934.00	538.00
220	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF BRAHAMPORE-FARAKA	998.79	998.79	1,610.00	611.00
221	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF FARAKA-RAIGANJ	1,078.84	1,078.84	1,922.00	843.00
222	ROAD TRANSPORT AND HIGHWAYS	NHAI	JAIPUR-REENGUS	267.81	267.81	564.50	297.00
223	ROAD TRANSPORT AND HIGHWAYS	NHAI	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	909.00	909.00	982.90	74.00
224	ROAD TRANSPORT AND HIGHWAYS	NHAI	BHUBANESWAR TO PURI	500.29	500.29	633.30	133.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
225	ROAD TRANSPORT AND HIGHWAYS	NHAI	2 LANNING OF MUZAFFARPUR - SONBARSA	511.54	511.54	1,179.00	667.00
226	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF CHAPRA-HAJIPUR	575.00	575.00	835.60	261.00
227	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING WITH PS MOTIHARI-RAXAUL	375.09	375.09	408.10	33.00
228	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHAMBAL BRIDGE, NH-76 (RJ-5)	275.00	281.31	180.10	6.00
229	ROAD TRANSPORT AND HIGHWAYS	NHAI	BRAHMPUTRA BRIDGE, NH NO-31	217.61	309.56	258.40	92.00
230	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG, NH-54	196.00	363.74	242.80	168.00
231	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	212.00	386.10	127.10	174.00
232	ROAD TRANSPORT AND HIGHWAYS	NHAI	DHARAMTUL TO SONAPUR (AS-19)	200.00	200.00	289.50	90.00
233	ROAD TRANSPORT AND HIGHWAYS	NHAI	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	160.00	160.00	197.60	38.00
234	ROAD TRANSPORT AND HIGHWAYS	NHAI	NALBARI T BIJNI (AS-7)	208.00	208.00	290.60	83.00
235	ROAD TRANSPORT AND HIGHWAYS	NHAI	NALBARI TO BIJNI (AS-6)	225.00	225.00	258.40	33.00
236	ROAD TRANSPORT AND HIGHWAYS	NHAI	GUWAHATI TO NALBARI (AS-5)	198.16	198.16	242.40	44.00
237	ROAD TRANSPORT AND HIGHWAYS	NHAI	KUNDUPUR-SURATHKAL & MANGLORE	671.00	671.00	1,273.00	602.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
238	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	852.00	852.00	901.60	50.00
239	ROAD TRANSPORT AND HIGHWAYS	NHAI	ARMUR TO KADLOOR YELLAREDDY	390.56	390.56	631.70	241.00
240	ROAD TRANSPORT AND HIGHWAYS	NHAI	HAZARIBAGH-RANCHI	625.07	625.07	995.90	371.00
241	ROAD TRANSPORT AND HIGHWAYS	NHAI	TALEGAON-AMRAVATI	567.00	567.00	1,388.00	821.00
242	ROAD TRANSPORT AND HIGHWAYS	NHAI	JAIPUR-TONK-DEOLI	792.06	792.06	1,983.00	1,191.00
243	ROAD TRANSPORT AND HIGHWAYS	NHAI	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	1,108.00	2,288.00	3,466.00	2,358.00
244	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	572.30	572.30	886.90	315.00
245	ROAD TRANSPORT AND HIGHWAYS	NHAI	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	1,693.75	1,693.75	2,762.00	1,068.00
246	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	785.50	785.50	941.00	156.00
247	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANNING OF AHMEDABAD TO GODHARA	1,008.50	1,008.50	1,392.00	384.00
248	ROAD TRANSPORT AND HIGHWAYS	NHAI	2 LANNING OF MOKAMA-MUNGER	351.54	351.54	396.60	45.00
249	ROAD TRANSPORT AND HIGHWAYS	NHAI	INDORE-DEWAS(NH-3)	325.00	325.00	447.50	123.00
250	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANING OF NAGPUR-BETUL	2,498.76	2,498.76	2,786.00	287.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
251	ROAD TRANSPORT AND HIGHWAYS	NHAI	MURADABAD-BAREILY	1,267.00	1,267.00	2,425.00	1,158.00
252	ROAD TRANSPORT AND HIGHWAYS	NHAI	DEVIHALLI-HASSAN	453.00	453.00	808.70	356.00
253	ROAD TRANSPORT AND HIGHWAYS	NHAI	PANIPAT-ROHTAK	807.00	807.00	1,209.43	402.00
254	ROAD TRANSPORT AND HIGHWAYS	NHAI	DEOLI-KOTA	593.00	593.00	761.30	168.00
255	ROAD TRANSPORT AND HIGHWAYS	NHAI	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	574.00	574.00	991.70	418.00
256	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING WITH PS KHAGARIA-PURNEA	664.00	664.00	776.40	112.00
257	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	1,535.00	1,535.00	2,188.00	653.00
258	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING OF SHILONG BYPASS	226.00	226.00	282.30	56.00
259	ROAD TRANSPORT AND HIGHWAYS	NHAI	JORBAT - BARAPANI	536.00	536.00	759.90	224.00
260	ROAD TRANSPORT AND HIGHWAYS	NHAI	SAMAIKHALI - GANDHIDHAM	805.39	805.39	842.20	37.00
261	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	1,250.00	1,250.00	1,374.00	124.00
262	ROAD TRANSPORT AND HIGHWAYS	NHAI	GHAZIABAD-ALIGARH NH-91	1,141.00	1,141.00	2,445.00	1,304.00
263	ROAD TRANSPORT AND HIGHWAYS	NHAI	ROHTAK-BAWAL	650.00	650.00	1,178.00	528.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
264	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHENNAI-TADA(SIX LANE)	353.37	353.37	446.20	93.00
265	ROAD TRANSPORT AND HIGHWAYS	NHAI	KISHANGARH-AJMER-BEAWER	795.00	795.00	1,133.00	338.00
266	ROAD TRANSPORT AND HIGHWAYS	NHAI	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	1,509.10	1,509.10	2,686.00	1,177.00
267	ROAD TRANSPORT AND HIGHWAYS	NHAI	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	940.00	940.00	1,601.00	661.00
268	ROAD TRANSPORT AND HIGHWAYS	NHAI	DELHI/ HARYANA BORDER TO ROHTAK	486.00	486.00	667.10	181.00
269	ROAD TRANSPORT AND HIGHWAYS	NHAI	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	232.45	232.45	317.50	85.00
270	ROAD TRANSPORT AND HIGHWAYS	NHAI	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	557.00	557.00	932.30	375.00
271	ROAD TRANSPORT AND HIGHWAYS	NHAI	AGRA-BYPASS(NS-1/UP-1), NH-2,3	348.16	465.50	322.70	117.00
272	ROAD TRANSPORT AND HIGHWAYS	NHAI	SONAPUR TO GUWAHTI (AS-3)	245.00	245.00	491.20	246.00
273	ROAD TRANSPORT AND HIGHWAYS	NHAI	NAGAON TO DHARAMTUL (AS-2)	264.72	264.72	299.20	34.00
274	ROAD TRANSPORT AND HIGHWAYS	NHAI	GUWAHTI TO NALBARI (AS-4)	175.96	175.96	182.50	7.00
275	ROAD TRANSPORT AND HIGHWAYS	NHAI	NALBARI TO BIJNI (AS-8)	200.00	200.00	281.60	82.00
276	ROAD TRANSPORT AND HIGHWAYS	NHAI	RAJMARG CHORHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	251.03	251.03	326.30	75.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
277	ROAD TRANSPORT AND HIGHWAYS	NHAI	KOTA BYPASS,RJ-4, NH-76 (NHAI)	275.00	250.39	285.30	10.00
278	ROAD TRANSPORT AND HIGHWAYS	NHAI	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	332.94	332.94	550.30	217.00
279	ROAD TRANSPORT AND HIGHWAYS	NHAI	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	195.00	195.00	231.20	36.00
280	ROAD TRANSPORT AND HIGHWAYS	NHAI	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	155.00	201.66	191.80	47.00
281	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	280.00	361.00	301.80	81.00
282	ROAD TRANSPORT AND HIGHWAYS	NHAI	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	199.81	385.13	83.98	185.00
283	ROAD TRANSPORT AND HIGHWAYS	NHAI	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	155.04	280.13	114.80	125.00
284	ROAD TRANSPORT AND HIGHWAYS	NHAI	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	230.00	230.00	233.00	3.00
285	SHIPPING AND PORTS	MUMBAI PORT TRU	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	1,228.00	1,460.00	1,049.37	232.00
286	SHIPPING AND PORTS	PORT TRUST	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	150.00	600.00	139.80	450.00
287	SHIPPING AND PORTS	RVNL	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	245.67	373.22	351.18	128.00
288	SHIPPING AND PORTS	MUMBAI PORT TRU	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	366.39	669.46	407.32	303.00
289	STEEL	RINL	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	8,692.00	12,291.00	11,339.32	3,599.00
290	STEEL	RINL	REVAMPING OF SINTER MACHINES - 1 AND 2	343.00	488.40	25.02	145.00
291	URBAN DEVELOPMENT	MRTD	BANGALORE METRO RAIL PROJECT	6,395.00	11,609.00	2,267.57	5,214.00
			TOTAL	301,355.57	513,113.63	318,126.18	235,679.00

Details of Delayed Projects w.r.t. Original and Revised Schedule

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	20,713.00	12/2008 -	10/2015	82	31.12	Slippage of commitments by M/s Atomstroyexport, Russian Federation.
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	5,006.93	09/2010 09/2016	09/2016	72	62.57	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	6,853.00	12/2015 -	10/2017	22	0	Late receipt of financial sanction.
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,669.00	12/2016 -	05/2018	17	0	Delay in supply of equipments from various vendors.
	Total		40,442.00 -	46,726.00	37,241.93					
	<u>CIVIL AVIATION</u>									
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]JAAI,CHANDIGARH	02/2011	452.00 489.00	489.00	449.63	03/2015 -	07/2015	4	8.19	
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]JAAI,MULTI STATE	10/2012	217.60 -	244.10	0.04	03/2015 -	09/2015	6	12.18	
7	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]JAAI,SIKKIM	01/2009	309.46 -	309.46	355.88	01/2011 06/2016	06/2017	77	0	
	Total		979.06 -	1,042.56	805.55					
	<u>COAL</u>									
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,583.77	3,213.77	06/2009 03/2013	07/2015	73	76.47	The project also got delayed due to the slow execution of work by M/s BHEL, the Main plant package contractor.

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,277.83	03/2012 05/2014	07/2015	40	34.63	The delay in late finalisation of sub-contractor by M/s BHEL, Change of design from pile foundation to open foundation, delay in execution of design and engineering, inadequate mobilization of resources by the contractor and slow progress of civil & structural fabrication & erection and TG erection in unit I & unit II.
10	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	151.74	10/2014 -	08/2015	10	0	There is delay in manufacturing and supply of WTG equipments and completion of foundations. As on 31.05.2015 all 34 lands had been registered but only 15 sets WTG components in full have been supplied. Only 14 WTG erection have been completed out of which only 8 WTG have been commissioned. Approval of 33 foundation drawings have been completed, but only 27 foundations have been completed. Out of 34 lands acquired, Soil investigation completed in 33 locations.
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.58	03/2013 09/2012	09/2015	30	478.5	-
12	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,844.83	03/2014 -	03/2016	24	0	
13	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,664.03	03/2014 -	03/2016	24	0	
14	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	473.48	03/2013 -	03/2016	36	-6.11	
15	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH	06/2011	746.04 535.10	535.10	379.04	03/2015 -	03/2016	12	-28.27	
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	76.55	07/2012 -	03/2016	44	0	
17	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	259.40	21.42	03/2012 -	03/2016	48	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
18	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.60	03/2014 -	03/2016	24	0	
19	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	57.62	03/2014 -	03/2016	24	0	(1)Delay in finalization of Global tender. (2) Delay in rehabilitation and Resettlement activity due to resistance by villagers.
20	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.28	03/2012 -	03/2016	48	0	-
21	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48	0	-
22	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.92	03/2011 -	03/2016	60	0	
23	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	-	03/2013 -	03/2016	36	0	
24	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	143.74	03/2012 -	03/2016	48	0	
25	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	9.97	04/2014 03/2016	03/2016	23	0	
26	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	77.47	03/2015 -	04/2016	13	0	-
27	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	89.89	05/2014 -	04/2016	23	0	
28	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	34.51	04/2014 -	04/2016	24	0	
29	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	147.57	03/2010 -	03/2017	84	0	
30	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 341.63	341.63	124.92	03/2011 -	03/2017	72	0	i)Law & Order ii) Coal evacuation problems

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.18	225.39	03/2011 -	03/2017	72	0	Lol for procurement of transporting equipment was issued on 14-01-2015 subject to the pending approval of CIL Board. It was placed before CIL Board on 22-02-2015. CIL Board advised to prepare a comprehensive report of Jhanjra. Further ECL has appealed to CIL for approval of advance actions for procurement of transporting equipment on 09-05-2015 citing the comprehensive report is under process of approval by ECL Board. Finally CIL Board approved the advance action proposal on 12-05-2015.
32	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	175.03	03/2013 -	03/2017	48	0	
33	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	148.45	03/2010 -	03/2017	84	0	
34	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	99.63	12/2012 -	03/2017	51	0	-
35	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	191.26	03/2012 -	03/2017	60	0	
36	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	173.03	03/2013 -	03/2017	48	.02	
37	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCCL, JHARKHAND	12/2007	179.87 -	179.87	81.52	03/2012 -	03/2017	60	0	
38	KARMA OCP (1.0 MTY) - [N06000088]CCCL, JHARKHAND	06/2009	162.46 -	162.46	65.96	03/2014 -	03/2017	36	0	
39	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	0	-
40	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	11.68	07/2016 -	03/2017	8	0	-
41	SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	71.72	03/2012 -	03/2018	72	0	-
42	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	206.52	03/2014 -	03/2018	48	0	
43	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	-
44	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	-

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
45	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	81.40	03/2016 -	03/2018	24	0	
46	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	965.20	12/2015 04/2018	04/2018	28	0	Delay is caused by retendering of SG & Aux. package and revision of time Schedule for the packages.
47	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2019	48	0	-
48	MOONIDH XV SEAM UG - [N06000098]JBCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	42.39	04/2015 -	04/2019	48	0	
49	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	
50	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	
51	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	
52	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	
	Total		31,417.66 -	35,425.80	19,096.76					
	<u>STEEL</u>									
53	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	463.35	04/2013 09/2014	06/2015	26	0	
54	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]JRLN, MULTI STATE	07/2007	480.00 -	450.00	388.34	09/2009 05/2012	07/2015	70	-6.25	
55	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	132.35	09/2014 -	07/2015	10	0	
56	CAPTIVE POWER PLANT - 2 - [N12000087]JRLN, ANDHRA PRADESH	02/2011	677.00 -	677.00	522.58	09/2013 -	07/2015	22	0	
57	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,164.71	12/2011 -	08/2015	44	0	
58	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	387.59	05/2013 01/2015	08/2015	27	0	
59	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	192.84	12/2014 -	09/2015	9	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
60	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATTISGARH - [N12000078]SAIL, CHHATTISGARH	07/2012	332.65 -	332.65	199.46	08/2014 -	11/2015	15	0	
61	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	158.95	10/2013 -	12/2015	26	0	
62	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	249.80	06/2015 -	12/2015	6	0	
63	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATTISGARH	08/2010	17,265.00 -	17,265.00	14,537.66	03/2013 -	03/2016	36	0	
64	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	260.12	07/2015 -	03/2016	8	0	
65	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATTISGARH	01/2010	15,525.00 -	15,525.00	7,257.18	05/2015 12/2016	12/2016	19	0	
66	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	152.00	07/2015 -	03/2017	20	0	
	Total		44,255.04 -	44,225.04	30,066.93					
	<u>PETROCHEMICALS</u>									
67	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,736.89	04/2012 12/2013	09/2015	41	80.08	• Lack of adequate and effective supervision by the EPMC, M/s EIL. • Misplacement / mismanagement of free issue materials.
	Total		5,460.61 -	9,833.52	8,736.89					
	<u>PETROLEUM</u>									

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
68	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 06/2012	06/2015	110	820.2	-Termination of Contract. - Non-cooperation by equipments suppliers, sub-contractors and consultant. - Delay in availability of subsea manifold and prolonged repairing work. - Complications in well G-1-9 and well control activities. -Delay in proceedings in Mumbai High Court and prolonged legal battle. -Delay in finalisation of out of court settlement. ONGC took over the project in 2010 after settlement with M/S CEL.
69	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	225.72	08/2012 06/2015	06/2015	34	-11.94	-Construction of activities hampered due to ROU related issues. -Marshy and highly undulating terrain resulting in poor progress in pipeline laying work.
70	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 06/2015	06/2015	22	-18.75	- Delay in award of work. - Slow progress by the contractors. -Custom bond issue with M/S SHM Shipcare and some vessels of M/s Abu Dhabi waiting for customs and DGFT clearances.
71	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,345.03	12/2012 -	06/2015	30	0	
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,079.05	10/2011 -	06/2015	44	75.35	Completion delayed primarily because the rectification of rock wedge failure in cavern A1 took more time.Zones of poor geology encountered during excavation of balance bench.Slow construction progress of AG facility Works as it was dependent on completion of UG works.
73	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,770.24	05/2015 05/2015	07/2015	2	0	

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
74	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,171.43	12/2014 -	08/2015	8	0	
75	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39	-38.7	- delay for obtaining NOC from the MOD (air force). -ROW problem at site due to intervention of local villagers. Work commenced under police protection. -Scope revision and delay in award of work.
76	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	158.12	12/2014 -	09/2015	9	0	Pre-commissioning activities are in progress. Hook up shutdown for Mounded bullet pipelines are to be done during existing Refinery-III Shutdown which is planned in July 2015.
77	PARADIP REFINERY PROJECT - [N16000058]OCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,273.28	11/2012 11/2013	10/2015	35	16.05	Repair of Steam Turbine
78	MARKETING TERMINAL AT PARADEEP - [N16000168]OCL, ODISHA	07/2009	199.75 239.73	239.73	190.20	07/2013 -	10/2015	27	20.02	
79	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 429.00	429.06	330.19	10/2014 10/2015	10/2015	12	0	-each well due to deeper depth needs more time. - slot damage
80	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41	-20.13	Delay in placement of order for 2 nos drilling rigs. One of the bidder went to court in anticipation of disqualification of their bid
81	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015	51	0	•Delay in preparation of drawing and additional model testing of Hull . •Delay in procurement of steel by PSL. •Shortage of skilled manpower at contractors end. •Inadequate ancillary / sub-contractors at the location. •Lack of planning to match resources to work targets. •Change in delivery location.
82	DE-BOTTLENECKING OF SMPL - [N16000089]OCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,234.16	08/2015 -	12/2015	4	0	Environment Clearance and Wildlife clearance is awaited in Banaskantha district in Gujarat.

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
83	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,436.51	01/2014 12/2015	12/2015	23	0	-Slow progress by contractor. - Slow progress by the contractor in laying of pipelines. - Delay in conversion work of Sagar Samrat to MOPU. - Delay in drilling of some wells due to non-availability of light rig.
84	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	114.88	09/2012 12/2015	12/2015	39	-24.14	-Slow progress in civil work and fabrication work due to less resource mobilization. -Unresolved commercial issues between M/s UEM and NSF Vendor. -Delay in finalization of Process package leading to delay in engg and procurement services. -Delay in delivery of Nut Shell filters and internal of IGF units.
85	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	885.75	05/2013 06/2014	12/2015	31	45.83	-Increase in scope of work -Delay in procurement of steel and fabrication of legs by the contractor.
86	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,MULTI STATE	08/2011	586.00 -	586.00	316.02	08/2015 -	12/2015	4	0	Delay in acquisition of land at Balasore by Govt of Odisha for pump station construction has affected the project completion schedule.
87	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	449.51	04/2015 04/2015	12/2015	8	-39.69	
88	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]OCL,JHARKHAND	04/2011	191.96 -	191.96	89.83	05/2015 -	12/2015	7	0	land acquisition
89	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	970.98	10/2011 -	01/2016	51	67.62	Some difficulties being faced during Cavern Acceptance Test, which is in progress.
90	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,404.06	01/2012 -	01/2016	48	70.49	Progress is slow due to heavy rains during the period.

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
91	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,146.48	09/2012 -	03/2016	42	0	Project is delayed primarily due to delay in receipt of Forest Clearance. Demand note against royalty is yet to be received for two Forest Divisions of Odisha, after which tree cutting will be commenced.
92	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	280.86	06/2011 03/2012	03/2016	57	0	
93	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,204.41	03/2015 05/2016	05/2016	14	29.42	• Pipeline package: Non-performance by the contractor: : The contractor of pipeline package was served notice of termination of the contract on 11.01.2014 and again on 07.03.2014 in view of contractor's inability to execute the work on time. The contractor served notice of arbitration on 01.10.2014 to settle disputes. ONGC proposed resolution of disputes through Outside Expert Committee (OEC) on 03.11.2014, which the contractor agreed on 07.11.2014. The contractor, thereafter, proposed certain pre-conditions to start the work and since then holding up the work. • Delay in conversion of Rig Sagar Laxmi to MOPU due to financial issues and non-performance of the contractor.
94	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	541.46	05/2014 05/2016	05/2016	24	0	-Delay due to retendering. -Package-1 delayed due to representation by M/s Essar in IEM. -Slow progress by contractor.

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
95	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	Pipeline package: Non-performance by the contractor : The contractor of pipeline package was served notice of termination of the contract on 11.01.2014 and again on 07.03.2014 in view of contractor's inability to execute the work on time. The contractor served notice of arbitration on 01.10.2014 to settle disputes. ONGC proposed resolution of disputes through Outside Expert Committee (OEC) on 03.11.2014, which the contractor agreed on 07.11.2014. The contractor, thereafter, proposed certain pre-conditions to start the work and since then holding up the work.
96	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	127.55	03/2014 05/2016	05/2016	26	0	-Design platform integrity issue was raised by the contractor which required review of integrity analysis and this took time in resolution. - Clubbing of project facilities alongwith C-26 Cluster development project. - slow progress by the contractor.
97	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	37.49	02/2016 -	05/2016	3	0	Anticipated completion is getting delayed due to retender of mechanical job.
98	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39	0	- Revision in scope of work. - High quoted price resulting in closure of the original tender. - Re-inviting tender after preparing revised BEC.
99	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	416.70	08/2015 -	06/2016	10	0	2nd Stage Forest clearance is awaited in Odisha.
100	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	273.36	03/2015 11/2015	06/2016	15	37.72	Heavy rain in Assam.Refloating of tender will have impact on timeline

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
101	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	699.72	11/2015 07/2016	07/2016	8	0	Restricted working environment due to nearby operating plants, availability of limited space for storage & fabrication, Restricted timings for radiography activities etc.. were affecting the progress of the work.
102	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	237.49	10/2014 10/2016	10/2016	24	49.38	
103	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	481.49	11/2015 11/2016	11/2016	12	25.84	
104	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,777.84	03/2013 03/2016	03/2017	48	-3.5	-Substantial time taken for mobilization by survey and other agency. -ROU acquisition and issue related to payment -Delay in forest clearance. -Inadequate manpower at working sites affected the construction progress. -Local problem and court cases by tea gardener. -Slow progress in engineering and procurement.
105	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2017	12	0	
106	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25	0	Delay in tendering process.
107	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 607.06	607.06	57.94	01/2016 07/2017	07/2017	18	0	
108	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	0	
109	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017	32	0	
110	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	335.37	02/2016 12/2017	12/2017	22	31.51	nil
111	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	96.08	09/2017 -	12/2017	3	0	Keeping the high cost in LSTK mode, execution methodology has been changed from LSTK to Hybrid which has resulted in extension by 3 months.

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
112	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 -	3,957.00	5.70	01/2013 -	12/2018	71	0	No firm customer tie up and non readiness of gas source.
113	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	0	
114	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	47.07	05/2019 03/2020	03/2020	10	0	nil
115	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 -	06/2018	53	-6.92	Termination of contract twice : on 24.01.2014 due to poor performance of the contractor and on 22.07.14 due to bids found Techno-Commercially unacceptable.
	Total		100,568.95 -	112,167.48	60,444.85					
	<u>POWER</u>									
116	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,727.47	11/2012 -	07/2015	32	0	Delay in land acquisition of Vindhyachal sub station & forest clearance.
117	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	198.64	03/2014 -	07/2015	16	0	Associated line not ready (TBCB line).
118	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	914.86	07/2013 -	08/2015	25	139.35	
119	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,825.87	03/2014 06/2015	08/2015	17	20.87	Involvement of wildlife sanctuary & forest clearance awaited.Severe ROW problem faced.
120	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	811.38	03/2015 -	09/2015	6	0	Delay in land acquisition of Kudgi Sub station (land acquired in Feb 14).
121	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,854.54	03/2013 06/2015	09/2015	30	13.18	Forest clearance & severe ROW problem in Odisha.
122	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,750.90	12/2013 -	09/2015	21	0	Delayed forest clearance.
123	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	135.50	01/2013 -	09/2015	32	0	Delayed due to delay in land acquisition of Kishanganj Sub station.

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
124	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,941.66	08/2014 -	09/2015	13	0	Delay in land acquisition for Varansai S/stn. & forest clearance.
125	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	520.00	02/2014 -	09/2015	19	0	Severe ROW problem
126	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,510.47	10/2014 -	09/2015	11	0	Severe ROW problem
127	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,088.18	11/2014 -	09/2015	10	0	Severe ROW problem faced in Guttur & Krishana Distt in Andhara Pradesh.
128	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	190.22	04/2015 -	09/2015	5	0	Delay in land acquisition of Varansai Sub station (land acquired in Jun 14).
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	485.72	07/2013 05/2015	11/2015	28	-8.45	Forest clearance delayed & weather problem.
130	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	1,000.61	12/2007 12/2009	12/2015	96	0	Severe ROW problem in Karnataka.
131	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,485.26	11/2013 -	12/2015	25	0	Delayed due to delay in land acquisition of Kishanganj S/stn. and severe ROW problem.
132	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	454.91	11/2013 -	12/2015	25	0	Delayed due to delay in S/stn. land acquisition (land acquired in Apr 13) and forest clearance delayed.
133	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	282.57	08/2014 06/2015	12/2015	16	16.63	Severe ROW problem in Karnataka.
134	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	521.62	11/2014 -	12/2015	13	0	Severe ROW problem in Ultrakhand & forest clearance delayed.
135	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	142.20	06/2015 -	12/2015	6	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
136	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	765.33	06/2015 -	12/2015	6	0	Forest clearance awaited & contractual issue.
137	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,893.05	09/2008 03/2012	03/2016	90	21.34	Severe ROW problem in Kerala.
138	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	520.99	09/2010 06/2013	03/2016	66	51.1	Severe ROW problem, forest clearance & non-readiness of Kudus S/stn. by MSETCL
139	PARE HYDRO ELECTRIC PROJECT - [N18000045]NNEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,007.62	08/2013 -	03/2016	31	159.15	Law & order problem from time to time and change in geotechnical parameters necessitating revision of side slopes.
140	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	468.06	11/2011 -	03/2016	52	0	Severe ROW problem in western UP due to farmers agitation & high compensation demand.
141	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	330.37	02/2012 -	03/2016	49	0	Severe ROW problem in western UP due to farmers agitation demanding high compensation.
142	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,086.48	10/2012 -	03/2016	41	0	Forest clearance awaited & contractual issue.
143	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,005.30	08/2013 -	03/2016	31	0	Generation Project delayed. Due to agitation by local people. Severe ROW problem in NER & West Bengal.
144	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,498.75	01/2015 -	03/2016	14	0	Delay in land acquisition of Alipurduar HVDC terminal & wildlife clearance for Punatsangchu - Alipurduar line awaited.
145	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,156.70	12/2012 -	03/2016	39	0	Severe ROW problem, forest clearance, local disturbance in NER & contractual issues.
146	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,052.09	08/2012 -	03/2016	43	0	Poor performance by contractor.
147	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	735.24	11/2012 -	03/2016	40	0	Severe ROW problem in western UP due to farmers agitation and high compensation demand.

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
148	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,313.72	04/2013 -	03/2016	35	0	Delay in land acquisition of Bareilly sub station & severe ROW problem faced.
149	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,713.45	05/2014 -	03/2016	22	0	Delay in land acquisition of Champa HVDC Station & contractual issue in 01 line.
150	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,199.43	07/2014 -	03/2016	20	0	Forest clearance awaited & severe ROW problem.
151	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,214.43	08/2014 12/2015	03/2016	19	27.6	Forest clearance awaited & non-readiness of Kudus extn. by MSETCL.
152	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,149.72	01/2015 -	03/2016	14	0	Forest clearance awaited.
153	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,478.09	06/2015 -	03/2016	9	0	Delayed due to delay in land acquisition of Champa HVDC station.
154	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,397.31	10/2014 -	03/2016	17	0	Delayed land acquisition of Kanpur sub station.
155	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	771.05	12/2015 -	03/2016	3	0	Involvement of Huge forest & severe ROW problem in Odisha.
156	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,916.06	01/2013 -	03/2016	38	0	Non performance of Civil, Swyd, CHP, AHP agencies

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
157	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,787.90	09/2009 -	06/2016	81	81.76	1. Initial delay in handing over of forest land & start of work 2. Bandh/ closure by locals, political outfits like GJMM and its effect 3. Due to inordinate delay and extended stay, BOQ rates became unworkable and resulted in cash deficit of Civil Contractor. 4. Delay in award of E&M contract due to clarification regarding participation of Chinese firm
158	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND INDBARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,813.96	09/2014 -	06/2016	21	0	Severe ROW problem & contractual issues in 01 line.
159	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	75.53	09/2014 -	06/2016	21	0	Severe ROW problem faced.
160	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	07/1998	368.72 1,381.71	1,381.71	843.49	07/2006 12/2015	10/2016	123	274.73	
161	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,996.61	01/2016 -	11/2016	10	50.95	1. Law & order problem in the project area and Kashmir Valley. 2. Delay in settlement of R&R plan of the project which is pending with J&K State Govt. for approval and strike by PFA's 3. Due to delay decision of International Court of Arbitration
162	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80 -	1,272.80	1,110.83	11/2012 -	12/2016	49	0	Delay in land acquisition of Sub station & forest clearance awaited.
163	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,892.98	12/2009 03/2017	03/2017	87	159.38	Commissioning Scheduled is delayed due to poor geology, Redesigning of Dam parameter as suggested by expert from CWC & CEA, Realignment of HPT, Flash flood, Deviation in work, Contractual issue Non-clearance for quarry operation from forest department of Arunachal Pradesh.

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
164	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,287.00	09/2011 -	03/2017	66	54.25	- Frequent Bandh calls by local outfits (Total Bandh- 262 days) leading to stoppage of work at site for more than 500 days. - Eruption of ethnic violence in Jul-12, May-14 & Dec-14 (41 days) leading to stoppage of work for 171 days. - Poor performance of BOP/Civil contractors due to geo-political situation in the region.
165	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	5,353.00	4,753.79	05/2014 -	06/2017	37	0	- Delay in balance land acquisition. - Law & order problem.
166	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,974.00	11/2016 -	08/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
167	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42 -	195.42	27.73	02/2014 -	09/2017	43	0	
168	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
169	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,899.00	01/2011 10/2014	03/2018	86	73.65	- Non performance of Russian agency M/s TPE & M/s PM. - TPE stopped work from Oct-13 and the contract of M/s TPE was terminated on 14.01.15.
170	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL, UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,292.48	07/2010 02/2016	05/2018	94	79.77	1. Non availability of Asena Quarry 2. 4.668 Ha. Land diversion case for dumping area at Village Chopra.
171	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,109.77	09/2009 -	12/2018	111	99.48	1. Initial delay in start of Dam works due to delay in Revised Forest clearance 2. Burial of TBM during Nov, 06. Heavy ingress of water with silt from TBM face. Treatment of shear zone, 3. Back hill slope failure of Power House three times, 4. Ban on use of aggregates by Hon'ble High Court, Shimla

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
172	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,480.00	03/2013 -	12/2018	69	29.14	- Flash Flood in Jun-12 in Uttarakhand leading to damage of coffer dam & approach road. - TBM stuck up thrice & L&T Alpine JV did not perform leading to termination of contract. - HRT Package is under retender & expected to be awarded in soon. The completion schedule is 3 years after award of HRT Package.
173	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	647.32	06/2013 12/2019	12/2019	78	50.31	
	Total		144,924.18 -	172,160.60	119,038.35					
	<u>HEAVY INDUSTRY</u>									
174	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	122.78	
	Total		1,718.00 -	3,827.30	.00					
	<u>RAILWAYS</u>									
175	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66	300.67	
176	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	30	81.45	Commissioning target is subject to handing over of land by GoK.
177	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	0	
178	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	79	156.57	Railway bridge targeted for commissioning in October, 2015 (resettlement of 3 families is involved.) Road bridge would take time as there are issues in land acquisition.

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
179	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	104.49	
180	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
181	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	367.76	Railway bridge targeted for commissioning in October, 2015. However Road bridge would take time as there are issues in land acquisition.
182	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	16.41	
183	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 12/2010	03/2016	144	259.68	Total length of railway line is 27 km. Land hasnot been acquired in 2.7 km length between Kharkopar and Ranjanpada (25 hectare private land and also forest land). Construction is in progress in part of the line and only part commissioning can be done.
184	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	177.01	02/2006 -	03/2016	121	6.99	Progress is slow due to explosive stocking is not allowed by SP.
185	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defroze and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut-Saharanpur).

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.65	03/2014 -	03/2016	24	-9.96	
187	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	
188	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	Line commissioned and freight train operations commenced. Passenger operations to commence in August 2015.
189	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	Work delayed due to foundation problem.
190	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
192	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	
193	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	
194	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	
195	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	
196	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
197	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
198	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
199	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
200	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	Phase- I of the project is to be completed by June, 2018 subject to availability of land and funds. Target for phase-II cannot be fixed since the works are held up due to State Govt's proposal for change of alignment of the underground portion.
201	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	
202	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
203	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
204	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Progress is going as per the allotment of budget grant.
205	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
206	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.
207	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
208	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
	Total		33,808.74 -	91,603.96	40,851.09					
	ROAD TRANSPORT AND HIGHWAYS									
209	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	06/2015	30	0	
210	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	07/2015	62	0	
211	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	07/2015	45	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
212	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	07/2015	25	0	
213	4 LANNING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	0	
214	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	07/2015	26	0	
215	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	07/2015	25	0	
216	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	07/2015	25	0	
217	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	07/2015	14	0	
218	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	07/2015	12	0	
219	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	07/2015	12	0	
220	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	08/2015	82	-8.95	
221	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 08/2015	08/2015	88	0	
222	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 08/2015	08/2015	88	0	
223	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 08/2015	08/2015	86	0	
224	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	363.74	242.80	07/2009 -	08/2015	73	85.58	
225	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	08/2015	39	0	
226	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	08/2015	24	0	
227	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	09/2015	84	30.1	
228	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	09/2015	21	0	

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
229	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	0	Project abandoned by contractor
230	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	09/2015	25	0	
231	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 10/2015	10/2015	89	0	
232	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	0	
233	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	11/2015	38	0	
234	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	0	
235	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	11/2015	22	0	
236	BEAWARE-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0	
237	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	0	
238	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	11/2015	14	0	
239	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	12/2015	87	0	
240	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0	
241	AGRA-BYPASS(NS-1/UP-1), NH-2.3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	12/2015	99	33.7	
242	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32	0	
243	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	0	
244	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31	0	
245	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
246	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	12/2015	29	0	
247	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2015	31	0	
248	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28	0	
249	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	0	
250	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	0	
251	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2015	25	0	
252	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	0	
253	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	0	Land acquisition Forest clearance Poor progress by the contractor
254	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	12/2015	15	0	
255	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	0	
256	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	0	
257	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	12/2015	15	0	
258	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2016	01/2016	94	0	
259	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2016	01/2016	93	0	
260	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69	42.25	
261	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	02/2016	21	0	
262	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
263	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	0	Funds constraint of contractor
264	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2016	37	0	
265	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	03/2016	28	0	
266	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29	0	
267	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2016	23	0	
268	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21	0	
269	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	0	
270	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	03/2016	23	0	
271	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	386.10	127.10	09/2007 -	04/2016	103	82.12	
272	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	04/2016	67	0	
273	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	0	
274	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12	0	
275	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	0	
276	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	0	
277	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0	
278	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	06/2016	29	0	
279	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
280	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	06/2016	39	0	
281	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36	0	
282	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	0	
283	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	09/2016	61	0	
284	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	09/2016	35	0	
285	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	11/2016	60	106.5	
286	WADNER-DEVDHAR(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	0	
287	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	0	Land acquisition and Wildlife clearance
288	SIX LANNING OF KRISHNAGIRI-WALA, JHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	12/2016	36	0	
289	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	
290	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2016	39	0	
291	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	12/2016	18	0	
292	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	2.29	
293	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	02/2017	31	0	
294	WALA, JAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	03/2017	16	0	
295	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	0	
296	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	05/2017	45	0	

(June 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
297	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	07/2017	47	0	
298	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2017	34	0	
	Total		72,960.45 -	74,719.94	69,760.64					
	<u>SHIPPING AND PORTS</u>									
299	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	407.32	12/2010 -	01/2016	61	82.72	
	Total		366.39 -	669.46	407.32					
	<u>TELECOMMUNICATIONS</u>									
300	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	66.02	10/2010 08/2015	09/2015	59	0	
	Total		384.00 -	384.00	66.02					
	<u>URBAN DEVELOPMENT</u>									
301	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	06/2015	36	0	Progress of balance work was hampered due to heavy rains and consequent water logging of site and change in decision by the Client department. Scheme of Electrical Services particularly HVAC work was changed after detailed elaboration and award of work was delayed due to General Election in May 2014.
302	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	Finalization of flooring work in 1st year lab building and approval of sample flat for Grade- A qtr from client awaited.
303	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2	0	

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
304	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	0	
305	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30	0	Initial delay of 1 year in availability of site, subsequent delay due to non-uniform flow of funds during 2012-13 & 2013-14, delay in finalization of interior scheme, non-availability of full site till date, non-performance of Interior Agency
306	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	
307	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	Extra time involved in finalization of tender for addressing certain issues of client department.
308	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
309	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,826.56	12/2015 -	08/2016	8	0	
310	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	8,110.85	03/2016 -	12/2016	9	0	
311	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	0	
312	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0	
313	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	0	The work was terminated on 24-07-2014 because of the non performance of the contractor for the first package. However, the tender for balance items of the package I along with package III has been awarded and work started at site.

(June 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		79,439.53	79,439.53	18,952.57					
	Grand Total		556,724.61	672,225.19	405,468.90					

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(June 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 219.08	219.00	141.77	09/2016 -	12/2015
2	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	123.49	01/2017 -	06/2016
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80	6,068.80	272.32	04/2019 -	03/2019
	Total		6,629.70 -	6,706.84	537.58		
	<u>POWER</u>						
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	474.07	10/2016 -	12/2015
	Total		1,315.90 -	1,315.90	474.07		
	Grand Total		7,945.60	8,022.74	1,011.65		

Details of On Schedule Projects w.r.t. Original Schedule

(June 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	764.69	03/2023 03/2023	03/2023
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	803.72	03/2016 -	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	208.60	03/2017 -	03/2017
4	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
5	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	112.65	03/2020 -	03/2020
6	AMLA OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.83	03/2016 -	03/2016
7	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.10	03/2016 -	03/2016
8	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	86.01	03/2018 -	03/2018
9	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	69.97	03/2016 -	03/2016
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	107.20	03/2020 -	03/2020
11	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
12	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2021
13	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	43.93	04/2017 04/2017	04/2017
14	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	158.97	03/2018 -	03/2018
15	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
16	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
17	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
18	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
19	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
20	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	13.38	03/2021 -	03/2021
21	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020
22	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	85.62	03/2021 -	03/2021

							(June 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	GOKUL - [N06000120]	11/2014	267.67 -	267.67	148.02	03/2018 -	03/2018
24	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	37.92	03/2023 -	03/2023
25	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
26	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	29.60	03/2018 -	03/2018
27	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.43	03/2021 -	03/2021
28	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	26.13	03/2021 -	03/2021
29	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	52.16	03/2019 -	03/2019
	Total		27,388.75 -	27,283.77	3,283.89		
	<u>FERTILISERS</u>						
30	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	21.94	11/2016 -	11/2016
	Total		197.79 -	197.79	21.94		
	<u>MINES</u>						
31	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
32	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	7,147.44	05/2016 -	05/2016
33	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	1,357.45	05/2017 05/2017	05/2017
34	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
35	CRU TO ISOMERIZATION (ISOM) - [N16000200]	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016
36	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	5.37	11/2016 -	11/2016
37	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
38	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	130.94	12/2016 -	12/2016
39	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
40	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	67.33	12/2018 -	12/2018

(June 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,066.43	11/2015 -	11/2015
42	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
43	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	98.95	09/2017 -	09/2017
44	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	21.93	07/2016 -	07/2016
45	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	57.16	07/2016 -	07/2016
	Total		29,787.63 -	32,450.56	9,991.05		
	<u>POWER</u>						
46	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,494.00	01/2017 -	01/2017
47	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,246.00	09/2017 -	09/2017
48	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	322.10	05/2016 -	05/2016
49	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
50	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	16.30	04/2017 -	04/2017
51	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	-	04/2018 -	04/2018
52	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
53	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	3,767.88	01/2018 -	01/2018
54	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
55	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
56	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017
57	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
58	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	28.80	05/2018 -	05/2018
59	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - - [N18000198]	5/2015	312.94 -	312.94	-	06/2016 -	06/2016
60	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017
61	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	1.90	11/2017 -	11/2017

							(June 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
63	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	77.70	04/2018 -	04/2018
64	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	111.00	09/2019 -	09/2019
65	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,106.00	02/2019 -	02/2019
66	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,639.00	08/2018 -	08/2018
67	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	70.90	10/2016 -	10/2016
68	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	1.00	05/2016 -	05/2016
69	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	24.80	11/2016 -	11/2016
70	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
71	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	2.00	08/2016 -	08/2016
72	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	63.10	12/2015 -	12/2015
73	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	112.90	08/2016 -	08/2016
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	46.40	06/2016 -	06/2016
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	38.80	06/2016 -	06/2016
76	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	718.00	03/2019 -	03/2019
77	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	651.00	12/2016 -	12/2016
78	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
79	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
80	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	1.00	02/2016 -	02/2016
81	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	1.00	02/2017 -	02/2017
82	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	12.40	02/2017 -	02/2017
83	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	481.30	03/2018 -	03/2018
84	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	6.40	04/2017 -	04/2017
85	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	236.94	04/2016 -	04/2016

							(June 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	265.19	03/2016 -	03/2016
87	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017
88	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,201.00	09/2016 -	09/2016
89	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,869.00	08/2015 -	08/2015
90	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	4,295.00	06/2017 -	06/2017
	Total		149,445.44 -	149,445.44	33,058.71		
	<u>RAILWAYS</u>						
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	688.50	03/2016 -	03/2016
92	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
93	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
94	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	558.46	03/2016 -	03/2016
95	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
96	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	60.84	03/2016 -	03/2016
97	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
98	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
	Total		10,168.70 -	14,503.41	1,481.07		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
99	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
100	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]	1/2014	158.04 -	158.04	2.67	12/2015 -	12/2015
101	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	-	03/2016 -	03/2016
102	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	27.32	01/2016 -	01/2016
103	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
104	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015

(June 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
106	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
107	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016
108	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015
	Total		8,786.28 -	8,786.28	1,759.73		
	<u>STEEL</u>						
109	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	40.89	05/2016 -	05/2016
110	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	141.19	04/2016 -	04/2016
111	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	128.09	07/2016 -	07/2016
112	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	25.02	10/2016 -	10/2016
113	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016
114	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
115	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018
116	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
117	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017
	Total		8,123.02 -	8,268.42	348.96		
	<u>TELECOMMUNICATIONS</u>						
118	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	.00		
	<u>URBAN DEVELOPMENT</u>						
119	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
120	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	-	09/2016 -	09/2016
121	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
122	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017

(June 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
123	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019
124	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
125	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		46,240.70 -	46,240.70	.00		
	Grand Total		295,328.31	302,366.37	49,945.35		

Details of Projects Without Milestones w.r.t. Original Schedule

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	05/2015	0/0
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	03/2015 -	07/2015	0/0
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	06/2017	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- 09/2018	09/2018	0/0
7	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-	0/0
	Total		2,599.56 -			0/0
	<u>FERTILISERS</u>					
8	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 197.79	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
9	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	09/2017	0/0
	Total		1,856.00 -			0/0
	<u>STEEL</u>					
10	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	10/2016	0/0
11	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
12	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
13	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
14	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0

				(June 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		5,913.68			0/0
	<u>PETROLEUM</u>					
15	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20	08/2013 06/2015	06/2015	0/0
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	10/2011 -	06/2015	0/0
17	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	10/2014 10/2015	10/2015	0/0
18	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 11/2015	11/2015	0/0
19	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 12/2015	12/2015	0/0
20	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 04/2015	12/2015	0/0
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	01/2016	0/0
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	01/2016	0/0
23	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	02/2016	0/0
24	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 06/2016	06/2016	0/0
25	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	06/2016	0/0
26	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	01/2017 -	06/2016	0/0
27	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	11/2016 -	11/2016	0/0
28	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	11/2016 -	11/2016	0/0
29	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
30	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
31	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	03/2017 -	03/2017	0/0
32	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
33	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2017	0/0
34	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 12/2017	12/2017	0/0
35	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	02/2016 12/2017	12/2017	0/0
36	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	09/2017 -	12/2017	0/0

				(June 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
37	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 -	01/2013 -	12/2018	0/0
38	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2018	0/0
39	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
40	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 03/2020	03/2020	0/0
41	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
42	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	04/2015 -	-	0/0
43	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
44	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
45	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
46	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-	0/0
	Total		59,298.17 -			0/0
	<u>POWER</u>					
47	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
48	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
49	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	06/2016 -	06/2016	0/0
50	BRCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	05/2014 -	06/2017	0/0
51	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
52	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	10/2017 -	10/2017	0/0
53	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	01/2018 -	01/2018	0/0
54	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	04/2018 -	04/2018	0/0
55	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
56	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		35,650.22 -			0/0
	<u>HEAVY INDUSTRY</u>					

			(June 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
57	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>RAILWAYS</u>					
58	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
59	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
60	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
61	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
62	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
63	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
64	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
65	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
66	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
67	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
68	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
69	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
70	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
71	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
72	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015	0/0
73	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
74	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
75	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
76	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
77	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
78	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
79	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
80	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
81	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
82	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
83	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0
84	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
85	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
86	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	10/2015	0/0
87	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
88	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
89	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
90	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
91	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	03/2004 12/2010	03/2016	0/0
92	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	03/2016	0/0
93	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
94	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
96	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
98	KATAKHAL TO BHAIKABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
99	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
100	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
101	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	03/2007 -	03/2016	0/0
102	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	03/2016 -	03/2016	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
103	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
104	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
105	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	12/2016	0/0
106	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
107	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
108	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
109	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
110	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
111	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
112	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
113	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
114	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
115	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	04/2008 03/2014	06/2017	0/0
116	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
117	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
118	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
119	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
120	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
121	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
122	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
123	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	- -	03/2018	0/0
124	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
125	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
126	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
127	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
128	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
129	AMBARİ FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
130	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
131	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
132	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0
133	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
134	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
135	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
136	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
137	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
138	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
139	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
140	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
141	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	03/1998 -	12/2019	0/0
142	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
143	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
144	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
145	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
146	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
147	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
148	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
149	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
150	VIRAMGAM-BHILD(I)(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
151	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
152	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
153	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
154	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
155	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
156	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
157	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
158	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
159	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
160	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-	0/0
161	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
162	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
163	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
164	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
165	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
166	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
167	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
168	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
169	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
170	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
171	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
172	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
173	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
174	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0

				(June 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
175	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
176	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
177	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
178	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
179	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
180	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
181	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
182	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
183	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
184	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
185	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
186	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
187	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
188	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
189	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
190	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
191	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
192	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
193	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
194	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
195	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
196	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
197	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
198	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0

			(June 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
199	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
200	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
201	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
202	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
203	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
204	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
205	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
206	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
207	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
208	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
209	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
210	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
211	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
212	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
213	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
214	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
215	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
216	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
217	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
218	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
219	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
220	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
221	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
222	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
223	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
224	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
225	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
226	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
227	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
228	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
229	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
230	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
231	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
232	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
233	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
234	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
235	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
236	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
237	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
238	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
239	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
240	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
241	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
242	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
243	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
244	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
245	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
246	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0

			(June 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
247	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
248	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
249	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
250	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
251	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
252	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
253	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
254	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
255	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
256	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
257	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
258	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
259	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
260	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
261	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
262	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
263	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
264	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
265	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
266	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
267	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
268	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
269	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
270	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
271	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
272	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
273	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
274	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
275	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
276	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
277	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
278	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
279	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
280	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
281	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
282	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
283	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
284	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
285	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
286	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
287	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
288	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
289	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
290	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
291	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
292	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
293	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
294	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0

			(June 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
295	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
296	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
297	GUDUR-DURGARA-JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
298	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
299	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
300	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
301	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
302	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
303	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
304	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
305	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
306	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
307	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
308	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
309	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
310	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
311	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
312	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
313	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
314	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
315	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
316	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
317	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
318	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
319	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
320	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
321	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
322	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
323	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
324	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
325	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
326	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
327	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
328	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
329	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
330	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
331	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
332	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
333	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
334	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
335	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
336	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
337	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
338	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0
339	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
340	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
341	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
342	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
343	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
344	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-	0/0
345	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-	0/0
346	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
347	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
348	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
349	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-	0/0
350	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-	0/0
351	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-	0/0
	Total		170,856.70 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
352	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012	0/0
353	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
354	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
355	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013	0/0
356	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
357	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
358	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
359	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015	0/0
360	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	03/2015	0/0
361	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	05/2015	0/0
362	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	05/2015	0/0
363	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	06/2015	0/0
364	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	07/2015	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
365	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	07/2015	0/0
366	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	07/2015	0/0
367	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
368	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	07/2015	0/0
369	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	07/2015	0/0
370	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	05/2014 -	07/2015	0/0
371	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	07/2015	0/0
372	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	07/2014 -	07/2015	0/0
373	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	10/2008 -	08/2015	0/0
374	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	04/2008 08/2015	08/2015	0/0
375	GUWHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	04/2008 08/2015	08/2015	0/0
376	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	06/2008 08/2015	08/2015	0/0
377	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	08/2015	0/0
378	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	05/2012 -	08/2015	0/0
379	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2015	0/0
380	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	09/2008 -	09/2015	0/0
381	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	12/2013 -	09/2015	0/0
382	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	02/2014 -	09/2015	0/0
383	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	08/2013 -	09/2015	0/0
384	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
385	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 10/2015	10/2015	0/0
386	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	02/2014 -	10/2015	0/0
387	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
388	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	11/2015	0/0

			(June 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
389	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	11/2015	0/0
390	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	11/2015	0/0
391	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	11/2015	0/0
392	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	12/2015	0/0
393	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	12/2015	0/0
394	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	12/2015	0/0
395	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	12/2015	0/0
396	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	12/2015	0/0
397	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2015	0/0
398	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	12/2015	0/0
399	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2015	0/0
400	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2015	0/0
401	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2015	0/0
402	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	12/2015	0/0
403	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2015	0/0
404	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2015	0/0
405	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2015	0/0
406	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	12/2015	0/0
407	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2015	0/0
408	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2015	0/0
409	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	12/2015	0/0
410	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	12/2015	0/0
411	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	12/2015	0/0
412	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2016	01/2016	0/0

				(June 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
413	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2016	01/2016	0/0
414	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	01/2016	0/0
415	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	01/2016	0/0
416	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	01/2016	0/0
417	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	02/2016	0/0
418	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	02/2016	0/0
419	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2016	0/0
420	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	03/2016	0/0
421	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	03/2016	0/0
422	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	03/2016	0/0
423	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2016	0/0
424	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	03/2016	0/0
425	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	03/2016	0/0
426	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	03/2016	0/0
427	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	03/2016	0/0
428	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	04/2016	0/0
429	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	04/2016	0/0
430	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	04/2016	0/0
431	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2016	0/0
432	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	04/2016 -	04/2016	0/0
433	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	05/2016	0/0
434	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	06/2016	0/0
435	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
436	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2016	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
437	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00	09/2014	06/2016	0/0
438	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00	03/2013	06/2016	0/0
439	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84	08/2013	08/2016	0/0
440	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-9 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20	02/2014	08/2016	0/0
441	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00	10/2013	09/2016	0/0
442	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60	09/2016	09/2016	0/0
443	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00	11/2011	11/2016	0/0
444	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79	11/2016	11/2016	0/0
445	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45	11/2012	12/2016	0/0
446	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00	09/2013	12/2016	0/0
447	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00	12/2013	12/2016	0/0
448	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00	01/2014	12/2016	0/0
449	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00	09/2013	12/2016	0/0
450	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00	06/2015	12/2016	0/0
451	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00	02/2010	02/2017	0/0
452	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16	07/2014	02/2017	0/0
453	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95	11/2015	03/2017	0/0
454	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00	03/2014	04/2017	0/0
455	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43	08/2013	05/2017	0/0
456	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79	08/2013	07/2017	0/0
457	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00	02/2015	12/2017	0/0
458	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00	06/2005	-	0/0
459	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00	10/2008	-	0/0
460	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00	02/2009	-	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
461	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
462	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
463	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
464	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-	0/0
465	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-	0/0
466	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-	0/0
467	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
468	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
469	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-	0/0
470	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
471	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
472	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
473	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-	0/0
474	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0
475	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-	0/0
476	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
477	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
	Total		88,871.21 -			0/0
	<u>SHIPPING AND PORTS</u>					
478	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	12/2010 -	01/2016	0/0
479	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
480	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	-	0/0
481	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
482	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	-	0/0

			(June 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
483	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-	0/0
484	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	-	0/0
	Total		5,524.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
485	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	07/2015	0/0
486	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 08/2015	09/2015	0/0
	Total		13,718.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
487	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013	0/0
488	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014	0/0
489	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014	0/0
490	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014	0/0
491	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	03/2015	0/0
492	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	04/2015	0/0
493	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
494	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	06/2012 -	06/2015	0/0
495	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	08/2015	0/0
496	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	08/2015	0/0
497	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	10/2015	0/0
498	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 -	11/2015	0/0
499	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
500	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
501	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	05/2016	0/0
502	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	09/2016	0/0

				(June 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
503	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00	03/2016	12/2016	0/0
504	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87	12/2014	12/2016	0/0
505	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57	09/2015	12/2016	0/0
506	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84	03/2017	03/2017	0/0
507	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	08/2014	06/2017	0/0
508	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21	07/2017	07/2017	0/0
509	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79	07/2017	07/2017	0/0
510	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00	03/2018	03/2018	0/0
511	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14	02/2019	02/2019	0/0
512	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10	09/2014	-	0/0
513	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90	-	-	0/0
	Total		113,421.82			0/0
	Grand Total		499,625.61			0/0

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	05/2015
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-
	Total		1,305.89 -		
	<u>COAL</u>				
4	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	03/2015 -	03/2015
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		671.60 -		
	<u>STEEL</u>				
6	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	12/2011 01/2015	03/2015
7	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	10/2009 10/2012	04/2015
8	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	04/2015
	Total		9,488.10 -		
	<u>PETROLEUM</u>				
9	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
10	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	04/2015 -	-
11	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
12	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
13	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
14	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
	Total		16,197.83 -		
	<u>POWER</u>				

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
15	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 10,852.46	10/2013 -	03/2015
16	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	12/2014 -	05/2015
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
18	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
19	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
20	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		14,849.51 -		
	<u>RAILWAYS</u>				
21	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
22	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
23	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
24	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
25	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
26	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTPT,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
27	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
28	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
29	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
30	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
31	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014
32	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014
33	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
34	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015
35	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
36	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
37	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015
38	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
39	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
40	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
41	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015
42	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
43	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	- -	03/2015
44	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	03/2015
45	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	- 03/2010	-
46	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-
47	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
48	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	514.68 -	- -	-
49	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	- -	-
50	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	- -	-
51	NANGALDAM-TALWARA(NL), NR - [220100188]NR, MULTI STATE	03/1981	450.00 -	07/2012 -	-
52	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 -	- -	-
53	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	227.00 997.58	- -	-
54	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
55	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 -	05/2008 -	-
56	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	501.69 501.69	03/2012 -	-
57	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 517.70	- -	-
58	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 -	- -	-
59	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU	09/1995	100.00 -	- -	-
61	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	- -	-
62	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 -	- -	-
63	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
64	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
65	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
66	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09	12/2012	-
67	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00	-	-
68	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21	-	-
69	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64	-	-
70	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65	-	-
71	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95	03/2012	-
72	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91	-	-
73	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92	-	-
74	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19	-	-
75	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03	-	-
76	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23	02/2015	-
77	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78	-	-
78	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62	12/2007	-
79	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92	03/2012	-
80	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56	-	-
81	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00	03/2008	-
82	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90	03/2010	-
83	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19	-	-
84	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00	03/2011	-
85	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00	-	-
86	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00	-	-
87	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62	12/2010	-
88	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19	03/2014	-
89	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23	03/2014	-
90	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73	03/2012	-
91	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38	12/2011	-
92	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74	12/2010	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
93	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
94	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
95	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
96	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
97	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
98	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
99	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
100	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
101	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
102	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
103	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
104	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
105	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
106	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
107	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
108	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
109	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
110	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
111	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
112	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
113	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
114	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
115	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
116	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
117	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
118	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
119	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
120	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-
121	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	- -	-
122	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-
123	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	-
124	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
125	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
126	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
127	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
128	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
129	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
130	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
131	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
132	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
133	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
134	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
135	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
136	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-
137	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-
138	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
139	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
140	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-
141	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-
142	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
143	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-
144	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-
145	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-
146	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU	04/1999	198.68 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
147	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
148	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
149	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
150	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
151	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
152	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
153	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
154	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
155	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
156	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
157	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
158	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
159	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
160	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
161	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
162	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
163	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
164	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
165	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
166	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
167	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
168	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
169	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
170	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
171	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
172	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
173	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
174	HANSIDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
175	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
176	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
177	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
178	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
179	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
180	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
181	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
182	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
183	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
184	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
185	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
186	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
187	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
188	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
189	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
190	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
191	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
192	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
193	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
194	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
195	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
196	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
197	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00	-	-
198	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00	-	-
199	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00	-	-
200	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88	-	-
201	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91	-	-
202	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	-	-
203	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00	-	-
204	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74	-	-
205	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34	-	-
206	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05	-	-
207	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	-	-
208	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00	-	-
209	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60	-	-
210	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48	-	-
211	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49	-	-
212	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00	-	-
213	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83	-	-
214	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54	-	-
215	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96	-	-
216	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00	-	-
217	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00	-	-
218	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00	-	-
219	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	-	-
220	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14	-	-
221	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00	-	-
222	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	-	-
223	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00	-	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
224	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
225	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
226	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
227	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
228	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
229	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
230	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
231	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
232	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
233	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	- -	-
234	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	-
235	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA	03/2006	201.00 -	- -	-
236	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
237	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
238	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
239	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
240	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
241	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
242	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
243	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
244	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
245	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
246	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
247	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-
	Total		109,613.40 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
248	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
249	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56	02/2012	06/2013
250	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50	08/2013	08/2013
251	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00	09/2013	09/2013
252	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00	11/2013	11/2013
253	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, MEGHALAYA	02/2011	226.00	02/2014	02/2014
254	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI, BIHAR	12/2011	325.00	05/2014	05/2014
255	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00	-	07/2014
256	PANIPAT-ROHTAK - [N24000151]NHAI, HARYANA	04/2011	807.00	10/2014	10/2014
257	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03	10/2008	01/2015
258	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47	09/2007	03/2015
259	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00	06/2008	05/2015
260	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07	01/2013	05/2015
261	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00	06/2005	-
262	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00	10/2008	-
263	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00	02/2009	-
264	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81	04/2009	-
265	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64	11/2008	-
266	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04	11/2008	-
267	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00	04/2009	-
268	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00	06/2008	-
269	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80	06/2008	-
270	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00	07/2008	-
271	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00	06/2008	-
272	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72	06/2008	-
273	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00	02/2010	-
274	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00	-	-
275	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55	03/2013	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
276	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
277	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
278	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-
279	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
280	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
281	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
282	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		17,180.57 -		
	<u>SHIPPING AND PORTS</u>				
283	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
284	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	-
285	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
286	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	-
287	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-
288	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	-
	Total		5,158.07 -		
	<u>URBAN DEVELOPMENT</u>				
289	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013
290	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014
291	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
292	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
293	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	03/2015
294	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	04/2015
295	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015
296	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
297	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
298	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		13,000.59 -		
	Grand Total		187,465.56		

Details of Projects Without Original Date of Commissioning

(June 2015)

(June 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>CIVIL AVIATION</u>								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	17.82	- 09/2018	09/2018	0(R3)	0/0
	Total		314.61	314.61	17.82				0/0
	<u>RAILWAYS</u>								
2	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40	203.40	153.29	- -	09/2015	-	0/0
3	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71	744.71	576.86	- -	03/2016	-	0/1
4	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17	914.98	846.18	- -	03/2016	-	0/0
5	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81	155.81	18.25	- -	12/2016	-	0/0
6	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
7	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
8	NEW B.G. LINE FROM TETELIA TO BYRNHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
9	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
10	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
11	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
12	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
13	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00	886.65	-	- -	03/2018	-	0/0
14	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
15	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
16	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
17	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0

(June 2015)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
19	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
20	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
21	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
22	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
23	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
24	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
25	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
26	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
27	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
28	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
	Total		18,290.57 -	29,584.45	5,970.54				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
29	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	808.70	- -	07/2015	-	1/1
30	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	12/2015	-	2/3
	Total		1,124.00 -	1,124.00	2,081.70				3/4
	Grand Total		19,729.18	31,023.06	8,070.06				3/5

List of ongoing projects having cost overrun w.r.t. to revised schedule

(June 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		553.21 -	632.63			
	<u>COAL</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	07/2015	76.47
4	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		2,660.90 -	4,261.99			
	<u>HEAVY INDUSTRY</u>						
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
7	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						
8	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
9	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
10	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	10/2014 -	10/2015	0.00

(June 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72
	Total		15,877.97 -	18,583.61			
	<u>POWER</u>						
12	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
14	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
15	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
16	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31
	Total		17,399.92 -	34,290.63			
	<u>RAILWAYS</u>						
17	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
18	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
19	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
20	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
21	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
22	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
23	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
24	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
25	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
26	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
27	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
28	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67

(June 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
29	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
30	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
31	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
32	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
33	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
34	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
35	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
36	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
37	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
38	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
39	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
40	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
41	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
42	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
43	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
44	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
45	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
46	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
47	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
48	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
49	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
50	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
51	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48

(June 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
52	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78 -	- -	-	902.01
53	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85 -	03/2005 12/2008	12/2019	2,019.62
54	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00 -	03/2012 -	12/2012	210.19
55	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25 -	- -	-	324.33
56	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64 -	- 09/2009	-	293.06
57	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00 -	02/2009 02/2009	08/2014	73.33
58	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75 -	03/2011 -	03/2019	803.12
59	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41 -	03/2012 -	-	5.72
60	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00 -	03/2009 -	10/2015	156.57
61	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00 -	10/2007 -	12/2015	367.76
62	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90 -	- -	03/2017	160.32
63	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00 -	- -	-	57.20
64	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16 -	- -	03/2017	186.92
65	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29 -	02/2015 -	-	346.59
66	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00 -	- -	10/2014	76.98
67	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00 -	03/2009 03/2009	08/2014	106.88
68	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80 -	- -	-	0.00
69	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93 -	12/2007 03/2010	-	112.22
70	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88 -	03/2012 -	-	43.54
71	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59 -	- -	-	109.11
72	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00 -	02/2006 -	03/2016	6.99
73	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11 -	03/2008 06/2008	-	50.35
74	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54 -	03/2010 -	-	18.66
75	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00 -	03/2010 -	12/2015	16.41

(June 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
77	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
78	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
79	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
80	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
81	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
82	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
83	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
84	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
85	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
86	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
87	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
88	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
89	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
90	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
91	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
92	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
93	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
94	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
95	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
96	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
97	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41

(June 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
99	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
100	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
101	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
102	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
103	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
104	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
105	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
106	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
107	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
108	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
109	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
110	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
111	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
112	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
113	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
114	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
115	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
116	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
117	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
118	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
119	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78

(June 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
120	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	-	-	180.17
121	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	-	-	91.71
122	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	-	-	55.74
123	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	-	-	28.14
124	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	-	03/2019	154.33
125	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
126	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	-	03/2018	251.85
127	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	-	03/2020	5.00
128	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	-	03/2018	110.44
129	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	-	03/2018	1.86
130	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	-	-	109.04
131	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	-	-	173.71
132	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	-	03/2015	285.12
133	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	-	-	16.29
134	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	-	03/2020	30.00
135	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	-	03/2018	180.56
136	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	-	03/2017	63.25
137	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	-	03/2018	162.68
138	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	-	03/2018	216.06
139	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	-	03/2018	45.17
140	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	-	03/2019	47.95
141	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
142	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	-	-	33.02

(June 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
143	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	499.30 -	2,501.05	- -	-	400.91
144	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
145	PEN ROHA DOUBLING - [N22000254	04/2007	98.74 -	203.00	- -	03/2015	105.59
146	PANVEL PEN DOUBLING - [N22000255	04/2006	96.16 -	260.16	- -	01/2015	170.55
147	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
148	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97
149	BAGALKOT-KUDACHI NL - [N22000258	04/2010	377.93 -	986.30	- -	-	160.97
150	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263	04/2008	184.26 -	2,000.00	- -	-	985.42
151	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	576.18	- -	-	100.76
152	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
153	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	- -	-	24.09
154	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	- -	-	57.65
155	SHIMOGA-HARIHAR NL - [N22000278	04/2011	562.74 -	832.47	- -	-	47.93
156	RAYADURGA-TUMKUR NL - [N22000279	04/2007	970.34 -	1,743.00	- -	-	79.63
157	WHITE FIELD-KOLAR NL - [N22000280	04/2011	341.05 -	348.85	- -	-	2.29
158	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	337.49 -	337.50	- -	-	0.00
159	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	329.97	- -	-	50.10
160	TORANAGALLU-RANJITPURA DL - [N22000298	04/2011	146.75 -	167.50	- -	-	14.14
161	GADAG-WADI NL - [N22000299	04/2013	1,117.00 -	1,922.00	- -	-	72.07
162	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	04/2013	327.25 -	367.77	- -	-	12.38
163	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
164	MM FROM BURAMARA-CHAKULIA - [N22000305	04/2008	466.48 -	800.00	01/1999 -	-	71.50
165	MM FROM PANSKURA-GHATAL NL - [N22000309	04/2011	276.69 -	426.00	01/1999 -	-	53.96
166	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70

(June 2015)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
167	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
168	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
169	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
170	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
171	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		83,122.43 -	204,587.68			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
172	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	09/2015	30.10
173	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
174	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
175	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
176	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	04/2016	82.12
177	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	08/2015	85.58
178	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29
179	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	12/2015	33.70
180	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2016	106.50
	Total		2,929.01 -	5,012.57			
	<u>SHIPPING AND PORTS</u>						
181	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
182	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
183	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,623.67 -	2,433.22			

(June 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
184	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
185	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		138,083.72	295,560.55			

List of Delayed Projects w.r.t. Latest Schedule

(June 2015)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	20,713.00	12/2008 -	10/2015	82	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	6,853.00	12/2015 -	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,669.00	12/2016 -	05/2018	17	-
	Total		36,950.00 -	41,049.00	32,235.00				
	<u>CIVIL AVIATION</u>								
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT (MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00 489.00	489.00	449.63	03/2015 -	07/2015	4	-
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	244.10	0.04	03/2015 -	09/2015	6	-
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	355.88	01/2011 06/2016	06/2017	77	12
	Total		979.06 -	1,042.56	805.55				
	<u>COAL</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,583.77	3,213.77	06/2009 03/2013	07/2015	73	28
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,277.83	03/2012 05/2014	07/2015	40	14
9	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	151.74	10/2014 -	08/2015	10	-
10	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.58	03/2013 09/2012	09/2015	30	36
11	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,844.83	03/2014 -	03/2016	24	-
12	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,664.03	03/2014 -	03/2016	24	-
13	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	473.48	03/2013 -	03/2016	36	-
14	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH	06/2011	746.04 535.10	535.10	379.04	03/2015 -	03/2016	12	-
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	76.55	07/2012 -	03/2016	44	-
16	NIGAHAI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	259.40	21.42	03/2012 -	03/2016	48	-
17	CHURCHA ROUG (1.35MTY) - [N06000046]SECL, CHHATISGARH	06/2008	462.35 -	462.35	298.60	03/2014 -	03/2016	24	-

(June 2015)

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82	153.82	57.62	03/2014	03/2016	24	-
19	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97	418.97	326.28	03/2012	03/2016	48	-
20	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19	181.19	36.60	03/2012	03/2016	48	-
21	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51	163.51	35.92	03/2011	03/2016	60	-
22	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98	210.98	-	03/2013	03/2016	36	-
23	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68	264.68	143.74	03/2012	03/2016	48	-
24	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78	209.78	77.47	03/2015	04/2016	13	-
25	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45	289.45	89.89	05/2014	04/2016	23	-
26	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82	269.82	34.51	04/2014	04/2016	24	-
27	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96	302.96	147.57	03/2010	03/2017	84	-
28	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL, JHARKHAND	12/2007	341.63	341.63	124.92	03/2011	03/2017	72	-
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18	287.18	225.39	03/2011	03/2017	72	-
30	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77	457.77	175.03	03/2013	03/2017	48	-
31	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08	172.08	148.45	03/2010	03/2017	84	-
32	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63	453.63	99.63	12/2012	03/2017	51	-
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28	207.28	191.26	03/2012	03/2017	60	-
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53	479.63	173.03	03/2013	03/2017	48	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87	179.87	81.52	03/2012	03/2017	60	-
36	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	65.96	03/2014	03/2017	36	-
37	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2017	21	-
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33	417.33	11.68	07/2016	03/2017	8	-
39	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03	249.03	71.72	03/2012	03/2018	72	-
40	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50	321.50	206.52	03/2014	03/2018	48	-
41	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29	242.29	0.03	03/2015	03/2018	36	-
42	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36	-
43	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56	258.56	81.40	03/2016	03/2018	24	-

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
44	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76	162.76	2.48	03/2015	03/2019	48	-
45	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27	1,230.27	42.39	04/2015	04/2019	48	-
46	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	-
47	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60	-
48	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72	-
49	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72	-
	Total		25,170.67	29,178.81	18,121.59				
	<u>STEEL</u>								
50	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00	572.00	463.35	04/2013 09/2014	06/2015	26	9
51	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00	450.00	388.34	09/2009 05/2012	07/2015	70	38
52	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48	160.48	132.35	09/2014	07/2015	10	-
53	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00	677.00	522.58	09/2013	07/2015	22	-
54	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00	6,325.00	5,164.71	12/2011	08/2015	44	-
55	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55	898.55	387.59	05/2013 01/2015	08/2015	27	7
56	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09	237.09	192.84	12/2014	09/2015	9	-
57	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65	332.65	199.46	08/2014	11/2015	15	-
58	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33	187.33	158.95	10/2013	12/2015	26	-
59	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05	313.05	249.80	06/2015	12/2015	6	-
60	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00	17,265.00	14,537.66	03/2013	03/2016	36	-
61	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73	877.73	260.12	07/2015	03/2016	8	-
62	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16	404.16	152.00	07/2015	03/2017	20	-
	Total		28,730.04	28,700.04	22,809.75				
	<u>PETROCHEMICALS</u>								

(June 2015)

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
63	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,736.89	04/2012 12/2013	09/2015	41	21
	Total		5,460.61 -	9,833.52	8,736.89				
	<u>PETROLEUM</u>								
64	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 06/2012	06/2015	110	36
65	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	2,915.00	1,345.03	12/2012 -	06/2015	30	-
66	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL, ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,079.05	10/2011 -	06/2015	44	-
67	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC, MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,770.24	05/2015 05/2015	07/2015	2	2
68	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,171.43	12/2014 -	08/2015	8	-
69	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39	6
70	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	158.12	12/2014 -	09/2015	9	-
71	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,273.28	11/2012 11/2013	10/2015	35	23
72	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL, ODISHA	07/2009	199.75 239.73	239.73	190.20	07/2013 -	10/2015	27	-
73	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,234.16	08/2015 -	12/2015	4	-
74	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	885.75	05/2013 06/2014	12/2015	31	18
75	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	316.02	08/2015 -	12/2015	4	-
76	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	449.51	04/2015 04/2015	12/2015	8	8
77	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	89.83	05/2015 -	12/2015	7	-
78	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	970.98	10/2011 -	01/2016	51	-
79	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,404.06	01/2012 -	01/2016	48	-
80	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,146.48	09/2012 -	03/2016	42	-
81	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	280.86	06/2011 03/2012	03/2016	57	48
82	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	12

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
83	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	37.49	02/2016 -	05/2016	3	-
84	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	416.70	08/2015 -	06/2016	10	-
85	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	273.36	03/2015 11/2015	06/2016	15	7
86	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,777.84	03/2013 03/2016	03/2017	48	12
87	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2017	12	12
88	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	-
89	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	96.08	09/2017 -	12/2017	3	-
90	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 -	3,957.00	5.70	01/2013 -	12/2018	71	-
91	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	-
92	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 -	06/2018	53	-
	Total		71,545.23 -	81,333.32	52,866.15				
	POWER								
93	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,727.47	11/2012 -	07/2015	32	-
94	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	198.64	03/2014 -	07/2015	16	-
95	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	914.86	07/2013 -	08/2015	25	-
96	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,825.87	03/2014 06/2015	08/2015	17	2
97	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	811.38	03/2015 -	09/2015	6	-
98	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,854.54	03/2013 06/2015	09/2015	30	3
99	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,750.90	12/2013 -	09/2015	21	-
100	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	135.50	01/2013 -	09/2015	32	-

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
101	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,941.66	08/2014 -	09/2015	13	-
102	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	520.00	02/2014 -	09/2015	19	-
103	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,510.47	10/2014 -	09/2015	11	-
104	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,088.18	11/2014 -	09/2015	10	-
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	190.22	04/2015 -	09/2015	5	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	485.72	07/2013 05/2015	11/2015	28	6
107	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	1,000.61	12/2007 12/2009	12/2015	96	72
108	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,485.26	11/2013 -	12/2015	25	-
109	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	454.91	11/2013 -	12/2015	25	-
110	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	282.57	08/2014 06/2015	12/2015	16	6
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	521.62	11/2014 -	12/2015	13	-
112	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	142.20	06/2015 -	12/2015	6	-
113	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	765.33	06/2015 -	12/2015	6	-
114	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,893.05	09/2008 03/2012	03/2016	90	48
115	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	520.99	09/2010 06/2013	03/2016	66	33
116	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,007.62	08/2013 -	03/2016	31	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	468.06	11/2011 -	03/2016	52	-
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	330.37	02/2012 -	03/2016	49	-
119	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,086.48	10/2012 -	03/2016	41	-

(June 2015)

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
120	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,005.30	08/2013 -	03/2016	31	-
121	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,498.75	01/2015 -	03/2016	14	-
122	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,156.70	12/2012 -	03/2016	39	-
123	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,052.09	08/2012 -	03/2016	43	-
124	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	735.24	11/2012 -	03/2016	40	-
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,313.72	04/2013 -	03/2016	35	-
126	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,713.45	05/2014 -	03/2016	22	-
127	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,199.43	07/2014 -	03/2016	20	-
128	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,214.43	08/2014 12/2015	03/2016	19	3
129	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,149.72	01/2015 -	03/2016	14	-
130	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,478.09	06/2015 -	03/2016	9	-
131	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,397.31	10/2014 -	03/2016	17	-
132	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	771.05	12/2015 -	03/2016	3	-
133	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,916.06	01/2013 -	03/2016	38	-
134	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,787.90	09/2009 -	06/2016	81	-
135	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,813.96	09/2014 -	06/2016	21	-

(June 2015)

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
136	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	75.53	09/2014 -	06/2016	21	-
137	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NNEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	843.49	07/2006 12/2015	10/2016	123	10
138	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,996.61	01/2016 -	11/2016	10	-
139	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,110.83	11/2012 -	12/2016	49	-
140	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,287.00	09/2011 -	03/2017	66	-
141	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,753.79	05/2014 -	06/2017	37	-
142	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,974.00	11/2016 -	08/2017	9	-
143	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	27.73	02/2014 -	09/2017	43	-
144	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9	-
145	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,899.00	01/2011 10/2014	03/2018	86	41
146	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,292.48	07/2010 02/2016	05/2018	94	27
147	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,109.77	09/2009 -	12/2018	111	-
148	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,480.00	03/2013 -	12/2018	69	-
	Total		139,935.70 -	161,939.18	114,498.05				
	HEAVY INDUSTRY								
149	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	.00				
	RAILWAYS								
150	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66	51
151	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	30	-
152	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	-
153	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	79	34
154	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	-
155	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	-

(June 2015)

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
156	PATNA GANGA BRIDGE (NL), ECR - [220100308] ECR, BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	36
157	BHOPAL BINA 3D LINE DOUBLING - [N22000077] RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	-
158	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164] MRT, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 12/2010	03/2016	144	63
159	GOELKERA-MANOHARPUR, (LD) (SER) - [N22000045] SER, JHARKHAND	03/1997	261.70 -	280.00	177.01	02/2006 -	03/2016	121	-
160	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094] RE, UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109] RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.65	03/2014 -	03/2016	24	-
162	KATAKHAL TO BHAIRABI - [N22000126] NFR, ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
163	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127] NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
164	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164] SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
165	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194] NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
166	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108] RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	-
167	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162] SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
168	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214] MRT, MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	-
169	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201] NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	39
170	KATIHAR - JOGBANI (GC) (NEFR) - [220100247] NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
171	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266] NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
172	AGARTALA SABROOM, NL, NEFR - [N22000099] NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
173	BHAIRABI SAIRONG, NL, NEFR - [N22000100] NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
174	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135] MRT, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	-
175	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133] NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-
176	JIRIBAM TO IMPHAL (TUPI) (NL) (NEFR) - [220100288] NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
177	GONDIA-JABALPUR (GC), (SECR) - [220100186] SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-

(June 2015)

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
178	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
179	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
180	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
	Total		27,333.74 -	79,079.96	37,976.32				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
181	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	06/2015	30	-
182	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	07/2015	62	-
183	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	07/2015	45	-
184	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	07/2015	25	-
185	4 LANNING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	-
186	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	07/2015	26	-
187	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	07/2015	25	-
188	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	07/2015	25	-
189	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	07/2015	14	-
190	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	07/2015	12	-
191	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	07/2015	12	-
192	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	08/2015	82	-
193	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	363.74	242.80	07/2009 -	08/2015	73	-
194	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	08/2015	39	-
195	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	08/2015	24	-
196	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	09/2015	84	-
197	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	09/2015	21	-
198	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	-

(June 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
199	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	09/2015	25	-
200	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	-
201	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	11/2015	38	-
202	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	-
203	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	11/2015	22	-
204	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	-
205	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	-
206	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	11/2015	14	-
207	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	12/2015	87	-
208	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	-
209	AGRA-BYPASS(NS-1/UP-1), NH-2, 3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	12/2015	99	-
210	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32	-
211	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	-
212	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31	-
213	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29	-
214	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	12/2015	29	-
215	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2015	31	-
216	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28	-
217	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	-
218	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	-
219	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2015	25	-
220	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	-
221	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	-
222	6-LANNING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	12/2015	15	-

(June 2015)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
223	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36	291.36	141.30	01/2014	12/2015	23	-
224	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69	942.69	286.80	06/2014	12/2015	18	-
225	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51	333.51	271.60	09/2014	12/2015	15	-
226	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00	1,535.00	2,188.00	05/2014	02/2016	21	-
227	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00	1,232.00	590.90	08/2015	02/2016	6	-
228	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00	617.00	156.90	08/2012	03/2016	43	-
229	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30	671.30	632.70	02/2013	03/2016	37	-
230	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00	650.00	1,178.00	11/2013	03/2016	28	-
231	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00	571.00	-	10/2013	03/2016	29	-
232	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09	375.09	408.10	04/2014	03/2016	23	-
233	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00	1,047.00	295.70	06/2014	03/2016	21	-
234	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	484.19	285.50	10/2014	03/2016	17	-
235	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00	624.00	441.80	04/2014	03/2016	23	-
236	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00	386.10	127.10	09/2007	04/2016	103	-
237	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45	232.45	317.50	09/2010	04/2016	67	-
238	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00	593.00	761.30	07/2013	04/2016	33	-
239	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22	1,928.22	647.40	04/2015	04/2016	12	-
240	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00	2,159.00	622.70	06/2015	05/2016	11	-
241	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37	353.37	446.20	10/2011	06/2016	56	-
242	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00	1,987.00	1,170.00	07/2015	06/2016	11	-
243	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00	536.00	759.90	01/2014	06/2016	29	-
244	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	1,410.00	929.60	09/2014	06/2016	21	-
245	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00	754.00	593.50	03/2013	06/2016	39	-
246	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84	1,078.84	1,922.00	08/2013	08/2016	36	-

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
247	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20	1,348.20	588.40	02/2014	08/2016	30	-
248	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75	1,693.75	2,762.00	08/2011	09/2016	61	-
249	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00	478.00	328.70	10/2013	09/2016	35	-
250	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00	2,288.00	3,466.00	11/2011	11/2016	60	-
251	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45	193.45	66.11	11/2012	12/2016	49	-
252	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00	359.00	39.55	09/2013	12/2016	39	-
253	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00	1,250.00	1,374.00	12/2013	12/2016	36	-
254	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00	586.00	237.60	01/2014	12/2016	35	-
255	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00	1,046.00	403.00	09/2013	12/2016	39	-
256	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00	1,479.00	368.60	06/2015	12/2016	18	-
257	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00	281.31	180.10	02/2010	02/2017	84	-
258	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16	702.16	726.40	07/2014	02/2017	31	-
259	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95	1,287.95	540.40	11/2015	03/2017	16	-
260	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00	2,848.00	1,138.00	03/2014	04/2017	37	-
261	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43	580.43	450.70	08/2013	05/2017	45	-
262	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79	998.79	1,610.00	08/2013	07/2017	47	-
263	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00	867.00	598.60	02/2015	12/2017	34	-
	Total		71,530.72	73,198.26	67,839.54				
	<u>SHIPPING AND PORTS</u>								
264	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39	669.46	407.32	12/2010	01/2016	61	-
	Total		366.39	669.46	407.32				
	<u>TELECOMMUNICATIONS</u>								
265	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00	384.00	66.02	10/2010	09/2015	59	1

(June 2015)

(June 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		384.00 -	384.00	66.02				
	<u>URBAN DEVELOPMENT</u>								
266	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	06/2015	36	-
267	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	-
268	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2	-
269	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	-
270	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30	-
271	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	-
272	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
273	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	-
274	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,826.56	12/2015 -	08/2016	8	-
275	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	8,110.85	03/2016 -	12/2016	9	-
276	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	-
277	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	-
278	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	-
	Total		79,439.53 -	79,439.53	18,952.57				
	Grand Total		489,543.69	589,674.94	375,314.75				

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 219.08	219.00	141.77	09/2016 -	12/2015
2	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	123.49	01/2017 -	06/2016
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80	6,068.80	272.32	04/2019 -	03/2019
	Total		6,629.70 -	6,706.84	537.58		
	<u>POWER</u>						
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) [N18000154]	10/2013	1,315.90 -	1,315.90	474.07	10/2016 -	12/2015
	Total		1,315.90 -	1,315.90	474.07		
	Grand Total		7,945.60	8,022.74	1,011.65		

List of Projects on schedule w.r.t. Latest Schedule

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N06000044]	9/2003	3,492.00 -	5,677.00	5,006.93	09/2010 09/2016	09/2016
	Total		3,492.00 -	5,677.00	5,006.93		
	<u>COAL</u>						
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	764.69	03/2023 03/2023	03/2023
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	803.72	03/2016 -	03/2016
4	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.83	03/2016 -	03/2016
6	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	86.01	03/2018 -	03/2018
7	MURADIDH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	9.97	04/2014 03/2016	03/2016
8	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	107.20	03/2020 -	03/2020
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2021
10	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020
11	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	13.38	03/2021 -	03/2021
12	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
13	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
14	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
15	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
16	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	158.97	03/2018 -	03/2018
18	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	43.93	04/2017 04/2017	04/2017

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	52.16	03/2019 -	03/2019
20	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	26.13	03/2021 -	03/2021
21	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.43	03/2021 -	03/2021
22	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	29.60	03/2018 -	03/2018
23	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
24	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	37.92	03/2023 -	03/2023
25	GOKUL - [N06000120]	11/2014	267.67 -	267.67	148.02	03/2018 -	03/2018
26	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	85.62	03/2021 -	03/2021
27	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
28	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	69.97	03/2016 -	03/2016
29	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	965.20	12/2015 04/2018	04/2018
30	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.10	03/2016 -	03/2016
31	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	112.65	03/2020 -	03/2020
32	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	208.60	03/2017 -	03/2017
	Total		33,635.74 -	33,530.76	4,259.06		
	<u>FERTILISERS</u>						
33	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	21.94	11/2016 -	11/2016
	Total		197.79 -	197.79	21.94		
	<u>MINES</u>						
34	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]	7/2008	288.04 288.04	253.66	225.72	08/2012 06/2015	06/2015
37	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]	6/2010	2,523.00 -	2,523.00	1,436.51	01/2014 12/2015	12/2015
38	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]	11/2010	331.20 -	269.10	190.04	08/2013 06/2015	06/2015
39	MEHESANA REDEVELOPMENT PROJECT - [N16000121]	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017
40	CONSTRUCTION OF 6 ETPS - [N16000117]	3/2009	317.64 -	240.95	114.88	09/2012 12/2015	12/2015
41	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]	1/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016
42	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,204.41	03/2015 05/2016	05/2016
43	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
44	CRU TO ISOMERIZATION (ISOM) - [N16000200]	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016
45	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	5.37	11/2016 -	11/2016
46	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	47.07	05/2019 03/2020	03/2020
47	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
48	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	130.94	12/2016 -	12/2016
49	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
50	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015
51	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	335.37	02/2016 12/2017	12/2017
52	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	57.16	07/2016 -	07/2016
53	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	237.49	10/2014 10/2016	10/2016
54	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	481.49	11/2015 11/2016	11/2016
55	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,066.43	11/2015 -	11/2015
56	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	7,147.44	05/2016 -	05/2016
57	IOR OF B-173A FIELD - [N16000140]	1/2012	352.49 -	352.49	127.55	03/2014 05/2016	05/2016
58	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	541.46	05/2014 05/2016	05/2016

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	1,357.45	05/2017 05/2017	05/2017
60	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	699.72	11/2015 07/2016	07/2016
61	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	67.33	12/2018 -	12/2018
62	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	330.19	10/2014 10/2015	10/2015
63	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	21.93	07/2016 -	07/2016
64	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	98.95	09/2017 -	09/2017
65	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
66	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	57.94	01/2016 07/2017	07/2017
67	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
	Total		58,811.35 -	63,284.72	17,569.75		
	<u>POWER</u>						
68	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	3,892.98	12/2009 03/2017	03/2017
69	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,745.08	647.32	06/2013 12/2019	12/2019
70	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,869.00	08/2015 -	08/2015
71	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	4,295.00	06/2017 -	06/2017
72	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,201.00	09/2016 -	09/2016
73	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,494.00	01/2017 -	01/2017
74	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	265.19	03/2016 -	03/2016
76	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
77	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	2.00	08/2016 -	08/2016
78	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	63.10	12/2015 -	12/2015

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	112.90	08/2016 -	08/2016
80	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	46.40	06/2016 -	06/2016
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	38.80	06/2016 -	06/2016
82	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
83	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	236.94	04/2016 -	04/2016
84	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	322.10	05/2016 -	05/2016
85	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
86	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	77.70	04/2018 -	04/2018
87	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	111.00	09/2019 -	09/2019
88	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,106.00	02/2019 -	02/2019
89	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,639.00	08/2018 -	08/2018
90	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	718.00	03/2019 -	03/2019
91	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	651.00	12/2016 -	12/2016
92	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
93	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
94	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
95	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	3,767.88	01/2018 -	01/2018
96	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
97	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
98	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
100	WARDHA-HYDERABAD 765 KV LINK - [N18000183	1/2015	3,662.02 -	3,662.02	28.80	05/2018 -	05/2018
101	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017
102	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181	1/2015	871.62 -	871.62	1.90	11/2017 -	11/2017
103	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198	5/2015	312.94 -	312.94	-	06/2016 -	06/2016
104	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197	4/2015	1,479.30 -	1,479.30	16.30	04/2017 -	04/2017
105	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196	4/2015	3,705.61 -	3,705.61	-	04/2018 -	04/2018
106	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171	2/2014	196.58 -	196.58	1.00	02/2016 -	02/2016
107	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170	8/2014	188.75 -	188.75	1.00	02/2017 -	02/2017
108	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169	8/2014	288.49 -	288.49	12.40	02/2017 -	02/2017
109	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168	6/2014	5,151.37 -	5,151.37	481.30	03/2018 -	03/2018
110	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167	6/2014	400.47 -	400.47	6.40	04/2017 -	04/2017
111	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166	2/2014	378.71 -	378.71	70.90	10/2016 -	10/2016
112	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165	3/2014	155.57 -	155.57	1.00	05/2016 -	05/2016
113	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 -	522.29	24.80	11/2016 -	11/2016
114	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	3/2013	11,638.55 -	11,638.55	3,246.00	09/2017 -	09/2017
	Total		154,433.92 -	159,666.86	37,599.01		
	RAILWAYS						
115	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
116	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	4/2010	2,913.51 -	2,619.02	558.46	03/2016 -	03/2016
117	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
118	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	4/2010	3,951.98 -	4,259.48	688.50	03/2016 -	03/2016
119	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019
120	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
121	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	816.55	60.84	03/2016 -	03/2016
122	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
123	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
124	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
125	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
	Total		16,643.70 -	27,027.41	4,355.84		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
126	GUWAHATI TO NALBARI (AS-4) - [N24000038	12/2003	175.96 -	175.96	182.50	04/2008 08/2015	08/2015
127	SONAPUR TO GUWAHATI (AS-3) - [N24000044	12/2003	245.00 -	245.00	491.20	03/2008 01/2016	01/2016
128	GUWAHATI TO NALBARI (AS-5) - [N24000046	12/2003	198.16 -	198.16	242.40	04/2008 08/2015	08/2015
129	NALBARI T BIJUNI (AS-7) - [N24000048	12/2003	208.00 -	208.00	290.60	04/2008 01/2016	01/2016
130	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
131	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016
132	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
133	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
134	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
135	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
136	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
137	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	258.40	04/2010 01/2016	01/2016
138	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	160.00	197.60	05/2008 10/2015	10/2015
139	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240	3/2014	240.10 -	240.10	-	03/2016 -	03/2016
140	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239	1/2014	368.15 -	368.15	27.32	01/2016 -	01/2016
141	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238	1/2014	158.04 -	158.04	2.67	12/2015 -	12/2015
142	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	258.40	06/2008 08/2015	08/2015
	Total		10,216.01 -	10,307.96	3,680.83		
	<u>STEEL</u>						
143	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	40.89	05/2016 -	05/2016
144	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084	6/2014	708.91 -	708.91	141.19	04/2016 -	04/2016
145	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	15,525.00	7,257.18	05/2015 12/2016	12/2016
146	3RD CONVERTER AND 4TH CASTER - [N12000088	7/2011	974.76 -	974.76	128.09	07/2016 -	07/2016
147	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	25.02	10/2016 -	10/2016
148	TURBO BLOWER - 5 - [N12000092	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016
149	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
150	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094	4/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018
151	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
152	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096	5/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017
	Total		23,648.02 -	23,793.42	7,606.14		
	<u>TELECOMMUNICATIONS</u>						
153	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015

(June 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		13,334.00 -	13,334.00	.00		
	<u>URBAN DEVELOPMENT</u>						
154	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
155	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	-	09/2016 -	09/2016
156	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
157	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
158	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019
159	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
160	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		46,240.70 -	46,240.70	.00		
	Grand Total		362,509.23	384,916.62	80,099.50		

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	10/2015	13171	82
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	05/2018	12320	17

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	06/2017	309.46	77
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	AAI	10/2012	03/2015	09/2015	217.6	6

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	07/2015	2030.78	73
8	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12
9	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	30
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	07/2015	4904.54	40
11	CHURCHA ROUG (1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	24
12	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
13	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
14	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
15	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
16	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2016	259.4	48
17	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
18	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
19	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
20	RKP OCP PHASE-I	SCCL	03/2010	03/2015	04/2016	209.78	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
21	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2016	418.97	48
22	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
23	JAGANNATHPOR OC	SECL	09/2008	03/2015	03/2020	152.43	60
24	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
25	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
26	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
27	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
28	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
29	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2019	162.76	48
30	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
31	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
32	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
33	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2016	210.98	36
34	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
35	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
36	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
37	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	04/2016	269.82	24
38	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	04/2016	289.45	23
39	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	08/2015	364.75	10
40	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
41	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
42	BAROUD OC EXPANSION (RCE) - 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
43	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23
45	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
46	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	706.4	44
47	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
48	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
49	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
50	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24
51	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	09/2015	5460.61	41

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
54	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	110
55	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV)	ONGC	01/2010	03/2013	06/2016	723.64	39
56	MARKETING TERMINAL AT PARADEEP	IOCL	07/2009	07/2013	10/2015	199.75	27
57	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	11/2015	270	41
58	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	12/2015	1138.5	8
59	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	22
60	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	01/2016	732	51
61	STRATEGIC CRUDE OIL STORAGE PROJECT	ISPRL	01/2006	10/2011	06/2015	672	44

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	AT VIZAG						
62	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	24
63	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	09/2015	279	9
64	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	06/2016	913	10
65	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
66	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
67	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	07/2016	3110.36	8
68	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	ONGC	10/2013	10/2014	10/2015	429.06	12
69	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
70	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	04/2017	4124.35	12
71	LPG TERMINAL AT KOCHI	IOCL	12/2012	01/2016	07/2017	607.06	18
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	01/2016	993	48
73	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
74	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY	BPCL	03/2012	12/2014	08/2015	1419	8
75	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
76	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
77	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2016	2592.17	24
78	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
79	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	GAIL	06/2009	12/2012	06/2015	2915	30
80	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2015	861.79	31
81	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	06/2016	871.35	15
82	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS (WIP)	ONGC	06/2010	01/2014	06/2018	202.94	53
83	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV)	ONGC	11/2010	08/2013	06/2015	331.2	22
84	ANKLESWAR REDEVELOPMENT	ONGC	11/2010	12/2014	12/2018	2189.63	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
85	MEHESANA REDEVELOPMENT PROJECT	ONGC	11/2010	04/2015	12/2017	3823	32
86	AHMEDABAD REDEVELOPMENT PROJECT	ONGC	11/2010	12/2014	12/2017	1916.1	36
87	102 MW WIND POWER PROJECT	ONGC	07/2010	06/2012	09/2015	1106	39
88	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	12/2015	317.64	39
89	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523	23
90	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA	ONGC	07/2008	08/2012	06/2015	288.04	34
91	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
92	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	12/2015	736.65	51
93	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
94	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
95	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
96	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	29777	35

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
97	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	03/2016	509.66	52
99	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	31
100	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
101	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
102	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	66
103	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
104	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
105	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	05/2018	1657	94

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
106	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	PGCIL	09/2012	03/2015	09/2015	1508.74	6
107	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	03/2016	965.58	40
108	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
109	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	03/2016	2144	39
110	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2016	4404.57	14
111	TRANSMISSION SYSTEM OF VINDHUACHAL - IV AND RIHAND -III GEN. PROJ.	PGCIL	03/2010	11/2012	07/2015	4672.99	32
112	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	25
113	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2016	11130.19	31
114	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2016	4824.12	41
115	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX	PGCIL	02/2009	02/2012	03/2016	410.29	49
116	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	03/2016	1422.85	14
117	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2016	1746.65	19
118	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2015	297.33	16
119	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	09/2015	552.44	19
120	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	09/2015	2422.66	13
121	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	03/2016	2127.51	20
122	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	12/2015	558.26	25
123	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
124	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	03/2016	1961.87	22
125	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
126	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
127	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	06/2017	5353	37
128	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	09/2017	195.42	43

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
129	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	12/2015	1909.24	6
130	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2015	514.2	6
131	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
132	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID	PGCIL	06/2012	11/2014	09/2015	1263.26	10
133	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	03/2016	3201.44	17
134	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2015	723.63	13
135	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	03/2016	9569.76	9
136	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION)	PGCIL	03/2012	03/2014	07/2015	213.78	16
137	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
138	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	09/2015	1927.16	11
139	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
140	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2016	1272.8	49
141	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	12/2015	1585.12	25
142	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	09/2015	250.03	32
143	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ. IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	17
144	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	03/2016	1677.57	35
145	NORTHERN REGION SYSTEM STRENGHENING SCHEME XVI	PGCIL	07/2010	07/2013	11/2015	752.64	28
146	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	PGCIL	12/2010	12/2013	09/2015	2743.19	21
147	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	09/2015	2074.86	30
148	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.9	87
149	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2018	8692.97	86
150	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
151	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	12/2015	1007.16	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
152	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	90

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
153	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
154	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	MRTTP	03/1996	03/2004	03/2016	495.44	144
155	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
156	GOELKERA-MANOHARPUR, (LD) (SER)	SER	03/1997	02/2006	03/2016	261.7	121
157	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
158	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	12/2015	194.07	138
159	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108	66
160	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
161	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733	111
162	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
163	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
164	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	10/2015	921	79
165	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
166	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
167	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTTP	03/2013	03/2016	06/2018	4874.58	27
168	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
169	KATAKHAL TO BHAI RABI	NFR	04/1998	12/2012	03/2016	227.9	39
170	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
171	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	09/2015	207.52	33
172	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	03/2016	2298.42	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
173	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482	30
174	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
175	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
176	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
177	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
178	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
179	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
180	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2019	5300	60
181	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
182	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.2	69
183	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	98
184	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	10/2015	120	82

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
185	GANGA BRIDGE TO RAMDEVI CROSSING PH. II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	09/2015	155	84
186	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	09/2008	12/2015	332.94	87
187	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	01/2016	245	94
188	NALBARI TO BIJUNI (AS-6)	NHAI	12/2003	06/2008	08/2015	225	86
189	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	10/2015	160	89
190	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	08/2015	196	73
191	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	12/2015	1813.76	29
192	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2016	2159	11
193	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
194	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	07/2015	2498.76	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
195	MURADABAD-BAREILY	NHAI	04/2010	06/2013	07/2015	1267	25
196	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
197	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM)	NHAI	02/2011	11/2012	12/2016	193.45	49
198	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION (KM 240-270KM)	NHAI	02/2010	08/2012	03/2016	617	43
199	DEOLI-KOTA	NHAI	01/2011	07/2013	04/2016	593	33
200	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	10/2015	664	20
201	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	02/2016	1535	21
202	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
203	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2016	536	29
204	SAMAIKHIALI - GANDHIDHAM	NHAI	09/2010	03/2013	12/2015	805.39	33
205	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	03/2016	571	29
206	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2015	485	28
207	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2015	374	31
208	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	12/2015	953.88	29
209	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	07/2017	998.79	47
210	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2016	1078.84	36
211	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	06/2016	754	39
212	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
213	BEAWAR-PALI-PINDWARA	NHAI	12/2011	06/2014	11/2015	2388	17
214	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2016	1410	21
215	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	NHAI	11/2011	05/2014	07/2015	909	14
216	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	09/2015	500.29	25
217	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
218	REENGUS SIKAR	NHAI	03/2012	09/2014	12/2015	333.51	15
219	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	11/2015	828	14
220	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	04/2016	1928.22	12
221	2 LANING WITH PS KANPUR KABRAI	NHAI	01/2013	07/2014	07/2015	373.47	12
222	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	02/2016	1232	6
223	PANVEL-INDAPUR	NHAI	12/2011	06/2014	12/2015	942.69	18
224	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2016	1479	18
225	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	NHAI	04/2011	10/2013	11/2015	682	25
226	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	NHAI	04/2012	04/2014	03/2016	624	23
227	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2016	1348.2	30
228	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
229	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	03/2017	1287.95	16
230	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	NHAI	11/2011	10/2013	09/2016	478	35
231	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	07/2015	356.4	12
232	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
233	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
234	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2015	291.36	23
235	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2015	1396.18	15
236	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
237	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
238	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	11/2015	835	22
239	BHOPAL-SANCHI	NHAI	10/2011	01/2013	12/2015	209	35
240	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	09/2015	398	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
241	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2015	1100.7	18
242	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2015	511.54	25
243	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2015	575	29
244	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2016	375.09	23
245	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	11/2015	574	20
246	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	07/2015	600	25
247	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2016	1250	36
248	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	12/2013	09/2015	535	21
249	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	08/2015	1141	24
250	ROHTAK-BAWAL	NHAI	05/2011	11/2013	03/2016	650	28
251	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	07/2015	1008.5	25
252	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	07/2015	351.54	26
253	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	03/2016	671.3	37
254	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	12/2015	1585	31
255	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	12/2015	852	33
256	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	12/2015	1175	32
257	JAIPUR-TONK-DEOLI	NHAI	06/2010	12/2012	06/2015	792.06	30
258	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	11/2016	1108	60
259	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	NHAI	05/2009	10/2011	07/2015	572.3	45
260	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	09/2016	1693.75	61
261	CHENNAI-TADA (SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
262	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	08/2015	795	39
263	GUJARAT/MAHARASHTRA BORDERSURAT-	NHAI	03/2010	09/2012	11/2015	1509.1	38

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	HAZIRA PORT SECTION						
264	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	07/2015	486	62
265	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	04/2016	232.45	67
266	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	12/2015	348.16	99
267	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	12/2015	604	72
268	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	02/2017	275	84
269	BRAMHPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	01/2016	217.61	69
270	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	04/2016	212	103
271	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	01/2016	208	93
272	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	08/2015	198.16	88
273	GUWAHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	08/2015	175.96	88
274	KOTA BYPASS, RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	08/2015	275	82

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
275	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMBAI	MUMBAI PORT TRUST	01/2007	12/2010	01/2016	366.39	61

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
276	AUGMENTATION OF IRON ORE STORAGE IN RMHP	RINL	07/2007	09/2009	07/2015	480	70
277	EXPANSION OF BOKARO STEEL PLANT	SAIL	05/2010	12/2011	08/2015	6325	44
278	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	03/2016	17265	36
279	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC)	NMDC	04/2011	04/2013	06/2015	572	26
280	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	NMDC	02/2011	05/2013	08/2015	898.55	27
281	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	12/2015	187.33	26
282	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	11/2015	332.65	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
283	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	09/2015	237.09	9
284	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	SAIL	11/2012	06/2015	12/2015	313.05	6
285	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	07/2015	160.48	10
286	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
287	CAPTIVE POWER PLANT - 2	RINL	02/2011	09/2013	07/2015	677	22
288	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	03/2016	877.73	8
289	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	03/2017	404.16	20

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
290	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	09/2015	384	59

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
291	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
292	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
293	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	06/2015	225.81	36
294	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	12/2016	156.57	15
295	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2015	270.83	11
296	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	CPWD	11/2012	02/2015	08/2015	238.43	6
297	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	11/2015	261.85	30
298	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
299	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	06/2017	884.3	34
300	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8
301	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	12/2015	23136	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	17270	4099
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	4904.54	6602.74	1698.2
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	2030.78	3583.77	1552.99
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9833.52	4372.91
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	672	1178.35	506.35
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
13	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
15	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
16	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	429.82	3955.21	3525.39
17	REWARI KANPUR PIPELINE PROJECT	HPCL	02/2012	11/2015	1210.64	1446.34	235.7

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
20	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	3513.07	4619.94	1106.87
21	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1487.49	913.5
23	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6476.34	3979.44
24	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	15300	9014.67
25	BARH STPP STAGE -II	NTPC	02/2008	10/2013	7341.04	10852.46	3511.42
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7818.68	3899.09
27	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3745.08	1253.5
28	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.7	482.05
29	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	2569.25	3105.51	536.26
30	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77
31	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.68	586.67
32	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	1779.29	2159.07	379.78
33	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
34	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
35	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12
36	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	1657	2978.86	1321.86
37	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
38	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	BARH STPP (3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
40	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	03/2008	743	1117.11	374.11
42	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	289.93	153.31
43	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
44	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
45	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5
46	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) , NEFR	NFR	09/2006	N.A.	300	827.73	527.73
47	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
48	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
49	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
50	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
51	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
52	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) , NEFR	NFR	09/2006	N.A.	200	496.24	296.24
53	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
54	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
55	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
56	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	800	112.8
57	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
58	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
59	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	SWR	02/1997	N.A.	295	1289.92	994.92
60	HUBLI-ANKOLA (NL) , SWR	SWR	04/1997	N.A.	227	2135	1908

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
62	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
63	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
64	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
65	KHURDA ROAD-BOLANGIR (NL) ECOR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
66	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
67	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	288	121.84
68	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	818.29	635.06
69	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	276	142.59
70	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
71	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
72	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
73	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
74	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
75	KANPUR-KASGANJ-MATHURA (GC) ,NER	NER	03/1997	N.A.	677.97	1651.54	973.57
76	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
77	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
78	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
79	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
80	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
81	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
82	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
83	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
85	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
86	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
87	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
88	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
89	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
90	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
91	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87
92	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
93	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
94	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	MRTTP	04/2012	03/2016	632.68	816.55	183.87
95	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
96	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
97	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
98	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
99	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	968.6	664.6
100	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
101	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
102	VIRAMGAM-BHILDI (WR) , GC	WR	04/1990	N.A.	155.66	548.01	392.35
103	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
104	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
105	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
106	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	645	426.76

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	1630.97	1383.31
108	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	847.75	222.45
109	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
110	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
111	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	270	177.37
112	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
113	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
114	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
115	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
116	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
117	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
118	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
119	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
120	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
121	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
122	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
123	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
124	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
125	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
126	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
127	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
128	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
129	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
131	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
132	KARUR-SALEM (NL) ,SR	SR	02/1997	N.A.	155.55	800	644.45
133	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
134	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
135	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
136	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
137	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
138	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
139	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
140	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
141	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
142	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
143	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
144	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
145	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
146	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
147	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
148	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
149	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
150	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
151	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
152	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
154	RAMGANJUMUNDI-BHOPAL (NL), WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
155	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
156	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
157	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
158	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	19565	17065
159	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
160	JIND-SONEPAT (NL), NR	NR	01/2004	03/2012	238.56	740	501.44
161	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
162	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
163	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
164	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
165	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
166	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
167	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
168	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
169	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
170	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	921	2363	1442
171	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
172	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
173	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
174	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	363.74	167.74
176	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
177	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	348.16	465.5	117.34
178	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	212	386.1	174.1
179	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
180	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
181	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	373.22	127.55
182	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
183	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
184	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT	11/2007	12/2010	1228	1460	232
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
185	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
186	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	8692	12291	3599
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
187	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	10/2015	1,3171.00	1,7270.00	4099	82
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	07/2015	2030.78	3583.77	1552.99	73
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	07/2015	4904.54	6602.74	1698.2	40
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	1228.39	1016.05	30

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	09/2015	5460.61	9833.52	4372.91	41

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	3955.21	3525.39	110
9	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
10	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	462.79	152.98	24
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	06/2016	871.35	1200.00	328.65	15
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	01/2016	993.00	1693.00	700	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	4619.94	1106.87	22
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	01/2016	732.00	1227.00	495	51
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	06/2015	672.00	1178.35	506.35	44
16	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2015	861.79	1256.72	394.93	31
18	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	2,9777.00	3,4555.00	4778	35

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
19	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7818.68	3899.09	111
20	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.90	6476.34	3979.44	87
21	BARH STPP (3X660MW) NTPC	NTPC	02/2005	01/2011	03/2018	8692.97	1,5095.67	6402.7	86
22	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81
23	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	2159.07	379.78	90
24	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	09/2015	2074.86	2348.37	273.51	30
25	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	1007.68	586.67	25
26	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	1487.49	913.5	31
27	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	3745.08	1253.5	78
28	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
29	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	721.81	244.12	66
30	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10
31	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
32	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	07/2010	05/2018	1657.00	2978.86	1321.86	94
33	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
34	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2016	1746.65	2228.70	482.05	19
35	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	3105.51	536.26	17

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
37	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
38	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
39	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
40	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138
41	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108.00	432.72	324.72	66
42	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
43	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
44	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
45	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
46	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482.00	874.57	392.57	30
47	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
48	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
49	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
50	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174
51	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
52	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
53	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
54	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
55	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
56	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	112.8	69
57	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
58	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
59	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	10/2015	921.00	2363.00	1442	79
60	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
61	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	10/2015	120.00	245.39	125.39	82

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
62	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	04/2016	212.00	386.10	174.1	103
63	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	08/2015	196.00	363.74	167.74	73
64	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	12/2015	348.16	465.50	117.34	99
65	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	11/2016	1108.00	2288.00	1180	60

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
66	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	01/2016	366.39	669.46	303.07	61

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun
