

केन्द्रीय क्षेत्र की परियोजनाओं
CENTRAL SECTOR PROJECTS
₹150 करोड़ और अधिक लागत वाली
(₹ 150 Crore and above)
368वीं फ्लैश रिपोर्ट / 368th Flash Report
जून, 2016 / June, 2016



भारत सरकार / Government of India
सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय
Ministry of Statistics and Programme Implementation
आधारी संरचना और परियोजना प्रबोधन प्रभाग
Infrastructure and Project Monitoring Division
सरदार पटेल भवन, संसद मार्ग
Sardar Patel Bhavan, Sansad Marg,
नई दिल्ली / New Delhi-110001
वेबसाइट / Website- www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

	Pages
Executive Summary Hindi	1-29
Executive Summary English	30-48
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2016-2017	49-51
Month wise List of Deleted Projects Costing Rs.150 crore and above during 2016-2017	52
Summary of projects	53-73
Graphical Presentation of All Projects	74-90
Sector wise Analysis of Projects	91-146
Sector wise Graph	147-161
Annexures	162-162
Status of central sector projects costing Rs.150 Crore and above	163-163
List of projects in which expenditure is more than approved cost	164-171
Details of Projects Ahead of Schedule w.r.t. Original Schedule	172-172
Details of On Schedule Projects w.r.t. Original Schedule	173-185
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	186-199
Details of Delayed Projects w.r.t. Original Schedule	200-227
Details of Ongoing Projects having Both Time and Cost Overruns w.r.t Original Schedule	228-233
Details of Projects Without Date of Commissioning	234-254
Details of projects without original Date of Commissioning	255-258
Details of projects without Milestones w.r.t. original schedule	259-293
List of Projects Ahead of Schedule w.r.t. Latest Schedule	294-294
List of Projects on schedule w.r.t. Latest Schedule	295-311
List of ongoing projects having cost overrun w.r.t. to latest schedule	312-321
List of Delayed Projects w.r.t. Latest Schedule	322-336
Details of Central Sector Projects Showing Time overruns of 6 Months and More	337-352
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	353-362
Details Of Central Sector Projects Showing Time Overruns of 6 Months and More and cost overruns of Rs. 100 Crore and above	363-367
Details of Ongoing Projects Under -Public Private Partnership Mode	368-372

कार्यकारी सारांश

1. जून, 2016 की फ्लैश रिपोर्ट में रु. 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 1132 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जून, 2016 के दौरान, 1 परियोजना (सड़क तथा परिवहन क्षेत्र) के पूरा होने की सूचना दी गई है।
2. संदर्भाधीन माह के दौरान, 1132 परियोजनाओं में से, 350 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 72 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 72 परियोजनाओं में से, 30 परियोजनाएं रु. 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	सड़क परिवहन एवं राजमार्ग	417	127	30	13
2.	रेलवे	345	38	9	4
3.	विद्युत	112	62	11	5
4.	कोयला	90	36	1	0
5.	पेट्रोलियम	74	41	11	5
6.	इस्पात	32	14	2	1
7.	शहरी विकास	28	16	4	2
8.	स्वास्थ्य और परिवार कल्याण	9	5	4	0
9.	पोत परिवहन एवं पत्तन	8	3	0	0
10.	नागर विमानन	4	1	0	0
11.	परमाणु ऊर्जा	4	3	0	0
12.	खान	3	1	0	0
13.	दूरसंचार	2	1	0	0
14.	उर्वरक	2	1	0	0
15.	पेट्रोरसायन	1	0	0	0
16.	भारी उद्योग	1	1	0	0
कुल		1132	350	72	30

3. 1132 परियोजनाओं के कार्यान्वयन की कुल मूल लागत रु. 13,48,915.99 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत रु. 15,23,477.16 करोड़ होने की संभावना है, जो रु. 1,74,561.17 करोड़ (मूल लागत का 12.94%) की समग्र लागत वृद्धि को दर्शाता है। जून, 2016 तक इन परियोजनाओं पर किया गया व्यय रु. 6,30,921.81 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 41.41% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(30-06-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	लागत वृद्धि (%)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं 56. फायर निविदाओं की एयरफील्ड आपूर्ति	10/2012	217.60	244.10	12.18
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	87.58
3	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	16.86
4	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	12.97
5	हिंगुला ओसी-II विस्तार	11/2008	479.53	479.63	0.02
उर्वरक					
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ ट्रॉम्बे	10/2014	197.79	209.44	5.89
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	122.78

	(एनएटीआरआईपी)				
	पेट्रोरसायन				
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	9965.00	82.49
	पेट्रोलियम				
1	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
2	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
3	इम्फाल में पॉल डीपोट के निर्माण मणिपुर	08/2010	103.02	171.04	66.03
4	कोरबा में मार्केटिंग टॉप	01/2011	141.86	232.00	63.54
5	उरान चाकन/शिकरापुर एलपीजी पाइपलाइन	12/2009	309.81	462.79	49.38
	विद्युत				
1	तुरीअल हाइड्रो इलेक्ट्रिक परियोजना (60 मेवा.)	07/1998	368.72	1441.52	290.95
2	सुबनसिरी लोअर एचईपी(8X250 मेगावाट) एनएचपीसी	09/2003	6285.33	17435.15	177.39
3	पारे जल विद्युत परियोजना	12/2008	573.99	1581.04	175.45
4	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	147.51
5	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.57	139.32
	रेलवे				
1	गजोल-इटाहार सहित इकलाखी-बेलूरघाट से नई बीजी लाइन (एनएल) एनईएफआर	04/1983	36.80	1336.57	3531.98
2	बांकुरा - दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
3	ललितपुर-सतना-रीवा-सिंगरौली एनएल, (एनसीआर)	09/1998	247.66	5050.00	1939.09
4	जिरिबम से इम्फाल (तुपुई) एनएल, (एनईएफआर)	04/2003	727.56	9046.72	1143.43
5	अकोला-खंडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
	सड़क परिवहन एवं राजमार्ग				
1	पानीपत-जालंधर 6 लेन (96 किमी . से 387.1 किमी)	05/2009	1108.00	2288.00	106.50

2	अरुणाचल प्रदेश पैकेज के तहत अरुणाचल प्रदेश में यूपिया-एचओजे सेक्शन की दो लेनिंग (20.40किमी.)	12/2009	104.00	201.00	93.27
3	मैबंग से लुमडिंग (एएस-25) 83.400 किमी से 111.000 किमी	12/2003	199.81	385.13	92.75
4	मैबंग से लुमडिंग (एएस-24) 111.000 किमी से 126.450 किमी.	12/2003	155.04	280.13	80.68
5	अरुणाचल प्रदेश के तहत अरुणाचल प्रदेश में खोंसा-टीस्सा-लुम्डिंग (एनएच-52बी) (42.50 किमी.)	12/2011	156.63	276.00	76.21
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
3	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	66.82
4	कामराजार पोर्ट लिमिटेड मे कोयला बर्थ-3 का निर्माण	10/2013	198.94	235.15	18.20
5	कामराजार पोर्ट लिमिटेड मे कोयला बर्थ-4 का निर्माण	02/2015	244.50	258.33	5.66
इस्पात					
1	सिंटर मशीन की रिवैम्पिंग - 1 और 2	12/2009	343.00	488.40	42.39
2	गुलबर्गा में मेडिकल कॉलेज और आस्पताल का निर्माण	05/2005	768.88	1070.97	39.29
3	प्रधानमंत्री ग्राम सड़क योजना चरण-VIII के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	206.71	17.79
4	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	175.94	17.50
5	प्रधानमंत्री ग्राम सड़क योजना चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	12.04
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	14405.01	125.25

2	प्लॉट सं. सी-41-43 जी ब्लॉक बांद्रा में आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	356.59	47.76
3	पूर्व किदवई नगर का पुनर्विकास	06/2012	4264.00	5298.00	24.25

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार है:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30-06-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	लागत वृद्धि (रु. करोड़)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं 56. फायर निविदाओं की एयरफील्ड आपूर्ति	10/2012	217.60	244.10	26.50
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	227.17
3	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	70.65
4	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	55.82
5	हिंगुला ओसी-II विस्तार चरण-III (15 मेवा)	11/2008	479.53	479.63	0.10

	उर्वरक				
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ थ्रोम्बे	10/2014	197.79	209.44	11.65
	भारी उद्योग				
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
	पेट्रोरसायन				
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9965.00	4504.39
	पेट्रोलियम				
1	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
2	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
3	बी-127 क्षेत्रों का एकीकृत विकास	12/2011	2059.63	2665.65	606.02
4	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	495.00
5	रिंग सागर सम्राट से मोबाइल ऑफशोर यूनिट का परिवर्तन (एमओपीएस)	03/2011	861.79	1256.72	394.93
	विद्युत				
1	सुबानसिरी लोअर एच.ई.पी (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	17435.15	11149.82
2	बाढ़ एसटीपीपी (3X660मेवा.), एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	रघुनाथपुर थर्मल पावर स्टेशन चरण-	04/2007	4122.00	9606.82	5484.82
4	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) द्वितीय	09/2002	3919.59	8398.75	4479.16
5	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	3683.06
	रेलवे				
1	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	2500.00	19565.00	17065.00
2	जिरीबाम से इंफाल (तुपुई) (एनएल) (एनईएफआर)	04/2003	727.56	9046.72	8319.16
3	ललितपुर-सतना-रीवा-सिंगरौली एनएल, (एनसीआर)	09/1998	247.66	5050.00	4802.34

4	लुमडिंग-सिलचर जिरीबाम, बदरपुर-बरायगाम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
5	बोगीबिल और लिंक लाइन एनईएफआर में ब्रह्मपुत्र पुल	09/1997	1500.00	4996.19	3496.19
सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर 6 लेन 96 किमी . 387.1 किमी	05/2009	1108.00	2288.00	1180.00
2	गोलियार शिवपुरी के चार लेनिंग	05/2013	1055.00	1601.77	546.77
3	मैबंग से लुमडिंग (एएस-25) 83.400 किमी से 111.000 किमी	12/2003	199.81	385.13	185.32
4	हरंगाजों से मैबंग, एनएच-54	12/2003	196.00	331.23	135.23
5	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी से 126.450 किमी एनएच -54	12/2003	155.04	280.13	125.09
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
3	कोचीन पोर्ट्स के बल्लापाड़म में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	164.16
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-3 के निर्माण	10/2013	198.94	235.15	36.21
5	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	13.83
इस्पात					
1	गुलबर्गा में पैरामेडिकल और संबद्ध स्वास्थ्य संस्थान का निर्माण	05/2005	768.88	1070.97	302.09
2	सिंटर मशीन की रिवैम्पिंग - 1 और 2	12/2009	343.00	488.40	145.40
3	पीएमजीएसवाई चरण-VIII के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	206.71	31.22
4	पीएमजीएसवाई चरण-V के तहत ग्रामीण सड़कों का निर्माण तथा	03/2007	149.73	175.94	26.21

	रखरखाव				
5	पीएमजीएसवाई चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	24.39
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	14405.01	8010.01
2	बांद्रा प्लॉट सं. सी 41-43 ब्लॉक के आयकर विभाग के लिए कार्यालय भवन	06/2012	4264.00	5298.00	1034.00
3	पूर्व किदवई नगर का पुनर्विकास	02/2011	241.33	356.59	115.26

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 1132 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 259 समय पर, 350 विलंबित तथा 268 परियोजनाएं लागत वृद्धि दर्शाती हैं तथा 87 परियोजनाएं समय तथा लागत वृद्धि दोनों दर्शाती हैं । तथापि, विलंबित परियोजनाओं की संख्या में 297 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 64 परियोजनाएं किसी आरंभ संबंधी तारीख के बिना स्वीकृत की गई हैं तथा 454 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 350 विलंबित परियोजनाओं में से, 68 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 58 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 150 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 74 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30-06-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत की तारीख	अनुमानित लागत की तारीख	समय वृद्धि (माह में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	09/2003	09/2010	09/2016	72
2	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	12/2019	36

3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	11/2018	35
नागर विमानन					
1	पाक्यांग सिक्किम हवाई अड्डे में नए हवाई अड्डे का निर्माण	01/2009	01/2011	09/2017	80
कोयला					
1	रामागुंडम ओसी-II विस्तार	12/2009	03/2012	03/2023	132
2	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	07/2012	03/2021	104
3	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
4	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
5	शांतिखानी लौंगवाल परियोजना-एससीसीएल	10/2006	03/2012	03/2018	72
उर्वरक					
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ ट्रम्बे	10/2014	11/2016	09/2017	10
स्वास्थ्य एवं परिवार कल्याण					
1	एम्स-रायबरेली-हाउसिंग	10/2013	11/2013	10/2016	35
2	सफदरजंग अस्पताल नई दिल्ली-पुनर्विकास और अन्य सुपर स्पेशियलिटी ब्लॉक	09/2013	12/2015	06/2016	6
3	आईआईटी खड़गपुर अस्पताल ब्लॉक का निर्माण	12/2014	05/2017	07/2017	2
4	एम्स- मातृ एवं शिशु ब्लॉक	12/2013	05/2017	06/2017	1
5	एम्स ओपीडी (नए)	08/2014	05/2017	06/2017	1
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
खान					
1	सीएपीएसी के वर्तमान ओपन कास्ट खान के तहत मलंजखंड खान का विस्तार-भूमिगत खान का विकास	09/2011	09/2017	04/2020	31
पेट्रोलियम					
1	कोच्ची-कूटनाड बंगलौर मंगलौर पाइपलाइन परियोजना	06/2009	12/2012	02/2019	74

2	फुप्लुर-हल्दिया पाइपलाइन परियोजना चरण -I	07/2009	01/2013	12/2018	71
3	12 ऑफशोर सप्लाई वेसेल्स (ओएसवी) का निर्माण	06/2007	09/2011	03/2017	66
4	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	12/2009	06/2011	10/2016	64
5	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	01/2012	09/2016	56
विद्युत					
1	तुरीअल जल विद्युत परियोजना (60 मेवा.)	07/1998	07/2006	03/2017	128
2	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
3	कुडनकुलम एपीपी पारेषण प्रणाली (पीजीसीआईएल)	05/2005	11/2008	06/2017	103
4	बाढ़ एसटीपीपी (3X660मेवा.), एनटीपीसी	02/2005	01/2011	05/2018	88
5	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	12/2009	03/2017	87
रेलवे					
1	गोंदिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
2	जगगएपेट -मेललेचेरिक	04/2007	01/1999	06/2017	221
3	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	11/2002	12/2018	193
4	ललितपुर-सतना-रेवा सिंगराली एनएल, एनसीआर	09/1998	05/2008	03/2023	178
5	बांकुड़ा - दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
सड़क परिवहन एवं राजमार्ग					
1	बिजनी से असम/पश्चिम बंगाल सीमा चरण.II, 30.00 किमी. से 0.00 किमी., एनएच-31 सी	12/2003	06/2005	12/2016	138
2	हरंगाजो से मैबंग, 164.08 किमी.- 190.587 किमी. एनएच-54	12/2003	09/2007	03/2017	114
3	आगरा-बाईपास (एन एस -1 / यूपी-1), एनएच 2,3	12/2003	09/2007	09/2016	108
4	सोनापुर से गुवाहाटी (एस -3)	12/2003	03/2008	12/2016	105

5	नलबाड़ी से बिजनी (एएस-7)	12/2003	04/2008	12/2016	104
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे एफ/ओ स्पेशल पर्पस ब्हीकल (एसपीवी)	10/2002	03/2006	07/2016	124
2	मुंबई बीओटी आधार पर ऑफशोर कंटेनर बर्थ्स का निर्माण तथा कंटेनर टर्मिनल का विकास	01/2007	12/2010	12/2018	96
3	कोचीन पोर्ट ट्रस्ट में बल्लापाड़म में आईसीटीटी से रेल कनेक्टिविटी	03/2007	04/2009	08/2016	88
इस्पात					
1	भिलाई इस्पात प्लांट का विस्तार	08/2010	03/2013	12/2016	45
2	45एमवीए साफ के साथ अन्य एसोसिएटेड सुविधाओं का संग्रहण	12/2011	10/2013	08/2016	34
3	एनएमडीसी समेकित इस्पात संयंत्र	01/2010	05/2015	12/2017	31
4	एसएमएस-1 कन्वर्टर्स रिवैम्पिंग	05/2012	07/2015	09/2017	26
5	बागमती का सिंचाई कार्य	10/2005	03/2015	03/2017	24
दूरसंचार					
1	इंटेलिजेंट फाइबर ऑप्टिक सी के पैकेज एफ तथा जी भाग ख स्पेक्ट्रम (एनएफएस) ओएफसी लेयिंग प्रोजेक्ट के लिए नेटवर्क	09/2014	09/2014	03/2017	30
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	06/2011	11/2016	65
2	नागपुर महाराष्ट्र में राष्ट्रीय फायर कॉलेज का उन्नयन	06/2010	03/2012	03/2017	60
3	संसदीय सौध संसद भवन परिसर में भवन के विस्तार हेतु निर्माण कार्य, नई दिल्ली	05/2009	05/2013	06/2016	37
4	आयकर विभाग के लिए कार्यालय भवन प्लॉट सं. सी-41-43 जी ब्लॉक बांद्रा	02/2011	11/2014	12/2017	37
5	इंफाल मणिपुर में एनआईटी अकादमी भवन	02/2014	03/2015	10/2017	31

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल 2016 में, इस मंत्रालय की निगरानी पर चल रहे 1061 परियोजनाओं में से, 241 परियोजनाओं के संबंध में लागतवृद्धि तथा 326 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि जून 2016 के दौरान, 1132 परियोजनाओं में से 268 परियोजनाओं के संबंध में लागतवृद्धि तथा 350 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है। अप्रैल 2016 की तुलना में, **लागतवृद्धि** दर्शाने वाली **परियोजनाओं** की संख्या **22.71%** से बढ़कर **23.67%** हो गई, जबकि **समयवृद्धि** दर्शाने वाली **परियोजनाओं** के संबंध में **30.73%** से बढ़कर **30.92%** हो गई है।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना उपलब्धियों वाली पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30-06-2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	संचयी व्यय (रु. करोड़)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	309.46	433.19	01/2011	09/2017
2	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण	05/2010	335.61	318.00	305.59	05/2012	03/2015
3	विभिन्न हवाई अड्डों पर सं 56 एयरफील्ड फायर टैंडर की आपूर्ति	10/2012	217.60	244.10	30.73	03/2015	09/2015

4	वीएसआई एयरपोर्ट पर नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण	10/2013	314.61	314.61	26.30	09/2018	09/2018
कोयला							
1	बिथनोक लिग्नाइट खान परियोजना (2.25एमटीपीए)	03/2015	513.63	513.63	74.76	12/2019	12/2019
2	हल्दा लिग्नाइट खान परियोजना (1.90 एमटीपीए)	03/2015	522.45	522.45	2.56	09/2019	09/2019
3	मदननगर ओसीपी	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
4	अमादंद ओसी विस्तार परियोजना	02/2016	198.68	198.68	0.00	03/2019	03/2019
5	भावाडी विस्तार ओसी खान	02/2016	304.52	304.52	0.00	03/2018	03/2018
उर्वरक							
1	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	209.44	72.96	11/2016	09/2017
स्वास्थ्य एवं परिवार कल्याण							
1	एलजीबीआरआईएमएच	07/2012	175.57	175.57	113.50	12/2014	03/2016
2	एलएचएमसी -अस्पताल	02/2013	414.11	414.11	210.92	11/2013	11/2014
3	सफदरजंग एसएसबी	09/2013	444.70	444.70	400.00	12/2015	06/2016
4	रायबरेली हाउसिंग	10/2013	159.50	159.50	127.80	11/2013	10/2016
5	सफदरजंग हॉस्पिटल, नई दिल्ली पुनः विकास और अन्य इमरजेंसी ब्लॉक	11/2013	196.70	196.70	197.38	01/2016	04/2016
भारी उद्योग							
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	2289.00	09/2011	12/2017
खान							
1	मलंजखंड खान का विस्तार - भूमिगत खान का विकास	09/2011	1856.00	1176.00	12.44	09/2017	04/2020
2	डब्ल्यूपीपीआरजे देवीकोट	12/2015	344.50	344.50	0.00	11/2016	11/2016
पेट्रोलियम							
1	हल्दिया में एलपीजी आयात	01/1991	694.00	694.00	57.19	10/2018	10/2018

	टर्मिनल						
2	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	1143.03	10/2011	04/2016
3	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1489.38	01/2012	09/2016
4	एन्नोर में नई विपणन टर्मिनल	11/2006	171.83	171.83	0.00	एन.ए.	एन.ए.
5	12 ऑफशोर सप्लाई वेजेल्स (ओएसवी) का निर्माण	06/2007	736.65	736.65	516.44	09/2011	03/2017
विद्युत							
1	सुबनसिरी लोअर एच.ई.पी (8x250 मेवा) (एनएचपीसी)	09/2003	6285.33	17435.15	8540.30	09/2010	एन.ए.
2	उत्तर में फाइबर ऑप्टिक संचार की स्थापना	03/2012	198.63	198.63	112.53	09/2014	10/2016
3	यूआरटीडीएसएम चरण-I	01/2014	374.63	374.63	27.60	04/2016	03/2017
4	पकल दुल जल विद्युत परियोजना (1000 मेवा.)	10/2014	8112.12	8112.12	141.80	04/2020	03/2022
5	फाइबर ऑप्टिक विस्तार परियोजना के तहत एनआर में संचार प्रणाली	03/2015	197.40	197.40	3.30	03/2018	03/2018
रेलवे							
1	हावड़ा अमटा चम्पादंगा एनएल, एसईआर	04/1974	393.46	1026.00	0.00	03/2007	एन.ए.
2	नांगल बांध-तलवाड़ा (एनएल), एन.आर.	03/1981	450.00	2100.00	496.00	07/2012	एन.ए.
3	एकलाखी-बलूरघाट सहित जी से नई बीजी रेलवे लाइन	04/1983	36.80	1336.57	259.15	एन.ए.	03/2019
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	1428.00	456.82	06/2005	12/2019
5	गुना-इटावा वाया शिवपुरी-ग्वालियर -भिंड एनएल, (एनसीआर)	04/1986	158.77	634.48	631.43	03/1994	02/2016
सड़क परिवहन एवं राजमार्ग							

1	"मधुगिरी-माल्वागल (400.330 किमी. से 483.151) - एलओटी-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	अनिशाबाद-औरंगाबाद-हरिनगंज (0.000 किमी. से 62.000 किमी.)-एलओटी	01/1991	282.41	282.41	75.32	08/2016	08/2016
3	अनिशाबाद-औरंगाबाद-हरिनगंज (62.000 किमी. से 154.625 किमी.)-	01/1991	358.22	358.22	200.21	10/2016	10/2016
4	बख्तियारपुर-मोकामा	01/1991	1167.45	1167.45	0.00	एन.ए.	एन.ए.
5	बंकुरा-पारुलिया (0.000 किमी. से 84.000 किमी.)	01/1991	322.00	322.00	66.59	03/2018	03/2018
पोत परिवहन एवं पत्तन							
1	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	07/2016
2	सेतुसमुंद्रम शिप चैनल प्रोजेक्ट	06/2005	2427.40	2427.40	831.21	10/2008	एन.ए.
3	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	415.01	12/2010	12/2018
4	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल कनक्टिविटी	03/2007	245.67	409.83	350.68	04/2009	08/2016
5	आरओआरओ-II कामराजर पोर्ट लिमिटेड	09/2015	210.00	210.00	0.00	01/2018	01/2018
इस्पात							
1	गुलबर्गा में मेडिकल कॉलेज एवं अस्पताल	05/2005	768.88	1070.97	1070.97	02/2014	03/2016
2	बागमती का सिंचाई कार्य	10/2005	956.00	956.00	650.35	03/2015	03/2017
3	पीएमजीएसवाई चरण-V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	175.94	178.61	12/2015	03/2017
4	पीएमजीएसवाई चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	200.20	12/2016	12/2016

5	गिरीडीह, कोडरमा में रोड एवं पुल का निर्माण	12/2007	200.00	200.00	136.15	03/2018	03/2018
दूरसंचार							
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	13334.00	13334.00	0.00	07/2015	एन.ए.
शहरी विकास							
1	सेवरेज परियोजना	08/2007	246.90	246.90	0.00	एन.ए.	एन.ए.
2	संसद भवन सौध परिसर में भवन के विस्तार हेतु निर्माण कार्य	05/2009	261.85	261.85	199.73	05/2013	06/2016
3	एनआईटी कालीकट केरल के लिए मेगा होस्टल II का निर्माण	01/2010	165.23	165.23	0.00	10/2012	एन.ए.
4	नागपुर, महाराष्ट्र में राष्ट्रीय फायर सर्विसेज कॉलेज का उन्नयन	06/2010	205.00	191.97	108.07	03/2012	03/2017
5	प्लॉट सं. सी-41-4 पर आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	356.59	108.43	11/2014	12/2017

एन.ए. : उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानों वाली शुरुआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30-06-2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	संशोधित लागत (रु. करोड़)	संचयी व्यय (रु. करोड़)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	21674.00

2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी 500 एमडब्ल्यूई)	09/2003	3492.00	0.00	4933.84
नागर विमानन					
1	पाक्यांग (सिक्किम) में नए हवाई अड्डा का निर्माण	01/2009	309.46	0.00	433.19
कोयला					
1	कुल्दा ओसीपी (महानदी कोल फील्ड लिमिटेड)	01/2005	302.96	0.00	318.74
2	बलराम ओसीपी विस्तार एमसीएल 8.00 एमटीवाई	12/2007	172.08	0.00	182.26
3	रामगुंडम ओसीपी -II विस्तार	12/2009	418.97	0.00	481.31
4	अद्वियाला शाफ्ट परियोजना	12/2009	212.34	0.00	880.45
स्वास्थ्य एवं परिवार कल्याण					
1	सफदरजंग अस्पताल, नई दिल्ली पुनर्विकास तथा अन्य आपातकालीन ब्लॉक	11/2013	196.70	0.00	197.38
भारी उद्योग					
1	राष्ट्रीय ऑटोमोटिव टेस्टिंग अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	0.00	2289.00
पेट्रोलियम					
1	कोरवा में नार्कटिंग टोप	01/2011	141.86	0.00	179.17
विद्युत					
1	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी)	09/2002	3919.59	0.00	5671.34
2	सुबनसिरी लोअर एचईपी (8X250 मेवा) (एनएचपीसी)	09/2003	6285.33	0.00	8540.30
3	तीस्ता लो डैम एचईपी, चरण-IV (4X40 मेवा.) (एनएचपीसी)	09/2005	1061.38	0.00	2028.58
4	बीआरबीसीएल-नबीनगर टीपीपी- जेवी (4X250 मेवा.)	01/2007	5353.00	0.00	5679.02
5	किशनगंगा एचईपी (3X110 मेवा.)	01/2009	3642.04	0.00	4617.51
रेलवे					
1	नंगल बांध-तलवारा (एनएल) एनआर	03/1981	450.00	0.00	496.00
2	त्रिचि तमलुक दीहा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	0.00	456.82
3	गुना-इटावा वाया शिवपुरी ग्वालियर ग्रिड, एनएल (एनसीआर)	04/1986	158.77	608.02	631.43

4	एमएसएच-ताह गौज के रूपांतरण परियोजना के लिए नए एमएम के साथ भिल्डी-विरमगढ़	04/1990	153.82	0.00	245.58
5	मुजफ्फरनगर सीतामढ़ी नई लाइन	01/1991	332.15	0.00	538.53
सड़क परिवहन एवं राजमार्ग					
1	हरंगाजो से मेबंग (एस-23), 126.450 किमी से 140.700 किमी	12/2003	280.00	0.00	427.01
2	मेबंग से लुमडिंग (एस-26), 60.500 किमी से 83.400 किमी, एनएच-54	12/2003	167.64	0.00	277.36
3	धरमतुल से सोनापुर किमी. 183 से किमी. 205 (एस-20)	12/2003	160.00	0.00	200.36
4	ब्रह्मपुत्र पुल एमएच सं. 31	12/2003	217.61	309.56	399.08
5	बिजनी से असम/पश्चिम बंगाल सीमा (एनएच-31) एनएचएआ	12/2003	237.80	0.00	409.39
इस्पात					
1	पीएमजीएसवाई चरण V के तहत ग्रामीण सड़क का निर्माण तथा प्रबंधन	03/2007	149.73	173.00	178.61
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	13845.01	13973.45
2	पुलिस प्रशिक्षण (सीएपीटी) भोपाल हेतु केन्द्रीय अकादमी का निर्माण	12/2012	188.87	0.00	10255.48

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30-06-2016 की स्थिति के अनुसार)

क्र.सं.	सेक्टर/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
	परमाणु ऊर्जा				

1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	10/2013	05/2016
	नागर विमानन				
1	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	एन.ए.	03/2015
2	विभिन्न हवाई अड्डों पर 56 एनओएस एयरफील्ड फायर टैंडर की सप्लाई	10/2012	03/2015	एन.ए.	09/2015
	कोयला				
1	कुल्दा ओसीपी (महानदी कोलफील्ड्स लिमिटेड)	01/2005	03/2010	एन.ए.	03/2016
2	चुरी बेंती यूजी (0.81 एमटीवाई)	08/2007	03/2011	एन.ए.	03/2016
3	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.ए.	एन.ए.
4	पूर्णाडीह ओसीपी (3.0 एमटीवाई)	07/2008	03/2013	एन.ए.	03/2016
5	तपिन ओसीपी (2.5 एमटीवाई)	08/2008	03/2012	एन.ए.	03/2016
	स्वास्थ्य एवं परिवार कल्याण				
1	एलजीबीआरआईएमएच-तेजपुर, असम	07/2012	12/2014	एन.ए.	03/2016
2	एलएचएमसी नई दिल्ली पुनः-विकास	02/2013	11/2013	एन.ए.	11/2014
3	सफदरजंग अस्पताल, नई दिल्ली-पुनर्विकास अन्य -इमरजेंसी ब्लॉक	11/2013	01/2016	एन.ए.	04/2016
	पेट्रोरसायन				
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2015	12/2015
	पेट्रोलियम				
1	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	एन.ए.	04/2016
2	एन्नोर में नई मार्केटिंग टर्मिनल	11/2006	एन.ए.	एन.ए.	एन.ए.
3	एक ईटीपी और तीन ईटीपी सह वाटर इंजेक्शन संयंत्रों का निर्माण (डब्ल्यूआईपी)	06/2010	01/2014	एन.ए.	एन.ए.
4	एन्नोर-त्रिची-मदुरै एलपीजी पाइपलाइन	05/2013	एन.ए.	एन.ए.	एन.ए.
5	पारादीप हल्दिया-दुर्गापुर एलपीजी पाइपलाइन और आईटीएस विस्तार मुजफ्फरपुर से पटना तक	01/2015	एन.ए.	एन.ए.	एन.ए.
	विद्युत				
1	सुबनसिरी लोअर एचईपी (8X250 मेवा.)	09/2003	09/2010	एन.ए.	एन.ए.

	(एनएचपीसी)				
2	रघुनाथपुर थर्मल पावर स्टेशन चरण-I	04/2007	02/2011	एन.ए.	03/2016
3	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	07/2013	एन.ए.	एन.ए.
4	उत्तरी क्षेत्र प्रणाली सुदृढीकरण स्कीम	03/2010	11/2012	एन.ए.	05/2016
5	केबीयूएनएल-मुजफ्फरपुर टीपीपी स्टेज-II सहायक (2X195 मेगावाट)	03/2010	01/2013	एन.ए.	03/2016
रेलवे					
1	हावड़ा एमटीए चंपादंगा एनएल	04/1974	03/2007	03/2007	एन.ए.
2	नांगलडैम-तालवारा (एनएल) एनआर	03/1981	07/2012	एन.ए.	एन.ए.
3	गुना-इटावा वाया शिवपुरी-ग्वालियर-भिंड एनएल, एनसीआर	04/1986	03/1994	02/2016	02/2016
4	नामखाना-चंद्रनगर, काकद्वीप-बुदाखली और चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना के बाद एमएम	04/1987	एन.ए.	एन.ए.	एन.ए.
5	मुजफ्फरपुर-सीतामढ़ी नई लाइन	01/1991	07/2014	एन.ए.	07/2014
सड़क परिवहन एवं राजमार्ग					
1	रिहैविलिटेशन एंड अपग्रेडेशन टू 2 लाइंस - 2 लेन पेव्ड शोल्डर कंफिग्रेशन एंड स्ट्रेंथनिंग	01/1991	04/2014	एन.ए.	एन.ए.
2	रिहैविलिटेशन एंड अपग्रेडेशन टू 2 लाइंस - 2 लेन पेव्ड शोल्डर (40 किमी से 219.945 किमी)	01/1991	05/2016	एन.ए.	05/2016
3	रिहैविलिटेशन एंड अपग्रेडेशन टू 2 लाइंस - 2 लेन पेव्ड शोल्डर कंफिग्रेशन ऑफ सीतामढ़ी 40 किमी	01/1991	एन.ए.	एन.ए.	एन.ए.
4	रिहैविलिटेशन एंड अपग्रेडेशन टू 2 लाइंस - 2 लेन पेव्ड शोल्डर कंफिग्रेशन	01/1991	एन.ए.	एन.ए.	एन.ए.
5	एनएच 31 के बख्तियारपुर-मोकामा सेक्शन के चार लेनिंग	01/1991	एन.ए.	एन.ए.	एन.ए.
पोत परिवहन एवं पत्तन					
1	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	एन.ए.	एन.ए.
इस्पात					
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल का निर्माण	05/2005	02/2014	एन.ए.	03/2016
2	गुलबर्गा में पारा मेडिकल और एलिड	07/2011	12/2015	एन.ए.	04/2016

	स्वास्थ्य इंस्टीट्यूट का निर्माण				
3	डिफर में 24 सं. नई औद्योगिक प्रशिक्षण संस्थानों (आईटीआई) के लिए कार्यशालाओं और भवनों का निर्माण	08/2012	03/2016	एन.ए.	03/2016
4	राजीव गांधी के अंतर्गत इनडोर खेल हॉल के लिए तेलंगाना में 123 ब्लॉकों तथा आंध्र प्रदेश में 167 ब्लॉकों का निर्माण	07/2014	01/1999	एन.ए.	एन.ए.
दूरसंचार					
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	एन.ए.	एन.ए.
शहरी विकास					
1	जोन 2 में मूसी के दक्षिण हेतु पुराने शहर क्षेत्र में सीवरेज प्रणाली का पुनर्वास तथा सुदृढीकरण	08/2007	एन.ए.	एन.ए.	एन.ए.
2	एनआईटी कालीकट केरल के लिए मेगा छात्रावास द्वितीय का निर्माण	01/2010	10/2012	एन.ए.	एन.ए.
3	प्रगति मैदान से सटी हुई भूमि पर सर्वोच्च न्यायालय के अतिरिक्त ओडी का निर्माण	07/2012	08/2014	एन.ए.	एन.ए.
4	मुंबई मेट्रो लाइन 3 (कोलाबा-बांद्रा सीपज)	07/2013	01/2015	एन.ए.	12/2015
5	रोपर में आईआईटी पंजाब के लिए चरण-I के अंतर्गत विभिन्न भवनों का निर्माण	02/2014	01/2015	एन.ए.	एन.ए.

एनए: उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार कार्य शुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

- i) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 417 परियोजनाओं में से, 127 परियोजनाएं विलंबित हैं। माह के दौरान 30 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	बिजनी से असम /पश्चिम बंगाल सीमा (एनएच 31.सी) (एनएचएआई)	1	एनआर

2	नलबाड़ी के बिजनी (एस 6) एनएचएआई	1	एनआर
3	जयपुर-रींगस एनएचएआई	1	एनआर
4	ब्यावर पाली पिंडवारा एनएचएआई	1	एनआर
5	रींगस सीकर एनएचएआई	1	एनआर
6	पीएस लांबिया-जायतरण-रायपुर के साथ 2 लेनिंग एनएचएआई	1	एनआर
7	निंबी जोधा-डेगाना-मेड़ता सिटी सेक्शन के पी एस साथ 2 लेन का सुदृढीकरण तथा चौड़ीकरण एनएचएआई	1	एनआर
8	गोमती चौराहा उदयपुर के 4 लेनिंग एनएचएआई	1	एनआर
9	रोहतक हिसार सेक्शन के 4 लेनिंग एनएचएआई	1	एनआर
10	गुड़गांव - कोटपुतली - जयपुर (छह लेन) एनएचएआई	1	एनआर
11	हरंगाजो से मैबंग (एस 23), 126.450 किमी. से 140.700 किमी. एनएचएआई	2	एनआर
12	इंदौर-झाबुआ-गुजरात/ मप्र. एनएचएआई	2	एनआर
13	चेन्गापल्ली से कोयंबटूर बाईपास 102.035 किमी.-144.740 किमी. एनएचएआई	2	एनआर
14	अहमदाबाद से गोधरा के 4 लेनिंग एनएचएआई	2	एनआर
15	चेन्नई एन्नोर पोर्ट कनेक्टिविटी के लिए आवश्यक सड़क संपर्क का विकास एनएचएआई	2	एनआर
16	ब्रह्मपुत्र-फरक्का के 4 लेनिंग एनएचएआई	2	एनआर
17	राजसमंद-गंगापुर-भीलवाड़ा के 4 लेनिंग एनएचएआई	2	एनआर
18	आगरा-बाईपास (एन एस -1 / यूपी-1), एनएच 2,3 एनएचएआई	3	एनआर

19	पीएस भीलवाड़ा-लोदपुरा सेक्शन के 2 लेनिंग एनएचएआई	3	एनआर
20	फरक्का-रायगंज के 4 लेनिंग एनएचएआई	4	एनआर
21	रोहतक जींद (लंबाई 45 किमी) के 4 लेनिंग एनएचएआई	5	एनआर
22	मुरादाबाद-बरेली एनएचएआई	6	एनआर
23	कांडला - मुंद्रा पोर्ट एनएचएआई	6	एनआर
24	नेल्लोर-चिलकालूरीपेट के छह लेनिंग 1182.802 किमी. से 1366.547 किमी. एनएचएआई	6	एनआर
25	अहमदाबाद से वडोदरा सेक्शन एनएचएआई	6	एनआर
26	एनएच -9 के एमएच-केएनटी सीमा संगारेड्डी सेक्सन के 4 लेनिंग एनएचएआई	6	एनआर
27	ग्वालियर-शिवपुरी के चार लेनिंग एनएचएआई	6	एनआर
28	इटवा- चकेरी एनएचएआई	8	एनआर
29	एनएच 50 के पुणे नासिक सेक्शन के खेड़-सिन्नार खिंचाव के चौड़ीकरण एनएचएआई	12	एनआर
30	गोवा / कर्नाटक सीमा-कुंदापुर सेक्शन के 4 लेनिंग एनएचएआई	12	एनआर

एनआर: परियोजना क्रियान्वयनकर्ता एजेंसी द्वारा परियोजना में विलंब के मामले में कोई विशेष कारण सूचित नहीं किया गया है ।

- ii) **विद्युत क्षेत्र में**, 112 परियोजनाओं में से, 62 परियोजनाएं विलंबित हैं । माह के दौरान 11 परियोजनाओं के संबंध में 1-4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	एनआर / डब्ल्यू आर भाग-क तक सिक्किम में जेनरेशन परियोजना के लिए विद्युत का हस्तांतरण के लिए पीजीसीआईएल	1	भूमि अधिग्रहण

2	झारखंड और पश्चिम बंगाल भाग-क1 में चरण -1 जेनरेशन परियोजनाओं के लिए पारेषण प्रणाली पीजीसीआईएल	1	भारी वर्षा, भूमि उग्रवादी समस्या
3	उत्तर क्षेत्र में फाइबर ऑप्टिक संचार प्रणाली की स्थापना पीजीसीआईएल	1	आरओडब्ल्यू, भारी वर्षा, कोहरा
4	अनन्तपुर जिला आंध्र प्रदेश भाग क (चरण - I) में अल्ट्रा मेगा सोलर पार्क के लिए पारेषण प्रणाली पीजीसीआईएल	1	एन.आर.
5	छत्तीसगढ़ में आईपीपी परियोजनाओं के लिए रायपुर वर्धा कोरिडोर में प्रणाली सुदृढीकरण पीजीसीआईएल	2	वन संबंधी अनुमति
6	छत्तीसगढ़ में आईपीपी परियोजनाओं के लिए डब्ल्यूआर-एनआर एचवीडीसी इंटरकनेक्टर पीजीसीआईएल	2	भूमि अधिग्रहण, आरओडब्ल्यू
7	झारखंड और पश्चिम बंगाल भाग-ख में चरण-I परियोजनाओं के लिए पारेषण प्रणाली पीजीसीआईएल	2	भारी वर्षा, भूमि अधिग्रहण
8	उत्तर क्षेत्र प्रणाली सुदृढीकरण योजना- XXVIII पीजीसीआईएल	2	एन.आर.
9	दक्षिणी क्षेत्र प्रणाली सुदृढीकरण - XIV पीजीसीआईएल	3	आरओडब्ल्यू, भारी मुआवजे की मांग
10	मौदा चरण- II के साथ जुड़े पारेषण प्रणाली पीजीसीआईएल	3	आरओडब्ल्यू, वन संबंधी अनुमति,
11	छत्तीसगढ़ में आईपीपी जेनरेशन परियोजनाओं के लिए चंपा और रायगढ़ में पूलिंग स्टेशनों की स्थापना पीजीसीआईएल	4	भूमि संबंधी मंजूरी

एनआर: परियोजना क्रियान्वयनकर्ता एजेंसी द्वारा परियोजना में विलंब के मामले में कोई विशेष कारण सूचित नहीं किया गया है ।

- iii) **पेट्रोलियम क्षेत्र में**, 74 परियोजनाओं में से 41 परियोजनाएं विलंबित हैं । माह के दौरान, 11 परियोजनाओं के संबंध में 1-9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	मधुबन तेल में निर्जलीकरण सुविधा और उपचार संयंत्र के साथ माध्यमिक टैंक फार्म	1	भूमि मुकदमेबाजी

2	चिनचिन्नडा काकीनाडा जंक्शन प्वाइंट पाइप लाइन गेल	1	प्रतिकूल सामान्य जन
3	इम्फाल, मणिपुर में पीओएल डिपोट का निर्माण आईओसीएल	1	एन.आर.
4	6 ईटीपीएस का निर्माण ओएनजीसी	3	सिविल कार्य में धीमी प्रगति
5	पारादीप रिफाइनरी में पॉलीप्रोपीलिन संयंत्र आईओसीएल	3	एन.आर.
6	एकीकृत रिफाइनरी विस्तार परियोजना बीपीसीएल	4	एन.आर.
7	पादुर में सामरिक कच्चा तेल भंडारण परियोजना आईएसपीआरएल	4	भारी वर्षा
8	पारादीप-रायपुर- रांची पाइप लाइन आईओसीएल	6	ठेकेदार द्वारा खराब कार्य
9	पारादीप हल्दिया बरौनी पाइप लाइन की वृद्धि आईओसीएल	6	भूमि अधिग्रहण
10	पलक्कड़ एलपीजी संयंत्र बीपीसीएल	6	एन.आर.
11	एसएमपीएल के डी-बोटलनेकिंग आईओसीएल	9	वन संबंधी अनुमति में विलंब

एनआर: परियोजना क्रियान्वयनकर्ता एजेंसी द्वारा परियोजना में विलंब के मामले में कोई विशेष कारण सूचित नहीं किया गया है ।

- iv) **रेलवे क्षेत्र में**, 345 परियोजनाओं में से, 38 परियोजनाएं विलंबित हैं । माह के दौरान 9 परियोजनाओं के संबंध में 8-46 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	रजतगढ़-बारंग (एलडी), ईसीओआर आरवीएनएल	8	संविदात्मक मुद्दे
2	अररिया से गलगलिया (ठाकुरगंज), के लिए नई बीजी लाइन एनईएफआर	12	निधि की कमी

3	अगरतला-अखौरा, एनएल, एनएफआर	16	बांग्लादेश के साथ एक संयुक्त उद्यम परियोजना के रूप में प्रशासनिक प्रक्रिया में देरी
4	तामलुक-बसुल्या-सुताहाटा दोहरीकरण आरवीएनएल	23	एन.आर.
5	भैरबी-सैरंग एनएल एनईएफआर एनएफआर	24	एन.आर.
6	किरंदुल - जगदलपुर दोहरीकरण ईसीओआर	24	एन.आर.
7	कोटा (जीसी) के लिए विस्तार के साथ ग्वालियर-सेवपुरकाला एनसीआर	34	एन.आर.
8	संबलपुर - अंगुल रेलवे विद्युतीकरण ईसीओआर	39	एन.आर.
9	गंगापुर सीट और मोहारी-तांतपुर और तानपुर-बंसी पहारपुर के विस्तार के साथ धौलपुर - सिमुत्रा एनसीआर	46	राजस्थान सरकार से अनुमति में विलंब

एनआर: परियोजना क्रियान्वयनकर्ता एजेंसी द्वारा परियोजना में विलंब के मामले में कोई विशेष कारण सूचित नहीं किया गया है ।

- v) **शहरी विकास क्षेत्र में**, 28 परियोजनाओं में से 16 परियोजनाएं विलंबित है । माह के दौरान 4 परियोजनाओं के संबंध में 2-17 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	फ्लैट नं. 4 सेक्टर 10 द्वारका नई दिल्ली में पीएनबी के प्रधान कार्यालय भवन के निर्माण सीपीडब्ल्यूडी	2	एनआर
2	कमांड में आईआईटी मंडी के लिए चरण I उत्तर के तहत विभिन्न भवन सीपीडब्ल्यूडी	12	एनआर
3	बेंगलुरु मेट्रो रेल परियोजना चरण -II बीएमआरीएल	13	भूमि अधिग्रहण
4	नई दिल्ली में केन्द्रीय सशस्त्र पुलिस बल संस्थान के मेडिकल साइंसेज (कैपफीम्स) की स्थापना सीपीडब्ल्यूडी	17	एनआर

एनआर: परियोजना क्रियान्वयनकर्ता एजेंसी द्वारा परियोजना में विलंब के मामले में कोई विशेष कारण सूचित नहीं किया गया है।

- vi) **स्वास्थ्य एवं परिवार कल्याण क्षेत्र में**, 9 परियोजनाओं में से, 5 परियोजना विलंबित है। माह के दौरान, 4 परियोजनाओं में 1-4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	एम्स मातृ एवं शिशु ब्लॉक एचएससीसी	1	निधि को जारी में देरी, सुरक्षा पहलु के कारण कार्य निलंबित करना
2	एम्स ओपीडी (नए) एचएससीसी	1	निधि को जारी में देरी, सुरक्षा पहलु के कारण कार्य निलंबित करना
3	अस्पताल ब्लॉक के निर्माण, आईआईटी, खड़गपुर एचएससीसी	2	समय पर निधियों अनुपलब्धता, रोजगार की मांग के लिए स्थानीय विरोध
4	एम्स रायबरेली आवास एचएससीसी	4	सिविल कार्य में देरी, स्थानीय रोजगार की मांग के लिए काम की ठहराव एमओएचएफडब्ल्यू के प्रतिनिधि की तैनाती में विलंब

- vii) **इस्पात क्षेत्र में**, 32 परियोजनाओं में से, 14 परियोजना विलंबित है। माह के दौरान, 2 परियोजनाओं में 1-2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	भिलाई इस्पात संयंत्र सेल का विस्तार	1	ठेकेदार द्वारा गैर वन भूमि और अपर्याप्त लामबंदी के अधिग्रहण में देरी

2	45 एमवीए सुरक्षित के साथ अन्य संबद्ध सुविधाओं सेल की स्थापना	2	ठेकेदार द्वारा परियोजना और कम संसाधन तैनाती को लागू करने में ठेकेदार में बदलें
---	--	---	--

viii) कोयला क्षेत्र में, 90 परियोजनाओं में से, 36 परियोजना विलंबित है। माह के दौरान, 1 परियोजना के संदर्भ में अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	विंड पावर परियोजना, काजहुनीरकुलम, तमिलनाडु एनएलसी	2	भूमि अधिग्रहण में विलंब, संसाधनों की आपूर्ति में विलंब तथा सिविल कार्यों में देरी

12. रेल मंत्रालय ने जुलाई, 2016 से मंत्रालय के ओसीएमएस पर 500 करोड़ और उससे अधिक लागत वाली (206 परियोजनाएं) चालू परियोजनाओं के आंकड़ा अपडेशन फिर से शुरू कर दिया गया है (जून 2016 की स्थिति के अनुसार)।

13. दिनांक 30.06.2016 की स्थिति के अनुसार, विभिन्न क्षेत्रों में रु. 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

14. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for June 2016 contains information on the status of the 1132 Central Sector Infrastructure Projects costing ₹150 crore and above. During June 2016, 1 project (Road & Transport Sector) has reported completion.

2. During the reference month, out of 1132 projects, 350 projects are delayed with respect to their original schedules and 72 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 72 projects, 30 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	417	127	30	13
2	RAILWAYS	345	38	9	4
3	POWER	112	62	11	5
4	COAL	90	36	1	0
5	PETROLEUM	74	41	11	5
6	STEEL	32	14	2	1
7	URBAN DEVELOPMENT	28	16	4	2
8	HEALTH AND FAMILY WELFARE	9	5	4	0
9	SHIPPING AND PORTS	8	3	0	0
10	CIVIL AVIATION	4	1	0	0
11	ATOMIC ENERGY	4	3	0	0
12	MINES	3	1	0	0
13	TELECOMMUNICATIONS	2	1	0	0
14	FERTILISERS	2	1	0	0
15	PETROCHEMICALS	1	0	0	0
16	HEAVY INDUSTRIES	1	1	0	0
Total		1132	350	72	30

3. Total original cost of implementation of the 1132 projects was ₹13,48,915.99 crore and their anticipated completion cost is likely to be ₹15,23,477.16 crore, which reflects overall cost overruns of ₹1,74,561.17 crore (12.94% of original cost). The expenditure incurred on these projects till June 2016 is ₹6,30,921.81 crore, which is 41.41% of the anticipated cost of the projects. The sector-wise

list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 30-06-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	16.86
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
5	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.02
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	82.49
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
3	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR	08/2010	103.02	171.04	66.03
4	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
5	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	462.79	49.38
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1441.52	290.95
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	177.39
3	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1581.04	175.45
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
5	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.57	139.32
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
2	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
3	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	5050.00	1939.09
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	9046.72	1143.43

5	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
2	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
5	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	156.63	276.00	76.21
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	66.82
4	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	235.15	18.20
5	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	5.66
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	39.29
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	17.79
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	17.50
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	14405.01	125.25
2	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-43 G BLOCK BANDRA	02/2011	241.33	356.59	47.76
3	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	5298.00	24.25

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 30-06-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	70.65
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
5	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.10
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	4504.39
PETROLEUM					
1	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
3	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	495.00
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	394.93
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	11149.82
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	5484.82
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.75	4479.16
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	3683.06
RAILWAYS					
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	9046.72	8319.16
3	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	5050.00	4802.34
4	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
5	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
2	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
4	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23

5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	164.16
4	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	235.15	36.21
5	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	13.83
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	302.09
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	31.22
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	26.21
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	14405.01	8010.01
2	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	5298.00	1034.00
3	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	356.59	115.26

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1132 projects, 5 projects are ahead of schedule, 259 are on schedule, 350 are delayed, 268 projects reported cost overrun and 87 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 297 if delay is calculated on the basis of latest schedule of completion. Further, 64 projects have been sanctioned without original commissioning date and for 454 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 350 delayed projects, 68 projects have overall delay in the range of 1 to 12 months, 58 projects have delay in the range of 13 to 24 months, 150 projects have delay in the range of 25 to 60 months and 74 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 30-06-2016)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2019	36
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11/2018	35

	CIVIL AVIATION				
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
	COAL				
1	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
2	MAGADH OC 20 MTY (CCL)	08/2008	07/2012	03/2021	104
3	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
4	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2018	72
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	09/2017	10
	HEALTH AND FAMILY WELFARE				
1	AIIMS-RAEBARELI-HOUSING	10/2013	11/2013	10/2016	35
2	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	12/2015	06/2016	6
3	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	07/2017	2
4	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	06/2017	1
5	AIIMS - OPD(NEW)	08/2014	05/2017	06/2017	1
	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	12/2017	75
	MINES				
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	09/2011	09/2017	04/2020	31
	PETROLEUM				
1	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	06/2009	12/2012	02/2019	74
2	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
3	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	03/2017	66
4	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	10/2016	64
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	09/2016	56
	POWER				
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	03/2017	128
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	06/2017	103
4	BARH STPP(3X660MW) NTPC	02/2005	01/2011	05/2018	88
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	03/2017	87
	RAILWAYS				
1	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
2	JAGGAYYAPET - MELLACHERUVU	04/2007	01/1999	06/2017	221
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
4	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	05/2008	03/2023	178
5	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
	ROAD TRANSPORT AND HIGHWAYS				
1	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2016	138
2	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	09/2007	03/2017	114
3	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	09/2016	108
4	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	12/2016	105
5	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2016	104
	SHIPPING AND PORTS				
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	07/2016	124

2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	12/2018	96
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	08/2016	88
STEEL					
1	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	12/2016	45
2	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	08/2016	34
3	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	12/2017	31
4	SMS-1 CONVERTERS REVAMPING	05/2012	07/2015	09/2017	26
5	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2017	24
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	09/2014	09/2014	03/2017	30
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	11/2016	65
2	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	03/2017	60
3	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	06/2016	37
4	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	11/2014	12/2017	37
5	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2017	31

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2016, out of 1061 projects on the monitor of this Ministry, 241 projects reported cost overruns and 326 projects reported time overruns; while during June 2016, out of 1132 projects, 268 projects reported cost overruns and 350 projects reported time overruns. In comparison to April 2016, number of projects reporting cost overrun has increased from 22.71% to 23.67% whereas projects reporting time overruns have increased from 30.73% to 30.92%.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones

(as on 30-06-2016)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIR	01/2009	309.46	309.46	433.19	01/2011	09/2017
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	318.00	305.59	05/2012	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	30.73	03/2015	09/2015
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRP	10/2013	314.61	314.61	26.30	09/2018	09/2018
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	74.76	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	2.56	09/2019	09/2019
3	MADANNAGAR OCP	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
4	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	198.68	0.00	03/2019	03/2019
5	BHATADI EXPANSION OC MINE	02/2016	304.52	304.52	0.00	03/2018	03/2018
FERTILISERS							
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	72.96	11/2016	09/2017
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	03/2016
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	414.11	210.92	11/2013	11/2014
3	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	444.70	444.70	400.00	12/2015	06/2016
4	AIIMS-RAEBARELI-HOUSING	10/2013	159.50	159.50	127.80	11/2013	10/2016
5	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	196.70	197.38	01/2016	04/2016
HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT	04/2011	1718.00	3827.30	2289.00	09/2011	12/2017
MINES							
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1176.00	12.44	09/2017	04/2020
2	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT	12/2015	344.50	344.50	0.00	11/2016	11/2016
PETROLEUM							
1	LPG IMPORT TERMINAL AT HALDIA	01/1991	694.00	694.00	57.19	10/2018	10/2018
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	1143.03	10/2011	04/2016
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1489.38	01/2012	09/2016
4	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	171.83	0.00	N.A.	N.A.
5	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	516.44	09/2011	03/2017
POWER							

1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	8540.30	09/2010	N.A.
2	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER	03/2012	198.63	198.63	112.53	09/2014	10/2016
3	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	27.60	04/2016	03/2017
4	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	141.80	04/2020	03/2022
5	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT	03/2015	197.40	197.40	3.30	03/2018	03/2018
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	0.00	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	496.00	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING G	04/1983	36.80	1336.57	259.15	N.A.	03/2019
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	1428.00	456.82	06/2005	12/2019
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	634.48	631.43	03/1994	02/2016
ROAD TRANSPORT AND HIGHWAYS							
1	"MADHUGIRI-MULBAGAL (KM 400.330 TO KM 483.151) - LOT-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	ANISABAD-AURANGABAD-HARIHARGANJ (KM 0.000 TO KM 62.000)- LOT	01/1991	282.41	282.41	75.32	08/2016	08/2016
3	ANISABAD-AURANGABAD-HARIHARGANJ (KM 62.000 TO KM 154.625) -	01/1991	358.22	358.22	200.21	10/2016	10/2016
4	BAKHTIYARPUR - MOKAMA	01/1991	1167.45	1167.45	0.00	N.A.	N.A.
5	BANKUARA- PURULIA (KM 0.000 TO KM 84.000)	01/1991	322.00	322.00	66.59	03/2018	03/2018
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI	10/2002	150.00	600.00	139.80	03/2006	07/2016
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF	01/2007	366.39	669.46	415.01	12/2010	12/2018
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	409.83	350.68	04/2009	08/2016
5	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED	09/2015	210.00	210.00	0.00	01/2018	01/2018
STEEL							
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1070.97	02/2014	03/2016
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	650.35	03/2015	03/2017
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER	03/2007	149.73	175.94	178.61	12/2015	03/2017
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER	12/2007	202.61	227.00	200.20	12/2016	12/2016
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERM	12/2007	200.00	200.00	136.15	03/2018	03/2018
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	13334.00	0.00	07/2015	N.A.

URBAN DEVELOPMENT							
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
2	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	261.85	261.85	199.73	05/2013	06/2016
3	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	165.23	165.23	0.00	10/2012	N.A.
4	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	205.00	191.97	108.07	03/2012	03/2017
5	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-4	02/2011	241.33	356.59	108.43	11/2014	12/2017

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 30-06-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	21674.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	4933.84
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	433.19
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	302.96	0.00	318.74
2	BALRAM OCP EXTENSION, MCL 8.00 MTY	12/2007	172.08	0.00	182.26
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	0.00	481.31
4	ADRIYALA SHAFT PROJECT	12/2009	212.34	0.00	880.45
HEALTH AND FAMILY WELFARE					
1	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	0.00	197.38
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	0.00	2289.00
PETROLEUM					
1	MARKETING TOP AT KORBA	01/2011	141.86	0.00	179.17
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5671.34
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	8540.30
3	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	2028.58

4	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	5679.02
5	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	4617.51
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	496.00
2	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	0.00	456.82
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	608.02	631.43
4	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT	04/1990	153.82	0.00	245.58
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	538.53
ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	427.01
2	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	0.00	277.36
3	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	200.36
4	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	399.08
5	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	12/2003	237.80	0.00	409.39
STEEL					
1	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.61
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	13845.01	13973.45
2	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	188.87	0.00	10255.48

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 30-06-2016)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	10/2013	05/2016
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	N.A.	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	N.A.	03/2016
2	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	N.A.	03/2016
3	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
4	PURNADIH OCP (3.0 MTY)	07/2008	03/2013	N.A.	03/2016
5	TAPIN OCP (2.5 MTY)	08/2008	03/2012	N.A.	03/2016
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2016
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
3	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	01/2016	N.A.	04/2016

PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2015	12/2015
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	N.A.	04/2016
2	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.A.	N.A.	N.A.
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	N.A.	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	02/2011	N.A.	03/2016
3	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
4	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	03/2010	11/2012	N.A.	05/2016
5	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW)	03/2010	01/2013	N.A.	03/2016
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	02/2016	02/2016
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	07/2014
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRAADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRAADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	01/1991	05/2016	N.A.	05/2016
3	REHABILITATION AND UPGRAADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
4	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	N.A.	N.A.	N.A.
5	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	N.A.	N.A.	N.A.
SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	03/2016
2	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	07/2011	12/2015	N.A.	04/2016
3	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW	08/2012	03/2016	N.A.	03/2016

	INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER				
4	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA	07/2014	01/1999	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	N.A.	N.A.
URBAN DEVELOPMENT					
1	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
2	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
3	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	N.A.	N.A.
4	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	N.A.	12/2015
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	01/2015	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

i) Road Transport & Highways Sector,

Out of 417 projects, 127 projects are delayed. During the month, the following 30 projects have reported additional delay in the range of 1-12 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	1	NR
2	NALBARI TO BIJNI (AS-6) NHAI	1	NR
3	JAIPUR-REENGUS NHAI	1	NR
4	BEAWAR PALI PINDWARA NHAI	1	NR
5	REENGUS SIKAR NHAI	1	NR
6	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR NHAI	1	NR
7	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION NHAI	1	NR
8	4 LANING OF GOMTI CHAURAHA - UDAIPUR NHAI	1	NR
9	4-LANING OF ROHTAK - HISSAR SECTION NHAI	1	NR
10	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) NHAI	1	NR

11	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	2	NR
12	INDORE-JHABUA-GUJRAT/MP NHAI	2	NR
13	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035- 144.740 KM NHAI	2	NR
14	4 LANNING OF AHMEDABAD TO GODHARA NHAI	2	NR
15	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY NHAI	2	NR
16	4-LANING OF BRAHAMPORE-FARAKA NHAI	2	NR
17	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA NHAI	2	NR
18	AGRA-BYPASS(NS-1/UP-1), NH-2,3 NHAI	3	NR
19	2-LANING WITH PS BHILWARA-LODPURA SECTION NHAI	3	NR
20	4-LANING OF FARAKA-RAIGANJ NHAI	4	NR
21	4-LANING OF ROHATAK JIND(LENGTH 45 KM) NHAI	5	NR
22	MURADABAD-BAREILY NHAI	6	NR
23	KANDLA - MUNDRA PORT NHAI	6	NR
24	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 NHAI	6	NR
25	AHMEDABAD TO VADODARA SECTION NHAI	6	NR
26	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 NHAI	6	NR
27	FOUR LANING OF GWALIOR-SHIVPURI NHAI	6	NR
28	ETAWAH CHAKERI NHAI	8	NR
29	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 NHAI	12	NR
30	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION NHAI	12	NR

NR: No specific reason has been reported by the project implementing agency for the delay in these projects

ii) Power Sector

Out of 112 projects, 62 projects are delayed. During the month, 11 projects have reported additional delay in the range of 1- 4 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	1	Land acquisition
2	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 PGCIL	1	Heavy Rain, land extremist problem
3	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION PGCIL	1	RoW, Heavy Rain, Fog
4	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH-PART A (PHASE-I) PGCIL	1	NR
5	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	2	Forest Clearance
6	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	2	Land acquisition, RoW
7	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B PGCIL	2	Heavy Rain, Land acquisition
8	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	2	NR
9	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	3	RoW, Huge compensation demand
10	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II PGCIL	3	RoW, forest clearance
11	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH PGCIL	4	Land clearance

NR: No specific reason has been reported by the project implementing agency for the delay in these projects

iii) In the **Petroleum Sector**, out of 74 projects, 41 projects are delayed. During the month, 11 projects have reported additional delays in the range of 1- 9 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN OIL	1	Land litigation
2	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE GAIL	1	Hostile public

3	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR IOCL	1	NR
4	CONSTRUCTION OF 6 ETPS ONGC	3	Slow progress in civil works
5	POLYPROPYLENE PLANT AT PARADIP REFINERY IOCL	3	NR
6	INTEGRATED REFINERY EXPANSION PROJECT BPCL	4	NR
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR ISPR	4	Heavy Rain
8	PARADIP-RAIPUR- RANCHI PIPELINE IOCL	6	Poor performance by contractor
9	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	6	Land acquisition
10	PALAKKAD LPG PLANT BPCL	6	NR
11	DE-BOTTLENECKING OF SMPL IOCL	9	Delay in forest clearance

NR: No specific reason has been reported by the project implementing agency for the delay in these projects

iv) In the **Railways Sector**, out of 345 projects, 38 projects are delayed. During the month, 9 projects have reported additional delays in the range of 8-46 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	RAJATGARH-BARANG(LD),ECOR RVNL	8	Contractual problem
2	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	12	Shortage of fund
3	AGARTALA-AKHAURA, NL NFR	16	Delay in administrative procedure as it's a joint venture project with Bangladesh
4	TAMLUK-BASULYA-SUTAHATA DOUBLING RVNL	23	NR
5	BHAIRABI -SAIRONG, NL, NEFR NFR	24	NR
6	KIRANDUL - JAGDALPUR DOUBLING ECOR	24	NR
7	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) NCR	34	NR
8	SAMBALPUR - ANGUL RLY. ELECTRIFICATION ECOR	39	NR

9	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR NCR	46	Delay in clearances from Government of Rajasthan
---	---	----	--

NR: No specific reason has been reported by the project implementing agency for the delay in these projects

- v) In the **Urban Development Sector**, out of 28 projects, 16 projects are delayed. During the month 4 projects have reported additional delays in the range of 2-17 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI CPWD	2	NR
2	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND CPWD	12	NR
3	BANGALORE METRO RAIL PROJECT PHASE-2 BMRCL	13	Land Acquisition
4	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD	17	NR

NR: No specific reason has been reported by the project implementing agency for the delay in these projects

- vi) In the **Health and Family Welfare Sector**, out of 9 projects, 5 projects are delayed. During the month 4 projects have reported additional delay in the range of 1-4 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	AIIMS-MOTHER AND CHILD BLOCK HSCC	1	Delay in release of fund, work suspended due to safety aspect
2	AIIMS-OPD (NEW) HSCC	1	Delay in release of fund, work suspended due to safety aspect
3	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR HSCC	2	Non-availability of fund in time, local protest for demanding employment

4	AIIMS-RAEBARELI-HOUSING HSCC	4	Delay in civil works, stoppage of work for demanding local employment and delay in deployment of MoHFW representative
---	---------------------------------	---	---

- vii) In the **Steel Sector**, out of 32 projects, 14 projects are delayed. During the month, 2 projects have reported additional delay in the range of 1-2 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	EXPANSION OF BHILAI STEEL PLANT SAIL	1	Delay in acquisition of non-forest land and inadequate mobilization by the contractor
2	INSTALLATION OF 45MVA SAFT WITH OTHER ASSOCIATED FACILITIES SAIL	2	Change in contractor in implementing project and less resource deployment by the contractor

- viii) In the **Coal Sector**, out of 90 projects, 36 projects are delayed. During the month following 1 project has reported additional delay.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU NLC	2	Delay in land acquisition, delay in supply of equipments and delay in civil works


12. Ministry of Railways has resumed the data updation of all its ongoing projects costing Rs.500 crore and above (206 projects) on the OCMS of this Ministry w.e.f. July 2016 (reporting month June 2016).

13. The status as on 30.06.2016 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

14. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	417	30
2	RAILWAYS	345	9
3	POWER	112	11
4	COAL	90	1
5	PETROLEUM	74	11
6	STEEL	32	2
7	URBAN DEVELOPMENT	28	4
8	HEALTH AND FAMILY WELFARE	9	4
9	SHIPPING AND PORTS	8	0
10	ATOMIC ENERGY	4	0
11	CIVIL AVIATION	4	0
12	MINES	3	0
13	FERTILISERS	2	0
14	TELECOMMUNICATIONS	2	0
15	PETROCHEMICALS	1	0
16	HEAVY INDUSTRY	1	0
	Total	1132	72

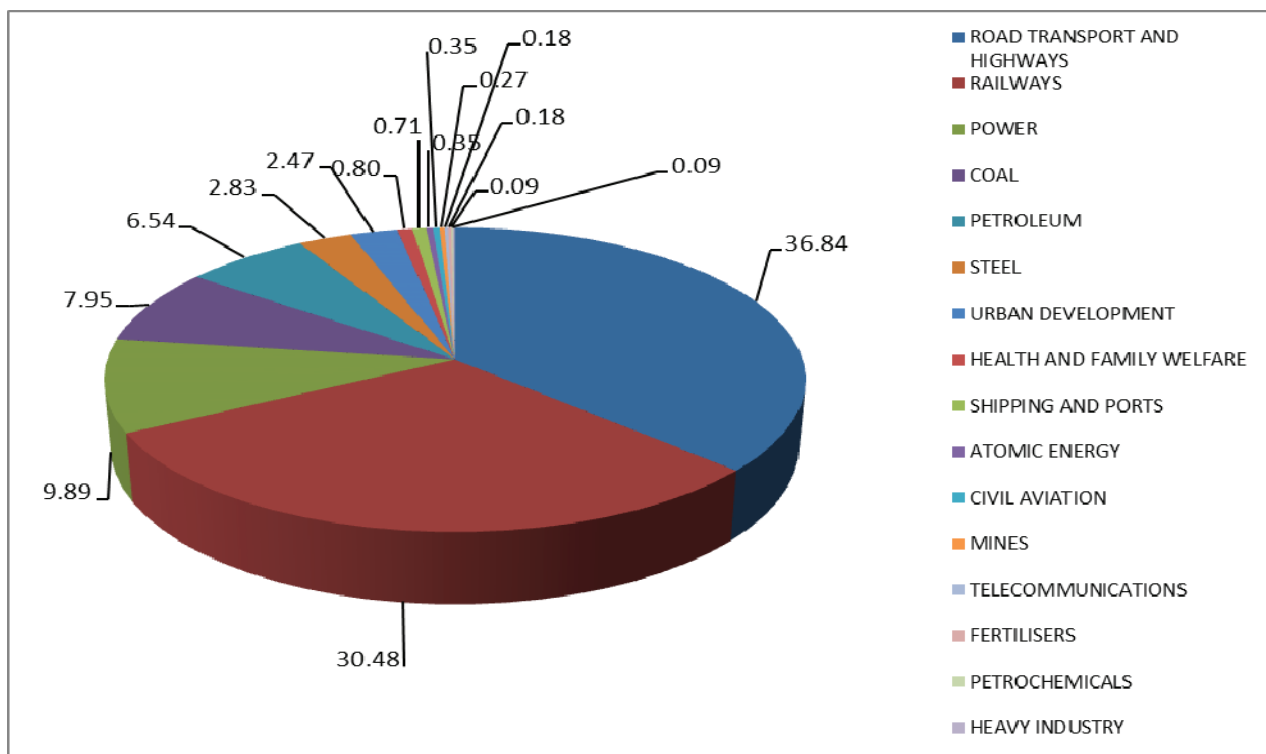

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April, 2016			
	<u>COAL</u>			
1	KRISHNASHILA (NCL) (4MTY) (NORTHERN COAL FIELDS LIMITED) - [N06000007]	789.88	03/2013	511.19
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) (NORTHERN COAL FIELDS LIMITED) - [N06000010]	1,352.04	03/2016	848.99
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
3	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100207]	157.47	09/2007	238.50
4	KOTA BYPASS,RJ-4, NH-76 (NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106297]	275.00	10/2008	184.63
5	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106304]	251.03	10/2008	326.30
6	SILIGURI TO ISLAMPUR (WB-7) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000028]	225.00	07/2008	191.00
7	NALBARI TO BIJNI (AS-8) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000035]	200.00	06/2008	281.60
8	GUWAHATI TO NALBARI (AS-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000046]	198.16	04/2008	242.40
9	DHARAMTUL TO SONAPUR (AS-19) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000051]	200.00	06/2008	289.50
10	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000107]	557.00	02/2010	932.30
11	KISHANGARH-AJMER-BEAWER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000128]	795.00	05/2012	1,512.11
12	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000132]	572.30	10/2011	761.40
13	JAIPUR-TONK-DEOLI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000135]	792.06	12/2012	1,983.00
14	HAZARIBAGH-RANCHI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000141]	625.07	01/2013	995.90
15	ARMUR TO KADLOOR YELLAREDDY (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000143]	390.56	02/2012	631.60
16	PANIPAT-ROHTAK (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000151]	807.00	10/2014	1,209.43
17	DEVIHALLI-HASSAN (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000152]	453.00	-	487.90
18	BELGAUM-DHARWAD(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000158]	480.00	-	438.00
19	UGRADATION OF HYDERABAD-BANGALORE SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000160]	680.00	-	188.40
20	2-LANNING OF SHILONG BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000181]	226.00	02/2014	282.30
21	BHOPAL-SANCHI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000192]	209.00	01/2013	11.28

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
22	PUNE-SHOLAPUR,PKG-II (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000193]	835.00	01/2014	1,684.00
23	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000196]	909.00	05/2014	844.10
24	LUCKNOW-RAIBAREILI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000207]	635.90	07/2012	616.50
25	NAGPUR-WAINGANGA BRIDGE (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000210]	484.19	10/2014	458.86
26	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000214]	682.00	10/2013	34.81
27	2 LANING WITH PS AGRA ALIGARH (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000220]	250.50	10/2014	65.30
28	2 LANING WITH PS KANPUR KABRAI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000221]	373.47	07/2014	358.30
29	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000237]	177.32	01/2016	86.50
30	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD(PUBLIC WORKS DEPT OF STATE) - [N24000304]	186.96	-	132.80
31	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000428]	569.38	06/2016	737.59
32	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000466]	285.00	01/2008	285.00
	May,2016			
	<u>STEEL</u>			
33	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000072]	572.00	04/2013	451.58
34	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000073]	898.55	05/2013	379.57
	<u>PETROLEUM</u>			
35	MOUNDED BULLET PROJECT AT CPCL (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000154]	279.00	12/2014	190.86
	<u>URBAN DEVELOPMENT</u>			
36	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000061]	225.81	06/2012	143.72
37	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000063]	171.10	09/2014	192.24
	June,2016			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
38	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000108]	232.45	09/2010	343.71

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2016			
	<u>URBAN DEVELOPMENT</u>			
1	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000066]	238.43	02/2015	.00


Summary of projects in the Flash Report for the month of June, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1076
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects Added in Current Month	57
Number of Projects in Current Month	1132


Brief Analysis

Project Status with respect to Original Schedule: Out of 1132 projects, 5 projects are ahead of schedule, 259 projects are on schedule 350 projects are delayed. 454 projects do not have fixed dates of commissioning. 64 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

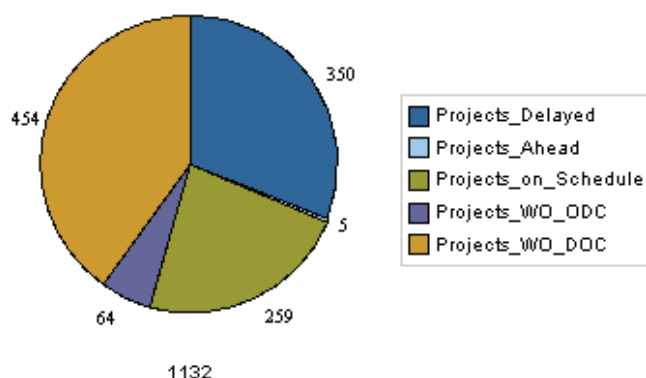

Investment Scenario

Total original cost of implementation of 1132 projects when sanctioned, was of the order of Rs. 1348915.99 crore but this was subsequently revised to Rs. 1523477.16 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till June, 2016 is Rs. 630921.81 crore, which is 41.4% of the revised cost of the projects.

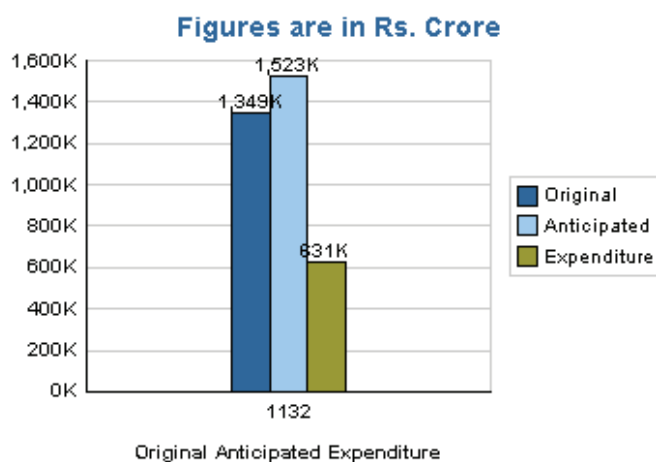

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	1076
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	57
No of Projects in Current Month	1132

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	350	5	259	64	454	1132	30.92
Latest Approved (Date)	297	8	309	64	454	1132	26.24

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	970	11,54,362.88	12,28,486.25	4,45,593.67	36.30	74,123.37	6.40
Project with Revision in Cost	162	2,75,212.93	2,94,990.91	1,85,328.14	62.80	19,777.98	7.20
Total	1,132	14,29,575.81	15,23,477.16	6,30,921.81	41.41	93901.35	6.57
Original Cost of All Projects							
Original Cost	1132	13,48,915.99	15,23,477.16	6,30,921.81	41.41	1,74,561.17	12.94

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	350	539,814.17	652,028.62	430,372.46	66.00	112,214.45	20.80
Latest Approved (RCE)	297	449,994.74	513,274.12	344,724.20	67.20	63,279.38	14.10

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	72	122,660.86	135,135.73	90,042.54	66.60	12,474.87	10.20

Extent of cost overrun in projects with respect to original schedule (Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun[^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	90	69,573.40	70,943.19	1.97	5	1,800.69	3,170.48	76.07
4	FERTILISERS	2	680.64	692.29	1.71	1	197.79	209.44	5.89
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	32	53,059.66	53,588.97	1.00	5	1,639.71	2,169.02	32.28
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	74	110,511.66	114,415.93	3.53	15	29,610.77	35,468.03	19.78
9	POWER	112	315,179.00	364,677.74	15.71	26	66,934.70	116,497.05	74.05
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	345	328,791.74	417,811.40	27.07	183	86,647.35	235,423.29	171.70
13	ROAD TRANSPORT AND HIGHWAYS	417	263,809.81	266,605.47	1.06	20	7,401.67	10,442.08	41.08
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	5	1,205.50	2,172.77	80.24
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	28	133,830.49	142,976.73	6.83	3	10,900.33	20,059.60	84.03
Total		1132	1,348,915.99	1,523,477.16	12.94	268	230,397.72	467,787.16	103.03

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to original schedule (State Wise)									
(All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun[^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	52	35,777.87	38,197.40	6.76	6	1,478.20	4,490.85	203.81
2	ARUNACHAL PRADESH	15	12,006.22	28,062.52	133.73	5	9,616.85	25,673.15	166.96
3	ASSAM	53	37,126.96	52,848.03	42.34	14	15,918.17	31,739.95	99.39
4	BIHAR	74	65,405.30	79,584.72	21.68	16	14,069.88	29,034.84	106.36
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	0.00
6	GUJARAT	41	36,708.85	39,153.30	6.66	11	5,242.79	7,814.56	49.05
7	HARYANA	17	12,170.13	14,140.75	16.19	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	6	8,361.75	14,761.02	76.53	2	4,966.47	11,365.74	128.85
9	JAMMU AND KASHMIR	9	25,620.25	44,826.38	74.96	2	6,142.04	25,348.17	312.70
10	KARNATAKA	39	70,774.99	88,393.13	24.89	19	15,313.82	34,078.99	122.54
11	KERALA	16	25,575.79	30,170.84	17.97	8	17,335.36	21,930.41	26.51
12	MADHYA PRADESH	47	51,315.42	55,759.38	8.66	7	4,634.35	9,766.85	110.75
13	MAHARASHTRA	94	152,704.24	161,995.06	6.08	17	18,848.13	30,448.91	61.55
14	MANIPUR	3	1,047.27	9,434.45	800.86	2	830.58	9,217.76	1009.79
15	MEGHALAYA	5	6,744.03	8,661.01	28.42	1	4,083.02	6,000.00	46.95
16	MIZORAM	5	2,001.20	5,274.91	163.59	2	988.06	4,261.77	331.33
17	NAGALAND	3	6,420.00	8,083.30	25.91	1	850.00	2,513.30	195.68
18	ODISHA	50	48,425.99	54,018.33	11.55	13	4,023.23	9,663.96	140.20
19	PUNJAB	23	11,796.33	11,800.33	0.03	1	573.96	605.00	5.41
20	RAJASTHAN	61	42,046.69	42,992.29	2.25	9	3,810.47	4,816.99	26.41
21	SIKKIM	5	2,149.08	4,894.32	127.74	1	1,339.48	4,085.00	204.97
22	TAMIL NADU	61	71,126.10	92,172.95	29.59	24	24,329.86	45,376.71	86.51
23	TRIPURA	9	3,776.07	7,783.63	106.13	7	2,909.18	6,916.74	137.76
24	UTTAR PRADESH	68	65,276.33	69,354.71	6.25	9	3,100.25	7,178.63	131.55
25	WEST BENGAL	49	51,751.33	65,273.19	26.13	14	8,788.66	24,561.97	179.47
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	16	49,997.48	51,031.48	2.07	1	4,264.00	5,298.00	24.25
28	CHHATISGARH	40	96,051.60	97,695.19	1.71	6	5,305.85	6,949.44	30.98
29	JHARKHAND	44	43,279.92	46,068.51	6.44	7	4,385.23	7,215.56	64.54
30	UTTARAKHAND	8	11,515.40	13,814.71	19.97	3	4,855.31	7,155.13	47.37
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
32	TELANGANA	37	27,647.71	31,047.68	12.30	9	2,836.21	6,324.39	122.99
33	MULTI STATE	172	263,989.52	245,875.08	-6.86	48	37,924.75	74,350.21	96.05
Total		1132	1,348,915.99	1,523,477.16	12.94	268	230,397.72	467,787.16	103.03

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	3	27,271.00	29,456.00	35 - 72
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	90	69,573.40	70,943.19	1.97	36	19,565.35	19,919.09	6 - 132
4	FERTILISERS	2	680.64	692.29	1.71	1	197.79	209.44	10 - 10
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	32	53,059.66	53,588.97	1.00	14	38,281.71	38,484.54	5 - 45
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	74	110,511.66	114,415.93	3.53	41	63,570.50	67,396.54	1 - 74
9	POWER	112	315,179.00	364,677.74	15.71	62	159,197.89	191,405.01	2 - 128
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	5	1,271.19	1,271.19	1 - 35
12	RAILWAYS	345	328,791.74	417,811.40	27.07	38	40,070.71	100,711.60	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	417	263,809.81	266,605.47	1.06	127	94,530.45	96,958.86	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	3	762.06	1,679.29	88 - 124
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	2,111.17	2,011.17	30 - 30
16	URBAN DEVELOPMENT	28	133,830.49	142,976.73	6.83	16	89,100.89	97,213.13	4 - 65
Total		1132	1,348,915.99	1,523,477.16	12.94	350	539,814.17	652,028.62	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of time overrun in projects with respect to original schedule (State Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	52	35,777.87	38,197.40	6.76	20	9,804.85	10,761.49	2 - 106
2	ARUNACHAL PRADESH	15	12,006.22	28,062.52	133.73	2	3,070.89	7,761.00	40 - 87
3	ASSAM	53	37,126.96	52,848.03	42.34	22	12,931.43	19,662.43	21 - 138
4	BIHAR	74	65,405.30	79,584.72	21.68	15	20,764.40	28,343.39	8 - 94
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	-
6	GUJARAT	41	36,708.85	39,153.30	6.66	14	22,256.50	22,132.56	5 - 84
7	HARYANA	17	12,170.13	14,140.75	16.19	6	4,089.45	5,269.45	1 - 79
8	HIMACHAL PRADESH	6	8,361.75	14,761.02	76.53	2	4,190.42	8,669.58	28 - 111
9	JAMMU AND KASHMIR	9	25,620.25	44,826.38	74.96	7	21,314.62	40,520.75	10 - 193
10	KARNATAKA	39	70,774.99	88,393.13	24.89	9	51,138.53	59,320.62	2 - 65
11	KERALA	16	25,575.79	30,170.84	17.97	6	16,871.73	20,122.08	4 - 88
12	MADHYA PRADESH	47	51,315.42	55,759.38	8.66	10	7,341.14	8,547.19	11 - 120
13	MAHARASHTRA	94	152,704.24	161,995.06	6.08	21	39,022.37	42,935.18	1 - 96
14	MANIPUR	3	1,047.27	9,434.45	800.86	3	1,047.27	9,434.45	1 - 96
15	MEGHALAYA	5	6,744.03	8,661.01	28.42	1	536.00	536.00	41 - 41
16	MIZORAM	5	2,001.20	5,274.91	163.59	2	988.06	4,261.77	71 - 128
17	NAGALAND	3	6,420.00	8,083.30	25.91	1	850.00	2,513.30	60 - 60
18	ODISHA	50	48,425.99	54,018.33	11.55	17	10,441.50	10,932.13	5 - 94
19	PUNJAB	23	11,796.33	11,800.33	0.03	1	523.85	523.85	14 - 14
20	RAJASTHAN	61	42,046.69	42,992.29	2.25	16	21,825.81	21,896.49	4 - 87
21	SIKKIM	5	2,149.08	4,894.32	127.74	2	1,648.94	4,394.46	51 - 80
22	TAMIL NADU	61	71,126.10	92,172.95	29.59	21	39,940.98	43,030.48	4 - 124
23	TRIPURA	9	3,776.07	7,783.63	106.13	3	1,138.56	3,258.65	7 - 48
24	UTTAR PRADESH	68	65,276.33	69,354.71	6.25	16	18,380.87	20,536.53	9 - 108
25	WEST BENGAL	49	51,751.33	65,273.19	26.13	19	30,260.55	33,385.16	2 - 177
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
27	DELHI	16	49,997.48	51,031.48	2.07	6	40,194.65	40,194.65	1 - 37
28	CHHATISGARH	40	96,051.60	97,695.19	1.71	15	52,473.99	53,365.40	15 - 93
29	JHARKHAND	44	43,279.92	46,068.51	6.44	16	9,533.40	11,683.91	7 - 104
30	UTTARAKHAND	8	11,515.40	13,814.71	19.97	4	7,605.57	9,794.74	35 - 78
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	37	27,647.71	31,047.68	12.30	13	5,476.78	5,787.12	6 - 132
33	MULTI STATE	172	263,989.52	245,875.08	-6.86	59	78,064.98	96,367.73	1 - 261
Total		1132	1,348,915.99	1,523,477.16	12.94	350	539,814.17	652,028.62	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of time overrun in projects with respect to latest schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	23,779.00	23,779.00	35 - 36
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	90	69,573.40	70,943.19	1.97	32	10,710.40	10,836.97	6 - 132
4	FERTILISERS	2	680.64	692.29	1.71	0	0.00	0.00	-
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	32	53,059.66	53,588.97	1.00	13	22,756.71	22,959.54	5 - 45
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	74	110,511.66	114,415.93	3.53	19	29,733.28	32,307.12	1 - 74
9	POWER	112	315,179.00	364,677.74	15.71	56	134,278.12	150,365.16	2 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	5	1,271.19	1,271.19	1 - 35
12	RAILWAYS	345	328,791.74	417,811.40	27.07	30	30,418.22	85,678.18	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	417	263,809.81	266,605.47	1.06	123	93,768.88	96,105.34	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	395.67	1,009.83	88 - 124
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	2,111.17	2,011.17	30 - 30
16	URBAN DEVELOPMENT	28	133,830.49	142,976.73	6.83	11	81,535.63	81,637.86	8 - 60
Total		1132	1,348,915.99	1,523,477.16	12.94	297	434,641.73	513,274.12	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	44,541.00	51,918.00	16.56	2	20,762.00	28,139.00	35.53
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	90	69,800.57	70,943.19	1.64	4	1,541.29	2,683.91	74.13
4	FERTILISERS	2	692.29	692.29	0.00	0	0.00	0.00	0.00
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	32	53,440.63	53,588.97	0.28	2	516.00	664.34	28.75
7	PETROCHEMICALS	1	9,965.00	9,965.00	0.00	0	0.00	0.00	0.00
8	PETROLEUM	74	111,638.98	114,415.93	2.49	5	17,261.99	20,256.25	17.35
9	POWER	112	344,706.00	364,677.74	5.79	8	29,710.09	49,681.83	67.22
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	345	359,265.98	417,811.40	16.30	151	83,829.75	201,206.59	140.02
13	ROAD TRANSPORT AND HIGHWAYS	417	265,684.89	266,605.47	0.35	16	6,318.32	8,899.42	40.85
14	SHIPPING AND PORTS	8	5,048.11	5,085.02	0.73	2	631.22	668.16	5.85
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	28	141,333.13	142,976.73	1.16	3	18,251.38	19,894.98	9.01
Total		1132	1,429,575.81	1,523,477.16	6.57	195	180,757.64	336,165.88	85.98

[^] - Cost Overrun = Anticipated Cost minus Latest Approved Cost.

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	0	0.00	0.00	0- 0
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	90	69,573.40	70,943.19	1.97	3	1,328.95	1,455.52	24- 132
4	FERTILISERS	2	680.64	692.29	1.71	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	32	53,059.66	53,588.97	1.00	2	492.73	664.34	8- 15
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	74	110,511.66	114,415.93	3.53	1	14,225.00	16,504.00	4- 4
9	POWER	112	315,179.00	364,677.74	15.71	5	11,238.50	21,058.82	4- 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	345	328,791.74	417,811.40	27.07	23	13,832.71	67,964.40	21- 261
13	ROAD TRANSPORT AND HIGHWAYS	417	263,809.81	266,605.47	1.06	9	4,598.85	6,936.33	13- 97
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	1	245.67	409.83	88- 88
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	28	133,830.49	142,976.73	6.83	1	205.00	191.97	60- 60
Total		1132	1348915.99	1523477.16	12.94	46	47885.41	119012.51	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest approved Cost

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	1	3,492.00	5,677.00	72- 72
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	90	69,573.40	70,943.19	1.97	4	1,588.35	1,942.09	24- 132
4	FERTILISERS	2	680.64	692.29	1.71	1	197.79	209.44	10- 10
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	32	53,059.66	53,588.97	1.00	3	668.22	871.05	7- 15
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	74	110,511.66	114,415.93	3.53	11	21,359.22	26,314.56	1- 56
9	POWER	112	315,179.00	364,677.74	15.71	21	53,626.76	85,897.49	10- 128
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	345	328,791.74	417,811.40	27.07	30	23,121.82	85,138.50	21- 261
13	ROAD TRANSPORT AND HIGHWAYS	417	263,809.81	266,605.47	1.06	10	4,816.46	7,245.89	13- 97
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	3	762.06	1,679.29	88- 124
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	28	133,830.49	142,976.73	6.83	2	6,636.33	14,761.60	37- 65
Total		1132	1348915.99	1523477.16	12.94	87	117987.01	233564.21	

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

State-Wise Position of Central Sector Projects costing Rs. 150 crore and above showing both Time and Cost Overruns (as on 01.07.2016)								
Total number of Projects					Projects with both Time and Cost overrun			
S.N.	State	No. of Projects	Original Cost (Rs. Crore)	Anticipated Cost (Rs. Crore)	No. of Projects	Original Cost (Rs. Crore)	Anticipated Cost (Rs. Crore)	Range of Time Overrun (months)
1	ANDHRA PRADESH	52	35777.87	38197.40	2	498.74	1455.38	8- 106
2	ARUNACHAL PRADESH	15	12006.22	28062.52	2	3070.89	7761.00	40- 87
3	ASSAM	53	37126.96	52848.03	8	7795.16	14612.42	21- 110
4	BIHAR	74	65405.30	79584.72	2	9185.95	16822.94	87- 88
5	GOA	8	3925.48	3907.87	0	0.00	0.00	0- 0
6	GUJARAT	41	36708.85	39153.30	1	318.24	321.62	84- 84
7	HARYANA	17	12170.13	14140.75	1	1108.00	2288.00	61- 61
8	HIMACHAL PRADESH	6	8361.75	14761.02	1	3919.59	8398.75	111- 111
9	JAMMU AND KASHMIR	9	25620.25	44826.38	2	6142.04	25348.17	10- 193
10	KARNATAKA	39	70774.99	88393.13	2	7061.00	15243.09	12- 65
11	KERALA	16	25575.79	30170.84	4	16070.73	19321.08	4- 88
12	MADHYA PRADESH	47	51315.42	55759.38	5	3779.64	5665.69	13- 120
13	MAHARASHTRA	94	152704.24	161995.06	7	9504.62	13882.38	10- 96
14	MANIPUR	3	1047.27	9434.45	2	830.58	9217.76	1- 96
15	MEGHALAYA	5	6744.03	8661.01	0	0.00	0.00	0- 0
16	MIZORAM	5	2001.20	5274.91	2	988.06	4261.77	71- 128
17	NAGALAND	3	6420.00	8083.30	1	850.00	2513.30	60- 60
18	ODISHA	50	48425.99	54018.33	4	929.00	1419.63	21- 94
19	PUNJAB	23	11796.33	11800.33	0	0.00	0.00	0- 0
20	RAJASTHAN	61	42046.69	42992.29	3	1238.19	1309.38	46- 87
21	SIKKIM	5	2149.08	4894.32	1	1339.48	4085.00	51- 51
22	TAMIL NADU	61	71126.10	92172.95	4	5608.55	8698.05	47- 124
23	TRIPURA	9	3776.07	7783.63	3	1138.56	3258.65	7- 48

24	UTTAR PRADESH	68	65276.33	69354.71	2	480.00	2635.66	84- 93
25	WEST BENGAL	49	51751.33	65273.19	4	1638.27	6371.59	42- 177
26	D & N HAVELI	1	6086.08	6086.08	0	0.00	0.00	0- 0
27	DELHI	16	49997.48	51031.48	0	0.00	0.00	0- 0
28	CHHATISGARH	40	96051.60	97695.19	3	4033.42	4924.83	30- 93
29	JHARKHAND	44	43279.92	46068.51	2	3213.05	5363.56	57- 99
30	UTTARAKHAND	8	11515.40	13814.71	2	4635.48	6825.16	43- 75
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0	0.00	0.00	0- 0
32	TELANGANA	37	27647.71	31047.68	3	1482.10	1792.44	21- 132
33	MULTI STATE	172	263989.52	245875.08	14	21127.67	39766.91	15- 261
TOTAL		1132	1348915.99	1523477.16	87	117987.01	233564.21	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
1	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	12/2003	232.45	09/2010	232.45	06/2016	343.71

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	198.68	3/2019	198.68	3/2019
2	BHATADI EXPANSION OC MINE	2/2016	304.52	3/2018	304.52	3/2018
	<u>RAILWAYS</u>					
3	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	1,750.00	3/2022	1,750.00	3/2022
4	GULBARGA-BIDAR	4/1994	844.15	/	1,542.42	-
5	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	1,491.47	12/2020	1,491.47	12/2020
6	KIUL - GAYA DOUBLING PROJECT	12/2015	1,200.20	12/2020	1,200.20	12/2020
7	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	1,762.94	12/2020	1,762.94	12/2020
8	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	9,968.00	/	9,968.00	-
9	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	2,750.00	/	2,750.00	-
10	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	2,326.00	/	2,326.00	-
11	PUNE-MIRAJ-LONDA (467 KM)	2/2015	4,670.00	/	3,627.00	-
12	VIJAYAWADA-GUDUR	4/2015	3,246.26	/	3,246.26	-
13	GUNTUR-GUNTAKAL	4/2016	4,000.00	/	3,571.00	-
14	DUVVADA-VIJAYAWADA	4/2015	3,873.07	/	3,873.07	-
15	KAZIPET-VIJAYAWADA III RD LINE WITH ELECTRIFICATION	4/2012	1,820.50	/	1,820.50	-
16	KONDAPALLI-KOTHAGUDEM	4/2013	616.08	/	616.08	-
17	GUDUR-DURGARAJU PATNAM	4/2010	760.17	/	760.17	-
18	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	912.00	/	912.00	-
19	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	854.00	/	854.00	-
20	DAUND - MANMAD (236 KM)	2/2016	1,876.00	/	1,876.00	-
21	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT	4/1990	153.82	3/2019	551.82	3/2019
22	HARMUTI-NAHARLAGUN	4/2096	614.54	/	614.54	-
23	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	1,172.92	3/2021	1,172.92	3/2021
24	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	701.61	3/2021	701.61	3/2021
25	DUDHNOI-MENDHIPATHAR	4/1992	315.64	/	315.64	-
26	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	2,361.74	3/2021	2,361.74	3/2021
27	KOTTAVALSA - KORAPUT DOUBLING	4/2015	2,499.71	3/2021	2,499.71	3/2021
28	JAGADALPUR-KORAPUT DOUBLING	4/2015	1,547.38	3/2021	1,547.38	3/2021
29	INDORE-DEWAS-UJJAIN(80 KM) DL	4/2016	600.00	/	600.00	-
30	KAZIPET-BALHRSHA	4/2015	2,063.03	/	2,063.03	-
31	INDORE DEWAS UJJAIN (80 KM)	4/2016	600.00	/	600.00	-
32	SURENDRA NAGAR RAJKOT	4/2015	1,002.39	/	1,002.39	-
33	VIRAMGAM BHILDI	4/1990	237.13	3/2018	237.13	3/2018
34	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF	4/2016	556.31	/	556.31	-

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	REMAINING PORTION (51.65 KM)					
35	DIGARU-HOJAI (102 KM)	4/2015	870.96	/	870.96	-
36	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	2,232.32	/	2,232.32	-
37	NEW GUWAHATI-DIGARU-PATCH DOUBLING	4/2007	180.09	/	180.09	-
38	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	4/2003	4,300.00	/	4,300.00	-
39	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM)	4/2093	971.22	/	971.22	-
40	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	332.15	7/2014	559.91	7/2014
41	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	187.26	4/2014	233.73	3/2018
42	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	524.00	3/2020	668.00	3/2020
43	SECUNDERABAD-MOHABOBNAGAR	4/2015	728.10	/	728.10	-
44	GOOTY-DHARMAVARAM-BANGLORE	4/2015	636.38	/	636.38	-
45	MANOHARABAD-KOTAPALLI	4/2006	1,160.47	/	1,160.47	-
46	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	630.00	/	1,272.00	-
47	PUNE-NASIK (265 KM)	2/2016	2,425.00	/	2,425.00	-
48	BARAMATI - LONAND (54 KM)	2/1998	75.00	/	736.00	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
49	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	294.17	1/2016	294.17	1/2016
50	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	252.00	1/2016	252.00	1/2016
51	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	763.23	6/2019	763.23	6/2019
52	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	649.00	6/2019	649.00	6/2019
53	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	581.84	5/2017	581.84	5/2017
54	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM	6/2016	725.95	6/2019	725.95	6/2019
55	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	637.18	6/2019	637.18	6/2019
56	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	1,101.58	/	1,101.58	-

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>STEEL</u>					
57	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	818.00	6/2020	818.00	6/2020

Milestones (Cumulative due & achieved)

Total	3954
Achieved up to month	1793

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU NLC	364.75	364.75	10/2014	06/2016	08/2016	2
	<u>STEEL</u>						
2	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	11/2016	12/2016	1
3	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES SAIL	187.33	187.33	10/2013	06/2016	08/2016	2
	<u>PETROLEUM</u>						
4	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN OIL	352.56	439.03	03/2017	05/2018	06/2018	1
5	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE GAIL	419.04	419.04	01/2017	06/2016	07/2016	1
6	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR IOCL	103.02	171.04	07/2016	07/2016	08/2016	1
7	CONSTRUCTION OF 6 ETPS ONGC	317.64	240.95	09/2012	06/2016	09/2016	3
8	POLYPROPYLENE PLANT AT PARADIP REFINERY IOCL	3,150.00	3,150.00	09/2017	12/2017	03/2018	3
9	INTEGRATED REFINERY EXPANSION PROJECT BPCL	14,225.00	16,504.00	05/2016	05/2016	09/2016	4
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR ISPRL	993.00	1,693.00	01/2012	05/2016	09/2016	4
11	PARADIP-RAIPUR- RANCHI PIPELINE IOCL	1,793.00	1,793.00	09/2012	06/2016	12/2016	6
12	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	586.00	586.00	08/2015	06/2016	12/2016	6
13	PALAKKAD LPG PLANT BPCL	184.00	184.00	06/2017	06/2017	12/2017	6
14	DE-BOTTLENECKING OF SMPL IOCL	1,584.00	1,584.00	03/2017	06/2016	03/2017	9
	<u>POWER</u>						
15	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	250.03	390.51	01/2013	06/2016	07/2016	1

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 PGCIL	558.26	558.26	11/2013	06/2016	07/2016	1
17	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION PGCIL	198.63	198.63	09/2014	09/2016	10/2016	1
18	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) PGCIL	312.94	312.94	05/2016	06/2016	07/2016	1
19	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,422.85	1,422.85	01/2015	10/2016	12/2016	2
20	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	9,569.76	9,569.76	06/2015	12/2016	02/2017	2
21	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B PGCIL	3,201.44	3,201.44	10/2014	06/2016	08/2016	2
22	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	05/2015	06/2016	08/2016	2
23	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	346.79	08/2014	09/2016	12/2016	3
24	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II PGCIL	1,575.30	1,575.30	05/2016	09/2016	12/2016	3
25	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH PGCIL	1,961.87	2,310.58	05/2014	07/2016	11/2016	4
HEALTH AND FAMILY WELFARE							
26	AIIMS - MOTHER AND CHILD BLOCK HSCC	204.44	204.44	05/2017	05/2017	06/2017	1
27	AIIMS - OPD(NEW) HSCC	293.65	293.65	05/2017	05/2017	06/2017	1
28	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR HSCC	168.90	168.90	05/2017	05/2017	07/2017	2
29	AIIMS-RAEBARELI-HOUSING HSCC	159.50	159.50	11/2013	06/2016	10/2016	4
RAILWAYS							
30	RAJATGARH-BARANG(LD),ECOR RVNL	166.16	370.00	02/2009	04/2016	12/2016	8
31	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR NFR	300.00	837.73	N.A.	03/2019	03/2020	12


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
32	AGARTALA-AKHAURA NL NFR	252.00	972.52	N.A.	03/2018	07/2019	16
33	TAMLUK-BASULYA-SUTAHATA DOUBLING RVNL	171.02	235.00	06/2013	01/2015	12/2016	23
34	BHAIRABI SAIRONG, NL, NEFR NFR	619.34	2,820.25	04/2014	03/2018	03/2020	24
35	KIRANDUL - JAGDALPUR DOUBLING ECOR	826.57	1,160.83	N.A.	03/2018	03/2020	24
36	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) NCR	1,176.09	3,845.60	02/2020	02/2020	12/2022	34
37	SAMBALPUR - ANGUL RLY. ELECTRIFICATION ECOR	155.81	238.03	N.A.	12/2016	03/2020	39
38	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR NCR	622.41	2,030.50	02/2019	02/2019	12/2022	46
ROAD TRANSPORT AND HIGHWAYS							
39	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) NHAI	237.80	237.80	06/2008	06/2016	07/2016	1
40	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	06/2016	07/2016	1
41	JAIPUR-REENGUS NHAI	267.81	267.81	02/2013	06/2016	07/2016	1
42	BEAWAR PALI PINDWARA NHAI	2,388.51	2,388.00	06/2014	06/2016	07/2016	1
43	REENGUS SIKAR NHAI	333.51	333.51	09/2014	06/2016	07/2016	1
44	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR NHAI	158.04	158.04	12/2015	06/2016	07/2016	1
45	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION NHAI	368.15	368.15	01/2016	06/2016	07/2016	1
46	4 LANING OF GOMTI CHAURAHA - UDAIPUR NHAI	914.50	914.50	10/2015	06/2016	07/2016	1
47	4-LANING OF ROHTAK - HISSAR SECTION NHAI	959.25	959.25	06/2016	06/2016	07/2016	1
48	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) NHAI	1,673.70	1,673.70	10/2011	06/2016	07/2016	1
49	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	280.00	361.00	02/2009	06/2016	08/2016	2
50	INDORE-JHABUA-GUJRAT/MP NHAI	1,175.00	1,206.10	04/2013	10/2016	12/2016	2
51	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM NHAI	852.00	852.00	03/2013	06/2016	08/2016	2
52	4 LANNING OF AHMEDABAD TO GODHARA NHAI	1,008.50	1,008.50	06/2013	06/2016	08/2016	2


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
53	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY NHAI	600.00	600.00	06/2013	06/2016	08/2016	2
54	4-LANING OF BRAHAMPORE-FARAKA NHAI	998.79	998.79	08/2013	07/2017	09/2017	2
55	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA NHAI	677.79	677.79	04/2016	06/2016	08/2016	2
56	AGRA-BYPASS(NS-1/UP-1), NH-2,3 NHAI	348.16	348.16	09/2007	06/2016	09/2016	3
57	2-LANING WITH PS BHILWARA-LODPURA SECTION NHAI	240.10	240.10	03/2016	06/2016	09/2016	3
58	4-LANING OF FARAKA-RAIGANJ NHAI	1,078.84	1,078.84	08/2013	08/2016	12/2016	4
59	4-LANING OF ROHATAK JIND(LENGTH 45 KM) NHAI	283.25	283.25	10/2015	12/2016	05/2017	5
60	MURADABAD-BAREILLY NHAI	1,267.00	1,267.00	06/2013	06/2016	12/2016	6
61	KANDLA - MUNDRA PORT NHAI	953.88	953.88	07/2013	06/2016	12/2016	6
62	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 NHAI	1,535.00	1,535.00	05/2014	06/2016	12/2016	6
63	AHMEDABAD TO VADODARA SECTION NHAI	2,125.24	2,125.24	12/2015	06/2016	12/2016	6
64	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 NHAI	1,266.60	1,266.60	09/2016	09/2016	03/2017	6
65	FOUR LANING OF GWALIOR-SHIVPURI NHAI	1,055.00	1,601.77	11/2015	06/2016	12/2016	6
66	ETAWAH CHAKERI NHAI	1,573.00	1,573.00	09/2015	06/2016	02/2017	8
67	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 NHAI	1,348.20	1,348.20	02/2014	08/2016	08/2017	12
68	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION NHAI	1,655.01	1,655.01	08/2016	08/2016	08/2017	12
	<u>URBAN DEVELOPMENT</u>						
69	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI CPWD	405.01	405.01	12/2014	10/2016	12/2016	2
70	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND CPWD	270.83	270.83	11/2014	03/2016	03/2017	12

List of projects reporting additional delays							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
71	BANGALORE METRO RAIL PROJECT PHASE-2 BMRCL	26,405.14	26,405.14	02/2019	02/2019	03/2020	13
72	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD	1,219.21	1,219.21	10/2019	07/2017	12/2018	17

Graphical Presentation of All Projects w.r.t. Original Schedule

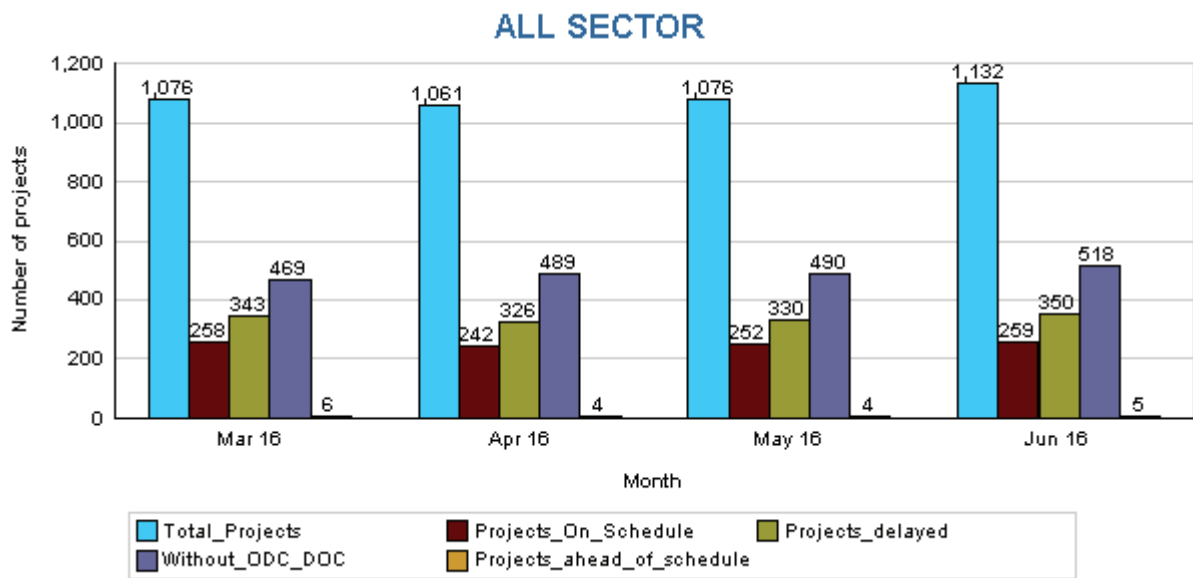


Break-up of 350 Delayed projects in June 2016

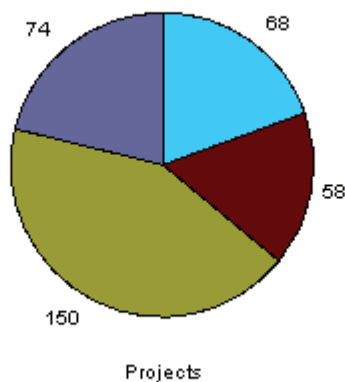


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

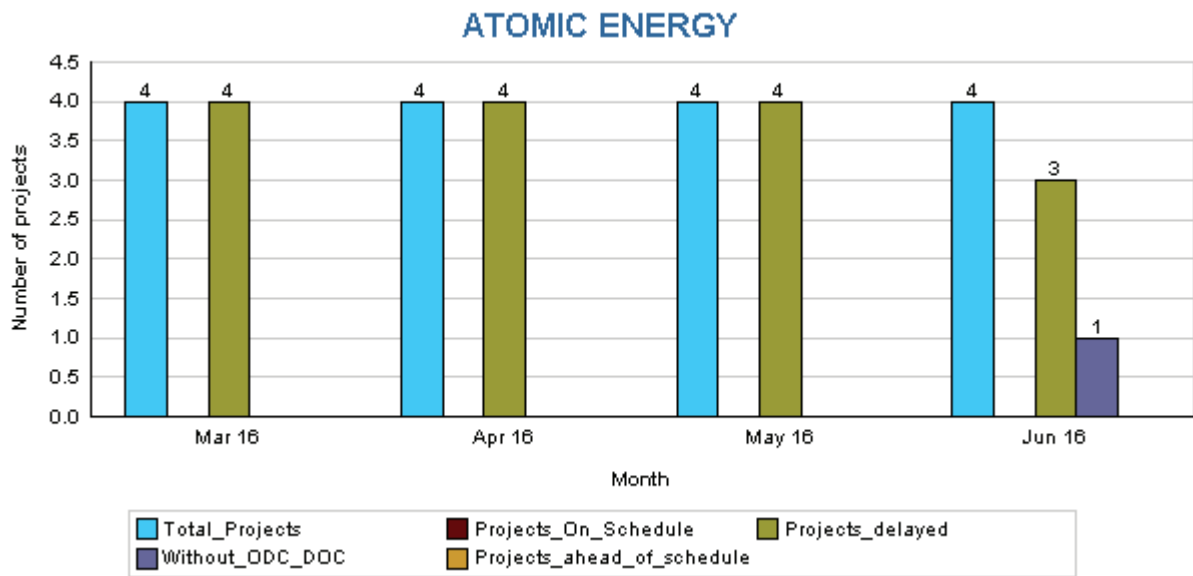


Break-up of 3 Delayed projects in June 2016

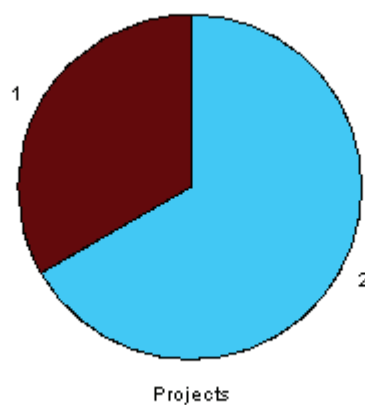


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

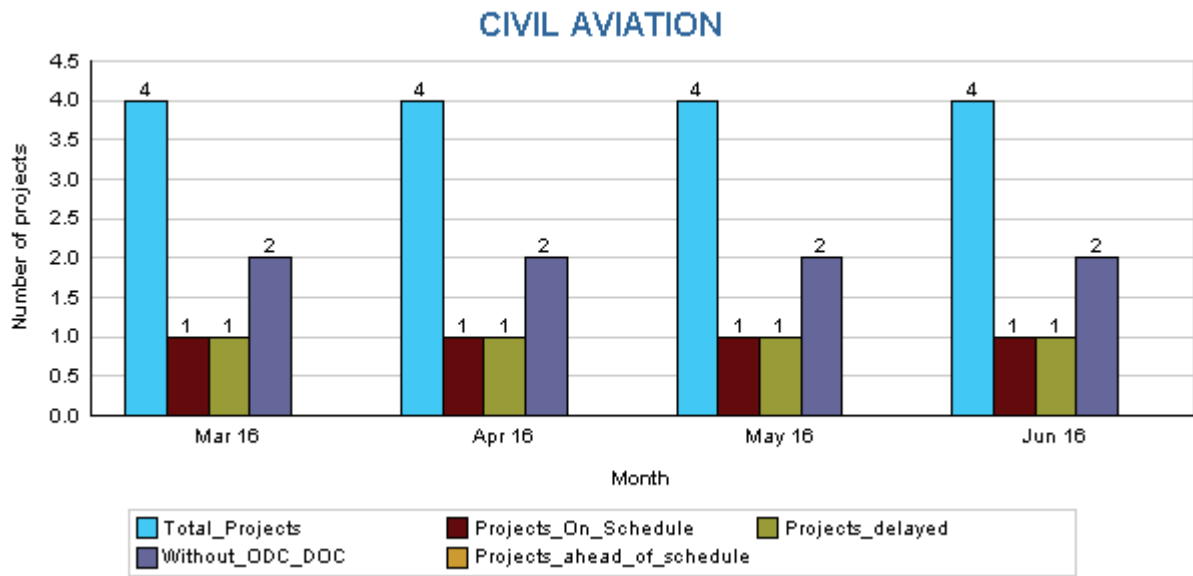


Break-up of 1 Delayed projects in June 2016




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

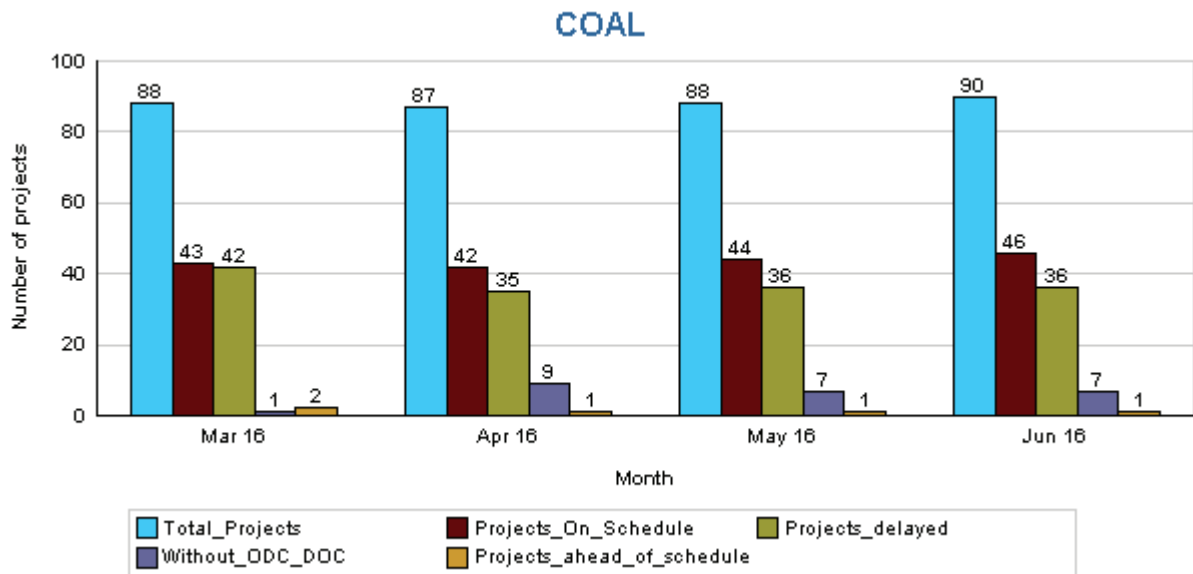


Break-up of 36 Delayed projects in June 2016

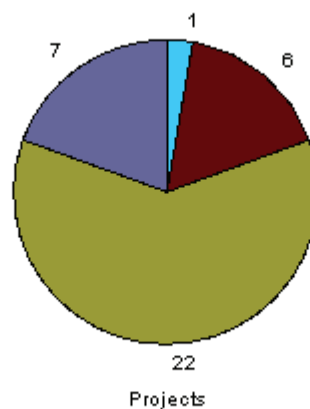


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

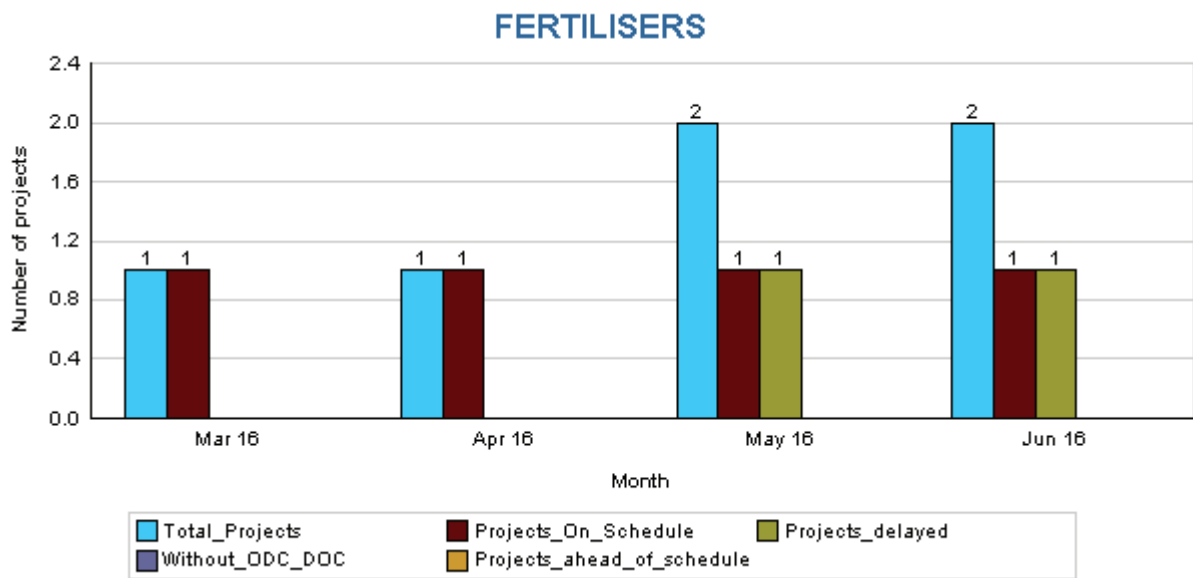


Break-up of 1 Delayed projects in June 2016




Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

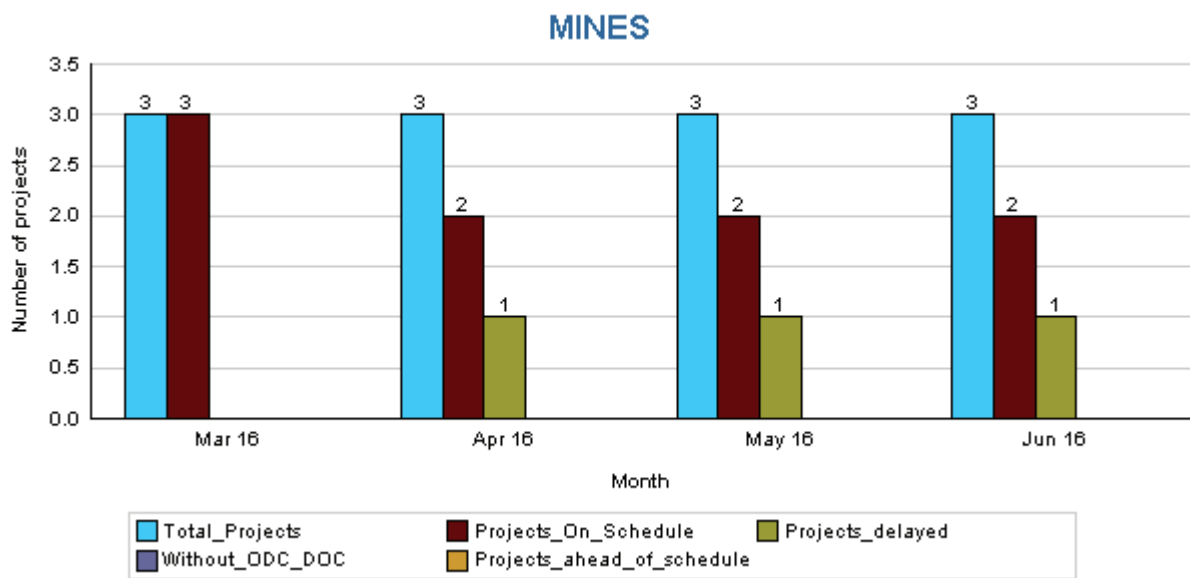


Break-up of 1 Delayed projects in June 2016




Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

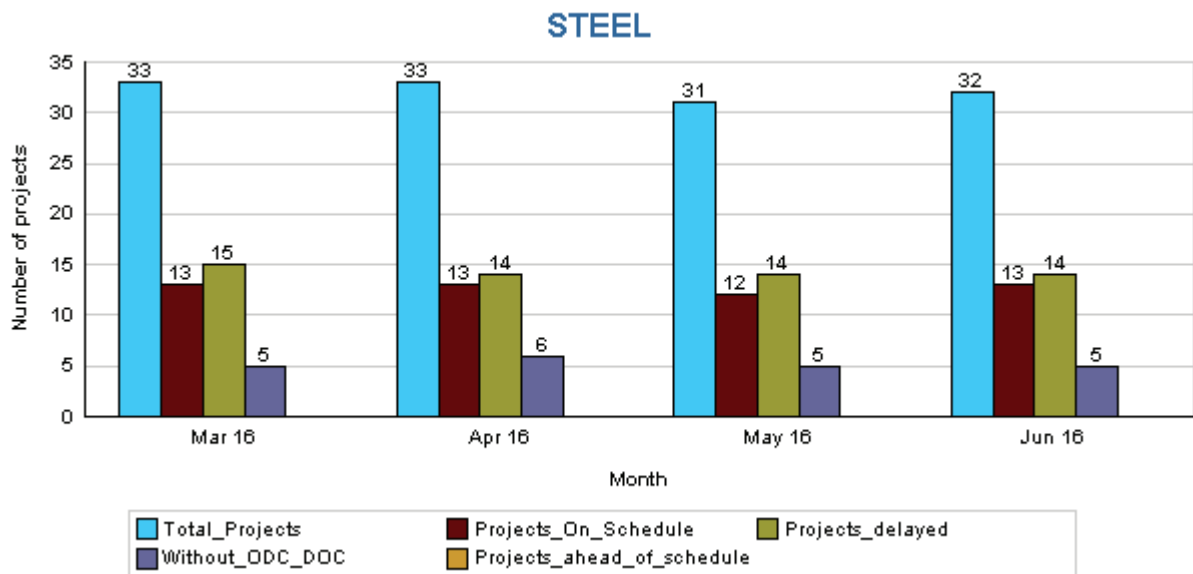


Break-up of 14 Delayed projects in June 2016

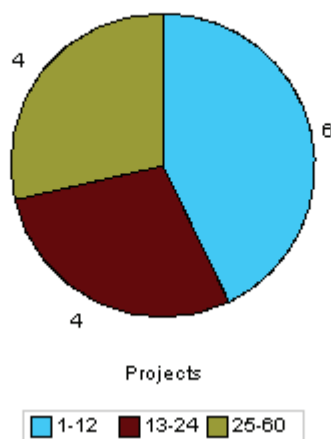


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

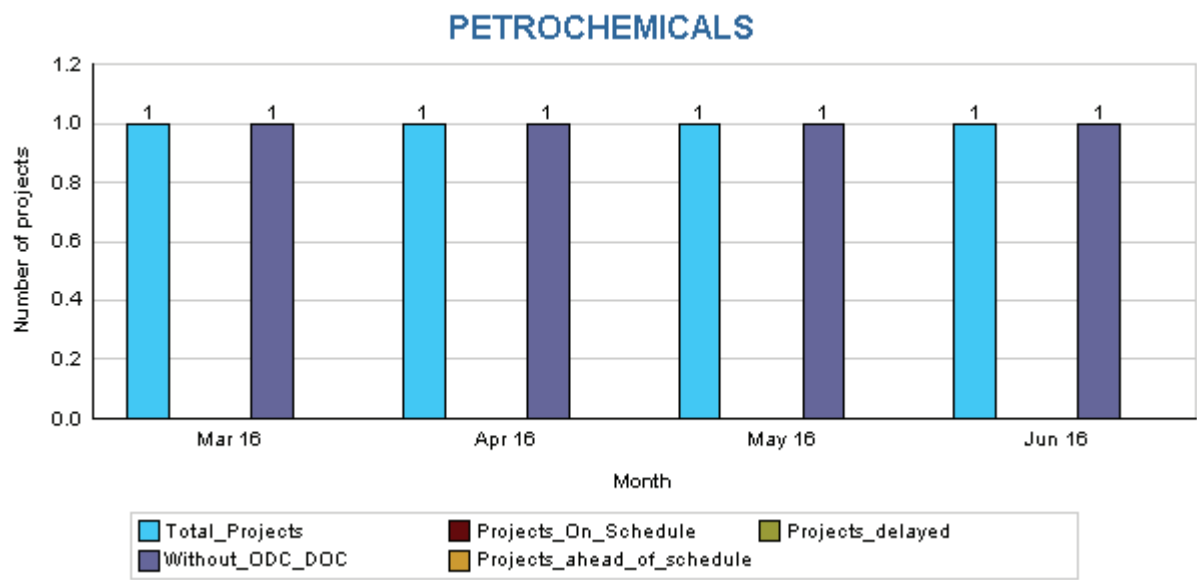


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

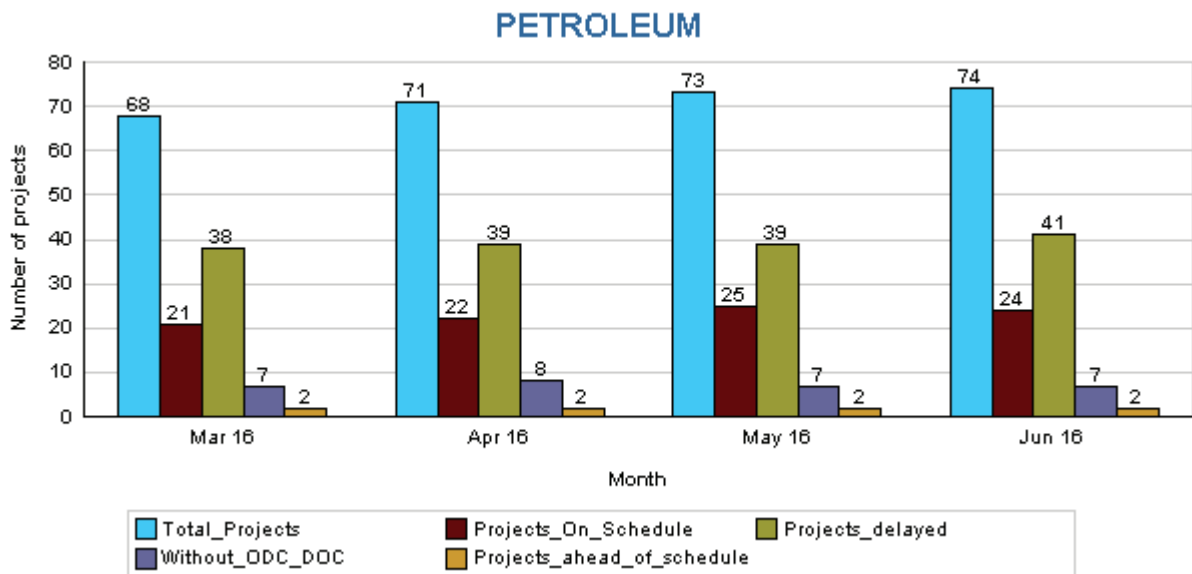


Break-up of 41 Delayed projects in June 2016

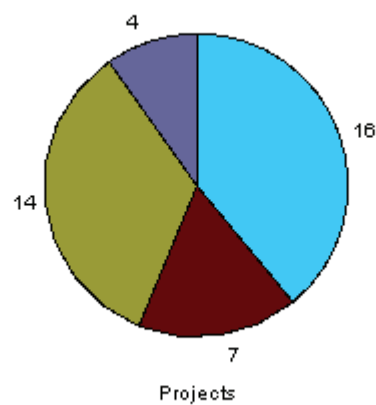


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

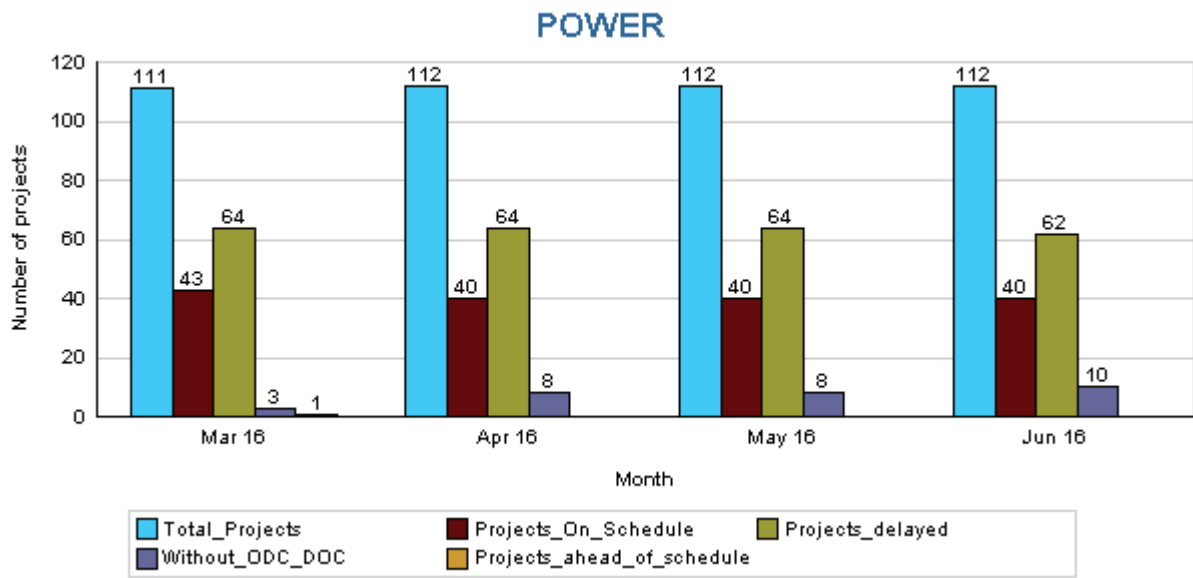


Break-up of 62 Delayed projects in June 2016

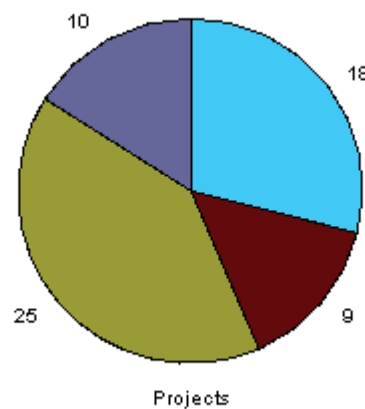


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

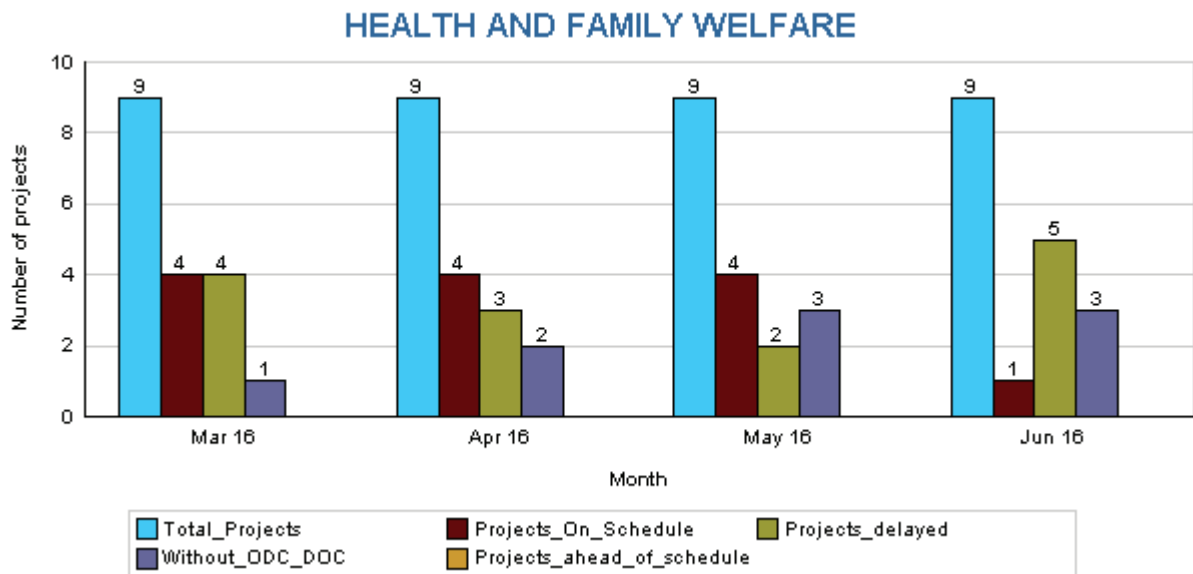


Break-up of 5 Delayed projects in June 2016

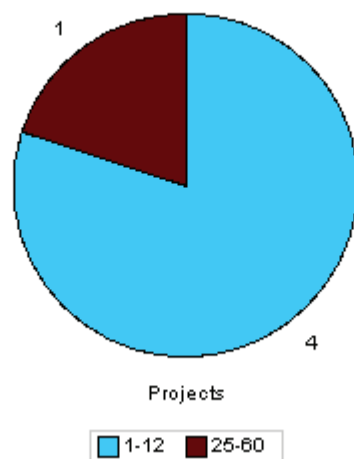


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

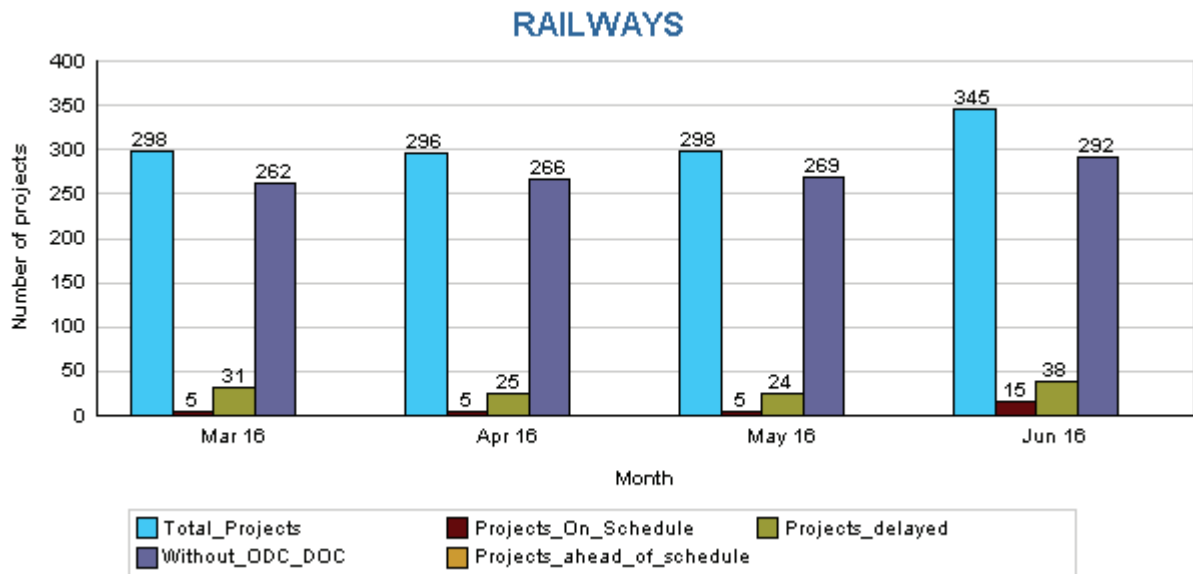


Break-up of 38 Delayed projects in June 2016

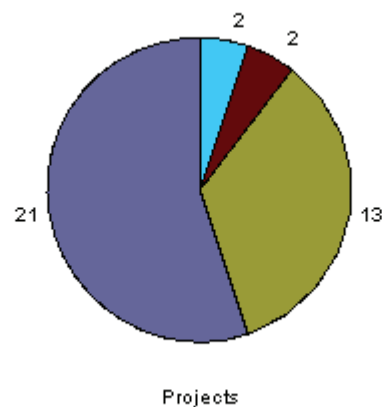


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

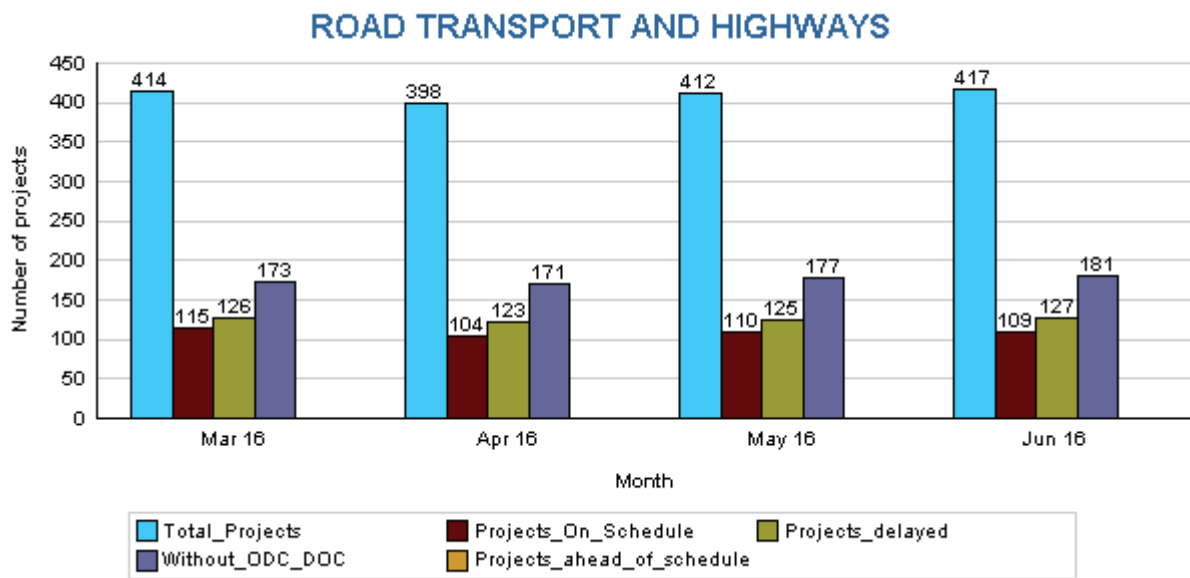


Break-up of 127 Delayed projects in June 2016

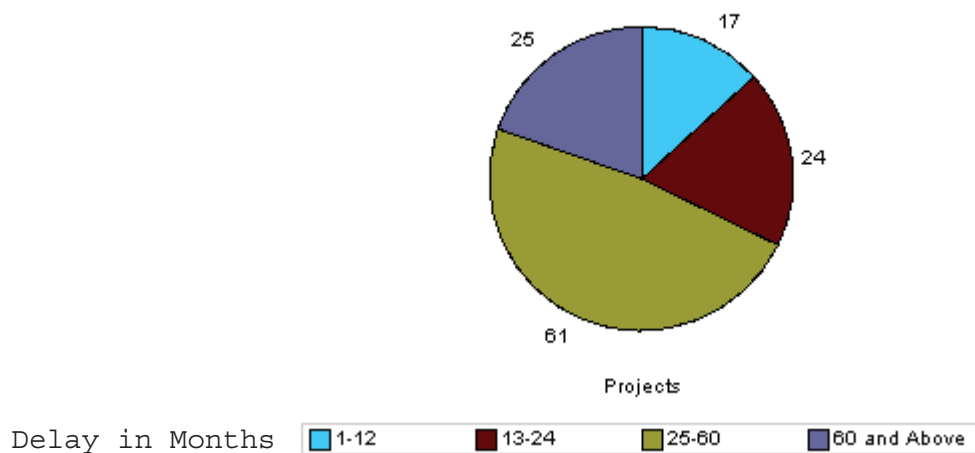

Graphical Presentation of All Projects w.r.t. Original Schedule

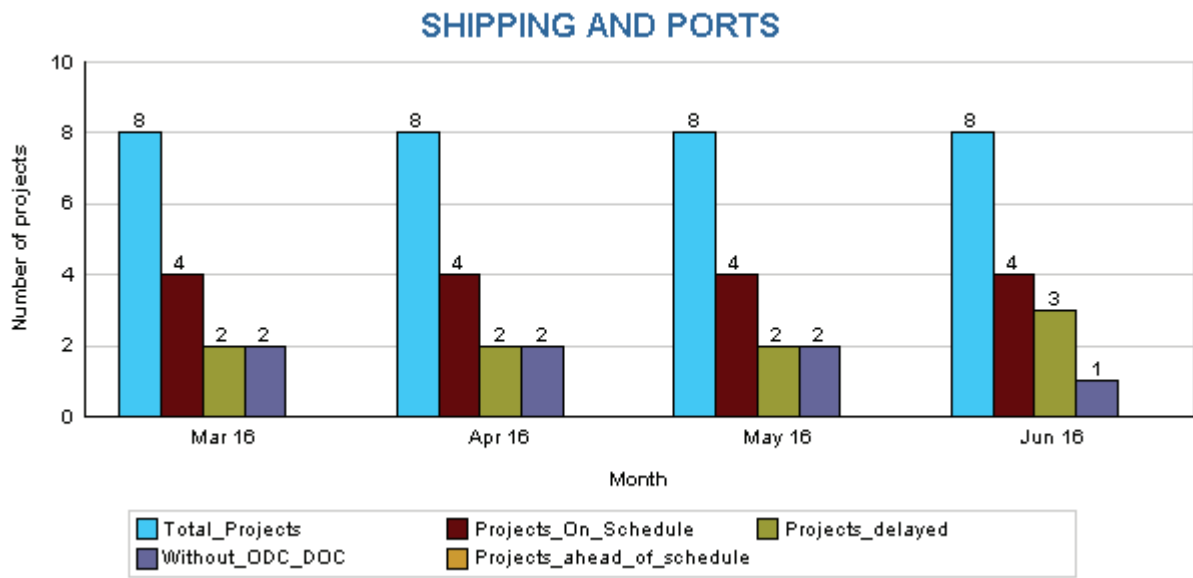


Break-up of 3 Delayed projects in June 2016

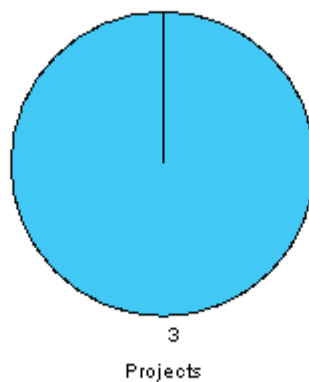


Delay in Months

■ 60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

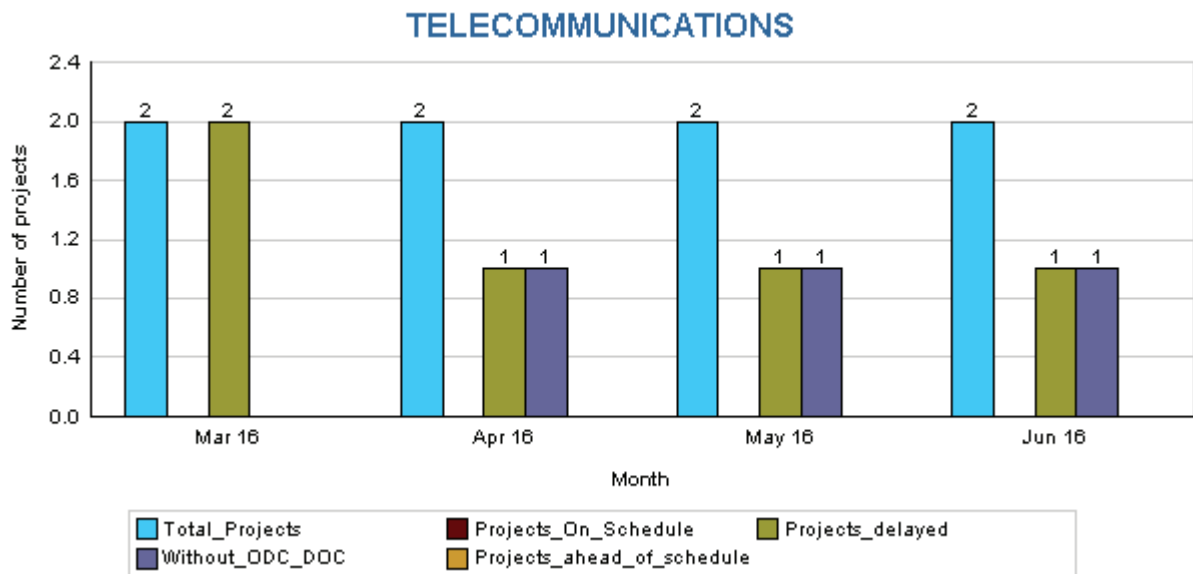


Break-up of 1 Delayed projects in June 2016




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

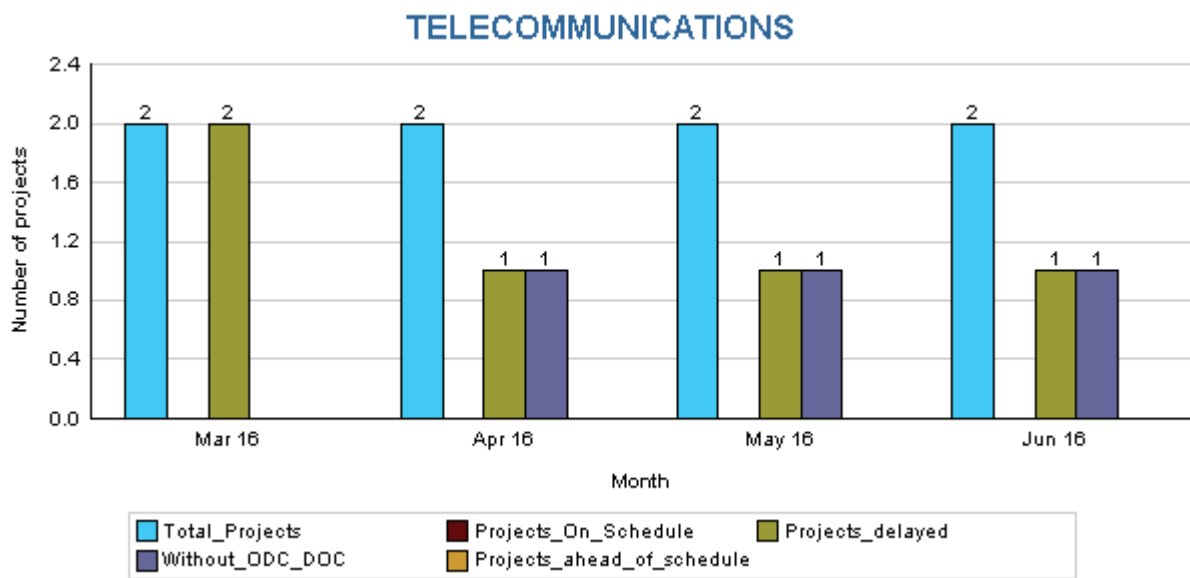


Break-up of 1 Delayed projects in June 2016




Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

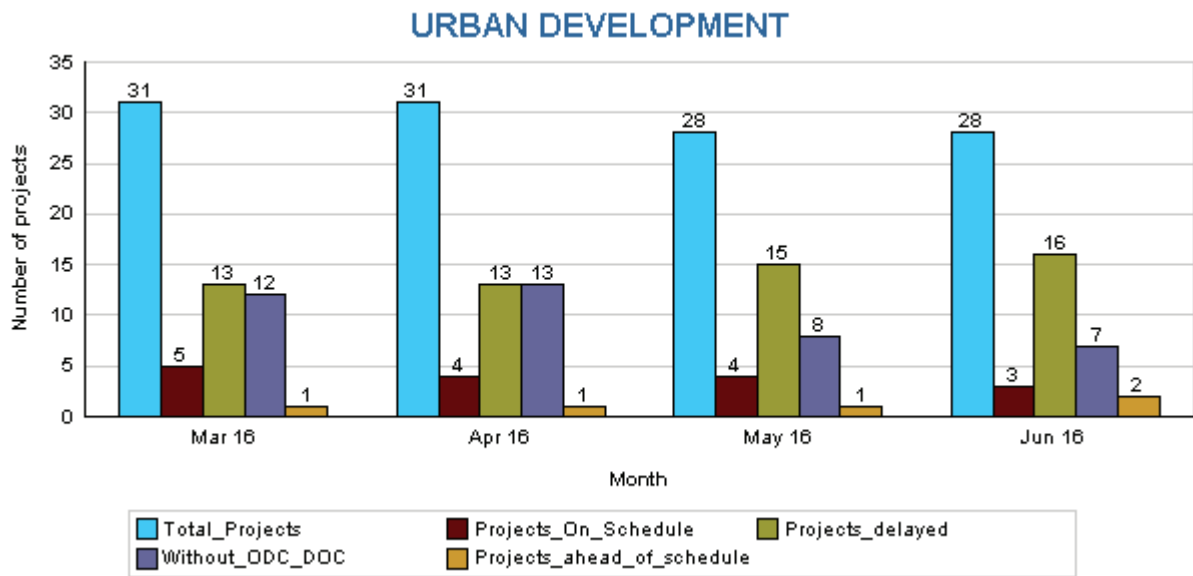

Break-up of 16 Delayed projects in June 2016

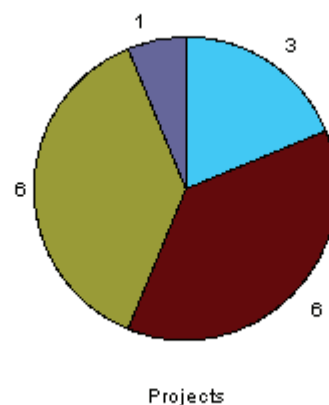

Delay in Months



Sector-wise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	44,541.00	51,918.00	41,625.84
CIVIL AVIATION	4	1,177.28	1,177.28	1,186.17	795.81
COAL	90	69,573.40	69,800.57	70,943.19	14,098.19
FERTILISERS	2	680.64	692.29	692.29	96.77
MINES	3	2,555.63	2,555.63	1,875.63	347.32
STEEL	32	53,059.66	53,440.63	53,588.97	32,166.42
PETROCHEMICALS	1	5,460.61	9,965.00	9,965.00	9,895.57
PETROLEUM	74	110,511.66	111,638.98	114,415.93	45,506.46
POWER	112	315,179.00	344,706.00	364,677.74	202,342.66
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	2,563.15	1,296.39
RAILWAYS	345	328,791.74	359,265.98	417,811.40	85,292.41
ROAD TRANSPORT AND HIGHWAYS	417	263,809.81	265,684.89	266,605.47	127,928.28
SHIPPING AND PORTS	8	4,117.75	5,048.11	5,085.02	2,064.65
TELECOMMUNICATIONS	2	15,445.17	15,445.17	15,345.17	301.57
URBAN DEVELOPMENT	28	133,830.49	141,333.13	142,976.73	64,874.47
Grand total	1132	1,348,915.99	1,429,575.81	1,523,477.16	630,921.81

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU , .	12/2001	13,171.00 17,270.00	22,462.00	21,674.00	12/2008 10/2013	05/2016	-	63/102
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU , .	09/2003	3,492.00 -	5,677.00	4,933.84	09/2010 09/2016	09/2016	72(O) 0(R)	12/88
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT , .	10/2009	11,459.00 -	11,459.00	8,603.00	12/2015 11/2016	11/2018	35(O) 24(R)	43/70
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN , .	10/2009	12,320.00 -	12,320.00	6,415.00	12/2016 03/2017	12/2019	36(O) 33(R)	30/69
	Total		40,442.00 -	51,918.00	41,625.84				148/329
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA , .	05/2010	335.61 -	318.00	305.59	05/2012 -	03/2015	-	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM , .	01/2009	309.46 -	309.46	433.19	01/2011 06/2016	09/2017	80(O) 15(R)	0/0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE , .	10/2012	217.60 -	244.10	30.73	03/2015 -	09/2015	-	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS , .	10/2013	314.61 -	314.61	26.30	09/2018 -	09/2018	0(O) -	0/0
	Total		1,177.28 -	1,186.17	795.81				0/0
	COAL								
9	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA , .	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA , .	01/2005	302.96 -	302.96	318.74	03/2010 -	03/2016	-	8/10
11	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH , .	06/2010	11,816.40 -	11,816.40	2,064.77	03/2023 -	03/2023	0(O) -	11/16
12	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND , .	12/2007	341.63 -	341.63	121.94	03/2011 -	03/2017	72(O) -	2/5
13	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH , .	08/2013	7,612.33 7,612.33	7,612.33	817.83	03/2023 03/2023	03/2023	0(O) 0(R)	2/17
14	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , .	08/2008	706.40 -	706.40	79.50	07/2012 03/2017	03/2021	104(O) 48(R)	1/3
15	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA , .	12/2009	212.34 -	1,228.39	880.45	03/2013 -	03/2016	-	21/22
16	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , .	10/2006	249.03 -	249.03	120.14	03/2012 -	03/2018	72(O) -	32/42
17	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL , .	11/2015	602.86 -	602.86	189.80	03/2022 -	03/2022	0(O) -	2/7

Sector Wise Details

(June 2016)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	NIGAI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , .	10/2007	259.40 486.57	486.57	170.89	03/2012 03/2018	03/2017	60(O) -12(R)	1/1
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , .	12/2007	490.10 -	490.10	206.73	03/2017 -	03/2017	0(O) -	11/11
20	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , .	12/2007	457.77 -	457.77	278.00	03/2013 -	03/2017	48(O) -	8/9
21	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA , .	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	2/13
22	TALABIRA OCP - [N06000043]MCL,ODISHA , .	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
23	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , .	12/2007	172.08 -	172.08	182.26	03/2010 -	03/2017	84(O) -	2/4
24	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH , .	11/2014	1,624.59 1,624.59	1,624.59	5.53	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
25	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , .	12/2008	453.63 -	453.63	121.97	12/2012 -	03/2017	51(O) -	11/44
26	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH , .	08/2015	1,186.64 -	1,186.64	12.75	03/2023 -	03/2023	0(O) -	1/9
27	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , .	09/2014	441.82 -	441.82	151.27	03/2020 -	03/2020	0(O) -	5/13
28	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , .	08/2008	207.28 -	207.28	198.63	03/2012 -	03/2017	60(O) -	4/5
29	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , .	11/2008	479.53 -	479.63	188.13	03/2013 -	03/2017	48(O) -	4/8
30	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH , .	09/2008	152.43 -	152.43	29.83	03/2015 -	03/2020	60(O) -	1/6
31	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH , .	07/2008	178.44 -	178.44	0.35	03/2014 -	03/2020	72(O) -	1/7
32	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , .	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132(O) -	0/2
33	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , .	03/2010	209.78 -	209.78	86.88	03/2015 -	03/2017	24(O) -	8/31
34	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , .	03/2010	181.19 -	181.19	108.66	03/2012 -	03/2017	60(O) -	5/6
35	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH , .	12/2009	321.50 -	321.50	197.76	03/2014 -	03/2018	48(O) -	4/7
36	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH , .	11/2009	198.59 -	198.59	134.17	03/2016 -	03/2018	24(O) -	4/7
37	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND , .	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2016	-	1/3
38	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND , .	12/2007	179.87 -	179.87	95.73	03/2012 -	03/2017	60(O) -	1/3
39	PURNADIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND , .	07/2008	210.98 -	210.98	152.14	03/2013 -	03/2016	-	1/3
40	TAPIN OCP (2.5 MTY) - [N06000086]JCL,JHARKHAND , .	08/2008	264.68 -	264.68	147.94	03/2012 -	03/2016	-	1/4
41	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCL,JHARKHAND , .	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2016	-	1/4
42	KARMA OCP (1.0MTY) - [N06000088]JCL,JHARKHAND , .	06/2009	162.46 -	162.46	72.08	03/2014 -	03/2017	36(O) -	1/4

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	KISTARAM OCP - [N06000089]SCCL,TELANGANA , .	11/2010	242.29 -	242.29	0.09	03/2015 -	03/2018	36(O) -	0/5
44	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]JNCL,UTTAR PRADESH , .	06/2011	1,131.28 1,131.28	1,131.28	307.11	03/2018 -	03/2018	0(O) -	6/9
45	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , .	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36(O) -	4/29
46	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , .	07/2011	447.06 -	447.06	85.33	03/2015 -	03/2018	36(O) -	4/13
47	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , .	02/2011	339.88 -	339.88	12.08	04/2014 -	03/2017	35(O) -	4/7
48	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH , .	04/2012	258.56 -	258.56	122.93	03/2016 -	03/2018	24(O) -	3/6
49	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , .	06/2012	365.01 -	365.01	39.49	06/2015 -	03/2017	21(O) -	15/36
50	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , .	07/2012	417.33 -	417.33	32.26	07/2016 -	03/2019	32(O) -	6/28
51	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , .	11/2012	430.45 -	486.27	92.33	03/2016 -	03/2018	24(O) -	16/39
52	AMRAPALI OC(12MTY) - [N06000103]JCL,JHARKHAND , .	02/2012	858.11 -	858.11	110.10	03/2020 -	03/2020	0(O) -	2/4
53	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH , .	12/2013	610.63 -	610.63	-	03/2022 -	03/2022	0(O) -	1/7
54	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , .	02/2014	555.52 -	555.52	4.36	03/2021 -	03/2017	-48(O) -	0/2
55	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH , .	05/2014	164.49 -	164.49	87.81	03/2020 -	03/2020	0(O) -	3/6
56	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , .	05/2014	479.15 -	479.15	14.12	03/2019 -	03/2019	0(O) -	1/9
57	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , .	05/2014	3,756.36 -	3,756.36	621.58	03/2026 -	03/2026	0(O) -	3/15
58	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , .	05/2014	337.66 -	337.66	1.03	03/2019 -	03/2019	0(O) -	2/6
59	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , .	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
60	GARJANBAHAL OCP - [N06000117]MCL,ODISHA , .	11/2014	1,375.38 -	1,375.38	181.29	03/2021 -	03/2021	0(O) -	1/9
61	DINESH OCP - [N06000118]WCL,MAHARASHTRA , .	11/2014	611.16 -	611.16	244.17	03/2020 -	03/2020	0(O) -	3/9
62	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , .	09/2014	266.23 -	266.23	111.75	03/2021 -	03/2021	0(O) -	4/12
63	GOKUL - [N06000120]WCL,MAHARASHTRA , .	11/2014	267.67 -	267.67	178.29	03/2018 -	03/2018	0(O) -	3/8
64	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA , .	02/2015	187.94 -	187.94	41.91	03/2023 -	03/2023	0(O) -	5/10
65	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , .	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
66	AMERA OC RCE - [N06000123]SECL,CHHATISGARH , .	02/2015	335.97 -	335.97	34.24	03/2018 -	03/2018	0(O) -	1/4
67	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , .	12/2014	357.80 -	357.80	111.65	03/2021 -	03/2021	0(O) -	0/7

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
68	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , .	12/2014	371.04 -	371.04	27.52	03/2021 -	03/2021	0(O) -	0/6
69	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , .	05/2015	295.56 -	295.56	84.76	03/2019 -	03/2019	0(O) -	8/14
70	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA , .	05/2015	397.09 -	397.09	0.30	03/2019 -	03/2019	0(O) -	5/18
71	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , .	06/2015	205.49 -	205.49	69.36	03/2020 -	03/2020	0(O) -	4/13
72	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , .	06/2015	483.69 -	483.69	57.98	03/2021 -	03/2021	0(O) -	3/8
73	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , .	08/2015	727.28 -	727.28	84.61	03/2025 -	03/2025	0(O) -	3/13
74	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , .	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	3/11
75	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , .	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	0/6
76	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH , .	07/2015	316.10 -	316.10	17.28	03/2020 -	03/2020	0(O) -	0/5
77	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH , .	02/2015	916.24 -	916.24	-	03/2023 -	03/2023	0(O) -	1/8
78	MALACHUA OPENCAS PROJECT - [N06000139]SECL,MADHYA PRADESH , .	10/2015	488.33 -	488.33	-	03/2023 -	03/2023	0(O) -	0/8
79	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH , .	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/0
80	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , .	11/2015	277.65 -	277.65	-	03/2021 -	03/2021	0(O) -	2/8
81	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , .	11/2015	498.42 -	498.42	0.21	03/2020 -	03/2020	0(O) -	1/9
82	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , .	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022	0(O) -	0/24
83	KOYAGUDEM OPENCAS PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2018	0(O) -	0/11
84	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA , .	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	0/17
85	AMADAND OPENCAS EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH , .	03/2016	869.44 -	869.44	108.08	03/2021 -	03/2021	0(O) -	0/0
86	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA , .	02/2016	198.68 -	198.68	1.95	03/2019 -	03/2019	0(O) -	0/0
87	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA , .	02/2016	304.52 -	304.52	88.68	03/2018 -	03/2018	0(O) -	0/0
88	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , .	06/2011	5,907.11 -	5,907.11	2,136.98	12/2015 04/2018	04/2018	28(O) 0(R)	13/35
89	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , .	08/2011	1,230.27 -	1,230.27	51.55	04/2015 04/2019	04/2019	48(O) 0(R)	1/6
90	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , .	08/2011	988.35 -	988.35	45.26	04/2017 -	04/2017	0(O) -	0/3
91	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU , .	04/2012	364.75 -	364.75	220.04	10/2014 -	08/2016	22(O) -	8/10
92	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU , .	04/2013	1,458.17 -	1,458.17	61.03	06/2015 08/2019	08/2019	50(O) 0(R)	1/7

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND , .	09/2009	153.82 -	153.82	82.97	03/2014 -	09/2016	30(O) -	4/6
94	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL , .	08/2012	1,055.05 -	1,055.05	228.71	03/2018 -	09/2018	6(O) -	4/12
95	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	2.56	09/2019 -	09/2019	0(O) -	0/0
96	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND , .	08/2010	289.45 -	289.45	122.47	05/2014 -	10/2016	29(O) -	0/8
97	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND , .	10/2012	269.82 -	269.82	80.41	04/2014 -	11/2016	31(O) -	0/10
98	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	74.76	12/2019 -	12/2019	0(O) -	0/0
	Total		69,573.40 -	70,943.19	14,098.19				315/998
	<u>FERTILISERS</u>								
99	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA , .	10/2014	197.79 209.44	209.44	72.96	11/2016 09/2017	09/2017	10(O) 0(R)	0/0
100	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA , .	02/2016	482.85 482.85	482.85	23.81	12/2017 -	12/2017	0(O) -	0/1
	Total		680.64 -	692.29	96.77				0/1
	<u>MINES</u>								
101	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JCL,MADHYA PRADESH , .	09/2011	1,856.00 -	1,176.00	12.44	09/2017 -	04/2020	31(O) -	0/0
102	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO,MAHARASHTRA , Private	12/2015	355.13 355.13	355.13	214.67	11/2016 11/2016	11/2016	0(O) 0(R)	0/5
103	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 344.50	344.50	120.21	11/2016 11/2016	11/2016	0(O) 0(R)	0/0
	Total		2,555.63 -	1,875.63	347.32				0/5
	<u>STEEL</u>								
104	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH , .	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
105	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH , .	07/2011	974.76 -	974.76	357.53	07/2016 -	03/2017	8(O) -	1/1
106	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH , .	12/2009	280.00 -	280.00	67.55	09/2016 -	03/2017	6(O) -	1/1
107	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND , .	03/2015	255.19 -	255.19	50.34	03/2018 -	03/2018	0(O) -	0/1
108	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA , .	03/2007	149.73 173.00	175.94	178.61	12/2015 -	03/2017	15(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
109	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA , .	05/2005	768.88 1,070.97	1,070.97	1,070.97	02/2014 -	03/2016	-	0/0
110	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN , .	05/2015	189.00 -	189.00	-	03/2017 -	03/2017	0(O) -	0/0
111	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR , .	10/2005	956.00 -	956.00	650.35	03/2015 -	03/2017	24(O) -	0/0
112	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , .	12/2007	200.00 -	200.00	136.15	03/2018 -	03/2018	0(O) -	0/0
113	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	03/2016	-	0/0
114	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA , .	04/2015	3,127.30 -	3,127.30	370.92	04/2018 -	04/2018	0(O) -	0/2
115	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , .	07/2011	324.87 324.87	324.87	263.57	12/2015 -	04/2016	-	0/0
116	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , .	04/2013	170.00 -	170.00	99.91	04/2018 -	04/2018	0(O) -	0/0
117	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , .	12/2009	343.00 -	488.40	100.51	10/2016 -	06/2017	8(O) -	0/0
118	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , .	12/2007	253.92 253.92	253.92	194.54	06/2016 -	06/2016	0(O) -	0/0
119	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH , .	11/2015	818.00 -	818.00	-	06/2020 -	06/2020	0(O) -	1/11
120	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA , .	10/2011	175.49 206.71	206.71	141.17	12/2016 -	07/2017	7(O) -	0/0
121	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA , .	12/2011	187.33 -	187.33	178.85	10/2013 -	08/2016	34(O) -	2/5
122	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA , .	06/2014	708.91 -	708.91	446.48	04/2016 -	09/2016	5(O) -	1/3
123	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH , .	05/2012	404.16 -	404.16	336.54	07/2015 -	09/2017	26(O) -	0/1
124	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , .	02/2014	4,749.00 -	4,749.00	13.87	09/2017 -	09/2017	0(O) -	0/0
125	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA , .	04/2014	151.33 -	151.33	11.86	09/2017 -	09/2017	0(O) -	0/0
126	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , .	03/2015	1,034.01 -	1,034.01	61.81	10/2017 -	10/2017	0(O) -	0/2
127	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH , .	07/2011	877.73 -	877.73	529.21	07/2015 -	11/2016	16(O) -	2/2
128	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , .	08/2010	17,265.00 -	17,265.00	16,235.61	03/2013 -	12/2016	45(O) -	33/37

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
129	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , .	10/2013	245.67 -	245.67	139.69	05/2016 -	12/2016	7(O) -	1/3
130	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , .	04/2014	188.93 -	188.93	78.23	04/2015 -	12/2016	20(O) -	2/4
131	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH , .	01/2010	15,525.00 -	15,525.00	9,652.03	05/2015 12/2017	12/2017	31(O) 0(R)	37/81
132	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND , .	05/2015	1,154.18 -	1,154.18	103.89	12/2017 -	12/2017	0(O) -	0/2
133	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA , .	12/2007	202.61 227.00	227.00	200.20	12/2016 -	12/2016	0(O) -	0/0
134	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT , .	01/2013	175.00 -	175.00	-	- -	12/2017	- -	0/0
135	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , .	02/2014	787.29 -	787.29	317.73	12/2016 -	12/2016	0(O) -	0/0
	Total		53,059.66 -	53,588.97	32,166.42				81/156
	PETROCHEMICALS								
136	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM , .	04/2006	5,460.61 9,965.00	9,965.00	9,895.57	04/2012 12/2015	12/2015	-	23/26
	Total		5,460.61 -	9,965.00	9,895.57				23/26
	PETROLEUM								
137	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU , .	05/2013	711.00 -	711.00	9.03	- -	-	-	0/0
138	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU , .	11/2006	171.83 -	171.83	-	- -	-	-	0/0
139	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , .	01/2015	1,823.00 -	1,823.00	3.61	- -	-	-	0/0
140	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE , .	01/2015	2,321.00 -	2,321.00	6.26	- -	-	-	0/0
141	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE , .	02/2015	890.00 -	890.00	5.52	- -	-	-	0/0
142	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	59.87	01/2018 -	01/2018	0(O) -	30/61
143	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN , .	11/2011	310.00 370.00	370.00	17.76	03/2013 01/2017	01/2017	46(O) 0(R)	0/27
144	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	173.28	95.20	01/2017 -	01/2017	0(O) -	0/0
145	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM , .	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30(O) -	0/12

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
146	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE , ,	06/2009	2,915.00 -	2,915.00	1,381.86	12/2012 -	02/2019	74(O) -	7/14
147	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA , ,	10/2015	607.06 714.25	714.25	101.37	10/2017 -	02/2018	4(O) -	21/52
148	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	182.96	02/2020 -	02/2020	0(O) -	0/0
149	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH , ,	01/2016	247.52 -	247.52	-	02/2019 -	02/2019	0(O) -	1/10
150	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM , ,	03/2009	2,465.15 2,378.89	2,378.89	1,873.19	03/2013 03/2017	03/2017	48(O) 0(R)	5/15
151	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE , ,	06/2007	736.65 -	736.65	516.44	09/2011 10/2016	03/2017	66(O) 5(R)	0/0
152	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA , ,	12/2009	1,584.00 -	1,584.00	1,405.13	03/2017 03/2017	03/2017	0(O) 0(R)	3/12
153	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA , ,	12/2011	2,059.63 2,665.65	2,665.65	1,351.65	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
154	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA , ,	03/2012	2,592.17 2,592.17	2,592.17	1,320.05	05/2014 03/2017	03/2017	34(O) 0(R)	0/21
155	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE , ,	04/2012	600.17 600.17	600.17	375.14	12/2014 03/2018	03/2018	39(O) 0(R)	0/8
156	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE , ,	02/2011	913.00 -	913.00	553.79	08/2015 -	03/2017	19(O) -	0/0
157	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE , ,	12/2009	309.81 462.79	462.79	289.76	10/2014 03/2017	03/2017	29(O) 0(R)	28/40
158	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL , ,	03/2014	3,076.00 -	3,076.00	330.01	09/2017 03/2018	03/2018	6(O) 0(R)	1/7
159	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA , ,	03/2014	3,150.00 -	3,150.00	206.25	09/2017 -	03/2018	6(O) -	2/6
160	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA , ,	11/2014	6,068.80 -	6,068.80	1,636.71	04/2019 -	03/2019	-1(O) -	0/0
161	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI , ,	08/2014	6,086.08 -	6,086.08	1,054.15	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
162	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU , ,	05/2015	257.87 -	257.87	36.88	11/2016 -	03/2017	4(O) -	14/22
163	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA , ,	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
164	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT , Central Sector Projects	11/2015	500.00 -	500.00	-	03/2017 -	03/2017	0(O) -	0/0
165	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA , ,	01/2006	732.00 1,227.00	1,227.00	1,143.03	10/2011 -	04/2016	-	0/0
166	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT , ,	09/2011	202.25 -	160.16	79.68	07/2016 -	04/2017	9(O) -	5/12
167	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,190.69	73.04	04/2018 -	04/2018	0(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
168	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects	02/2016	367.11 -	367.11 -	9.25 -	04/2017 -	04/2017 -	0(O) -	13/22
169	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219]BPCL,MAHARASHTRA , .	08/2014	393.00 -	393.00 -	-	04/2018 -	04/2018 -	0(O) -	0/0
170	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU , .	08/2014	393.00 -	393.00 -	84.95 -	04/2018 -	04/2018 -	0(O) -	0/0
171	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE , .	04/2013	284.82 -	284.82 -	7.98 -	04/2015 05/2017	05/2017 -	25(O) 0(R)	0/5
172	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA , .	06/2014	5,706.47 5,813.25	5,813.25 -	4,080.91 -	05/2017 05/2017	05/2017 -	0(O) 0(R)	7/16
173	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA , .	02/2015	2,899.93 2,098.43	2,098.43 -	1,188.25 -	05/2017 -	05/2017 -	0(O) -	0/0
174	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE , .	07/2011	352.56 -	439.03 -	10.60 -	03/2017 06/2018	06/2018 -	15(O) 0(R)	0/0
175	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH , .	07/2014	419.04 -	419.04 -	361.10 -	01/2017 -	07/2016 -	-6(O) -	13/16
176	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT , .	12/2011	160.00 -	160.00 -	94.30 -	02/2016 07/2016	07/2016 -	5(O) 0(R)	4/4
177	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE , .	04/2010	270.00 -	251.66 -	172.53 -	06/2012 11/2015	08/2016 -	50(O) 9(R)	0/0
178	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA , .	03/2014	238.50 -	238.50 -	26.16 -	03/2017 -	08/2017 -	5(O) -	3/6
179	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]IOCL,MANIPUR , Central Sector Projects	08/2010	103.02 171.04	171.04 -	117.61 -	07/2016 08/2016	08/2016 -	1(O) 0(R)	5/9
180	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT , .	03/2009	317.64 -	240.95 -	139.01 -	09/2012 09/2016	09/2016 -	48(O) 0(R)	2/5
181	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA , .	03/2012	14,225.00 -	16,504.00 -	11,626.55 -	05/2016 -	09/2016 -	4(O) -	0/16
182	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA , .	01/2006	993.00 1,693.00	1,693.00 -	1,489.38 -	01/2012 -	09/2016 -	56(O) -	0/0
183	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH , .	01/2011	141.86 -	232.00 -	179.17 -	09/2016 -	09/2016 -	0(O) -	0/12
184	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	195.63 -	64.81 -	09/2018 -	09/2018 -	0(O) -	0/0
185	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL , .	08/2014	190.45 -	190.45 -	53.48 -	09/2017 -	09/2017 -	0(O) -	0/0
186	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE , .	12/2009	463.32 -	463.32 -	344.95 -	06/2011 10/2016	10/2016 -	64(O) 0(R)	13/20
187	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR , .	04/2013	480.00 -	422.00 -	268.52 -	02/2016 10/2016	10/2016 -	8(O) 0(R)	5/6
188	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221]BPCL,MAHARASHTRA , .	01/1991	694.00 -	694.00 -	57.19 -	10/2018 -	10/2018 -	0(O) -	0/0
189	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL , .	03/2015	694.00 -	694.00 -	58.32 -	10/2018 -	10/2018 -	0(O) -	0/0
190	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA , .	02/2012	666.00 838.08	838.08 -	632.64 -	11/2015 11/2016	11/2016 -	12(O) 0(R)	27/29

Sector Wise Details									
(June 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
191	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU , .	03/2013	3,110.36 -	3,110.36	1,840.40	11/2015 11/2016	11/2016	12(O) 0(R)	48/52
192	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT , .	05/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
193	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE , .	07/2009	3,957.00 3,561.00	3,561.00	215.38	01/2013 12/2018	12/2018	71(O) 0(R)	13/38
194	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE , .	08/2009	1,793.00 -	1,793.00	1,447.36	09/2012 -	12/2016	51(O) -	6/7
195	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA , .	03/2011	861.79 1,256.72	1,256.72	1,055.56	05/2013 12/2016	12/2016	43(O) 0(R)	1/5
196	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE , .	01/2012	352.49 -	352.49	187.61	03/2014 05/2016	12/2016	33(O) 7(R)	0/3
197	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE , .	08/2011	586.00 -	586.00	467.91	08/2015 12/2016	12/2016	16(O) 0(R)	3/12
198	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA , .	03/2013	1,138.50 686.58	686.58	650.62	04/2015 05/2016	12/2016	20(O) 7(R)	0/0
199	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE , .	05/2013	4,124.35 4,124.35	4,124.35	789.44	04/2016 12/2017	12/2017	20(O) 0(R)	0/3
200	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE , .	03/2014	2,476.82 -	2,476.82	982.92	12/2018 -	12/2018	0(O) -	8/8
201	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , .	04/2011	191.96 -	191.96	117.38	05/2015 -	12/2016	19(O) -	0/12
202	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM , .	03/2009	228.64 -	214.19	147.72	12/2016 -	12/2016	0(O) -	0/0
203	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE , .	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5(O) -	1/38
204	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE , .	10/2011	725.00 -	725.00	275.75	11/2016 -	12/2016	1(O) -	0/8
205	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA , .	05/2015	2,443.00 -	2,443.00	227.71	12/2017 -	12/2017	0(O) -	0/0
206	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	1,121.78	12/2017 -	12/2017	0(O) -	0/0
207	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220]BPCL,MAHARASHTRA , .	02/2015	184.00 -	184.00	16.26	12/2017 -	12/2017	0(O) -	0/0
208	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA , .	02/2015	184.00 -	184.00	16.26	06/2017 -	12/2017	6(O) -	0/0
209	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM , .	09/2012	871.35 -	1,200.00	627.43	03/2015 12/2016	12/2016	21(O) 0(R)	0/5
210	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM , .	06/2010	202.94 -	202.94	2.95	01/2014 -	-	-	0/2
	Total		110,511.66 -	114,415.93	45,506.46				289/695
	POWER								

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
211	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , .	07/2009	421.01 1,007.57	1,007.57	988.44	07/2013 -	-	-	25/26
212	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH , .	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
213	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , .	01/2013	12,964.60 -	12,964.60	6,735.12	01/2018 -	01/2018	0(O) -	23/31
214	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH , .	03/2012	9,569.76 -	9,569.76	6,274.99	06/2015 -	02/2017	20(O) -	21/30
215	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , .	08/2014	288.49 -	288.49	99.90	02/2017 -	02/2017	0(O) -	1/12
216	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH , .	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	2/2
217	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , .	02/2014	14,366.58 -	14,366.58	2,967.00	02/2019 -	02/2019	0(O) -	12/18
218	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , .	05/2011	195.42 -	195.42	72.21	02/2014 -	02/2018	48(O) -	1/3
219	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH , .	12/2004	2,496.90 6,179.96	6,179.96	4,721.52	12/2009 03/2017	03/2017	87(O) 0(R)	16/30
220	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , .	12/2007	477.69 738.48	738.48	603.59	09/2010 01/2016	03/2017	78(O) 14(R)	4/8
221	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM , .	01/2008	4,375.35 6,749.18	6,749.18	6,067.00	09/2011 08/2016	03/2017	66(O) 7(R)	22/37
222	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE , .	10/2008	4,824.12 -	4,824.12	4,327.38	10/2012 -	03/2017	53(O) -	7/11
223	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL , .	04/2010	4,404.57 -	4,404.57	2,831.55	01/2015 -	03/2017	26(O) -	8/16
224	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , .	02/2010	232.34 -	232.34	220.09	06/2012 -	03/2017	57(O) -	1/4
225	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE , .	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	03/2016	-	11/12
226	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , .	10/2011	487.49 639.46	639.46	449.02	06/2014 03/2016	03/2017	33(O) 12(R)	10/12
227	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT , .	12/2011	552.44 609.44	609.44	501.60	02/2014 03/2016	03/2016	-	10/10
228	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH , .	12/2011	1,746.65 2,228.71	2,228.71	1,586.53	08/2014 12/2015	03/2017	31(O) 15(R)	7/11
229	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM , .	07/1998	368.72 1,441.52	1,441.52	1,049.75	07/2006 03/2017	03/2017	128(O) 0(R)	5/13
230	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA , .	01/2012	15,166.19 -	15,166.19	11,196.00	01/2017 -	03/2017	2(O) -	32/46
231	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE , .	01/2014	374.63 -	374.63	27.60	04/2016 -	03/2017	11(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
232	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE , .	02/2014	539.82 -	539.82	163.50	06/2016 -	03/2017	9(O) -	8/11
233	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE , .	02/2014	908.08 -	908.08	416.10	06/2016 -	03/2017	9(O) -	10/18
234	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE , .	06/2014	5,151.37 -	5,151.37	851.60	03/2018 -	03/2018	0(O) -	8/12
235	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR , .	10/2014	8,112.12 -	8,112.12	141.80	04/2020 -	03/2022	23(O) -	0/0
236	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH , .	09/2014	9,188.98 -	9,188.98	1,553.00	03/2019 -	03/2019	0(O) -	16/17
237	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE , .	01/2015	268.80 -	268.80	49.00	03/2018 -	03/2018	0(O) -	0/3
238	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , .	03/2015	197.40 -	197.40	3.30	03/2018 -	03/2018	0(O) -	0/0
239	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH , .	03/2015	550.06 -	550.06	38.50	03/2018 -	03/2018	0(O) -	0/3
240	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR , .	03/2010	3,984.03 -	3,984.03	3,329.07	01/2013 -	03/2016	-	1/1
241	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL , .	04/2007	4,122.00 8,781.30	9,606.82	8,450.32	02/2011 -	03/2016	-	26/26
242	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH , .	01/2016	305.04 -	305.04	9.30	03/2017 -	03/2017	0(O) -	0/0
243	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE , .	12/2011	2,422.66 -	2,422.66	2,488.16	08/2014 -	04/2016	-	13/14
244	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE , .	02/2012	1,927.16 1,940.58	1,940.58	1,638.17	10/2014 03/2016	04/2016	-	7/7
245	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE , .	06/2014	400.47 -	400.47	155.00	04/2017 -	04/2017	0(O) -	1/3
246	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , .	12/2014	6,517.36 -	6,517.36	740.80	04/2018 -	04/2018	0(O) -	3/12
247	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , .	04/2015	3,705.61 -	3,705.61	570.60	04/2018 -	04/2018	0(O) -	4/9
248	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , .	04/2015	1,479.30 -	1,479.30	182.20	04/2017 -	04/2017	0(O) -	2/8
249	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , .	02/2005	8,692.97 15,095.67	15,095.67	11,863.00	01/2011 05/2018	05/2018	88(O) 0(R)	27/48
250	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE , .	03/2010	965.58 -	965.58	790.44	11/2012 -	05/2016	-	10/10
251	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE , .	01/2015	3,662.02 -	3,662.02	696.10	05/2018 -	05/2018	0(O) -	0/5

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
252	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , .	03/2015	1,394.52 -	1,394.52 -	1.70	05/2017 -	05/2017 -	0(O) -	0/9
253	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU , .	01/2016	162.11 -	162.11 -	3.50	05/2018 -	05/2018 -	0(O) -	0/0
254	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU , .	05/2005	1,779.29 2,187.32	2,187.32	1,908.05	11/2008 01/2016	06/2017	103(O) 17(R)	20/22
255	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND , .	11/2006	2,978.48 3,846.30	3,846.30	2,869.00	03/2013 03/2016	06/2019	75(O) 39(R)	3/15
256	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE , .	02/2009	410.29 -	410.29 -	388.37	02/2012 -	06/2016	52(O) -	10/10
257	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE , .	02/2010	2,144.00 2,932.88	2,932.88	2,335.20	12/2012 12/2016	06/2017	54(O) 6(R)	11/23
258	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE , .	08/2010	1,677.57 -	1,677.57 -	1,481.22	04/2013 -	06/2016	38(O) -	10/11
259	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE , .	07/2010	1,272.80 1,731.10	1,731.10	1,298.13	11/2012 03/2016	06/2017	55(O) 15(R)	10/13
260	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH , .	12/2012	11,846.00 -	11,846.00 -	6,517.00	06/2017 -	06/2017	0(O) -	25/40
261	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , .	03/2013	2,514.88 -	2,514.88 -	1,285.25	12/2015 -	06/2017	18(O) -	15/18
262	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , .	02/2015	302.49 302.00	302.49	276.70	02/2016 -	06/2016	4(O) -	0/1
263	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA , .	01/2016	187.04 -	187.04 -	1.70	06/2018 -	06/2018	0(O) -	0/0
264	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE , .	05/2010	250.03 390.51	390.51	261.30	01/2013 03/2016	07/2016	42(O) 4(R)	13/15
265	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND , .	10/2011	558.26 -	558.26 -	615.91	11/2013 -	07/2016	32(O) -	11/12
266	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA , .	02/2014	167.40 -	167.40 -	92.40	12/2015 -	07/2016	7(O) -	6/8
267	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE , .	01/2015	203.28 -	203.28 -	21.80	07/2017 -	07/2017	0(O) -	0/5
268	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE , .	03/2015	1,071.24 -	1,071.24 -	0.70	09/2017 -	07/2018	10(O) -	0/0
269	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI , .	05/2015	780.33 -	780.33 -	0.90	07/2017 -	07/2017	0(O) -	0/0
270	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH , .	05/2015	312.94 -	312.94 -	65.20	05/2016 -	07/2016	2(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
271	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE , .	07/2015	2,247.37 -	2,247.37	29.90	07/2018 -	07/2018	0(O) -	0/0
272	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT , .	01/2016	244.19 -	244.19	-	07/2018 -	07/2018	0(O) -	0/0
273	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE , .	01/2016	1,455.47 -	1,455.47	13.90	07/2018 -	07/2018	0(O) -	0/0
274	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH , .	01/2016	207.88 -	207.88	-	07/2018 -	07/2018	0(O) -	0/0
275	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA , .	01/2016	10,598.98 -	10,598.98	171.00	07/2020 -	07/2020	0(O) -	4/4
276	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE , .	12/2009	1,216.83 -	1,216.83	1,081.09	08/2012 -	08/2016	48(O) -	3/5
277	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE , .	02/2012	3,201.44 -	3,201.44	3,294.11	10/2014 -	08/2016	22(O) -	13/17
278	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA , .	03/2012	9,395.18 -	9,395.18	6,564.00	11/2016 -	08/2017	9(O) -	27/35
279	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE , .	09/2012	524.40 -	524.40	357.52	05/2015 -	08/2016	15(O) -	10/12
280	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND , .	07/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017	0(O) -	0/9
281	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE , .	03/2013	514.20 -	514.20	381.00	06/2015 -	08/2016	14(O) -	7/10
282	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE , .	06/2012	1,909.24 -	1,909.24	1,172.03	06/2015 -	08/2016	14(O) -	3/5
283	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , .	05/2014	829.98 -	829.98	233.90	08/2016 -	08/2016	0(O) -	1/4
284	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , .	02/2014	12,532.44 -	12,532.44	3,546.00	08/2018 -	08/2018	0(O) -	19/21
285	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL , .	09/2005	1,061.38 -	2,336.74	2,028.58	09/2009 -	09/2016	84(O) -	3/4
286	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , .	07/2006	1,657.00 - 2,978.86	2,978.86	1,752.36	02/2016 09/2019	09/2019	43(O) 0(R)	12/23
287	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE , .	02/2009	509.66 -	509.66	585.16	11/2011 -	09/2016	58(O) -	8/11
288	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE , .	07/2010	752.64 689.03	689.03	573.02	07/2013 11/2015	09/2016	38(O) 10(R)	7/9
289	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE , .	11/2011	723.63 -	723.63	633.62	11/2014 -	09/2016	22(O) -	7/10
290	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , .	03/2013	11,638.55 -	11,638.55	5,937.00	09/2017 -	09/2017	0(O) -	21/41
291	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE , .	09/2013	680.69 -	680.69	504.09	03/2016 -	09/2016	6(O) -	10/12

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
292	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 -	155.57	26.20	03/2016 -	09/2016	6(O) -	2/6
293	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	197.00	09/2019 -	09/2019	0(O) -	4/6
294	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR ,	01/2007	5,353.00 -	5,353.00	5,679.02	05/2014 03/2017	09/2017	40(O) 6(R)	1/4
295	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH ,	04/2012	9,750.89 -	9,750.89	5,332.28	12/2016 -	09/2017	9(O) -	26/32
296	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND ,	08/2006	2,313.00 4,138.41	4,237.67	3,574.18	12/2011 03/2016	09/2016	57(O) 6(R)	13/14
297	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC, MADHYA PRADESH ,	03/2015	9,870.51 -	9,870.51	1,599.00	09/2019 -	09/2019	0(O) -	13/14
298	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE ,	03/2012	198.63 -	198.63	112.53	09/2014 -	10/2016	25(O) -	0/0
299	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL, GUJARAT ,	02/2014	378.71 -	378.71	138.90	10/2016 -	10/2016	0(O) -	8/11
300	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE ,	01/2015	871.62 -	871.62	57.70	10/2017 -	10/2017	0(O) -	0/5
301	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL, GUJARAT ,	10/2015	315.00 -	315.00	46.34	10/2016 -	10/2016	0(O) -	0/2
302	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR ,	01/2009	3,642.04 -	5,783.17	4,617.51	01/2016 -	11/2016	10(O) -	3/6
303	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH ,	05/2011	1,961.87 2,310.58	2,310.58	1,822.25	05/2014 06/2016	11/2016	30(O) 5(R)	8/12
304	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE ,	05/2014	522.29 -	522.29	214.00	11/2016 -	11/2016	0(O) -	2/12
305	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL, MULTI STATE ,	11/2014	972.42 -	972.42	113.30	11/2017 -	11/2017	0(O) -	0/3
306	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN ,	07/2015	307.18 -	307.18	13.10	11/2017 -	11/2017	0(O) -	0/0
307	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75	5,671.34	09/2009 -	12/2018	111(O) -	2/3
308	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND ,	08/2008	2,491.58 -	2,491.58	849.35	06/2013 -	12/2019	78(O) -	6/10
309	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH ,	12/2008	573.99 1,580.04	1,581.04	1,229.17	08/2013 12/2016	12/2016	40(O) 0(R)	29/38
310	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,010.40	08/2013 12/2017	12/2017	52(O) 0(R)	17/26
311	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU ,	09/2011	1,940.13 -	1,940.13	2,078.46	09/2014 -	12/2016	27(O) -	8/13

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
312	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATISGARH , .	11/2011	2,127.51 -	2,127.51	2,407.93	07/2014 -	12/2016	29(O) -	6/8
313	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE , .	12/2011	297.33 346.79	346.79	313.97	08/2014 06/2015	12/2016	28(O) 18(R)	8/10
314	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH , .	01/2012	1,422.85 -	1,422.85	1,546.52	01/2015 -	12/2016	23(O) -	9/11
315	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , .	03/2012	7,921.47 -	7,921.47	5,596.00	09/2016 -	12/2016	3(O) -	33/40
316	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE , .	09/2013	1,575.30 -	1,575.30	1,018.20	05/2016 -	12/2016	7(O) -	8/13
317	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE , .	10/2013	1,364.52 -	1,364.52	753.84	04/2016 -	12/2016	8(O) -	8/12
318	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE , .	05/2014	303.07 -	303.07	62.60	07/2016 -	12/2016	5(O) -	3/9
319	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE , .	02/2014	196.58 -	196.58	38.00	02/2016 -	12/2016	10(O) -	7/17
320	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , .	07/2013	3,363.12 -	3,363.12	1,467.00	12/2016 -	12/2016	0(O) -	20/22
321	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR , .	05/2015	436.68 -	436.68	443.28	12/2016 -	12/2016	0(O) -	0/6
322	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH , .	09/2003	6,285.33 -	17,435.15	8,540.30	09/2010 -	-	-	0/0
	Total		315,179.00 -	364,677.74	202,342.66				898/1358
	<u>HEAVY INDUSTRY</u>								
323	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]NATIS,MULTI STATE , .	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
324	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM , .	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	-	0/0
325	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA , .	09/2014	505.58 -	505.58	70.00	03/2018 -	03/2018	0(O) -	0/0
326	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI , .	11/2013	196.70 -	196.70	197.38	01/2016 -	04/2016	-	0/0
327	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI , .	09/2013	444.70 -	444.70	400.00	12/2015 -	06/2016	6(O) -	0/0
328	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI , .	12/2013	204.44 -	204.44	59.29	05/2017 -	06/2017	1(O) -	0/0
329	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI , .	08/2014	293.65 -	293.65	101.00	05/2017 -	06/2017	1(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
330	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N2100010]HSCC, WEST BENGAL , .	12/2014	168.90 -	168.90	16.50	05/2017 -	07/2017	2(O) -	0/0
331	AIIMS-RAEBARELI-HOUSING - [N2100006]HSCC, UTTAR PRADESH , .	10/2013	159.50 -	159.50	127.80	11/2013 -	10/2016	35(O) -	0/0
332	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI , .	02/2013	414.11 -	414.11	210.92	11/2013 -	11/2014	-	0/0
	Total		2,563.15 -	2,563.15	1,296.39				0/0
	RAILWAYS								
333	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR) - [220100106]SCR, TELANGANA , .	12/1994	124.43 926.23	1,010.00	935.87	- -	02/2014	-	0/0
334	AMRAVATI-NARKHER NL (CR) - [220100118]CR, MAHARASHTRA , .	06/1994	663.01 668.34	668.34	613.87	06/1999 -	-	-	0/0
335	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH , .	04/1995	304.00 -	631.78	270.23	12/2012 -	-	-	0/0
336	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE , .	02/1996	240.00 -	579.37	532.98	- -	-	-	0/0
337	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA , .	03/1996	495.44 1,781.98	1,781.98	242.40	03/2004 -	-	-	0/0
338	AHMEDNAGAR-PARLI VAJUNATH (NL) CR - [220100181]CR, MAHARASHTRA , .	02/1997	514.68 2,271.50	2,271.50	813.83	- -	-	-	0/0
339	DAUSA-GANGAPUR CITY (NL), NWR - [220100184]NWR, RAJASTHAN , .	02/1997	410.08 -	560.00	311.85	- -	-	-	0/0
340	NANGALDAM-TALWARA (NL), NR - [220100188]NR, MULTI STATE , .	03/1981	450.00 -	2,100.00	496.00	07/2012 -	-	-	0/0
341	KARUR-SALEM (NL), SR - [220100191]SR, TAMIL NADU , .	02/1997	155.55 -	870.00	832.15	- -	-	-	0/0
342	HUBLI-ANKOLA (NL), SWR - [220100193]SWR, KARNATAKA , .	04/1997	227.00 -	2,135.00	-	- -	-	-	0/0
343	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL , .	04/1974	393.46 154.30	1,026.00	-	03/2007 03/2007	-	-	0/0
344	RANCHI-LOHARDAGA (GC), SER - [220100214]SER, JHARKHAND , .	04/1997	194.07 -	335.00	226.39	06/2004 -	12/2015	-	0/0
345	MACHERLA-NALGONDA (NL) (SCR) - [220100220]SCR, TELANGANA , .	07/1998	125.00 -	480.00	3.49	07/2008 -	-	-	0/0
346	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND , .	03/1999	2,957.21 -	2,957.21	-	07/2005 -	-	-	0/0
347	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR - [220100240]ECR, BIHAR , .	04/1997	501.69 335.77	1,043.56	-	03/2012 -	-	-	0/0
348	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH , .	04/1999	108.00 -	432.72	-	12/2009 -	-	-	0/0
349	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE , .	04/1999	744.71 -	744.71	-	- -	03/2016	-	1/1
350	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, MULTI STATE , .	03/2002	625.30 408.76	847.75	841.76	06/2007 -	-	-	0/0
351	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC) - [220100262]SR, TAMIL NADU , .	09/1995	100.00 -	980.00	612.90	- -	-	-	0/0
352	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH , .	12/2001	330.00 -	2,125.18	34.21	- -	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
353	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , .	04/1998	92.63 -	270.00	293.59	02/2011 -	-	-	0/0
354	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE , .	04/2000	607.09 -	1,500.00	592.30	12/2012 12/2012	-	-	0/0
355	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA , .	04/1996	138.00 1,382.78	1,382.78	4.41	- -	-	-	0/0
356	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , .	01/2004	238.56 -	740.00	728.91	03/2012 -	12/2012	-	0/0
357	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA , .	04/1996	301.64 -	1,185.64	670.38	- 09/2009	-	-	0/0
358	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND , .	04/2002	459.91 -	418.17	252.86	- -	-	-	0/0
359	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR , .	04/2002	921.00 -	2,363.00	1,649.05	03/2009 -	-	-	0/0
360	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR , .	04/2001	624.47 2,921.46	3,142.46	3,104.92	10/2007 02/2016	-	-	0/0
361	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA , .	04/1998	183.23 -	1,202.70	221.76	02/2015 -	-	-	0/0
362	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA , .	04/1995	127.13 -	225.00	237.94	- -	10/2014	-	0/0
363	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA , .	04/2005	810.78 1,969.16	811.36	269.80	- -	-	-	0/0
364	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH , .	04/2003	136.62 -	360.00	360.11	12/2007 03/2010	-	-	0/0
365	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MTRP,TAMIL NADU , .	04/2006	495.74 -	495.74	341.11	06/2013 -	06/2013	-	1/4
366	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA , .	04/2006	378.56 1,160.47	1,160.47	1.74	- -	-	-	0/1
367	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND , .	03/1997	261.70 -	360.00	282.53	02/2006 -	-	-	0/1
368	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH , .	07/2006	743.00 -	732.81	929.04	03/2008 06/2008	-	-	0/0
369	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU , .	09/2007	404.19 -	2,072.50	572.47	- -	-	-	0/0
370	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU , .	09/2006	343.17 -	1,065.00	969.97	- -	03/2016	-	0/0
371	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE , .	12/2006	170.00 -	485.00	435.57	03/2011 -	-	-	0/0
372	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU , .	09/2006	125.00 -	490.00	54.73	- -	-	-	0/0
373	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU , .	09/2006	456.00 -	1,080.00	201.46	- -	-	-	0/0
374	BARDHAMAN-KATWA (GC) - [N22000091],WEST BENGAL , .	04/2007	1,106.62 -	1,106.62	397.03	12/2010 -	-	-	3/7
375	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , .	04/2007	482.00 874.57	874.57	877.59	03/2013 -	09/2015	-	0/0
376	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL , .	04/2010	2,298.42 -	1,655.68	38.56	03/2014 -	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
377	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN , .	04/2008	829.74 -	829.74	216.81	03/2015 -	03/2015	-	0/0
378	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN , .	04/2008	516.23 732.06	735.00	706.65	03/2014 -	-	-	0/0
379	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL , .	04/2009	533.38 -	533.38	128.88	12/2011 -	-	-	0/0
380	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL , .	04/2009	611.03 -	611.03	136.48	12/2011 -	11/2013	-	0/0
381	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM , .	04/1998	227.90 -	326.51	317.58	12/2012 -	03/2016	-	0/0
382	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM , .	04/1996	1,676.31 -	5,500.00	-	03/2009 -	03/2016	-	0/0
383	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH , .	03/2013	643.00 -	643.00	-	-	-	-	0/0
384	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE , .	04/2007	1,347.26 -	1,347.26	301.07	-	-	-	0/0
385	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT , .	04/2012	376.59 -	644.38	0.11	-	-	-	0/0
386	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT , .	04/2011	439.88 -	845.68	1.56	-	-	-	0/0
387	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE , .	04/2011	2,082.75 -	3,500.00	134.05	-	-	-	0/1
388	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN , .	04/2013	822.00 -	822.00	-	-	-	-	0/1
389	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN , .	04/2013	456.00 855.16	860.00	557.31	-	-	-	0/0
390	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR , .	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
391	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR , .	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
392	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU , .	04/2008	446.87 -	528.00	3.04	-	-	-	0/0
393	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE , .	04/2008	523.52 -	1,200.00	2.26	-	-	-	0/0
394	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU , .	04/2013	839.00 -	1,500.00	0.26	-	-	-	0/0
395	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU , .	04/1999	198.68 -	556.64	303.72	-	-	-	0/0
396	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU , .	04/1998	271.24 -	520.00	463.73	-	-	-	0/0
397	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR, MULTI STATE , .	04/2007	270.14 -	346.15	155.87	-	-	-	0/0
398	KUMBALAM-TURAVUR - [N22000191]SR, KERALA , .	04/2011	252.96 -	252.96	5.39	-	-	-	0/0
399	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA , .	04/1999	895.00 -	1,451.00	1,251.49	03/2007 -	03/2016	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
400	ERODE-PALANI - [N22000199]SR,TAMIL NADU , .	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
401	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , .	04/2008	164.41 -	450.00	25.38	- -	-	-	0/0
402	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU , .	04/2007	247.00 -	951.24	696.59	- -	03/2015	-	0/0
403	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , .	04/2006	191.72 -	342.85	280.75	- -	-	-	0/0
404	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , .	04/2010	189.24 -	189.24	4.21	- -	-	-	0/0
405	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE , .	04/2011	601.43 -	800.00	22.60	- -	-	-	0/0
406	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , .	04/2013	915.98 -	2,103.00	0.10	- -	-	-	0/0
407	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , .	04/2001	923.52 -	923.52	226.48	- -	-	-	0/0
408	CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , .	04/2005	595.91 595.91	595.91	103.62	- -	-	-	0/0
409	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , .	04/2008	499.30 2,491.43	2,491.43	163.20	- -	-	-	0/0
410	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , .	04/2011	277.70 792.89	792.89	65.05	- -	-	-	0/0
411	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA , .	04/2011	184.06 199.12	199.12	70.16	- -	-	-	0/0
412	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA , .	04/2012	297.85 540.02	540.02	19.21	- -	-	-	0/0
413	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , .	04/2007	98.74 203.00	365.00	320.29	- -	03/2015	-	0/0
414	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE , .	04/2006	96.16 260.16	280.00	268.93	- -	01/2015	-	0/0
415	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , .	04/2011	913.00 1,801.00	1,801.01	2.09	- 06/2016	-	-	0/0
416	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , .	04/2007	179.65 1,350.91	1,350.91	522.43	- -	-	-	0/1
417	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA , .	04/2010	377.93 -	986.30	95.16	- -	-	-	0/1
418	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE , .	04/2013	723.00 -	723.00	0.36	- -	-	-	0/0
419	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE , .	04/2012	1,054.35 -	2,200.00	93.84	- -	-	-	0/0
420	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , .	04/2012	923.23 -	923.23	1.13	- -	-	-	0/1
421	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH , .	04/2011	283.54 -	283.54	0.51	- -	-	-	0/0
422	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]JNR,UTTAR PRADESH , .	04/2013	654.00 -	654.00	-	- -	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
423	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , .	04/2013	1,239.00 -	1,239.00	-	-	-	-	0/0
424	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , .	04/2012	287.00 -	576.18	4.70	-	-	-	0/0
425	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH , .	04/2008	1,046.88 -	2,966.99	3.77	-	-	-	0/0
426	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , .	04/2013	558.00 692.43	692.43	-	-	-	-	0/0
427	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , .	04/2013	296.00 466.65	466.65	-	-	-	-	0/0
428	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , .	04/2011	562.74 832.47	832.47	0.94	-	-	-	0/0
429	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE , .	04/2007	970.34 1,714.49	1,714.49	478.15	-	-	-	0/2
430	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , .	04/2011	341.05 348.85	348.85	0.35	-	-	-	0/0
431	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI , .	04/2012	295.68 -	295.68	0.68	-	-	-	0/0
432	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , .	04/2013	829.00 -	829.00	0.48	-	-	-	0/1
433	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , .	04/2011	1,313.48 -	1,313.48	8.44	-	-	-	0/1
434	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , .	04/2010	337.49 -	792.01	1.13	-	-	-	0/1
435	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE , .	04/2013	876.00 -	876.00	-	-	-	-	0/0
436	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE , .	04/2007	328.14 -	328.14	45.90	-	-	-	0/0
437	GADAG-WADI NL - [N22000299]SWR,KARNATAKA , .	04/2013	1,117.00 1,922.00	1,922.00	2.62	-	-	-	0/0
438	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , .	04/2013	327.25 367.77	367.77	-	-	-	-	0/0
439	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU , .	04/1999	460.94 -	1,170.00	1,002.57	01/1999 -	-	-	0/0
440	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , .	04/2012	285.57 279.54	279.54	1.51	01/1999 -	-	-	0/0
441	KAKINADA-PITHAPURAM - [N22000314]SCR,ANDHRA PRADESH , .	03/1999	215.06 -	220.29	0.01	-	-	-	0/0
442	HOSADURGA- CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA , .	04/2010	203.40 -	203.40	-	-	09/2015	-	0/0
443	HUBLI- CHIKAJAJUR - [N22000325]SWR,KARNATAKA , .	03/2015	1,900.00 1,141.00	1,141.00	11.44	- 03/2016	-	-	0/1
444	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE , .	05/2015	600.00 -	620.00	-	-	-	-	0/0
445	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE , .	03/2015	1,830.00 1,190.92	1,190.92	-	-	-	-	0/0
446	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN , .	05/2015	873.71 -	873.71	-	-	-	-	0/0
447	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE , .	03/2015	1,618.00 1,614.59	1,614.59	111.34	-	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
448	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH , .	04/1997	836.26 -	1,072.51	-	-	-	-	0/0
449	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	-	-	-	0/0
450	GULBARGA-BIDAR - [N22000348]SCR,KARNATAKA , .	04/1994	844.15 1,542.42	1,542.42	-	-	-	-	0/0
451	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA , .	02/2016	9,968.00 -	9,968.00	-	-	-	-	0/0
452	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA , .	02/2016	2,425.00 -	2,425.00	-	-	-	-	0/0
453	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA , .	02/2016	2,750.00 -	2,750.00	-	-	-	-	0/0
454	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA , .	02/2015	630.00 -	1,272.00	-	-	-	-	0/0
455	MANOHARABAD-KOTAPALLI - [N22000357],TELANGANA , .	04/2006	1,160.47 -	1,160.47	-	-	-	-	0/0
456	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA , .	02/2015	2,326.00 -	2,326.00	-	-	-	-	0/0
457	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA , .	02/2015	4,670.00 3,627.00	3,627.00	-	-	-	-	0/0
458	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA , .	02/2016	1,876.00 -	1,876.00	-	-	-	-	0/0
459	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA , .	02/2016	854.00 -	854.00	-	-	-	-	0/0
460	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA , .	02/2016	912.00 -	912.00	-	-	-	-	0/0
461	GUDUR-DURGARAJU PATNAM - [N22000363]SCR,ANDHRA PRADESH , .	04/2010	760.17 -	760.17	-	-	-	-	0/0
462	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA , .	04/2013	616.08 -	616.08	-	-	-	-	0/1
463	KAZIPET-VIJAYAWADA III RD LINE WITH ELECTRIFICATION - [N22000365]SCR,TELANGANA , .	04/2012	1,820.50 -	1,820.50	-	-	-	-	0/0
464	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH , .	04/2015	3,873.07 -	3,873.07	-	-	-	-	0/0
465	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE , .	04/2015	2,063.03 -	2,063.03	-	-	-	-	0/0
466	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH , .	04/2016	4,000.00 -	3,571.00	-	-	-	-	0/0
467	VIJAYAWADA-GUDUR - [N22000369]SCR,ANDHRA PRADESH , .	04/2015	3,246.26 -	3,246.26	-	-	-	-	0/0
468	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]SCR,MULTI STATE , .	04/2015	636.38 -	636.38	-	-	-	-	0/0
469	SECUNDERABAD-MOHABOONNAGAR - [N22000371]SCR,TELANGANA , .	04/2015	728.10 -	728.10	-	-	-	-	0/0
470	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR , .	01/1991	332.15 -	559.91	538.53	07/2014 -	07/2014	-	0/0
471	INDORE-DEWAS-UJJAIN(80 KM) DL - [N22000375]WR,MADHYA PRADESH , .	04/2016	600.00 -	600.00	-	-	-	-	0/0
472	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE , .	04/1992	315.64 -	315.64	-	-	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
473	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE , .	04/2096	614.54 -	614.54	-	-	-	-	0/0
474	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM , .	04/2093	971.22 -	971.22	-	-	-	-	0/0
475	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM , .	04/2003	4,300.00 -	4,300.00	-	-	-	-	0/0
476	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM , .	04/2007	180.09 -	180.09	-	-	-	-	0/0
477	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM , .	04/2015	2,232.32 -	2,232.32	-	-	-	-	0/0
478	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM , .	04/2015	870.96 -	870.96	-	-	-	-	0/0
479	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL , .	04/2016	556.31 -	556.31	-	-	-	-	0/0
480	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT , .	04/2015	1,002.39 -	1,002.39	-	-	-	-	0/0
481	INDORE DEWAS UJJAIN (80 KM) - [N22000393]WR,GUJARAT , .	04/2016	600.00 -	600.00	-	-	-	-	0/0
482	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT , .	04/2006	117.36 196.95	193.00	192.05	03/2011 -	01/2011	-	0/0
483	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE , .	04/1986	158.77 608.02	634.48	631.43	03/1994 02/2016	02/2016	-	0/0
484	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE , .	04/1990	155.66 551.50	548.01	257.05	- 03/2019	03/2019	- 0(R)	0/0
485	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL , .	04/1983	36.80 274.41	1,336.57	259.15	-	03/2019	-	0/0
486	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , .	04/1995	900.05 1,125.89	1,125.89	983.85	12/2011 03/2020	03/2020	99(O) 0(R)	0/0
487	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , .	03/1997	677.97 1,062.36	1,651.54	-	-	03/2018	-	0/0
488	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE , .	04/1997	218.24 372.09	525.00	269.92	-	03/2019	-	0/0
489	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE , .	09/1998	247.66 -	5,050.00	983.61	05/2008 -	03/2023	178(O) -	0/0
490	KATIHAH - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR , .	09/2001	492.98 -	1,727.27	742.05	12/2010 -	03/2018	87(O) -	0/0
491	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA , .	02/1998	242.42 369.70	844.00	-	- 05/2009	03/2015	-	0/1
492	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE , .	04/2000	733.00 -	2,531.34	2,269.43	12/2008 -	03/2018	111(O) -	0/0
493	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL , .	04/2000	1,188.91 1,188.91	1,188.91	765.74	- 12/2009	03/2019	- 111(R)	0/0
494	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR , .	04/2003	727.56 -	9,046.72	5,338.49	03/2011 -	03/2019	96(O) -	0/0
495	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND , .	04/1996	768.87 -	768.87	595.54	- 03/2010	03/2010	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
496	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH , .	04/2005	383.79 -	1,101.16	194.91	- -	03/2017	- -	0/0
497	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM , .	09/2006	200.00 200.00	496.24	181.19	- -	03/2017	- -	0/0
498	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR , .	09/2006	300.00 -	837.73	361.62	- -	03/2020	- -	0/0
499	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH , .	04/2006	325.00 -	2,434.00	669.00	03/2010 -	03/2017	84(O) -	0/0
500	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA , .	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
501	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH , .	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	-	0/0
502	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA , .	04/2008	813.34 813.34	2,876.00	546.61	03/2014 -	03/2018	48(O) -	0/0
503	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM , .	04/2008	619.34 -	2,820.25	679.78	04/2014 -	03/2020	71(O) -	0/0
504	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR , .	04/2008	282.92 -	565.13	3.13	- -	03/2018	- -	0/0
505	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM , .	04/2008	1,339.48 4,085.00	4,085.00	385.59	12/2015 -	03/2020	51(O) -	0/0
506	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN , .	04/2008	653.19 658.07	658.07	453.55	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
507	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH , .	04/2008	603.04 1,030.29	1,421.25	690.23	03/2012 -	03/2022	120(O) -	0/0
508	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT , .	04/2008	394.14 -	385.60	45.70	03/2013 -	03/2020	84(O) -	0/0
509	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT , .	04/2008	318.24 321.62	321.62	40.64	03/2012 03/2019	03/2019	84(O) 0(R)	0/0
510	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND , .	04/2006	850.00 -	2,513.30	148.39	03/2015 -	03/2020	60(O) -	0/0
511	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE , .	04/2007	1,640.04 -	1,640.04	345.37	- 03/2022	03/2022	- 0(R)	0/0
512	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT , .	04/2012	567.18 -	975.62	67.20	- -	03/2020	- -	0/0
513	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , .	04/1994	320.66 -	399.63	19.78	- -	03/2019	- -	0/0
514	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , .	04/2011	446.00 -	1,037.15	538.68	- -	03/2019	- -	0/0
515	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , .	04/2010	739.65 -	872.22	798.43	- -	03/2017	- -	0/1
516	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND , .	04/2010	309.44 388.67	583.00	74.85	12/2015 -	03/2016	- -	0/0
517	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE , .	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	- -	0/0
518	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE , .	04/2008	822.39 -	1,480.83	1,451.09	- -	03/2018	- -	0/1

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
519	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL , .	04/2010	221.42 -	467.91	27.30	-	03/2019	-	0/0
520	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND , .	04/2013	4,274.00 -	4,274.00	-	-	03/2020	-	0/0
521	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL , .	04/2011	209.77 -	440.05	368.34	-	03/2018	-	0/0
522	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL , .	04/2012	283.55 -	288.11	95.03	-	03/2018	-	0/0
523	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR, MEGHALAYA , .	04/2010	4,083.02 -	6,000.00	17.62	-	03/2020	-	0/0
524	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE , .	04/2010	242.22 -	599.90	45.92	-	03/2018	-	0/0
525	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE , .	04/2010	241.52 210.00	394.28	148.33	-	03/2017	-	0/0
526	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE , .	04/2011	165.82 -	412.53	0.79	-	03/2018	-	0/0
527	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR, MULTI STATE , .	04/1999	523.17 380.60	1,653.55	1,038.26	-	03/2018	-	0/0
528	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM , .	04/2011	312.12 -	453.10	302.32	-	03/2018	-	0/0
529	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM , .	04/2012	246.07 -	386.68	0.57	-	03/2019	-	0/0
530	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA , .	04/2012	714.10 -	714.10	65.20	04/2016	03/2017	11(O)	0/0
531	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE , .	04/2011	248.07 -	248.07	12.88	03/2015	03/2015	-	0/0
532	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE , .	04/2011	299.60 -	299.60	-	03/2017	03/2017	0(O)	0/0
533	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE , .	04/2009	257.42 -	257.42	67.47	03/2014	03/2014	-	0/0
534	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE , .	04/2010	423.66 -	423.66	163.59	03/2017	03/2017	0(O)	0/0
535	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL, KARNATAKA , .	04/2010	2,127.00 -	2,127.00	621.81	-	03/2019	-	0/1
536	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH , .	03/2012	1,503.71 -	1,503.71	194.57	-	03/2020	-	0/0
537	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA , .	03/2011	679.27 -	1,111.99	217.99	-	03/2021	-	0/0
538	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA , .	03/2013	858.67 -	810.28	4.75	-	03/2021	-	0/0
539	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH , .	12/2012	826.57 1,160.83	1,160.83	206.92	-	03/2020	-	0/1
540	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA , .	03/2012	155.81 -	238.03	106.05	-	03/2020	-	0/0
541	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU , .	04/2011	190.10 -	455.96	173.63	-	03/2019	-	0/0

Sector Wise Details									
(June 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
542	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE , .	05/2015	860.43 860.43	860.43	25.46	- -	03/2020	- -	0/0
543	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA , .	03/2015	960.00 578.00	578.00	58.10	- -	03/2020	- -	0/0
544	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH , .	03/2015	1,750.00 -	1,750.00	-	03/2022 -	03/2022	0(O) -	0/0
545	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH , .	04/2015	524.00 668.00	668.00	-	03/2020 -	03/2020	0(O) -	0/0
546	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU , .	10/2013	187.26 -	233.73	28.33	04/2014 -	03/2018	47(O) -	0/0
547	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA , .	04/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021	0(O) -	0/0
548	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH , .	04/2015	2,499.71 -	2,499.71	-	03/2021 -	03/2021	0(O) -	0/0
549	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA , .	04/2015	2,361.74 -	2,361.74	-	03/2021 -	03/2021	0(O) -	0/0
550	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA , .	04/2015	701.61 -	701.61	0.84	03/2021 -	03/2021	0(O) -	0/0
551	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA , .	04/2015	1,172.92 -	1,172.92	1.11	03/2021 -	03/2021	0(O) -	0/0
552	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT - [N22000384]GUJARAT , .	04/1990	153.82 -	551.82	245.58	03/2019 -	03/2019	0(O) -	0/0
553	VIRAMGAM BHILDI - [N22000391]WR,GUJARAT , .	04/1990	237.13 -	237.13	25.05	03/2018 -	03/2018	0(O) -	0/0
554	BPUTRA BRIDGE AT BOGIBI AND LINK LINES NEFR - [220100201]NFR,ASSAM , .	09/1997	1,500.00 -	4,996.19	3,689.32	04/2008 12/2011	06/2017	110(O) 66(R)	0/0
555	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA , .	04/1994	470.21 -	3,004.90	608.32	- 06/2021	06/2021	- 0(R)	0/0
556	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , .	09/2007	687.20 -	950.00	928.13	03/2010 -	06/2017	87(O) -	0/0
557	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL , .	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	06/2016	3(O) -	0/0
558	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL , .	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
559	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , .	04/2007	313.24 -	554.70	384.84	01/1999 06/2017	06/2017	221(O) 0(R)	0/0
560	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , .	04/2012	252.00 972.52	972.52	97.63	- -	07/2019	- -	0/1
561	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA , .	03/2011	165.16 -	234.71	227.05	03/2015 -	07/2015	- -	0/0
562	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL , .	04/1999	207.52 -	207.52	191.41	12/2012 -	09/2015	- -	0/0
563	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , .	04/2010	279.40 -	355.00	337.82	- -	09/2015	- -	0/0
564	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , .	04/1997	120.00 245.39	245.39	210.67	12/2008 -	10/2015	- -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
565	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA , .	04/2000	133.41 207.00	340.00	328.43	03/2009 03/2009	10/2016	91(O) 91(R)	1/1
566	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA , .	03/2006	201.00 -	230.00	205.82	- -	10/2015	-	0/0
567	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , .	03/1995	2,500.00 -	19,565.00	-	11/2002 -	12/2018	193(O) -	0/0
568	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA , .	02/1997	295.00 1,289.92	1,289.92	1,281.11	- -	12/2016	-	0/1
569	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , .	02/1997	386.30 1,160.54	1,776.81	1,027.59	03/1998 -	12/2019	261(O) -	0/0
570	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH , .	03/1996	155.74 843.45	966.98	884.25	02/2009 12/2017	12/2017	106(O) 0(R)	0/0
571	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL , .	03/1998	111.90 1,039.29	2,371.85	479.90	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
572	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA , .	04/1999	166.16 -	370.00	356.17	02/2009 02/2009	12/2016	94(O) 94(R)	0/1
573	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , .	09/2006	324.90 -	385.54	402.56	03/2010 -	12/2017	93(O) -	0/3
574	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL , .	03/1984	293.97 -	1,428.00	456.82	06/2005 -	12/2019	174(O) -	0/0
575	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL , .	04/2010	3,951.98 -	3,161.58	998.39	03/2016 -	12/2020	57(O) -	0/0
576	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL , .	04/2010	2,913.51 -	2,095.20	641.78	03/2016 -	12/2018	33(O) -	0/0
577	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT , .	04/2008	1,389.62 2,173.50	1,389.62	1,571.89	03/2014 12/2017	12/2017	45(O) 0(R)	0/0
578	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT , .	04/2013	1,266.89 -	1,266.89	75.26	- -	12/2020	-	0/0
579	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE , .	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
580	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE , .	04/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022	46(O) 0(R)	0/0
581	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA , .	04/2010	149.90 -	230.00	54.96	03/2015 -	12/2016	21(O) -	0/0
582	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL , .	04/2010	171.02 -	235.00	226.99	06/2013 -	12/2016	42(O) -	0/0
583	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , .	04/2012	258.20 315.13	365.00	1.19	- -	12/2017	-	0/0
584	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA , .	04/2012	632.68 -	816.55	-	03/2016 -	12/2017	21(O) -	0/0
585	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , .	04/2012	148.77 -	209.00	0.36	12/2016 -	12/2016	0(O) -	0/0
586	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE , .	05/2015	720.00 678.54	678.54	0.45	- 12/2018	12/2018	- 0(R)	0/38
587	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR , .	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020	0(O) -	0/1

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
588	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR , .	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020	0(0) -	1/1
589	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH , .	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(0) -	1/1
590	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , .	10/1998	550.00 [220100252]517.70	1,566.00	137.40	- -	-	-	0/0
591	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , .	04/1997	162.87 -	541.00	147.39	- -	-	-	0/0
592	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , .	03/1998	280.00 -	1,122.00	834.61	- -	-	-	0/6
593	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTT, WEST BENGAL , .	03/2000	1,049.69 3,385.14	3,404.92	3,544.30	12/2006 -	-	-	0/0
594	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR , .	04/2003	528.65 -	324.66	221.71	- -	-	-	0/0
595	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR , .	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
596	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR , .	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
597	RAMGANJ-MUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH , .	04/2001	470.92 727.13	3,000.00	312.15	- -	03/2017	-	0/0
598	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR , .	04/2003	218.19 -	343.00	191.82	- -	-	-	0/0
599	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE , .	04/2005	230.03 -	230.03	151.26	- -	-	-	0/0
600	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR , .	04/1996	332.92 332.92	477.88	495.40	03/2012 -	-	-	0/0
601	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND , .	04/2008	167.73 -	167.73	84.90	03/2012 -	-	-	0/0
602	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL , .	04/2004	293.74 -	293.74	139.08	12/2010 -	-	-	0/0
603	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH , .	03/2013	307.00 -	307.00	-	- -	-	-	0/0
604	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE , .	03/2007	243.78 -	243.78	27.13	- -	-	-	0/0
605	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH , .	03/2008	195.64 -	195.64	79.93	- -	-	-	0/0
606	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH , .	03/2012	199.75 -	199.75	45.47	- -	-	-	0/0
607	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE , .	03/2013	295.00 -	494.92	0.32	- -	-	-	0/0
608	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN , .	04/2012	246.08 -	246.08	4.13	- -	-	-	0/0
609	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , .	04/2013	236.93 -	262.00	0.41	- -	-	-	0/0
610	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , .	04/2013	323.00 -	323.00	-	- -	-	-	0/0
611	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN , .	04/2011	239.73 -	179.32	30.33	- -	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
612	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , .	04/2011	213.39 -	218.39	21.65	-	-	-	0/0
613	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , .	04/2012	288.97 -	288.97	0.62	-	-	-	0/0
614	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , .	04/2013	242.09 -	242.09	-	-	-	-	0/0
615	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL , .	04/2010	267.37 -	434.00	34.01	-	-	-	0/0
616	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , .	04/2010	553.63 651.17	1,009.00	7.08	-	12/2019	-	0/0
617	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL , .	04/2011	289.64 -	760.00	0.09	-	-	-	0/0
618	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , .	04/2008	490.80 -	490.80	0.39	-	-	-	0/0
619	NAWADA-LAXMIPUR (NL) - [N22000167]JECR,BIHAR , .	04/2008	620.57 -	620.57	-	-	-	-	0/0
620	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]JECR,BIHAR , .	04/2008	445.25 -	445.25	1.14	-	-	-	0/0
621	GAYA-CHATRA (NL) - [N22000169]JECR,MULTI STATE , .	04/2008	415.67 -	415.67	13.88	-	-	-	0/0
622	BIHTA-AURANGABAD (NL) - [N22000170]JECR,BIHAR , .	04/2008	326.20 -	326.20	1.68	-	-	-	0/0
623	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECR,BIHAR , .	04/1999	175.69 -	325.00	253.10	-	-	-	0/0
624	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]JECR,BIHAR , .	04/2006	285.07 -	378.56	111.71	-	-	-	0/0
625	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]JECR,BIHAR , .	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
626	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]JECR,BIHAR , .	04/2008	678.62 -	239.32	17.17	-	-	-	0/0
627	ARARIA-SUPAUL (NL) - [N22000177]JECR,BIHAR , .	04/2008	304.41 -	304.41	0.19	-	-	-	0/0
628	KURSELA-BIHARIGANJ (NL) - [N22000178]JECR,BIHAR , .	04/2008	192.56 -	192.56	0.38	-	-	-	0/0
629	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]JECR,BIHAR , .	04/2008	281.30 -	281.30	0.58	-	-	-	0/0
630	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]JECR,BIHAR , .	04/2004	372.14 -	355.81	283.44	-	-	-	0/0
631	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]JECR,BIHAR , .	04/2009	470.00 -	470.00	40.00	-	-	-	0/0
632	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]JECR,BIHAR , .	04/2013	213.01 -	367.17	13.00	-	-	-	0/0
633	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL , .	04/2009	573.78 -	573.78	166.89	-	-	-	0/0
634	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]JER,MULTI STATE , .	04/1987	406.99 -	406.99	140.17	-	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
635	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , .	04/2007	450.00 -	450.00	7.41	- -	-	-	0/0
636	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , .	04/2010	172.03 -	172.03	5.05	- -	-	-	0/0
637	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , .	04/2011	288.35 -	288.35	6.00	- -	-	-	0/0
638	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , .	04/2011	261.38 -	261.38	14.71	- -	-	-	0/0
639	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE , .	04/2000	157.17 -	157.17	76.53	- -	-	-	0/0
640	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , .	04/2010	174.56 -	174.56	53.02	- -	-	-	0/0
641	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , .	04/2010	277.28 -	277.28	55.74	- -	-	-	0/0
642	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , .	04/2010	296.44 -	296.44	3.86	- -	-	-	0/0
643	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , .	04/2010	157.94 -	157.94	41.67	- -	-	-	0/0
644	BARIAPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , .	04/2007	450.55 -	450.55	10.91	- -	-	-	0/0
645	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , .	04/2010	365.17 -	365.17	1.29	- -	-	-	0/0
646	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , .	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
647	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , .	04/2011	193.44 -	193.44	15.86	- -	-	-	0/0
648	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , .	04/2011	175.80 -	175.80	1.22	- -	-	-	0/0
649	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , .	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
650	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE , .	04/2000	297.47 -	297.47	51.81	- -	-	-	0/0
651	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE , .	04/2003	337.96 -	337.96	60.00	- -	-	-	0/0
652	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , .	04/2009	493.96 -	493.96	118.87	- -	-	-	0/0
653	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , .	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0

Sector Wise Details

(June 2016)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
654	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , .	04/2011	166.89 -	166.89	0.02	-	-	-	0/0
655	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , .	04/2013	1,112.00 -	1,112.00	-	-	-	-	0/1
656	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE , .	04/2008	184.26 -	2,000.00	17.32	-	-	-	0/0
657	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , .	04/2012	377.44 -	377.44	0.36	-	-	-	0/0
658	MANSABHATINDA PH-1 INCLUDING MM FOR RAMAMANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOONL - [N22000268]NR,PUNJAB , .	04/2009	396.04 -	369.00	88.77	-	-	-	0/0
659	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , .	04/1999	156.65 -	156.65	50.64	-	-	-	0/0
660	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , .	04/2007	336.91 -	336.91	142.78	-	-	-	0/0
661	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA , .	04/2011	390.60 -	390.60	2.11	-	-	-	0/0
662	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRIPH-I - [N22000288]SCR,MULTI STATE , .	04/2008	2,050.00 -	2,050.00	176.88	-	-	-	0/1
663	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND , .	04/2012	219.83 -	329.97	0.34	-	-	-	0/0
664	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE , .	04/2010	338.54 -	338.54	104.75	-	-	-	0/0
665	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE , .	04/2008	162.96 -	162.96	141.13	-	-	-	0/0
666	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA , .	04/2013	400.00 -	400.00	-	-	-	-	0/0
667	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH , .	04/2012	380.00 -	380.00	1.02	-	-	-	0/0
668	QADIAN-BEAS - [N22000295]NR,PUNJAB , .	04/2011	205.22 -	205.22	1.54	-	-	-	0/0
669	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , .	04/2011	146.75 -	167.50	0.32	-	-	-	0/0
670	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE , .	04/2012	250.93 -	250.93	-	-	-	-	0/0
671	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL , .	04/2012	255.64 -	255.64	-	-	-	-	0/0
672	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , .	04/2008	466.48 -	800.00	0.83	01/1999	-	-	0/0
673	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL , .	04/2011	276.69 -	426.00	-	01/1999	-	-	0/0
674	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH , .	04/2014	182.92 -	197.73	-	-	-	-	0/0
675	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR , .	05/2015	380.00 -	380.00	-	-	-	-	0/0
676	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA , .	05/2015	400.00 -	400.00	-	-	-	-	0/0
677	BARAMATI - LONAND (54 KM) - [N22000352]CR,MAHARASHTRA , .	02/1998	75.00 736.00	736.00	128.32	-	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		328,791.74	417,811.40	85,292.41				8/87
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
678	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00	604.00	423.83	12/2009	-	-	0/0
679	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU , PPP (BOT)	04/2009	353.37	353.37	365.08	10/2011	06/2016	56(O)	0/0
680	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU , PPP (BOT)	09/2010	1,655.00	1,655.00	641.78	09/2013	-	-	0/0
681	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00	567.00	1,055.94	11/2013	-	-	0/0
682	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18	177.18	40.51	03/2016	03/2016	-	3/4
683	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65	158.65	37.36	03/2016	03/2016	-	3/4
684	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08	244.08	38.32	03/2016	-	-	1/4
685	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00	340.00	-	03/2016	-	-	0/2
686	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00	270.00	19.84	03/2016	-	-	1/4
687	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA , .	03/2011	218.31	339.82	208.28	12/2015	-	-	0/3
688	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , EPC	03/2015	298.33	298.33	18.41	-	-	-	0/4
689	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA , EPC	03/2015	184.05	184.05	21.90	-	-	-	0/4
690	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16	280.16	42.17	-	-	-	0/4
691	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12	201.12	-	02/2015	-	-	0/4
692	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH , .	01/2014	361.30	207.40	192.97	07/2014	-	-	0/1

Sector Wise Details									
(June 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
693	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	-	-	-	0/1
694	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDI/GUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	-	-	-	0/4
695	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	-	-	-	0/0
696	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	0.05	-	-	-	0/0
697	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	69.34	- 03/2013	-	-	0/0
698	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	213.67	- 11/2014	-	-	0/0
699	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	-	-	0/0
700	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	-	-	0/0
701	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	-	-	0/0
702	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
703	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	-	-	-	0/0
704	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
705	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	49.93	-	-	-	0/0
706	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	50.74	-	-	-	0/0
707	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	77.55	-	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
708	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
709	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	217.74	- -	-	-	0/0
710	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
711	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	59.97	01/2015 -	-	-	0/0
712	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	53.14	01/2015 -	-	-	0/0
713	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
714	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
715	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
716	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
717	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
718	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0
719	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0
720	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
721	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM , .	04/2013	151.59 -	151.59	-	08/2013 -	-	-	0/0
722	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
723	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
724	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
725	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
726	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	161.70	-	07/2015 -	-	-	0/0
727	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	-	-	0/0
728	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
729	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	-	-	0/0
730	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.53	- -	-	-	0/0
731	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	101.48	- -	-	-	0/0
732	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	96.10	- -	-	-	0/0
733	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.42	- -	-	-	0/0
734	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
735	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	205.09	05/2015 -	-	-	0/0
736	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	69.06	02/2016 -	-	-	0/0
737	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
738	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	27.40	- -	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
739	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.69	- -	-	-	0/0
740	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	267.63	- -	-	-	0/0
741	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
742	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
743	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	-	-	0/0
744	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
745	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	18.13	- -	-	-	0/0
746	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	-	-	0/0
747	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
748	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	135.20	- -	-	-	0/0
749	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	-	-	0/0
750	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	-	-	0/0
751	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	-	-	0/0
752	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	-	-	0/0
753	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
754	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18 -	-	-	-	-	0/0
755	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , .	07/2015	1,282.94 -	1,282.94 -	-	-	-	-	0/0
756	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01 -	-	-	-	-	0/0
757	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA , .	09/2015	414.51 -	414.00 -	-	-	-	-	0/0
758	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA , .	10/2015	531.13 -	531.13 -	-	-	-	-	0/0
759	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74 -	-	-	-	-	0/0
760	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA , .	10/2015	593.26 -	593.26 -	-	-	-	-	0/0
761	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA , .	12/2015	649.50 -	649.50 -	-	-	-	-	0/0
762	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40 -	54.54	-	-	-	0/0
763	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82 -	590.00	02/2015 -	-	-	0/0
764	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72 -	-	-	-	-	0/0
765	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA , .	08/2015	505.00 -	505.00 -	-	-	-	-	0/0
766	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20 -	-	-	-	-	0/0
767	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00 -	-	10/2013 -	-	-	0/0
768	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00 -	-	10/2013 -	-	-	0/0
769	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA , .	09/2005	168.00 -	168.00 -	279.92	06/2006 -	-	-	0/0
770	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR , .	08/2015	556.07 -	556.07 -	-	-	-	-	0/0
771	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB , .	09/2015	273.06 -	273.06 -	-	-	-	-	0/0
772	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR , .	12/2015	1,041.10 -	1,041.10 -	-	-	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
773	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR , .	08/2015	814.04 -	814.04	-	-	-	-	0/0
774	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI, ODISHA , .	12/2015	752.28 -	752.28	-	-	-	-	0/0
775	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA , .	12/2015	1,423.96 -	1,423.96	-	-	-	-	0/0
776	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH , .	12/2015	596.67 -	596.67	-	-	-	-	0/0
777	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH , .	06/2015	1,012.90 -	1,012.90	-	03/2016 -	-	-	0/0
778	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR , .	08/2015	322.09 -	322.09	-	-	-	-	0/0
779	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH , .	12/2015	509.13 -	509.13	-	-	-	-	0/0
780	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	-	-	-	0/0
781	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR , .	01/1991	642.41 -	642.41	-	-	-	-	0/0
782	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR , .	01/1991	1,167.45 -	1,167.45	-	-	-	-	0/0
783	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH , .	12/2015	726.67 -	726.67	-	-	-	-	0/0
784	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	-	-	0/0
785	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH, UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
786	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH, GOA , EPC	12/2015	773.98 -	773.98	20.88	-	-	-	0/0
787	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH, GOA , EPC	12/2015	819.95 -	819.95	22.00	-	-	-	0/0
788	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA , .	12/2015	479.20 -	479.20	6.14	-	-	-	0/0
789	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR , .	08/2015	399.54 -	399.54	-	-	-	-	0/0
790	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH, BIHAR , .	01/1991	478.35 -	478.35	-	-	-	-	0/0
791	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD, PUNJAB , EPC	06/2015	892.17 -	892.17	45.25	-	-	-	0/0
792	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD, PUNJAB , EPC	06/2015	899.21 -	899.21	42.99	-	-	-	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
793	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0
794	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
795	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	-	-	-	0/0
796	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	-	-	-	0/0
797	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR , .	10/2013	278.39 -	278.39	22.18	08/2014 -	-	-	0/0
798	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA , .	01/2014	292.98 -	292.98	114.78	11/2014 -	-	-	0/0
799	MEERUT-BULANDSHAHAHAR - [N24000539]NHAI,UTTAR PRADESH , .	01/2016	683.24 -	683.24	0.45	-	-	-	0/0
800	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH , .	01/2016	701.12 -	701.12	-	-	-	-	0/0
801	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH , .	01/2016	1,081.57 -	1,081.57	-	-	-	-	0/0
802	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA , .	03/2016	197.69 -	197.69	-	-	-	-	0/0
803	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH , .	03/2016	676.73 -	676.73	-	-	-	-	0/0
804	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH , .	01/2016	1,134.97 -	1,134.97	-	-	-	-	0/0
805	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH , .	02/2016	273.20 -	273.20	-	-	-	-	0/0
806	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH , .	03/2016	1,404.50 -	1,404.50	-	-	-	-	0/0
807	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND , .	02/2016	997.15 -	997.15	-	-	-	-	0/0
808	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH , .	03/2016	1,396.74 -	1,396.74	-	-	-	-	0/0
809	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA , .	02/2016	1,069.65 -	1,069.65	-	-	-	-	0/0
810	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH , .	03/2016	1,587.49 -	1,587.49	-	-	-	-	0/0
811	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA , .	03/2016	701.40 -	701.40	-	-	-	-	0/0

Sector Wise Details									
(June 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
812	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL , .	03/2016	229.37 -	229.37	-	-	-	-	0/0
813	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA , .	03/2016	870.00 -	870.00	-	-	-	-	0/0
814	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU , .	02/2016	707.82 -	707.82	-	-	-	-	0/0
815	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH , .	03/2016	899.00 -	899.00	-	-	-	-	0/0
816	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU , .	02/2016	641.17 -	641.17	-	-	-	-	0/0
817	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA , .	03/2016	546.00 -	546.00	-	-	-	-	0/0
818	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND , .	03/2016	720.00 -	720.00	-	-	-	-	0/0
819	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA , .	03/2016	591.66 -	591.66	-	-	-	-	0/0
820	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA , .	03/2016	244.00 -	244.00	-	-	-	-	0/0
821	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND , .	03/2016	1,443.00 -	1,443.00	-	-	-	-	0/0
822	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH , .	03/2016	1,668.00 -	1,668.00	-	-	-	-	0/0
823	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH , .	03/2016	1,408.00 -	1,408.00	-	-	-	-	0/0
824	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH , .	03/2016	1,737.00 -	1,737.00	-	-	-	-	0/0
825	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA , .	04/2016	804.97 -	804.97	-	-	-	-	0/0
826	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT , .	05/2016	998.18 -	998.18	-	-	-	-	0/0
827	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT , .	05/2016	834.64 -	834.64	-	-	-	-	0/0
828	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT , .	05/2016	723.64 -	723.64	-	-	-	-	0/0
829	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT , .	05/2016	763.08 -	763.08	-	-	-	-	0/0

Sector Wise Details									
(June 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
830	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT , .	05/2016	425.60 -	425.60	-	-	-	-	0/0
831	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT , .	05/2016	364.56 -	364.56	-	-	-	-	0/0
832	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH, BIHAR , .	01/2013	322.01 -	322.01	102.34	08/2014 -	08/2014	-	0/0
833	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH, BIHAR , .	02/2016	178.85 -	178.85	-	05/2016 -	05/2016	-	0/0
834	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH, BIHAR , .	02/2016	553.30 -	553.30	-	05/2016 -	05/2016	-	0/0
835	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH, BIHAR , .	08/2015	288.24 -	288.24	16.23	11/2015 -	11/2015	-	0/0
836	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/0
837	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD, MAHARASHTRA , .	03/2016	1,101.58 -	1,101.58	-	-	-	-	0/0
838	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	1,722.39	04/2015 -	01/2017	21(O) -	0/0
839	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	0(O) -	0/0
840	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL, ASSAM , EPC	06/2016	829.00 -	829.00	-	01/2019 -	01/2019	0(O) -	0/4
841	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL, ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	-	01/2019 -	01/2019	0(O) -	0/0
842	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU , .	07/2014	401.11 -	401.11	239.02	01/2017 -	01/2017	0(O) -	0/0
843	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH, KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
844	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD, ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	0(O) -	0/0
845	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL , .	10/2015	361.15 -	361.15	-	-	01/2018	-	0/0
846	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	1,254.01	-	01/2018	-	0/0
847	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	1,474.76	01/2018 -	01/2018	0(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
848	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM , EPC	01/2016	252.00 -	252.00	-	01/2016 -	01/2016	-	0/0
849	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31(O) -	0/0
850	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,878.76	09/2015 -	02/2017	17(O) -	0/0
851	REHABILITATION AND UPGRADE OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD, TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	0(O) -	0/1
852	REHABILITATION AND UPGRADE OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD, ANDHRA PRADESH , .	02/2015	241.61 -	241.61	46.68	02/2017 -	02/2017	0(O) -	0/1
853	REHABILITATION AND UPGRADE OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	0(O) -	0/0
854	REHABILITATION UPGRADE OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24(O) -	0/1
855	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN , .	08/2015	538.08 -	538.08	57.99	02/2018 -	02/2018	0(O) -	0/0
856	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA , .	08/2015	723.54 -	723.54	259.05	02/2018 -	02/2018	0(O) -	0/0
857	JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN , .	08/2015	482.27 -	482.27	76.80	02/2018 -	02/2018	0(O) -	0/0
858	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD, ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	0(O) -	0/0
859	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD, ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
860	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN , .	08/2015	275.90 -	275.90	-	- -	02/2018	- -	0/0
861	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM , .	12/2003	212.00 -	212.00	122.22	09/2007 -	03/2017	114(O) -	0/0
862	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION KM 240 270KM - [N24000149]NHAI, KERALA , PPP (BOT)	02/2010	617.00 -	617.00	284.10	08/2012 -	03/2017	55(O) -	0/0
863	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR , .	10/2011	375.09 -	375.09	506.50	04/2014 -	03/2017	35(O) -	0/0
864	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,630.30	06/2014 -	03/2017	33(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
865	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	901.00	09/2016 -	03/2017	6(O) -	0/0
866	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	-	03/2018 -	03/2018	0(O) -	0/4
867	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB , .	01/2014	523.85 -	523.85	103.60	01/2016 -	03/2017	14(O) -	0/0
868	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN , .	09/2015	567.51 -	567.51	42.79	03/2018 -	03/2018	0(O) -	0/0
869	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017	0(O) -	0/0
870	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	0(O) -	0/0
871	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	6.33	03/2018 -	03/2018	0(O) -	0/0
872	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL , EPC	01/1991	322.00 -	322.00	66.59	03/2018 -	03/2018	0(O) -	0/0
873	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017	0(O) -	0/0
874	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017	0(O) -	0/0
875	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH , .	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(O) -	0/0
876	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH , .	09/2015	664.53 -	664.53	-	03/2018 -	03/2018	0(O) -	0/0
877	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH , .	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(O) -	0/0
878	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE , .	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
879	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH , .	09/2015	785.78 -	785.78	-	03/2018 -	03/2018	0(O) -	0/0
880	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0
881	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH , .	09/2015	934.46 -	934.46	57.43	03/2018 -	03/2018	0(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
882	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA , .	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69(O) -	0/0
883	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
884	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	681.17	03/2014 -	04/2017	37(O) -	0/0
885	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	53.59	-	04/2018	-	0/1
886	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	-	04/2017 -	04/2017	0(O) -	0/3
887	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN , .	10/2014	206.12 -	206.12	112.00	04/2017 -	04/2017	0(O) -	0/0
888	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN , .	10/2014	264.72 -	264.72	116.15	04/2017 -	04/2017	0(O) -	0/0
889	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA , .	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
890	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	95.00	04/2018 -	04/2018	0(O) -	0/0
891	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR , .	08/2015	516.13 -	516.13	42.36	-	04/2018	-	0/0
892	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN , .	12/2003	275.00 -	281.31	185.05	02/2010 -	05/2017	87(O) -	0/0
893	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA , PPP (BOT)	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58(O) -	3/3
894	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL , PPP (BOT)	02/2011	580.43 -	580.43	269.89	08/2013 -	05/2017	45(O) -	0/0
895	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	564.59	06/2015 -	05/2017	23(O) -	0/0
896	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA , PPP (BOT)	10/2013	283.25 -	283.25	180.61	10/2015 -	05/2017	19(O) -	0/0
897	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24(O) -	2/4
898	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	-	05/2018 -	05/2018	0(O) -	0/1
899	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	46.11	05/2018 -	05/2018	0(O) -	0/4
900	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN , .	11/2014	279.14 -	279.14	105.62	05/2017 -	05/2017	0(O) -	0/0
901	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH , .	05/2015	261.09 -	261.09	34.10	05/2017 -	05/2017	0(O) -	0/0

Sector Wise Details									
(June 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
902	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	0.54	05/2017 -	05/2017	0(O) -	0/0
903	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	0(O) -	0/0
904	SHAHDL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	166.22	05/2017 -	05/2017	0(O) -	0/0
905	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAU LI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	219.99	05/2016 -	05/2016	-	0/0
906	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , .	01/1991	229.41 -	229.41	10.32	05/2018 -	05/2018	0(O) -	0/0
907	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0
908	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	-	05/2018 -	05/2018	0(O) -	0/4
909	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , .	02/2015	327.32 -	327.32	162.33	05/2017 -	05/2017	0(O) -	0/0
910	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA , .	11/2015	867.66 -	867.66	200.46	-	05/2018	-	0/0
911	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR , .	05/2015	581.84 -	581.84	-	05/2017 -	05/2017	0(O) -	0/0
912	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH , .	12/2003	155.00 -	201.66	248.73	09/2008 -	06/2016	93(O) -	0/0
913	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM , .	12/2003	195.00 -	195.00	294.65	06/2008 -	06/2016	96(O) -	0/0
914	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM , .	12/2003	264.72 -	264.72	320.02	06/2008 -	06/2016	96(O) -	0/0
915	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , .	09/2010	946.00 -	946.00	818.53	-	06/2016	-	3/3
916	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT , PPP (BOT)	03/2011	785.50 -	785.50	923.28	08/2013 -	06/2016	34(O) -	0/3
917	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU , PPP (BOT)	06/2011	535.00 -	535.00	924.70	12/2013 -	06/2016	30(O) -	0/0
918	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	691.92	01/2014 -	06/2017	41(O) -	0/0
919	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,761.23	09/2014 -	06/2017	33(O) -	0/0
920	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	97.05	-	06/2017	-	0/4

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
940	FOUR LANE OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23	763.23	-	06/2019	06/2019	0(O)	0/0
941	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI,RAJASTHAN , PPP (BOT)	06/2016	725.95	725.95	-	06/2019	06/2019	0(O)	0/0
942	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN , .	06/2016	649.00	649.00	-	06/2019	06/2019	0(O)	0/0
943	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM , .	12/2003	237.80	237.80	409.39	06/2008	07/2016	97(O)	0/0
944	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR , .	12/2003	332.94	332.94	514.30	09/2008	07/2016	94(O)	0/0
945	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM , .	12/2003	175.96	175.96	309.01	04/2008 08/2016	07/2016	99(O) -1(R)	0/0
946	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM , .	12/2003	225.00	225.00	313.71	06/2008 06/2016	07/2016	97(O) 1(R)	0/0
947	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM , .	12/2003	160.00	160.00	200.36	05/2008 07/2016	07/2016	98(O) 0(R)	0/0
948	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00	1,987.00	1,682.27	07/2015	07/2017	24(O)	0/0
949	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00	2,159.00	4,211.50	06/2015	07/2016	13(O)	0/0
950	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54	351.54	351.23	05/2013	07/2016	38(O)	0/0
951	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00	1,141.00	1,948.72	08/2013	07/2016	35(O)	0/0
952	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT , PPP (BOT)	09/2010	805.39	805.39	1,406.70	03/2013	07/2016	40(O)	0/0
953	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00	664.00	654.59	02/2014	07/2016	29(O)	0/0
954	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00	574.00	899.71	03/2014	07/2016	28(O)	0/0
955	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54	511.54	549.10	11/2013	07/2016	32(O)	0/0
956	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN , .	08/2010	267.81	267.81	699.60	02/2013	07/2016	41(O)	0/0
957	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN , PPP (BOT)	12/2011	2,388.51	2,388.00	2,490.61	06/2014	07/2016	25(O)	0/0
958	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN , PPP (ANNUITY)	03/2012	333.51	333.51	226.96	09/2014	07/2016	22(O)	0/0
959	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN , .	01/2014	158.04	158.04	129.37	12/2015	07/2016	7(O)	0/0
960	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN , .	01/2014	368.15	368.15	190.73	01/2016	07/2016	6(O)	0/0
961	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79	187.79	57.60	07/2016	07/2016	0(O)	0/12

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
962	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	24(O) -	0/1
963	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP, MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	63.38	07/2017 -	07/2017	0(O) -	0/0
964	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN , .	07/2015	455.60 -	455.60	54.50	07/2017 -	07/2017	0(O) -	0/0
965	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA , .	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
966	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,101.09	07/2017 -	07/2017	0(O) -	0/0
967	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]NHAI, RAJASTHAN , EPC	03/2012	914.50 -	914.50	1,128.25	10/2015 -	07/2016	9(O) -	0/0
968	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]NHAI, HARYANA , PPP (BOT)	03/2013	959.25 -	959.25	1,229.40	06/2016 -	07/2016	1(O) -	0/0
969	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	2,946.14	10/2011 -	07/2016	57(O) -	0/0
970	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH , .	06/2016	667.00 -	667.00	-	07/2018 -	07/2018	0(O) -	0/0
971	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI, MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	79.70	07/2018 -	07/2018	0(O) -	0/0
972	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH, BIHAR , .	11/2013	683.83 -	683.83	-	07/2016 -	07/2016	0(O) -	0/0
973	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH, BIHAR , .	02/2014	665.50 -	665.50	-	07/2016 -	07/2016	0(O) -	0/0
974	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH, BIHAR , .	03/2015	206.80 -	206.80	-	07/2016 -	07/2016	0(O) -	0/0
975	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM , .	12/2003	280.00 -	361.00	427.01	02/2009 -	08/2016	90(O) -	0/0
976	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	889.94	03/2013 -	08/2016	41(O) -	0/0
977	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,016.24	05/2013 -	08/2016	39(O) -	0/0
978	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT , PPP (BOT)	12/2010	1,008.50 -	1,008.50	1,282.25	06/2013 -	08/2016	38(O) -	0/3
979	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU , .	06/2011	600.00 -	600.00	312.80	06/2013 -	08/2016	38(O) -	0/0
980	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,488.67	02/2014 -	08/2017	42(O) -	2/2
981	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN , PPP (BOT)	10/2013	677.79 -	677.79	878.97	04/2016 -	08/2016	4(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
982	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23(O) -	0/4
983	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT , .	03/2014	503.16 -	503.16	258.39	08/2016 -	08/2016	0(O) -	0/0
984	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	75.32	08/2016 -	08/2016	0(O) -	0/0
985	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	393.88	09/2015 -	08/2016	11(O) -	0/0
986	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	234.67	08/2016 -	08/2016	0(O) -	0/0
987	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH , PPP (BOT)	02/2012	912.00 -	912.00	120.43	08/2016 -	08/2016	0(O) -	0/0
988	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	899.00	08/2016 -	08/2017	12(O) -	0/0
989	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	01/1991	1,388.00 -	1,388.00	112.51	- -	08/2018	- -	0/0
990	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	0(O) -	0/0
991	BRAHMPUTRA BRIDGE,NH NO-31 - [N2400063]NHAI,ASSAM , .	12/2003	217.61 309.56	309.56	399.08	04/2010 09/2016	09/2016	77(O) 0(R)	0/0
992	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH , .	12/2003	348.16 -	348.16	398.79	09/2007 -	09/2016	108(O) -	0/0
993	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	474.72	05/2013 -	09/2016	40(O) -	0/0
994	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,745.49	08/2013 -	09/2017	49(O) -	0/0
995	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	356.34	01/2014 -	09/2016	32(O) -	0/0
996	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTERAKHAND , .	11/2011	478.51 -	478.00	283.84	10/2013 -	09/2016	35(O) -	0/0
997	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN , .	03/2014	240.10 -	240.10	162.19	03/2016 -	09/2016	6(O) -	0/0
998	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017	0(O) -	0/0
999	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA , .	05/2015	709.00 -	709.00	19.24	09/2017 -	09/2017	0(O) -	0/0
1000	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND , .	09/2015	341.61 -	341.61	140.65	09/2017 -	09/2017	0(O) -	0/0
1001	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN , .	09/2014	425.19 -	425.19	274.20	09/2016 -	09/2016	0(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1002	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH , .	09/2015	368.73 -	368.73	104.81	09/2016 -	09/2017	12(O) -	0/0
1003	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	192.55	08/2015 -	09/2016	13(O) -	0/0
1004	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,377.79	-	09/2016	-	0/0
1005	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR , .	10/2014	377.64 -	377.64	-	03/2014 -	09/2016	30(O) -	0/0
1006	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	871.15	09/2014 -	10/2017	37(O) -	0/3
1007	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU , PPP (BOT)	06/2013	1,287.95 -	1,287.95	757.57	11/2015 -	10/2017	23(O) -	0/0
1008	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	19.23	-	10/2017	-	0/4
1009	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
1010	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	-	10/2018 -	10/2018	0(O) -	0/4
1011	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	0(O) -	0/0
1012	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH , .	04/2014	351.34 -	351.34	199.74	01/2016 -	10/2016	9(O) -	0/0
1013	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH , .	04/2014	495.78 -	495.78	301.70	01/2016 -	10/2016	9(O) -	0/0
1014	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN , .	01/1991	269.26 -	269.26	218.10	10/2016 -	10/2016	0(O) -	0/0
1015	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	17.71	10/2016 -	10/2016	0(O) -	0/0
1016	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	41.21	10/2017 -	10/2017	0(O) -	0/0
1017	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	200.21	10/2016 -	10/2016	0(O) -	0/0
1018	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	21.03	10/2016 -	10/2016	0(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1019	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	0(O) -	0/0
1020	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN , .	10/2015	597.00 -	597.00	55.86	10/2017 -	10/2017	0(O) -	0/0
1021	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR , .	01/2014	1,408.85 -	1,408.85	-	10/2016 -	10/2016	0(O) -	0/0
1022	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,492.63	11/2016 -	11/2016	0(O) -	0/0
1023	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA , .	06/2014	260.39 -	260.39	102.12	11/2016 -	11/2016	0(O) -	0/2
1024	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	108.37	11/2016 -	11/2016	0(O) -	0/4
1025	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017	0(O) -	0/0
1026	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24(O) -	0/4
1027	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	24(O) -	0/4
1028	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	-	11/2018 -	11/2018	0(O) -	0/4
1029	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	-	11/2018 -	11/2018	0(O) -	0/4
1030	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24(O) -	0/0
1031	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24(O) -	0/0
1032	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU , .	05/2015	1,387.11 -	1,387.11	190.00	11/2017 -	11/2017	0(O) -	0/0
1033	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU , .	11/2014	563.92 -	563.92	124.09	11/2016 -	11/2016	0(O) -	0/0
1034	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA , .	06/2015	845.24 -	845.24	108.33	-	11/2017	-	0/0
1035	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH , .	02/2013	1,232.00 -	1,232.00	1,123.15	08/2015 -	11/2016	15(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1036	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	0(O) -	0/0
1037	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM , .	12/2003	230.00 -	230.00	203.60	06/2005 -	12/2016	138(O) -	0/0
1038	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM , .	12/2003	199.81 -	385.13	211.01	04/2009 -	12/2016	92(O) -	0/0
1039	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM , .	12/2003	167.64 -	167.64	277.36	11/2008 -	12/2016	97(O) -	0/0
1040	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM , .	12/2003	155.04 -	280.13	196.86	11/2008 -	12/2016	97(O) -	0/0
1041	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM , .	12/2003	200.00 -	200.00	247.56	04/2009 -	12/2016	92(O) -	0/0
1042	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM , .	12/2003	245.00 -	245.00	214.88	03/2008 07/2016	12/2016	105(O) 5(R)	0/0
1043	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM , .	12/2003	208.00 230.00	208.00	306.09	04/2008 01/2017	12/2016	104(O) -1(R)	0/0
1044	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM , .	12/2003	196.00 -	331.23	365.05	07/2009 -	12/2016	89(O) -	0/0
1045	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	469.41	05/2010 -	12/2016	79(O) -	0/0
1046	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 2,782.54	1,509.10	3,200.86	09/2012 -	12/2016	51(O) -	2/3
1047	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.29	08/2011 -	12/2016	64(O) -	2/2
1048	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,822.02	11/2011 -	12/2016	61(O) -	0/0
1049	INDORE-JHABUA-GUJARAT/MP - [N24000136]NHAI, MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	1,206.10	04/2013 -	12/2016	44(O) -	0/0
1050	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,038.84	07/2013 -	12/2016	41(O) -	0/0
1051	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	39(O) -	0/0
1052	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	12/2016	42(O) -	0/0
1053	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,488.49	08/2014 -	12/2016	28(O) -	0/0
1054	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	1,893.03	03/2013 -	12/2016	45(O) -	0/0
1055	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,415.99	07/2013 -	12/2016	41(O) -	0/0
1056	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	880.67	02/2013 -	12/2016	46(O) -	0/0
1057	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	12/2016	37(O) -	0/0
1058	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1059	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	974.56	07/2013 -	12/2016	41(O) -	0/0
1060	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55(O) -	0/0
1061	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	309.66	08/2013 -	12/2017	52(O) -	0/0
1062	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	622.90	10/2013 -	12/2017	50(O) -	0/0
1063	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,802.56	05/2014 -	12/2016	31(O) -	0/0
1064	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	604.75	07/2013 -	12/2016	41(O) -	0/0
1065	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,363.70	06/2014 -	12/2016	30(O) -	0/0
1066	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA , PPP (BOT)	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35(O) -	0/0
1067	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	875.56	08/2013 -	12/2016	40(O) -	0/0
1068	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	600.65	09/2013 -	12/2016	39(O) -	0/0
1069	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,089.05	03/2013 -	12/2016	45(O) -	0/0
1070	4-LANNING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,133.37	08/2013 -	12/2016	40(O) -	0/0
1071	6-LANNING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,430.70	09/2014 -	12/2016	27(O) -	0/0
1072	2-LANNING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR , PPP (BOT)	07/2012	356.40 -	356.40	349.50	07/2014 -	12/2017	41(O) -	0/0
1073	2-LANNING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2016	32(O) -	0/0
1074	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA , .	12/2011	942.69 -	942.69	347.50	06/2014 -	12/2016	30(O) -	0/0
1075	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	12/2016	12(O) -	0/3
1076	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1077	REHABILITATION AND UPGRADE OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD, TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	0(O) -	0/4
1078	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD, ANDHRA PRADESH , .	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	12(O) -	0/2
1079	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH , .	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12(O) -	0/0
1080	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU , .	06/2015	563.92 -	563.92	13.66	12/2017 -	12/2017	0(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1081	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH , .	06/2014	301.04 -	301.04	57.42	01/2016 -	12/2016	11(O) -	0/0
1082	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA , .	06/2015	996.37 -	996.37	-	12/2017 -	12/2017	0(O) -	0/0
1083	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	0(O) -	0/0
1084	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	225.02	-	12/2018 -	12/2018	0(O) -	0/0
1085	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
1086	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	329.25	11/2016 -	12/2016	1(O) -	0/0
1087	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , .	09/2014	479.00 -	479.00	360.06	-	12/2016	-	0/0
1088	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , .	12/2015	239.23 -	239.23	22.60	12/2017 -	12/2017	0(O) -	0/0
1089	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , .	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
1090	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , .	03/2015	928.83 -	928.83	13.80	-	12/2017	-	0/0
1091	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,357.85	11/2015 -	12/2016	13(O) -	0/0
1092	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB , .	10/2015	447.29 -	447.29	-	12/2017 -	12/2017	0(O) -	0/0
1093	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , .	08/2015	854.80 -	854.80	79.59	-	12/2017	-	0/0
1094	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	-	-	-	0/0
	Total		263,809.81 -	266,605.47	127,928.28				22/163
	<u>SHIPPING AND PORTS</u>								
1095	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1096	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , .	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
1097	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU , .	12/2014	274.85 -	274.85	160.22	04/2017 -	04/2017	0(O) -	0/1
1098	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 235.15	235.15	157.96	06/2017 -	06/2017	0(O) -	0/1
1099	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 600.00	600.00	139.80	03/2006 01/2016	07/2016	124(O) 6(R)	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1100	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA , .	03/2007	245.67 373.22	409.83	350.68	04/2009 03/2010	08/2016	88(O) 77(R)	0/0
1101	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 669.49	669.46	415.01	12/2010 12/2018	12/2018	96(O) 0(R)	0/0
1102	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	9.77	12/2017 -	12/2017	0(O) -	0/1
	Total		4,117.75 -	5,085.02	2,064.65				0/3
	<u>TELECOMMUNICATIONS</u>								
1103	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , .	03/2012	13,334.00 -	13,334.00	-	07/2015 -	-	-	0/0
1104	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	301.57	09/2014 -	03/2017	30(O) -	0/70
	Total		15,445.17 -	15,345.17	301.57				0/70
	<u>URBAN DEVELOPMENT</u>								
1105	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI , .	07/2012	884.30 -	884.30	285.09	08/2014 -	-	-	0/0
1106	CONSTRUCTION OF 100 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI , Central Sector Projects	06/2015	197.33 -	197.33	0.14	- -	-	-	0/0
1107	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB , .	02/2014	388.00 -	388.00	128.37	01/2015 -	-	-	3/12
1108	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU , .	12/2015	209.00 -	209.00	-	- -	-	-	0/0
1109	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU , .	04/2014	332.72 -	332.72	117.94	09/2016 01/2017	01/2017	4(O) 0(R)	0/0
1110	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA , .	02/2014	26,405.14 -	26,405.14	700.85	02/2019 -	03/2020	13(O) -	0/0
1111	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH , .	12/2012	188.87 -	188.87	10,255.48	12/2014 12/2016	03/2017	27(O) 3(R)	0/1
1112	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH , .	11/2012	270.83 270.83	270.83	81.52	11/2014 03/2017	03/2017	28(O) 0(R)	0/0
1113	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA , .	06/2010	205.00 142.37	191.97	108.07	03/2012 08/2016	03/2017	60(O) 7(R)	0/0
1114	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH , .	06/2014	157.84 -	157.84	40.61	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details									
(June 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1115	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA , .	08/2014	8,680.00 -	8,680.00	161.22	03/2018 -	03/2018	0(O) -	0/0
1116	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN , Central Sector Projects	08/2014	350.02 -	350.02	144.54	03/2015 03/2017	03/2017	24(O) 0(R)	0/0
1117	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL , .	02/2014	156.57 -	156.57	48.61	09/2015 07/2016	04/2017	19(O) 9(R)	1/7
1118	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI , .	05/2009	261.85 -	261.85	199.73	05/2013 10/2015	06/2016	37(O) 8(R)	0/0
1119	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA , .	07/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017	-1(O) -	0/0
1120	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU , .	02/2009	14,600.00 14,600.00	14,600.00	12,738.83	12/2015 -	08/2016	8(O) -	1/24
1121	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND , .	09/2012	171.86 -	171.86	24.51	03/2016 -	09/2017	18(O) -	0/6
1122	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	17.54	03/2015 10/2017	10/2017	31(O) 0(R)	0/0
1123	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA , .	05/2006	6,395.00 13,845.01	14,405.01	13,973.45	06/2011 11/2016	11/2016	65(O) 0(R)	3/3
1124	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA , .	12/2012	315.00 315.00	315.00	196.71	06/2015 08/2016	11/2016	17(O) 3(R)	0/0
1125	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI , .	06/2012	4,264.00 -	5,298.00	1,528.93	11/2019 -	11/2019	0(O) -	0/7
1126	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI , .	09/2011	38,585.00 -	38,585.00	23,763.22	03/2016 -	12/2016	9(O) -	0/0
1127	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA , .	02/2011	241.33 356.59	356.59	108.43	11/2014 -	12/2017	37(O) -	0/0
1128	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI , .	10/2013	1,219.21 -	1,219.21	14.23	10/2019 -	12/2018	-10(O) -	0/0
1129	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI , .	05/2012	405.01 405.01	405.01	236.45	12/2014 -	12/2016	24(O) -	1/3
1130	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA , .	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	-	0/0
1131	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA , .	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
1132	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH , .	08/2007	246.90 -	246.90	-	-	-	-	0/0
	Total		133,830.49 -	142,976.73	64,874.47				9/63
	Grand Total		1,348,915.99	1,523,477.16	630,921.81				1793/3954


Summary of projects in the Flash Report for the month of June, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1076
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects Added in Current Month	57
Number of Projects in Current Month	1132


Brief Analysis

Project Status with respect to Original Schedule: Out of 1132 projects, 5 projects are ahead of schedule, 259 projects are on schedule 350 projects are delayed. 454 projects do not have fixed dates of commissioning. 64 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

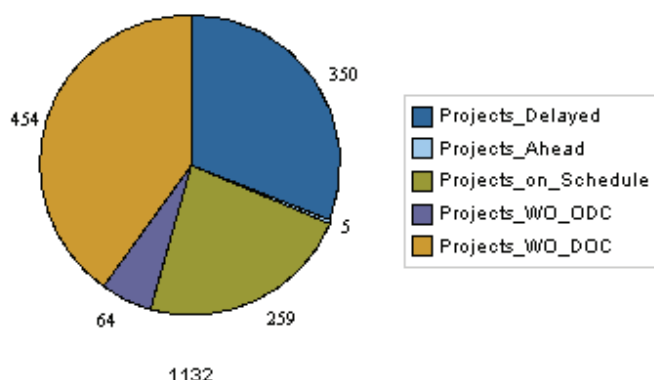

Investment Scenario

Total original cost of implementation of 1132 projects when sanctioned, was of the order of Rs. 1348915.99 crore but this was subsequently revised to Rs. 1523477.16 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till June, 2016 is Rs. 630921.81 crore, which is 41.4% of the revised cost of the projects.

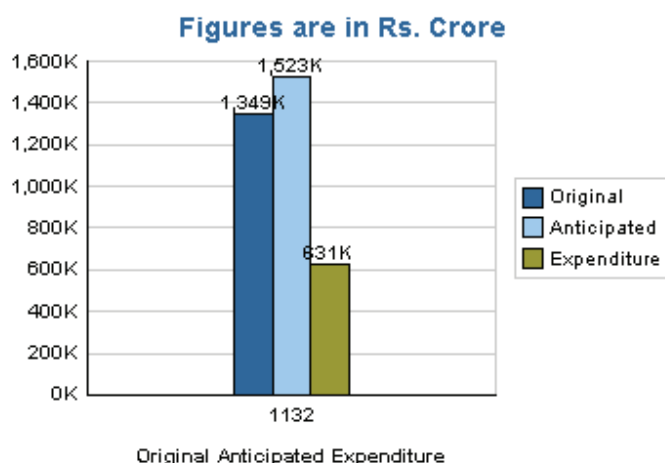

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed. 1 project does not have fixed dates of commissioning.

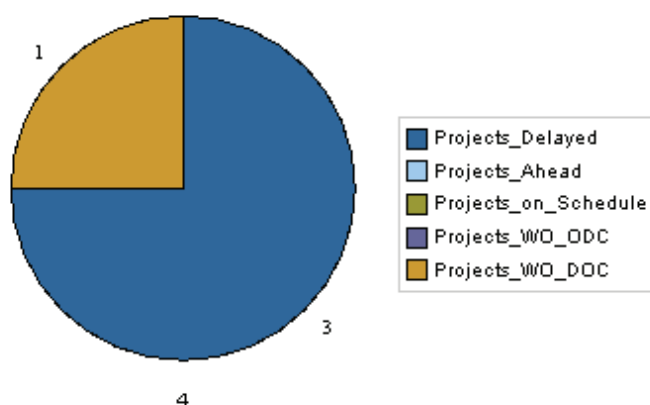

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till June, 2016 is Rs. 41625.84 crore, which is 80.2% of the revised cost of the projects.

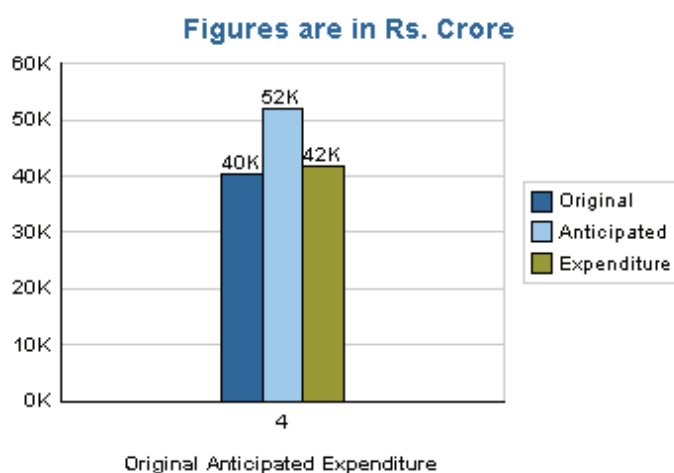

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 1 project is delayed. 2 projects do not have fixed dates of commissioning.

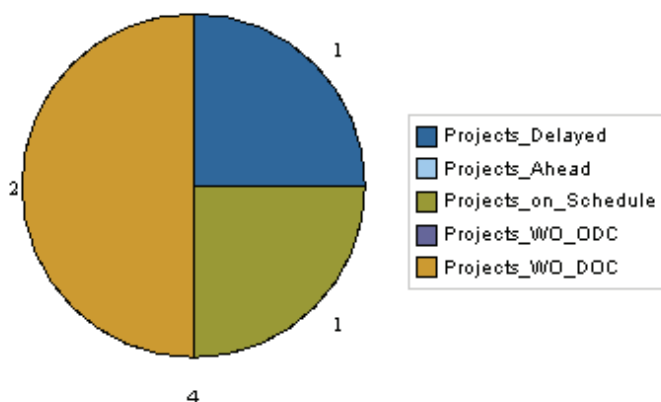

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1177.28 crore but this was subsequently anticipated to Rs. 1186.17 crore implying a cost overrun of .8%. The expenditure incurred on these projects till June, 2016 is Rs. 795.81 crore, which is 67.1% of the revised cost of the projects.

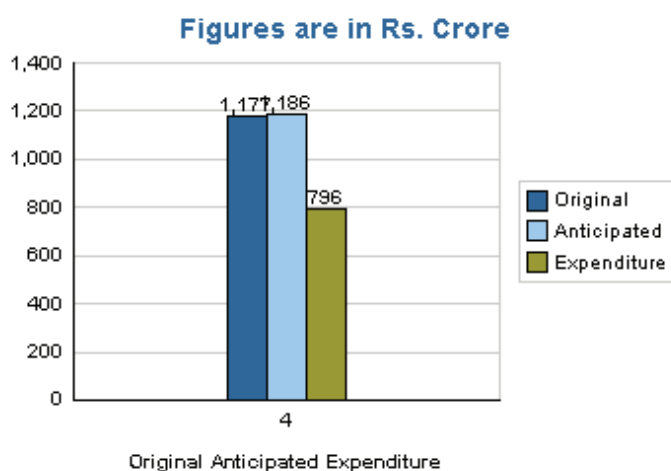

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	90
Number of Projects On Schedule	46
Number of Projects Delayed	36
Number of Projects Ahead	1

Number of Projects Without Date Of Commissioning	7
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 90 projects, 1 project is ahead of schedule, 46 projects are on schedule 36 projects are delayed. 7 projects do not have fixed dates of commissioning.

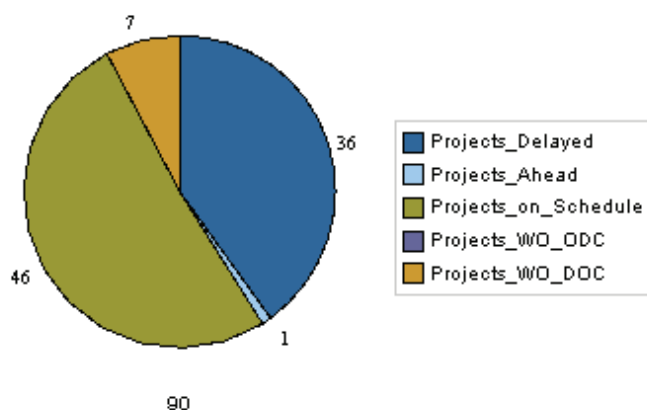

Investment Scenario

Total original cost of implementation of 90 projects when sanctioned, was of the order of Rs. 69573.4 crore but this was subsequently anticipated to Rs. 70943.19 crore implying a cost overrun of 2%. The expenditure incurred on these projects till June, 2016 is Rs. 14098.19 crore, which is 19.9% of the revised cost of the projects.

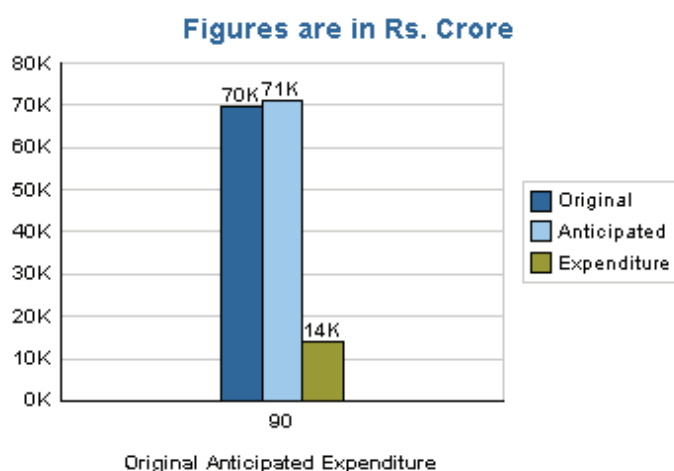

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.



Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 692.29 crore implying a cost overrun of 1.7%. The expenditure incurred on these projects till June, 2016 is Rs. 96.77 crore, which is 14% of the revised cost of the projects.

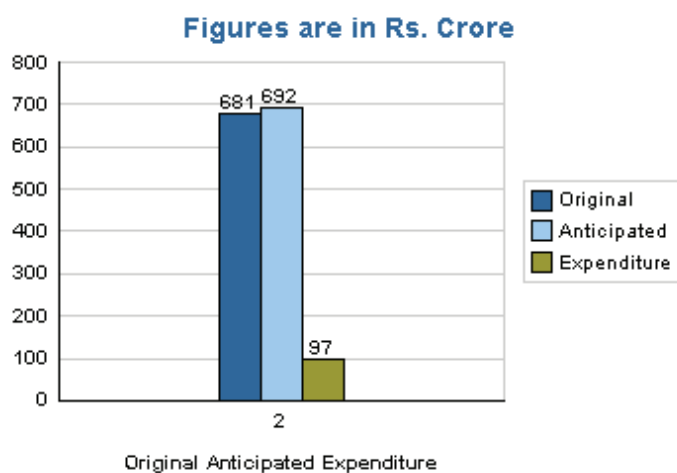

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	3
Number of Projects On Schedule	2
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are on schedule 1 project is delayed.

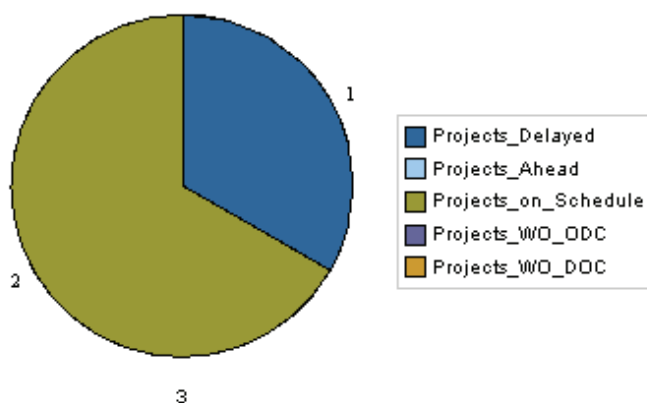

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 2555.63 crore but this was subsequently anticipated to Rs. 1875.63 cr. The expenditure incurred on these projects till June, 2016 is Rs. 347.32 crore, which is 18.5% of the revised cost of the projects.

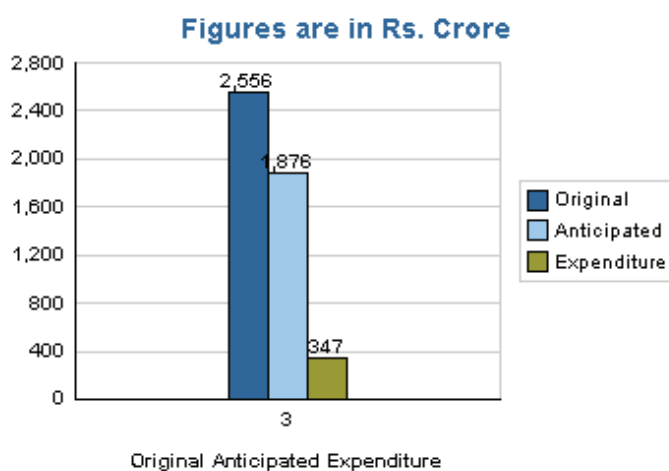

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	32
Number of Projects On Schedule	13
Number of Projects Delayed	14
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 32 projects, 13 projects are on schedule 14 projects are delayed. 4 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

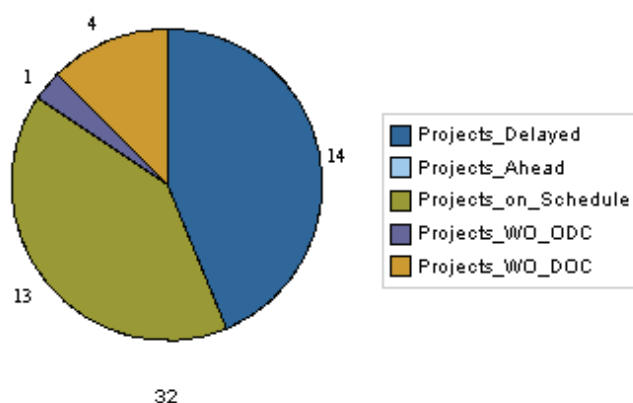

Investment Scenario

Total original cost of implementation of 32 projects when sanctioned, was of the order of Rs. 53059.66 crore but this was subsequently anticipated to Rs. 53588.97 crore implying a cost overrun of 1%. The expenditure incurred on these projects till June, 2016 is Rs. 32166.42 crore, which is 60% of the revised cost of the projects.

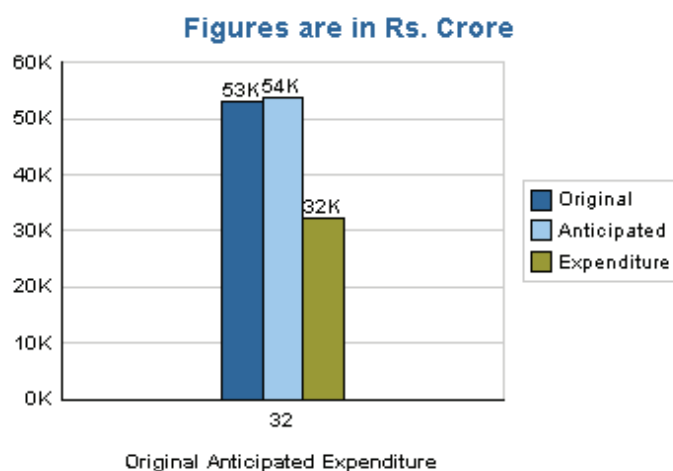

Sector wise current status of projects on the Flash Report

PETROLEUM


Current Status:

Number of Projects	74
Number of Projects On Schedule	24
Number of Projects Delayed	41
Number of Projects Ahead	2

Number of Projects Without Date Of Commissioning	7
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 74 projects, 2 projects are ahead of schedule, 24 projects are on schedule 41 projects are delayed. 7 projects do not have fixed dates of commissioning.

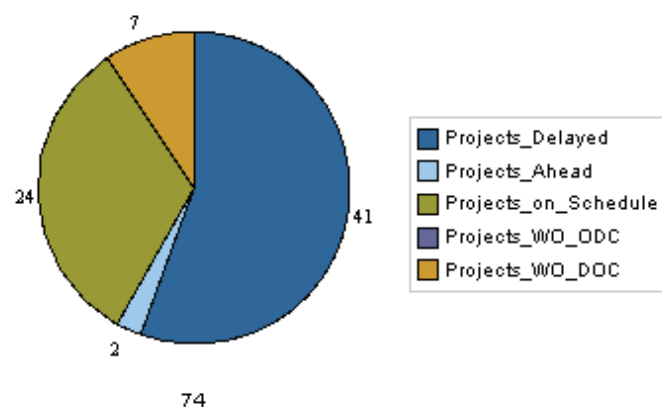

Investment Scenario

Total original cost of implementation of 74 projects when sanctioned, was of the order of Rs. 110511.66 crore but this was subsequently anticipated to Rs. 114415.93 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till June, 2016 is Rs. 45506.46 crore, which is 39.8% of the revised cost of the projects.

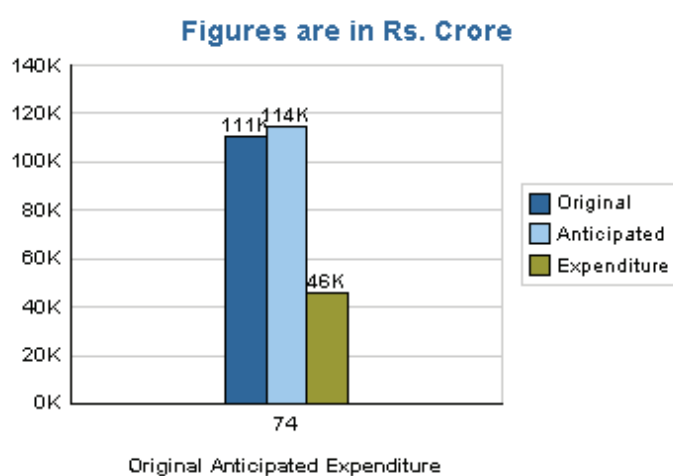

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	112
Number of Projects On Schedule	40
Number of Projects Delayed	62

Number of Projects Without Date Of Commissioning	10
--	----


Brief Analysis

Project Status with respect to Original Schedule: Out of 112 projects, 40 projects are on schedule 62 projects are delayed. 10 projects do not have fixed dates of commissioning.

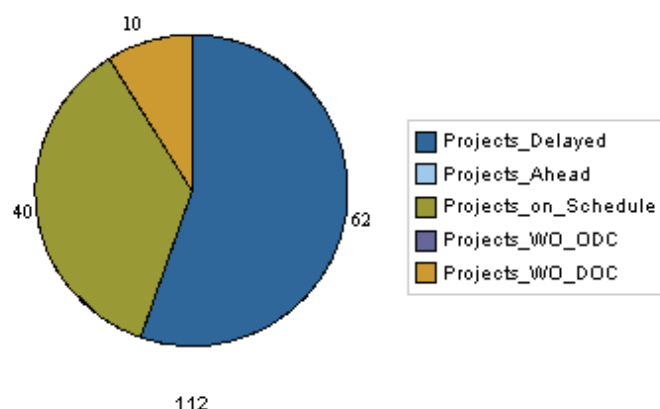

Investment Scenario

Total original cost of implementation of 112 projects when sanctioned, was of the order of Rs. 315179 crore but this was subsequently anticipated to Rs. 364677.74 crore implying a cost overrun of 15.7%. The expenditure incurred on these projects till June, 2016 is Rs. 202342.66 crore, which is 55.5% of the revised cost of the projects.

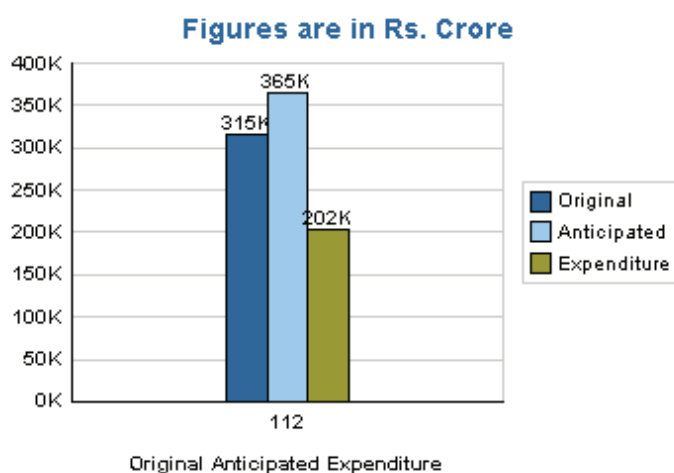

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	5

Number of Projects Without Date Of Commissioning	3
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 5 projects are delayed. 3 projects do not have fixed dates of commissioning.

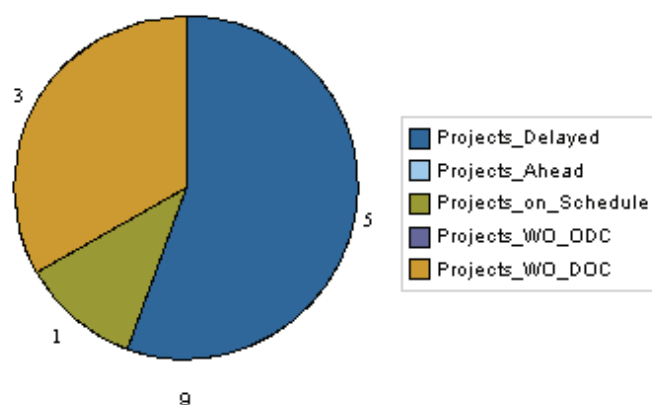

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 2563.15 crore but this was subsequently anticipated to Rs. 2563.15 crore. The expenditure incurred on these projects till June, 2016 is Rs. 1296.39 crore, which is 50.6% of the revised cost of the projects.

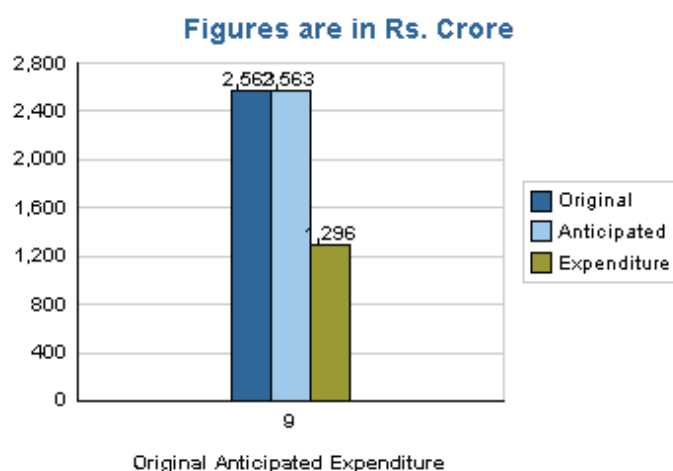

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	345
Number of Projects On Schedule	15
Number of Projects Delayed	38
Number of Projects Without Original Date of Commissioning	45
Number of Projects Without Date Of Commissioning	247


Brief Analysis

Project Status with respect to Original Schedule: Out of 345 projects, 15 projects are on schedule 38 projects are delayed. 247 projects do not have fixed dates of commissioning. 45 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

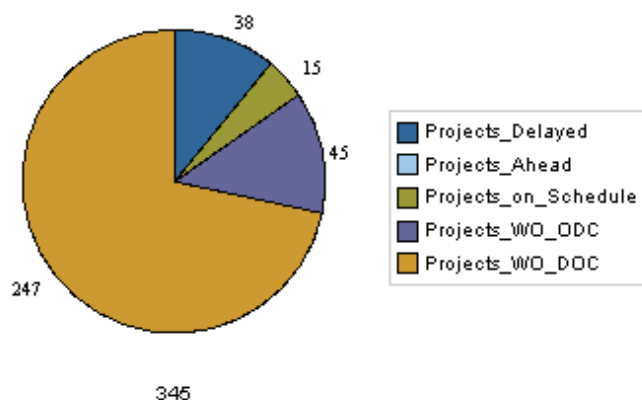

Investment Scenario

Total original cost of implementation of 345 projects when sanctioned, was of the order of Rs. 328791.74 crore but this was subsequently anticipated to Rs. 417811.4 crore implying a cost overrun of 27.1%. The expenditure incurred on these projects till June, 2016 is Rs. 85292.41 crore, which is 20.4% of the revised cost of the projects.

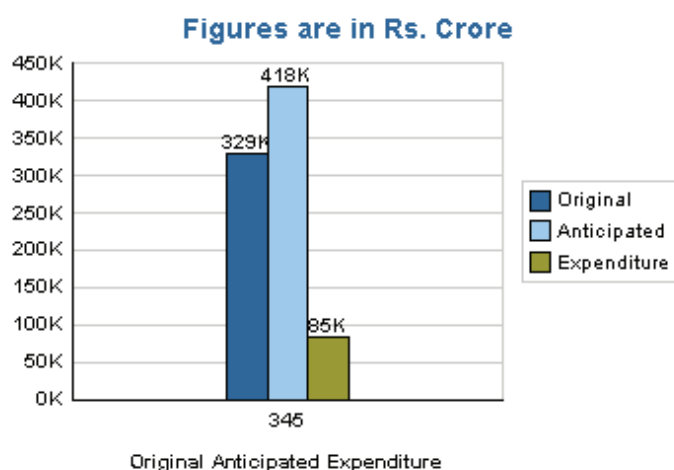

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	417
Number of Projects On Schedule	109
Number of Projects Delayed	127
Number of Projects Without Original Date of Commissioning	18
Number of Projects Without Date Of Commissioning	163


Brief Analysis

Project Status with respect to Original Schedule: Out of 417 projects, 109 projects are on schedule 127 projects are delayed. 163 projects do not have fixed dates of commissioning. 18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

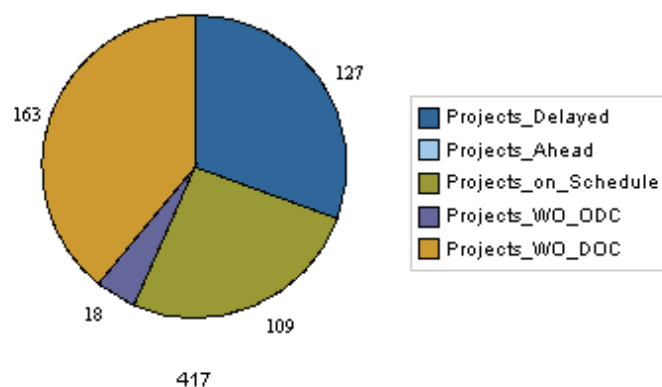

Investment Scenario

Total original cost of implementation of 417 projects when sanctioned, was of the order of Rs. 263809.81 crore but this was subsequently anticipated to Rs. 266605.47 crore implying a cost overrun of 1.1%. The expenditure incurred on these projects till June, 2016 is Rs. 127928.28 crore, which is 48% of the revised cost of the projects.

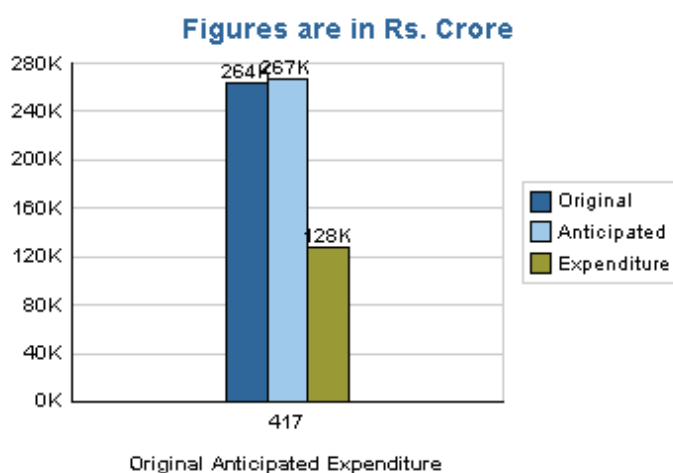

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule 3 projects are delayed. 1 project does not have fixed dates of commissioning.

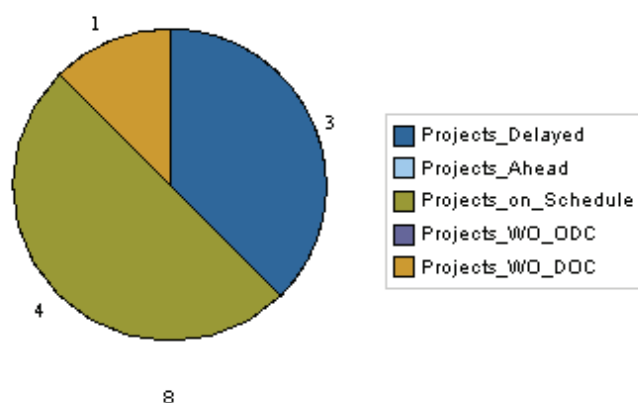

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5085.02 crore implying a cost overrun of 23.5%. The expenditure incurred on these projects till June, 2016 is Rs. 2064.65 crore, which is 40.6% of the revised cost of the projects.

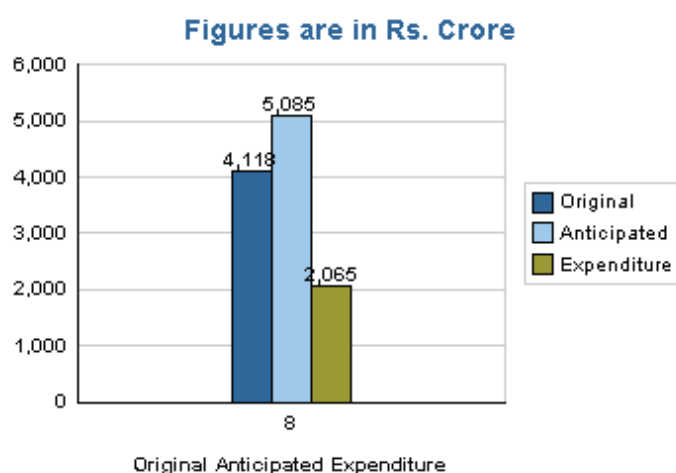

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.



Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 15445.17 crore but this was subsequently anticipated to Rs. 15345.17 cr. The expenditure incurred on these projects till June, 2016 is Rs. 301.57 crore, which is 2% of the revised cost of the projects.

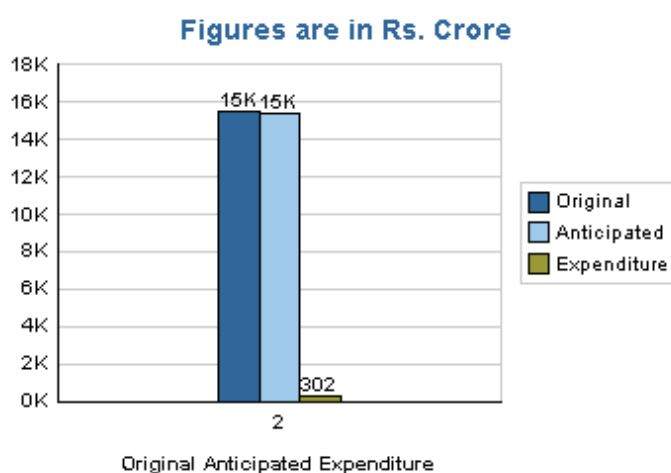

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	28
Number of Projects On Schedule	3
Number of Projects Delayed	16
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 2 projects are ahead of schedule, 3 projects are on schedule 16 projects are delayed. 7 projects do not have fixed dates of commissioning.

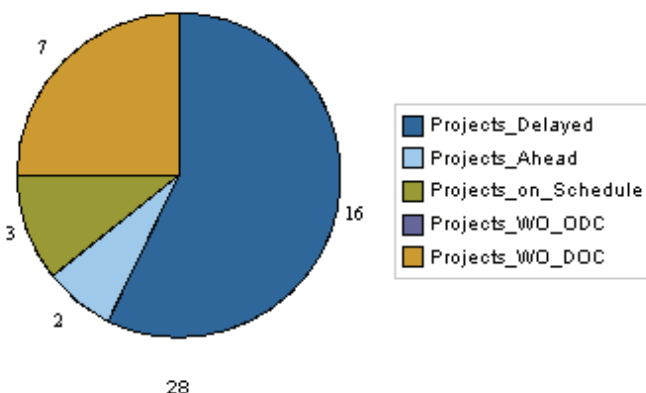

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 133830.49 crore but this was subsequently anticipated to Rs. 142976.73 crore implying a cost overrun of 6.8%. The expenditure incurred on these projects till June, 2016 is Rs. 64874.47 crore, which is 45.4% of the revised cost of the projects.

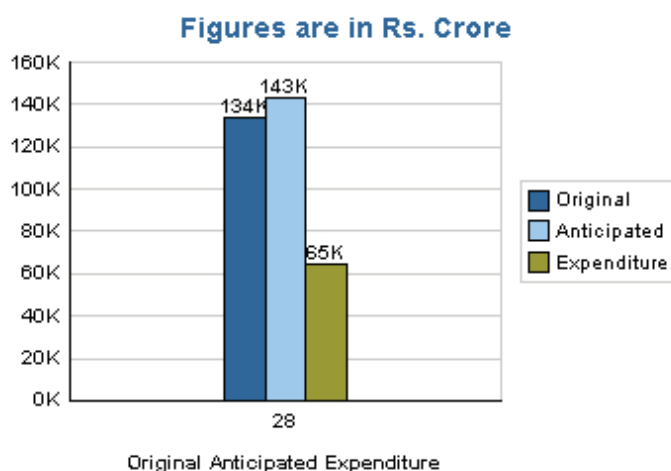

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE
 (All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	26.3
2	ANDHRA PRADESH	52	35,777.87	38,197.4	10,155.95
3	ARUNACHAL PRADESH	15	12,006.22	28,062.52	14,669.31
4	ASSAM	53	37,126.96	52,848.03	28,236.09
5	BIHAR	74	65,405.3	79,584.72	43,526.87
6	CHHATISGARH	40	96,051.6	97,695.19	51,865.55
7	D & N HAVELI	1	6,086.08	6,086.08	1,054.15
8	DELHI	16	49,997.48	51,031.48	27,050.3
9	GOA	8	3,925.48	3,907.87	539.08
10	GUJARAT	41	36,708.85	39,153.3	26,446.84
11	HARYANA	17	12,170.13	14,140.75	9,050.96
12	HIMACHAL PRADESH	6	8,361.75	14,761.02	7,306.69
13	JAMMU AND KASHMIR	9	25,620.25	44,826.38	14,432.77
14	JHARKHAND	44	43,279.92	46,068.51	13,070.51
15	KARNATAKA	39	70,774.99	88,393.13	34,587.77
16	KERALA	16	25,575.79	30,170.84	14,404.46
17	MADHYA PRADESH	47	51,315.42	55,759.38	26,054.46
18	MAHARASHTRA	94	1,52,704.24	1,61,995.06	46,365.31
19	MANIPUR	3	1,047.27	9,434.45	5,473.64
20	MEGHALAYA	5	6,744.03	8,661.01	727.54
21	MIZORAM	5	2,001.2	5,274.91	1,860.35
22	MULTI STATE	172	2,63,989.52	2,45,875.08	82,835.57
23	NAGALAND	3	6,420	8,083.3	148.39
24	ODISHA	50	48,425.99	54,018.33	14,907.65
25	PUNJAB	23	11,796.33	11,800.33	3,022.07
26	RAJASTHAN	61	42,046.69	42,992.29	22,244.54
27	SIKKIM	5	2,149.08	4,894.32	843.14
28	TAMIL NADU	61	71,126.1	92,172.95	62,910.38
29	TELANGANA	37	27,647.71	31,047.68	4,410.78
30	TRIPURA	9	3,776.07	7,783.63	3,404.15
31	UTTAR PRADESH	68	65,276.33	69,354.71	18,910.38
32	UTTARAKHAND	8	11,515.4	13,814.71	5,899.89
33	WEST BENGAL	49	51,751.33	65,273.19	34,479.97
TOTAL		1,132	13,48,915.99	15,23,477.16	6,30,921.81

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

ATOMIC ENERGY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	13171	17270	21674
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	3492	-	4933.84
CIVIL AVIATION						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	433.19
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
4	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	302.96	-	318.74
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	212.34	-	880.45
6	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	182.26
7	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	418.97	-	481.31
HEALTH AND FAMILY WELFARE						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
8	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	HSCC	11/2013	196.7	-	197.38
HEAVY INDUSTRY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	1718	-	2289
PETROLEUM						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
10	MARKETING TOP AT KORBA	IOCL	01/2011	141.86	-	179.17
POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
11	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	5671.34
12	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	8540.3
13	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	1061.38	-	2028.58
14	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	3642.04	-	4617.51

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
15	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	509.66	-	585.16
16	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER (MADRAS) LIMITED L	PGCIL	09/2011	1940.13	-	2078.46
17	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	558.26	-	615.91
18	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	2127.51	-	2407.93
19	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	2422.66	-	2488.16
20	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	1422.85	-	1546.52
21	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B	PGCIL	02/2012	3201.44	-	3294.11
22	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	5353	-	5679.02
23	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVNL	05/2015	436.68	-	443.28
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
24	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	608.02	631.43
25	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	124.43	926.23	935.87
26	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	532.98
27	NANGALDAM-TALWARA (NL) ,NR	NR	03/1981	450	-	496
28	KARUR-SALEM (NL) , SR	SR	02/1997	155.55	-	832.15
29	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	155.74	843.45	884.25
30	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	1500	-	3689.32
31	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	194.07	-	226.39
32	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	983.61
33	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	492.98	-	742.05
34	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) ,NR	NR	03/2002	625.3	408.76	841.76
35	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	100	-	612.9

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
36	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	280	-	834.61
37	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	733	-	2269.43
38	TOLLYGANJ-GARIA WITH EXTENSION TO DUM-DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	1049.69	3385.14	3544.3
39	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	92.63	-	293.59
40	JIND-SONEPAT (NL), NR	NR	01/2004	238.56	-	728.91
41	KHURDA ROAD-BOLANGIR (NL) ECR	ECOR	04/1994	470.21	-	608.32
42	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	301.64	-	670.38
43	RAJATGARH-BARANG (LD), ECR	RVNL	04/1999	166.16	-	356.17
44	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	727.56	-	5338.49
45	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	921	-	1649.05
46	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	624.47	2921.46	3104.92
47	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	183.23	-	221.76
48	CUTTACK - BARANG (LD)	RVNL	04/1995	127.13	-	237.94
49	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	328.43
50	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	136.62	-	360.11
51	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	332.92	332.92	495.4
52	GOELKERA-MANOHARPUR, (LD) (SER)	RVNL	03/1997	261.7	-	282.53
53	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	743	-	929.04
54	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	324.9	-	402.56
55	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	687.2	-	928.13
56	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY' -AGASTIYAMPALLI	SR	09/2007	404.19	-	572.47
57	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	969.97
58	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	170	-	435.57

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
59	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	300	-	361.62
60	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	325	-	669
61	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	293.97	-	456.82
62	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	619.34	-	679.78
63	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	482	874.57	877.59
64	KATAKHAL TO BHAIRABI	NFR	04/1998	227.9	-	317.58
65	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	446	-	538.68
66	VIRAMGAM-SURENDRANAGAR (DL)	WR	04/2010	279.4	-	337.82
67	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	739.65	-	798.43
68	TAMLUK-BASULYA-SUTAHATA DOUBLING	RVNL	04/2010	171.02	-	226.99
69	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.69	-	253.1
70	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	198.68	-	303.72
71	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	463.73
72	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	822.39	-	1451.09
73	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	-	1251.49
74	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	209.77	-	368.34
75	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	247	-	696.59
76	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	280.75
77	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI	NFR	04/1999	523.17	380.6	1038.26
78	PEN ROHA DOUBLING	CR	04/2007	98.74	203	320.29
79	PANVEL PEN DOUBLING	CR	04/2006	96.16	260.16	268.93
80	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	460.94	-	1002.57
81	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	313.24	-	384.84

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
82	JHARSUGUDA-RENGALI DOUBLING	ECOR	03/2006	201	-	205.82
83	DELANG-PURI DOUBLING	ECOR	03/2011	165.16	-	227.05
84	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.53
85	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT		04/1990	153.82	-	245.58
ROAD TRANSPORT AND HIGHWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
86	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	155	-	248.73
87	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	280	-	427.01
88	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	199.81	-	211.01
89	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	167.64	-	277.36
90	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	155.04	-	196.86
91	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	200	-	247.56
92	BIJNI TO ASSAM WB BORDER (NH-31.C) (1) (NHAI)	NHAI	12/2003	195	-	294.65
93	BIJNI TO ASSAM /WB.BORDER (NH-31.C) (NHAI)	NHAI	12/2003	237.8	-	409.39
94	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	332.94	-	514.3
95	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	175.96	-	309.01
96	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	264.72	-	320.02
97	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	225	-	313.71
98	NALBARI T BIJNI (AS-7)	NHAI	12/2003	208	230	306.09
99	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	160	-	200.36
100	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	365.05
101	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	217.61	309.56	399.08
102	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	348.16	-	398.79
103	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-	NHAI	03/2005	940	-	1415.36

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
	PHASE-III)					
104	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	1509.1	2782.54	3200.86
105	CHENNAI-TADA (SIX LANE)	NHAI	04/2009	353.37	-	365.08
106	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	NHAI	02/2009	1693.75	-	2675.29
107	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	1108	-	3822.02
108	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	1175	-	1206.1
109	TALEGAON-AMRAVATI	NHAI	11/2009	567	-	1055.94
110	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	852	-	889.94
111	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2016.24
112	DEOLI-KOTA	NHAI	01/2011	593	-	1038.84
113	MURADABAD-BAREILLY	NHAI	04/2010	1267	-	2666.66
114	PUNE-SATARA (NH-4)	NHAI	10/2010	1724.55	-	1893.03
115	INDORE-DEWAS (NH-3)	NHAI	11/2010	325	-	474.72
116	NASHRI- CHANANI	NHAI	05/2011	2159	-	4211.5
117	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	1813.76	-	2415.99
118	PATNA-MUZZAFFARPUR	NHAI	08/2010	671.3	-	880.67
119	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	1008.5	-	1282.25
120	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	NHAI	03/2011	785.5	-	923.28
121	ROHTAK-BAWAL	NHAI	05/2011	650	-	832.39
122	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1948.72
123	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	535	-	924.7
124	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1328.82
125	KANDLA - MUNDRA PORT	NHAI	01/2011	953.88	-	974.56

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
126	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	622.9
127	SAMAIKHALI - GANDHIDHAM	NHAI	09/2010	805.39	-	1406.7
128	JORBAT - BARAPANI	NHAI	01/2011	536	-	691.92
129	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	2802.56
130	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	574	-	899.71
131	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	375.09	-	506.5
132	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	575	-	604.75
133	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	511.54	-	549.1
134	SRINAGAR TO BANIHAL	NHAI	06/2011	1100.7	-	1363.7
135	BHUBANESWAR TO PURI	NHAI	03/2011	500.29	-	875.56
136	PANIKHOLI-RIMOLI	NHAI	03/2012	1410	-	1761.23
137	JAIPUR-REENGUS	NHAI	08/2010	267.81	-	699.6
138	BEAWAR PALI PINDWARA	NHAI	12/2011	2388.51	-	2490.61
139	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1089.05
140	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2133.37
141	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	998.79	-	1745.49
142	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	1047	-	1630.3
143	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2430.7
144	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	356.34
145	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1878.76
146	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	2125.24	-	4700.69
147	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	828	-	871.15
148	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1488.67

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
149	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA	NHAI	10/2013	677.79	-	878.97
150	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1101.09
151	4 LANING OF GOMTI CHAURAHA - UDAIPUR	NHAI	03/2012	914.5	-	1128.25
152	4-LANING OF ROHTAK - HISSAR SECTION	NHAI	03/2013	959.25	-	1229.4
153	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92
154	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	2946.14
155	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	1055	-	1357.85
156	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2041.03
157	TRICHY - KARUR	NHAI	03/2007	516	-	761.19
STEEL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
158	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.61
URBAN DEVELOPMENT						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
159	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	6395	13845.01	13973.45
160	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	188.87	-	10255.48

Annexure - III

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(June 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.36	03/2021 -	03/2017
	Total		555.52 -	555.52	4.36		
	<u>PETROLEUM</u>						
2	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	361.10	01/2017 -	07/2016
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	1,636.71	04/2019 -	03/2019
	Total		6487.84 -	6487.84	1997.81		
	<u>URBAN DEVELOPMENT</u>						
4	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	14.23	10/2019 -	12/2018
5	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017
	Total		6,401.00 -	6,401.00	14.23		
	Grand Total		13,444.36	13,444.36	2,016.40		

Annexure - IV

Details of On Schedule Projects w.r.t. Original Schedule

						(June 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	314.61	26.30	09/2018 -	09/2018
	Total		314.61 -	314.61	26.30		
	<u>COAL</u>						
2	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	108.08	03/2021 -	03/2021
3	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
4	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
5	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.24	03/2018 -	03/2018
6	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	88.68	03/2018 -	03/2018
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	206.73	03/2017 -	03/2017
8	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	181.29	03/2021 -	03/2021
9	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	307.11	03/2018 -	03/2018
10	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	17.28	03/2020 -	03/2020
11	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
12	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	111.75	03/2021 -	03/2021
13	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
14	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
15	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	0.21	03/2020 -	03/2020
16	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	69.36	03/2020 -	03/2020
17	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	189.80	03/2022 -	03/2022
18	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	151.27	03/2020 -	03/2020
19	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	84.76	03/2019 -	03/2019
20	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	1.95	03/2019 -	03/2019

(June 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,064.77	03/2023 -	03/2023
22	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
23	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.53	03/2023 03/2023	03/2023
24	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	1.03	03/2019 -	03/2019
25	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	87.81	03/2020 -	03/2020
26	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
27	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	41.91	03/2023 -	03/2023
28	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	74.76	12/2019 -	12/2019
29	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
30	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	110.10	03/2020 -	03/2020
31	GOKUL - [N06000120]	11/2014	267.67 -	267.67	178.29	03/2018 -	03/2018
32	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	12.75	03/2023 -	03/2023
33	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	14.12	03/2019 -	03/2019
34	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.30	03/2019 -	03/2019
35	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
36	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	57.98	03/2021 -	03/2021
37	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
38	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
39	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	244.17	03/2020 -	03/2020
40	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
41	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
42	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
43	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	817.83	03/2023 03/2023	03/2023
44	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	27.52	03/2021 -	03/2021
45	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	621.58	03/2026 -	03/2026

						(June 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
46	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	84.61	03/2025 -	03/2025
47	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	111.65	03/2021 -	03/2021
	Total		47,319.43 -	47,319.43	6,163.53		
	<u>FERTILISERS</u>						
48	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	23.81	12/2017 -	12/2017
	Total		482.85 -	482.85	23.81		
	<u>HEALTH AND FAMILY WELFARE</u>						
49	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	70.00	03/2018 -	03/2018
	Total		505.58 -	505.58	70.00		
	<u>MINES</u>						
50	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]	12/2015	355.13 -	355.13	214.67	11/2016 11/2016	11/2016
51	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	120.21	11/2016 11/2016	11/2016
	Total		699.63 -	699.63	334.88		
	<u>PETROLEUM</u>						
52	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,188.25	05/2017 -	05/2017
53	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220]	2/2015	184.00 -	184.00	16.26	12/2017 -	12/2017
54	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	179.17	09/2016 -	09/2016
55	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	53.48	09/2017 -	09/2017
56	DE-BOTTLENECKING OF SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	1,405.13	03/2017 03/2017	03/2017
57	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	147.72	12/2016 -	12/2016
58	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	982.92	12/2018 -	12/2018
59	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	4,080.91	05/2017 05/2017	05/2017
60	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	58.32	10/2018 -	10/2018
61	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	227.71	12/2017 -	12/2017

(June 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221]	1/1991	694.00 -	694.00	57.19	10/2018 -	10/2018
63	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	84.95	04/2018 -	04/2018
64	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219]	8/2014	393.00 -	393.00	-	04/2018 -	04/2018
65	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]	2/2016	367.11 -	367.11	9.25	04/2017 -	04/2017
66	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	59.87	01/2018 -	01/2018
67	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,190.69	73.04	04/2018 -	04/2018
68	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]	1/2015	4,619.94 -	4,619.94	1,121.78	12/2017 -	12/2017
69	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
70	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	195.63	64.81	09/2018 -	09/2018
71	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	173.28	95.20	01/2017 -	01/2017
72	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	182.96	02/2020 -	02/2020
73	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
74	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	-	02/2019 -	02/2019
75	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
	Total		33,601.55 -	33,184.78	10,088.92		
	<u>POWER</u>						
76	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017
77	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	21.80	07/2017 -	07/2017
78	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	851.60	03/2018 -	03/2018
79	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,467.00	12/2016 -	12/2016
80	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	13.10	11/2017 -	11/2017
81	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	570.60	04/2018 -	04/2018
82	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	3.50	05/2018 -	05/2018
83	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017

(June 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
84	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	29.90	07/2018 -	07/2018
85	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	6,517.00	06/2017 -	06/2017
86	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	443.28	12/2016 -	12/2016
87	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	233.90	08/2016 -	08/2016
88	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	740.80	04/2018 -	04/2018
89	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	13.90	07/2018 -	07/2018
90	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	182.20	04/2017 -	04/2017
91	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	9.30	03/2017 -	03/2017
92	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	1,553.00	03/2019 -	03/2019
93	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	-	07/2018 -	07/2018
94	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	49.00	03/2018 -	03/2018
95	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	5,937.00	09/2017 -	09/2017
96	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	197.00	09/2019 -	09/2019
97	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04 -	187.04	1.70	06/2018 -	06/2018
98	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	57.70	10/2017 -	10/2017
99	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	155.00	04/2017 -	04/2017
100	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	113.30	11/2017 -	11/2017
101	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	99.90	02/2017 -	02/2017
102	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	1,599.00	09/2019 -	09/2019
103	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,967.00	02/2019 -	02/2019
104	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
105	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
106	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	3.30	03/2018 -	03/2018
107	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	6,735.12	01/2018 -	01/2018

(June 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	3,546.00	08/2018 -	08/2018
109	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	171.00	07/2020 -	07/2020
110	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
111	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	214.00	11/2016 -	11/2016
112	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	696.10	05/2018 -	05/2018
113	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	46.34	10/2016 -	10/2016
114	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	38.50	03/2018 -	03/2018
115	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	138.90	10/2016 -	10/2016
	Total		133,509.34 -	133,509.34	35,564.34		
	<u>RAILWAYS</u>						
116	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT - [N22000384]	4/1990	153.82 -	551.82	245.58	03/2019 -	03/2019
117	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
118	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
119	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
120	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
121	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	-	03/2021 -	03/2021
122	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021
123	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	0.36	12/2016 -	12/2016
124	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	1.11	03/2021 -	03/2021
125	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	-	03/2021 -	03/2021
126	VIRAMGAM BHILDI - [N22000391]	4/1990	237.13 -	237.13	25.05	03/2018 -	03/2018
127	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,750.00	-	03/2022 -	03/2022
128	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	0.84	03/2021 -	03/2021
129	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017

(June 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
130	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
	Total		16,274.95 -	16,877.18	436.53		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
131	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
132	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	57.43	03/2018 -	03/2018
133	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
134	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	259.05	02/2018 -	02/2018
135	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
136	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	190.00	11/2017 -	11/2017
137	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342]	5/2015	709.00 -	709.00	19.24	09/2017 -	09/2017
138	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
139	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	76.80	02/2018 -	02/2018
140	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
141	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
142	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]	11/2013	683.83 -	683.83	-	07/2016 -	07/2016
143	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]	5/2015	581.84 -	581.84	-	05/2017 -	05/2017
144	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]	7/2014	401.11 -	401.11	239.02	01/2017 -	01/2017
145	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,474.76	01/2018 -	01/2018
146	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,101.09	07/2017 -	07/2017
147	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
148	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
149	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
150	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00 -	912.00	120.43	08/2016 -	08/2016

(June 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
151	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	79.70	07/2018 -	07/2018
152	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	234.67	08/2016 -	08/2016
153	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,492.63	11/2016 -	11/2016
154	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	95.00	04/2018 -	04/2018
155	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
156	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
157	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]	6/2015	563.92 -	563.92	13.66	12/2017 -	12/2017
158	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
159	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
160	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
161	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017
162	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	63.38	07/2017 -	07/2017
163	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017
164	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	0.54	05/2017 -	05/2017
165	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	-	05/2018 -	05/2018
166	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	-	06/2018 -	06/2018
167	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	41.21	10/2017 -	10/2017
168	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
169	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
170	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
171	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018

(June 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
172	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
173	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377	1/2014	397.04 -	397.04	17.71	10/2016 -	10/2016
174	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	166.22	05/2017 -	05/2017
175	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017
176	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	-	06/2018 -	06/2018
177	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
178	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	1/1991	282.41 -	282.41	75.32	08/2016 -	08/2016
179	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373	11/2010	305.49 -	305.49	-	03/2017 -	03/2017
180	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	1/1991	358.22 -	358.22	200.21	10/2016 -	10/2016
181	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
182	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
183	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
184	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
185	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	-	01/2019 -	01/2019
186	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	-	04/2017 -	04/2017
187	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
188	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	66.59	03/2018 -	03/2018
189	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	-	10/2018 -	10/2018
190	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	-	03/2018 -	03/2018

(June 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
191	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	108.37	11/2016 -	11/2016
192	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
193	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017
194	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
195	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	21.03	10/2016 -	10/2016
196	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	156.09	-	12/2016 -	12/2016
197	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
198	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
199	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018
200	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
201	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
202	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017
203	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	-	10/2016 -	10/2016
204	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	-	05/2018 -	05/2018
205	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
206	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	225.02	-	12/2018 -	12/2018
207	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	46.11	05/2018 -	05/2018
208	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
209	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	6.33	03/2018 -	03/2018
210	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253	8/2014	187.79 -	187.79	57.60	07/2016 -	07/2016

(June 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
211	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	57.99	02/2018 -	02/2018
212	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	55.86	10/2017 -	10/2017
213	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340	12/2014	451.58 -	451.58	28.00	06/2017 -	06/2017
214	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	102.12	11/2016 -	11/2016
215	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
216	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	10.32	05/2018 -	05/2018
217	FOUR LANING OF CHADIGARH - KHARAR - [N24000503	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
218	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344	9/2014	425.19 -	425.19	274.20	09/2016 -	09/2016
219	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26 -	269.26	218.10	10/2016 -	10/2016
220	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	162.33	05/2017 -	05/2017
221	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368	11/2014	563.92 -	563.92	124.09	11/2016 -	11/2016
222	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579	1/2014	1,408.85 -	1,408.85	-	10/2016 -	10/2016
223	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	22.60	12/2017 -	12/2017
224	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	4.47	06/2018 -	06/2018
225	PADI - DAHOD - [N24000353	11/2014	279.14 -	279.14	105.62	05/2017 -	05/2017
226	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
227	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343	9/2015	341.61 -	341.61	140.65	09/2017 -	09/2017
228	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
229	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
230	VADODARA-SURAT SECTION - [N24000361	3/2014	503.16 -	503.16	258.39	08/2016 -	08/2016
231	FOUR LANING OF VARANASI BYPASS - [N24000356	5/2015	261.09 -	261.09	34.10	05/2017 -	05/2017
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575	2/2014	665.50 -	665.50	-	07/2016 -	07/2016

						(June 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
233	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]	3/2015	206.80 -	206.80	-	07/2016 -	07/2016
234	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
235	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
236	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	54.50	07/2017 -	07/2017
237	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	112.00	04/2017 -	04/2017
238	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]	10/2014	264.72 -	264.72	116.15	04/2017 -	04/2017
239	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	46.68	02/2017 -	02/2017
	Total		59,881.59 -	60,020.97	8,532.34		
	SHIPPING AND PORTS						
240	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]	12/2014	274.85 -	274.85	160.22	04/2017 -	04/2017
241	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	9.77	12/2017 -	12/2017
242	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
243	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	235.15	157.96	06/2017 -	06/2017
	Total		928.29 -	978.33	327.95		
	STEEL						
244	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	13.87	09/2017 -	09/2017
245	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	136.15	03/2018 -	03/2018
246	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 253.92	253.92	194.54	06/2016 -	06/2016
247	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	200.20	12/2016 -	12/2016
248	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
249	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]	4/2014	151.33 -	151.33	11.86	09/2017 -	09/2017

(June 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
250	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]	2/2014	787.29 -	787.29	317.73	12/2016 -	12/2016
251	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	50.34	03/2018 -	03/2018
252	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	103.89	12/2017 -	12/2017
253	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	61.81	10/2017 -	10/2017
254	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	-	06/2020 -	06/2020
255	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	370.92	04/2018 -	04/2018
256	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	99.91	04/2018 -	04/2018
	Total		13,091.83 -	13,116.22	1,561.22		
	URBAN DEVELOPMENT						
257	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	161.22	03/2018 -	03/2018
258	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	40.61	03/2017 -	03/2017
259	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	5,298.00	1,528.93	11/2019 -	11/2019
	Total		13,101.84 -	14,135.84	1,730.76		
	Grand Total		319,711.49	321,144.76	64,860.58		

Annexure - V

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,800.69 -	3,170.48			
	<u>FERTILISERS</u>						
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2017	5.89
	Total		197.79 -	209.44			
	<u>HEAVY INDUSTRY</u>						
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						

(June 2016)

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
11	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	-	82.49
	Total		5,460.61 -	9,965.00			
	<u>PETROLEUM</u>						
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	06/2018	24.53
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	09/2016	70.49
14	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	02/2018	17.66
15	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	09/2016	63.54
16	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
17	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2016	45.83
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
20	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	09/2016	16.02
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
22	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	04/2016	67.62
24	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	12/2016	37.72
25	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	01/2017	19.35
26	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]	08/2010	103.02 -	171.04	07/2016 -	08/2016	66.03
	Total		29,610.77 -	35,468.03			
	<u>POWER</u>						
27	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
28	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
29	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	2,336.74	09/2009 -	09/2016	120.16

(June 2016)

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
30	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	03/2017	54.59
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
32	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2017	36.79
33	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	05/2011	1,961.87 -	2,310.58	05/2014 -	11/2016	17.77
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14
35	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
36	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]	05/2010	250.03 -	390.51	01/2013 -	07/2016	56.19
37	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	06/2017	36.01
38	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	09/2016	83.21
39	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06
40	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2017	147.51
41	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
42	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	03/2017	31.17
43	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,581.04	08/2013 -	12/2016	175.45
44	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
45	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2016	16.63
46	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	03/2017	27.60
47	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	11/2016	58.79
48	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	06/2017	22.93
49	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
50	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,441.52	07/2006 02/2015	03/2017	290.95
51	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	-	139.32

(June 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
52	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B [N18000122]	02/2012	1,927.16	1,940.58	10/2014	04/2016	0.70
	Total		66,934.70	116,497.05			
	<u>RAILWAYS</u>						
53	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77	634.48	03/1994	02/2016	299.62
54	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80	1,336.57	-	03/2019	3,531.98
55	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00	579.37	-	-	141.40
56	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55	870.00	-	-	459.31
57	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98	1,727.27	12/2010	03/2018	250.37
58	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42	844.00	-	03/2015	248.16
59	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00	1,122.00	-	-	300.71
60	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00	2,125.18	-	-	543.99
61	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69	3,404.92	12/2006	-	224.37
62	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63	270.00	02/2011	-	191.48
63	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09	1,500.00	12/2012	-	147.08
64	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90	2,371.85	03/2005	12/2019	2,019.62
65	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56	740.00	03/2012	-	210.19
66	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64	1,185.64	-	-	293.06
67	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00	2,363.00	03/2009	-	156.57
68	RAMGANJMUINDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92	3,000.00	-	-	537.05
69	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19	343.00	-	-	57.20
70	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00	245.39	12/2008	10/2015	104.49
71	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	1,101.16	-	03/2017	186.92
72	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23	1,202.70	02/2015	-	556.39

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
73	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	-	76.98
74	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	10/2016	154.85
75	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	811.36	- -	-	0.07
76	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
77	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	360.00	02/2006 -	-	37.56
78	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
79	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	2,072.50	- -	-	412.75
80	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
81	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
82	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
83	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
84	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2020	355.36
85	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
86	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	03/2019	252.06
87	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	-	206.55
88	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	658.07	03/2014 -	03/2019	0.75
89	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	03/2022	135.68
90	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	193.00	03/2011 -	01/2011	64.45
91	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	326.51	12/2012 -	-	43.27
92	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,491.43	- -	-	398.98
93	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	-	185.52
94	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	-	8.18
95	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	-	81.31
96	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	365.00	- -	-	269.66

(June 2016)

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
97	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
98	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
99	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
100	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
101	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
102	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
103	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
104	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
105	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
106	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
107	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
108	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
109	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
110	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
111	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
112	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
113	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
114	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
115	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,170.00	01/1999 -	-	153.83
116	JAGGAYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017	77.08
117	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
118	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
119	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	-	341.34
120	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	-	259.68

(June 2016)

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
121	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
122	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
123	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	5,050.00	05/2008 -	03/2023	1,939.09
124	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
125	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
126	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
127	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
128	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
129	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,046.72	03/2011 -	03/2019	1,143.43
130	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
131	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	3,142.46	10/2007 -	-	403.22
132	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
133	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
134	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	837.73	- -	03/2020	179.24
135	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,513.30	03/2015 -	03/2020	195.68
136	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
137	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	-	228.10
138	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
139	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	565.13	- -	03/2018	99.75
140	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,085.00	12/2015 -	03/2020	204.97
141	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
142	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	560.00	- -	-	36.56

(June 2016)

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
143	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114	04/2008	516.23 -	735.00	03/2014 -	-	42.38
144	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
145	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
146	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
147	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	2,434.00	03/2010 -	03/2017	648.92
148	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
149	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	12/2016	122.68
150	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
151	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89
152	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
153	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
154	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
155	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
156	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
157	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	-	72.62
158	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
159	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345	04/1997	836.26 -	1,072.51	- -	-	28.25
160	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	1,289.92	- -	12/2016	337.26
161	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
162	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	-	81.45
163	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
164	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
165	KAKINADA-PITHAPURAM - [N22000314	03/1999	215.06 -	220.29	- -	-	2.43

(June 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
166	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99 -	- -	03/2021	63.70
167	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00 -	- -	10/2015	14.43
168	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83 -	- -	03/2020	40.44
169	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03 -	- -	03/2020	52.77
170	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71 -	03/2015 -	07/2015	42.11
171	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73 -	- -	-	8.10
172	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	455.96 -	- -	03/2019	139.85
173	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00 -	12/2016 -	12/2016	40.49
174	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	620.00 -	- -	-	3.33
175	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00 -	- -	-	711.70
176	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	668.34 -	06/1999 -	-	0.80
177	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00 -	- -	-	184.73
178	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92 -	- -	-	67.77
179	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62 -	- -	03/2020	72.01
180	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38 -	- -	-	71.11
181	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68 -	- -	-	92.25
182	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63 -	- -	03/2019	24.63
183	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15 -	- -	03/2019	132.54
184	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00 -	- -	09/2015	27.06
185	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00 -	- -	-	68.05
186	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60 -	02/2020 -	12/2022	226.98
187	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00 -	- -	-	10.58
188	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	860.00 -	- -	-	88.60

(June 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
189	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	03/2017	17.92
190	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
191	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
192	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
193	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
194	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
195	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
196	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41
197	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
198	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
199	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
200	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
201	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
202	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
203	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
204	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
205	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
206	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
207	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
208	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	- -	03/2018	80.06
209	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
210	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	467.91	- -	03/2019	111.32
211	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,451.00	03/2007 -	-	62.12

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
212	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	972.52	- -	07/2019	285.92
213	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	440.05	- -	03/2018	109.78
214	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.11	- -	03/2018	1.61
215	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
216	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
217	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
218	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
219	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2020	46.95
220	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	599.90	- -	03/2018	147.67
221	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
222	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	412.53	- -	03/2018	148.78
223	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
224	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
225	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	386.68	- -	03/2019	57.14
226	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
227	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
228	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,103.00	- -	-	129.59
229	GULBARGA-BIDAR - [N22000348]	04/1994	844.15 1,542.42	1,542.42	- -	-	82.72
230	BARAMATI - LONAND (54 KM) - [N22000352]	02/1998	75.00 -	736.00	- -	-	881.33
231	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.00	- -	-	101.90
232	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
233	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	233.73	04/2014 -	03/2018	24.82
234	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
235	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT - [N22000384]	04/1990	153.82 -	551.82	03/2019 -	03/2019	258.74
	Total		86,647.35 -	235,423.29			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
236	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	08/2016	28.93
237	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2016	92.75
238	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	12/2016	80.68
239	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	12/2016	68.99
240	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50
241	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]	11/2014	573.96 605.00	605.00	- -	-	5.41
242	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
243	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
244	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	161.70	07/2015 -	-	2.88
245	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25
246	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2016	30.10
247	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
248	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	12/2016	2.65
249	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
250	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66
251	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24

(June 2016)

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
252	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
253	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
254	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
255	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2016	51.83
	Total		7,401.67 -	10,442.08			
	<u>SHIPPING AND PORTS</u>						
256	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	07/2016	300.00
257	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20
258	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
259	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
260	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
261	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	12/2016	12.04
262	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79
263	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29
264	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
265	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50
	Total		1,639.71 -	2,169.02			
	<u>URBAN DEVELOPMENT</u>						

(June 2016)

(June 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
266	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	14,405.01	06/2011 -	11/2016	125.25
267	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	356.59	11/2014 -	12/2017	47.76
268	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	5,298.00	11/2019 -	11/2019	24.25
	Total		10,900.33 -	20,059.60			
	Grand Total		230,397.72	467,787.16			

Annexure - VI

Details of Delayed Projects w.r.t. Original Schedule

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,933.84	09/2010 09/2016	09/2016	72	62.57	Local Protests - Law & Order issues
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	8,603.00	12/2015 11/2016	11/2018	35	0	NR
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	6,415.00	12/2016 03/2017	12/2019	36	0	Delay in supply/equipment, lack of skilled manpower, cash flow problems
	Total		27,271.00 -	29,456.00	19,951.84					
	<u>CIVIL AVIATION</u>									
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]JAAI, SIKKIM	01/2009	309.46 -	309.46	433.19	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		309.46 -	309.46	433.19					
	<u>COAL</u>									
5	WIND POWER PROJECT, KAZHUNEERKULAM, TAMIL NADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	220.04	10/2014 -	08/2016	22	0	i) Land acquisition, ii) delay in civil works, iii) delay in supply of equipment
6	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	82.97	03/2014 -	09/2016	30	0	Delay/ non issuance of Patta for land/plots allotted to PAFs in area acquired under CBA Act & delay in finalization of pending title cases of land in CBA tribunals.
7	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	122.47	05/2014 -	10/2016	29	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator
8	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	80.41	04/2014 -	11/2016	31	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator

(June 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
9	ASHOK EXPN OCP CCL (10 MTY) - [N060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	121.94	03/2011 -	03/2017	72	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator.
10	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 486.57	486.57	170.89	03/2012 03/2018	03/2017	60	87.58	i) Land acquisition ii) Rehabilitation and Resettlement problem
11	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	278.00	03/2013 -	03/2017	48	0	i) Delay in forest land diversion and construction of MGR by NTPC.
12	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	182.26	03/2010 -	03/2017	84	0	i) Land acquisition ii) Rehabilitation and Resettlement problem
13	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	121.97	12/2012 -	03/2017	51	0	i) Contractual Issues ii) Adverse Geomining Conditions
14	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	198.63	03/2012 -	03/2017	60	0	Delay in forest land diversion and EMP clearance.
15	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	188.13	03/2013 -	03/2017	48	.02	Delay in forest land diversion and EMP clearance.
16	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	86.88	03/2015 -	03/2017	24	0	N.R.
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	108.66	03/2012 -	03/2017	60	0	Delay in forest land diversion
18	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	95.73	03/2012 -	03/2017	60	0	Delay in land authentication ii) Delay in release of forest land.
19	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	72.08	03/2014 -	03/2017	36	0	i) Delay in land authentication ii) Delay in release of forest land.
20	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	03/2017	35	0	Delay in Environmental Clearance
21	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	39.49	06/2015 -	03/2017	21	0	i) Delay in land acquisition ii) Resettlement and Rehabilitation issues.
22	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	120.14	03/2012 -	03/2018	72	0	Adverse Geo-mining condition.
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	197.76	03/2014 -	03/2018	48	0	Delay in getting possession of forest land and environment clearance.
24	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	134.17	03/2016 -	03/2018	24	0	i) Delay in getting CTO (consent to operate) ii) Delay in getting forest clearance.

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
25	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.09	03/2015 -	03/2018	36	0	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues. iii) delay in diversion of forest land.
26	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	0	i) Land acquisition ii) Rehabilitation and Resettlement problem
27	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	85.33	03/2015 -	03/2018	36	0	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues. iii) delay in diversion of forest land.
28	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	122.93	03/2016 -	03/2018	24	0	Delay in land acquisition and forestry clearance.
29	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	486.27	92.33	03/2016 -	03/2018	24	12.97	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues
30	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	2,136.98	12/2015 04/2018	04/2018	28	0	i) Delay in supply of equipments ii) Delay in civil works.
31	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	228.71	03/2018 -	09/2018	6	0	i) Delay in forest clearance ii) Delay in tendering of CHP.
32	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	32.26	07/2016 -	03/2019	32	0	Acquisition of non forest land and R&R
33	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	51.55	04/2015 04/2019	04/2019	48	0	i) Land Acquisition ii) Contractual issues.
34	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	1,458.17	61.03	06/2015 08/2019	08/2019	50	0	N.R.
35	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	Delay in Environment and forestry Clearance.
36	JAGANNATHPOR OCP (3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	29.83	03/2015 -	03/2020	60	0	i) Delay in forest and environment clearance ii) Delay in land acquisition.
37	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.35	03/2014 -	03/2020	72	0	i) Delay in forest and environment clearance ii) Delay in land acquisition.
38	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	79.50	07/2012 03/2017	03/2021	104	0	i) Coal Evacuation problem ii) Delay in land authentication iii) Delay in forestry clearance and handing over site.

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
39	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	i) Delay in environment & Forest clearance ii) Rehabilitation and Resettlement issues.
40	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132	16.86	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues.
	Total		19,565.35 -	19,919.09	6,167.31					
	<u>FERTILISERS</u>									
41	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA	10/2014	197.79 209.44	209.44	72.96	11/2016 09/2017	09/2017	10	5.89	i) Delay in implementation by the Contractor ii) Financial constraints of the contractor iii) Technical challenge.
	Total		197.79 -	209.44	72.96					
	<u>MINES</u>									
42	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL, MADHYA PRADESH	09/2011	1,856.00 -	1,176.00	12.44	09/2017 -	04/2020	31	-36.64	
	Total		1,856.00 -	1,176.00	12.44					
	<u>STEEL</u>									
43	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	178.85	10/2013 -	08/2016	34	0	i) Contractual issues ii) Delay in environment clearance.
44	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	446.48	04/2016 -	09/2016	5	0	Delay in supply & erection of structures & equipment by M/s Danieli & Essar Projects.
45	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	529.21	07/2015 -	11/2016	16	0	N.R.
46	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	16,235.61	03/2013 -	12/2016	45	0	i) Site infringement due to Brown Field Area. ii) Poor performance by the contractor iii) Inadequate resource deployment by Contractor

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
47	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND	10/2013	245.67 -	245.67	139.69	05/2016 -	12/2016	7	0	i) Delay in supply and erection by the contractors.
48	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93 -	188.93	78.23	04/2015 -	12/2016	20	0	Delay in deployment of Security Forces and handing over of clear site by Government.
49	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH	07/2011	974.76 -	974.76	357.53	07/2016 -	03/2017	8	0	N.R.
50	TURBO BLOWER - 5 - [N12000092]RINL, ANDHRA PRADESH	12/2009	280.00 -	280.00	67.55	09/2016 -	03/2017	6	0	N.R.
51	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	175.94	178.61	12/2015 -	03/2017	15	17.5	N.R.
52	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	650.35	03/2015 -	03/2017	24	0	N.R.
53	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	100.51	10/2016 -	06/2017	8	42.39	N.R.
54	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 206.71	206.71	141.17	12/2016 -	07/2017	7	17.79	N.R.
55	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	336.54	07/2015 -	09/2017	26	0	N.R.
56	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	9,652.03	05/2015 12/2017	12/2017	31	0	i) Delay in obtaining forest clearance ii) Delay in approval from eascoast Railways iii) Inadequate man power and resource mobilization by the contractors.
	Total		38,281.71 -	38,484.54	29,092.36					
	PETROLEUM									
57	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL, GUJARAT	12/2011	160.00 -	160.00	94.30	02/2016 07/2016	07/2016	5	0	Slow progress by contractor.
58	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	251.66	172.53	06/2012 11/2015	08/2016	50	-6.79	Court Cases
59	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]IOCL, MANIPUR	08/2010	103.02 171.04	171.04	117.61	07/2016 08/2016	08/2016	1	66.03	

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
60	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	139.01	09/2012 09/2016	09/2016	48	-24.14	Slow progress in civil work and fabrication work Delay in delivery of Nut Shell filters and internal of IGF units.
61	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00 -	16,504.00	11,626.55	05/2016 -	09/2016	4	16.02	
62	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,489.38	01/2012 -	09/2016	56	70.49	Progress is slow due to heavy rains during the period, RoU issue, court case.
63	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	344.95	06/2011 10/2016	10/2016	64	0	Forest clearance, termination of contract
64	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	422.00	268.52	02/2016 10/2016	10/2016	8	-12.08	Delay by vendor
65	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	632.64	11/2015 11/2016	11/2016	12	25.84	interference by land owners and there is law and order problem, Delay in getting forest clearance and weather problem
66	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	1,840.40	11/2015 11/2016	11/2016	12	0	Restricted working environment due to nearby operating plants, availability of limited space for storage and fabrication, Restricted timings for radiography activities
67	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,447.36	09/2012 -	12/2016	51	0	Delay in receipt of Forest clearance. Law and order problems. Poor performance by contractors.Fund constraint of Contractor.
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,055.56	05/2013 12/2016	12/2016	43	45.83	Increase in scope of work
69	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	187.61	03/2014 05/2016	12/2016	33	0	Slow progress by contractor
70	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	467.91	08/2015 12/2016	12/2016	16	0	Delay in acquisition of land at Balasore by Govt of Odisha
71	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	650.62	04/2015 05/2016	12/2016	20	-39.69	Shut down issues for the hook up, financial problem of contractor, slow progress of contractor

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
72	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]JOCL,JHARKHAND	04/2011	191.96 -	191.96	117.38	05/2015 -	12/2016	19	0	delay in acquisition of additional land
73	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	275.75	11/2016 -	12/2016	1	0	Forest clearance
74	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	627.43	03/2015 12/2016	12/2016	21	37.72	Heavy rain in Assam, Refloating of tender. Delay in delivery of critical items due to financial instability Poor participation of vendors bundhs, environmental issues in North East
75	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 370.00	370.00	17.76	03/2013 01/2017	01/2017	46	19.35	
76	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]JOCL,ASSAM	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30	0	
77	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,873.19	03/2013 03/2017	03/2017	48	-3.5	ROU acquisition Delay in forest clearance.Inadequate manpower at -Local problem and court cases by tea gardener.Slow progress in engineering and procurement.
78	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	516.44	09/2011 10/2016	03/2017	66	0	Delay in preparation of drawings, shortage of skilled manpower, change in delivery location
79	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	1,320.05	05/2014 03/2017	03/2017	34	0	Retendering
80	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]JOCL,MULTI STATE	02/2011	913.00 -	913.00	553.79	08/2015 -	03/2017	19	0	Delay in getting Forest clearance in Odisha and West Bengal. Land acquisition
81	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	289.76	10/2014 03/2017	03/2017	29	49.38	delay in getting pipeline permission
82	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	36.88	11/2016 -	03/2017	4	0	Delay due to poor response to purchase & works tender
83	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	79.68	07/2016 -	04/2017	9	-20.81	Intermittent problems/ protests. Acquisition of Land Slow manufacturing

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
84	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017	25	0	Re-visit of the techno-economics of the project in view of new development.
85	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	238.50	26.16	03/2017 -	08/2017	5	0	Delay in getting approval
86	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,124.35	4,124.35	789.44	04/2016 12/2017	12/2017	20	0	Interruption of Site works by villagers
87	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00 -	184.00	16.26	06/2017 -	12/2017	6	0	
88	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	101.37	10/2017 -	02/2018	4	17.66	
89	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,351.65	03/2015 03/2018	03/2018	36	29.42	Non-performance of contractor
90	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 03/2018	03/2018	39	0	Non-performance of contractor
91	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	330.01	09/2017 03/2018	03/2018	6	0	
92	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	206.25	09/2017 -	03/2018	6	0	
93	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	439.03	10.60	03/2017 06/2018	06/2018	15	24.53	land litigation
94	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	215.38	01/2013 12/2018	12/2018	71	-10.01	No firm commitment from anchor load customers.
95	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	0	Delay in Obtaining statutory clearances.
96	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,381.86	12/2012 -	02/2019	74	0	Stiff resistance from farmers/ land owners in Kerala and RoU..
97	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	1,054.15	05/2019 03/2020	03/2020	10	0	
	Total		63,570.50 -	67,396.54	32,249.33					
	POWER									

(June 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	388.37	02/2012 -	06/2016	52	0	
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,481.22	04/2013 -	06/2016	38	0	
100	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	302.49	276.70	02/2016 -	06/2016	4	0	
101	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 390.51	390.51	261.30	01/2013 03/2016	07/2016	42	56.19	land acquisition
102	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	615.91	11/2013 -	07/2016	32	0	land acquisition, extremists affecting progress.Progress affected due to heavy rains.
103	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	92.40	12/2015 -	07/2016	7	0	
104	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	312.94	65.20	05/2016 -	07/2016	2	0	
105	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,081.09	08/2012 -	08/2016	48	0	
106	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	3,294.11	10/2014 -	08/2016	22	0	land acquisition , shut-down of Sasaram-A'bad & UPPCL line.Heavy rains also progress affected.
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	357.52	05/2015 -	08/2016	15	0	
108	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	381.00	06/2015 -	08/2016	14	0	

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
109	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL, MULTI STATE	06/2012	1,909.24	1,909.24	1,172.03	06/2015	08/2016	14	0	forest clearance
110	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38	2,336.74	2,028.58	09/2009	09/2016	84	120.16	
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, MULTI STATE	02/2009	509.66	509.66	585.16	11/2011	09/2016	58	0	ROW problem
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, MULTI STATE	07/2010	752.64 689.03	689.03	573.02	07/2013 11/2015	09/2016	38	-8.45	delay final forest clearance. Forest clearance received in ROW problem
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE	11/2011	723.63	723.63	633.62	11/2014	09/2016	22	0	ROW problem.
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE	09/2013	680.69	680.69	504.09	03/2016	09/2016	6	0	ROW problem.
115	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE	03/2014	155.57	155.57	26.20	03/2016	09/2016	6	0	
116	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,574.18	12/2011 03/2016	09/2016	57	83.21	Nil
117	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63	198.63	112.53	09/2014	10/2016	25	0	ROW problem, due to Power System constraints
118	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR	01/2009	3,642.04	5,783.17	4,617.51	01/2016	11/2016	10	58.79	
119	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH	05/2011	1,961.87 2,310.58	2,310.58	1,822.25	05/2014 06/2016	11/2016	30	17.77	Land acquisition
120	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH	12/2008	573.99 1,580.04	1,581.04	1,229.17	08/2013 12/2016	12/2016	40	175.45	

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
121	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	2,078.46	09/2014 -	12/2016	27	0	01 line completed but charging awaited. resolved. Work under progress.
122	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,407.93	07/2014 -	12/2016	29	0	delay in forest clearance
123	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	313.97	08/2014 06/2015	12/2016	28	16.63	ROW problem, seeking huge compensation of tower location & corridor. Issue still
124	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	1,546.52	01/2015 -	12/2016	23	0	Completion delayed due to delay in forest clearance. (Huge forest forest clearance obtained in Dec'15. Problem being faced due to
125	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	5,596.00	09/2016 -	12/2016	3	0	
126	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	1,018.20	05/2016 -	12/2016	7	0	ROW problem,. Final forest clearance awaited.
127	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	753.84	04/2016 -	12/2016	8	0	land acquisition ,(ROW problem
128	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	62.60	07/2016 -	12/2016	5	0	
129	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	38.00	02/2016 -	12/2016	10	0	
130	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	6,274.99	06/2015 -	02/2017	20	0	delay in land , ROW problem.

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
131	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	4,721.52	12/2009 03/2017	03/2017	87	147.51	
132	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, MAHARASHTRA	12/2007	477.69 738.48	738.48	603.59	09/2010 01/2016	03/2017	78	54.59	ROW problem forest clearance.
133	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,067.00	09/2011 08/2016	03/2017	66	54.25	
134	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 -	4,824.12	4,327.38	10/2012 -	03/2017	53	0	ROW problem
135	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,831.55	01/2015 -	03/2017	26	0	ROW problem, forest clearance, awaited.
136	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL, MULTI STATE	02/2010	232.34 -	232.34	220.09	06/2012 -	03/2017	57	0	ROW problem, Court case problem.
137	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 639.46	639.46	449.02	06/2014 03/2016	03/2017	33	31.17	ROW problem
138	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL, CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,586.53	08/2014 12/2015	03/2017	31	27.6	ROW problem
139	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	07/1998	368.72 1,441.52	1,441.52	1,049.75	07/2006 03/2017	03/2017	128	290.95	
140	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19 -	15,166.19	11,196.00	01/2017 -	03/2017	2	0	
141	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	27.60	04/2016 -	03/2017	11	0	
142	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL, MULTI STATE	02/2014	539.82 -	539.82	163.50	06/2016 -	03/2017	9	0	
143	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL, MULTI STATE	02/2014	908.08 -	908.08	416.10	06/2016 -	03/2017	9	0	

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
144	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,908.05	11/2008 01/2016	06/2017	103	22.93	ROW problem
145	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,335.20	12/2012 12/2016	06/2017	54	36.79	ROW problem ,compensation to forest.
146	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,298.13	11/2012 03/2016	06/2017	55	36.01	delay in land acquisition of.
147	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,285.25	12/2015 -	06/2017	18	0	Implementation affected due to severe ROW problems in Odisha & Huger
148	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	6,564.00	11/2016 -	08/2017	9	0	
149	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,679.02	05/2014 03/2017	09/2017	40	0	
150	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,332.28	12/2016 -	09/2017	9	0	
151	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,010.40	08/2013 12/2017	12/2017	52	23.65	agitation against Big Dam ,adverse law & order
152	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	72.21	02/2014 -	02/2018	48	0	ROW problem
153	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,863.00	01/2011 05/2018	05/2018	88	73.65	
154	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	0.70	09/2017 -	07/2018	10	0	
155	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	5,671.34	09/2009 -	12/2018	111	114.28	
156	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,869.00	03/2013 03/2016	06/2019	75	29.14	
157	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,752.36	02/2016 09/2019	09/2019	43	79.77	

(June 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
158	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	849.35	06/2013 -	12/2019	78	0	hindrances by villagers. Regular support of Distt. Administration is required.
159	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	141.80	04/2020 -	03/2022	23	0	
	Total		159,197.89 -	191,405.01	138,555.39					
	<u>HEAVY INDUSTRY</u>									
160	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	122.78	Non availability of trained manpower in the country
	Total		1,718.00 -	3,827.30	2,289.00					
	<u>HEALTH AND FAMILY WELFARE</u>									
161	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	400.00	12/2015 -	06/2016	6	0	Fund Constraints.
162	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	127.80	11/2013 -	10/2016	35	0	i) Delay in Civil Works ii) Stoppage of Work for demanding local employment iii) Delay in deployment of MOHFW representative.
163	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	59.29	05/2017 -	06/2017	1	0	i) Delay in release of funds ii) Work suspended due to safety aspect.
164	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	101.00	05/2017 -	06/2017	1	0	i) Delay in release of funds ii) Work suspended due to safety aspect.
165	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	168.90	16.50	05/2017 -	07/2017	2	0	i) Non availability of funds in time ii) Local protest for demanding local employment.
	Total		1,271.19 -	1,271.19	704.59					
	<u>RAILWAYS</u>									

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
166	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
167	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	340.00	328.43	03/2009 03/2009	10/2016	91	154.85	
168	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, ODISHA	04/1999	166.16 -	370.00	356.17	02/2009 02/2009	12/2016	94	122.68	i) Delay in awarding contract and cancellation of contract.
169	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	54.96	03/2015 -	12/2016	21	53.44	
170	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	235.00	226.99	06/2013 -	12/2016	42	37.41	i) Delay in release of funds ii) Work suspended due to safety aspect.
171	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	2,434.00	669.00	03/2010 -	03/2017	84	648.92	
172	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11	0	
173	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	4,996.19	3,689.32	04/2008 12/2011	06/2017	110	233.08	
174	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	950.00	928.13	03/2010 -	06/2017	87	38.24	
175	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	554.70	384.84	01/1999 06/2017	06/2017	221	77.08	
176	NANDYAL- YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 843.45	966.98	884.25	02/2009 12/2017	12/2017	106	520.89	
177	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	385.54	402.56	03/2010 -	12/2017	93	18.66	
178	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 2,173.50	1,389.62	1,571.89	03/2014 12/2017	12/2017	45	0	
179	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	12/2017	21	29.06	
180	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	742.05	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
181	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	2,531.34	2,269.43	12/2008 -	03/2018	111	245.34	25.26 Hac estimate for land acquisition not submitted by DC/Jalpaiguri. Hence, Y Connection at NMX-NQH could not be completed.
182	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	546.61	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
183	OMALUR-METTURDAM- DOUBLING WITH ELCTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU	10/2013	187.26 -	233.73	28.33	04/2014 -	03/2018	47	24.82	
184	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	
185	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	-	11/2002 -	12/2018	193	682.6	
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	641.78	03/2016 -	12/2018	33	-28.09	
187	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	9,046.72	5,338.49	03/2011 -	03/2019	96	1143.43	In Tupul- Imphal section, estimate for land acquisition was to be submitted by state gov. on 31.7.16 but not received, hence work stopped.
188	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
189	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 658.07	658.07	453.55	03/2014 03/2019	03/2019	60	.75	
190	BHUJ-NALIYA (GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 321.62	321.62	40.64	03/2012 03/2019	03/2019	84	1.06	
191	GONDIA-JABALPUR (GC), (SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,160.54	1,776.81	1,027.59	03/1998 -	12/2019	261	359.96	
192	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	479.90	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
193	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 -	1,428.00	456.82	06/2005 -	12/2019	174	385.76	

(June 2016)

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
194	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 1,125.89	1,125.89	983.85	12/2011 03/2020	03/2020	99	25.09	Total Land acquisition required is 18.0 Hectares, out of which proposal for 15.2 hectares is with Govt. of West Bengal.
195	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 -	2,820.25	679.78	04/2014 -	03/2020	71	355.36	
196	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 4,085.00	4,085.00	385.59	12/2015 -	03/2020	51	204.97	Forest Clearance awaited for Kurseong Division and Kalimpong Division in West Bengal.
197	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	385.60	45.70	03/2013 -	03/2020	84	-2.17	
198	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,513.30	148.39	03/2015 -	03/2020	60	195.68	Finalization of alignment. Take off point shifted to Dhansiri from Dimapur
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	998.39	03/2016 -	12/2020	57	-20	
200	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 1,030.29	1,421.25	690.23	03/2012 -	03/2022	120	135.68	
201	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	
202	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022	46	226.23	i) Delay in clearances from Govt. of Rajasthan.
203	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 -	5,050.00	983.61	05/2008 -	03/2023	178	1939.09	
	Total		40,070.71 -	100,711.60	31,019.02					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
204	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56	0	
205	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	248.73	09/2008 -	06/2016	93	30.1	Land acquisition and Slow progress

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
206	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHA) - [240106290]NHA,ASSAM	12/2003	195.00 -	195.00	294.65	06/2008 -	06/2016	96	0	
207	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHA,ASSAM	12/2003	264.72 -	264.72	320.02	06/2008 -	06/2016	96	0	
208	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHA,GUJARAT	03/2011	785.50 -	785.50	923.28	08/2013 -	06/2016	34	0	
209	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHA,TAMIL NADU	06/2011	535.00 -	535.00	924.70	12/2013 -	06/2016	30	0	
210	REHABILITATION AND UPGRADE OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	24	0	
211	BIJUNI TO ASSAM /WB.BORDER (NH-31.C)(NHA) - [240106293]NHA,ASSAM	12/2003	237.80 -	237.80	409.39	06/2008 -	07/2016	97	0	
212	FORBESGANJ TO SIMRAHI (NH-57)(NHA) - [240106294]NHA,BIHAR	12/2003	332.94 -	332.94	514.30	09/2008 -	07/2016	94	0	
213	GUWHATI TO NALBARI (AS-4) - [N24000038]NHA,ASSAM	12/2003	175.96 -	175.96	309.01	04/2008 08/2016	07/2016	99	0	
214	NALBARI TO BIJUNI (AS-6) - [N24000047]NHA,ASSAM	12/2003	225.00 -	225.00	313.71	06/2008 06/2016	07/2016	97	0	
215	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHA,ASSAM	12/2003	160.00 -	160.00	200.36	05/2008 07/2016	07/2016	98	0	
216	NASHRI- CHANANI - [N24000162]NHA,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	4,211.50	06/2015 -	07/2016	13	0	
217	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHA,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	07/2016	38	0	
218	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHA,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	07/2016	35	0	
219	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHA,GUJARAT	09/2010	805.39 -	805.39	1,406.70	03/2013 -	07/2016	40	0	
220	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHA,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	07/2016	29	0	
221	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHA,BIHAR	09/2011	574.00 -	574.00	899.71	03/2014 -	07/2016	28	0	
222	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHA,BIHAR	05/2011	511.54 -	511.54	549.10	11/2013 -	07/2016	32	0	

(June 2016)

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
223	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	07/2016	41	0	
224	BEAWARE PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	2,388.00	2,490.61	06/2014 -	07/2016	25	-0.2	
225	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	226.96	09/2014 -	07/2016	22	0	
226	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	129.37	12/2015 -	07/2016	7	0	
227	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	190.73	01/2016 -	07/2016	6	0	
228	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	24	0	
229	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]NHAI,RAJASTHAN	03/2012	914.50 -	914.50	1,128.25	10/2015 -	07/2016	9	0	
230	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]NHAI,HARYANA	03/2013	959.25 -	959.25	1,229.40	06/2016 -	07/2016	1	0	
231	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,946.14	10/2011 -	07/2016	57	0	
232	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	427.01	02/2009 -	08/2016	90	28.93	
233	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	889.94	03/2013 -	08/2016	41	0	
234	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,016.24	05/2013 -	08/2016	39	0	
235	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,282.25	06/2013 -	08/2016	38	0	
236	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	08/2016	38	0	
237	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	677.79	878.97	04/2016 -	08/2016	4	0	

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
238	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15	871.15	393.88	09/2015	08/2016	11	0	
239	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61	309.56	399.08	04/2010	09/2016	77	42.25	
240	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16	348.16	398.79	09/2007	09/2016	108	0	
241	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00	325.00	474.72	05/2013	09/2016	40	0	
242	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36	291.36	356.34	01/2014	09/2016	32	0	
243	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51	478.00	283.84	10/2013	09/2016	35	-11	
244	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10	240.10	162.19	03/2016	09/2016	6	0	
245	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48	320.48	192.55	08/2015	09/2016	13	0	
246	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64	377.64	-	03/2014	09/2016	30	0	
247	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34	351.34	199.74	01/2016	10/2016	9	0	
248	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78	495.78	301.70	01/2016	10/2016	9	0	
249	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45	195.45	-	11/2014	11/2016	24	0	
250	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21	170.21	5.65	11/2014	11/2016	24	0	

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
251	FOUR LANE OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00	1,232.00	1,123.15	08/2015	11/2016	15	0	
252	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00	230.00	203.60	06/2005	12/2016	138	0	
253	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81	385.13	211.01	04/2009	12/2016	92	92.75	
254	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64	167.64	277.36	11/2008	12/2016	97	0	
255	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04	280.13	196.86	11/2008	12/2016	97	80.68	
256	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00	200.00	247.56	04/2009	12/2016	92	0	
257	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00	245.00	214.88	03/2008 07/2016	12/2016	105	0	
258	NALBARI T BIJUNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	306.09	04/2008 01/2017	12/2016	104	0	
259	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00	331.23	365.05	07/2009	12/2016	89	68.99	
260	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00	486.00	469.41	05/2010	12/2016	79	0	Lack of work planning, labor, machinery and frequent changes
261	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 2,782.54	1,509.10	3,200.86	09/2012	12/2016	51	0	
262	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75	1,693.75	2,675.29	08/2011	12/2016	64	0	Land acquisition and forest issue
263	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00	2,288.00	3,822.02	11/2011	12/2016	61	106.5	Poor performance by contractor
264	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00	1,206.10	1,206.10	04/2013	12/2016	44	2.65	
265	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00	593.00	1,038.84	07/2013	12/2016	41	0	
266	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00	359.00	2.74	09/2013	12/2016	39	0	Land acquisition and Wildlife clearance
267	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00	1,267.00	2,666.66	06/2013	12/2016	42	0	

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
268	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	2,488.49	08/2014 -	12/2016	28	0	
269	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,893.03	03/2013 -	12/2016	45	0	
270	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,415.99	07/2013 -	12/2016	41	0	
271	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	880.67	02/2013 -	12/2016	46	0	
272	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	12/2016	37	0	
273	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	974.56	07/2013 -	12/2016	41	0	
274	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,802.56	05/2014 -	12/2016	31	0	
275	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	604.75	07/2013 -	12/2016	41	0	
276	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,363.70	06/2014 -	12/2016	30	0	
277	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35	0	
278	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	875.56	08/2013 -	12/2016	40	0	
279	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	600.65	09/2013 -	12/2016	39	0	
280	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	1,089.05	03/2013 -	12/2016	45	0	Poor performance of Contractor and land acquisition
281	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,133.37	08/2013 -	12/2016	40	0	
282	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,430.70	09/2014 -	12/2016	27	0	
283	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2016	32	0	
284	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	347.50	06/2014 -	12/2016	30	0	Inadequate mobilization of resources by contractor. Forest clearance & land related issues
285	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	12/2016	12	0	

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
286	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	12	0	
287	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	0	
288	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	301.04	57.42	01/2016 -	12/2016	11	0	
289	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	329.25	11/2016 -	12/2016	1	0	
290	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,357.85	11/2015 -	12/2016	13	51.83	
291	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	1,722.39	04/2015 -	01/2017	21	0	
292	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	0	
293	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,878.76	09/2015 -	02/2017	17	0	
294	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	0	
295	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	122.22	09/2007 -	03/2017	114	0	
296	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	284.10	08/2012 -	03/2017	55	0	
297	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	506.50	04/2014 -	03/2017	35	0	
298	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	1,630.30	06/2014 -	03/2017	33	0	

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
299	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	901.00	09/2016 -	03/2017	6	0	
300	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	103.60	01/2016 -	03/2017	14	0	
301	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	681.17	03/2014 -	04/2017	37	0	
302	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	185.05	02/2010 -	05/2017	87	2.29	rehabilitation and corrective action necessitated after construction accident on 24.12.2009.
303	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	0	Court case, public agitation
304	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43 -	580.43	269.89	08/2013 -	05/2017	45	0	
305	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	564.59	06/2015 -	05/2017	23	0	
306	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	283.25	180.61	10/2015 -	05/2017	19	0	
307	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	0	
308	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	691.92	01/2014 -	06/2017	41	0	
309	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	1,761.23	09/2014 -	06/2017	33	0	
310	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,682.27	07/2015 -	07/2017	24	0	
311	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,488.67	02/2014 -	08/2017	42	0	
312	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	0	
313	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	1,655.01	899.00	08/2016 -	08/2017	12	0	

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
314	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,745.49	08/2013 -	09/2017	49	0	
315	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	368.73	104.81	09/2016 -	09/2017	12	0	
316	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	871.15	09/2014 -	10/2017	37	0	
317	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	1,287.95	757.57	11/2015 -	10/2017	23	0	
318	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	
319	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	0	
320	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	0	
321	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48	0	
322	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55	0	
323	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	309.66	08/2013 -	12/2017	52	0	
324	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	622.90	10/2013 -	12/2017	50	0	
325	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	349.50	07/2014 -	12/2017	41	0	

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
326	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	
327	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69	0	
328	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA) - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	
329	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
330	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	0	
	Total		94,530.45 -	96,958.86	105,902.09					
	SHIPPING AND PORTS									
331	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 600.00	600.00	139.80	03/2006 01/2016	07/2016	124	300	Relocating of fishing stalls for a length about 300m in fishing harbour.
332	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	409.83	350.68	04/2009 03/2010	08/2016	88	66.82	
333	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.49	669.46	415.01	12/2010 12/2018	12/2018	96	82.72	nil
	Total		762.06 -	1,679.29	905.49					
	TELECOMMUNICATIONS									
334	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	301.57	09/2014 -	03/2017	30	-4.74	
	Total		2,111.17 -	2,011.17	301.57					

(June 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	URBAN DEVELOPMENT									
335	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	199.73	05/2013 10/2015	06/2016	37	0	Non-availability of funds
336	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	12,738.83	12/2015 -	08/2016	8	0	Contractual problem
337	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 13,845.01	14,405.01	13,973.45	06/2011 11/2016	11/2016	65	125.25	difficult geological conditions, densely populated area
338	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	315.00	196.71	06/2015 08/2016	11/2016	17	0	
339	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	23,763.22	03/2016 -	12/2016	9	0	Rehabilitation and Resettlement, Land Acquisition problem.
340	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 405.01	405.01	236.45	12/2014 -	12/2016	24	0	
341	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	117.94	09/2016 01/2017	01/2017	4	0	
342	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10,255.48	12/2014 12/2016	03/2017	27	0	
343	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 270.83	270.83	81.52	11/2014 03/2017	03/2017	28	0	
344	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	191.97	108.07	03/2012 08/2016	03/2017	60	-6.36	
345	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 -	350.02	144.54	03/2015 03/2017	03/2017	24	0	Delay by consultant

(June 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
346	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	48.61	09/2015 07/2016	04/2017	19	0	Slow work
347	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	24.51	03/2016 -	09/2017	18	0	
348	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69 -	216.69	17.54	03/2015 10/2017	10/2017	31	0	stopped due to water-logging of the site and non-depositing of fund by NIT Authority
349	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33 356.59	356.59	108.43	11/2014 -	12/2017	37	47.76	Non-availability of funds, delay in approval from local body
350	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA	02/2014	26,405.14 -	26,405.14	700.85	02/2019 -	03/2020	13	0	land acquisition
	Total		89,100.89 -	97,213.13	62,715.88					
	Grand Total		539,814.17	652,028.62	430,372.46					

Annexure - VII

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2016)

(June 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
	Total		3,492.00 -	5,677.00				
	<u>COAL</u>							
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58	60
3	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
4	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97	24
5	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
	Total		1,588.35 -	1,942.09				
	<u>FERTILISERS</u>							
6	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2017	5.89	10
	Total		197.79 -	209.44				
	<u>HEAVY INDUSTRY</u>							
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROLEUM</u>							
8	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]	08/2010	103.02 -	171.04	07/2016 -	08/2016	66.03	1
9	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38	29
10	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	01/2017	19.35	46

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
11	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	439.03	03/2017 -	06/2018	24.53	15
12	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	02/2018	17.66	4
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,256.72	05/2013 -	12/2016	45.83	43
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	12/2016	37.72	21
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	09/2016	70.49	56
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42	36
18	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	03/2012	14,225.00 -	16,504.00	05/2016 -	09/2016	16.02	4
	Total		21,359.22 -	26,314.56				
	<u>POWER</u>							
19	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098	05/2010	250.03 -	390.51	01/2013 -	07/2016	56.19	42
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	346.79	08/2014 -	12/2016	16.63	28
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,441.52	07/2006 02/2015	03/2017	290.95	128
22	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	03/2017	54.59	78
23	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	03/2017	31.17	33
24	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,581.04	08/2013 -	12/2016	175.45	40
25	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	2,336.74	09/2009 -	09/2016	120.16	84
26	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100	07/2010	1,272.80 -	1,731.10	11/2012 -	06/2017	36.01	55
27	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77	43
28	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	2,228.71	08/2014 -	03/2017	27.60	31
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	06/2017	22.93	103

(June 2016)

(June 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
30	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	05/2011	1,961.87 -	2,310.58	05/2014 -	11/2016	17.77	30
31	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2017	36.79	54
32	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	09/2016	83.21	57
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2017	147.51	87
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14	75
35	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	11/2016	58.79	10
36	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28	111
37	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
38	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
39	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		53,626.76 -	85,897.49				
	<u>RAILWAYS</u>							
40	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
41	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	10/2016	154.85	91
42	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
43	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89	106
44	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	370.00	02/2009 02/2009	12/2016	122.68	94
45	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41	42
46	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	233.73	04/2014 -	03/2018	24.82	47
47	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	5,050.00	05/2008 -	03/2023	1,939.09	178
48	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
49	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
50	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66	93
51	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	2,434.00	03/2010 -	03/2017	648.92	84
52	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
53	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
54	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	03/2022	135.68	120
55	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2020	355.36	71
56	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
57	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06	21
58	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	658.07	03/2014 -	03/2019	0.75	60
59	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24	87
60	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,046.72	03/2011 -	03/2019	1,143.43	96
61	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
62	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
63	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,513.30	03/2015 -	03/2020	195.68	60
64	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
65	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
66	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,085.00	12/2015 -	03/2020	204.97	51
67	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
68	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
69	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		23,121.82 -	85,138.50				
	ROAD TRANSPORT AND HIGHWAYS							

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
70	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	06/2016	30.10	93
71	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	12/2016	80.68	97
72	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	12/2016	68.99	89
73	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2016	92.75	92
74	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25	77
75	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29	87
76	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	08/2016	28.93	90
77	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2016	51.83	13
78	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50	61
79	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	12/2016	2.65	44
	Total		4,816.46 -	7,245.89				
	<u>SHIPPING AND PORTS</u>							
80	ENMORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	07/2016	300.00	124
81	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82	88
82	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		762.06 -	1,679.29				
	<u>STEEL</u>							
83	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50	15
84	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79	7
85	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39	8
	Total		668.22 -	871.05				
	<u>URBAN DEVELOPMENT</u>							

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
86	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	356.59	11/2014 -	12/2017	47.76	37
87	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	14,405.01	06/2011 -	11/2016	125.25	65
	Total		6,636.33 -	14,761.60				
	Grand Total		117,987.01	233,564.21				

Annexure - VIII

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>ATOMIC ENERGY</u>				
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	12/2008 10/2013	05/2016
	Total		13,171.00 -		
	<u>CIVIL AVIATION</u>				
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015
	Total		553.21 -		
	<u>COAL</u>				
4	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	03/2010 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 -	03/2013 -	03/2016
6	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	03/2011 -	03/2016
7	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	03/2013 -	03/2016
8	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	03/2012 -	03/2016
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	03/2016 -	03/2016
10	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		2,133.10 -		
	<u>STEEL</u>				
11	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	03/2016
12	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016
13	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	04/2016
14	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
	Total		1,511.12 -		

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	PETROCHEMICALS				
15	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 9,965.00	04/2012 12/2015	12/2015
	Total		5,460.61 -		
	PETROLEUM				
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	04/2016
17	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	- -	-
18	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU	11/2006	171.83 -	- -	-
19	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	- -	-
20	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL, MULTI STATE	01/2015	2,321.00 -	- -	-
21	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE	02/2015	890.00 -	- -	-
22	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC, ASSAM	06/2010	202.94 -	01/2014 -	-
	Total		6,851.77 -		
	POWER				
23	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	11/2013 -	03/2016
24	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 609.44	02/2014 03/2016	03/2016
25	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR	03/2010	3,984.03 -	01/2013 -	03/2016
26	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016
27	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL, MULTI STATE	12/2011	2,422.66 -	08/2014 -	04/2016
28	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 1,940.58	10/2014 03/2016	04/2016
29	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	11/2012 -	05/2016
30	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,007.57	07/2013 -	-
31	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL, ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	Total		22,471.77 -		

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>HEALTH AND FAMILY WELFARE</u>				
33	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014
34	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016
35	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	04/2016
	Total		786.38 -		
	<u>RAILWAYS</u>				
36	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	01/2015
37	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- -	02/2014
38	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
39	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015
40	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	- -	03/2015
41	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	- -	03/2016
42	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2016
43	KATAKHAL TO BHARABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	03/2016
44	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016
45	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016
46	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 -	06/2013
47	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]JECR,BIHAR	01/1991	332.15 -	07/2014 -	07/2014
48	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	09/2015
49	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015
50	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- -	10/2014
51	GHUTIASARIF-CANNING (ER) - [N22000117]JER,WEST BENGAL	04/2009	611.03 -	12/2011 -	11/2013
52	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	12/2012
53	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015
54	KODERMA GIRIDH (NL), ECR - [220100306]JECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
55	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	01/2011
56	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
57	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
58	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
59	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	07/2015
60	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015
61	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	09/2015
62	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
63	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	10/2015
64	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016
65	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016
66	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016
67	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
68	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
69	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
70	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	-
71	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- -	-
72	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
73	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
74	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
75	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
76	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
77	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-
78	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
80	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
81	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
82	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
83	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
84	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-
85	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
86	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
87	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
88	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
89	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 -	-
90	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.46	10/2007 02/2016	-
91	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
92	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,969.16	- -	-
93	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
94	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 1,160.47	- -	-
95	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	02/2006 -	-
96	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
97	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
98	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
99	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
100	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
101	BARDHAMAN-KATWA (GC) - [N22000091],WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
102	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
103	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
104	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
105	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
107	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	- -	-
108	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
109	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
110	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
111	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 855.16	- -	-
112	MOTIHARI-SITAMARHI (NL) - [N22000174]JECR,BIHAR	04/2006	211.00 -	- -	-
113	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]JECR,BIHAR	04/2008	228.05 -	- -	-
114	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
115	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
116	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
117	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
118	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
119	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
120	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
121	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
122	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
123	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
124	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
125	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
126	PIRPAINTI-JASIDIH - [N22000219]JER,MULTI STATE	04/2013	915.98 -	- -	-
127	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]JER,MULTI STATE	04/2001	923.52 -	- -	-
128	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]JER,MULTI STATE	04/2005	595.91 595.91	- -	-
129	WARDHA-NANDED MAHARASHTRA - [N22000231]JCR,MAHARASHTRA	04/2008	499.30 2,491.43	- -	-
130	KALYAN-KASARA 3RD LINE - [N22000233]JCR,MAHARASHTRA	04/2011	277.70 792.89	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
131	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- -	-
132	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	-
133	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	- -	-
134	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
135	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
136	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
137	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
138	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
139	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
140	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
141	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
142	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
143	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
144	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	- -	-
145	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 832.47	- -	-
146	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 1,714.49	- -	-
147	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 348.85	- -	-
148	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
149	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
150	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
151	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
152	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
153	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
154	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
155	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
156	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
158	KAKINADA-PITHAPURAM - [N22000314]SCR,ANDHRA PRADESH	03/1999	215.06 -	- -	-
159	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 1,141.00	- 03/2016	-
160	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
161	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
162	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
163	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
164	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-
165	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
166	GULBARGA-BIDAR - [N22000348]SCR,KARNATAKA	04/1994	844.15 1,542.42	- -	-
167	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-
168	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-
169	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-
170	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 -	- -	-
171	MANOHARABAD-KOTAPALLI - [N22000357],TELANGANA	04/2006	1,160.47 -	- -	-
172	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 -	- -	-
173	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-
174	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- -	-
175	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- -	-
176	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	- -	-
177	GUDUR-DURGARAJU PATNAM - [N22000363]SCR,ANDHRA PRADESH	04/2010	760.17 -	- -	-
178	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
179	KAZIPET-VIJAYAWADA III RD LINE WITH ELECTRIFICATION - [N22000365]SCR,TELANGANA	04/2012	1,820.50 -	- -	-
180	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
181	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	- -	-
182	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
183	VIJAYAWADA-GUDUR - [N22000369]SCR,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
184	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]SCR,MULTI STATE	04/2015	636.38 -	- -	-
185	SECUNDERABAD-MOHABOBNAGAR - [N22000371]SCR,TELANGANA	04/2015	728.10 -	- -	-
186	INDORE-DEWAS-UJJAIN(80 KM) DL - [N22000375]WR,MADHYA PRADESH	04/2016	600.00 -	- -	-
187	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	-
188	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2096	614.54 -	- -	-
189	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2093	971.22 -	- -	-
190	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	-
191	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	-
192	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	-
193	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	-
194	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-
195	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	-
196	INDORE DEWAS UJJAIN (80 KM) - [N22000393]WR,GUJARAT	04/2016	600.00 -	- -	-
197	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
198	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
199	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
200	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
201	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
202	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
203	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
204	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
205	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
206	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
207	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
208	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
209	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
210	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-
211	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-
212	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	-
213	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-
214	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-
215	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-
216	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
217	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-
218	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	- -	-
219	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-
220	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	-
221	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
222	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
223	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
224	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
225	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
226	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
227	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
228	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
229	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
230	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
231	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
232	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-
233	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
234	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
235	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
236	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
237	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
238	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
239	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
240	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
241	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
242	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
243	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
244	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
245	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
246	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
247	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
248	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
249	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
250	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
251	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
252	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
253	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
254	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
255	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
256	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
258	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
259	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
260	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
261	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
262	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
263	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
264	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
265	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
266	MUDKHEP-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
267	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
268	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
269	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
270	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
271	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
272	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
273	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
274	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
275	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
276	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
277	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
278	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
279	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
280	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
281	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
282	BARAMATI - LONAND (54 KM) - [N22000352]CR,MAHARASHTRA	02/1998	75.00 736.00	- -	-
	Total		238,503.78 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
283	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
284	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	03/2016
285	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	03/2016
286	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	05/2016
287	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	05/2016
288	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	08/2014
289	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	11/2015
290	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
291	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
292	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
293	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
294	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
295	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
296	YAN TO NIRMAL SERE REHABILITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
297	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
298	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
299	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
300	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
301	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
302	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
303	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
304	REHABILITATION AND UPGADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
305	REHABILITATION AND UPGADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
306	REHABILITATION AND UPGADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
307	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
308	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
309	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
310	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	-
311	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
312	REHABILITATION AND UPGADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
313	REHABILITATION AND UPGADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
314	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
315	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
316	REHABILITATION AND UPGADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
317	REHABILITATION AND UPGADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
318	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
319	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
320	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
321	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
322	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
323	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
324	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
325	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
326	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
327	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
328	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
329	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
330	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
331	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
332	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
333	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
334	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
335	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
336	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
337	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
338	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
339	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
340	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
341	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
342	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
343	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
344	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
345	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
346	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
347	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
348	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
349	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
350	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
351	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
352	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
353	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
354	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
355	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
356	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
357	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
358	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
359	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
360	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
361	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
362	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-
363	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-
364	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
365	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
366	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-
367	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
368	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
369	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	-
370	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	- -	-
371	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-
372	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-
373	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-
374	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
375	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
376	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
377	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	- -	-
378	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	- -	-
379	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN	09/2012	511.00 -	10/2013 -	-
380	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN	09/2012	511.00 -	10/2013 -	-
381	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
382	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
383	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, PUNJAB	09/2015	273.06 -	- -	-
384	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	- -	-
385	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	- -	-
386	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	- -	-
387	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	- -	-
388	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	- -	-
389	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
390	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	- -	-
391	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	- -	-
392	FOUR LANING OF BIAORA - DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	- -	-
393	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
394	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	01/1991	1,167.45 -	- -	-
395	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	- -	-
396	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
397	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH, UTTAR PRADESH	12/2014	207.88 -	- -	-
398	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH, GOA	12/2015	773.98 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
399	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
400	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	-
401	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-
402	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
403	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
404	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
405	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
406	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
407	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
408	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
409	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
410	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-
411	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
412	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	-
413	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	-
414	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	-
415	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	-
416	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	-
417	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	-
418	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
419	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
420	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-
421	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-
422	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	- -	-
423	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI, KARNATAKA	03/2016	701.40 -	- -	-
424	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	- -	-
425	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	- -	-
426	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	- -	-
427	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	- -	-
428	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	- -	-
429	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	- -	-
430	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-
431	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	- -	-
432	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA	03/2016	244.00 -	- -	-
433	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
434	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-
435	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	- -	-
436	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 -	- -	-
437	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	- -	-
438	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-
439	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
440	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
441	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
442	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
443	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
444	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
445	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
	Total		95,564.71 -		
	<u>SHIPPING AND PORTS</u>				
446	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		2,427.40 -		
	<u>TELECOMMUNICATIONS</u>				
447	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	-
	Total		13,334.00 -		
	<u>URBAN DEVELOPMENT</u>				
448	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015
449	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-
450	CONSTRUCTION OF 100 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	- -	-
451	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	01/2015 -	-
452	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
453	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
454	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		25,226.76 -		
	Grand Total		427,995.61		

Annexure - IX

Details of Projects Without Original Date of Commissioning

(June 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00	175.00	-	-	12/2017	-	0/0
	Total		175.00	175.00	.00				0/0
	<u>RAILWAYS</u>								
2	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 1,289.92	1,289.92	1,281.11	-	12/2016	-	0/1
3	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79	1,101.16	194.91	-	03/2017	-	0/0
4	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	181.19	-	03/2017	-	0/0
5	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65	872.22	798.43	-	03/2017	-	0/1
6	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	148.33	-	03/2017	-	0/0
7	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	1.19	-	12/2017	-	0/0
8	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	-	-	03/2018	-	0/0
9	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92	565.13	3.13	-	03/2018	-	0/0
10	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE	04/2008	822.39	1,480.83	1,451.09	-	03/2018	-	0/1
11	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77	440.05	368.34	-	03/2018	-	0/0
12	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55	288.11	95.03	-	03/2018	-	0/0
13	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22	599.90	45.92	-	03/2018	-	0/0
14	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82	412.53	0.79	-	03/2018	-	0/0

(June 2016)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,038.26	- -	03/2018	-	0/0
16	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	453.10	302.32	- -	03/2018	-	0/0
17	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 678.54	678.54	0.45	- 12/2018	12/2018	0(R3)	0/38
18	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 551.50	548.01	257.05	- 03/2019	03/2019	0(R3)	0/0
19	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	1,336.57	259.15	- -	03/2019	-	0/0
20	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 372.09	525.00	269.92	- -	03/2019	-	0/0
21	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,188.91	1,188.91	765.74	- 12/2009	03/2019	111(R1)	0/0
22	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	399.63	19.78	- -	03/2019	-	0/0
23	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	1,037.15	538.68	- -	03/2019	-	0/0
24	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
25	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	467.91	27.30	- -	03/2019	-	0/0
26	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	386.68	0.57	- -	03/2019	-	0/0
27	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,127.00	621.81	- -	03/2019	-	0/1
28	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	455.96	173.63	- -	03/2019	-	0/0
29	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 972.52	972.52	97.63	- -	07/2019	-	0/1
30	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	837.73	361.62	- -	03/2020	-	0/0
31	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	975.62	67.20	- -	03/2020	-	0/0
32	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0
33	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	6,000.00	17.62	- -	03/2020	-	0/0
34	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	194.57	- -	03/2020	-	0/0

(June 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
35	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 1,160.83	1,160.83	206.92	- 03/2020	03/2020	0(R3)	1/1
36	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	238.03	106.05	- -	03/2020	-	0/0
37	YELAHANKA-PENKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 860.43	860.43	25.46	- -	03/2020	-	0/0
38	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 578.00	578.00	58.10	- -	03/2020	-	0/0
39	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,266.89 -	1,266.89	75.26	- -	12/2020	-	0/0
40	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	1,111.99	217.99	- -	03/2021	-	0/0
41	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	810.28	4.75	- -	03/2021	-	0/0
42	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	470.21 -	3,004.90	608.32	- 06/2021	06/2021	0(R3)	0/0
43	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	1,640.04	345.37	- 03/2022	03/2022	0(R3)	0/0
44	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	913.00 1,801.00	1,801.01	2.09	- 06/2016	-	-	0/0
45	RAMGANJUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	3,000.00	312.15	- -	03/2017	-	0/0
46	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	1,009.00	7.08	- -	12/2019	-	0/0
	Total		33,942.30 -	54,057.90	11,552.30				1/44
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
47	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	818.53	- -	06/2016	-	3/3
48	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	1,665.00	1,377.79	- -	09/2016	-	0/0
49	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	479.00	360.06	- -	12/2016	-	0/0
50	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP, MAHARASHTRA	01/2014	446.77 -	446.77	97.05	- -	06/2017	-	0/4
51	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	795.76	-	- -	06/2017	-	0/0
52	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	794.30	-	- -	06/2017	-	0/0
53	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	810.22	-	- -	06/2017	-	0/0

(June 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
54	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP, MAHARASHTRA	03/2015	168.30 -	168.30	19.23	- -	10/2017	-	0/4
55	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	845.24	108.33	- -	11/2017	-	0/0
56	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	928.83	13.80	- -	12/2017	-	0/0
57	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	854.80	79.59	- -	12/2017	-	0/0
58	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	-	- -	01/2018	-	0/0
59	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	1,393.00	1,254.01	- -	01/2018	-	0/0
60	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	275.90	-	- -	02/2018	-	0/0
61	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHINDEAPAR BRIDGE - [N24000251]NHDP, GOA	03/2015	297.00 -	297.00	53.59	- -	04/2018	-	0/1
62	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	516.13	42.36	- -	04/2018	-	0/0
63	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	867.66	200.46	- -	05/2018	-	0/0
64	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	01/1991	1,388.00 -	1,388.00	112.51	- -	08/2018	-	0/0
	Total		13,833.06 -	13,833.06	4,537.31				3/12
	Grand Total		47,950.36	68,065.96	16,089.61				4/56

Annexure - X

Details of Projects Without Milestones w.r.t. Original Schedule

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	09/2017	0/0
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	09/2018	0/0
	Total		1,177.28 -			0/0
	<u>COAL</u>					
5	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	03/2018 -	03/2018	0/0
6	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	03/2019 -	03/2019	0/0
7	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
9	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	03/2021 -	03/2021	0/0
10	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	03/2024 -	03/2024	0/0
	Total		4,284.04 -			0/0
	<u>FERTILISERS</u>					
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 09/2017	09/2017	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
12	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 344.50	11/2016 11/2016	11/2016	0/0
13	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	04/2020	0/0
	Total		2,200.50 -			0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>STEEL</u>					
14	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	03/2016	0/0
15	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016	0/0
16	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	04/2016	0/0
17	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	06/2016	0/0
18	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2016	0/0
19	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2016	0/0
20	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	03/2017	0/0
21	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	03/2017	0/0
22	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2017	0/0
23	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	06/2017	0/0
24	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	07/2017	0/0
25	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
26	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	09/2017	0/0
27	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
28	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
29	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
30	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
	Total		10,013.49 -			0/0
	<u>PETROLEUM</u>					
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	04/2016	0/0
32	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 11/2015	08/2016	0/0
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	09/2016	0/0
34	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 05/2016	12/2016	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64	12/2016	12/2016	0/0
36	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH	03/2009	181.02	01/2017	01/2017	0/0
37	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65	09/2011 10/2016	03/2017	0/0
38	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00	08/2015	03/2017	0/0
39	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]OIL, GUJARAT	11/2015	500.00	03/2017	03/2017	0/0
40	PIPELINE REPLACEMENT PROJECT - 4 - [N16000203]ONGC, MAHARASHTRA	02/2015	2,899.93 2,098.43	05/2017	05/2017	0/0
41	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45	09/2017	09/2017	0/0
42	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL, MAHARASHTRA	05/2015	2,443.00	12/2017	12/2017	0/0
43	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC, MAHARASHTRA	01/2015	4,619.94	12/2017	12/2017	0/0
44	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220]BPCL, MAHARASHTRA	02/2015	184.00	12/2017	12/2017	0/0
45	PALAKKAD LPG PLANT - [N16000225]BPCL, KERALA	02/2015	184.00	06/2017	12/2017	0/0
46	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA	12/2015	3,190.69	04/2018	04/2018	0/0
47	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219]BPCL, MAHARASHTRA	08/2014	393.00	04/2018	04/2018	0/0
48	ENNORE TERMINAL - [N16000224]BPCL, TAMIL NADU	08/2014	393.00	04/2018	04/2018	0/0
49	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56	03/2017 06/2018	06/2018	0/0
50	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC, GUJARAT	11/2014	195.63	09/2018	09/2018	0/0
51	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221]BPCL, MAHARASHTRA	01/1991	694.00	10/2018	10/2018	0/0
52	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00	10/2018	10/2018	0/0
53	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA	11/2014	6,068.80	04/2019	03/2019	0/0
54	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA	08/2015	2,818.88	03/2019	03/2019	0/0
55	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT	05/2015	1,671.22	11/2019	11/2019	0/0
56	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA	02/2015	749.00	02/2020	02/2020	0/0
57	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08	05/2019 03/2020	03/2020	0/0
58	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00	-	-	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
59	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83	-	-	0/0
60	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00	-	-	0/0
61	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00	-	-	0/0
62	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00	-	-	0/0
	Total		45,437.82			0/0
	<u>POWER</u>					
63	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94	05/2016	07/2016	0/0
64	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63	09/2014	10/2016	0/0
65	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63	04/2016	03/2017	0/0
66	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04	03/2017	03/2017	0/0
67	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33	07/2017	07/2017	0/0
68	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18	11/2017	11/2017	0/0
69	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40	03/2018	03/2018	0/0
70	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11	05/2018	05/2018	0/0
71	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA	01/2016	187.04	06/2018	06/2018	0/0
72	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24	09/2017	07/2018	0/0
73	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37	07/2018	07/2018	0/0
74	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT	01/2016	244.19	07/2018	07/2018	0/0
75	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47	07/2018	07/2018	0/0
76	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH	01/2016	207.88	07/2018	07/2018	0/0
77	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12	04/2020	03/2022	0/0
78	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33	09/2010	-	0/0
	Total		22,448.90			0/0
	<u>HEAVY INDUSTRY</u>					

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
79	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00	09/2011	12/2017	0/0
	Total		1,718.00			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
80	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11	11/2013	11/2014	0/0
81	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57	12/2014	03/2016	0/0
82	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70	01/2016	04/2016	0/0
83	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70	12/2015	06/2016	0/0
84	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50	11/2013	10/2016	0/0
85	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44	05/2017	06/2017	0/0
86	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65	05/2017	06/2017	0/0
87	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90	05/2017	07/2017	0/0
88	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58	03/2018	03/2018	0/0
	Total		2,563.15			0/0
	<u>RAILWAYS</u>					
89	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16	-	01/2015	0/0
			260.16	-		
90	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43	-	02/2014	0/0
			926.23	-		
91	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74	03/2015	03/2015	0/0
			-	-		
92	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00	-	03/2015	0/0
			-	-		
93	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74	-	03/2015	0/0
			203.00	-		
94	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17	-	03/2016	0/0
			-	-		
95	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90	12/2012	03/2016	0/0
			-	-		
96	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31	03/2009	03/2016	0/0
			-	-		
97	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00	03/2007	03/2016	0/0
			-	-		
98	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]JECR,BIHAR	01/1991	332.15	07/2014	07/2014	0/0
			-	-		

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
99	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	09/2015	0/0
100	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
101	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- -	10/2014	0/0
102	GHUTIASHARIF-CANNING (ER) - [N22000117]JER, WEST BENGAL	04/2009	611.03 -	12/2011 -	11/2013	0/0
103	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	12/2012	0/0
104	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
105	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
106	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	01/2011	0/0
107	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]JER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
108	PLASSEY-JIAGANJ DOUBLING - [N22000220]JER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
109	DELANG-PURI DOUBLING - [N22000320]JECOR,ODISHA	03/2011	165.16 -	03/2015 -	07/2015	0/0
110	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]JER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
111	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	09/2015	0/0
112	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
113	JHARSUGUDA-RENGALI DOUBLING - [N22000317]JECOR,ODISHA	03/2006	201.00 -	- -	10/2015	0/0
114	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016	0/0
115	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]JRE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
116	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
117	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
118	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
119	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016	0/0
120	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
121	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	03/2017	0/0
122	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0

			(June 2016)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
123	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	03/2017	0/0
124	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
125	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
126	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
127	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
128	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2017	0/0
129	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
130	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 06/2017	06/2017	0/0
131	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 843.45	02/2009 12/2017	12/2017	0/0
132	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,173.50	03/2014 12/2017	12/2017	0/0
133	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
134	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
135	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
136	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
137	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	12/2008 -	03/2018	0/0
138	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
139	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	03/2018	0/0
140	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
141	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	- -	03/2018	0/0
142	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	03/2018	0/0
143	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	- -	03/2018	0/0
144	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
145	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	- -	03/2018	0/0
146	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2018	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
147	VIRAMGAM BHILDI - [N22000391]WR,GUJARAT	04/1990	237.13 -	03/2018 -	03/2018	0/0
148	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
149	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2018	0/0
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
151	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 551.50	- 03/2019	03/2019	0/0
152	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	- -	03/2019	0/0
153	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 372.09	- -	03/2019	0/0
154	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,188.91	- 12/2009	03/2019	0/0
155	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	03/2011 -	03/2019	0/0
156	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
157	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 658.07	03/2014 03/2019	03/2019	0/0
158	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	03/2012 03/2019	03/2019	0/0
159	RAJKOT-VERAVAL,WANSJALIA TO JATASAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	03/2019	0/0
160	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	03/2019	0/0
161	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
162	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	03/2019	0/0
163	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	- -	03/2019	0/0
164	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU	04/2011	190.10 -	- -	03/2019	0/0
165	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT - [N22000384]GUJARAT	04/1990	153.82 -	03/2019 -	03/2019	0/0
166	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,160.54	03/1998 -	12/2019	0/0
167	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
168	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 -	06/2005 -	12/2019	0/0
169	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 1,125.89	12/2011 03/2020	03/2020	0/0
170	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	- -	03/2020	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
171	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34	04/2014	03/2020	0/0
172	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,085.00	12/2015	03/2020	0/0
173	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14	03/2013	03/2020	0/0
174	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00	03/2015	03/2020	0/0
175	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18	-	03/2020	0/0
176	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00	-	03/2020	0/0
177	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02	-	03/2020	0/0
178	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71	-	03/2020	0/0
179	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81	-	03/2020	0/0
180	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	-	03/2020	0/0
181	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	-	03/2020	0/0
182	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	524.00 668.00	03/2020	03/2020	0/0
183	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98	03/2016	12/2020	0/0
184	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89	-	12/2020	0/0
185	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27	-	03/2021	0/0
186	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67	-	03/2021	0/0
187	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38	03/2021	03/2021	0/0
188	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71	03/2021	03/2021	0/0
189	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74	03/2021	03/2021	0/0
190	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61	03/2021	03/2021	0/0
191	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92	03/2021	03/2021	0/0
192	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21	-	06/2021	0/0
193	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	03/2012	03/2022	0/0
194	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04	-	03/2022	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
195	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
196	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
197	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 12/2022	12/2022	0/0
198	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	03/2023	0/0
199	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
200	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
201	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
202	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	-	0/0
203	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- -	-	0/0
204	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
205	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
206	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
207	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
208	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
209	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-	0/0
210	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
211	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
212	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
213	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
214	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
215	KOTPALI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
216	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-	0/0
217	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
218	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
219	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
220	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-	0/0
221	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	03/2009 -	-	0/0
222	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 2,921.46	10/2007 02/2016	-	0/0
223	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
224	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 1,969.16	- -	-	0/0
225	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
226	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
227	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	404.19 -	- -	-	0/0
228	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
229	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	125.00 -	- -	-	0/0
230	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU	09/2006	456.00 -	- -	-	0/0
231	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
232	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
233	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]JER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
234	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
235	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
236	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	376.59 -	- -	-	0/0
237	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-	0/0
238	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 855.16	- -	-	0/0
239	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
240	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0
241	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-	0/0
242	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
243	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
244	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
245	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
246	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
247	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
248	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
249	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
250	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
251	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
252	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
253	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
254	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
255	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 595.91	- -	-	0/0
256	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	- -	-	0/0
257	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- -	-	0/0
258	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- -	-	0/0
259	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	-	0/0
260	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 1,801.00	- 06/2016	-	0/0
261	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
262	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
263	GUDUR-DURGARA-JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
264	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]JNR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
265	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]JNR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
266	ROHTAK-MEHAM HANSI - [N22000272]JNR,HARYANA	04/2012	287.00 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
267	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
268	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
269	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	- -	-	0/0
270	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 832.47	- -	-	0/0
271	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 348.85	- -	-	0/0
272	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
273	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
274	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
275	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
276	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
277	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
278	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
279	KAKINADA-PITHAPURAM - [N22000314]SCR,ANDHRA PRADESH	03/1999	215.06 -	- -	-	0/0
280	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
281	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
282	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
283	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
284	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
285	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
286	GULBARGA-BIDAR - [N22000348]SCR,KARNATAKA	04/1994	844.15 1,542.42	- -	-	0/0
287	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-	0/0
288	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-	0/0
289	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-	0/0
290	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
291	MANOHARABAD-KOTAPALLI - [N22000357], TELANGANA	04/2006	1,160.47 -	- -	-	0/0
292	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR, MAHARASHTRA	02/2015	2,326.00 -	- -	-	0/0
293	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR, MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-	0/0
294	DAUND - MANMAD (236 KM) - [N22000360]CR, MAHARASHTRA	02/2016	1,876.00 -	- -	-	0/0
295	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR, MAHARASHTRA	02/2016	854.00 -	- -	-	0/0
296	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR, MAHARASHTRA	02/2016	912.00 -	- -	-	0/0
297	GUDUR-DURGARAJU PATNAM - [N22000363]SCR, ANDHRA PRADESH	04/2010	760.17 -	- -	-	0/0
298	KAZIPET-VIJAYAWADA III RD LINE WITH ELECTRIFICATION - [N22000365]SCR, TELANGANA	04/2012	1,820.50 -	- -	-	0/0
299	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
300	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	- -	-	0/0
301	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	4,000.00 -	- -	-	0/0
302	VIJAYAWADA-GUDUR - [N22000369]SCR, ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
303	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]SCR, MULTI STATE	04/2015	636.38 -	- -	-	0/0
304	SECUNDERABAD-MOHABOONAGAR - [N22000371]SCR, TELANGANA	04/2015	728.10 -	- -	-	0/0
305	INDORE-DEWAS-UJJAIN(80 KM) DL - [N22000375]WR, MADHYA PRADESH	04/2016	600.00 -	- -	-	0/0
306	DUDHNOI-MENDHIPATHAR - [N22000378]NFR, MULTI STATE	04/1992	315.64 -	- -	-	0/0
307	HARMUTI-NAHARLAGUN - [N22000382]NFR, MULTI STATE	04/2096	614.54 -	- -	-	0/0
308	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR, ASSAM	04/2093	971.22 -	- -	-	0/0
309	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR, ASSAM	04/2003	4,300.00 -	- -	-	0/0
310	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR, ASSAM	04/2007	180.09 -	- -	-	0/0
311	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	- -	-	0/0
312	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	- -	-	0/0
313	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	- -	-	0/0
314	SURENDRA NAGAR RAJKOT - [N22000392]WR, GUJARAT	04/2015	1,002.39 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	INDORE DEWAS UJJAIN (80 KM) - [N22000393]WR, GUJARAT	04/2016	600.00 -	- -	-	0/0
316	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
317	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
318	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
319	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
320	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
321	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
322	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
323	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
324	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
325	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
326	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
327	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
328	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
329	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
330	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
331	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
332	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
333	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
334	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
335	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
336	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
337	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
338	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
339	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09	-	-	0/0
340	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37	-	-	0/0
341	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	-	12/2019	0/0
342	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64	-	-	0/0
343	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80	-	-	0/0
344	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57	-	-	0/0
345	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25	-	-	0/0
346	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67	-	-	0/0
347	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20	-	-	0/0
348	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69	-	-	0/0
349	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07	-	-	0/0
350	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00	-	-	0/0
351	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62	-	-	0/0
352	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41	-	-	0/0
353	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56	-	-	0/0
354	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30	-	-	0/0
355	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14	-	-	0/0
356	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00	-	-	0/0
357	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01	-	-	0/0
358	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78	-	-	0/0
359	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99	-	-	0/0
360	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00	-	-	0/0
361	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	-	-	0/0
362	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35	-	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
363	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
364	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
365	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
366	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
367	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
368	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
369	BARIAPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
370	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
371	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
372	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
373	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
374	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
375	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
376	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
377	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
378	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
379	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
380	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
381	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
382	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
383	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
384	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
385	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
386	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
387	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54	-	-	0/0
388	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96	-	-	0/0
389	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00	-	-	0/0
390	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00	-	-	0/0
391	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	-	-	0/0
392	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	-	-	0/0
393	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93	-	-	0/0
394	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64	-	-	0/0
395	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48	01/1999	-	0/0
396	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69	01/1999	-	0/0
397	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92	-	-	0/0
398	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00	-	-	0/0
399	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00	-	-	0/0
400	BARAMATI - LONAND (54 KM) - [N22000352]CR,MAHARASHTRA	02/1998	75.00 736.00	- -	-	0/0
	Total		300,906.35			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
401	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17	01/2016	01/2016	0/0
402	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85	05/2016	05/2016	0/0
403	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30	05/2016	05/2016	0/0
404	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37	10/2011	06/2016	0/0
405	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01	08/2014	08/2014	0/0
406	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24	11/2015	11/2015	0/0
407	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00	01/2016	01/2016	0/0
408	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
409	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
410	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	06/2016	0/0
411	BIJNI TO ASSAM WB BORDER (NH-31.C)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	06/2016	0/0
412	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	06/2016	0/0
413	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	06/2016	0/0
414	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	07/2016	0/0
415	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	07/2016	0/0
416	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 08/2016	07/2016	0/0
417	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 06/2016	07/2016	0/0
418	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 07/2016	07/2016	0/0
419	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	07/2016	0/0
420	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	07/2016	0/0
421	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	07/2016	0/0
422	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	07/2016	0/0
423	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	07/2016	0/0
424	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	07/2016	0/0
425	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	07/2016	0/0
426	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	07/2016	0/0
427	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	06/2014 -	07/2016	0/0
428	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	07/2016	0/0
429	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	07/2016	0/0
430	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	07/2016	0/0
431	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]NHAI,RAJASTHAN	03/2012	914.50 -	10/2015 -	07/2016	0/0
432	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]NHAI,HARYANA	03/2013	959.25 -	06/2016 -	07/2016	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
433	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	07/2016	0/0
434	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	07/2016	0/0
435	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	07/2016	0/0
436	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	07/2016	0/0
437	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	08/2016	0/0
438	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	08/2016	0/0
439	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	08/2016	0/0
440	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	08/2016	0/0
441	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	04/2016 -	08/2016	0/0
442	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	08/2016	0/0
443	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
444	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
445	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	08/2016	0/0
446	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH	02/2012	912.00 -	08/2016 -	08/2016	0/0
447	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2016	09/2016	0/0
448	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	09/2016	0/0
449	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	09/2016	0/0
450	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2016	0/0
451	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	09/2016	0/0
452	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	09/2016	0/0
453	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2016	0/0
454	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
455	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	09/2016	0/0
456	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	09/2016	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
457	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
458	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	10/2016	0/0
459	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	10/2016	0/0
460	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
461	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
462	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
463	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
464	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
465	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	10/2016	0/0
466	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
467	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	11/2016	0/0
468	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	11/2016	0/0
469	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	12/2016	0/0
470	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	12/2016	0/0
471	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	12/2016	0/0
472	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	12/2016	0/0
473	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	12/2016	0/0
474	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 07/2016	12/2016	0/0
475	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	12/2016	0/0
476	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	12/2016	0/0
477	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	12/2016	0/0
478	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	12/2016	0/0
479	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	12/2016	0/0
480	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	12/2016	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
481	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
482	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	12/2016	0/0
483	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2016	0/0
484	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2016	0/0
485	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	12/2016	0/0
486	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2016	0/0
487	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	12/2016	0/0
488	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2016	0/0
489	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	12/2016	0/0
490	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2016	0/0
491	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2016	0/0
492	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
493	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	12/2016	0/0
494	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2016	0/0
495	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2016	0/0
496	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2016	0/0
497	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2016	0/0
498	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	12/2016	0/0
499	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	12/2016	0/0
500	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
501	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016	0/0
502	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	12/2016	0/0
503	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	12/2016	0/0
504	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2016	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
505	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	01/2017	0/0
506	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
507	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	01/2017	0/0
508	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
509	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	02/2017	0/0
510	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	02/2017	0/0
511	REHABILITATION AND UPGADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
512	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	03/2017	0/0
513	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2017	0/0
514	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2017	0/0
515	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2017	0/0
516	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	03/2017	0/0
517	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	03/2017	0/0
518	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
519	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
520	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
521	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
522	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2017	0/0
523	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN	10/2014	206.12 -	04/2017 -	04/2017	0/0
524	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017	0/0
525	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	05/2017	0/0
526	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL	02/2011	580.43 -	08/2013 -	05/2017	0/0
527	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	05/2017	0/0
528	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	05/2017	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
529	PADI - DAHOD - [N24000353]NHAI, RAJASTHAN	11/2014	279.14 -	05/2017 -	05/2017	0/0
530	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	05/2017	0/0
531	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
532	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD, ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
533	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP, MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
534	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP, MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
535	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	05/2017	0/0
536	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2017	0/0
537	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	06/2017	0/0
538	2 LANING WITH PAVED SHOULDER OF KARAUKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI, TAMIL NADU	12/2014	451.58 -	06/2017 -	06/2017	0/0
539	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	06/2017	0/0
540	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	06/2017	0/0
541	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	06/2017	0/0
542	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	07/2017	0/0
543	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP, MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
544	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
545	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	07/2017	0/0
546	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2017	0/0
547	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD, MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
548	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	09/2017	0/0
549	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
550	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
551	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI, JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
552	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
553	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	10/2017	0/0
554	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
555	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	10/2017	0/0
556	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2017	0/0
557	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
558	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
559	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
560	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
561	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017	0/0
562	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
563	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2017	0/0
564	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
565	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2017	0/0
566	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
567	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	12/2017	0/0
568	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
569	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2017	0/0
570	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
571	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
572	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
573	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0
574	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	12/2017	0/0
575	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	12/2017	0/0
576	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
577	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0
578	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
579	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
580	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BORDER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
581	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
582	JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
583	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD, ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
584	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD, ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
585	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	02/2018	0/0
586	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
587	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHAI, UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
588	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
589	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI, UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
590	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI, UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
591	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI, UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
592	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
593	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
594	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHAI, MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
595	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
596	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
597	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
598	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA - BARWALA - PANCHKULA (PKG - 2) - [N24000358]NHAI, HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
599	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
600	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	- -	04/2018	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
601	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH, ODISHA	01/1991	229.41 -	05/2018 -	05/2018	0/0
602	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	- -	05/2018	0/0
603	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	06/2018	0/0
604	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
605	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
606	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
607	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
608	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
609	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
610	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
611	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
612	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
613	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
614	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	07/2018	0/0
615	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI, MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
616	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	01/1991	1,388.00 -	- -	08/2018	0/0
617	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL, ASSAM	12/2015	225.02 -	12/2018 -	12/2018	0/0
618	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
619	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
620	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL, ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	01/2019	0/0
621	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
622	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0
623	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
624	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI, RAJASTHAN	06/2016	725.95 -	06/2019 -	06/2019	0/0

				(June 2016)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
625	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
626	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
627	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
628	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
629	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH, ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
630	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH, MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
631	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH, MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
632	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH, MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	-	0/0
633	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD, CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
634	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD, CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
635	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD, CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
636	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD, CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
637	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD, CHHATISGARH	12/2014	394.20 -	- -	-	0/0
638	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
639	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH, CHHATISGARH	03/2015	422.34 -	- -	-	0/0
640	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD, PUNJAB	03/2015	435.90 -	- -	-	0/0
641	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD, PUNJAB	01/2015	279.68 -	- -	-	0/0
642	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71 (NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD, PUNJAB	11/2014	463.65 546.00	- -	-	0/0
643	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71 (NEW NH-52) FROM - [N24000292]PWD, PUNJAB	11/2014	573.96 605.00	- -	-	0/0
644	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150 (KATHIPUDI TO START OF K - [N24000293]MORTH, ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
645	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH, RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
646	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH, RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
647	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH, RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
648	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH, RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
649	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
650	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
651	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
652	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
653	TWO LANING OF LALPUL - MANMAO - CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
654	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
655	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
656	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
657	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
658	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
659	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
660	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
661	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
662	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
663	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
664	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
665	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC.IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
666	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
667	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
668	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
669	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
670	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
671	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
672	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
673	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOU LA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
674	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
675	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
676	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
677	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
678	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
679	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
680	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
681	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
682	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
683	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
684	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-	0/0
685	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0
686	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
687	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
688	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-	0/0
689	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
690	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
691	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	-	0/0
692	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	- -	-	0/0
693	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-	0/0
694	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-	0/0
695	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-	0/0
696	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0

			(June 2016)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
697	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82	02/2015	-	0/0
698	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72	-	-	0/0
699	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00	-	-	0/0
700	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20	-	-	0/0
701	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00	10/2013	-	0/0
702	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00	10/2013	-	0/0
703	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00	06/2006	-	0/0
704	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07	-	-	0/0
705	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06	-	-	0/0
706	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10	-	-	0/0
707	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04	-	-	0/0
708	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28	-	-	0/0
709	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96	-	-	0/0
710	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67	-	-	0/0
711	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90	03/2016	-	0/0
712	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09	-	-	0/0
713	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13	-	-	0/0
714	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79	-	-	0/0
715	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41	-	-	0/0
716	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45	-	-	0/0
717	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67	-	-	0/0
718	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54	08/2015	-	0/0
719	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88	-	-	0/0
720	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98	-	-	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
721	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
722	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	-	0/0
723	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-	0/0
724	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
725	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
726	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
727	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
728	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
729	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
730	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
731	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
732	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-	0/0
733	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
734	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	-	0/0
735	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	-	0/0
736	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	-	0/0
737	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	-	0/0
738	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	-	0/0
739	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	-	0/0
740	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
741	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	-	0/0
742	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
743	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
744	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	-	0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
745	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-	0/0
746	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	- -	-	0/0
747	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-	0/0
748	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	- -	-	0/0
749	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	- -	-	0/0
750	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	- -	-	0/0
751	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	- -	-	0/0
752	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
753	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	- -	-	0/0
754	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA	03/2016	244.00 -	- -	-	0/0
755	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
756	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
757	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
758	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
759	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	- -	-	0/0
760	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-	0/0
761	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-	0/0
762	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-	0/0
763	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-	0/0
764	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-	0/0
765	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	-	0/0
766	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD, MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
767	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD, CHHATISGARH	12/2015	291.05 -	- -	-	0/0
	Total		240,492.75 -			0/0

			(June 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	SHIPPING AND PORTS					
768	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 600.00	03/2006 01/2016	07/2016	0/0
769	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	04/2009 03/2010	08/2016	0/0
770	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL, TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
771	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.49	12/2010 12/2018	12/2018	0/0
772	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		3,399.46 -			0/0
	TELECOMMUNICATIONS					
773	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 -	-	0/0
	Total		13,334.00 -			0/0
	URBAN DEVELOPMENT					
774	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
775	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	05/2013 10/2015	06/2016	0/0
776	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 315.00	06/2015 08/2016	11/2016	0/0
777	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
778	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	09/2016 01/2017	01/2017	0/0
779	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 270.83	11/2014 03/2017	03/2017	0/0
780	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 142.37	03/2012 08/2016	03/2017	0/0
781	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD, ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
782	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02 -	03/2015 03/2017	03/2017	0/0
783	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	07/2017 -	06/2017	0/0
784	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69 -	03/2015 10/2017	10/2017	0/0
785	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33 356.59	11/2014 -	12/2017	0/0
786	NAGPUR METRO RAIL - [N28000085]NMRL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0

			(June 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
787	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	10/2019 -	12/2018	0/0
788	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
789	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-	0/0
790	CONSTRUCTION OF 100 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	- -	-	0/0
791	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-	0/0
792	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
793	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		107,261.18 -			0/0
	Grand Total		755,434.71			0/0

Annexure - XI

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
1	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	309.01	04/2008 08/2016	07/2016
	Total		175.96 -	175.96	309.01		
	<u>COAL</u>						
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	170.89	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	170.89		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
3	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 230.00	208.00	306.09	04/2008 01/2017	12/2016
	Total		208.00 -	208.00	306.09		
	<u>COAL</u>						
4	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.36	03/2021 -	03/2017
	Total		555.52 -	555.52	4.36		
	<u>PETROLEUM</u>						
5	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	361.10	01/2017 -	07/2016
	Total		419.04 -	419.04	361.10		
	<u>URBAN DEVELOPMENT</u>						
6	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	14.23	10/2019 -	12/2018
7	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017
	Total		6,401.00 -	6,401.00	14.23		
	<u>PETROLEUM</u>						
8	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE- III - [N16000197]	11/2014	6,068.80 -	6,068.80	1,636.71	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	1,636.71		
	Grand Total		14,087.72	14,314.89	2,802.39		

Annexure - XII

List of Projects on schedule w.r.t. Latest Schedule

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	5,677.00	4,933.84	09/2010 09/2016	09/2016
	Total		3,492.00 -	5,677.00	4,933.84		
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	314.61	26.30	09/2018 -	09/2018
	Total		314.61 -	314.61	26.30		
	<u>COAL</u>						
3	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	108.08	03/2021 -	03/2021
4	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
5	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	206.73	03/2017 -	03/2017
7	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	84.61	03/2025 -	03/2025
8	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	307.11	03/2018 -	03/2018
9	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	27.52	03/2021 -	03/2021
10	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	817.83	03/2023 03/2023	03/2023
11	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	111.75	03/2021 -	03/2021
12	MOONIDH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	51.55	04/2015 04/2019	04/2019
13	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
14	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
15	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	0.21	03/2020 -	03/2020
16	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	69.36	03/2020 -	03/2020

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
17	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	189.80	03/2022 -	03/2022
18	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	151.27	03/2020 -	03/2020
19	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	621.58	03/2026 -	03/2026
20	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,064.77	03/2023 -	03/2023
21	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
22	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.53	03/2023 03/2023	03/2023
23	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	1.03	03/2019 -	03/2019
24	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	87.81	03/2020 -	03/2020
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
26	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	41.91	03/2023 -	03/2023
27	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
28	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	110.10	03/2020 -	03/2020
29	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	74.76	12/2019 -	12/2019
30	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
31	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
32	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	244.17	03/2020 -	03/2020
33	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	1,458.17	61.03	06/2015 08/2019	08/2019
34	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	2,136.98	12/2015 04/2018	04/2018
35	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
36	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
37	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
38	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	84.76	03/2019 -	03/2019
39	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	1.95	03/2019 -	03/2019
40	GOKUL - [N06000120]	11/2014	267.67 -	267.67	178.29	03/2018 -	03/2018

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
41	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	12.75	03/2023 -	03/2023
42	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	14.12	03/2019 -	03/2019
43	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.30	03/2019 -	03/2019
44	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
45	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	57.98	03/2021 -	03/2021
46	AMGAON OPENCAS PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	17.28	03/2020 -	03/2020
47	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
48	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	111.65	03/2021 -	03/2021
49	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	181.29	03/2021 -	03/2021
50	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.24	03/2018 -	03/2018
51	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	88.68	03/2018 -	03/2018
	Total		55,914.98 -	55,914.98	8,413.09		
	<u>FERTILISERS</u>						
52	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	23.81	12/2017 -	12/2017
53	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	72.96	11/2016 09/2017	09/2017
	Total		680.64 -	692.29	96.77		
	<u>HEALTH AND FAMILY WELFARE</u>						
54	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	70.00	03/2018 -	03/2018
	Total		505.58 -	505.58	70.00		
	<u>MINES</u>						
55	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR [N10000008]	12/2015	355.13 -	355.13	214.67	11/2016 11/2016	11/2016
56	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	120.21	11/2016 11/2016	11/2016
	Total		699.63 -	699.63	334.88		

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
57	REPLACEMENT OF COKE CHAMBERS - [N16000177]	4/2013	480.00 -	422.00	268.52	02/2016 10/2016	10/2016
58	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]	2/2016	367.11 -	367.11	9.25	04/2017 -	04/2017
59	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	59.87	01/2018 -	01/2018
60	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,190.69	73.04	04/2018 -	04/2018
61	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]	1/2015	4,619.94 -	4,619.94	1,121.78	12/2017 -	12/2017
62	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
63	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	195.63	64.81	09/2018 -	09/2018
64	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	173.28	95.20	01/2017 -	01/2017
65	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	182.96	02/2020 -	02/2020
66	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]	8/2010	103.02 -	171.04	117.61	07/2016 08/2016	08/2016
67	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
68	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	1,320.05	05/2014 03/2017	03/2017
69	RESID UPGRADEATION PROJECT - [N16000184]	3/2013	3,110.36 -	3,110.36	1,840.40	11/2015 11/2016	11/2016
70	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	439.03	10.60	03/2017 06/2018	06/2018
71	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	7/2009	3,957.00 -	3,561.00	215.38	01/2013 12/2018	12/2018
72	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	330.01	09/2017 03/2018	03/2018
73	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	632.64	11/2015 11/2016	11/2016
74	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	1,055.56	05/2013 12/2016	12/2016
75	CONSTRUCTION OF 6 ETPS - [N16000117]	3/2009	317.64 -	240.95	139.01	09/2012 09/2016	09/2016
76	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220]	2/2015	184.00 -	184.00	16.26	12/2017 -	12/2017
77	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	789.44	04/2016 12/2017	12/2017

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
78	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	179.17	09/2016 -	09/2016
79	NEW 250 TMTPL LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	53.48	09/2017 -	09/2017
80	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	147.72	12/2016 -	12/2016
81	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	982.92	12/2018 -	12/2018
82	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	4,080.91	05/2017 05/2017	05/2017
83	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]	12/2009	463.32 -	463.32	344.95	06/2011 10/2016	10/2016
84	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	375.14	12/2014 03/2018	03/2018
85	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	58.32	10/2018 -	10/2018
86	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	94.30	02/2016 07/2016	07/2016
87	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	227.71	12/2017 -	12/2017
88	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221]	1/1991	694.00 -	694.00	57.19	10/2018 -	10/2018
89	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017
90	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,351.65	03/2015 03/2018	03/2018
91	DE-BOTTLENECKING OF SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	1,405.13	03/2017 03/2017	03/2017
92	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	467.91	08/2015 12/2016	12/2016
93	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	17.76	03/2013 01/2017	01/2017
94	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	84.95	04/2018 -	04/2018
95	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219]	8/2014	393.00 -	393.00	-	04/2018 -	04/2018
96	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
97	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	289.76	10/2014 03/2017	03/2017
98	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	1,200.00	627.43	03/2015 12/2016	12/2016
99	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	-	02/2019 -	02/2019

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
100	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,188.25	05/2017 -	05/2017
101	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	1,873.19	03/2013 03/2017	03/2017
102	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	1,054.15	05/2019 03/2020	03/2020
	Total		67,438.77 -	68,274.20	23,312.36		
	<u>POWER</u>						
103	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017
104	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	21.80	07/2017 -	07/2017
105	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	851.60	03/2018 -	03/2018
106	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,467.00	12/2016 -	12/2016
107	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	13.10	11/2017 -	11/2017
108	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	13.90	07/2018 -	07/2018
109	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	214.00	11/2016 -	11/2016
110	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	696.10	05/2018 -	05/2018
111	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	46.34	10/2016 -	10/2016
112	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	38.50	03/2018 -	03/2018
113	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	138.90	10/2016 -	10/2016
114	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	11,863.00	01/2011 05/2018	05/2018
115	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	3.50	05/2018 -	05/2018
116	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
117	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	29.90	07/2018 -	07/2018
118	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	182.20	04/2017 -	04/2017

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
119	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239	12/2004	2,496.90 -	6,179.96	4,721.52	12/2009 03/2017	03/2017
120	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206	1/2016	305.04 -	305.04	9.30	03/2017 -	03/2017
121	TANDA TPP STAGE-II (2X660 MW) - [N18000175	9/2014	9,188.98 -	9,188.98	1,553.00	03/2019 -	03/2019
122	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210	1/2016	207.88 -	207.88	-	07/2018 -	07/2018
123	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180	1/2015	268.80 -	268.80	49.00	03/2018 -	03/2018
124	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	3/2013	11,638.55 -	11,638.55	5,937.00	09/2017 -	09/2017
125	RAMMAM-III HEPP (3X40 MW) - [N18000178	9/2014	1,381.84 -	1,381.84	197.00	09/2019 -	09/2019
126	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	7/2006	1,657.00 -	2,978.86	1,752.36	02/2016 09/2019	09/2019
127	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS [N18000211	1/2016	187.04 -	187.04	1.70	06/2018 -	06/2018
128	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) [N18000181	1/2015	871.62 -	871.62	57.70	10/2017 -	10/2017
129	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	7/1998	368.72 -	1,441.52	1,049.75	07/2006 03/2017	03/2017
130	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC [N18000167	6/2014	400.47 -	400.47	155.00	04/2017 -	04/2017
131	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	1/2016	10,598.98 -	10,598.98	171.00	07/2020 -	07/2020
132	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	2/2009	11,130.19 -	13,762.80	12,010.40	08/2013 12/2017	12/2017
133	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173	11/2014	972.42 -	972.42	113.30	11/2017 -	11/2017
134	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169	8/2014	288.49 -	288.49	99.90	02/2017 -	02/2017
135	KHARGONE STPP STAGE I (1320 MW) - [N18000205	3/2015	9,870.51 -	9,870.51	1,599.00	09/2019 -	09/2019
136	NORTH KARANPURA STPP (3X660 MW) - [N18000177	2/2014	14,366.58 -	14,366.58	2,967.00	02/2019 -	02/2019
137	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
138	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
139	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184	3/2015	197.40 -	197.40	3.30	03/2018 -	03/2018
140	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	1/2013	12,964.60 -	12,964.60	6,735.12	01/2018 -	01/2018
141	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	2/2014	12,532.44 -	12,532.44	3,546.00	08/2018 -	08/2018
142	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
143	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	11,846.00	6,517.00	06/2017 -	06/2017
144	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194	5/2015	436.68 -	436.68	443.28	12/2016 -	12/2016
145	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,581.04	1,229.17	08/2013 12/2016	12/2016
146	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162	5/2014	829.98 -	829.98	233.90	08/2016 -	08/2016
147	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179	12/2014	6,517.36 -	6,517.36	740.80	04/2018 -	04/2018
148	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196	4/2015	3,705.61 -	3,705.61	570.60	04/2018 -	04/2018
	Total		158,429.11 -	174,549.19	68,190.54		
	<u>RAILWAYS</u>						
149	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT - [N22000384	4/1990	153.82 -	551.82	245.58	03/2019 -	03/2019
150	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
151	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113	4/2008	653.19 -	658.07	453.55	03/2014 03/2019	03/2019
152	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
153	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
154	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379	4/2015	2,361.74 -	2,361.74	-	03/2021 -	03/2021
155	JAGADALPUR-KORAPUT DOUBLING - [N22000376	4/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021
156	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	209.00	0.36	12/2016 -	12/2016
157	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	2,499.71	-	03/2021 -	03/2021

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
158	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,750.00 -	1,750.00	-	03/2022 -	03/2022
159	VIRAMGAM BHILDI - [N22000391	4/1990	237.13 -	237.13	25.05	03/2018 -	03/2018
160	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	4/2015	701.61 -	701.61	0.84	03/2021 -	03/2021
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	4/2008	5,300.00 -	7,986.04	2,423.55	03/2014 03/2019	03/2019
162	KIUL - GAYA DOUBLING PROJECT - [N22000349	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
163	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	3/1996	155.74 164.36	966.98	884.25	02/2009 12/2017	12/2017
164	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	1,571.89	03/2014 12/2017	12/2017
165	JAGGAYYAPET - MELLACHERUVU - [N22000304	4/2007	313.24 -	554.70	384.84	01/1999 06/2017	06/2017
166	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	4/2008	318.24 -	321.62	40.64	03/2012 03/2019	03/2019
167	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
168	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	1.11	03/2021 -	03/2021
169	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022
170	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	4/1995	900.05 -	1,125.89	983.85	12/2011 03/2020	03/2020
171	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
	Total		25,927.44 -	31,910.60	7,191.33		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
172	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
173	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
174	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	57.43	03/2018 -	03/2018
175	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) [N24000450	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
176	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	259.05	02/2018 -	02/2018
177	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) [N24000440	9/2015	789.31 -	789.31	-	03/2018 -	03/2018

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
178	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	190.00	11/2017 -	11/2017
179	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00 -	709.00	19.24	09/2017 -	09/2017
180	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
181	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
182	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]	8/2014	187.79 -	187.79	57.60	07/2016 -	07/2016
183	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,474.76	01/2018 -	01/2018
184	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,101.09	07/2017 -	07/2017
185	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
186	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
187	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
188	4 LANING OF OBDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00 -	912.00	120.43	08/2016 -	08/2016
189	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	79.70	07/2018 -	07/2018
190	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	234.67	08/2016 -	08/2016
191	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	282.41	75.32	08/2016 -	08/2016
192	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]	11/2010	305.49 -	305.49	-	03/2017 -	03/2017
193	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	1/1991	358.22 -	358.22	200.21	10/2016 -	10/2016
194	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
195	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
196	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]	12/2013	319.80 -	319.80	-	10/2016 -	10/2016

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
197	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
198	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	-	01/2019 -	01/2019
199	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	-	04/2017 -	04/2017
200	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
201	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	66.59	03/2018 -	03/2018
202	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	-	10/2018 -	10/2018
203	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	-	03/2018 -	03/2018
204	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	108.37	11/2016 -	11/2016
205	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
206	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017
207	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
208	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
209	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
210	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
211	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
212	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377	1/2014	397.04 -	397.04	17.71	10/2016 -	10/2016
213	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	166.22	05/2017 -	05/2017

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
214	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017
215	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	-	06/2018 -	06/2018
216	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
217	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	21.03	10/2016 -	10/2016
218	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	156.09	-	12/2016 -	12/2016
219	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
220	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
221	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018
222	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
223	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
224	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017
225	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
226	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017
227	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	63.38	07/2017 -	07/2017
228	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017
229	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	497.05	0.54	05/2017 -	05/2017
230	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	-	05/2018 -	05/2018

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
231	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	-	06/2018 -	06/2018
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	41.21	10/2017 -	10/2017
233	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
234	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	-	10/2016 -	10/2016
235	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	-	05/2018 -	05/2018
236	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
237	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	225.02	-	12/2018 -	12/2018
238	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	46.11	05/2018 -	05/2018
239	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
240	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	6.33	03/2018 -	03/2018
241	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,492.63	11/2016 -	11/2016
242	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	95.00	04/2018 -	04/2018
243	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
244	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
245	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350	6/2015	563.92 -	563.92	13.66	12/2017 -	12/2017
246	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26 -	269.26	218.10	10/2016 -	10/2016
248	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	-	03/2018 -	03/2018

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
249	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	57.99	02/2018 -	02/2018
250	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	160.00	200.36	05/2008 07/2016	07/2016
251	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	55.86	10/2017 -	10/2017
252	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH - [N24000340	12/2014	451.58 -	451.58	28.00	06/2017 -	06/2017
253	VADODARA-SURAT SECTION - [N24000361	3/2014	503.16 -	503.16	258.39	08/2016 -	08/2016
254	FOUR LANING OF VARANASI BYPASS - [N24000356	5/2015	261.09 -	261.09	34.10	05/2017 -	05/2017
255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575	2/2014	665.50 -	665.50	-	07/2016 -	07/2016
256	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
257	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	162.33	05/2017 -	05/2017
258	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344	9/2014	425.19 -	425.19	274.20	09/2016 -	09/2016
259	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368	11/2014	563.92 -	563.92	124.09	11/2016 -	11/2016
260	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579	1/2014	1,408.85 -	1,408.85	-	10/2016 -	10/2016
261	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	22.60	12/2017 -	12/2017
262	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	4.47	06/2018 -	06/2018
263	PADI - DAHOD - [N24000353	11/2014	279.14 -	279.14	105.62	05/2017 -	05/2017
264	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
265	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343	9/2015	341.61 -	341.61	140.65	09/2017 -	09/2017
266	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	102.12	11/2016 -	11/2016
267	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
268	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	10.32	05/2018 -	05/2018
269	FOUR LANING OF CHADIGARH - KHARAR - [N24000503	10/2015	447.29 -	447.29	-	12/2017 -	12/2017

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
270	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66	2,168.66	-	06/2019	06/2019
271	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580	3/2015	206.80	206.80	-	07/2016	07/2016
272	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2-LANE WITH P - [N24000574	11/2013	683.83	683.83	-	07/2016	07/2016
273	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590	5/2015	581.84	581.84	-	05/2017	05/2017
274	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338	10/2014	206.12	206.12	112.00	04/2017	04/2017
275	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72	264.72	116.15	04/2017	04/2017
276	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60	455.60	54.50	07/2017	07/2017
277	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61	309.56	399.08	04/2010 09/2016	09/2016
278	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11	401.11	239.02	01/2017	01/2017
279	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34	562.34	-	04/2018	04/2018
280	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366	6/2015	996.37	996.37	-	12/2017	12/2017
281	JAISALMER - BARMER - [N24000348	8/2015	482.27	482.27	76.80	02/2018	02/2018
282	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263	2/2015	241.61	241.61	46.68	02/2017	02/2017
	Total		60,259.20	60,490.53	9,131.78		
	SHIPPING AND PORTS						
283	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85	274.85	160.22	04/2017	04/2017
284	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	1/2007	366.39	669.46	415.01	12/2010 12/2018	12/2018
285	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	9.77	12/2017	12/2017
286	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94	235.15	157.96	06/2017	06/2017
287	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00	210.00	-	01/2018	01/2018

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,294.68 -	1,647.79	742.96		
	<u>STEEL</u>						
288	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	13.87	09/2017 -	09/2017
289	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	370.92	04/2018 -	04/2018
290	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	61.81	10/2017 -	10/2017
291	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	103.89	12/2017 -	12/2017
292	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 253.92	253.92	194.54	06/2016 -	06/2016
293	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	200.20	12/2016 -	12/2016
294	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
295	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]	4/2014	151.33 -	151.33	11.86	09/2017 -	09/2017
296	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]	2/2014	787.29 -	787.29	317.73	12/2016 -	12/2016
297	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	50.34	03/2018 -	03/2018
298	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	99.91	04/2018 -	04/2018
299	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	-	06/2020 -	06/2020
300	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	136.15	03/2018 -	03/2018
301	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	9,652.03	05/2015 12/2017	12/2017
	Total		28,616.83 -	28,641.22	11,213.25		
	<u>URBAN DEVELOPMENT</u>						
302	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	117.94	09/2016 01/2017	01/2017
303	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	40.61	03/2017 -	03/2017

(June 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
304	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]	11/2012	270.83 -	270.83	81.52	11/2014 03/2017	03/2017
305	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]	2/2014	216.69 -	216.69	17.54	03/2015 10/2017	10/2017
306	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]	8/2014	350.02 -	350.02	144.54	03/2015 03/2017	03/2017
307	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	5,298.00	1,528.93	11/2019 -	11/2019
308	BANGALORE METRO RAIL PROJECT - [N28000008]	5/2006	6,395.00 -	14,405.01	13,973.45	06/2011 11/2016	11/2016
309	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	161.22	03/2018 -	03/2018
	Total		20,667.10 -	29,711.11	16,065.75		
	Grand Total		424,240.57	459,028.73	149,722.85		

Annexure - XIII

List of ongoing projects having cost overrun w.r.t. to latest schedule

(June 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
5	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
7	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,541.29 -	2,683.91			
	<u>HEAVY INDUSTRY</u>						
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
9	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	06/2018	24.53
10	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	09/2016	63.54
11	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57

(June 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	09/2016	16.02
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	12/2016	37.72
	Total		17,261.99 -	20,256.25			
	<u>POWER</u>						
14	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
15	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
16	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	2,336.74	09/2009 -	09/2016	120.16
17	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49	02/2016 -	06/2016	0.16
18	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	09/2016	2.38
19	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	9.40
20	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,581.04	08/2013 -	12/2016	175.45
21	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	11/2016	58.79
	Total		22,219.82 -	49,681.83			
	<u>RAILWAYS</u>						
22	GUNA-ETAWAH VIA SHIVPURI-GWALIOR-BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	02/2016	131.09
23	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	387.07
24	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
25	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	870.00	- -	-	459.31
26	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
27	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	128.29
28	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
29	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	-	543.99

(June 2016)

(June 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
30	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
31	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
32	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,500.00	12/2012 12/2012	-	147.08
33	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
34	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	-	210.19
35	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
36	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	-	156.57
37	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	3,000.00	- -	-	312.58
38	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
39	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
40	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
41	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	-	76.98
42	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	340.00	03/2009 03/2009	10/2016	64.25
43	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
44	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	360.00	02/2006 -	-	37.56
45	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
46	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	2,072.50	- -	-	412.75
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	1,065.00	- -	-	210.34
48	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	490.00	- -	-	292.00
49	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	1,080.00	- -	-	136.84
50	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
51	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2020	355.36
52	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30

(June 2016)

(June 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	03/2022	135.68
54	KATAKHAL TO BHAI RABI - [N22000126]	04/1998	227.90 -	326.51	12/2012 -	-	43.27
55	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	365.00	- -	-	269.66
56	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
57	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
58	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
59	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
60	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
61	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
62	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
63	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
64	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
65	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
66	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,170.00	01/1999 -	-	153.83
67	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017	77.08
68	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
69	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
71	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	5,050.00	05/2008 -	03/2023	1,939.09
72	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
73	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
74	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
75	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34

(June 2016)

(June 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
77	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,046.72	03/2011 -	03/2019	1,143.43
78	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
79	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	3,142.46	10/2007 -	-	403.22
80	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
81	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
82	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	837.73	- -	03/2020	179.24
83	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,513.30	03/2015 -	03/2020	195.68
84	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
85	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	-	228.10
86	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
87	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	565.13	- -	03/2018	99.75
88	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	55.46
89	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	560.00	- -	-	36.56
90	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114	04/2008	516.23 -	735.00	03/2014 -	-	42.38
91	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
92	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
93	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	107.40
94	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	2,434.00	03/2010 -	03/2017	648.92
95	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
96	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	12/2016	122.68
97	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66

(June 2016)

(June 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	488.33
99	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
100	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	-	284.00
101	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
102	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
103	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
104	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	-	72.62
105	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
106	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]	04/1997	836.26 -	1,072.51	- -	-	28.25
107	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
108	KAKINADA-PITHAPURAM - [N22000314]	03/1999	215.06 -	220.29	- -	-	2.43
109	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	03/2021	63.70
110	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	10/2015	14.43
111	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	- -	03/2020	52.77
112	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
113	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
114	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	455.96	- -	03/2019	139.85
115	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
116	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	620.00	- -	-	3.33
117	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
118	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
119	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
120	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01

(June 2016)

(June 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
121	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38 -	- -	- -	71.11
122	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68 -	- -	- -	92.25
123	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63 -	- -	03/2019 -	24.63
124	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15 -	- -	03/2019 -	132.54
125	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00 -	- -	09/2015 -	27.06
126	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00 -	- -	- -	68.05
127	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60 -	02/2020 -	12/2022 -	226.98
128	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00 -	- -	- -	10.58
129	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	860.00 -	- -	- -	88.60
130	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22 -	- -	03/2017 -	17.92
131	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39 -	- -	- -	2.34
132	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50 -	02/2019 -	12/2022 -	226.23
133	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00 -	- -	- -	62.32
134	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00 -	- -	- -	82.25
135	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00 -	- -	- -	162.39
136	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00 -	03/2015 -	12/2016 -	53.44
137	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00 -	06/2013 -	12/2016 -	37.41
138	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00 -	12/2015 -	03/2016 -	88.40
139	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00 -	- -	12/2017 -	41.36
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00 -	- -	- -	84.98
141	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56 -	- -	- -	32.80
142	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09 -	- -	- -	338.91

(June 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
143	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
144	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
145	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
146	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
147	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
148	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
149	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	- -	03/2018	80.06
150	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
151	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	467.91	- -	03/2019	111.32
152	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,451.00	03/2007 -	-	62.12
153	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	440.05	- -	03/2018	109.78
154	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.11	- -	03/2018	1.61
155	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
156	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
157	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
158	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
159	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2020	46.95
160	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	599.90	- -	03/2018	147.67
161	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
162	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	412.53	- -	03/2018	148.78
163	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJBHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
164	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17

(June 2016)

(June 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
165	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	386.68	- -	03/2019	57.14
166	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
167	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
168	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,103.00	- -	-	129.59
169	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.00	- -	-	101.90
170	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	233.73	04/2014 -	03/2018	24.82
171	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
172	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT [N22000384]	04/1990	153.82 -	551.82	03/2019 -	03/2019	258.74
	Total		71,133.24 -	201,206.59			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
173	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	08/2016	28.93
174	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2016	92.75
175	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	12/2016	80.68
176	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	12/2016	68.99
177	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50
178	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]	01/2014	361.30 -	207.40	07/2014 -	-	-42.60
179	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2016	30.10
180	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
181	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	12/2016	2.65
182	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
183	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66

(June 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
184	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	0.12
185	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	0.01
186	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	0.06
187	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
188	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2016	51.83
	Total		6,301.96 -	8,899.42			
	<u>SHIPPING AND PORTS</u>						
189	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	0.13
190	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
	Total		490.17 -	668.16			
	<u>STEEL</u>						
191	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
192	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	1.70
	Total		492.73 -	664.34			
	<u>URBAN DEVELOPMENT</u>						
193	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	14,405.01	06/2011 -	11/2016	125.25
194	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073	06/2010	205.00 -	191.97	03/2012 -	03/2017	-6.36
195	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	5,298.00	11/2019 -	11/2019	24.25
	Total		10,864.00 -	19,894.98			
	Grand Total		148,903.80	336,165.88			

Annexure- XIV

List of Delayed Projects w.r.t. Latest Schedule

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	8,603.00	12/2015 11/2016	11/2018	35	24
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	6,415.00	12/2016 03/2017	12/2019	36	33
	Total		23,779.00 -	23,779.00	15,018.00				
	<u>CIVIL AVIATION</u>								
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	433.19	01/2011 06/2016	09/2017	80	15
	Total		309.46 -	309.46	433.19				
	<u>COAL</u>								
4	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	220.04	10/2014 -	08/2016	22	-
5	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	82.97	03/2014 -	09/2016	30	-
6	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	122.47	05/2014 -	10/2016	29	-
7	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	80.41	04/2014 -	11/2016	31	-
8	ASHOK EXPN OCP CCL (10 MTY) - [N06100096]CCL, JHARKHAND	12/2007	341.63 -	341.63	121.94	03/2011 -	03/2017	72	-
9	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	278.00	03/2013 -	03/2017	48	-
10	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	182.26	03/2010 -	03/2017	84	-
11	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	121.97	12/2012 -	03/2017	51	-
12	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	198.63	03/2012 -	03/2017	60	-
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	188.13	03/2013 -	03/2017	48	-
14	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	86.88	03/2015 -	03/2017	24	-
15	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	108.66	03/2012 -	03/2017	60	-
16	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	95.73	03/2012 -	03/2017	60	-
17	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	72.08	03/2014 -	03/2017	36	-
18	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	03/2017	35	-

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	39.49	06/2015 -	03/2017	21	-
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	120.14	03/2012 -	03/2018	72	-
21	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	197.76	03/2014 -	03/2018	48	-
22	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	134.17	03/2016 -	03/2018	24	-
23	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.09	03/2015 -	03/2018	36	-
24	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	-
25	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	85.33	03/2015 -	03/2018	36	-
26	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	122.93	03/2016 -	03/2018	24	-
27	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	486.27	92.33	03/2016 -	03/2018	24	-
28	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	228.71	03/2018 -	09/2018	6	-
29	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	32.26	07/2016 -	03/2019	32	-
30	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	-
31	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	29.83	03/2015 -	03/2020	60	-
32	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.35	03/2014 -	03/2020	72	-
33	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	79.50	07/2012 03/2017	03/2021	104	48
34	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132	-
	Total		10,710.40 -	10,836.97	3,746.86				
	<u>MINES</u>								
36	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL, MADHYA PRADESH	09/2011	1,856.00 -	1,176.00	12.44	09/2017 -	04/2020	31	-
	Total		1,856.00 -	1,176.00	12.44				
	<u>STEEL</u>								
37	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	178.85	10/2013 -	08/2016	34	-
38	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	446.48	04/2016 -	09/2016	5	-

(June 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
39	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	529.21	07/2015 -	11/2016	16	-
40	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	16,235.61	03/2013 -	12/2016	45	-
41	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	139.69	05/2016 -	12/2016	7	-
42	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	78.23	04/2015 -	12/2016	20	-
43	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	357.53	07/2016 -	03/2017	8	-
44	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	67.55	09/2016 -	03/2017	6	-
45	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	178.61	12/2015 -	03/2017	15	-
46	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	650.35	03/2015 -	03/2017	24	-
47	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	100.51	10/2016 -	06/2017	8	-
48	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	206.71	141.17	12/2016 -	07/2017	7	-
49	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	336.54	07/2015 -	09/2017	26	-
	Total		22,756.71 -	22,959.54	19,440.33				
	<u>PETROLEUM</u>								
50	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	251.66	172.53	06/2012 11/2015	08/2016	50	9
51	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00 -	16,504.00	11,626.55	05/2016 -	09/2016	4	-
52	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,489.38	01/2012 -	09/2016	56	-
53	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,447.36	09/2012 -	12/2016	51	-
54	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	187.61	03/2014 05/2016	12/2016	33	7
55	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	650.62	04/2015 05/2016	12/2016	20	7
56	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	117.38	05/2015 -	12/2016	19	-
57	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	275.75	11/2016 -	12/2016	1	-
58	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30	-
59	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	516.44	09/2011 10/2016	03/2017	66	5

(June 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
60	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	553.79	08/2015 -	03/2017	19	-
61	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	36.88	11/2016 -	03/2017	4	-
62	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	79.68	07/2016 -	04/2017	9	-
63	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	238.50	26.16	03/2017 -	08/2017	5	-
64	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00 -	184.00	16.26	06/2017 -	12/2017	6	-
65	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	101.37	10/2017 -	02/2018	4	-
66	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	206.25	09/2017 -	03/2018	6	-
67	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	-
68	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,381.86	12/2012 -	02/2019	74	-
	Total		29,733.28 -	32,307.12	19,025.89				
	POWER								
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	388.37	02/2012 -	06/2016	52	-
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,481.22	04/2013 -	06/2016	38	-
71	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	302.49	276.70	02/2016 -	06/2016	4	-
72	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 390.51	390.51	261.30	01/2013 03/2016	07/2016	42	4
73	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	615.91	11/2013 -	07/2016	32	-
74	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	92.40	12/2015 -	07/2016	7	-
75	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	312.94	65.20	05/2016 -	07/2016	2	-
76	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,081.09	08/2012 -	08/2016	48	-
77	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	3,294.11	10/2014 -	08/2016	22	-

(June 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	357.52	05/2015 -	08/2016	15	-
79	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	381.00	06/2015 -	08/2016	14	-
80	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,172.03	06/2015 -	08/2016	14	-
81	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	2,336.74	2,028.58	09/2009 -	09/2016	84	-
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	585.16	11/2011 -	09/2016	58	-
83	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	573.02	07/2013 11/2015	09/2016	38	10
84	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	633.62	11/2014 -	09/2016	22	-
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	504.09	03/2016 -	09/2016	6	-
86	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	26.20	03/2016 -	09/2016	6	-
87	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,574.18	12/2011 03/2016	09/2016	57	6
88	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	112.53	09/2014 -	10/2016	25	-
89	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR	01/2009	3,642.04 -	5,783.17	4,617.51	01/2016 -	11/2016	10	-
90	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH	05/2011	1,961.87 2,310.58	2,310.58	1,822.25	05/2014 06/2016	11/2016	30	5
91	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	2,078.46	09/2014 -	12/2016	27	-
92	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL, CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,407.93	07/2014 -	12/2016	29	-
93	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	313.97	08/2014 06/2015	12/2016	28	18
94	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,546.52	01/2015 -	12/2016	23	-
95	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	7,921.47	5,596.00	09/2016 -	12/2016	3	-

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
96	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	1,018.20	05/2016 -	12/2016	7	-
97	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	753.84	04/2016 -	12/2016	8	-
98	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	62.60	07/2016 -	12/2016	5	-
99	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	38.00	02/2016 -	12/2016	10	-
100	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	6,274.99	06/2015 -	02/2017	20	-
101	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	603.59	09/2010 01/2016	03/2017	78	14
102	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,067.00	09/2011 08/2016	03/2017	66	7
103	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,327.38	10/2012 -	03/2017	53	-
104	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,831.55	01/2015 -	03/2017	26	-
105	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	220.09	06/2012 -	03/2017	57	-
106	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	449.02	06/2014 03/2016	03/2017	33	12
107	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,586.53	08/2014 12/2015	03/2017	31	15
108	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	11,196.00	01/2017 -	03/2017	2	-
109	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	27.60	04/2016 -	03/2017	11	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	163.50	06/2016 -	03/2017	9	-
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	416.10	06/2016 -	03/2017	9	-
112	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,908.05	11/2008 01/2016	06/2017	103	17
113	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,335.20	12/2012 12/2016	06/2017	54	6
114	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,298.13	11/2012 03/2016	06/2017	55	15
115	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,285.25	12/2015 -	06/2017	18	-

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	6,564.00	11/2016 -	08/2017	9	-
117	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,679.02	05/2014 03/2017	09/2017	40	6
118	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,332.28	12/2016 -	09/2017	9	-
119	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	72.21	02/2014 -	02/2018	48	-
120	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	0.70	09/2017 -	07/2018	10	-
121	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	5,671.34	09/2009 -	12/2018	111	-
122	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,869.00	03/2013 03/2016	06/2019	75	39
123	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	849.35	06/2013 -	12/2019	78	-
124	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	141.80	04/2020 -	03/2022	23	-
	Total		134,278.12 -	150,365.16	105,929.19				
	<u>HEAVY INDUSTRY</u>								
125	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	2,289.00				
	<u>HEALTH AND FAMILY WELFARE</u>								
126	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	400.00	12/2015 -	06/2016	6	-
127	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	127.80	11/2013 -	10/2016	35	-
128	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	59.29	05/2017 -	06/2017	1	-
129	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	101.00	05/2017 -	06/2017	1	-
130	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	168.90	16.50	05/2017 -	07/2017	2	-
	Total		1,271.19 -	1,271.19	704.59				
	<u>RAILWAYS</u>								
131	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	06/2016	3	-
132	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	340.00	328.43	03/2009 03/2009	10/2016	91	91

(June 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
133	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	370.00	356.17	02/2009 02/2009	12/2016	94	94
134	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	54.96	03/2015 -	12/2016	21	-
135	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	235.00	226.99	06/2013 -	12/2016	42	-
136	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	2,434.00	669.00	03/2010 -	03/2017	84	-
137	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11	-
138	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	4,996.19	3,689.32	04/2008 12/2011	06/2017	110	66
139	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	928.13	03/2010 -	06/2017	87	-
140	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	402.56	03/2010 -	12/2017	93	-
141	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	12/2017	21	-
142	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	742.05	12/2010 -	03/2018	87	-
143	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	2,531.34	2,269.43	12/2008 -	03/2018	111	-
144	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	546.61	03/2014 -	03/2018	48	-
145	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	233.73	28.33	04/2014 -	03/2018	47	-
146	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
147	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	-	11/2002 -	12/2018	193	-
148	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	641.78	03/2016 -	12/2018	33	-
149	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	9,046.72	5,338.49	03/2011 -	03/2019	96	-
150	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,160.54	1,776.81	1,027.59	03/1998 -	12/2019	261	-
151	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	479.90	03/2005 12/2008	12/2019	177	132
152	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 -	1,428.00	456.82	06/2005 -	12/2019	174	-
153	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	2,820.25	679.78	04/2014 -	03/2020	71	-
154	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,085.00	4,085.00	385.59	12/2015 -	03/2020	51	-
155	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	45.70	03/2013 -	03/2020	84	-

(June 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,513.30	148.39	03/2015 -	03/2020	60	-
157	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	3,161.58	998.39	03/2016 -	12/2020	57	-
158	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	1,421.25	690.23	03/2012 -	03/2022	120	-
159	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
160	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	5,050.00	983.61	05/2008 -	03/2023	178	-
	Total		30,418.22 -	85,678.18	24,264.22				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
161	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56	-
162	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	248.73	09/2008 -	06/2016	93	-
163	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	294.65	06/2008 -	06/2016	96	-
164	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	320.02	06/2008 -	06/2016	96	-
165	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	923.28	08/2013 -	06/2016	34	-
166	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	924.70	12/2013 -	06/2016	30	-
167	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	24	-
168	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	409.39	06/2008 -	07/2016	97	-
169	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	514.30	09/2008 -	07/2016	94	-
170	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	313.71	06/2008 06/2016	07/2016	97	1
171	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	4,211.50	06/2015 -	07/2016	13	-
172	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	07/2016	38	-
173	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	07/2016	35	-
174	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	1,406.70	03/2013 -	07/2016	40	-
175	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	07/2016	29	-
176	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	899.71	03/2014 -	07/2016	28	-

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
177	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	549.10	11/2013 -	07/2016	32	-
178	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	07/2016	41	-
179	BEAWAR PALI PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.51 -	2,388.00	2,490.61	06/2014 -	07/2016	25	-
180	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	226.96	09/2014 -	07/2016	22	-
181	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI, RAJASTHAN	01/2014	158.04 -	158.04	129.37	12/2015 -	07/2016	7	-
182	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI, RAJASTHAN	01/2014	368.15 -	368.15	190.73	01/2016 -	07/2016	6	-
183	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	24	-
184	4 LANING OF GOMTI CHAURAH - UDAIPUR - [N24000455]NHAI, RAJASTHAN	03/2012	914.50 -	914.50	1,128.25	10/2015 -	07/2016	9	-
185	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]NHAI, HARYANA	03/2013	959.25 -	959.25	1,229.40	06/2016 -	07/2016	1	-
186	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,946.14	10/2011 -	07/2016	57	-
187	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	427.01	02/2009 -	08/2016	90	-
188	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	889.94	03/2013 -	08/2016	41	-
189	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,016.24	05/2013 -	08/2016	39	-
190	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	1,282.25	06/2013 -	08/2016	38	-
191	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	08/2016	38	-
192	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN	10/2013	677.79 -	677.79	878.97	04/2016 -	08/2016	4	-
193	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD, MADHYA PRADESH	11/2011	871.15 -	871.15	393.88	09/2015 -	08/2016	11	-
194	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	348.16	398.79	09/2007 -	09/2016	108	-
195	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	474.72	05/2013 -	09/2016	40	-
196	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	356.34	01/2014 -	09/2016	32	-
197	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	283.84	10/2013 -	09/2016	35	-
198	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	240.10	162.19	03/2016 -	09/2016	6	-
199	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD, MADHYA PRADESH	01/2012	320.48 -	320.48	192.55	08/2015 -	09/2016	13	-

(June 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
200	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH, BIHAR	10/2014	377.64 -	377.64	-	03/2014 -	09/2016	30	-
201	2-LANING WITH PAVED SHOULDERS OF RAEABARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	351.34	199.74	01/2016 -	10/2016	9	-
202	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEABARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	495.78	301.70	01/2016 -	10/2016	9	-
203	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD, ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	-
204	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD, ANDHRA PRADESH	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	24	-
205	FOUR LANING OF ORISSA/CHHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00 -	1,232.00	1,123.15	08/2015 -	11/2016	15	-
206	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00 -	230.00	203.60	06/2005 -	12/2016	138	-
207	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	211.01	04/2009 -	12/2016	92	-
208	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	277.36	11/2008 -	12/2016	97	-
209	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	196.86	11/2008 -	12/2016	97	-
210	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	247.56	04/2009 -	12/2016	92	-
211	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	214.88	03/2008 07/2016	12/2016	105	5
212	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	331.23	365.05	07/2009 -	12/2016	89	-
213	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	469.41	05/2010 -	12/2016	79	-
214	GUJARAT/MAHARASHTRA BORDERSURAT- HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 2,782.54	1,509.10	3,200.86	09/2012 -	12/2016	51	-
215	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,675.29	08/2011 -	12/2016	64	-
216	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,822.02	11/2011 -	12/2016	61	-
217	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,206.10	04/2013 -	12/2016	44	-
218	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	1,038.84	07/2013 -	12/2016	41	-
219	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	39	-
220	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	12/2016	42	-

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,488.49	08/2014 -	12/2016	28	-
222	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,893.03	03/2013 -	12/2016	45	-
223	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,415.99	07/2013 -	12/2016	41	-
224	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	880.67	02/2013 -	12/2016	46	-
225	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	12/2016	37	-
226	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	974.56	07/2013 -	12/2016	41	-
227	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,802.56	05/2014 -	12/2016	31	-
228	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.75	07/2013 -	12/2016	41	-
229	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,363.70	06/2014 -	12/2016	30	-
230	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35	-
231	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	875.56	08/2013 -	12/2016	40	-
232	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	600.65	09/2013 -	12/2016	39	-
233	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,089.05	03/2013 -	12/2016	45	-
234	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,133.37	08/2013 -	12/2016	40	-
235	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,430.70	09/2014 -	12/2016	27	-
236	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2016	32	-
237	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	347.50	06/2014 -	12/2016	30	-
238	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	12/2016	12	-
239	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	12	-
240	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	-
241	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	301.04	57.42	01/2016 -	12/2016	11	-
242	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	329.25	11/2016 -	12/2016	1	-
243	FOUR LANING OF GWALIOR-SHIPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,357.85	11/2015 -	12/2016	13	-
244	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	1,722.39	04/2015 -	01/2017	21	-

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
245	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	-
246	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,878.76	09/2015 -	02/2017	17	-
247	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	-
248	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 -	212.00	122.22	09/2007 -	03/2017	114	-
249	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	284.10	08/2012 -	03/2017	55	-
250	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	506.50	04/2014 -	03/2017	35	-
251	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,630.30	06/2014 -	03/2017	33	-
252	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	901.00	09/2016 -	03/2017	6	-
253	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	103.60	01/2016 -	03/2017	14	-
254	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	681.17	03/2014 -	04/2017	37	-
255	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	185.05	02/2010 -	05/2017	87	-
256	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	-
257	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43 -	580.43	269.89	08/2013 -	05/2017	45	-
258	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	564.59	06/2015 -	05/2017	23	-
259	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	283.25	180.61	10/2015 -	05/2017	19	-
260	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
261	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	691.92	01/2014 -	06/2017	41	-
262	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	1,761.23	09/2014 -	06/2017	33	-
263	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,682.27	07/2015 -	07/2017	24	-
264	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,488.67	02/2014 -	08/2017	42	-
265	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	-
266	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	1,655.01	899.00	08/2016 -	08/2017	12	-

(June 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
267	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,745.49	08/2013 -	09/2017	49	-
268	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	368.73	104.81	09/2016 -	09/2017	12	-
269	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	871.15	09/2014 -	10/2017	37	-
270	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	1,287.95	757.57	11/2015 -	10/2017	23	-
271	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
272	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	-
273	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	-
274	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48	-
275	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55	-
276	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	309.66	08/2013 -	12/2017	52	-
277	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	622.90	10/2013 -	12/2017	50	-
278	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	349.50	07/2014 -	12/2017	41	-
279	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
280	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69	-
281	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
282	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
283	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	-
	Total		93,768.88 -	96,105.34	104,687.55				
	SHIPPING AND PORTS								

(June 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
284	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 600.00	600.00	139.80	03/2006 01/2016	07/2016	124	6
285	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	409.83	350.68	04/2009 03/2010	08/2016	88	77
	Total		395.67 -	1,009.83	490.48				
	<u>TELECOMMUNICATIONS</u>								
286	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	301.57	09/2014 -	03/2017	30	-
	Total		2,111.17 -	2,011.17	301.57				
	<u>URBAN DEVELOPMENT</u>								
287	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	199.73	05/2013 10/2015	06/2016	37	8
288	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	12,738.83	12/2015 -	08/2016	8	-
289	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 315.00	315.00	196.71	06/2015 08/2016	11/2016	17	3
290	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	23,763.22	03/2016 -	12/2016	9	-
291	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 405.01	405.01	236.45	12/2014 -	12/2016	24	-
292	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	10,255.48	12/2014 12/2016	03/2017	27	3
293	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 142.37	191.97	108.07	03/2012 08/2016	03/2017	60	7
294	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	48.61	09/2015 07/2016	04/2017	19	9
295	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	24.51	03/2016 -	09/2017	18	-
296	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33 356.59	356.59	108.43	11/2014 -	12/2017	37	-
297	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 -	26,405.14	700.85	02/2019 -	03/2020	13	-
	Total		81,535.63 -	81,637.86	48,380.89				
	Grand Total		434,641.73	513,274.12	344,724.20				

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2019	12320	36
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2018	11459	35
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
6	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2019	417.33	32
7	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
8	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
9	RCE OF INDARAM OCP (1.20 MTPA)	SCCL	07/2011	03/2015	03/2018	162.76	36
10	BAROUD OC EXPANSION (RCE) - 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
11	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2017	339.88	35
12	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
13	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
14	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
15	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
16	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
17	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
18	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
19	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2017	209.78	24
20	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
22	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
23	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
24	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	09/2016	153.82	30
25	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
26	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
27	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
28	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2018	198.59	24
29	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2017	181.19	60
30	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
31	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
32	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
33	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
34	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
35	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	08/2019	1458.17	50
36	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	09/2018	1055.05	6
37	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	08/2016	364.75	22
38	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
39	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
40	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
41	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	09/2017	197.79	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
42	AIIMS-RAEBARELI-HOUSING	HSCC	10/2013	11/2013	10/2016	159.5	35
43	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	HSCC	09/2013	12/2015	06/2016	444.7	6

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
45	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	HCL	09/2011	09/2017	04/2020	1856	31

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	PALAKKAD LPG PLANT	BPCL	02/2015	06/2017	12/2017	184	6
47	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	01/2017	150	30
48	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	12/2016	871.35	21
49	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	HPCL	11/2011	03/2013	01/2017	310	46
50	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	IOCL	08/2011	08/2015	12/2016	586	16
51	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
52	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
53	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	08/2016	270	50
54	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	06/2018	352.56	15
55	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	09/2016	993	56
56	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
57	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
58	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	03/2018	3076	6
59	REPLACEMENT OF COKE CHAMBERS	IOCL	04/2013	02/2016	10/2016	480	8
60	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	03/2018	3150	6
61	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	11/2016	3110.36	12
62	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	04/2017	202.25	9
63	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	12/2016	1138.5	20
64	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	03/2017	736.65	66
65	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2016	191.96	19
66	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
67	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	09/2016	317.64	48
68	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
69	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2016	861.79	43
70	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	12/2016	1793	51
71	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	10/2016	463.32	64
72	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	GAIL	06/2009	12/2012	02/2019	2915	74
73	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
74	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	03/2017	2592.17	34
75	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	03/2018	600.17	39
76	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	12/2016	352.49	33
77	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	03/2017	913	19
78	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
80	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2017	2514.88	18
81	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2016	297.33	28
82	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	12/2011	08/2014	03/2017	1746.65	31
83	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
84	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	06/2017	1779.29	103
85	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
86	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	12/2016	1422.85	23
87	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	03/2017	368.72	128
88	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	10/2016	198.63	25
89	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	02/2017	9569.76	20
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	09/2016	752.64	38
91	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	07/2016	250.03	42
92	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	06/2017	1272.8	55
93	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	07/2018	1071.24	10
94	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	03/2017	232.34	57
95	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48
96	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
97	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
98	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	09/2016	2313	57
99	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
100	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	84
101	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2017	477.69	78

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	PGCIL	02/2009	02/2012	06/2016	410.29	52
103	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2017	4824.12	53
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	06/2016	1677.57	38
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	09/2016	509.66	58
106	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2017	4404.57	26
107	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
108	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	08/2016	1216.83	48
109	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2017	2144	54
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV	PGCIL	09/2013	03/2016	09/2016	680.69	6
111	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II	PGCIL	09/2013	05/2016	12/2016	1575.3	7
112	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2016	1364.52	8
113	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	03/2017	374.63	11
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	03/2017	539.82	9
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	03/2017	908.08	9
116	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS	PGCIL	02/2014	12/2015	07/2016	167.4	7
117	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	75
118	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
119	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	03/2022	8112.12	23
120	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
121	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.9	87
122	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	07/2016	558.26	32
123	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	12/2016	1940.13	27
124	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
125	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2017	487.49	33
126	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH	PGCIL	11/2011	07/2014	12/2016	2127.51	29
127	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	12/2016	573.99	40
128	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	09/2016	155.57	6
129	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	11/2016	1961.87	30
130	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	12/2016	196.58	10
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	09/2016	723.63	22
132	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	08/2016	3201.44	22
133	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
134	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	08/2016	524.4	15
135	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
136	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2018	187.26	47
137	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	21
138	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
139	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
140	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
141	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	91
142	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87
143	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
144	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
145	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
146	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	03/2022	603.04	120

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
147	RAJATGARH-BARANG (LD) , ECR	RVNL	04/1999	02/2009	12/2016	166.16	94
148	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
149	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
150	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	12/2017	155.74	106
151	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
152	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
153	UDHNA-JALGAON WITH ELECTRIFICATION (DOUBLING) (WR)	WR	04/2008	03/2014	12/2017	1389.62	45
154	BHUJ-NALIYA (GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
155	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
156	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	221
157	MANDARHILL-DUMKA-RAMPURHAT (NL) , ER	ER	04/1995	12/2011	03/2020	900.05	99
158	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
159	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
160	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	03/2018	733	111
161	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
162	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
163	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
164	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
165	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
166	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	12/2018	2500	193
167	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
168	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
169	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
170	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
171	TAMLUK-BASULYA-SUTAHATA DOUBLING	RVNL	04/2010	06/2013	12/2016	171.02	42
172	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
173	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	MORTH	10/2014	03/2014	09/2016	377.64	30
174	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
175	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	11/2016	1232	15
176	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	PWD	02/2014	07/2014	07/2016	258.99	24
177	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24
178	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	PWD	01/2014	11/2014	11/2016	195.45	24
179	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	PWD	02/2014	11/2014	11/2016	170.21	24
180	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
181	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	PWD	03/2015	09/2015	08/2017	309.01	23
182	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
183	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	PWD	02/2014	06/2014	06/2016	417.61	24
184	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
185	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
186	4 LANING OF GOMTI CHAURAH - UDAIPUR	NHAI	03/2012	10/2015	07/2016	914.5	9
187	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
188	SATANA-BELA SECTION OF NH-75(4L) IN MP	PWD	01/2012	08/2015	09/2016	320.48	13
189	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	08/2016	871.15	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
190	REENGUS SIKAR	NHAI	03/2012	09/2014	07/2016	333.51	22
191	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
192	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	12/2016	2498.76	28
193	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	07/2017	1987	24
194	NASHRI- CHANANI	NHAI	05/2011	06/2015	07/2016	2159	13
195	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	12/2016	1813.76	41
196	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2016	671.3	46
197	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	07/2016	351.54	38
198	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
199	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2017	485	52
200	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2017	536	41
201	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	07/2016	664	29
202	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2016	575	41
203	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	07/2016	511.54	32
204	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2016	1100.7	30
205	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
206	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	NHAI	04/2012	04/2014	12/2016	624	32
207	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	05/2017	1479	23
208	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	12/2016	486	79
209	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	12/2016	1108	61
210	DEOLI-KOTA	NHAI	01/2011	07/2013	12/2016	593	41
211	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	10/2017	828	37
212	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	10/2017	1287.95	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
213	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2017	1348.2	42
214	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2017	617	55
215	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
216	MURADABAD-BAREILY	NHAI	04/2010	06/2013	12/2016	1267	42
217	PUNE-SATARA (NH-4)	NHAI	10/2010	03/2013	12/2016	1724.55	45
218	INDORE-DEWAS (NH-3)	NHAI	11/2010	05/2013	09/2016	325	40
219	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	08/2016	852	41
220	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	08/2016	1585	39
221	4-LANING OF ROHATAK JIND (LENGTH 45 KM)	NHAI	10/2013	10/2015	05/2017	283.25	19
222	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	03/2017	1266.6	6
223	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2016	1509.1	51
224	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	12/2016	1175	44
225	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	07/2012	05/2017	940	58
226	CHENNAI-TADA (SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
227	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	12/2016	1693.75	64
228	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	08/2016	1008.5	38
229	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	NHAI	03/2011	08/2013	06/2016	785.5	34
230	ROHTAK-BAWAL	NHAI	05/2011	11/2013	12/2016	650	37
231	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	07/2016	1141	35
232	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	12/2013	06/2016	535	30
233	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2017	1250	48
234	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	12/2016	953.88	41
235	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
236	SAMAIKHIALI - GANDHIDHAM	NHAI	09/2010	03/2013	07/2016	805.39	40
237	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
238	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	12/2016	1535	31
239	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	07/2016	574	28
240	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
241	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	12/2016	500.29	40
242	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2017	1410	33
243	BEAWAR PALI PINDWARA	NHAI	12/2011	06/2014	07/2016	2388.51	25
244	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
245	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2016	754	45
246	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2016	1078.84	40
247	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	09/2017	998.79	49
248	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
249	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR	NHAI	12/2011	06/2014	03/2017	1047	33
250	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2016	1396.18	27
251	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2016	291.36	32
252	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	12/2017	356.4	41
253	ETAWAH CHAKERI	NHAI	03/2013	09/2015	02/2017	1573	17
254	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	12/2016	2125.24	12
255	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	01/2017	1928.22	21
256	4-LANING OF GOA/KARNATAKA BORDER- KUNDAPUR SECTION	NHAI	05/2014	08/2016	08/2017	1655.01	12
257	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	07/2016	1673.7	57
258	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	12/2016	1055	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
259	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2016	230	138
260	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	08/2016	280	90
261	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2016	199.81	92
262	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	12/2016	167.64	97
263	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	12/2016	155.04	97
264	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	12/2016	200	92
265	2-LANING WITH PS LAMBIA-JAITRAN- RAIPUR	NHAI	01/2014	12/2015	07/2016	158.04	7
266	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION	NHAI	01/2014	01/2016	07/2016	368.15	6
267	2-LANING WITH PS BHILWARA-LODPURA SECTION	NHAI	03/2014	03/2016	09/2016	240.1	6
268	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	08/2016	600	38
269	BIJUNI TO ASSAM /WB.BORDER (NH- 31.C) (NHAI)	NHAI	12/2003	06/2008	07/2016	237.8	97
270	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2017	375.09	35
271	JAIPUR-REENGUS	NHAI	08/2010	02/2013	07/2016	267.81	41
272	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	09/2016	478.51	35
273	PANVEL-INDAPUR	NHAI	12/2011	06/2014	12/2016	942.69	30
274	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
275	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
276	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	06/2016	264.72	96
277	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	12/2016	245	105
278	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	09/2016	217.61	77
279	NALBARI T BIJUNI (AS-7)	NHAI	12/2003	04/2008	12/2016	208	104
280	NALBARI TO BIJUNI (AS-6)	NHAI	12/2003	06/2008	07/2016	225	97
281	BIJUNI TO ASSAM WB BORDER (NH- 31.C) (1) (NHAI)	NHAI	12/2003	06/2008	06/2016	195	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
282	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	06/2016	155	93
283	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
284	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	09/2016	348.16	108
285	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	07/2016	160	98
286	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	07/2016	175.96	99
287	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	09/2008	07/2016	332.94	94
288	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	03/2017	212	114
289	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2016	196	89
290	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C)	PWD	07/2015	12/2015	12/2016	333.21	12
291	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	12/2016	333.21	12
292	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	10/2016	495.78	9
293	2-LANING WITH PS SITARGANJ BAREILY SECTION	NHAI	06/2014	01/2016	12/2016	301.04	11
294	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	NHAI	09/2015	09/2016	09/2017	368.73	12
295	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	10/2016	351.34	9
296	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	03/2017	523.85	14

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
297	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	88
298	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96
299	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	07/2016	150	124

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
300	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	08/2016	187.33	34

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
301	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	11/2016	877.73	16
302	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2017	15525	31
303	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	12/2016	245.67	7
304	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	07/2017	175.49	7
305	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2017	956	24
306	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	12/2016	17265	45
307	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	SAIL	04/2014	04/2015	12/2016	188.93	20
308	3RD CONVERTER AND 4TH CASTER	RINL	07/2011	07/2016	03/2017	974.76	8
309	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	09/2017	404.16	26
310	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	03/2017	149.73	15
311	TURBO BLOWER - 5	RINL	12/2009	09/2016	03/2017	280	6
312	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343	8

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
313	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	ITI	09/2014	09/2014	03/2017	2111.17	30

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
314	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
315	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2017	171.86	18
316	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	04/2017	156.57	19
317	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	03/2017	350.02	24
318	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2017	216.69	31
319	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	11/2016	6395	65
320	BANGALORE METRO RAIL PROJECT PHASE-2	BM RCL	02/2014	02/2019	03/2020	26405.14	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
321	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	03/2017	188.87	27
322	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	03/2017	270.83	28
323	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	11/2014	12/2017	241.33	37
324	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	12/2016	405.01	24
325	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	CPWD	12/2012	06/2015	11/2016	315	17
326	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	06/2016	261.85	37
327	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	03/2017	205	60
328	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
8	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
9	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
12	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
14	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
17	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
19	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	17435.15	11149.82
20	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
21	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
22	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	2336.74	1275.36
23	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
24	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1581.04	1007.05
25	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
26	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
27	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
28	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9606.82	5484.82
29	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
30	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
31	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	250.03	390.51	140.48
32	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
33	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.57	586.56
34	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1441.52	1072.8
35	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
37	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5783.17	2141.13
38	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	1961.87	2310.58	348.71
40	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
42	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
43	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
44	KARUR-SALEM (NL) ,SR	SR	02/1997	N.A.	155.55	870	714.45
45	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
46	GULBARGA-BIDAR,SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
47	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
48	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18
49	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
50	GADWAL - RAICHUR (NL) , SCR	SCR	04/1998	02/2011	92.63	270	177.37
51	DEOGHAR - SULTANGANJ (INL) , ER	ER	04/2000	12/2012	607.09	1500	892.91
52	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
53	JIND-SONEPAT (NL) ,NR	NR	01/2004	03/2012	238.56	740	501.44
54	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
55	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
56	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	280	183.84
57	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	365	266.26
58	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
59	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
60	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2491.43	1992.13

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
62	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
63	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
64	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
65	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
66	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	554.7	241.46
67	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1170	709.06
68	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
69	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
70	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52
71	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
72	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
73	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
74	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2513.3	1663.3
75	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	837.73	537.73
76	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
77	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
78	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	624.47	3142.46	2517.99
79	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	9046.72	8319.16
80	KHURDA ROAD-BOLANGIR (NL) ECR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
81	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
82	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT		04/1990	03/2019	153.82	551.82	398

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
84	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
85	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272	642
86	BARAMATI - LONAND (54 KM)	CR	02/1998	N.A.	75	736	661
87	GULBARGA-BIDAR	SCR	04/1994	N.A.	844.15	1542.42	698.27
88	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	2103	1187.02
89	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
90	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
91	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	386.68	140.61
92	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
93	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
94	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	412.53	246.71
95	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
96	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	599.9	357.68
97	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
98	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
99	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
100	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
101	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
102	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	440.05	230.28
103	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	972.52	720.52
104	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1451	556
105	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	467.91	246.49

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1480.83	658.44
107	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
108	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
109	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
110	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
111	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
112	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
113	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
114	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
115	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
116	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
117	DIGHA-JALESWAR INCLUDING MM FOR DIGHA- EGRA	SER	04/2010	N.A.	553.63	1009	455.37
118	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
119	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
120	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
121	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	NWR	04/2013	N.A.	456	860	404
122	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
123	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
124	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	1037.15	591.15
125	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	845.68	405.8
126	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79
127	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
128	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
130	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
131	MUNEERABAD-MAHABOONAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	525	306.76
132	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	966.98	811.24
133	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	370	203.84
134	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
135	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	2434	2109
136	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	847.75	222.45
137	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	19565	17065
138	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
139	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
140	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	455.96	265.86
141	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
142	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
143	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
144	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
145	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
146	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	SWR	02/1997	N.A.	295	1289.92	994.92
147	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	N.A.	836.26	1072.51	236.25
148	HUBLI-ANKOLA (NL) , SWR	SWR	04/1997	N.A.	227	2135	1908
149	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
150	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
151	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	NANGALDAM-TALWARA (NL) ,NR	NR	03/1981	07/2012	450	2100	1650
153	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	516.23	735	218.77
154	DAUSA-GANGAPUR CITY (NL) ,NWR	NWR	02/1997	N.A.	410.08	560	149.92
155	KANPUR KASGANJ MATHURA (GC) NER	NER	03/1997	N.A.	677.97	1651.54	973.57
156	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4085	2745.52
157	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
158	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
159	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
160	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
161	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
162	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) ,ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
163	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	5050	4802.34
164	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
165	MANDARHILL-DUMKA-RAMPURHAT (NL) ,ER	ER	04/1995	12/2011	900.05	1125.89	225.84
166	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
167	AHMEDNAGAR-PARLI VAJUNATH (NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
168	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
169	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
170	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	2966.99	1920.11
171	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
172	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
173	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
174	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
176	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
177	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
178	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
179	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
180	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
181	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	360	223.38
182	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	340	206.59
183	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
184	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
185	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
186	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
187	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
188	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
189	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
190	RAMGANJMUNDI-BHOPAL (NL) ,WCR	WCR	04/2001	N.A.	470.92	3000	2529.08
191	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	921	2363	1442
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
192	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
193	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
194	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
195	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
196	CONSTRUCTION OF GODAVARI RIVER BRIDGE	PWD	03/2011	12/2015	218.31	339.82	121.51

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S						
197	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
198	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
199	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
200	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
201	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
202	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1070.97	302.09
203	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
204	BANGALORE METRO RAIL PROJECT	MRTP	05/2006	06/2011	6395	14405.01	8010.01
205	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	11/2014	241.33	356.59	115.26
206	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	5298	1034

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	12/2016	871.35	1200.00	328.65	21
5	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	462.79	152.98	29
6	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36
7	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	09/2016	993.00	1693.00	700	56
9	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2016	861.79	1256.72	394.93	43

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	03/2017	368.72	1441.52	1072.8	128
11	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	06/2017	1779.29	2187.32	408.03	103
12	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2017	1746.65	2228.71	482.06	31

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2017	487.49	639.46	151.97	33
14	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	3846.30	867.82	75
15	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
16	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	07/2016	250.03	390.51	140.48	42
17	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	06/2017	1272.80	1731.10	458.3	55
18	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	09/2016	2313.00	4237.67	1924.67	57
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.90	6179.96	3683.06	87
20	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
21	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	12/2016	573.99	1581.04	1007.05	40
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	4479.16	111
23	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	2336.74	1275.36	84
24	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2017	477.69	738.48	260.79	78
25	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
26	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2017	2144.00	2932.88	788.88	54
27	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	11/2016	1961.87	2310.58	348.71	30
28	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5783.17	2141.13	10
29	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
30	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
31	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
32	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
33	RAJATGARH-BARANG (LD) , ECR	RVNL	04/1999	02/2009	12/2016	166.16	370.00	203.84	94
34	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
35	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
36	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	340.00	206.59	91
38	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
39	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	2820.25	2200.91	71
40	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	03/2022	603.04	1421.25	818.21	120
41	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	554.70	241.46	221
42	MANDARHILL-DUMKA-RAMPURHAT (NL) , ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
43	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
44	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	5050.00	4802.34	178
45	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
46	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	9046.72	8319.16	96
47	NEW LINE FROM DIMAPUR TO	NFR	04/2006	03/2015	03/2020	850.00	2513.30	1663.3	60

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)								
48	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
49	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
50	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4085.00	2745.52	51
51	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	2434.00	2109	84
52	NANDYAL-YERRAGUNTALA (NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	811.24	106
53	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174
54	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
55	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2016	196.00	331.23	135.23	89
56	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2016	199.81	385.13	185.32	92
57	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	12/2016	1055.00	1601.77	546.77	13
58	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	12/2016	1108.00	2288.00	1180	61
59	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	12/2016	155.04	280.13	125.09	97

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
60	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	409.83	164.16	88
61	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
62	ENMORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	07/2016	150.00	600.00	450	124

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
63	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343.00	488.40	145.4	8

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	11/2014	12/2017	241.33	356.59	115.26	37
65	BANGALORE METRO RAIL PROJECT	MRTD	05/2006	06/2011	11/2016	6395.00	1,4405.01	8010.01	65

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure- XVIII

Details of Ongoing Projects Under -Public Private Partnership Mode

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
1	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - PPP (ANNUITY) - [N10000009]	12/2015	344.50	344.50	11/2016	11/2016	0.00	0
	Total		344.50	344.50				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
2	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - PPP (BOT) - [N24000231]	10/2013	283.25	283.25	10/2015	05/2017	0.00	19
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36	291.36	01/2014	09/2016	0.00	32
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00	325.00	05/2013	09/2016	0.00	40
5	REENGUS SIKAR - PPP (ANNUITY) - [N24000227]	03/2012	333.51	333.51	09/2014	07/2016	0.00	22
6	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54	351.54	05/2013	07/2016	0.00	38
7	CHENNAI-TADA(SIX LANE) - PPP (BOT) - [N24000129]	04/2009	353.37	353.37	10/2011	-	0.00	56
8	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - PPP (BOT) - [N24000211]	07/2012	356.40	356.40	07/2014	12/2017	0.00	41
9	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - PPP (BOT) - [N24000153]	03/2011	359.00	359.00	09/2013	12/2016	0.00	39
10	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00	374.00	05/2013	12/2017	0.00	55
11	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00	485.00	08/2013	12/2017	0.00	52
12	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00	486.00	05/2010	12/2016	0.00	79
13	BHUBANESWAR TO PURI - PPP (BOT) - [N24000195]	03/2011	500.29	500.29	08/2013	12/2016	0.00	40
14	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54	511.54	11/2013	07/2016	0.00	32
15	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00	516.00	07/2008	-	0.00	0
16	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07	530.07	08/2016	08/2016	0.00	0

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - PPP (BOT) - [N24000171]	06/2011	535.00 -	535.00	12/2013 -	06/2016	0.00	30
18	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	06/2017	0.00	41
19	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00 -	567.00	11/2013 -	-	0.00	0
20	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2017	0.00	50
21	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	07/2016	0.00	28
22	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	12/2016	0.00	41
23	4-LANING OF RAIGANJ-DALKOLA - PPP (BOT) - [N24000204]	02/2011	580.43 -	580.43	08/2013 -	05/2017	0.00	45
24	NIROLI-ROXY-RAJAMUNDA - PPP (BOT) - [N24000194]	07/2011	586.00 -	586.00	01/2014 -	12/2016	0.00	35
25	DEOLI-KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	12/2016	0.00	41
26	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	0.00	0
27	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	03/2017	0.00	55
28	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	12/2016	0.00	32
29	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	06/2019	0.00	0
30	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	12/2016	0.00	37
31	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00 -	664.00	02/2014 -	07/2016	0.00	29
32	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	12/2016	0.00	46
33	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - PPP (BOT) - [N24000236]	10/2013	677.79 -	677.79	04/2016 -	08/2016	0.00	4
34	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	02/2017	0.00	31
35	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - PPP (BOT) - [N24000588]	06/2016	725.95 -	725.95	06/2019 -	06/2019	0.00	0
36	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2016	0.00	45
37	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	06/2019	0.00	0
38	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - PPP (BOT) - [N24000168]	03/2011	785.50 -	785.50	08/2013 -	06/2016	0.00	34

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	SAMAIKHIALI - GANDHIDHAM - PPP (BOT) - [N24000179]	09/2010	805.39	805.39	03/2013	07/2016	0.00	40
40	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	04/2018	0.00	0
41	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - PPP (BOT) - [N24000225]	03/2012	828.00	828.00	09/2014	10/2017	0.00	37
42	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36	830.36	07/2018	07/2018	0.00	0
43	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - PPP (BOT) - [N24000144]	09/2010	852.00	852.00	03/2013	08/2016	0.00	41
44	BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229]	08/2012	867.00	867.00	02/2015	12/2017	0.00	34
45	4 LANING OF OBEDULLAGANJ-BETUL SECTION - PPP (BOT) - [N24000457]	02/2012	912.00	912.00	08/2016	08/2016	0.00	0
46	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	12/2016	0.00	1
47	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - PPP (BOT) - [N24000123]	03/2005	940.00	940.00	07/2012	05/2017	0.00	58
48	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	12/2016	0.00	41
49	4-LANING OF ROHTAK - HISSAR SECTION - PPP (BOT) - [N24000456]	03/2013	959.25	959.25	06/2016	07/2016	0.00	1
50	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	07/2017	0.00	0
51	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	09/2017	0.00	49
52	4 LANNING OF AHMEDABAD TO GODHARA - PPP (BOT) - [N24000167]	12/2010	1,008.50	1,008.50	06/2013	08/2016	0.00	38
53	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00	1,046.00	09/2013	12/2016	0.00	39
54	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	03/2017	0.00	33
55	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	12/2016	51.83	13
56	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	12/2016	0.00	40
57	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	12/2016	0.00	30
58	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	12/2016	106.50	61
59	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	07/2016	0.00	35
60	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,206.10	04/2013	12/2016	2.65	44

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
61	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2017	0.00	48
62	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,266.60	09/2016 -	03/2017	0.00	6
63	MURADABAD-BAREILY - PPP (BOT) - [N24000154]	04/2010	1,267.00 -	1,267.00	06/2013 -	12/2016	0.00	42
64	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - PPP (BOT) - [N24000228]	06/2013	1,287.95 -	1,287.95	11/2015 -	10/2017	0.00	23
65	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	08/2017	0.00	42
66	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	01/1991	1,388.00 -	1,388.00	- -	08/2018	0.00	0
67	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00 -	1,393.00	- -	01/2018	0.00	0
68	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	12/2016	0.00	27
69	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	06/2017	0.00	33
70	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	05/2017	0.00	23
71	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	12/2016	0.00	51
72	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	12/2016	0.00	31
73	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	02/2017	0.00	17
74	FOUR LANING OF BIAORA-DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79 -	1,583.79	- -	-	0.00	0
75	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00 -	1,585.00	05/2013 -	08/2016	0.00	39
76	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - PPP (BOT) - [N24000139]	09/2010	1,655.00 -	1,655.00	09/2013 -	-	0.00	0
77	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	08/2017	0.00	12
78	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	- -	-	0.00	0
79	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	- -	09/2016	0.00	0
80	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	07/2016	0.00	57
81	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	12/2016	0.00	64

(June 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
82	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	12/2016	0.00	45
83	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	12/2016	0.00	41
84	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	01/2018	0.00	0
85	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	11/2016	0.00	0
86	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	01/2017	0.00	21
87	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	07/2017	0.00	24
88	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	12/2016	0.00	12
89	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	-	-	0.00	0
90	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,159.00	06/2015	07/2016	0.00	13
91	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	-	-	0.00	0
92	BEAWAR PALI PINDWARA - PPP (BOT) - [N24000199]	12/2011	2,388.51	2,388.00	06/2014	07/2016	-0.02	25
93	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	12/2016	0.00	28
94	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00	2,848.00	03/2014	04/2017	0.00	37
	Total		100,424.57	102,181.93				
	SHIPPING AND PORTS							
95	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94	235.15	06/2017	06/2017	18.20	0
96	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	258.33	12/2017	12/2017	5.66	0
97	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39	669.46	12/2010	12/2018	82.72	96
	Total		809.83	1,162.94				
	Grand Total		101,578.90	103,689.37				
