

404th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
Jun, 2019



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for June 2019 contains information on the status of the 1608 Central Sector Infrastructure Projects costing ₹150 crore and above. During June 2019, 39 projects (Railways sector) have reported completion.
2. During the reference month, out of 1608 projects, 550 projects are delayed with respect to their original schedules and 119 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 119 projects, 51 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	831	227	31	7
2	RAILWAYS	320	138	56	33
3	PETROLEUM	150	44	7	2
4	COAL	102	30	2	1
5	POWER	75	52	15	6
6	URBAN DEVELOPMENT	62	26	3	1
7	HEALTH AND FAMILY WELFARE	20	12	0	0
8	STEEL	14	9	3	1
9	SHIPPING AND PORTS	8	1	0	0
10	FERTILISERS	5	1	1	0
11	MINES	5	0	0	0
12	TELECOMMUNICATIONS	5	3	1	0
13	ATOMIC ENERGY	4	4	0	0
14	HEAVY INDUSTRY	2	1	0	0
15	WATER RESOURCES	2	1	0	0
16	DEFENCE PRODUCTION	2	0	0	0
17	CIVIL AVIATION	1	1	0	0
Total		1608	550	119	51

3. Total original cost of implementation of the 1608 projects was ₹19,17,796.07 crore and their anticipated completion cost is likely to be ₹23,05,860.33 crore, which reflects overall cost overruns of ₹3,88,064.26 crore (20.23% of original cost). The expenditure incurred on these projects till June 2019 is ₹9,35,021.39 crore, which is 40.55% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-07-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
	COAL				
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	19.86
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	24.10
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.06
	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3727.30	116.96
	PETROLEUM				
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	95.30
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	345.92	70.45
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
2	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	5024.35	203.22
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7419.34	197.14
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	155.05
5	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
	RAILWAYS				
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
2	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	1800.00	1391.30
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
4	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
5	ATTIPPATTU PUTTUR	04/2008	151.84	1105.00	627.74
	ROAD TRANSPORT AND HIGHWAYS				
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	880.06
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1	05/2009	1108.00	2288.00	106.50

	KM)				
3	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	195.04	377.99	93.80
4	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
5	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	03/2012	207.03	389.45	88.11
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	12.88
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	49.05
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	3.58
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	219.60	2.00
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58
4	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	488.28	25.85

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-07-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
COAL					
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	1173.30
2	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06

3	BHANEGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	99.78
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.09
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3727.30	2009.30
PETROLEUM					
1	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
2	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
3	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
4	MUMBAI REFINERY EXPANSION PROJECT	09/2015	4199.00	5060.00	861.00
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	821.27
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	6077.52
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7419.34	4922.44
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	9996.59	4643.59
RAILWAYS					
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	13809.00	9354.83
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
ROAD TRANSPORT AND HIGHWAYS					
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	6786.82
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
3	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
4	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
5	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	03/2017	993.16	1434.00	440.84
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	31.48
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	7615.00
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	8.30
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	219.60	4.30
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5687.79	506.00

3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
4	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1608 projects, 390 are on schedule, 550 are delayed, 360 projects reported cost overrun and 185 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 474 if delay is calculated on the basis of latest schedule of completion. Further, for 644 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 550 delayed projects, 182 (33.09%) projects have overall delay in the range of 1 to 12 months, 119 (21.64%) projects have delay in the range of 13 to 24 months, 133 (24.18%) projects have delay in the range of 25 to 60 months and 116 (21.09%) projects have delay of 61 months and above. **The average time overrun in these 550 delayed projects is 39.24 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-07 -2019)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
COAL					
1	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2022	144
2	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
4	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2020	120
5	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2021	120
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	08/2019	33
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	10/2020	83
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	09/2019	28
3	AIIMS - OPD(NEW)	08/2014	05/2017	08/2019	27
4	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	09/2019	19
5	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	09/2019	16

	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	03/2020	102
	PETROLEUM				
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
2	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	12/2019	81
3	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2019	79
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
5	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014	08/2019	58
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	08/2019	129
3	BARH STPP(3X660MW) NTPC	02/2005	10/2011	08/2021	118
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	08/2019	116
5	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2022	114
	RAILWAYS				
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
2	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
3	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2021	252
4	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2021	229
	ROAD TRANSPORT AND HIGHWAYS				
1	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2019	140
2	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	09/2019	138
3	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	10/2019	136
4	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	06/2019	133
5	GWALIOR-JHANSI, NH-75	12/2003	12/2009	08/2020	128
	SHIPPING AND PORTS				
1	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	12/2017	05/2020	29
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2020	62
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	03/2021	53
3	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
4	COKE OVEN BATTERY-5	12/2011	12/2017	09/2019	21
5	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	06/2019	18
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
2	MADHYA PRADESH ACCESS (LOT1)	08/2017	05/2018	07/2019	14
3	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	09/2019	11
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2020	89
2	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	06/2019	87
3	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
4	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70
5	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2020	67

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-07-2019)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	09/2019
3	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	18.45	03/2022	03/2022
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	6531.52	11/2021	11/2021
5	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	319.81	03/2020	03/2020
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	147.00	11/2013	10/2020
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	184.93	06/2020	08/2020
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	244.66	04/2020	06/2020
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	241.39	09/2018	06/2019
HEAVY INDUSTRY							
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER	08/2016	1554.00	1554.00	335.03	09/2019	09/2019

	PLANTS IN INDIA						
	PETROLEUM						
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.57	02/2017	10/2021
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
5	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	07/2014	247.00	247.00	0.00	03/2021	03/2021
	POWER						
1	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10868.18	09/2010	N.A.
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3268.00	10/2017	N.A.
4	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	210.72	04/2016	12/2019
5	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1135.82	04/2020	12/2023
	RAILWAYS						
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	03/2025
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2010.00	644.09	07/2012	03/2024
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	271.06	03/2019	03/2020
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	575.65	148.40	03/2006	03/2025
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	559.91	541.07	07/2014	N.A.
	ROAD TRANSPORT AND HIGHWAYS						
1	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	110.39	N.A.	10/2020
2	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	319.68	0.00	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	219.40	219.40	0.00	01/2018	N.A.

	"MADHUGIRI-MULB						
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	282.41	67.52	08/2016	N.A.
	SHIPPING AND PORTS						
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	411.12	12/2010	N.A.
4	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	600.00	257.90	1.45	12/2017	05/2020
5	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	05/2016	970.00	970.00	109.97	05/2020	05/2020
	STEEL						
1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	4749.00	4749.00	110.95	09/2017	N.A.
	TELECOMMUNICATIONS						
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.03	06/2017	N.A.
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	219.60	33.46	05/2018	07/2019
4	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	117.63	10/2018	09/2019
	URBAN DEVELOPMENT						
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.

WATER RESOURCES							
1	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	233.57	233.57	32.20	12/2019	12/2019

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-07-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5784.74
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	13711.00
COAL					
1	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.10	0.00	493.85
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	346.99
3	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	539.59
4	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	241.15
5	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	0.00	203.90
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	508.29
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	0.00	1265.01
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7399.82
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10868.18
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	2187.32	2237.45
4	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	0.00	2935.92
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	7816.71
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	644.09
2	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	541.07
3	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF.	04/1991	329.39	0.00	815.41
4	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	669.21
5	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	927.86

ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	472.00
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	319.96
3	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	12/2003	160.00	0.00	223.68
4	BRAHMPUTRA BRIDGE, NH NO-31	12/2003	217.61	0.00	451.15
5	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	326.35
SHIPPING AND PORTS					
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	411.12
2	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.00	275.58
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	0.00	15729.80
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.77
4	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	5188.00
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	0.00	418.79
WATER RESOURCES					
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	0.00	16417.99

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-07-2019)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	03/2016	N.A.	N.A.
3	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
4	RKP OCP PHASE-I	03/2010	03/2015	N.A.	03/2019
5	MADHUBAND NLW WASHERY	08/2010	05/2014	N.A.	04/2018
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 4	12/2016	05/2018	03/2019	N.A.
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	PARADIP-RAIPUR- RANCHI PIPELINE	08/2009	12/2016	N.A.	N.A.
3	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.

4	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
5	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	03/2015	N.A.	N.A.
POWER					
1	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
4	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
5	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
RAILWAYS					
1	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
2	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	N.A.
3	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	02/2009	N.A.	N.A.
4	ETAWAH-MAINPURI (NL),NCR	04/1997	12/2008	03/2015	03/2015
5	MACHERLA-NALGONDA(NL)(SCR)	07/1998	N.A.	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	N.A.	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	N.A.	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	N.A.	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	N.A.	N.A.
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	12/2017	N.A.	N.A.
STEEL					
1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	09/2017	N.A.	N.A.
2	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	04/2015	N.A.	N.A.
3	INSTALLATION OF NEW HOT STRIP MILL AT RSP	04/2015	04/2018	05/2019	05/2019
TELECOMMUNICATIONS					

1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	03/2018	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 30.06.2019 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	831	31
2	RAILWAYS	320	56
3	PETROLEUM	150	7
4	COAL	102	2
5	POWER	75	15
6	URBAN DEVELOPMENT	62	3
7	HEALTH AND FAMILY WELFARE	20	0
8	STEEL	14	3
9	SHIPPING AND PORTS	8	0
10	FERTILISERS	5	1
11	MINES	5	0
12	TELECOMMUNICATIONS	5	1
13	ATOMIC ENERGY	4	0
14	HEAVY INDUSTRY	2	0
15	WATER RESOURCES	2	0
16	DEFENCE PRODUCTION	2	0
17	CIVIL AVIATION	1	0
	Total	1608	119

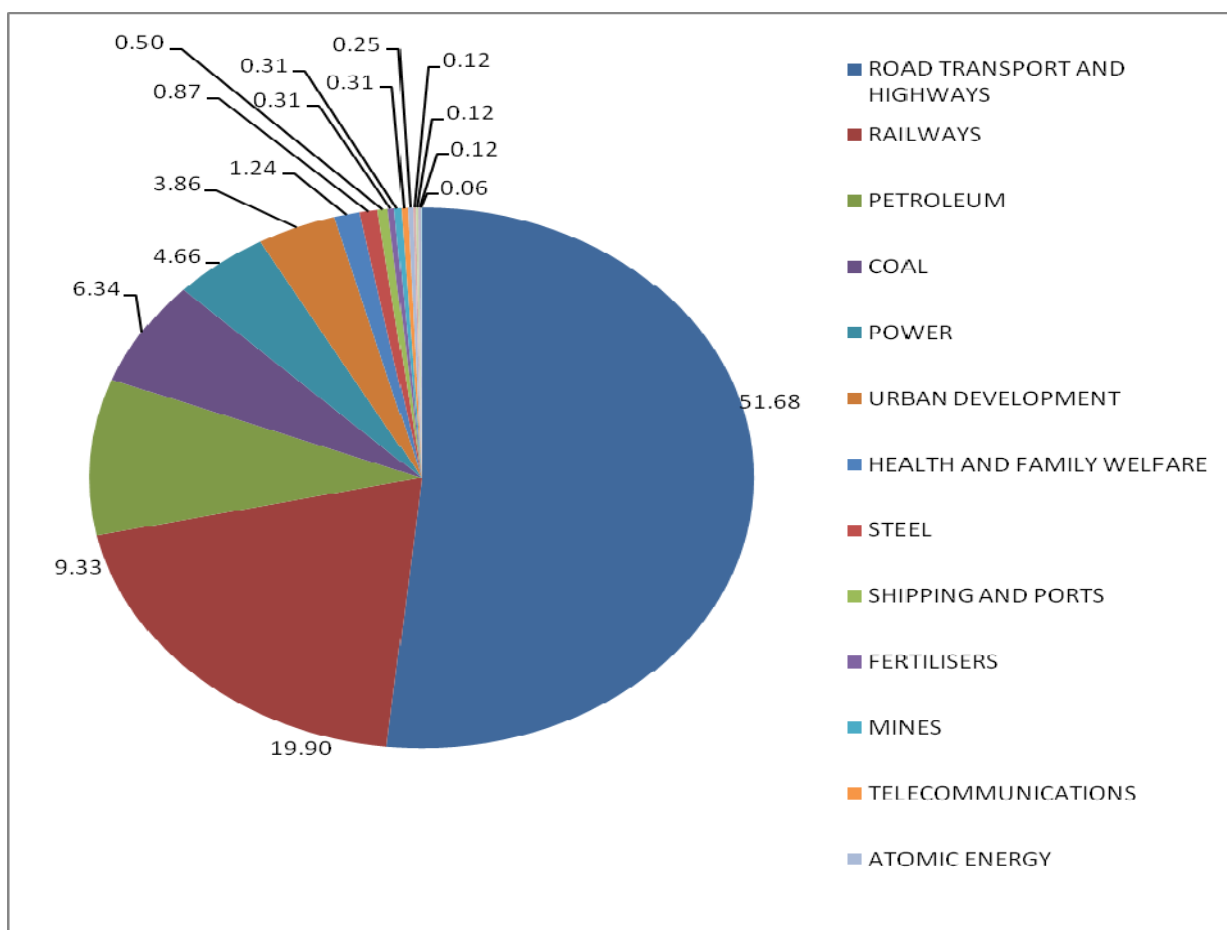


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2019			
	<u>COAL</u>			
1	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI (NORTHERN COAL FIELDS LIMITED) - [N06000033]	259.40	03/2012	266.38
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) (NORTHERN COAL FIELDS LIMITED) - [N06000091]	1,131.28	03/2018	796.85
	<u>PETROLEUM</u>			
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000175]	3,076.00	09/2017	3,450.30
	<u>POWER</u>			
4	BONGAIGAON THERMAL POWER PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000041]	4,375.35	10/2011	7,000.00
5	TRIPURA GAS BASED POWER PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000071]	421.01	07/2013	963.23
	<u>RAILWAYS</u>			
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) RAILWAY) - [N22000113]	653.19	03/2014	862.17
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000357]	567.51	03/2018	421.60
	May,2019			
	<u>COAL</u>			
8	MAKARDHOKRA I OC (WESTERN COAL FIELDS LIMITED) - [N06000119]	266.23	03/2021	144.38
	<u>PETROLEUM</u>			
9	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000084]	736.65	09/2011	331.47
10	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000290]	474.15	05/2019	348.64
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	WESTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000035]	477.69	09/2010	691.96
12	KUDGI STPP STAGE 1 (NATIONAL THERMAL POWER CORPORATION) - [N18000131]	15,166.19	01/2017	15,364.00
13	SOLAPUR STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000133]	9,395.18	01/2017	8,617.00
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000158]	539.82	06/2016	434.33
15	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000174]	3,363.12	12/2016	2,244.00
16	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000222]	790.13	06/2019	575.24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000145]	1,585.00	05/2013	2,023.33
18	JORBAT - BARAPANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000180]	536.00	01/2014	845.41
19	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S EPC(PUBLIC WORKS DEPT OF STATE) - [N24000241]	177.18	03/2016	40.51
20	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000242]	158.65	03/2016	103.50
21	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW EPC(PUBLIC WORKS DEPT OF STATE) - [N24000243]	244.08	03/2016	38.32
22	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000244]	340.00	03/2016	2.00
23	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000246]	244.30	12/2016	2.00
24	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S (PUBLIC WORKS DEPT OF STATE) - [N24000249]	218.31	12/2015	208.28
25	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000250]	260.39	11/2016	188.00
26	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000255]	220.72	11/2016	155.30
27	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000261]	267.16	11/2017	308.33
28	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A EPC(DEPT OF ROAD TRANSPORT & HIGHWAYS) - [N24000262]	201.12	02/2015	150.19
29	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) (PUBLIC WORKS DEPT OF STATE) - [N24000263]	241.61	02/2017	178.94

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
30	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN EPC(PUBLIC WORKS DEPT OF STATE) - [N24000265]	297.78	02/2017	284.89
31	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC (PUBLIC WORKS DEPT OF STATE) - [N24000266]	361.30	07/2014	203.29
32	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) EPC(PUBLIC WORKS DEPT OF STATE) - [N24000267]	258.99	07/2014	200.44
33	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC EPC(PUBLIC WORKS DEPT OF STATE) - [N24000268]	251.55	02/2015	172.65
34	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000269]	175.03	-	152.53
35	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP EPC(PUBLIC WORKS DEPT OF STATE) - [N24000272]	266.00	-	182.13
36	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000273]	314.43	-	216.96
37	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000277]	185.82	-	142.23
38	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000278]	213.47	03/2015	182.91
39	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV EPC(PUBLIC WORKS DEPT OF STATE) - [N24000279]	298.34	03/2015	269.93
40	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I EPC(PUBLIC WORKS DEPT OF STATE) - [N24000280]	262.54	03/2015	215.11
41	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000283]	169.26	12/2012	280.72
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000284]	170.21	11/2014	140.09
43	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000286]	394.20	-	332.62
44	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000288]	422.34	-	406.40
45	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE EPC(PUBLIC WORKS DEPT OF STATE) - [N24000289]	435.90	-	380.41
46	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000290]	279.68	-	286.96
47	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000291]	463.65	-	536.84

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
48	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000292]	573.96	-	557.08
49	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000293]	480.21	-	372.37
50	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000299]	224.83	05/2015	189.85
51	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU EPC(PUBLIC WORKS DEPT OF STATE) - [N24000300]	309.01	09/2015	391.89
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION EPC(PUBLIC WORKS DEPT OF STATE) - [N24000303]	417.61	06/2014	261.29
53	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000310]	377.83	07/2017	318.66
54	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000329]	497.89	04/2017	735.92
55	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000330]	629.74	-	721.04
56	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000336]	227.74	10/2016	187.85
57	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000369]	269.26	10/2016	212.72
58	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI EPC(PUBLIC WORKS DEPT OF STATE) - [N24000370]	483.38	-	470.16
59	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000372]	616.36	-	554.68
60	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000374]	486.74	-	415.58
61	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000377]	397.04	10/2016	368.49
62	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000381]	257.80	02/2016	59.30
63	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000383]	312.79	-	258.86
64	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K EPC(PUBLIC WORKS DEPT OF STATE) - [N24000384]	319.80	-	289.40
65	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000387]	264.16	-	533.18

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
66	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000390]	1,494.48	02/2011	2,158.50
67	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000393]	774.57	03/2018	613.58
68	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000394]	532.49	05/2017	386.02
69	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000399]	317.76	03/2017	344.30
70	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000403]	283.45	10/2016	285.18
71	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000404]	578.38	-	481.30
72	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA EPC(PUBLIC WORKS DEPT OF STATE) - [N24000405]	789.83	-	608.55
73	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000406]	208.87	05/2016	206.78
74	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000409]	176.22	02/2018	0.10
75	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000410]	641.02	12/2017	449.66
76	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000416]	224.83	04/2015	189.85
77	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000418]	493.94	03/2017	503.25
78	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000419]	165.00	09/2010	174.57
79	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000420]	104.00	09/2010	218.29
80	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000421]	235.08	05/2018	235.08
81	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000447]	670.82	02/2015	590.00
82	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000474]	327.32	05/2017	301.41
83	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000476]	273.06	-	199.72

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
84	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000512]	207.88	-	179.58
85	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000526]	899.21	-	748.74
86	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000529]	207.88	-	179.58
87	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000536]	377.64	03/2014	755.28
88	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO (PUBLIC WORKS DEPT OF STATE) - [N24000538]	292.98	11/2014	160.96
89	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000561]	244.00	07/2018	231.90
90	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000573]	322.01	08/2014	267.00
91	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY - KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000615]	334.22	06/2016	334.22
92	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000647]	162.51	05/2016	136.31
93	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 (PUBLIC WORKS DEPT OF STATE) - [N24000856]	170.00	02/2015	115.57
94	REHABILITATION AND UPGRADATION OF PURANPUR - KHUTAR SECTION FROM KM 38.00 TO KM 82.00 OF NH-730 TO 2 (PUBLIC WORKS DEPT OF STATE) - [N24001142]	225.96	06/2018	174.63
	June,2019			
	<u>RAILWAYS</u>			
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) (NORTH CENTRAL RAILWAY) - [220100007]	158.77	03/1994	682.34
96	AMRAVATI-NARKHER NL(CR) (CENTRAL RAILWAYS) - [220100118]	663.01	06/1999	726.33
97	CALICUT-MANGALORE (DL) (SR) (SOUTHERN RAILWAY) - [220100151]	240.00	-	0.01
98	MANDARHILL-DUMKA-RAMPURHAT (NL),ER (EASTERN RAILWAYS) - [220100168]	1,125.89	03/2016	1,180.08
99	KARUR-SALEM(NL),SR (SOUTHERN RAILWAY) - [220100191]	155.55	-	863.54
100	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR (NORTH CENTRAL RAILWAY) - [220100243]	108.00	12/2009	455.39
101	KATI HAR - JOGBANI (GC)(NEFR) (NORTH EAST FRONTIER RAILWAY) - [220100247]	792.46	12/2010	944.80

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
102	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) (NORTH EASTERN RAILWAY) - [220100256]	744.71	-	917.49
103	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) (SOUTHERN RAILWAY) - [220100263]	280.00	-	942.28
104	JIND-SONEPAT (NL),NR (NORTHERN RAILWAY) - [220100280]	238.56	03/2012	785.75
105	KODERMA GIRIDH (NL), ECR (EAST CENTRAL RAILWAYS) - [220100306]	768.87	-	988.38
106	MAHARAJGANJ-MASRAKH (NL) - NER (NORTH EASTERN RAILWAY) - [220100316]	218.19	06/2018	380.50
107	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000049]	732.81	03/2008	2,191.46
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE (SOUTHERN RAILWAY) - [N22000080]	343.17	-	1,110.44
109	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) (NORTHERN RAILWAY) - [N22000088]	369.90	03/2010	891.24
110	AGARTALA SABROOM, NL, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000099]	1,142.00	03/2014	3,354.18
111	DAKSHIN-BARASAL-LAKSHMIKANTAPUR (EASTERN RAILWAYS) - [N22000116]	259.51	02/2012	148.37
112	GHUTIASHARIF-CANNING (ER) (EASTERN RAILWAYS) - [N22000117]	193.08	12/2011	154.30
113	PANDABESWAR-CHINPAI DOUBLING (ER) (EASTERN RAILWAYS) - [N22000118]	293.74	12/2010	128.78
114	BHOJIPUR TANAKPUR VIA PILIBHIT (NORTH EASTERN RAILWAY) - [N22000132]	195.64	-	450.62
115	AUNRIHAR MANDUADIH (NORTH EASTERN RAILWAY) - [N22000133]	199.75	08/2018	287.33
116	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000164]	309.44	12/2015	529.27
117	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC (SOUTHERN RAILWAY) - [N22000188]	271.24	-	468.58
118	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA (NORTH EAST FRONTIER RAILWAY) - [N22000194]	895.00	03/2007	1,566.57
119	CHENGANNUR-CHINGAVANAM (SOUTHERN RAILWAY) - [N22000203]	191.72	-	447.03
120	LUMDING-HOJAI PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000211]	246.07	03/2019	490.29
121	MEERUT-MUZAFARNAGAR PATCH DL (NORTHERN RAILWAY) - [N22000267]	377.44	-	430.12
122	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER- CHANDIGARH (NORTHERN RAILWAY) - [N22000290]	338.54	-	384.61
123	JAKHAL-MANSA DOUBLING ON SPR SECTION (NORTHERN RAILWAY) - [N22000291]	162.96	-	160.25
124	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI (SOUTHERN RAILWAY) - [N22000303]	460.94	01/1999	0.01
125	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000439]	458.63	03/2015	367.71
126	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000440]	200.84	03/2014	394.51
127	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000446]	600.00	03/2010	673.80

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
128	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000450]	199.55	03/2009	238.61
129	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. (SOUTHERN RAILWAY) - [N22000453]	208.00	03/2012	206.20
130	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. (SOUTHERN RAILWAY) - [N22000454]	241.00	03/2014	293.37
131	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR- LUCKNOW (NORTH EASTERN RAILWAY) - [N22000455]	233.00	04/1999	349.37
132	MANDHANA - BRAHMAWART NEW LINE PROJECT. (NORTH EASTERN RAILWAY) - [N22000458]	609.04	04/1999	1,806.84
133	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM (EAST CENTRAL RAILWAYS) - [N22000474]	624.47	02/2016	3,376.08

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2019			
	<u>RAILWAYS</u>			
1	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL (RAIL VIKAS NIGAM LTD.) - [220100149]	631.78	12/2012	762.72
2	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR (NORTHERN RAILWAY) - [220100258]	625.30	06/2007	848.84
3	TAMLUK DIGHA,LINE DOUBLING (SER) (SOUTH EASTERN RAILWAY) - [N22000097]	293.97	06/2005	0.00
4	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) (NORTH WESTERN RAILWAY) - [N22000112]	829.74	03/2015	823.85
5	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE (EASTERN RAILWAYS) - [N22000248]	268.52	-	0.00
6	MUNIRABAD (GINGERA) -RAICHUR NL (SOUTH WESTERN RAILWAY) - [N22000257]	179.65	-	940.47
7	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL (NORTHERN RAILWAY) - [N22000268]	396.04	-	225.18
8	CHANDIGARH-BADDI NL (NORTHERN RAILWAY) - [N22000296]	328.14	-	233.84
9	MM FROM BURAMARA-CHAKULIA (SOUTH EASTERN RAILWAY) - [N22000305]	466.48	-	0.83
10	MIRAJ-LONDA (SOUTH WESTERN RAILWAY) - [N22000327]	1,830.00	-	254.57
11	CHHINDWARA-MANDLA FORT GC (SOUTH EAST CENTRAL RAILWAY) - [N22000481]	556.54	03/2012	0.00
12	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM (SOUTH EAST CENTRAL RAILWAY) - [N22000482]	1,471.93	03/2022	0.00
	<u>WATER RESOURCES</u>			
13	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [300100001]	542.90	12/2007	0.00

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1623
No of Projects Completed/Dropped/Frozen in Current Month	52
No of Projects Elevated in Current Month	10
No of Projects added in Current Month	27
No of Projects in Current Month	1608

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	550 (34.20%)	24 (1.49%)	390(24.25%)	165 (10.26%)	479(9.79%)	1608
Latest Approved (Date)	474 (29.48%)	24 (1.49%)	472(29.35%)	158 (9.83%)	480(9.85%)	1608

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1364	16,64,360.19	19,20,992.75	7,50,279.92	39.10	2,56,632.56	15.40
Project with Revision in Cost	244	3,78,867.20	3,84,867.58	1,84,741.47	48.00	6,000.38	1.60
Total	1,608	20,43,227.39	23,05,860.33	9,35,021.39	40.55	2,62,632.94	12.85
Original Cost of All Projects							
Original Cost	1,608	19,17,796.07	23,05,860.33	9,35,021.39	40.55	3,88,064.26	20.23

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	550	8,14,174.52	10,46,384.21	5,25,399.68	50.20	2,32,209.69	28.52
Latest Approved (RCE)	474	6,36,510.86	7,76,054.26	3,51,495.02	45.30	1,39,543.40	21.92

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	119	1,87,635.63	2,46,067.14	1,34,895.99	54.80	58,431.51	31.10
Total	119	1,87,635.63	2,46,067.14	1,34,895.99	54.82	58,431.51	31.14


Summary of projects in the Flash Report for the month of June, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1623
Number of Projects completed/dropped/frozen in Current Month	52
Number of Projects elevated to the status of Major project during the current month	10
Number of Projects Added in Current Month	27
Number of Projects in Current Month	1608

Brief Analysis

Project Status with respect to Original Schedule: Out of 1608 projects, 24 projects are ahead of schedule, 390 projects are on schedule 550 projects are delayed. 479 projects do not have fixed dates of commissioning. 165 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

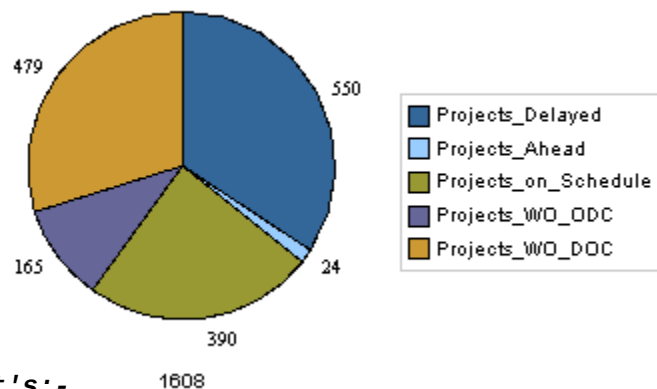

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1608 projects when sanctioned, was of the order of Rs. 1917796.07 crore but this was subsequently revised to Rs. 2305860.33 crore implying a cost overrun of 20.2%. The expenditure incurred on these projects till June, 2019 is Rs. 935021.39 crore, which is 40.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

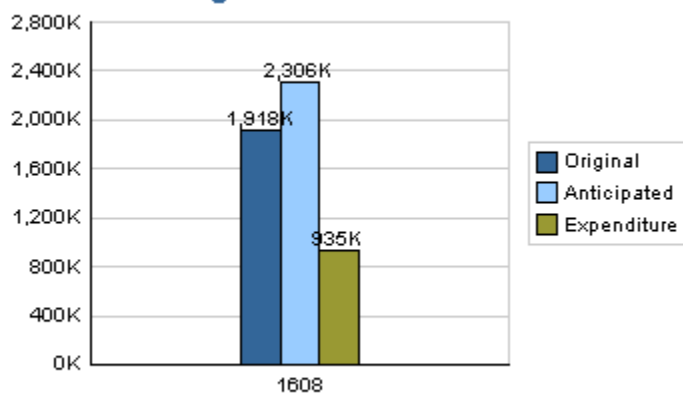


TABLE-5

<u>Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 150 Crore and above</u> (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	102	1,01,584.05	1,02,037.39	0.45	11	25,725.94	28,037.55	8.99
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	14	32,793.01	40,195.41	22.57	2	15,868.00	23,628.40	48.91
7	PETROLEUM	150	2,47,891.38	2,55,071.46	2.90	26	42,201.80	52,135.03	23.54
8	POWER	75	2,77,523.99	3,51,070.74	26.50	32	1,55,595.63	2,29,659.43	47.60
9	HEAVY INDUSTRY	2	3,272.00	5,281.30	61.41	1	1,718.00	3,727.30	116.96
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
11	RAILWAYS	320	4,64,773.55	6,70,541.38	44.27	197	1,81,516.40	4,00,102.03	120.42
12	ROAD TRANSPORT AND HIGHWAYS	831	4,92,220.43	5,07,134.63	3.03	62	33,028.53	48,641.44	47.27
13	SHIPPING AND PORTS	8	10,757.29	11,199.74	4.11	3	760.89	1,545.44	103.11
14	TELECOMMUNICATIONS	5	16,310.53	27,553.13	68.93	3	13,781.10	25,123.70	82.31
15	URBAN DEVELOPMENT	62	1,75,890.06	1,82,113.88	3.54	14	29,058.09	35,281.91	21.42
16	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0.00
Total		1608	19,17,796.07	23,05,860.33	20.23	360	5,38,265.07	9,45,774.41	75.71

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	76	1,20,417.63	1,69,552.26	40.80	11	20,045.74	69,683.59	247.62
2	ARUNACHAL PRADESH	38	19,572.19	38,180.70	95.08	9	10,017.70	28,626.21	185.76
3	ASSAM	46	24,306.66	28,182.62	15.95	14	5,045.57	9,194.62	82.23
4	BIHAR	90	76,140.96	1,21,061.57	59.00	30	38,926.75	83,922.99	115.59
5	GOA	12	5,779.51	5,789.94	0.18	1	280.16	290.59	3.72
6	GUJARAT	55	53,993.80	59,554.74	10.30	8	14,902.13	21,496.55	44.25
7	HARYANA	33	22,790.13	24,261.34	6.46	3	1,900.58	3,505.00	84.42
8	HIMACHAL PRADESH	12	16,702.17	26,812.70	60.53	2	6,886.58	16,997.11	146.82
9	JAMMU AND KASHMIR	12	24,323.57	49,772.57	104.63	1	2,500.00	27,949.00	1017.96
10	KARNATAKA	63	71,493.59	74,471.44	4.17	12	8,855.40	12,068.26	36.28
11	KERALA	22	39,078.60	41,496.22	6.19	5	12,198.89	14,812.05	21.42
12	MADHYA PRADESH	74	84,643.15	91,734.75	8.38	9	28,541.25	37,229.83	30.44
13	MAHARASHTRA	254	2,35,175.32	2,44,487.65	3.96	31	39,484.73	54,082.63	36.97
14	MANIPUR	4	5,767.05	15,062.08	161.17	1	4,454.17	13,809.00	210.02
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	1	906.46	6,000.00	561.92
16	MIZORAM	12	7,570.66	10,884.08	43.77	4	3,406.61	6,720.03	97.26
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	28.95
18	ODISHA	97	1,06,664.83	1,09,523.39	2.68	19	28,187.75	34,625.84	22.84
19	PUNJAB	27	13,539.35	13,656.94	0.87	3	2,031.78	2,149.37	5.79
20	RAJASTHAN	62	47,167.18	53,718.94	13.89	13	17,425.66	23,977.42	37.60
21	SIKKIM	9	3,476.73	6,308.80	81.46	2	1,521.76	4,353.83	186.10
22	TAMIL NADU	67	1,15,852.79	1,34,404.28	16.01	23	37,211.30	57,551.00	54.66
23	TRIPURA	5	1,466.46	1,628.65	11.06	4	1,097.46	1,259.65	14.78
24	UTTAR PRADESH	107	1,39,187.34	1,43,133.84	2.84	19	38,386.02	43,726.56	13.91
25	WEST BENGAL	63	59,288.55	71,207.49	20.10	23	22,868.69	35,108.90	53.52
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	2	552.41	679.33	22.98
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	23	55,482.27	62,957.50	13.47	6	6,981.71	14,456.94	107.07
29	CHHATISGARH	36	74,436.64	85,988.61	15.52	7	33,816.43	45,670.42	35.05
30	JHARKHAND	48	65,190.64	69,228.28	6.19	7	20,868.70	24,910.12	19.37
31	UTTARAKHAND	30	35,308.06	44,082.86	24.85	8	9,591.33	18,392.63	91.76
32	TELANGANA	57	40,255.16	43,275.56	7.50	12	6,282.64	9,429.38	50.09
33	MULTI STATE	137	3,27,381.15	4,34,465.77	32.71	69	1,10,762.19	2,20,095.56	98.71
Total		1608	19,17,796.07	23,05,860.33	20.23	360	5,38,265.07	9,45,774.41	75.71

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	102	1,01,584.05	1,02,037.39	0.45	30	17,014.82	18,205.04	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	33 - 33
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	14	32,793.01	40,195.41	22.57	9	23,646.42	31,048.82	11 - 62
7	PETROLEUM	150	2,47,891.38	2,55,071.46	2.90	44	1,04,117.69	1,06,787.83	1 - 110
8	POWER	75	2,77,523.99	3,51,070.74	26.50	52	1,83,618.66	2,42,602.99	1 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,281.30	61.41	1	1,718.00	3,727.30	102 - 102
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	12	4,937.67	5,037.45	2 - 83
11	RAILWAYS	320	4,64,773.55	6,70,541.38	44.27	138	1,72,020.18	2,55,911.58	1 - 324
12	ROAD TRANSPORT AND HIGHWAYS	831	4,92,220.43	5,07,134.63	3.03	227	1,33,025.16	1,38,078.80	1 - 140
13	SHIPPING AND PORTS	8	10,757.29	11,199.74	4.11	1	600.00	257.90	29 - 29
14	TELECOMMUNICATIONS	5	16,310.53	27,553.13	68.93	3	13,781.10	25,123.70	11 - 58
15	URBAN DEVELOPMENT	62	1,75,890.06	1,82,113.88	3.54	26	81,911.38	83,055.16	1 - 89
16	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	-
Total		1608	19,17,796.07	23,05,860.33	20.23	550	8,14,174.52	10,46,384.21	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	76	1,20,417.63	1,69,552.26	40.80	41	71,017.19	1,17,444.04	1 - 168
2	ARUNACHAL PRADESH	38	19,572.19	38,180.70	95.08	11	5,692.01	10,787.72	15 - 116
3	ASSAM	46	24,306.66	28,182.62	15.95	13	6,154.08	7,502.21	1 - 140
4	BIHAR	90	76,140.96	1,21,061.57	59.00	23	39,708.79	65,350.17	6 - 118
5	GOA	12	5,779.51	5,789.94	0.18	0	0.00	0.00	-
6	GUJARAT	55	53,993.80	59,554.74	10.30	13	18,307.92	24,552.32	2 - 120
7	HARYANA	33	22,790.13	24,261.34	6.46	8	3,900.77	5,441.45	6 - 118
8	HIMACHAL PRADESH	12	16,702.17	26,812.70	60.53	4	6,949.55	13,027.07	4 - 147
9	JAMMU AND KASHMIR	12	24,323.57	49,772.57	104.63	4	14,917.75	40,366.75	10 - 229
10	KARNATAKA	63	71,493.59	74,471.44	4.17	26	48,580.66	49,671.35	3 - 264
11	KERALA	22	39,078.60	41,496.22	6.19	9	17,162.14	18,394.45	8 - 89
12	MADHYA PRADESH	74	84,643.15	91,734.75	8.38	33	31,801.29	37,538.47	2 - 54
13	MAHARASHTRA	254	2,35,175.32	2,44,487.65	3.96	80	1,12,024.78	1,13,256.61	1 - 204
14	MANIPUR	4	5,767.05	15,062.08	161.17	3	5,188.43	14,483.46	36 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	3	1,149.47	1,149.47	2 - 16
16	MIZORAM	12	7,570.66	10,884.08	43.77	4	3,406.61	6,720.03	96 - 116
17	NAGALAND	21	13,711.07	14,384.55	4.91	4	3,525.63	4,199.11	36 - 79
18	ODISHA	97	1,06,664.83	1,09,523.39	2.68	36	44,950.43	47,165.25	3 - 177
19	PUNJAB	27	13,539.35	13,656.94	0.87	7	3,169.78	3,271.79	1 - 28
20	RAJASTHAN	62	47,167.18	53,718.94	13.89	19	22,409.87	28,014.34	1 - 70
21	SIKKIM	9	3,476.73	6,308.80	81.46	3	1,673.35	4,505.42	51 - 82
22	TAMIL NADU	67	1,15,852.79	1,34,404.28	16.01	25	69,645.32	77,501.99	2 - 133
23	TRIPURA	5	1,466.46	1,628.65	11.06	1	569.63	650.00	21 - 21
24	UTTAR PRADESH	107	1,39,187.34	1,43,133.84	2.84	27	40,347.28	43,147.18	2 - 68
25	WEST BENGAL	63	59,288.55	71,207.49	20.10	30	30,745.31	38,938.46	9 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	23	55,482.27	62,957.50	13.47	6	3,723.26	4,195.83	14 - 83
29	CHHATISGARH	36	74,436.64	85,988.61	15.52	12	38,081.27	49,580.75	9 - 84
30	JHARKHAND	48	65,190.64	69,228.28	6.19	15	22,171.11	23,196.81	4 - 120
31	UTTARAKHAND	30	35,308.06	44,082.86	24.85	10	25,218.73	33,506.44	6 - 114
32	TELANGANA	57	40,255.16	43,275.56	7.50	17	18,657.18	19,497.20	2 - 156
33	MULTI STATE	137	3,27,381.15	4,34,465.77	32.71	61	96,924.24	1,37,044.43	1 - 252
Total		1608	19,17,796.07	23,05,860.33	20.23	550	8,14,174.52	10,46,384.21	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	71,879.00	80,348.00	11.78	4	71,879.00	80,348.00	36 - 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	102	1,02,757.35	1,02,037.39	-0.70	30	18,188.12	18,205.04	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	33 - 33
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	14	32,938.41	40,195.41	22.03	0	0.00	0.00	-
7	PETROLEUM	150	2,53,410.80	2,55,071.46	0.66	31	68,815.80	69,165.38	1 - 110
8	POWER	75	3,02,701.94	3,51,070.74	15.98	33	82,392.54	1,05,718.20	1 - 147
9	HEAVY INDUSTRY	2	5,281.30	5,281.30	0.00	1	3,727.30	3,727.30	102 - 102
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	12	4,937.67	5,037.45	2 - 83
11	RAILWAYS	320	5,49,890.62	6,70,541.38	21.94	114	1,60,959.57	2,06,327.47	1 - 324
12	ROAD TRANSPORT AND HIGHWAYS	831	4,93,523.16	5,07,134.63	2.76	220	1,31,093.16	1,35,159.56	1 - 140
13	SHIPPING AND PORTS	8	10,428.79	11,199.74	7.39	1	258.00	257.90	29 - 29
14	TELECOMMUNICATIONS	5	16,323.13	27,553.13	68.80	1	13,334.00	24,664.00	58 - 58
15	URBAN DEVELOPMENT	62	1,76,432.75	1,82,113.88	3.22	24	70,262.26	71,244.32	0 - 89
16	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
17	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	-
Total		1608	20,43,227.39	23,05,860.33	12.85	474	6,36,510.86	7,76,054.26	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS. 150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	71,879.00	80,348.00	11.78	2	14,951.00	23,420.00	56.65
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	102	1,02,757.35	1,02,037.39	-0.70	10	19,818.83	20,957.14	5.74
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	14	32,938.41	40,195.41	22.03	1	15,525.00	23,140.00	49.05
7	PETROLEUM	150	2,53,410.80	2,55,071.46	0.66	16	22,400.65	26,553.69	18.54
8	POWER	75	3,02,701.94	3,51,070.74	15.98	27	1,26,683.43	1,75,569.28	38.59
9	HEAVY INDUSTRY	2	5,281.30	5,281.30	0.00	0	0.00	0.00	0.00
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
11	RAILWAYS	320	5,49,890.62	6,70,541.38	21.94	174	1,42,904.80	2,70,176.49	89.06
12	ROAD TRANSPORT AND HIGHWAYS	831	4,93,523.16	5,07,134.63	2.76	79	38,715.77	53,266.07	37.58
13	SHIPPING AND PORTS	8	10,428.79	11,199.74	7.39	3	774.39	1,545.44	99.57
14	TELECOMMUNICATIONS	5	16,323.13	27,553.13	68.80	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	62	1,76,432.75	1,82,113.88	3.22	10	28,341.60	34,022.73	20.05
16	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
17	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0.00
Total		1608	20,43,227.39	23,05,860.33	12.85	329	4,35,189.16	7,10,708.02	63.31

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	71,879.00	80,348.00	11.78	2	14,951.00	23,420.00	54- 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	102	1,02,757.35	1,02,037.39	-0.70	6	1,549.74	2,394.02	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	33- 33
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	14	32,938.41	40,195.41	22.03	0	0.00	0.00	0- 0
7	PETROLEUM	150	2,53,410.80	2,55,071.46	0.66	5	8,639.79	9,701.19	6- 110
8	POWER	75	3,02,701.94	3,51,070.74	15.98	13	39,476.55	62,802.21	12- 147
9	HEAVY INDUSTRY	2	5,281.30	5,281.30	0.00	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	1	414.11	513.89	83- 83
11	RAILWAYS	320	5,49,890.62	6,70,541.38	21.94	64	61,062.10	1,06,903.39	6- 324
12	ROAD TRANSPORT AND HIGHWAYS	831	4,93,523.16	5,07,134.63	2.76	36	20,140.62	24,607.33	1- 140
13	SHIPPING AND PORTS	8	10,428.79	11,199.74	7.39	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	5	16,323.13	27,553.13	68.80	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	62	1,76,432.75	1,82,113.88	3.22	4	7,285.00	8,267.06	17- 40
16	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
17	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0- 0
Total		1608	20,43,227.39	23,05,860.33	12.85	135	1,77,516.35	3,19,472.73	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	102	1,01,584.05	1,02,037.39	0.45	7	7,456.85	9,474.43	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	33- 33
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	14	32,793.01	40,195.41	22.57	2	15,868.00	23,628.40	53- 62
7	PETROLEUM	150	2,47,891.38	2,55,071.46	2.90	13	25,847.77	30,331.66	1- 110
8	POWER	75	2,77,523.99	3,51,070.74	26.50	27	1,33,344.83	1,92,329.16	12- 147
9	HEAVY INDUSTRY	2	3,272.00	5,281.30	61.41	1	1,718.00	3,727.30	102- 102
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	1	414.11	513.89	83- 83
11	RAILWAYS	320	4,64,773.55	6,70,541.38	44.27	83	81,236.13	1,73,802.32	3- 324
12	ROAD TRANSPORT AND HIGHWAYS	831	4,92,220.43	5,07,134.63	3.03	36	19,392.26	24,611.08	1- 140
13	SHIPPING AND PORTS	8	10,757.29	11,199.74	4.11	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	5	16,310.53	27,553.13	68.93	3	13,781.10	25,123.70	11- 58
15	URBAN DEVELOPMENT	62	1,75,890.06	1,82,113.88	3.54	6	7,948.75	9,092.53	5- 70
16	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0- 0
Total		1608	19,17,796.07	23,05,860.33	20.23	185	3,44,942.24	5,89,333.11	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	76	1,20,417.63	1,69,552.26	40.80	6	13,148.57	59,933.42	2 - 168
2	ARUNACHAL PRADESH	38	19,572.19	38,180.70	95.08	6	3,368.71	8,464.42	36 - 116
3	ASSAM	46	24,306.66	28,182.62	15.95	5	1,155.95	2,661.03	12 - 140
4	BIHAR	90	76,140.96	1,21,061.57	59.00	11	31,302.59	56,951.68	12 - 118
5	GOA	12	5,779.51	5,789.94	0.18	0	0.00	0.00	-
6	GUJARAT	55	53,993.80	59,554.74	10.30	5	13,479.15	19,879.88	12 - 120
7	HARYANA	33	22,790.13	24,261.34	6.46	2	1,395.00	2,982.00	100 - 111
8	HIMACHAL PRADESH	12	16,702.17	26,812.70	60.53	1	3,919.59	9,997.11	147 - 147
9	JAMMU AND KASHMIR	12	24,323.57	49,772.57	104.63	1	2,500.00	27,949.00	229 - 229
10	KARNATAKA	63	71,493.59	74,471.44	4.17	5	3,185.52	4,292.22	3 - 36
11	KERALA	22	39,078.60	41,496.22	6.19	3	10,025.83	11,282.18	15 - 29
12	MADHYA PRADESH	74	84,643.15	91,734.75	8.38	6	17,231.95	23,065.44	6 - 36
13	MAHARASHTRA	254	2,35,175.32	2,44,487.65	3.96	18	20,834.18	27,219.86	1 - 204
14	MANIPUR	4	5,767.05	15,062.08	161.17	1	4,454.17	13,809.00	108 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	0	0.00	0.00	-
16	MIZORAM	12	7,570.66	10,884.08	43.77	4	3,406.61	6,720.03	96 - 116
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	79 - 79
18	ODISHA	97	1,06,664.83	1,09,523.39	2.68	13	23,487.74	29,202.13	3 - 177
19	PUNJAB	27	13,539.35	13,656.94	0.87	2	1,142.54	1,244.55	1 - 28
20	RAJASTHAN	62	47,167.18	53,718.94	13.89	7	14,217.88	19,822.35	5 - 48
21	SIKKIM	9	3,476.73	6,308.80	81.46	2	1,521.76	4,353.83	51 - 82
22	TAMIL NADU	67	1,15,852.79	1,34,404.28	16.01	8	17,651.33	26,599.21	12 - 133
23	TRIPURA	5	1,466.46	1,628.65	11.06	1	569.63	650.00	21 - 21
24	UTTAR PRADESH	107	1,39,187.34	1,43,133.84	2.84	7	13,162.81	16,500.52	5 - 68
25	WEST BENGAL	63	59,288.55	71,207.49	20.10	14	18,291.65	26,484.81	12 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	23	55,482.27	62,957.50	13.47	2	1,633.32	2,105.89	17 - 83
29	CHHATISGARH	36	74,436.64	85,988.61	15.52	6	32,944.43	44,443.91	9 - 62
30	JHARKHAND	48	65,190.64	69,228.28	6.19	2	14,515.35	15,541.05	27 - 35
31	UTTARAKHAND	30	35,308.06	44,082.86	24.85	4	7,241.32	15,555.53	70 - 114
32	TELANGANA	57	40,255.16	43,275.56	7.50	5	2,730.04	3,648.31	39 - 144
33	MULTI STATE	137	3,27,381.15	4,34,465.77	32.71	36	63,783.49	1,04,532.42	8 - 252
Total		1608	19,17,796.07	23,05,860.33	20.23	185	3,44,942.24	5,89,333.11	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	158	33
2	ROAD TRANSPORT AND HIGHWAYS	143	7
3	PETROLEUM	56	2
4	POWER	41	6
5	COAL	15	1
6	URBAN DEVELOPMENT	15	1
7	STEEL	7	1
8	ATOMIC ENERGY	4	0
9	SHIPPING AND PORTS	3	0
10	HEAVY INDUSTRY	2	0
11	TELECOMMUNICATIONS	2	0
12	MINES	1	0
13	WATER RESOURCES	1	0
	Total	448	51

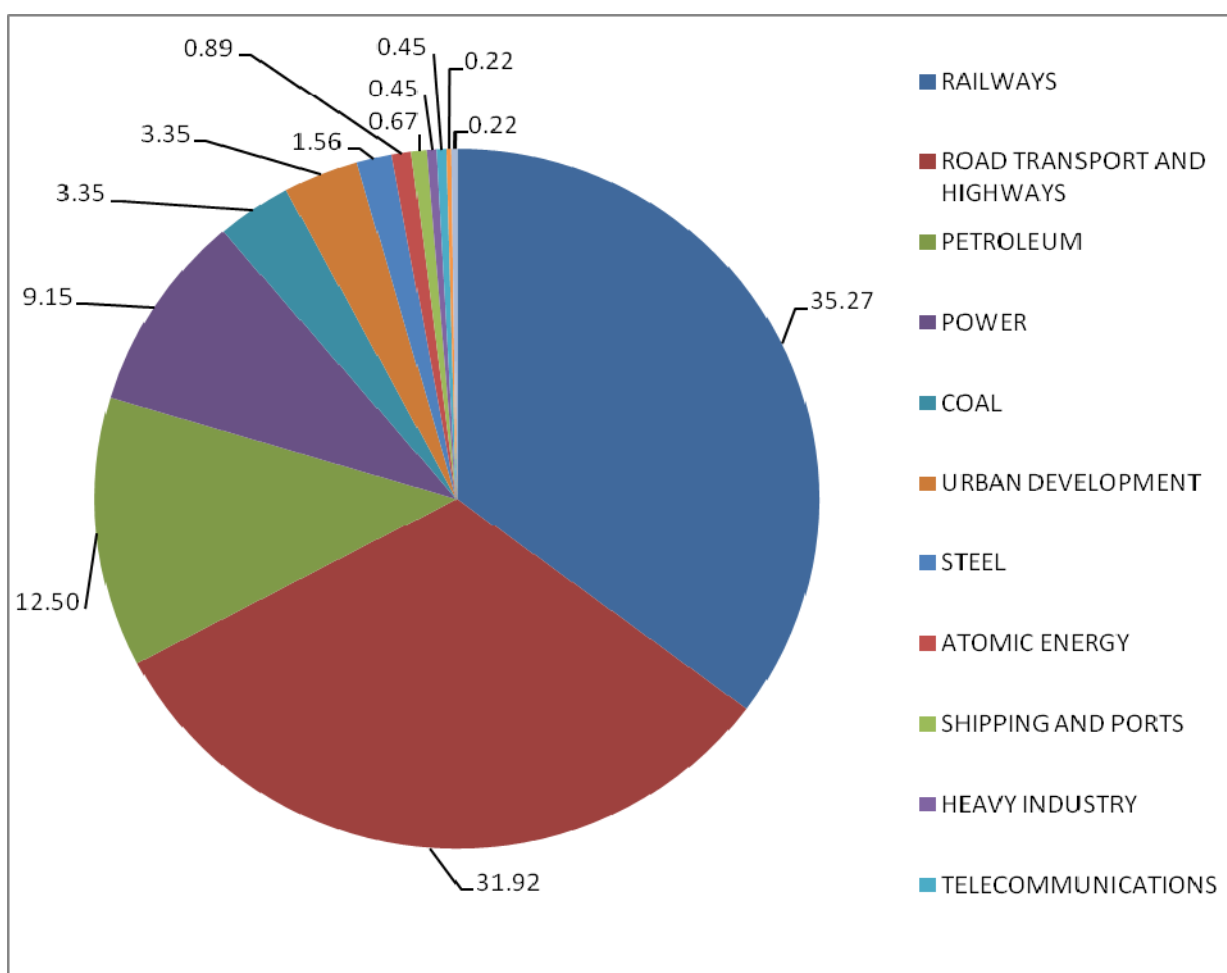


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	456
No of Projects Completed/Dropped/Frozen in Current Month	19
No of Projects added in Current Month	0
No of Projects in Current Month	448

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	183 (40.85%)	6 (1.34%)	100(22.32%)	54 (12.05%)	105(3.44%)	448
Latest Approved (Date)	138 (30.80%)	7 (1.56%)	146(32.59%)	51 (11.38%)	106(3.66%)	448

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	388	12,62,367.88	15,03,602.82	5,86,995.67	39.00	2,41,234.94	19.10
Project with Revision in Cost	60	3,08,268.94	3,12,714.06	1,55,715.12	49.80	4,445.12	1.40
Total	448	15,70,636.82	18,16,316.88	7,42,710.79	40.89	2,45,680.06	15.64
Original Cost of All Projects							
Original Cost	448	14,45,342.56	18,16,316.88	7,42,710.79	40.89	3,70,974.32	25.67

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	183	6,60,741.23	8,87,304.68	4,42,150.17	49.80	2,26,563.45	34.29
Latest Approved (RCE)	138	4,99,157.59	6,32,258.97	2,76,851.47	43.80	1,33,101.38	26.67

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	55	1,58,108.43	2,13,972.04	1,15,745.87	54.10	55,863.61	35.30
Total	55	1,58,108.43	2,13,972.04	1,15,745.87	54.09	55,863.61	35.33

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	COAL	15	64,463.42	65,637.52	1.82	2	23,144.11	24,318.21	5.07
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	37,387.34	24.09	1	15,525.00	23,140.00	49.05
5	PETROLEUM	56	2,09,794.97	2,15,740.85	2.83	14	36,955.90	45,485.15	23.08
6	POWER	41	2,64,026.02	3,36,972.26	27.63	24	1,52,955.09	2,26,418.38	48.03
7	HEAVY INDUSTRY	2	3,272.00	5,281.30	61.41	1	1,718.00	3,727.30	116.96
8	RAILWAYS	158	3,95,361.73	5,89,748.62	49.17	100	1,49,139.68	3,49,043.55	134.04
9	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.25	2,21,059.85	5.51	15	17,709.70	29,252.30	65.18
10	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	15	1,62,094.22	1,67,950.70	3.61	5	26,033.88	31,890.36	22.50
13	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		448	14,45,342.56	18,16,316.88	25.67	167	4,73,937.40	8,53,987.12	80.19

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-16

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	21	98,791.39	1,47,893.34	49.70	7	18,977.19	68,437.14	260.63
2	ARUNACHAL PRADESH	4	11,753.92	29,887.37	154.28	2	8,782.23	26,915.68	206.48
3	ASSAM	7	10,628.98	13,232.87	24.50	3	2,127.51	4,868.01	128.81
4	BIHAR	25	47,389.75	88,955.45	87.71	16	33,657.10	75,222.80	123.50
5	GUJARAT	16	34,897.59	40,605.78	16.36	3	13,264.36	18,972.55	43.03
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	14,146.19	24,256.72	71.47	2	6,886.58	16,997.11	146.82
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	1017.96
9	KARNATAKA	18	53,474.10	55,881.81	4.50	5	5,713.62	8,317.34	45.57
10	KERALA	10	32,670.86	35,060.11	7.31	3	11,336.08	13,749.37	21.29
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	8	28,044.20	36,348.78	29.61
12	MAHARASHTRA	51	1,54,156.84	1,66,251.78	7.85	18	35,563.76	48,430.57	36.18
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	210.02
14	MEGHALAYA	1	906.46	6,000.00	561.92	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	109.80
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	28.95
17	ODISHA	33	80,852.03	82,843.71	2.46	10	25,048.54	30,539.79	21.92
18	PUNJAB	3	3,627.54	3,627.54	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	11	24,061.71	29,327.58	21.88	3	14,015.71	19,281.58	37.57
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	25	97,194.58	1,13,365.79	16.64	11	33,622.33	50,490.54	50.17
22	UTTAR PRADESH	42	1,10,405.14	1,13,944.76	3.21	8	34,043.60	38,355.17	12.66
23	WEST BENGAL	23	43,206.76	53,503.42	23.83	10	18,286.35	28,599.02	56.40
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
25	DELHI	7	50,481.91	57,816.75	14.53	3	6,254.39	13,589.23	117.28
26	CHHATISGARH	14	65,083.62	76,328.53	17.28	6	33,664.00	45,210.93	34.30
27	JHARKHAND	12	51,836.51	55,290.95	6.66	3	19,637.61	23,092.05	17.59
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	8,654.06	17,090.60	97.49
29	TELANGANA	6	19,991.02	22,068.26	10.39	2	2,378.60	4,455.84	87.33
30	MULTI STATE	64	2,97,079.88	3,99,457.78	34.46	33	98,951.48	2,02,870.88	105.02
Total		448	14,45,342.56	18,16,316.88	25.67	167	4,73,937.40	8,53,987.12	80.19

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	COAL	15	64,463.42	65,637.52	1.82	2	6,962.16	8,135.46	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	37,387.34	24.09	5	22,254.04	29,511.04	12 - 62
5	PETROLEUM	56	2,09,794.97	2,15,740.85	2.83	18	93,133.16	95,193.53	1 - 110
6	POWER	41	2,64,026.02	3,36,972.26	27.63	28	1,74,083.23	2,32,469.05	3 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,281.30	61.41	1	1,718.00	3,727.30	102 - 102
8	RAILWAYS	158	3,95,361.73	5,89,748.62	49.17	79	1,41,190.31	2,23,223.13	3 - 324
9	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.25	2,21,059.85	5.51	38	54,753.15	57,563.37	1 - 100
10	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	15	1,62,094.22	1,67,950.70	3.61	6	76,042.14	76,920.93	1 - 64
13	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		448	14,45,342.56	18,16,316.88	25.67	183	6,60,741.23	8,87,304.68	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-18

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,47,893.34	49.70	10	59,598.89	1,05,859.16	1 - 168
2	ARUNACHAL PRADESH	4	11,753.92	29,887.37	154.28	2	3,750.00	8,672.44	60 - 116
3	ASSAM	7	10,628.98	13,232.87	24.50	2	2,850.35	3,910.86	12 - 81
4	BIHAR	25	47,389.75	88,955.45	87.71	9	32,035.52	57,007.05	12 - 118
5	GUJARAT	16	34,897.59	40,605.78	16.36	3	14,247.62	19,849.11	2 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	100 - 100
7	HIMACHAL PRADESH	6	14,146.19	24,256.72	71.47	2	6,405.52	12,483.04	15 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	4	14,917.75	40,366.75	10 - 229
9	KARNATAKA	18	53,474.10	55,881.81	4.50	10	39,631.87	40,402.12	3 - 264
10	KERALA	10	32,670.86	35,060.11	7.31	5	15,319.19	16,458.82	8 - 33
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	8	22,560.85	28,010.34	5 - 26
12	MAHARASHTRA	51	1,54,156.84	1,66,251.78	7.85	22	83,588.24	88,325.72	1 - 204
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	33	80,852.03	82,843.71	2.46	14	36,399.57	37,839.28	3 - 177
18	PUNJAB	3	3,627.54	3,627.54	0.00	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	29,327.58	21.88	2	13,749.38	18,508.38	6 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	25	97,194.58	1,13,365.79	16.64	11	62,367.44	70,594.89	12 - 133
22	UTTAR PRADESH	42	1,10,405.14	1,13,944.76	3.21	12	34,676.06	37,350.72	2 - 28
23	WEST BENGAL	23	43,206.76	53,503.42	23.83	13	23,749.79	31,292.67	18 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
25	DELHI	7	50,481.91	57,816.75	14.53	2	2,613.73	2,986.52	17 - 31
26	CHHATISGARH	14	65,083.62	76,328.53	17.28	6	35,847.00	47,039.42	9 - 62
27	JHARKHAND	12	51,836.51	55,290.95	6.66	4	18,278.97	19,076.44	9 - 32
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	23,343.06	31,505.53	15 - 114
29	TELANGANA	6	19,991.02	22,068.26	10.39	4	14,450.02	14,727.42	7 - 156
30	MULTI STATE	64	2,97,079.88	3,99,457.78	34.46	28	82,652.69	1,20,992.55	3 - 252
Total		448	14,45,342.56	18,16,316.88	25.67	183	6,60,741.23	8,87,304.68	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	71,879.00	80,348.00	11.78	4	71,879.00	80,348.00	36 - 133
2	COAL	15	65,636.72	65,637.52	0.00	2	8,135.46	8,135.46	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	37,387.34	24.09	0	0.00	0.00	-
5	PETROLEUM	56	2,14,847.46	2,15,740.85	0.42	8	59,072.29	59,280.39	6 - 110
6	POWER	41	2,89,203.97	3,36,972.26	16.52	14	75,254.43	98,133.55	3 - 147
7	HEAVY INDUSTRY	2	5,281.30	5,281.30	0.00	1	3,727.30	3,727.30	102 - 102
8	RAILWAYS	158	4,82,181.61	5,89,748.62	22.31	64	1,38,228.78	1,79,357.10	3 - 324
9	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.50	2,21,059.85	5.51	38	54,753.15	57,563.37	1 - 100
10	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	15	1,62,396.31	1,67,950.70	3.42	5	64,622.14	65,500.93	13 - 64
13	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		448	15,70,636.82	18,16,316.88	15.64	138	4,99,157.59	6,32,258.97	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

<u>Extent of cost overrun in projects with respect to latest schedule RS.1000 Crore and above</u> (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	71,879.00	80,348.00	11.78	2	14,951.00	23,420.00	56.65
2	COAL	15	65,636.72	65,637.52	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	37,387.34	24.09	1	15,525.00	23,140.00	49.05
5	PETROLEUM	56	2,14,847.46	2,15,740.85	0.42	8	18,395.56	21,628.55	17.57
6	POWER	41	2,89,203.97	3,36,972.26	16.52	19	1,24,042.89	1,72,328.23	38.93
7	HEAVY INDUSTRY	2	5,281.30	5,281.30	0.00	0	0.00	0.00	0.00
8	RAILWAYS	158	4,82,181.61	5,89,748.62	22.31	87	1,13,512.67	2,25,273.09	98.46
9	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.50	2,21,059.85	5.51	15	17,709.70	29,252.30	65.18
10	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	15	1,62,396.31	1,67,950.70	3.42	5	26,335.97	31,890.36	21.09
13	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		448	15,70,636.82	18,16,316.88	15.64	140	3,71,194.83	6,24,383.20	68.21

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-21

Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	71,879.00	80,348.00	11.78	2	14,951.00	23,420.00	54- 133
2	COAL	15	65,636.72	65,637.52	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	37,387.34	24.09	0	0.00	0.00	0- 0
5	PETROLEUM	56	2,14,847.46	2,15,740.85	0.42	2	7,503.29	8,295.43	15- 110
6	POWER	41	2,89,203.97	3,36,972.26	16.52	7	37,653.50	60,532.62	12- 147
7	HEAVY INDUSTRY	2	5,281.30	5,281.30	0.00	0	0.00	0.00	0- 0
8	RAILWAYS	158	4,82,181.61	5,89,748.62	22.31	37	50,537.76	91,831.11	9- 324
9	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.50	2,21,059.85	5.51	11	11,890.31	14,700.53	2- 100
10	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	15	1,62,396.31	1,67,950.70	3.42	2	6,401.00	7,279.79	17- 29
13	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		448	15,70,636.82	18,16,316.88	15.64	63	1,52,421.90	2,86,272.35	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-22

Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	COAL	15	64,463.42	65,637.52	1.82	1	5,907.11	7,080.41	48- 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	37,387.34	24.09	1	15,525.00	23,140.00	62- 62
5	PETROLEUM	56	2,09,794.97	2,15,740.85	2.83	7	23,720.31	27,466.65	1- 110
6	POWER	41	2,64,026.02	3,36,972.26	27.63	20	1,31,034.29	1,89,420.11	12- 147
7	HEAVY INDUSTRY	2	3,272.00	5,281.30	61.41	1	1,718.00	3,727.30	102- 102
8	RAILWAYS	158	3,95,361.73	5,89,748.62	49.17	49	68,624.05	1,54,321.47	3- 324
9	ROAD TRANSPORT AND HIGHWAYS	143	2,09,517.25	2,21,059.85	5.51	11	11,890.31	14,700.53	2- 100
10	SHIPPING AND PORTS	3	8,426.40	8,426.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	15	1,62,094.22	1,67,950.70	3.61	2	6,401.00	7,279.79	17- 29
13	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		448	14,45,342.56	18,16,316.88	25.67	97	3,15,576.11	5,47,848.13	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,47,893.34	49.70	3	12,237.86	58,856.13	2 - 168
2	ARUNACHAL PRADESH	4	11,753.92	29,887.37	154.28	1	2,496.90	7,419.34	116 - 116
3	ASSAM	7	10,628.98	13,232.87	24.50	1	385.20	1,532.00	12 - 12
4	BIHAR	25	47,389.75	88,955.45	87.71	7	29,343.85	54,315.38	12 - 118
5	GUJARAT	16	34,897.59	40,605.78	16.36	2	12,288.74	17,890.23	12 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	100 - 100
7	HIMACHAL PRADESH	6	14,146.19	24,256.72	71.47	1	3,919.59	9,997.11	147 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	229 - 229
9	KARNATAKA	18	53,474.10	55,881.81	4.50	2	1,824.74	2,611.00	3 - 4
10	KERALA	10	32,670.86	35,060.11	7.31	2	9,770.08	10,933.75	15 - 29
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	5	16,734.90	22,184.39	6 - 26
12	MAHARASHTRA	51	1,54,156.84	1,66,251.78	7.85	10	18,663.53	24,172.88	1 - 204
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	33	80,852.03	82,843.71	2.46	8	21,764.83	26,704.11	3 - 177
18	PUNJAB	3	3,627.54	3,627.54	0.00	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	29,327.58	21.88	1	12,320.00	17,079.00	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	25	97,194.58	1,13,365.79	16.64	6	17,160.09	25,387.54	12 - 133
22	UTTAR PRADESH	42	1,10,405.14	1,13,944.76	3.21	3	11,862.61	14,686.28	5 - 28
23	WEST BENGAL	23	43,206.76	53,503.42	23.83	8	16,223.21	23,766.10	29 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
25	DELHI	7	50,481.91	57,816.75	14.53	1	1,219.21	1,592.00	17 - 17
26	CHHATISGARH	14	65,083.62	76,328.53	17.28	5	32,792.00	43,984.42	9 - 62
27	JHARKHAND	12	51,836.51	55,290.95	6.66	1	14,366.58	15,164.05	27 - 27
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	3	7,127.06	15,289.53	76 - 114
29	TELANGANA	6	19,991.02	22,068.26	10.39	1	1,266.60	1,544.00	39 - 39
30	MULTI STATE	64	2,97,079.88	3,99,457.78	34.46	20	57,686.89	96,586.75	8 - 252
Total		448	14,45,342.56	18,16,316.88	25.67	97	3,15,576.11	5,47,848.13	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>RAILWAYS</u>						
1	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	03/1994	685.00	06/2019	682.34
2	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	N.A.	579.37	06/2019	0.01
3	KARUR-SALEM(NL),SR	02/1997	155.55	N.A.	920.00	06/2019	863.54
4	KATIHAR - JOGBANI (GC)(NEFR)	09/2001	792.46	12/2010	1,320.00	06/2019	944.80
5	MAHARAJGANJ-MASRAKH (NL) - NER	04/2003	218.19	06/2018	413.56	06/2019	380.50
6	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	07/2006	732.81	03/2008	2,200.00	06/2019	2,191.46
7	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE	04/2010	268.52	N.A.	268.52	06/2019	0.00
8	MEERUT-MUZAFARNAGAR PATCH DL	04/2012	377.44	N.A.	450.00	06/2019	430.12
9	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH	04/2010	338.54	N.A.	390.00	06/2019	384.61
10	PANDABESWAR-CHINPAI DOUBLING (ER)	04/2004	293.74	12/2010	160.00	06/2019	128.78
11	GHUTIASHARIF-CANNING (ER)	04/2009	193.08	12/2011	683.89	06/2019	154.30
12	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	04/1999	108.00	12/2009	462.48	06/2019	455.39
13	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	04/1995	1,125.89	03/2016	1,207.90	06/2019	1,180.08
14	KODERMA GIRIDH (NL), ECR	04/1996	768.87	N.A.	160.00	06/2019	988.38
15	MM FROM BURAMARA-CHAKULIA	04/2008	466.48	N.A.	1,241.11	12/2024	0.83
16	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	04/1999	460.94	01/1999	160.00	06/2019	0.01
17	CHANDIGARH-BADDI NL	04/2007	328.14	N.A.	1,540.00	06/2019	233.84
18	JAKHAL-MANSA DOUBLING ON SPR SECTION	04/2008	162.96	N.A.	162.96	06/2019	160.25
19	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION	02/1997	458.63	03/2015	458.63	06/2019	367.71
20	LUMDING-HOJAI PATCH DOUBLING PROJECT	04/2012	246.07	03/2019	785.22	06/2019	490.29
21	CHENGANNUR-CHINGAVANAM	04/2006	191.72	N.A.	369.83	06/2019	447.03
22	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	04/1999	895.00	03/2007	1,731.78	06/2019	1,566.57
23	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	04/1998	271.24	N.A.	520.00	06/2019	468.58
24	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	04/2010	309.44	12/2015	614.11	06/2019	529.27
25	AUNRIHAR MANDUADIH	03/2012	199.75	08/2018	378.26	06/2019	287.33

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
26	BHOJIPUR TANAKPUR VIA PILIBHIT	03/2008	195.64	N.A.	435.00	06/2019	450.62
27	AMRAVATI-NARKHER NL(CR)	06/1994	663.01	06/1999	858.96	06/2019	726.33
28	KENDRI-DHANTARI INCLUDING ABHANPUR-RAJIM	04/2011	1,471.93	03/2022	543.93	06/2019	0.00
29	CHHINDWARA-MANDLA FORT GC	03/2011	556.54	03/2012	1,342.46	06/2019	0.00
30	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	11/2001	624.47	02/2016	3,550.00	06/2019	3,376.08
31	MANDHANA - BRAHMAWART NEW LINE PROJECT.	04/1997	609.04	04/1999	1,807.88	06/2019	1,806.84
32	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	04/1997	233.00	04/1999	318.42	06/2019	349.37
33	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	02/2005	241.00	03/2014	241.88	06/2019	293.37
34	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION.	02/2006	208.00	03/2012	231.58	06/2019	206.20
35	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING	02/2003	199.55	03/2009	330.32	06/2019	238.61
36	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	02/2005	600.00	03/2010	780.00	06/2019	673.80
37	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	02/2000	200.84	03/2014	503.99	06/2019	394.51
38	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	04/2008	829.74	03/2015	1,216.00	06/2019	823.85
39	MIRAJ-LONDA	03/2015	1,830.00	N.A.	1,190.92	06/2019	254.57
40	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	06/2005	749.69	06/2019	0.00
41	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	04/1995	631.78	12/2012	1,195.00	06/2019	762.72
42	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	04/2006	369.90	03/2010	1,581.53	06/2019	891.24
43	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	03/2002	625.30	06/2007	876.00	06/2019	848.84
44	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER)	04/1999	744.71	N.A.	1,126.79	06/2019	917.49
45	AGARTALA SABROOM, NL, NEFR	04/2008	1,142.00	03/2014	3,407.00	06/2019	3,354.18
46	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	04/2009	396.04	N.A.	400.00	06/2019	225.18
47	MUNIRABAD (GINGERA) -RAICHUR NL	04/2007	179.65	N.A.	1,350.91	12/2023	940.47
48	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	04/2009	259.51	02/2012	533.59	06/2019	148.37
49	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	09/2006	343.17	N.A.	1,120.00	06/2019	1,110.44
50	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	03/1998	280.00	N.A.	1,220.00	06/2019	942.28
51	JIND-SONEPAT (NL),NR	01/2004	238.56	03/2012	790.00	06/2019	785.75

<u>List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above</u> (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>WATER RESOURCES</u>						
52	PAGLADIYA DAM PROJECT	01/2001	542.90	12/2007	1,187.00	06/2019	0.00

TABLE-25

<u>List of projects added Rs.150 Crore and above</u>					(June 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	SRP OC-II EXPANSION PROJECT	11/2016	272.73	/	272.73	-
2	RAMPURAM SHAFT BLOCK	8/2016	431.92	/	431.92	-
3	SRAVANAPALLI OPENCAST PROJECT	2/2018	412.70	/	412.70	-
4	SEMARIA OPENCAST PROJECT	5/2019	396.58	3/2026	396.58	3/2026
	<u>PETROLEUM</u>					
5	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY	8/2016	154.84	11/2019	154.84	11/2019
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
6	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	392.33	3/2018	392.33	11/2019
7	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	160.00	9/2021	160.00	9/2021
8	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	197.37	2/2014	197.37	12/2019
9	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	367.44	1/2017	367.44	1/2017
10	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH - 167 HAGARI JADECHERLA SECT	8/2016	175.20	1/2017	175.20	1/2019
11	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	166.67	9/2017	166.67	9/2017
12	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	175.50	2/2017	175.50	2/2017
13	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	159.97	6/2019	159.97	6/2019
14	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	159.70	7/2018	159.70	7/2018
15	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	191.60	10/2018	191.60	10/2018
16	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF	12/2017	297.30	1/2019	297.30	1/2019

<u>List of projects added Rs.150 Crore and above</u>					(June 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	MUDIGERE TO KADUR SECTION OF NH-					
17	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	325.86	10/2018	325.86	10/2018
18	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	329.01	2/2017	329.01	2/2017
19	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	396.96	3/2017	396.96	3/2017
20	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	314.90	3/2017	314.90	3/2017
21	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	159.12	1/2016	159.12	5/2019
22	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	165.67	1/2016	165.67	5/2019
23	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	171.60	5/2018	171.60	5/2020
24	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	471.16	8/2014	471.16	8/2016
25	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	291.49	8/2017	291.49	8/2019
26	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	157.32	5/2019	157.32	5/2021
	URBAN DEVELOPMENT					
27	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	790.79	6/2021	800.00	6/2021

TABLE-26

Milestones (Cumulative due & achieved) Rs.150 Crore and above

Total	5321
Achieved up to month	2712

TABLE-27

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(June 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) NLC	5,907.11	7,080.41	12/2015	09/2019	12/2019	3
2	BAROUD OC EXPANSION (RCE)- 3MTY SECL	258.56	258.56	03/2016	03/2019	03/2020	12
	<u>FERTILISERS</u>						
3	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY RCF	197.79	209.44	11/2016	07/2019	08/2019	1
	<u>STEEL</u>						
4	CENTRAL DISPATCH YARD RINL	320.66	320.66	08/2018	06/2019	07/2019	1
5	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) RINL	465.85	465.85	07/2018	06/2019	07/2019	1
6	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	23,140.00	05/2015	10/2019	07/2020	9
	<u>PETROLEUM</u>						
7	FIELD DEVELOPMENT OF NELP BLOCK KG- ONN-2003, NAGAYALANKA-KG ONGC	420.76	420.76	09/2018	06/2019	07/2019	1
8	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV ONGC	3,660.71	3,740.05	04/2021	04/2021	05/2021	1
9	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	06/2019	08/2019	2
10	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE MANGALORE REFIN	135.00	170.70	03/2019	05/2019	08/2019	3
11	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE IOCL	890.00	887.00	10/2019	06/2019	10/2019	4
12	HALDIA LPG IMPORT FACILITY BPCL	694.00	694.00	10/2018	06/2019	11/2019	5
13	BSVI UPGRADATION MANGALORE REFIN	1,810.00	1,810.00	12/2019	02/2020	07/2020	5
	<u>POWER</u>						

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(June 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP PGCIL	268.80	340.88	03/2018	06/2019	07/2019	1
15	SOUTHERN REGION STRENGTHENING SCHEME-XXI PGCIL	562.25	562.25	03/2019	06/2019	07/2019	1
16	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI PGCIL	608.24	608.24	04/2019	06/2019	07/2019	1
17	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI PGCIL Central Sector Projects	3,654.00	3,654.00	04/2019	06/2019	07/2019	1
18	KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL	1,779.29	2,187.32	11/2008	06/2019	08/2019	2
19	BUXAR THERMAL POWER PLANT (1320 MW) SJVN	436.68	602.44	12/2016	05/2019	07/2019	2
20	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA PGCIL	844.64	844.64	04/2019	06/2019	08/2019	2
21	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	546.36	11/2016	12/2019	03/2020	3
22	TANDA TPP STAGE-II (2X660 MW) NTPC	9,188.98	9,188.98	07/2019	03/2020	06/2020	3
23	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTRIC PGCIL	808.63	808.63	01/2018	12/2019	03/2020	3
24	DARLIPALLI STPP STAGE-I (2X800 MW) NTPC	12,532.44	13,740.53	12/2018	02/2020	06/2020	4
25	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,598.98	11/2020	02/2021	06/2021	4
26	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	06/2019	10/2019	4
27	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I PGCIL	374.63	374.63	04/2016	06/2019	12/2019	6
28	MUNPL-MEJA TPP - JV (2X660 MW) NTPC Joint Venture	9,750.89	12,176.28	02/2018	08/2019	06/2020	10
	<u>RAILWAYS</u>						
29	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND SER	148.77	377.00	12/2016	09/2019	11/2019	2
30	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING SER	258.20	358.68	N.A.	01/2020	06/2020	5
31	KATNI - SINGRAULI DOUBLING PROJECT WCR	1,763.93	1,763.93	03/2020	10/2021	03/2022	5

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(June 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
32	KATNI GRADE SEPARATOR/BYE PASS WCR	582.13	1,247.64	03/2022	03/2022	09/2022	6
33	GONDIA-JABALPUR(GC),(SECR) SECR	511.86	1,756.92	04/2020	04/2020	12/2020	8
34	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	27,949.00	11/2002	03/2021	12/2021	9
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) RVNL	133.41	385.00	03/2009	03/2019	12/2019	9
36	3RD LINE BETWEEN BHUSAWAL-JALGAON CR	184.06	305.00	03/2019	03/2019	12/2019	9
37	JHARSUGUDA-BILASPUR 4TH LINE SECR	1,973.00	1,973.66	03/2021	03/2021	12/2021	9
38	GEVRA ROAD PENDRA ROAD IRCON	2,288.00	4,970.11	03/2022	03/2022	12/2022	9
39	HAJIPUR - BACHAWARA ECR	678.54	678.54	03/2019	03/2020	02/2021	11
40	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) MRTPT	495.44	2,973.73	03/2004	03/2020	03/2021	12
41	AHMEDNAGAR-PARLI VAIJNATH(NL) CR CR	2,271.50	3,712.50	03/2021	03/2021	03/2022	12
42	MANOHARABAD-KOTHPALL NEW LINE(SCR) SCR	1,160.48	1,160.48	03/2010	03/2022	03/2023	12
43	RATLAM-MHOW-KHANDWA-AKOLA (GC) WR	3,503.69	3,860.40	03/2022	03/2022	03/2023	12
44	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) WR	829.74	1,310.23	03/2020	03/2020	03/2021	12
45	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) WR	1,640.04	1,640.04	03/2022	03/2022	03/2023	12
46	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA SER	651.00	1,009.00	03/2015	03/2024	03/2025	12
47	KALYAN-KASARA 3RD LINE CR	792.89	792.89	03/2021	03/2021	03/2022	12
48	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I SCR	2,132.77	2,132.77	03/2014	03/2023	03/2024	12
49	SAMBALPUR-TALCHER DOUBLING ECR	1,111.99	1,539.28	02/2019	03/2021	03/2022	12
50	WARDHA-BALHARSHAH - 3RD LINE (132 KM) CR	1,272.19	1,272.19	03/2022	03/2022	03/2023	12
51	MANMAD - JALGAON - 3RD LINE (160 KM) CR	1,035.16	1,035.16	03/2022	03/2023	03/2024	12
52	WARDHA - NAGPUR - 4TH LINE (76 KM) CR	637.95	637.95	03/2023	03/2023	03/2024	12
53	JAGADALPUR-KORAPUT DOUBLING ECR	1,547.38	1,547.38	03/2022	03/2022	03/2023	12

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(June 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
54	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. ECR	1,172.92	1,172.92	12/2018	03/2021	03/2022	12
55	SURENDRA NAGAR RAJKOT WR	1,002.39	1,002.39	03/2021	03/2020	03/2021	12
56	KATNI-BINA 3RD LINE (263 KM) WCR	2,478.23	2,478.23	03/2022	03/2022	03/2023	12
57	INDORE-DEWAS-UJJAIN (80 KMS) WR	700.00	603.69	06/2020	06/2020	06/2021	12
58	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM WR	691.84	663.29	03/2020	03/2020	03/2021	12
59	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE ECR	1,491.47	1,491.47	03/2020	10/2021	12/2022	14
60	BHAIRABI SAIRONG, NL, NEFR NFR	2,393.47	5,021.45	03/2014	12/2020	03/2022	15
61	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING SR	760.00	1,182.31	03/2020	03/2020	06/2021	15
62	WADSA-GADHCHIROLI NEW LINE (52.36 KM) SECR	229.00	860.92	12/2021	12/2021	03/2023	15
63	MUNEERABAD-MAHABOONNAGAR(NL),SCR SCR	1,723.00	2,542.75	03/2000	03/2019	03/2021	24
64	RAMGANJMUHDI-BHOPAL (NL),WCR WCR	424.60	2,909.99	03/2021	03/2021	03/2023	24
65	KISHANGANJ JALALGARH, NL, NEFR NFR	333.76	360.00	N.A.	03/2020	03/2022	24
66	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC ECR	548.00	785.87	03/2020	03/2020	03/2022	24
67	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR NFR	221.42	380.00	N.A.	03/2020	03/2022	24
68	WARDHA-SEWAGRAM NGP 3RD LINE CR	540.02	540.02	03/2022	03/2022	03/2024	24
69	NADIKUDE-SRI KALAHASTI SCR	2,288.70	2,288.70	03/2021	03/2022	03/2024	24
70	BHADRAK - NERGUNDI 3RD LINE ECR	843.04	843.04	10/2020	03/2021	03/2023	24
71	KAZIPET-BALHRSHA SCR	2,063.03	2,063.03	03/2021	03/2021	03/2023	24
72	BARDHAMAN-KATWA (GC) ER	1,106.62	1,536.44	12/2010	12/2017	03/2020	27
73	KHURDA ROAD-BOLANGIR(NL)ECOR ECR	2,923.13	3,798.80	03/2009	06/2021	12/2023	30
74	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) NCR	2,912.96	3,845.60	03/2022	03/2022	12/2024	33

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(June 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
75	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	1,188.91	1,670.01	03/2019	03/2022	03/2025	36
76	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) WR	318.24	321.62	03/2012	03/2019	03/2022	36
77	PIRPAINTI-JASIDIH ER	915.98	2,137.81	03/2022	03/2022	03/2025	36
78	KIRANDUL - JAGDALPUR DOUBLING ECOR	1,160.00	1,160.83	03/2020	03/2020	03/2023	36
79	KORAPUT - SINGAPUR ROAD DOUBLING ECOR	2,361.74	2,361.74	03/2022	03/2022	03/2025	36
80	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL IRCON	5,200.00	1,700.43	03/2020	03/2020	06/2023	39
81	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL ER	277.28	328.75	03/2016	03/2020	03/2025	60
82	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL ER	499.96	726.95	02/2012	12/2013	03/2025	135
83	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 ER	923.52	1,218.71	03/2016	02/2010	03/2025	181
84	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG ER	406.99	575.65	03/2006	01/2006	03/2025	230
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
85	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 NHAI	199.81	385.13	04/2009	06/2019	07/2019	1
86	PUNE-SATARA(NH-4) NHAI PPP (BOT)	1,724.55	1,724.55	03/2013	06/2019	07/2019	1
87	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T NHAI	804.97	804.97	06/2018	12/2019	01/2020	1
88	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) NHAI	1,532.62	1,532.62	03/2021	03/2021	04/2021	1
89	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 PWD	279.70	398.52	08/2017	06/2019	07/2019	1
90	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 PWD	178.23	178.23	09/2018	06/2019	07/2019	1


List of projects reporting additional delayed Rs.150 Crore and above							(June 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
91	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 NHAI	1,387.11	1,387.11	11/2017	05/2019	07/2019	2
92	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP NHDP BOT (TOLL)	410.72	410.72	04/2015	06/2019	08/2019	2
93	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 NHAI	248.97	248.97	05/2019	08/2019	11/2019	3
94	BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	217.61	04/2010	04/2019	08/2019	4
95	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 NHAI PPP (BOT)	1,535.00	1,535.00	05/2014	06/2019	10/2019	4
96	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION NHAI	997.15	997.15	03/2019	03/2019	07/2019	4
97	FOUR LANING OF BARHI-HAZARIBAGH NH-33 NHAI	323.72	323.72	08/2018	08/2019	01/2020	5
98	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM NHAI	328.67	328.67	N.A.	06/2019	11/2019	5
99	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	06/2019	12/2019	6
100	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 NHAI PPP (BOT)	1,266.60	1,544.00	09/2016	06/2019	12/2019	6
101	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S MORTH	282.08	282.08	06/2019	06/2019	12/2019	6
102	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT NHAI	1,995.34	1,995.34	N.A.	05/2021	11/2021	6
103	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) NHAI	709.00	709.00	09/2017	05/2019	12/2019	7
104	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 NHAI PPP (BOT)	972.50	972.50	07/2017	12/2018	07/2019	7
105	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER NHAI	946.00	946.00	06/2018	04/2019	12/2019	8
106	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) NHAI	726.67	726.67	04/2018	06/2019	02/2020	8
107	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A NHDP EPC	390.51	390.51	N.A.	06/2019	03/2020	9

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(June 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
108	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION NHAI	479.00	479.00	N.A.	06/2019	03/2020	9
109	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION NHAI PPP (BOT)	923.04	923.04	11/2016	06/2019	05/2020	11
110	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN NHAI	181.78	181.78	N.A.	06/2019	06/2020	12
111	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (NHAI	531.13	531.13	05/2018	05/2019	06/2020	13
112	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 NHAI	505.00	505.00	05/2018	04/2019	05/2020	13
113	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D NHAI	414.51	414.00	05/2018	03/2019	06/2020	15
114	DELHI/ HARYANA BORDER TO ROHTAK NHAI PPP (BOT)	486.00	486.00	05/2010	10/2018	03/2020	17
115	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 NHAI	593.26	593.26	05/2018	04/2019	12/2020	20
	<u>TELECOMMUNICATIONS</u>						
116	MADHYA PRADESH ACCESS (LOT1) BSNL Central Sector Projects	215.30	219.60	05/2018	06/2019	07/2019	1
	<u>URBAN DEVELOPMENT</u>						
117	PUNE METRO RAIL PROJECT (PHASE 1) MMRC	11,420.00	11,420.00	11/2021	11/2021	12/2021	1
118	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA CPWD	156.57	156.57	08/2016	07/2019	10/2019	3
119	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD CPWD	209.84	209.84	03/2020	03/2020	05/2021	14


TABLE-28

<u>Sector wise analysis of projects Rs.150 Crore and above</u>					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	718,79.00	80,348.00	44,910.74
CIVIL AVIATION	1	314.61	3,14.61	441.33	85.79
COAL	102	1,01,584.05	1,027,57.35	1,02,037.39	34,533.21
FERTILISERS	5	1,299.07	12,99.07	1,310.72	494.66
MINES	5	7,078.62	70,78.62	7,078.62	585.89
STEEL	14	32,793.01	329,38.41	40,195.41	23,602.88
PETROLEUM	150	2,47,891.38	2,534,10.80	2,55,071.46	89,795.86
POWER	75	2,77,523.99	3,027,01.94	3,51,070.74	2,11,507.55
HEAVY INDUSTRY	2	3,272.00	52,81.30	5,281.30	3,517.13
HEALTH AND FAMILY WELFARE	20	8,129.23	81,29.23	8,246.52	3,239.95
RAILWAYS	320	4,64,773.55	5,498,90.62	6,70,541.38	1,81,731.32
ROAD TRANSPORT AND HIGHWAYS	831	4,92,220.43	4,935,23.16	5,07,134.63	2,33,897.96
SHIPPING AND PORTS	8	10,757.29	104,28.79	11,199.74	3,046.68
TELECOMMUNICATIONS	5	16,310.53	163,23.13	27,553.13	9,169.02
URBAN DEVELOPMENT	62	1,75,890.06	1,764,32.75	1,82,113.88	78,238.37
WATER RESOURCES	2	10,384.61	103,84.61	55,782.44	16,450.19
DEFENCE PRODUCTION	2	453.64	4,54.00	453.64	214.19
Grand total	1608	19,17,796.07	20,43,227.39	23,05,860.33	9,35,021.39

Graphical Presentation of All Projects w.r.t. Original Schedule

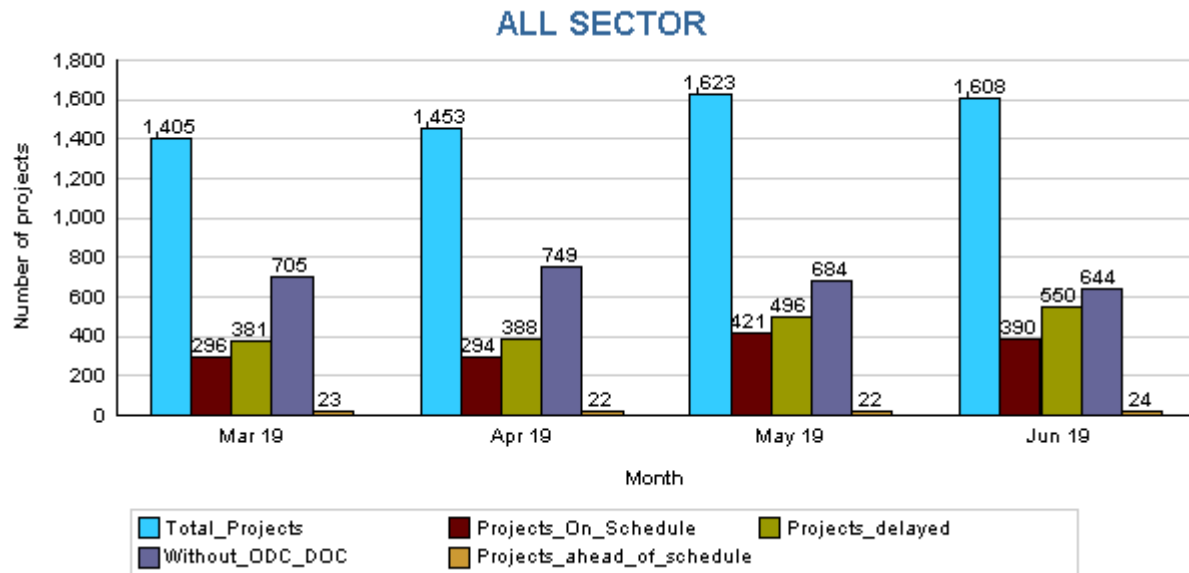


Break-up of 550 Delayed projects in June 2019

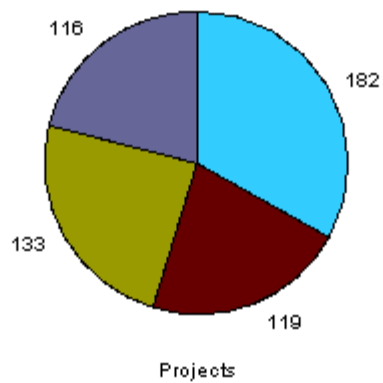


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

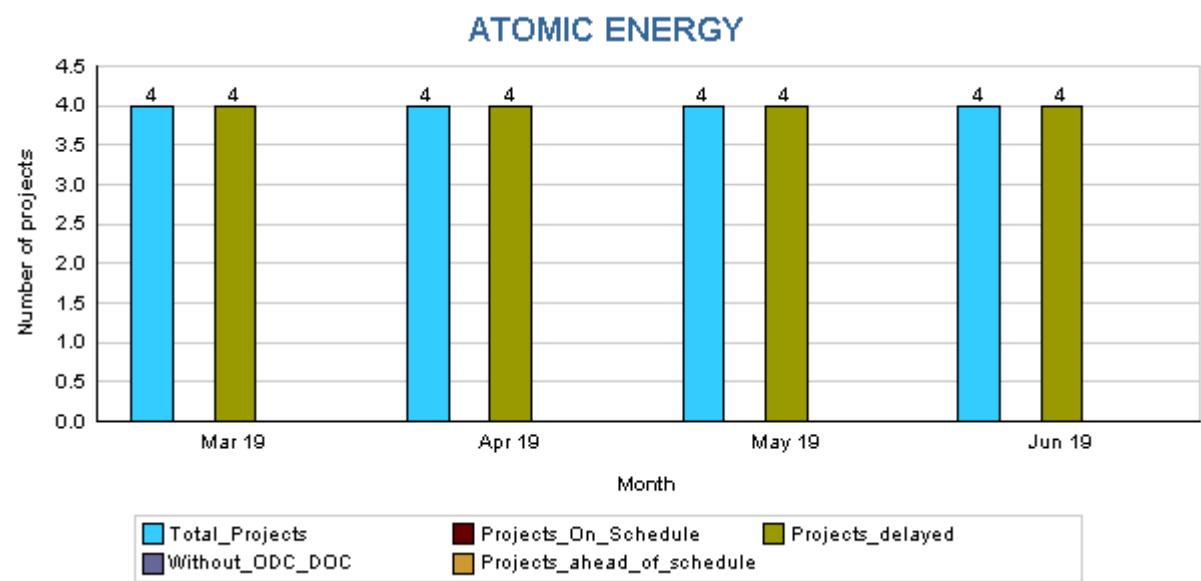

Break-up of 550 Delayed projects in June 2019

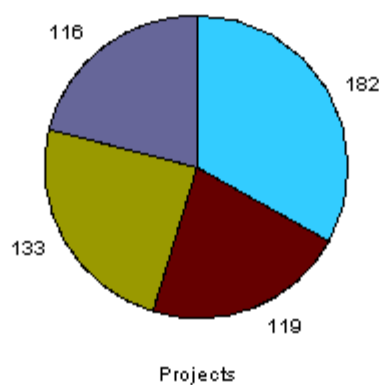


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- 60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule



Break-up of 550 Delayed projects in June 2019

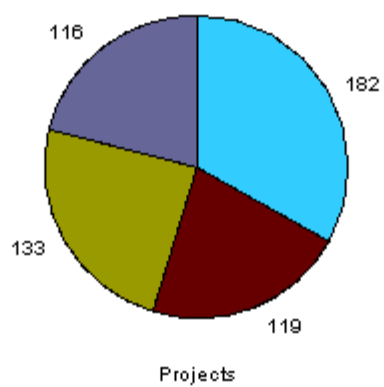

Delay in Months


1-12

13-24


25-60

60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

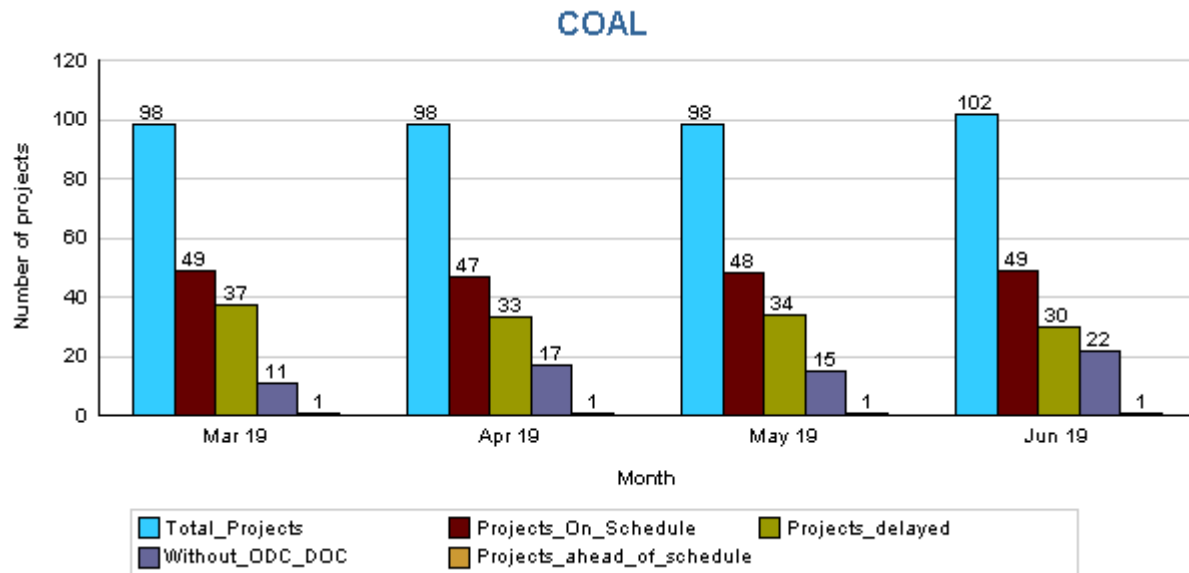


Break-up of 550 Delayed projects in June 2019

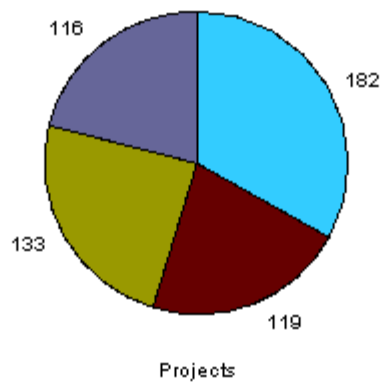


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

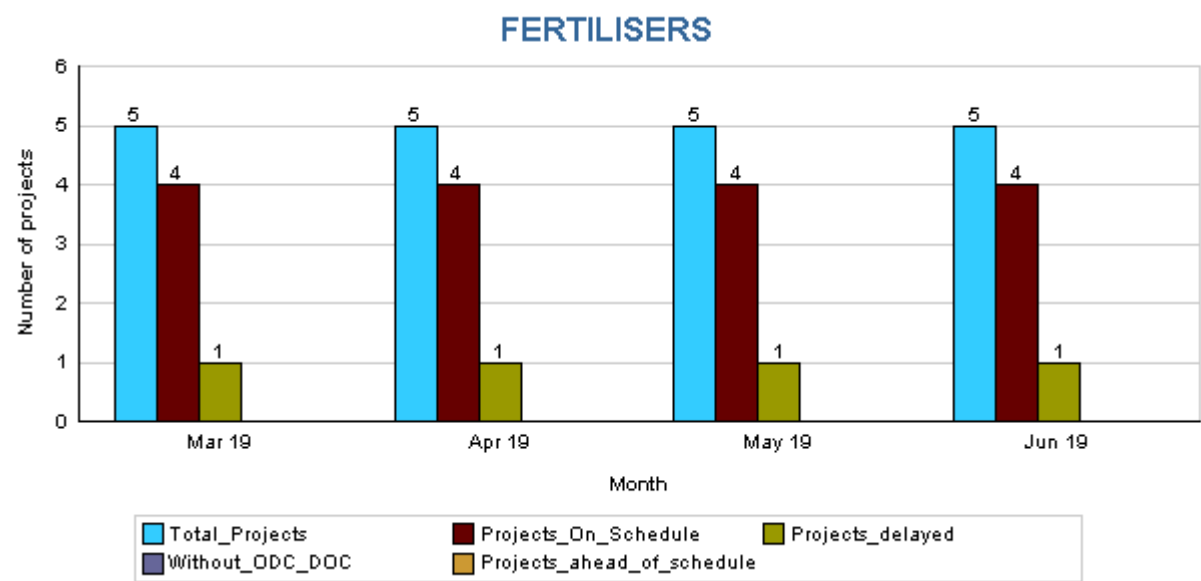


Break-up of 550 Delayed projects in June 2019

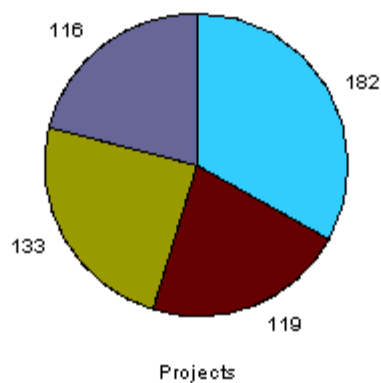


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

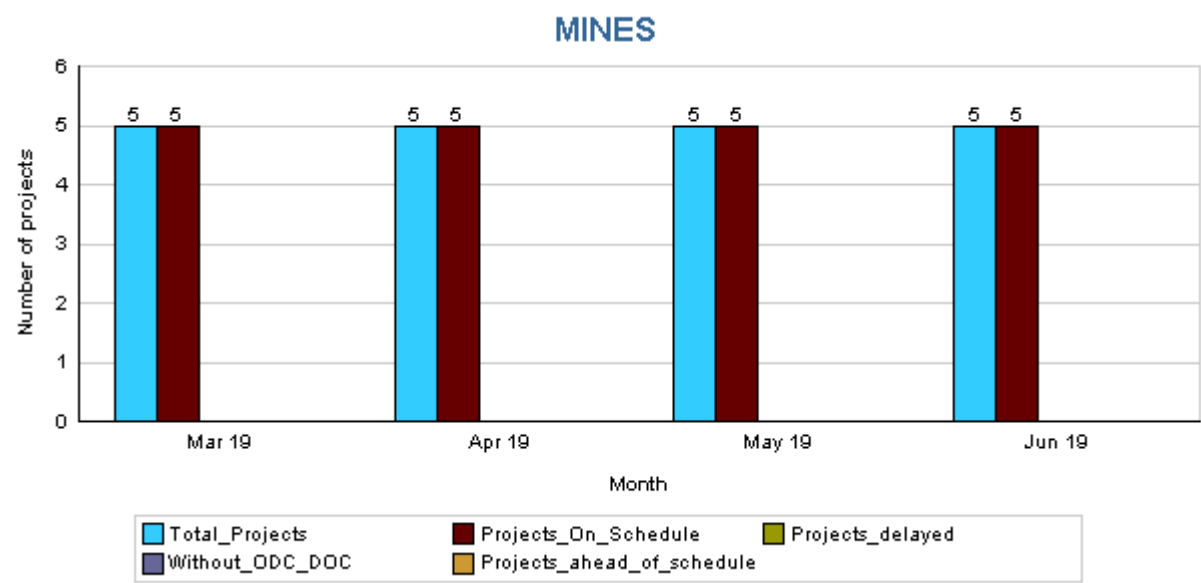


Break-up of 550 Delayed projects in June 2019

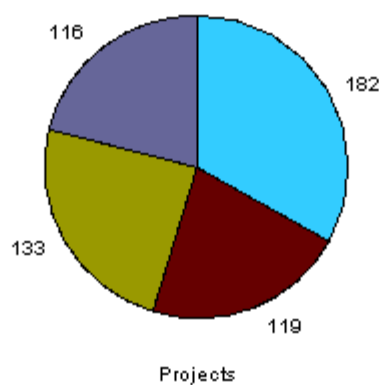


Delay in Months

Delay in Months	Projects
1-12	182
13-24	119
25-60	133
60 and Above	116

Graphical Presentation of All Projects w.r.t. Original Schedule

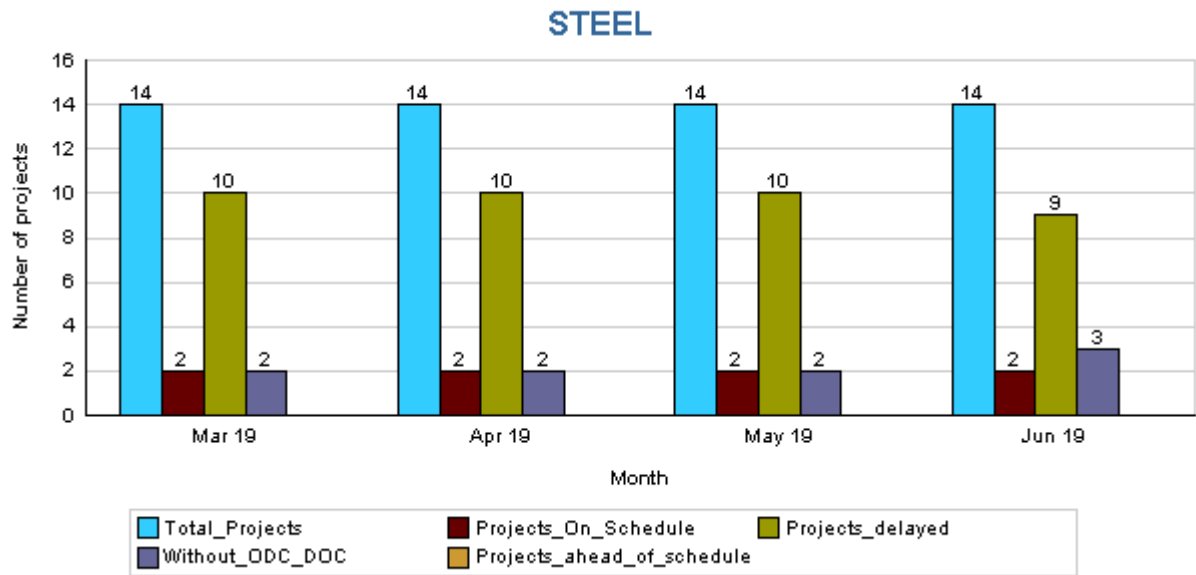


Break-up of 550 Delayed projects in June 2019

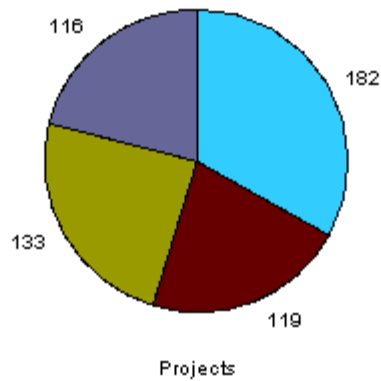


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

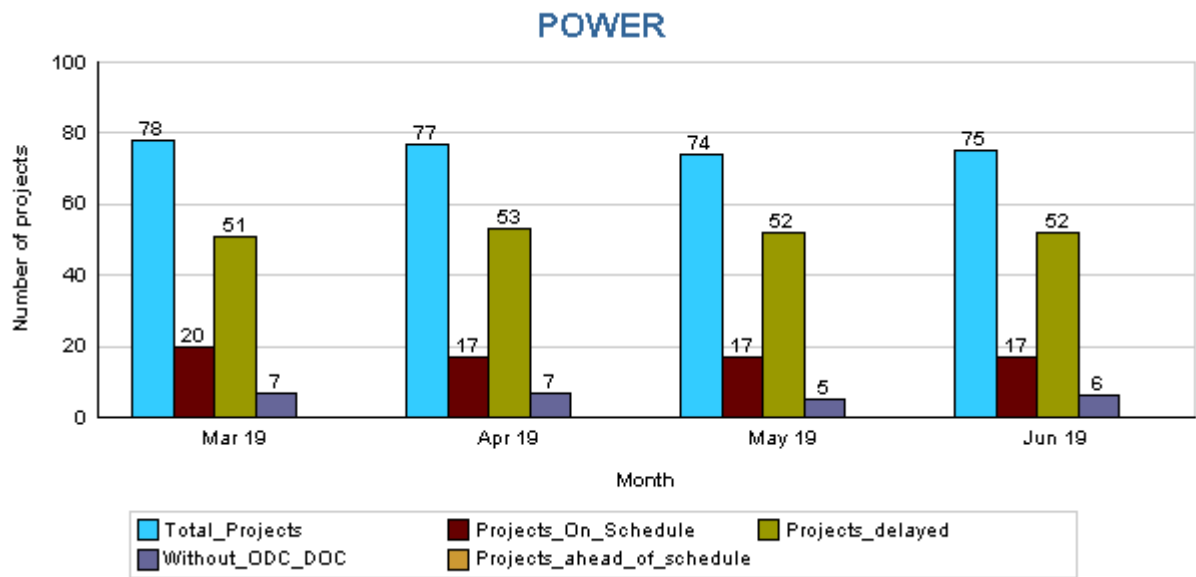


Break-up of 550 Delayed projects in June 2019

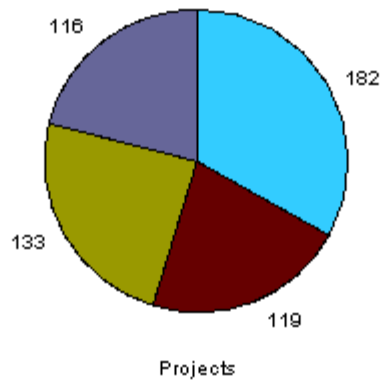


Delay in Months 1-12 13-24 25-60 60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

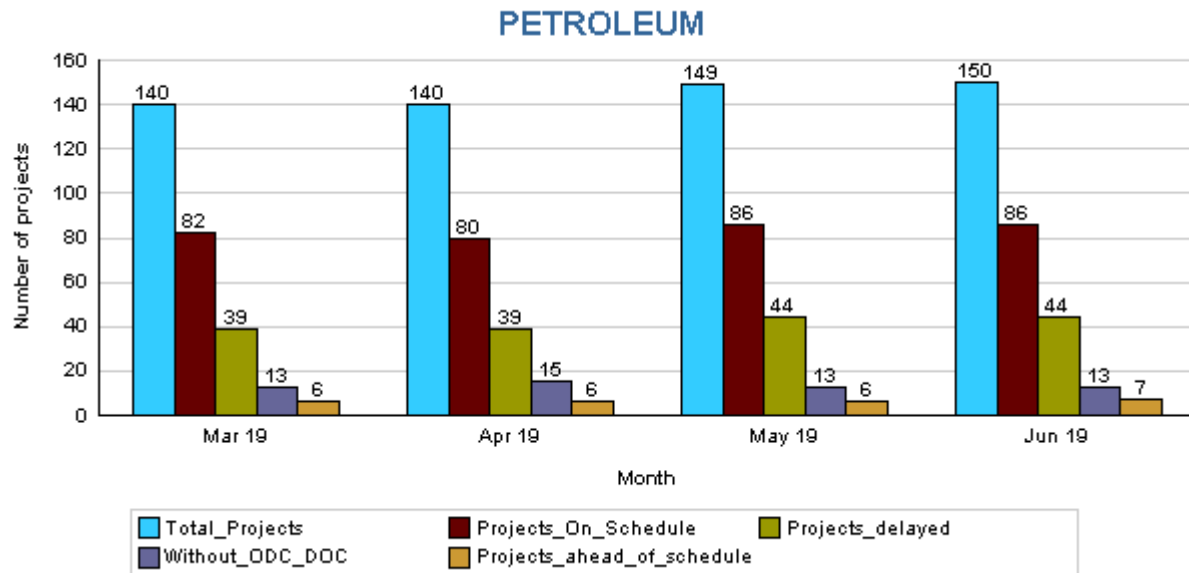


Break-up of 550 Delayed projects in June 2019

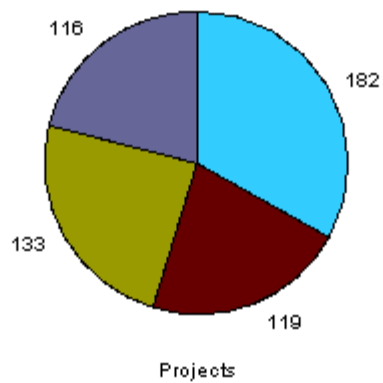


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

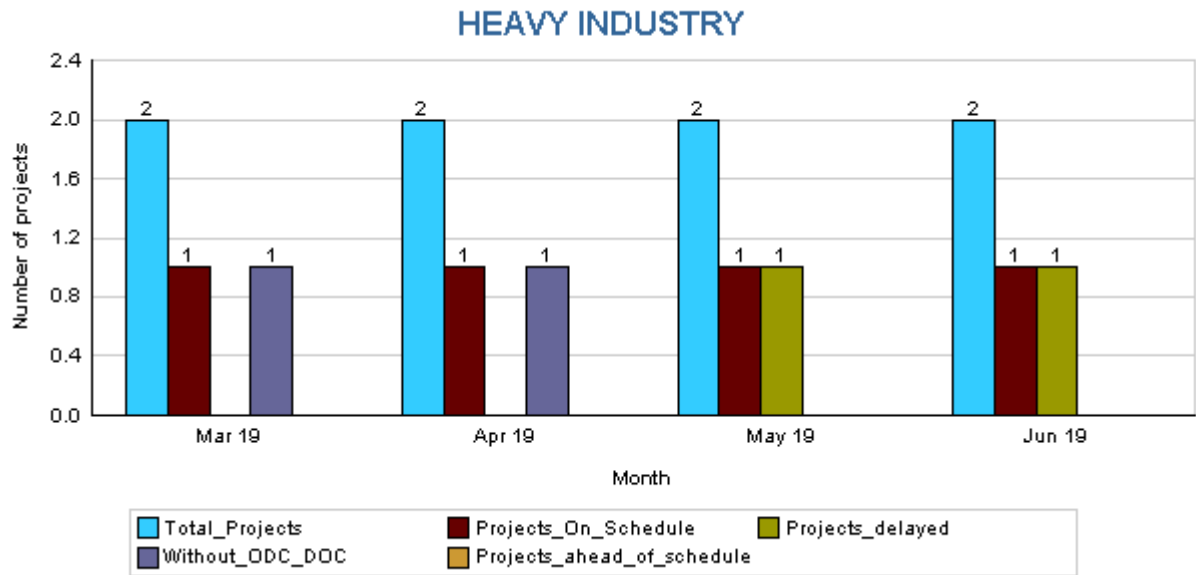


Break-up of 550 Delayed projects in June 2019

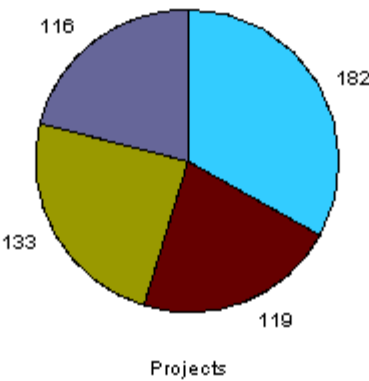


Delay in Months

Delay in Months	Count
1-12	182
13-24	119
25-60	133
60 and Above	116

Graphical Presentation of All Projects w.r.t. Original Schedule

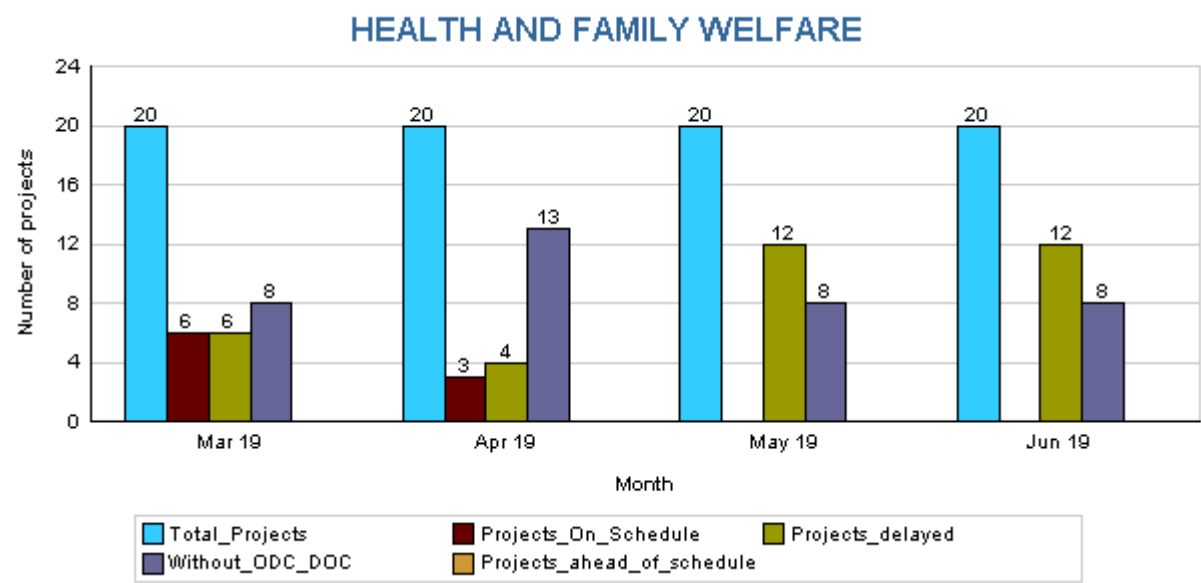


Break-up of 550 Delayed projects in June 2019

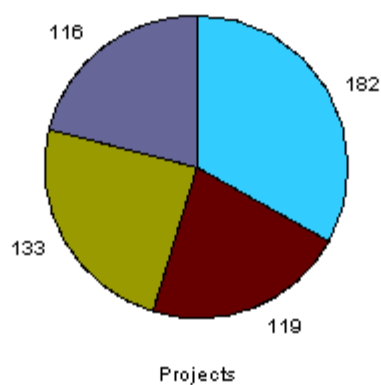


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

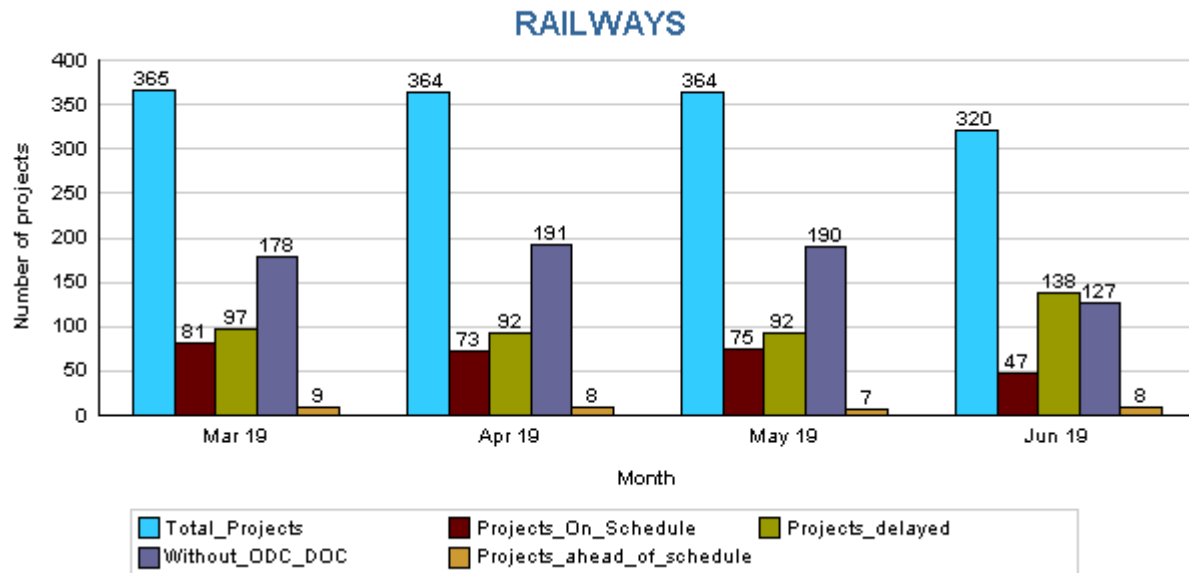


Break-up of 550 Delayed projects in June 2019

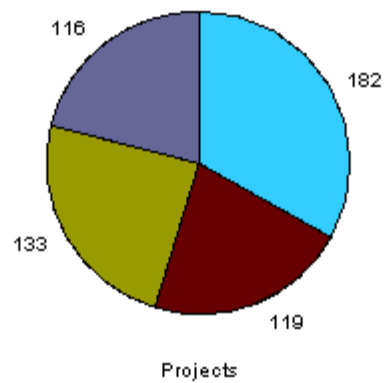


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

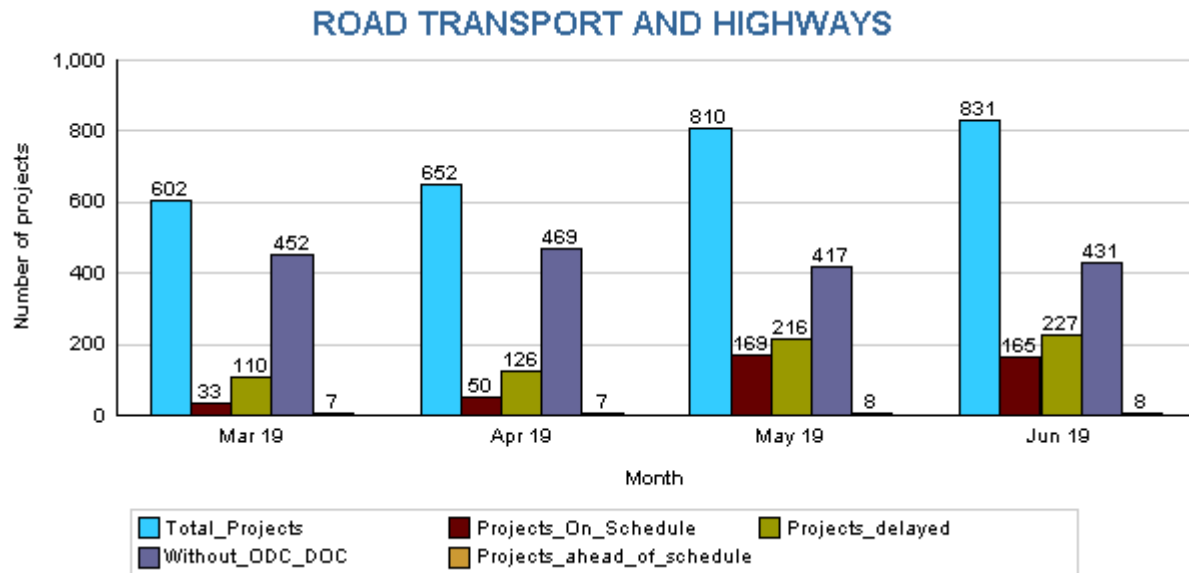


Break-up of 550 Delayed projects in June 2019

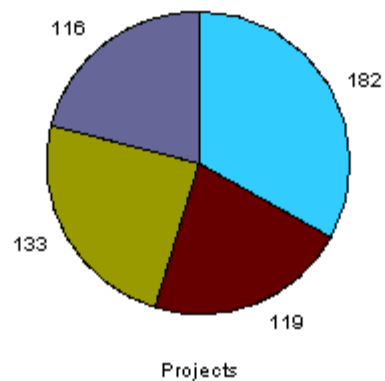


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

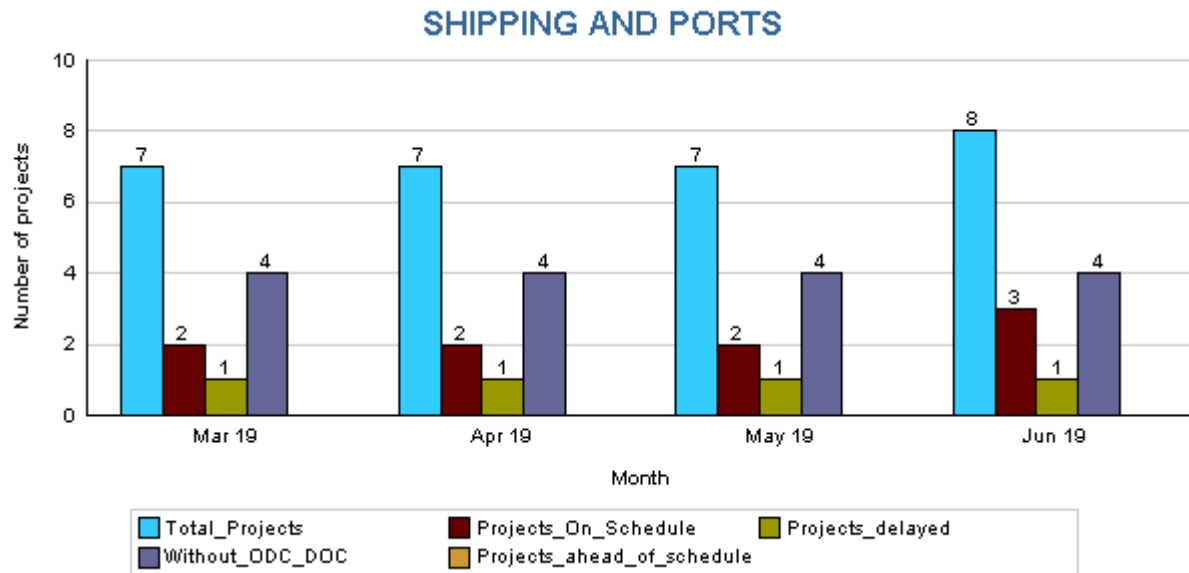


Break-up of 550 Delayed projects in June 2019

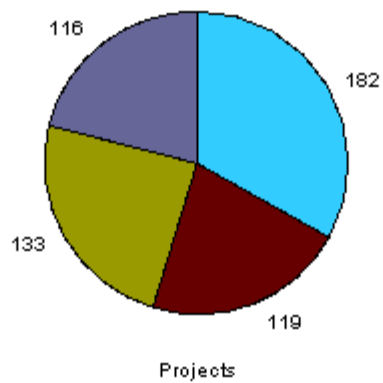


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

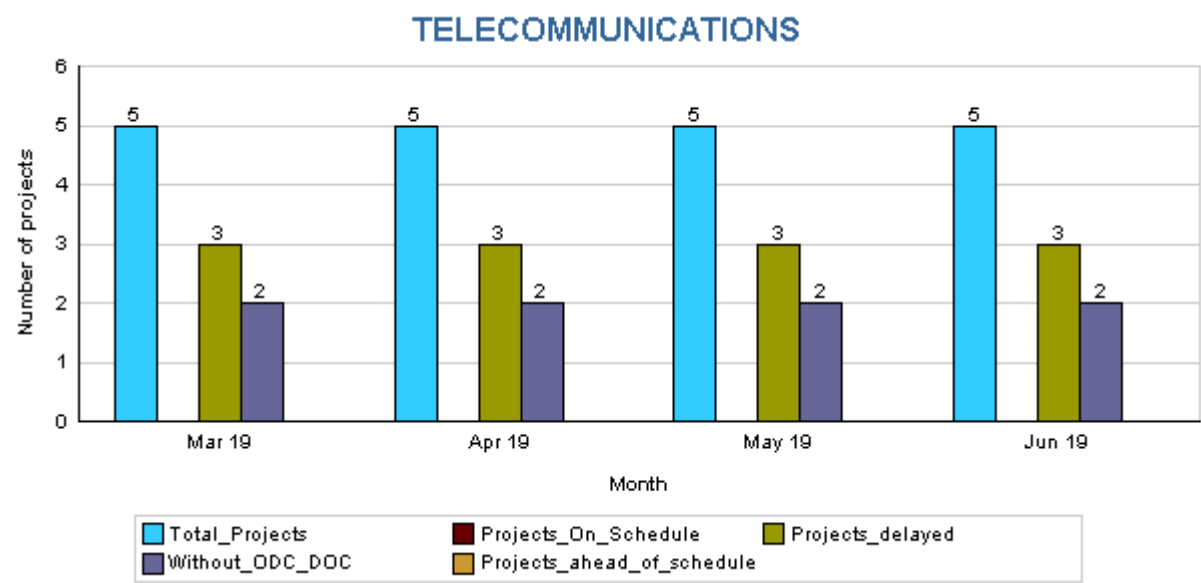


Break-up of 550 Delayed projects in June 2019

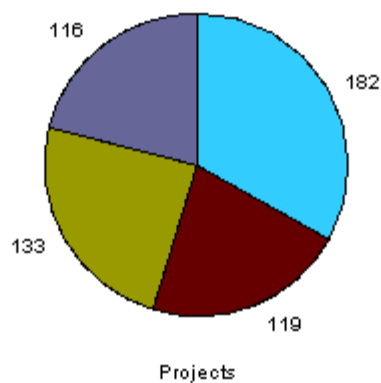


Delay in Months

Delay in Months	Number of Projects
1-12	182
13-24	119
25-60	133
60 and Above	116

Graphical Presentation of All Projects w.r.t. Original Schedule

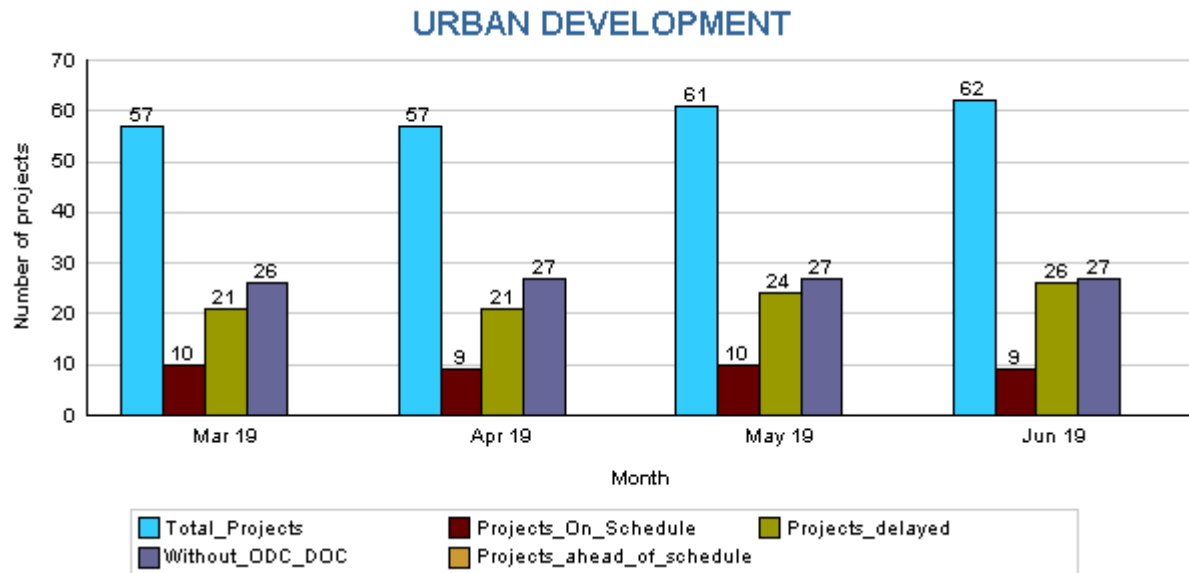


Break-up of 550 Delayed projects in June 2019

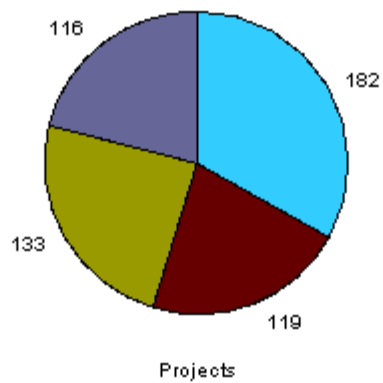


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

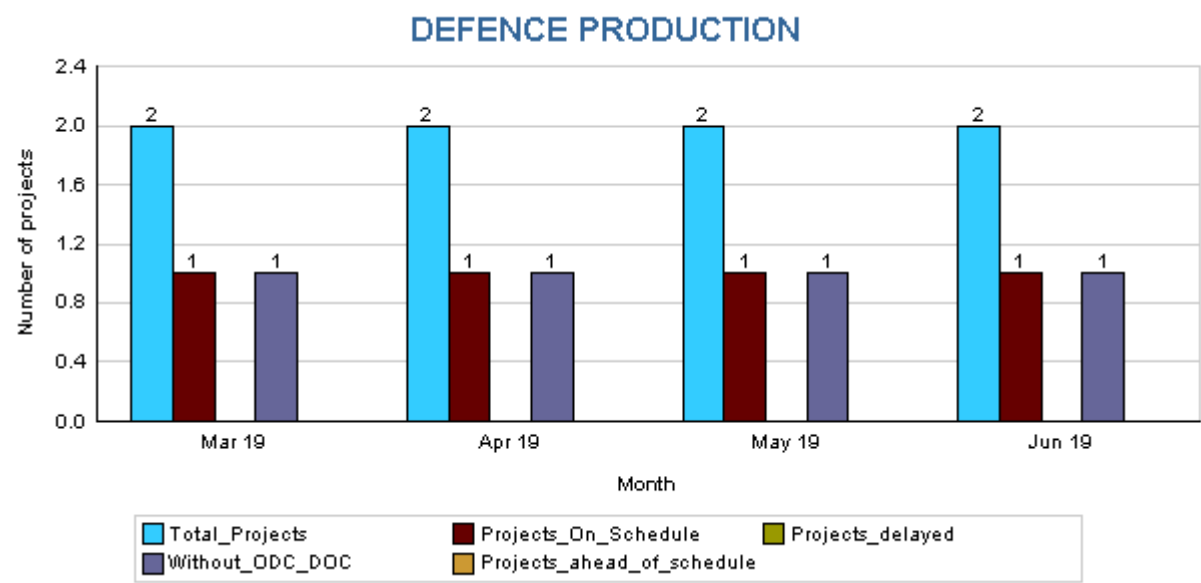

Break-up of 550 Delayed projects in June 2019

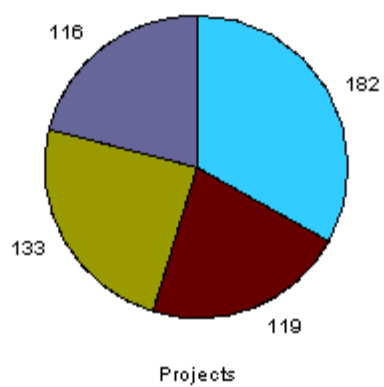

Delay in Months



TABLE-29

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	13,711.00	12/2015 -	06/2020	54(O) -	52/70
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 17,079.00	17,079.00	10,993.00	12/2016 -	12/2020	48(O) -	40/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	14,422.00	11/2020 -	11/2023	36(O) -	23/76
	Total		67,120.00 -	80,348.00	44,910.74				198/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
	Total		314.61 -	441.33	85.79				0/0
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,902.94	03/2023 -	03/2023	0(O) -	14/19
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,057.87	03/2023 -	03/2023	0(O) -	7/21
8	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.29	03/2023 -	03/2023	0(O) -	1/12
9	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 -	459.49	203.90	03/2015 -	03/2020	60(O) -	6/10
10	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	2/8
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	207.04	03/2014 -	03/2021	84(O) -	0/5
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.15	03/2016 -	-	-	7/9
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	172.88	03/2016 -	03/2020	48(O) -	4/7
14	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	88.29	03/2022 -	03/2022	0(O) -	2/10
15	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	80.33	03/2020 -	03/2020	0(O) -	5/9
16	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	51.66	03/2018 -	-	-	1/7

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	67.40	03/2020 -	03/2020	0(O) -	1/6
18	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	3.94	03/2023 -	03/2023	0(O) -	1/11
19	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	1/5
20	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
21	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/1
22	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	0/1
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	336.64	07/2012 -	03/2022	116(O) -	5/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120(O) -	4/6
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,	12/2007	179.87 -	179.87	163.23	03/2012 -	07/2019	88(O) -	5/6
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	179.87	03/2012 -	03/2021	108(O) -	5/6
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	359.23	03/2016 -	03/2021	60(O) -	5/6
28	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	89.82	03/2014 -	03/2021	84(O) -	6/6
29	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	- -	4/7
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	354.29	04/2015 -	04/2019	- -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	186.88	03/2020 -	03/2020	0(O) -	6/7
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.24	03/2021 -	03/2021	0(O) -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	- -	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	228.71	05/2014 -	04/2018	- -	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	180.52	04/2014 -	04/2018	- -	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	87.14	03/2022 -	03/2022	0(O) -	2/22
37	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	90.13	03/2024 -	03/2024	0(O) -	0/16
38	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021	-24(O) -	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/9
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	115.41	03/2021 -	03/2021	0(O) -	3/10
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	47.59	03/2021 -	03/2021	0(O) -	3/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/8
43	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	26.61	03/2023 -	03/2023	0(O) -	0/4
44	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	112.60	03/2021 -	03/2021	0(O) -	2/5
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	18.45	03/2022 -	03/2022	0(O) -	0/0
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	255.65	03/2021 -	03/2021	0(O) -	0/9
47	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022	0(O) -	0/9
48	SEMARIA OPENCAST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	0/5
49	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	213.24	03/2020 -	03/2020	0(O) -	8/11
50	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020	0(O) -	3/8
51	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	208.78	03/2018 -	03/2018	-	7/7
52	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	409.68	119.73	03/2023 -	03/2023	0(O) -	7/11
53	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	123.60	03/2019 -	03/2019	-	10/13
54	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	121.74	03/2020 -	03/2020	0(O) -	6/10
55	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	168.92	03/2021 -	03/2021	0(O) -	2/6
56	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	258.40	03/2025 -	03/2025	0(O) -	5/13
57	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	17.71	03/2023 -	03/2024	12(O) -	3/10
58	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	313.34	115.28	03/2021 -	03/2024	36(O) -	3/6
59	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	175.30	03/2020 -	03/2020	0(O) -	2/6
60	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	254.72	03/2019 -	-	-	2/9
61	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	153.29	03/2019 -	03/2019	-	2/8
62	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	319.81	03/2020 -	03/2020	0(O) -	0/0
63	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	58.04	03/2022 -	03/2022	0(O) -	0/3
64	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	20.86	03/2022 -	03/2022	0(O) -	1/12
65	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	150.04	03/2021 -	03/2021	0(O) -	1/6
66	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120(O) -	10/10

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10	490.10	493.85	03/2017	03/2020	36(O)	11/12
68	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77	457.77	539.59	03/2013	03/2022	108(O)	8/9
69	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08	172.08	346.99	03/2010	03/2022	144(O)	3/4
70	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28	207.28	241.15	03/2012	03/2021	108(O)	5/7
71	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53	479.53	390.53	03/2013	03/2021	96(O)	6/9
72	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15	479.15	196.26	03/2019	03/2022	36(O)	2/9
73	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36	3,756.36	1,546.73	03/2026	03/2026	0(O)	7/15
74	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66	337.66	183.98	03/2019	03/2020	12(O)	5/6
75	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03	289.03	75.79	03/2018	03/2020	24(O)	4/6
76	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38	1,375.38	437.89	03/2021	03/2021	0(O)	6/9
77	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75	2,434.75	82.60	03/2027	03/2027	0(O)	2/12
78	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87	2,838.87	1,111.70	03/2029	03/2029	0(O)	0/9
79	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45	522.45	9.88	09/2019	09/2019	0(O)	0/0
80	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63	513.63	175.30	12/2019	12/2019	0(O)	0/0
81	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11	7,080.41	6,451.65	12/2015	12/2019	48(O)	30/35
82	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17	709.06	439.27	06/2015	09/2019	51(O)	5/7
83	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03	448.86	232.81	03/2012	03/2024	144(O)	35/42
84	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63	453.63	121.91	12/2012	-	-	11/44
85	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97	489.62	331.25	03/2012	03/2023	132(O)	0/2
86	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78	209.78	154.02	03/2015	03/2019	-	30/31
87	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19	181.19	170.60	03/2012	-	-	6/6
88	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29	164.04	115.71	03/2015	07/2019	52(O)	2/5
89	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76	349.28	7.01	03/2015	03/2021	72(O)	4/29
90	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06	473.22	69.93	03/2015	09/2017	-	8/13
91	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01	365.01	132.04	06/2015	12/2015	-	35/36

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	86.94	07/2016 -	04/2017	-	24/28
93	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	181.91	03/2016 -	12/2016	-	38/39
94	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	78.30	03/2019 -	09/2017	-	15/18
95	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24(O) -	0/9
96	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020	0(O) -	5/17
97	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	53.00	03/2019 -	03/2022	36(O) -	1/11
98	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	.00	-	-	-	0/6
99	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA ,	08/2016	431.92 -	431.92	.00	-	-	-	0/9
100	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA ,	02/2018	412.70 -	412.70	.00	-	-	-	0/7
101	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	6,531.52	11/2021 -	11/2021	0(O) -	0/0
102	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	308.29	03/2022 -	03/2022	0(O) -	9/13
103	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	460.96	03/2018 -	03/2020	24(O) -	11/16
104	RANGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	2,661.73	258.98	08/2019 -	08/2019	0(O) -	0/19
105	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/21
106	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	.00	03/2029 -	03/2029	0(O) -	0/22
107	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.00	03/2027 -	03/2027	0(O) -	0/26
	Total		1,01,584.05 -	1,02,037.39	34,533.21				511/1103
	<u>FERTILISERS</u>								
108	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	72.95	11/2019 -	11/2019	0(O) -	0/2
109	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 -	209.44	159.41	11/2016 -	08/2019	33(O) -	1/13
110	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	92.10	04/2020 -	04/2020	0(O) -	1/14
111	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	88.74	11/2019 -	11/2019	0(O) -	0/2

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	81.46	11/2019 -	11/2019	0(O) -	0/2
	Total		1,299.07 -	1,310.72	494.66				2/33
	<u>MINES</u>								
113	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	102.61	04/2021 04/2021	04/2021	0(O) 0	3/3
114	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	316.08	01/2020 01/2020	01/2020	0(O) 0	1/2
115	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020	0(O) -	2/2
116	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.30	04/2021 04/2021	04/2021	0(O) 0	1/1
117	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 -	166.62	134.98	06/2019 -	06/2019	0(O) -	1/1
	Total		7,078.62 -	7,078.62	585.89				8/9
	<u>STEEL</u>								
118	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 488.40	488.40	254.29	10/2016 03/2021	03/2021	53(O) 0	1/2
119	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,277.76	12/2017 09/2019	09/2019	21(O) 0	5/6
120	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	199.91	08/2018 07/2019	07/2019	11(O) 1	2/4
121	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	390.25	07/2018 07/2019	07/2019	12(O) 1	4/4
122	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	136.74	04/2015 -	-	-	4/5
123	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	23,140.00	15,729.80	05/2015 07/2020	07/2020	62(O) 9	64/86
124	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020	0(O) -	5/12
125	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	431.23	10/2017 06/2020	06/2020	32(O) 0	0/2
126	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	922.73	12/2017 06/2019	06/2019	18(O) 0	1/2
127	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	110.95	09/2017 -	-	-	0/0
128	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	99.65	06/2019 06/2020	06/2020	12(O) 0	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
129	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,872.84	04/2018 05/2019	05/2019	-	3/3
130	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,144.53	09/2018 09/2019	09/2019	12(O) 0	4/5
131	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	.60	09/2020 -	09/2020	0(O) -	0/4
	Total		32,793.01 -	40,195.41	23,602.88				93/136
	<u>PETROLEUM</u>								
132	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	4,913.36	07/2020 -	07/2020	0(O) -	81/111
133	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	359.31	09/2019 -	09/2019	0(O) -	24/27
134	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	2,670.11	06/2020 -	08/2021	14(O) -	15/20
135	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
136	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
137	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 -	420.76	193.15	09/2018 07/2019	07/2019	10(O) 1	3/5
138	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	73.31	04/2021 -	04/2020	-12(O) -	0/0
139	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	74.36	04/2021 -	07/2021	3(O) -	0/0
140	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	13.97	04/2022 -	02/2023	10(O) -	0/0
141	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021	0(O) -	0/0
142	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	27.71	02/2021 -	02/2021	0(O) -	0/16
143	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81(O) 0	6/15
144	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 -	345.92	139.45	01/2014 -	11/2019	70(O) -	6/7
145	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	244.44	08/2019 -	09/2019	1(O) -	5/13
146	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,498.18	11/2019 -	11/2019	0(O) -	13/17

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
147	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 265.49	265.49	145.01	05/2020 -	05/2020	0(O) -	4/5
148	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8(O) -	0/0
149	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	460.33	09/2019 -	09/2019	0(O) -	6/7
150	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	682.90	6.12	02/2020 -	02/2020	0(O) -	1/14
151	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	101.40	02/2020 -	02/2020	0(O) -	1/5
152	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	224.75	3.30	08/2020 -	08/2020	0(O) -	0/0
153	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
154	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	822.02	11/2018 -	07/2019	8(O) -	8/8
155	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	564.33	12/2020 -	02/2020	-10(O) -	4/5
156	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	147.63	06/2020 -	03/2020	-3(O) -	3/4
157	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	8.19	03/2021 -	03/2021	0(O) -	10/26
158	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020	0(O) -	2/2
159	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	58.27	10/2022 -	10/2022	0(O) -	0/0
160	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	6.71	01/2021 -	01/2021	0(O) -	2/8
161	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	125.80	03/2021 -	03/2021	0(O) -	0/0
162	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR ,	06/2017	951.64 -	951.64	300.50	10/2019 -	10/2019	0(O) -	9/11
163	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021	0(O) -	0/0
164	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,780.91	05/2019 10/2019	10/2019	5(O) 0	13/14
165	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	135.09	04/2018 -	08/2019	16(O) -	18/20
166	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	1,162.56	354.67	03/2026 -	03/2026	0(O) -	7/10
167	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	105.30	07/2020 -	07/2020	0(O) -	10/10

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
168	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL, GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	-	-	0/0
169	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL, GUJARAT ,	08/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020	0(O) -	1/1
170	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL, GUJARAT ,	03/2018	3,380.00 -	3,380.00	1,824.73	09/2019 -	09/2019	0(O) -	7/9
171	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL, GUJARAT ,	10/2017	906.00 -	906.00	75.19	02/2020 -	10/2020	8(O) -	4/8
172	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL, GUJARAT ,	03/2018	588.20 -	588.20	.94	-	-	-	6/17
173	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL, GUJARAT ,	09/2018	225.54 -	225.54	.00	02/2021 -	02/2021	0(O) -	2/8
174	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL, HARYANA ,	11/2017	255.00 -	255.00	58.20	11/2020 -	11/2020	0(O) -	18/46
175	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL, HARYANA ,	04/2018	206.63 -	206.63	6.82	02/2020 -	02/2020	0(O) -	3/6
176	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL, HARYANA ,	12/2017	3,529.00 -	3,529.00	1,453.91	07/2019 -	07/2019	0(O) -	7/9
177	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL, HARYANA ,	08/2018	1,636.00 -	1,636.00	161.68	08/2020 -	08/2020	0(O) -	3/6
178	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL, HARYANA ,	01/2019	909.00 -	909.00	13.11	01/2021 -	01/2021	0(O) -	0/0
179	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL, HARYANA ,	10/2018	598.00 -	598.00	13.44	02/2020 -	02/2020	0(O) -	3/4
180	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL, HARYANA ,	08/2018	286.42 -	286.42	.99	08/2020 -	08/2020	0(O) -	5/16
181	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL, HARYANA ,	12/2018	278.60 -	278.60	.00	06/2021 -	06/2021	0(O) -	0/3
182	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL, HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	147.35	09/2019 -	06/2019	-3(O) -	4/4
183	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND ,	04/2011	191.96 -	191.96	76.28	05/2015 -	-	-	8/12
184	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC, JHARKHAND ,	12/2015	658.62 -	910.23	303.30	03/2023 03/2022	03/2022	-12(O) 0	6/10
185	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL, JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	06/2020	0(O) -	0/0
186	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL, JHARKHAND ,	10/2017	226.45 -	226.45	42.87	10/2022 -	10/2022	0(O) -	9/17
187	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL, JHARKHAND ,	10/2017	221.45 -	221.45	40.86	10/2022 -	10/2022	0(O) -	0/0
188	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	0(O) -	0/0
190	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	185.00	164.61	04/2019 06/2019	10/2018	-	8/8
191	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	152.13	03/2019 -	08/2019	5(O) -	11/11
192	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	643.05	12/2019 07/2020	07/2020	7(O) 5	8/9
193	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	621.00	66.19	03/2020 04/2020	09/2020	6(O) 0	2/3
194	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	.30	03/2021 -	03/2021	0(O) -	0/0
195	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	354.84	10/2017 -	-	-	39/52
196	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 -	5,245.96	3,283.70	08/2018 -	11/2019	15(O) -	0/20
197	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 -	3,288.96	816.62	02/2020 -	10/2020	8(O) -	0/20
198	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,112.00	467.00	06/2019 -	06/2020	12(O) -	0/0
199	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	14.14	03/2023 -	03/2023	0(O) -	0/0
200	PROVISION OF 2ND SPUR FOR TWL GANTRY TWO FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	21.97	06/2020 -	08/2020	2(O) -	0/0
201	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 -	1,683.06	1,265.01	05/2013 12/2019	12/2019	79(O) 0	4/8
202	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,906.55	03/2015 12/2019	05/2019	-	14/18
203	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 -	5,296.93	4,748.30	04/2019 12/2019	12/2019	8(O) 0	8/9
204	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	2,185.47	03/2019 05/2020	05/2020	14(O) 0	4/5
205	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	4,313.38	12/2017 03/2020	03/2020	27(O) 0	4/5
206	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,180.79	04/2018 05/2020	05/2020	25(O) 0	13/15

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
207	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	887.73	08/2021 -	08/2021	0(O) -	4/5
208	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	315.44	02/2020 -	02/2020	0(O) -	0/10
209	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	153.11	12/2019 -	12/2019	0(O) -	0/17
210	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	28.55	01/2021 -	04/2021	3(O) -	0/0
211	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	20.85	01/2021 -	10/2021	9(O) -	0/0
212	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	27.66	01/2021 -	01/2021	0(O) -	0/0
213	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	2,068.39	03/2020 -	03/2020	0(O) -	104/135
214	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 565.15	565.15	425.96	11/2019 03/2020	03/2020	4(O) 0	4/5
215	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 -	511.30	406.35	11/2019 -	11/2019	0(O) -	4/5
216	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 -	1,033.95	833.51	11/2019 -	11/2019	0(O) -	4/5
217	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,475.92	2,555.11	05/2021 12/2021	12/2021	7(O) 0	11/15
218	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	105.42	08/2020 -	08/2020	0(O) -	0/15
219	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	58.33	06/2020 -	06/2020	0(O) -	0/0
220	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	434.78	12/2019 -	12/2019	0(O) -	4/5
221	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,292.46	45.81	05/2021 -	05/2021	0(O) -	0/0
222	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 -	3,228.80	370.84	03/2022 -	03/2022	0(O) -	0/0
223	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 05/2021	05/2021	1(O) 1	0/0
224	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	05/2019	2,494.68 -	2,494.68	.00	12/2021 -	12/2021	0(O) -	0/0
225	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 -	3,397.00	2,707.26	12/2018 -	06/2019	6(O) -	39/39
226	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 -	-	-	8/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
227	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	678.31	10/2014 08/2019	08/2019	58(O) 0	34/40
228	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	224.72	03/2017 -	12/2019	33(O) -	2/15
229	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	759.67	12/2020 -	12/2020	0(O) -	4/5
230	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	1,649.57	12/2020 -	08/2020	-4(O) -	4/5
231	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	598.85	10/2019 -	10/2019	0(O) -	5/6
232	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	256.76	07/2018 -	10/2020	27(O) -	23/36
233	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	1,386.04	06/2020 -	06/2020	0(O) -	18/24
234	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	82.95	10/2020 -	10/2020	0(O) -	6/12
235	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	142.82	12/2019 -	12/2019	0(O) -	6/22
236	LAYING OF VIJAIIPUR-AURAIYA PIPELINE SECTION OF VIJAIIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,237.86	12/2020 -	12/2020	0(O) -	19/24
237	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	1,327.89	12/2020 -	12/2020	0(O) -	16/24
238	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	1,248.16	12/2020 -	12/2020	0(O) -	17/24
239	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	3,049.47	2,291.18	12/2012 -	02/2022	110(O) -	18/42
240	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	600.15	03/2021 -	03/2021	0(O) -	8/26
241	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
242	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	935.94	12/2021 -	12/2021	0(O) -	10/20
243	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,740.12	09/2017 -	07/2019	22(O) -	6/6
244	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	988.14	12/2020 -	12/2020	0(O) -	18/24
245	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	300.23	01/2019 -	12/2019	11(O) -	6/6
246	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	36.68	12/2019 -	12/2019	0(O) -	17/26

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
247	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL, ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	45.20	07/2022 -	07/2022	0(O) -	0/0
248	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL, ODISHA ,	08/2017	315.00 -	315.00	109.28	12/2021 -	12/2021	0(O) -	2/3
249	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL, ODISHA ,	07/2017	182.20 -	182.20	25.83	07/2022 -	07/2022	0(O) -	0/0
250	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL, ODISHA ,	04/2018	5,654.00 -	5,654.00	240.73	10/2021 -	10/2021	0(O) -	2/10
251	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL, ODISHA ,	08/2017	750.00 -	750.00	32.69	12/2020 -	12/2020	0(O) -	0/14
252	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL, ODISHA ,	10/2018	1,297.50 -	1,297.50	7.18	10/2021 -	10/2021	0(O) -	0/1
253	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL, ODISHA ,	11/2018	462.30 -	462.30	.00	09/2021 -	09/2021	0(O) -	0/0
254	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL, ODISHA ,	05/2019	3,361.00 -	3,361.00	269.74	08/2021 -	08/2021	0(O) -	2/11
255	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
256	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN ,	03/2018	229.80 -	229.80	69.10	-	03/2021	-	5/26
257	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
258	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.00	11/2015 -	-	-	52/52
259	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU ,	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56(O) -	0/0
260	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU ,	11/2015	390.52 -	390.52	367.94	03/2019 -	05/2020	14(O) -	4/5
261	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	444.28	12/2018 -	02/2021	26(O) -	4/5
262	AUGMENTATION OF CTMPL - [N16000286]IOCL, TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	6.64	06/2020 -	06/2020	0(O) -	4/5
263	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	848.87	12/2019 -	12/2019	0(O) -	0/0
264	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU ,	08/2017	421.00 -	421.00	100.28	08/2020 -	08/2020	0(O) -	0/0
265	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL, TAMIL NADU ,	12/2017	466.43 -	466.43	25.99	10/2020 -	08/2021	10(O) -	0/0
266	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL, TELANGANA ,	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022	0(O) -	0/0
267	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL, UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	116.05	04/2022 -	04/2022	0(O) -	32/43
268	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH ,	08/2017	318.80 -	318.80	37.30	08/2021 -	11/2021	3(O) -	0/0
269	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL, UTTAR PRADESH ,	01/2018	666.64 -	666.64	374.07	09/2019 -	09/2019	0(O) -	5/6

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
270	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	.44	08/2020 -	08/2020	0(O) -	1/1
271	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	10.40	12/2021 -	12/2021	0(O) -	2/3
272	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH ,	03/2014	204.00 -	204.00	132.24	09/2019 -	09/2019	0(O) -	0/6
273	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	13.10	12/2021 -	12/2021	0(O) -	0/0
274	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH ,	08/2016	154.84 -	154.84	104.23	11/2019 -	11/2019	0(O) -	0/0
275	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	38.51	02/2020 -	10/2020	8(O) -	18/26
276	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 -	694.00	671.48	10/2018 -	11/2019	13(O) -	0/15
277	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
278	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	157.26	12/2020 -	12/2020	0(O) -	12/24
279	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	44.00	04/2020 -	03/2021	11(O) -	17/26
280	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	1,409.29	09/2019 -	09/2019	0(O) -	10/11
281	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	33.85	09/2022 -	06/2021	-15(O) -	1/1
	Total		2,47,891.38 -	2,55,071.46	89,795.86				1044/1713
	POWER								
282	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,868.18	09/2010 -	-	-	0/0
283	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,419.34	7,419.34	7,327.76	12/2009 08/2019	08/2019	116(O) 0	30/30
284	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	16,182.14	10/2011 08/2021	08/2021	118(O) 0	26/47
285	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	9,996.59	7,816.71	07/2012 -	09/2020	98(O) -	12/25
286	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	13,589.31	05/2018 06/2019	07/2019	14(O) -13	33/45
287	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	05/2015	436.68 -	602.44	561.74	12/2016 -	07/2019	31(O) -	16/19
288	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	12,104.40	10/2017 03/2020	03/2020	29(O) 0	35/41

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
289	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,595.15	11/2019 -	11/2019	0(O) -	0/0
290	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	405.65	05/2017 06/2019	12/2019	31(O) 0	4/9
291	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	332.00	331.46	11/2017 -	04/2019	-	4/4
292	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	92.78	09/2018 09/2019	09/2019	12(O) 0	0/0
293	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3(O) -	0/0
294	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,997.11	7,399.82	09/2009 -	12/2021	147(O) -	3/5
295	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,135.82	04/2020 -	12/2023	44(O) -	0/0
296	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	8,852.51	06/2019 09/2019	09/2021	27(O) 0	22/23
297	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,268.00	10/2017 -	-	-	0/0
298	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	18,668.00	1,780.00	03/2023 -	03/2023	0(O) -	0/1
299	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10(O) -	0/0
300	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	11,322.86	01/2018 03/2020	03/2020	26(O) 0	39/42
301	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	8,127.53	01/2020 -	01/2020	0(O) -	32/39
302	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	298.76	09/2020 -	09/2020	0(O) -	9/16
303	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
304	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
305	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 12/2019	12/2019	86(O) 0	8/11
306	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022	103(O) 0	23/26
307	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019	63(O) 0	10/12
308	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 08/2019	08/2019	40(O) 0	8/12
309	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 374.63	374.63	210.72	04/2016 03/2017	12/2019	44(O) 6	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
310	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 -	546.36	465.21	11/2016 12/2019	03/2020	40(O) 3	8/12
311	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 5,151.37	5,151.37	3,115.72	03/2018 12/2019	12/2019	21(O) 0	9/12
312	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 -	225.28	162.30	02/2016 04/2019	06/2019	40(O) 0	16/17
313	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 -	340.88	251.33	03/2018 03/2019	07/2019	16(O) 1	1/3
314	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	548.30	10/2017 09/2019	09/2019	23(O) 0	0/5
315	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	190.80	07/2017 06/2019	08/2019	25(O) 0	3/5
316	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	81.97	03/2018 03/2018	08/2019	17(O) 0	0/0
317	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	513.85	01/2018 12/2019	03/2020	26(O) 3	0/0
318	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4(O) -	0/0
319	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019	0(O) -	0/0
320	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	392.96	03/2019 03/2019	07/2019	4(O) 1	0/0
321	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	185.94	06/2019 -	06/2019	0(O) -	0/0
322	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	187.60	11/2019 11/2019	11/2019	0(O) 0	0/0
323	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	266.03	01/2019 09/2019	09/2019	8(O) 0	0/0
324	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	407.79	04/2019 04/2019	07/2019	3(O) 1	0/0
325	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	116.76	02/2020 02/2020	02/2020	0(O) 0	0/0
326	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	153.70	02/2019 06/2019	08/2019	6(O) 0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
327	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	117.15	06/2019 06/2019	10/2019	4(O) 4	0/0
328	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	52.63	12/2019 12/2019	12/2019	0(O) 0	0/0
329	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020	0(O) -	0/0
330	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	84.17	06/2019 -	07/2019	1(O) -	0/0
331	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12(O) -	0/0
332	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 12/2018	12/2020	24(O) 0	0/0
333	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,308.50	04/2019 -	07/2019	3(O) -	0/0
334	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020	0(O) -	0/0
335	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020	0(O) -	0/0
336	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5(O) -	0/0
337	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020	0(O) -	0/0
338	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	9,298.78	12/2018 06/2020	06/2020	18(O) 4	33/38
339	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	430.71	04/2019 04/2019	08/2019	4(O) 2	0/0
340	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	1,011.38	01/2019 -	07/2019	6(O) -	0/0
341	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	2,237.45	11/2008 06/2019	08/2019	129(O) 2	20/22
342	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2(O) -	0/0
343	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	4,988.68	11/2020 06/2021	06/2021	7(O) 4	23/23
344	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	6,271.59	07/2019 06/2020	06/2020	11(O) 3	32/35
345	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 -	294.60	292.85	02/2014 -	10/2019	68(O) -	7/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
346	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	9,645.00	02/2018 06/2020	06/2020	28(O) 10	33/40
347	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	503.39	09/2023 -	09/2023	0(O) -	0/0
348	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020	0(O) -	0/0
349	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	125.00	11/2020 -	11/2020	0(O) -	0/0
350	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 -	5,024.35	2,935.92	02/2016 -	06/2022	76(O) -	16/30
351	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,025.80	03/2013 12/2020	12/2020	93(O) 0	6/15
352	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,397.80	1,697.38	06/2013 -	12/2022	114(O) -	10/13
353	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.16	08/2017 -	-	-	0/15
354	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	222.91	12/2021 -	12/2021	0(O) -	3/32
355	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,592.34	443.47	09/2019 02/2022	02/2022	29(O) 0	5/9
356	EASTERN REGION STRENGTHENING SCHEME-XV - [N180000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	287.52	04/2018 01/2020	01/2020	21(O) 0	0/0
	Total		2,77,523.99 -	3,51,070.74	2,11,507.55				580/782
	HEAVY INDUSTRY								
357	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019	0(O) -	0/0
358	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 3,727.30	3,727.30	3,182.10	09/2011 06/2019	03/2020	102(O) 0	23/25
	Total		3,272.00 -	5,281.30	3,517.13				23/25
	HEALTH AND FAMILY WELFARE								
359	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7(O) -	0/0
360	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	85.04	- -	02/2020	- -	0/0
361	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
362	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5(O) -	0/0
363	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
364	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28(O) -	2/2
365	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27(O) -	3/5
366	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.65	54.94	-	02/2020	-	0/0
367	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	73.40	-	05/2020	-	0/0
368	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	508.29	03/2018 -	-	-	1/2
369	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7(O) -	0/0
370	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	112.97	-	02/2020	-	0/0
371	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16(O) -	0/0
372	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19(O) -	1/1
373	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2(O) -	0/0
374	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	99.26	-	04/2020	-	0/0
375	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2(O) -	0/0
376	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	241.39	09/2018 -	06/2019	9(O) -	0/0
377	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12(O) -	0/0
378	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	112.82	-	02/2020	-	0/0
	Total		8,129.23 -	8,246.52	3,239.95				7/10
	<u>RAILWAYS</u>								
379	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
380	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168(O) -	0/0
381	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	-	-	-	0/0
382	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	-	-	-	1/1
383	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36(O) -	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
384	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	1,235.96	03/2020 -	03/2022	24(O) -	0/0
385	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
386	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12(O) -	0/0
387	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	709.85	12/2023 -	12/2023	0(O) -	0/0
388	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	3,382.95	325.64	03/2022 -	03/2022	0(O) -	0/0
389	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
390	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	5.59	03/2019 -	12/2020	21(O) -	0/0
391	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,532.00	606.19	03/2019 -	03/2020	12(O) -	0/0
392	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 -	700.00	687.37	03/2019 -	03/2019	-	0/0
393	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	571.56	03/2022 -	03/2020	-24(O) -	0/0
394	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	2,136.01	454.63	03/2021 -	03/2021	0(O) -	0/0
395	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 -	1,156.41	1,028.71	03/2012 -	03/2020	96(O) -	0/0
396	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	589.15	303.96	- -	03/2022	-	0/0
397	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.77	1,403.38	- -	03/2023	-	0/0
398	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	389.29	03/2020 -	03/2020	0(O) -	0/0
399	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
400	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	749.00	672.82	03/2012 -	03/2020	96(O) -	0/0
401	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 -	2,145.00	932.80	03/2019 -	03/2020	12(O) -	0/0
402	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.67	- 03/2022	03/2022	- 24	0/0
403	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	2,396.88	.40	- -	03/2023	-	0/0
404	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	2,626.98	.28	- -	03/2024	-	0/0
405	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	2,860.55	1.14	- -	03/2024	-	0/0
406	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	1.91	- -	03/2024	-	0/0
407	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 -	729.92	349.60	- -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
408	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	2,614.36	375.63	-	03/2022	-	0/0
409	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	03/2024	-	0/0
410	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	24.16	-	03/2024	-	0/0
411	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.20	-	03/2024	-	0/0
412	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	-	03/2024	-	0/0
413	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	23.40	-	03/2023	-	0/0
414	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	-	03/2024	-	0/0
415	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	-	03/2024	-	0/0
416	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	356.81	-	03/2021	-	0/0
417	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	785.87	457.46	03/2020	03/2022	24(O)	0/0
418	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	400.17	378.41	-	01/2020	-	0/0
419	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 519.33	519.33	126.80	-	02/2023	-	0/0
420	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	390.91	03/2020	10/2021	19(O)	0/1
421	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	424.98	03/2020	12/2022	33(O)	1/1
422	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	541.07	07/2014	-	-	0/0
423	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	35.10	03/2021	03/2022	12(O)	0/0
424	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	15.39	03/2021	03/2022	12(O)	0/0
425	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	727.29	488.81	-	09/2019	-	0/0
426	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	1,483.14	815.41	-	12/2021	-	0/0
427	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 -	1,160.83	654.74	03/2020	03/2023	36(O)	1/1
428	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,100.00	987.29	03/2020	03/2020	0(O)	0/0
429	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018	-	-	0/0
430	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 1,226.51	1,226.51	1,034.58	12/2019 10/2019	10/2019	-2(O) -2	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
431	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 1,973.66	1,973.66	121.56	03/2021 12/2021	12/2021	9(O) 9	0/1
432	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	619.50	03/2022 12/2022	12/2022	9(O) 9	0/0
433	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 12/2020	12/2020	27(O) 0	0/0
434	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	102.06	- -	03/2024	- -	0/0
435	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	68.13	- -	03/2023	- -	0/0
436	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,215.34	1,310.23	1,294.00	03/2020 03/2021	03/2021	12(O) 12	0/0
437	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120(O) 36	0/0
438	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	404.70	03/2011 03/2017	03/2017	-	0/0
439	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	902.37	12/2021 -	12/2021	0(O) -	0/0
440	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	267.40	03/2021 -	03/2021	0(O) -	0/0
441	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	87.81	- 03/2021	03/2021	- -24	0/0
442	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36(O) 0	0/0
443	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	1,140.64	12/2021 -	12/2021	0(O) -	0/0
444	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 -	160.00	952.24	03/2021 -	03/2019	-	0/0
445	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	348.91	03/2021 03/2021	03/2021	0(O) 12	0/0
446	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9(O) -	0/0
447	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
448	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
449	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
450	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 809.07	809.07	596.89	03/2019 03/2020	03/2020	12(O) 0	0/0
451	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 663.29	663.29	81.64	03/2020 03/2021	03/2021	12(O) 12	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
452	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	694.00	189.71	12/2011 -	03/2021	111(O) -	0/0
453	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	.00	- -	03/2025	- -	0/0
454	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	285.74	03/2019 -	03/2020	12(O) -	0/0
455	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	366.38	12/2026 -	12/2026	0(O) -	0/0
456	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	18,512.58	11/2002 -	12/2021	229(O) -	0/0
457	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,031.00	3,376.00	3,180.37	- -	03/2021	- -	0/0
458	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	456.83	- -	03/2021	- -	0/0
459	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	231.84	- -	06/2020	- -	0/0
460	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019	35(O) 2	0/0
461	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	332.04	03/2021 -	12/2021	9(O) -	0/0
462	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	156.48	03/2021 -	12/2020	-3(O) -	0/0
463	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	144.76	- -	12/2024	- -	0/0
464	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
465	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,801.01	44.36	- -	12/2023	- -	0/0
466	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93(O) -	0/1
467	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	- -	12/2023	- -	0/0
468	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
469	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.35	- -	12/2023	- -	0/0
470	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,541.10	03/2023 -	03/2023	0(O) -	0/1
471	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	12/2023	- -	0/0
472	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72(O) -	0/0
473	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	- -	12/2023	- -	0/0
474	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93(O) -	0/0
475	HUBLI- CHIKAJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12(O) -	0/5
476	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	578.00	509.07	03/2020 -	03/2020	0(O) -	0/2

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
477	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36(O) -	0/0
478	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 2,815.62	2,815.62	262.37	- -	-	-	0/0
479	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 252.96	252.96	8.50	- -	-	-	0/0
480	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 189.24	189.24	6.72	- -	-	-	0/0
481	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 1,431.90	1,431.90	61.69	- 06/2022	-	-	0/0
482	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 828.50	828.50	.08	- -	-	-	0/0
483	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
484	RAMGANJMUUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 2,909.99	2,909.99	1,027.12	03/2021 03/2023	03/2023	24(O) 24	0/14
485	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 1,413.76	1,413.76	1,309.02	- 10/2019	10/2019	- 0	0/0
486	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 3,338.15	3,860.40	1,577.87	03/2022 03/2023	03/2023	12(O) 12	0/0
487	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 1,763.93	1,763.93	624.49	03/2020 03/2022	03/2022	24(O) 5	1/1
488	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	994.43	12/2020 -	12/2020	0(O) -	0/0
489	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	367.59	03/2022 03/2023	03/2023	12(O) 12	0/10
490	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	154.63	03/2022 09/2022	09/2022	6(O) 6	0/1
491	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	149.66	03/2019 -	02/2020	11(O) -	0/0
492	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 737.72	1,300.44	626.21	02/2019 03/2020	06/2020	16(O) 0	0/1
493	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.00	1,370.00	253.18	12/2021 12/2021	12/2021	0(O) 0	0/0
494	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	64.48	06/2020 06/2021	06/2021	12(O) 12	0/0
495	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	2,973.73	1,394.89	03/2004 -	03/2021	204(O) -	0/0
496	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	3,712.50	2,211.41	03/2021 -	03/2022	12(O) -	0/0
497	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 918.53	918.53	256.68	03/2014 03/2021	03/2021	84(O) 0	0/0
498	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
499	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,180.11	03/2023 -	03/2023	0(O) -	0/0
500	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	792.89	294.10	03/2021 -	03/2022	12(O) -	0/0
501	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 -	305.00	260.45	03/2019 12/2019	12/2019	9(O) 9	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
502	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	215.95	03/2022 -	03/2024	24(O) -	0/0
503	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
504	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
505	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
506	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,272.19	256.28	03/2022 -	03/2023	12(O) -	0/0
507	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	140.79	03/2023 -	03/2023	0(O) -	0/0
508	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 - 3,627.00	3,627.47	480.35	03/2024 -	03/2022	-24(O) -	0/0
509	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	66.23	03/2023 -	03/2023	0(O) -	0/0
510	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	65.16	03/2022 -	03/2024	24(O) -	0/0
511	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	48.42	03/2023 -	03/2024	12(O) -	0/0
512	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	1,950.00	1,803.73	03/2020 -	03/2020	0(O) -	0/0
513	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
514	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 - 2,686.63	2,686.63	393.46	03/2023 03/2023	03/2023	0(O) 0	0/1
515	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	259.90	03/2019 -	12/2019	9(O) -	0/0
516	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
517	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
518	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 - 403.00	860.92	39.80	12/2021 03/2023	03/2023	15(O) 15	0/1
519	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	13,809.00	8,818.98	03/2011 -	03/2020	108(O) -	0/0
520	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.00	261.67	03/2021 -	03/2021	0(O) -	0/0
521	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 -	5,021.45	2,933.84	03/2014 03/2022	03/2022	96(O) 15	0/0
522	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 - 1,756.92	1,756.92	1,645.84	04/2020 12/2020	12/2020	8(O) 8	0/1
523	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,010.00	644.09	07/2012 -	03/2024	140(O) -	0/0
524	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 - 1.00	2,542.75	1,413.56	03/2000 -	03/2021	252(O) -	0/0
525	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023	178(O) 0	0/9

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
526	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 -	3,500.00	3,257.97	12/2008 -	03/2019	-	0/0
527	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,026.30	637.72	02/2013 -	03/2024	133(O) -	0/0
528	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	770.08	277.14	12/2022 -	12/2022	0(O) -	0/0
529	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	106.55	12/2021 -	12/2021	0(O) -	0/0
530	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	256.42	01/2019 -	01/2020	12(O) -	0/0
531	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	700.60	03/2022 03/2022	03/2022	0(O) 0	0/0
532	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	665.69	03/2022 03/2023	03/2023	12(O) 12	0/0
533	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,079.15	184.67	- -	-	-	0/1
534	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33(O) -	0/3
535	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	12/2022	-	0/0
536	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
537	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.47	- -	03/2024	-	0/0
538	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	.00	03/2019 -	03/2019	-	0/0
539	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,300.00	2.28	- -	-	-	0/0
540	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 457.08	457.08	360.07	- -	-	-	0/0
541	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	68.14	03/2020 -	03/2020	0(O) -	0/0
542	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 373.87	394.28	272.88	- -	03/2021	-	0/0
543	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	121.92	03/2020 -	03/2020	0(O) -	0/0
544	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
545	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9(O) -	0/0
546	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	575.65	148.40	03/2006 -	03/2025	228(O) -	0/0
547	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	9.31	- -	03/2025	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
548	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.73	-	03/2025	-	0/0
549	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	307.25	03/2022 -	03/2025	36(O) -	0/0
550	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	364.98	364.98	-	03/2020	-	0/0
551	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	444.81	444.81	-	05/2019	-	0/0
552	HABRA-CHANDPARA MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE ,	04/2000	157.17 -	160.00	77.29	-	-	-	0/0
553	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	1,218.71	431.90	03/2016 -	03/2025	108(O) -	0/0
554	CHINPAI- SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	160.00	102.25	03/2017 -	05/2010	-	0/0
555	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	175.99	71.37	-	03/2025	-	0/0
556	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	328.75	165.55	03/2016 -	03/2025	108(O) -	0/0
557	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	182.35	03/2017 -	03/2025	96(O) -	0/0
558	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.47	11/2018 -	03/2021	28(O) -	0/0
559	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.12	-	03/2025	-	0/0
560	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	-	03/2025	-	0/0
561	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	693.80	403.81	03/2020 -	03/2020	0(O) -	0/0
562	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	226.22	226.22	-	-	-	0/0
563	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
564	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	506.42	32.00	03/2005 -	03/2025	240(O) -	0/0
565	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	319.75	52.09	-	03/2025	-	0/0
566	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	381.75	70.22	-	03/2025	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
567	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	726.95	150.36	02/2012 -	03/2025	157(O) -	0/0
568	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	258.73	103.91	03/2014 -	03/2025	132(O) -	0/0
569	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	246.00	- -	03/2025	- -	0/0
570	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12(O) -	0/0
571	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	1,787.00	2.46	- -	-	-	1/1
572	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	.00	- -	03/2025	- -	0/0
573	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 791.39	800.00	495.17	- -	03/2022	- -	0/0
574	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- -	12/2023	- -	0/0
575	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 -	2,062.20	825.58	- -	03/2022	- -	0/2
576	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 1,352.74	1,352.74	269.07	03/2020 03/2020	03/2020	0(O) 0	1/1
577	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120(O) -	1/1
578	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	.00	- -	03/2025	- -	0/0
579	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	243.97	- -	03/2024	- -	0/0
580	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	38.93	03/2020 -	04/2022	25(O) -	0/0
581	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	860.43	697.21	03/2020 -	03/2020	0(O) -	0/0
582	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24(O) -	0/0
583	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	678.54	446.51	03/2019 -	02/2021	23(O) -	0/38
584	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
585	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24(O) -	0/0
586	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
587	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	2,812.27	12/2023 -	12/2023	0(O) -	0/0
588	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
589	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
590	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 876.00	876.00	848.84	03/2016 -	03/2021	60(O) -	0/0
591	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	3,000.00	756.82	03/2015 -	10/2021	79(O) -	0/0
592	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0(O) -	0/0
593	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,798.80	1,354.80	03/2009 -	12/2023	177(O) -	0/0
594	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,709.83	12/2017 -	03/2020	27(O) -	0/0
595	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	1,202.70	833.73	02/2015 -	12/2021	82(O) -	0/0
596	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	381.48	03/2009 03/2009	12/2019	129(O) 9	1/1
597	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 -	1,928.07	624.68	06/2021 -	03/2023	21(O) -	0/0
598	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
599	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	879.96	02/2019 -	03/2022	37(O) -	0/0
600	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 -	843.04	125.30	10/2020 -	03/2023	29(O) -	0/0
601	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	224.63	03/2020 -	03/2020	0(O) -	0/0
602	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	320.30	03/2022 -	03/2023	12(O) -	0/0
603	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	148.96	03/2022 -	03/2025	36(O) -	0/0
604	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	116.91	11/2018 -	03/2021	28(O) -	0/0
605	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	349.23	12/2018 -	03/2022	39(O) -	0/0
606	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	494.27	03/2020 -	06/2020	3(O) -	0/0
607	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	184.33	12/2021 -	12/2024	36(O) -	0/0
608	VIZIANAGARAM-SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.68	482.27	12/2024 -	12/2024	0(O) -	0/0
609	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	1,500.00	1,197.11	03/2020 -	03/2020	0(O) -	0/0
610	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,120.00	977.00	03/2019 -	03/2021	24(O) -	0/0
611	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 1,700.43	1,700.43	48.00	03/2020 06/2023	06/2023	39(O) 39	0/0
612	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.79	- -	03/2024	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
613	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	886.41	510.24	02/2019 -	12/2021	34(O) -	0/0
614	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	199.54	12/2019 -	06/2020	6(O) -	0/0
615	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	138.99	10/2018 -	10/2019	12(O) -	0/0
616	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
617	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
618	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITT SURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	420.18	142.63	03/2020 -	06/2020	3(O) -	0/0
619	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	245.81	11/2019 -	05/2020	6(O) -	0/0
620	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 281.03	410.00	341.67	02/2019 -	12/2019	10(O) -	0/0
621	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,103.04	4.25	- -	-	-	0/0
622	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	436.07	03/2018 -	03/2020	24(O) -	0/0
623	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	33.39	08/2022 -	09/2022	1(O) -	0/0
624	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	285.46	12/2015 06/2021	03/2020	51(O) -	0/0
625	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12(O) -	0/0
626	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	445.91	06/2013 -	-	-	1/4
627	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12(O) -	0/0
628	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	62.50	- -	-	-	0/0
629	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	241.39	- -	-	-	0/0
630	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	-	0/0
631	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	- -	-	-	0/0
632	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	303.72	- -	-	-	0/0
633	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
634	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	151.50	- -	03/2020	-	0/0
635	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 951.24	951.24	724.96	- -	03/2020	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
636	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71(O) -	0/0
637	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	927.86	03/2005 -	-	-	0/0
638	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	268.31	03/2018 -	03/2018	-	0/0
639	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
640	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022	0(O) -	0/0
641	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15(O) -	0/0
642	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.26	3.83	- -	-	-	0/0
643	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156(O) -	1/1
644	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	668.38	03/2016 -	12/2020	57(O) -	0/0
645	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
646	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	723.00 997.09	997.09	.00	- -	-	-	0/1
647	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	281.85	03/2021 -	03/2021	0(O) -	3/3
648	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	309.16	12/2024 -	12/2024	0(O) -	0/0
649	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022	0(O) -	0/0
650	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 569.63	650.00	45.24	03/2020 03/2020	12/2021	21(O) -10	2/3
651	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 314.09	346.00	345.51	12/2008 03/2015	03/2015	-	0/0
652	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
653	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
654	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
655	FAIZABAD-LALGANJ VIA AKBARGANJ MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	700.00	.00	- -	03/2025	- -	0/0
656	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,230.00	102.72	- -	03/2023	- -	0/0
657	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
658	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	249.27	03/2022 -	12/2019	-27(O) -	0/0
659	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 680.00	680.00	330.00	03/2020 03/2020	03/2020	0(O) 0	4/6
660	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	750.56	285.50	03/2022 -	12/2024	33(O) -	0/0
661	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,200.00	1,100.58	03/2019 -	03/2020	12(O) -	0/0
662	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	455.60	03/2023 -	12/2024	21(O) -	0/0
663	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	982.53	12/2020 -	03/2021	3(O) -	0/0
664	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	426.16	03/2020 -	03/2021	12(O) -	0/0
665	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	72.25	03/2019 -	12/2019	9(O) -	0/0
666	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	4.89	04/2016 -	02/2020	46(O) -	0/0
667	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
668	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
669	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,345.00	.00	01/2018 -	-	-	0/0
670	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	116.58	04/2017 -	01/2020	33(O) -	0/0
671	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
672	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	7.64	-	-	-	0/0
673	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	9.10	01/2022 -	01/2020	-24(O) -	0/0
674	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	3.12	12/2019 -	04/2021	16(O) -	0/0
675	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	3.56	03/2023 -	03/2023	0(O) -	0/0
676	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	395.59	03/2021 03/2023	03/2021	0(O) 0	0/6
677	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
678	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	213.80	-	06/2020	-	0/0
679	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,458.67	12/2024 -	03/2026	15(O) -	0/0
680	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	271.06	03/2019 -	03/2020	12(O) -	0/0
681	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	03/2025	216(O) 0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
682	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268]MRTP, WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
683	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [N220100272]ER, WEST BENGAL ,	04/2000	1,188.91 -	1,670.01	847.87	03/2019 12/2009	03/2025	72(O) 36	0/0
684	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	1,106.62 -	1,536.44	815.11	12/2010 12/2017	03/2020	111(O) 27	7/7
685	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
686	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	2,106.28	03/2014 -	12/2025	141(O) -	0/0
687	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,110.08	03/2016 -	03/2025	108(O) -	0/0
688	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	2,913.50	842.61	03/2016 -	03/2025	108(O) -	0/0
689	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
690	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- -	03/2025	- -	0/0
691	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL ,	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
692	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	- 24	0/0
693	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
694	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	140.00	- -	09/2021	- -	0/0
695	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL ,	04/2011	276.69 -	426.00	.00	- -	03/2030	- -	0/0
696	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	612.00	181.63	12/2021 -	03/2020	-21(O) -	0/0
697	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL ,	01/1991	1,013.45 -	1,428.00	484.82	12/2021 -	12/2021	0(O) -	0/0
698	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
	Total		4,64,773.55 -	6,70,541.38	1,81,731.32				27/135
	ROAD TRANSPORT AND HIGHWAYS								

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
699	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4
700	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	9.77	12/2017 -	-	-	0/4
701	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	124.89	04/2017 -	-	-	2/4
702	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	2.33	10/2018 -	-	-	0/4
703	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	.00	10/2018 -	-	-	0/4
704	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019	0(O) -	0/0
705	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019	0(O) -	0/0
706	AJANTHA TO BULDHANA - [N24001008]MORTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	82.81	07/2019 -	07/2019	0(O) -	0/4
707	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	-	-	0/0
708	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65(O) -	0/0
709	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 06/2019	06/2019	42(O) 0	0/2
710	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
711	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	143.16	10/2015 09/2019	09/2019	47(O) 0	0/0
712	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 06/2019	06/2019	42(O) 0	0/2
713	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 353.89	353.89	256.11	11/2015 06/2019	06/2019	43(O) 0	0/0
714	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	21.73	11/2018 -	05/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
715	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
716	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	.95	03/2020 -	11/2019	-4(O) -	0/0
717	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	687.88	03/2020 -	05/2020	2(O) -	0/0
718	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	18.02	06/2017 -	11/2019	29(O) -	0/0
719	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	176.29	- -	11/2019	- -	0/0
720	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	.00	- -	07/2021	- -	0/0
721	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	70.71	- -	-	-	0/0
722	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	.00	- -	07/2021	- -	0/0
723	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	1,532.62	.00	03/2021 -	04/2021	1(O) -	0/0
724	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	.00	- -	07/2021	- -	0/0
725	REHABILITATION AND UPGRADE OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	.00	- -	02/2021	- -	0/0
726	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	17.64	- -	12/2020	- -	0/0
727	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	33.63	- -	03/2020	- -	0/0
728	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH ,	10/2015	333.21 -	333.21	.00	12/2015 -	06/2019	42(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
729	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	.00	02/2017 -	-	-	0/0
730	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	.00	01/2018 -	01/2020	24(O) -	0/0
731	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	.00	05/2017 -	-	-	0/0
732	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	97.23	08/2017 -	08/2019	24(O) -	0/0
733	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	179.81	11/2017 -	11/2019	24(O) -	0/0
734	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	20.13	08/2018 -	03/2020	19(O) -	0/0
735	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	75.36	08/2018 -	08/2020	24(O) -	0/0
736	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	60.76	08/2018 -	02/2020	18(O) -	0/0
737	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MORTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	297.12	119.08	07/2018 -	01/2020	18(O) -	0/0
738	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	136.30	11/2018 -	05/2020	18(O) -	0/0
739	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	401.90	05/2016 -	-	-	0/0
740	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	100.00	08/2018 -	02/2020	18(O) -	0/0
741	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	301.70	01/2017 -	06/2019	29(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
742	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965])MORTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	153.98	05/2016 -	06/2019	37(O) -	0/0
743	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966])MORTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	144.95	08/2016 -	-	-	0/0
744	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967])MORTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	208.09	09/2016 -	06/2019	33(O) -	0/0
745	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968])MORTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	169.76	08/2017 -	08/2019	24(O) -	0/0
746	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969])MORTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	43.79	09/2017 -	09/2019	24(O) -	0/0
747	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970])MORTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	177.36	01/2018 -	01/2020	24(O) -	0/0
748	REHABILITATION AND UPGRADATION OF EEPURPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 - [N24000971])MORTH,ANDHRA PRADESH ,	08/2016	574.19 -	574.19	.00	07/2017 -	07/2019	24(O) -	0/0
749	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	-	0/0
750	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
751	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	389.45	275.19	05/2012 -	-	-	0/0
752	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324])NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	174.80	05/2018 -	08/2019	15(O) -	3/4
753	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325])NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	182.19	01/2019 -	-	-	3/4
754	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326])NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	53.23	10/2018 -	-	-	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
755	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	240.21	06/2018 -	03/2020	21(O) -	1/3
756	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	69.97	11/2016 -	-	-	0/4
757	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	128.92	- -	09/2020	- -	0/4
758	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36(O) -	2/4
759	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	126.58	- -	12/2020	- -	2/4
760	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	94.49	01/2017 -	01/2020	36(O) -	2/4
761	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60(O) -	1/4
762	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	80.64	04/2017 -	02/2021	46(O) -	1/4
763	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	37.30	04/2017 -	-	-	1/4
764	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	48.16	04/2017 -	-	-	1/4
765	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	56.15	04/2017 -	-	-	1/4
766	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	202.05	42.83	04/2017 -	02/2021	46(O) -	1/4
767	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	215.70	45.21	04/2017 -	02/2021	46(O) -	0/4
768	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	262.62	31.11	04/2017 -	02/2021	46(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
769	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	209.71	47.37	04/2017 -	02/2021	46(O) -	0/1
770	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	24.14	04/2017 -	-	-	1/4
771	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
772	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	.00	- -	-	-	0/0
773	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	.00	- -	-	-	0/0
774	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH ,	05/2016	259.52 -	259.52	.00	- -	-	-	0/0
775	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	.00	- -	-	-	0/0
776	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	.00	- -	-	-	0/0
777	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	.00	- -	-	-	0/0
778	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	.00	- -	-	-	0/0
779	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH ,	02/2017	199.02 -	199.02	.00	- -	-	-	0/0
780	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH ,	02/2017	184.88 -	184.88	.00	- -	-	-	0/0
781	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 -	210.50	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
782	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL, ARUNACHAL PRADESH ,	07/2015	189.91 -	189.91	.00	- -	-	-	0/0
783	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL, ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	.00	- -	-	-	0/0
784	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL, ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	.00	- -	-	-	0/0
785	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM ,	12/2003	280.00 -	280.00	472.00	02/2009 -	-	-	0/0
786	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM ,	12/2003	199.81 -	385.13	319.96	04/2009 -	07/2019	123(O) -	0/0
787	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI, ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	-	-	0/0
788	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	-	-	0/0
789	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM ,	12/2003	245.00 -	174.34	224.28	03/2008 -	09/2019	138(O) -	0/0
790	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM ,	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019	136(O) -	0/0
791	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM ,	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019	140(O) -	0/0
792	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM ,	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019	133(O) -	0/0
793	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI, ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0
794	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI, ASSAM ,	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019	112(O) -	0/0
795	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM , EPC	05/2015	454.89 -	454.89	120.86	05/2018 -	-	-	2/4
796	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM , EPC	06/2015	437.39 -	437.39	6.27	06/2018 -	-	-	0/4
797	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM , EPC	06/2015	463.49 -	463.49	6.62	06/2018 -	-	-	0/4
798	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL, ASSAM , EPC	06/2016	829.00 -	829.00	292.25	01/2019 -	01/2019	-	0/4
799	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM , EPC	03/2015	168.39 -	168.39	168.40	11/2018 -	-	-	2/4
800	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM , EPC	10/2014	588.95 -	588.95	347.18	11/2018 -	-	-	2/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
801	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	188.71	05/2017 -	11/2010	-	0/0
802	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	344.32	02/2011 -	06/2018	-	0/0
803	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 307.47	307.47	239.76	02/2018 -	11/2014	-	0/0
804	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	26.00	12/2018 -	-	-	0/4
805	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	61.56	06/2018 -	12/2015	-	0/2
806	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	34.00	- -	-	-	1/4
807	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	4.48	12/2018 -	10/2017	-	0/4
808	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	48.09	01/2016 -	-	-	1/4
809	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	.00	01/2016 -	-	-	0/4
810	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	292.24	01/2016 -	-	-	2/3
811	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	105.48	- -	-	-	0/4
812	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]PWD,ASSAM ,	09/2018	160.00 -	160.00	.50	09/2021 -	09/2021	0(O) -	0/0
813	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70(O) -	0/0
814	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	885.31	02/2013 -	06/2019	76(O) -	0/0
815	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	329.40	05/2013 -	-	-	0/0
816	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
817	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
818	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	843.67	07/2013 -	06/2019	71(O) -	0/0
819	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	566.60	11/2013 -	12/2018	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
820	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	.00	- -	-	-	0/0
821	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	-	-	0/0
822	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	-	-	0/0
823	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
824	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	214.34	04/2019 -	04/2019	-	0/0
825	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	367.27	- -	01/2020	-	0/0
826	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24(O) -	0/0
827	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	110.39	- -	10/2020	-	0/0
828	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	99.74	- -	12/2019	-	0/0
829	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6(O) -	0/0
830	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0
831	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	579.78	- -	03/2019	-	0/0
832	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	417.09	04/2018 -	-	-	0/0
833	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
834	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	.00	- -	-	-	0/0
835	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
836	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	473.00	07/2016 -	-	-	0/0
837	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
838	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	52.50	05/2016 -	-	-	0/0
839	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
840	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	239.77	05/2016 -	-	-	0/0
841	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	753.03	10/2016 -	-	-	0/0
842	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
843	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	241.00	11/2015 -	-	-	0/0
844	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25(O) -	0/0
845	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	517.08	12/2016 -	-	-	0/0
846	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
847	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	05/2021	14(O) -	0/0
848	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54(O) -	0/0
849	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	-	-	-	0/0
850	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	-	-	-	0/0
851	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	-	-	-	0/0
852	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	-	-	-	0/0
853	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
854	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD,BIHAR ,	11/2016	230.34 -	230.34	167.64	10/2019 -	10/2019	0(O) -	0/0
855	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR ,	03/2018	153.24 -	153.24	.00	- -	-	-	0/0
856	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR ,	05/2014	199.98 -	199.98	.00	08/2016 -	12/2020	52(O) -	0/0
857	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	178.85	- -	-	-	0/0
858	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.70	12/2015 -	-	-	0/0
859	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	385.09	05/2018 -	10/2019	17(O) -	0/0
860	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	7.21	04/2018 -	-	-	0/0
861	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	357.06	04/2018 -	02/2020	22(O) -	0/0
862	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,029.96	.00	- -	03/2021	-	0/0
863	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	-	-	0/0
864	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	306.64	04/2018 -	-	-	0/1
865	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	212.33	- -	-	-	0/4
866	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	90.39	- -	-	-	2/4
867	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	290.59	209.47	- -	-	-	3/4
868	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	310.25	- -	-	-	0/0
869	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	274.46	- -	-	-	0/0
870	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	235.30	- -	-	-	0/0
871	PATRADEVI TO KARASWADA 4L - [N24001004]MORTH,GOA ,	03/2017	634.32 634.32	634.32	102.33	05/2020 -	05/2020	0(O) -	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
872	KARASWADA TO BAMBOLIM - [N24001005]MORTH,GOA ,	03/2017	852.67 852.67	852.67	108.04	12/2019 -	12/2019	0(O) -	1/4
873	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,187.21	09/2012 -	-	-	2/3
874	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	12/2018	-	0/0
875	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-	-	0/3
876	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0
877	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	435.25	- -	08/2019	- -	0/0
878	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	140.44	- -	10/2019	- -	0/0
879	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	321.67	- -	09/2019	- -	0/0
880	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	357.12	- -	08/2019	- -	0/0
881	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	03/2019	-	0/0
882	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	364.56	208.94	- -	12/2019	- -	0/0
883	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	75.08	- -	01/2020	- -	0/0
884	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	262.83	- -	09/2019	- -	0/0
885	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	- -	0/0
886	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2(O) -	0/0
887	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	11/2019	25(O) -	0/0
888	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 -	1,052.21	1,080.00	- -	01/2021	- -	0/0
889	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	- -	01/2021	- -	0/0
890	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 -	1,437.64	.00	- -	07/2021	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
891	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	-	-	-	0/0
892	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN - [N24000920]PWD, GUJARAT ,	03/2016	223.67 -	223.67	112.81	02/2017 -	02/2017	-	0/4
893	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD, GUJARAT , EPC	03/2016	208.34 -	208.34	112.87	02/2016 -	-	-	0/4
894	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD, GUJARAT , EPC	12/2017	867.97 -	867.97	4.37	11/2018 -	-	-	0/1
895	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]PWD, GUJARAT , EPC	03/2018	464.07 -	464.07	.05	11/2018 -	-	-	0/1
896	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD, GUJARAT , EPC	10/2018	400.76 -	400.76	3.06	05/2019 -	-	-	0/0
897	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD, GUJARAT , EPC	08/2017	962.43 -	962.43	45.70	03/2018 -	-	-	0/1
898	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118(O) -	0/0
899	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020	100(O) -	0/0
900	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -1 - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
901	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 -	602.95	417.86	06/2016 -	08/2019	38(O) -	0/0
902	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 -	574.28	448.92	07/2018 -	07/2019	12(O) -	0/0
903	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	971.24	04/2019 -	04/2019	-	0/0
904	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
905	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA ,	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6(O) -	0/0
906	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	1,004.67	.00	05/2019 -	05/2019	-	0/0
907	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA ,	03/2017	639.79 -	552.90	480.73	03/2020 -	09/2019	-6(O) -	0/0
908	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA ,	03/2018	1,484.30 -	1,484.30	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
909	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	.00	- -	03/2020	- -	0/0
910	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	.00	- -	03/2020	- -	0/0
911	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	634.70	.00	- -	-	-	0/0
912	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	795.50	.00	- -	-	-	0/0
913	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	.00	- -	03/2020	- -	0/0
914	REHABILITATION AND UPGADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	.00	- -	06/2020	- -	0/0
915	REDESIGNING REHABILITATION AND UPGADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	.00	- -	03/2020	- -	0/0
916	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA ,	01/2017	247.25 -	247.25	139.25	03/2019 -	09/2019	6(O) -	0/0
917	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA ,	01/2017	276.01 -	276.01	155.40	03/2019 -	05/2019	-	0/0
918	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	04/2019	-	0/0
919	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	452.30	03/2018 -	03/2019	-	0/0
920	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	256.25	02/2019 -	06/2019	4(O) -	0/0
921	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	234.67	- -	09/2020	- -	0/0
922	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	07/2020	- -	0/0
923	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	179.17	- -	11/2019	- -	0/0
924	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15(O) -	0/0
925	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	.00	- -	05/2021	- -	0/0
926	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,580.88	07/2015 -	03/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
927	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
928	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
929	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,075.87	06/2014 -	-	-	0/0
930	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	301.68	06/2019 -	12/2020	18(O) -	0/0
931	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,154.18	12/2018 -	10/2019	10(O) -	0/0
932	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	305.75	- -	01/2021	- -	0/0
933	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	30.43	08/2018 -	-	-	1/4
934	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	.00	11/2018 -	-	-	0/4
935	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	.00	07/2019 -	07/2019	0(O) -	0/0
936	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
937	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	712.41	03/2019 -	07/2019	4(O) -	0/0
938	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	158.64	- -	12/2019	- -	0/0
939	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	192.02	08/2018 -	01/2020	17(O) -	0/0
940	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	107.13	03/2020 -	06/2019	-9(O) -	0/0
941	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	89.96	03/2020 -	06/2019	-9(O) -	0/0
942	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
943	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0
944	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
945	REHABILITATION AND UPGRADEMENT OF BALRAMPUR-TULSIKUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD,JHARKHAND ,	03/2018	212.99 -	212.99	59.56	06/2020 -	06/2020	0(O) -	0/0
946	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18(O) -	3/3
947	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
948	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
949	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	433.12	09/2017 -	12/2019	27(O) -	0/0
950	REHABILITATION AND UPGRADEMENT TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
951	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52(O) -	0/0
952	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,098.56	08/2018 -	11/2019	15(O) -	0/0
953	4-LANING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20(O) -	0/0
954	4-LANING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	12.95	03/2019 -	11/2020	20(O) -	0/0
955	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	-	-	-	0/0
956	FOUR LANING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	525.24	04/2020 -	04/2020	0(O) -	0/0
957	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	238.96	03/2019 -	06/2020	15(O) -	0/0
958	TWO/FOUR LANING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	782.81	08/2019 -	12/2020	16(O) -	0/0
959	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	513.98	03/2020 -	07/2020	4(O) -	0/0
960	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	566.10	03/2020 -	06/2020	3(O) -	0/0
961	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
962	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	1,995.34	.00	- -	11/2021	- -	0/0
963	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,177.80	.00	- -	-	-	0/0
964	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	01/2017	-	0/0
965	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	01/2019	-	0/0
966	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]PWD,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	09/2017	-	0/0
967	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	02/2017	-	0/0
968	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	06/2019	0(O) -	0/0
969	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA ,	01/2018	159.70 -	159.70	21.16	07/2018 -	07/2018	-	0/0
970	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	10/2018	-	0/0
971	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]PWD,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	01/2019	-	0/0
972	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA ,	03/2018	325.86 -	325.86	62.54	10/2018 -	10/2018	-	0/0
973	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	02/2017	-	0/0
974	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	03/2017	-	0/0
975	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	03/2017	-	0/0
976	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	05/2019	-	0/0
977	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	05/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
978	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24(O) -	0/0
979	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	08/2016	-	0/0
980	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24(O) -	0/0
981	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
982	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88(O) -	0/0
983	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	09/2019	24(O) -	0/0
984	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	788.62	- -	10/2019	- -	0/0
985	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	402.47	06/2018 -	01/2020	19(O) -	0/0
986	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	256.47	09/2017 -	06/2020	33(O) -	0/0
987	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,424.77	.00	- -	-	-	0/0
988	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-	-	0/0
989	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/0
990	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
991	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	178.32	- -	03/2020	- -	0/0
992	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	5.21	05/2015 -	-	-	0/0
993	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020	36(O) -	0/0
994	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
995	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54(O) -	0/0
996	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	.00	04/2015 -	08/2019	52(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
997	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	564.36	-	03/2019	-	0/0
998	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	492.23	-	05/2019	-	0/0
999	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	207.68	01/2020 -	01/2020	0(O) -	0/0
1000	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	412.39	02/2020 -	02/2020	0(O) -	0/0
1001	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	588.21	-	06/2019	-	0/0
1002	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	12/2018	-	0/0
1003	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	-	-	0/0
1004	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	586.36	-	06/2019	-	0/0
1005	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	5(O) -	0/0
1006	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	219.26	08/2017 -	02/2020	30(O) -	0/0
1007	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	100.96	01/2019 -	03/2019	-	0/0
1008	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27(O) -	0/0
1009	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1010	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	.00	09/2017 -	-	-	0/0
1011	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	-	-	-	0/0
1012	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	.00	-	08/2020	-	0/0
1013	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1014	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH ,	03/2018	162.56 -	162.56	66.95	03/2018 -	12/2019	21(O) -	0/0
1015	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH ,	03/2018	166.21 -	166.21	14.37	08/2018 -	06/2020	22(O) -	0/0
1016	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH ,	02/2018	169.63 -	169.63	7.10	03/2018 -	07/2020	28(O) -	0/0
1017	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH ,	11/2017	235.91 -	235.91	73.09	02/2018 -	11/2019	21(O) -	0/0
1018	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH ,	11/2017	184.62 -	184.62	47.70	02/2018 -	11/2019	21(O) -	0/0
1019	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH ,	03/2018	191.21 -	191.21	68.26	11/2019 -	11/2019	0(O) -	0/0
1020	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH ,	01/2017	205.05 -	205.05	62.60	03/2017 -	06/2020	39(O) -	0/0
1021	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH ,	03/2018	214.69 -	214.69	15.22	03/2018 -	11/2019	20(O) -	0/0
1022	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH ,	03/2018	217.22 -	217.22	4.45	08/2018 -	06/2020	22(O) -	0/0
1023	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH ,	03/2018	233.04 -	233.04	93.96	03/2018 -	11/2019	20(O) -	0/0
1024	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH ,	11/2017	249.05 -	249.05	100.10	07/2018 -	01/2020	18(O) -	0/0
1025	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH ,	11/2017	254.17 -	254.17	115.54	02/2018 -	11/2019	21(O) -	0/0
1026	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH ,	02/2018	279.44 -	279.44	50.39	03/2018 -	04/2020	25(O) -	0/0
1027	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH ,	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10(O) -	0/0
1028	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH ,	01/2017	373.82 -	373.82	116.33	09/2019 -	09/2019	0(O) -	0/0
1029	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH ,	01/2016	809.16 -	809.16	173.16	07/2018 -	02/2020	19(O) -	0/0
1030	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH ,	03/2016	877.79 -	877.79	356.56	06/2019 -	11/2019	5(O) -	0/0
1031	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH ,	09/2016	178.23 -	178.23	114.16	09/2018 -	07/2019	10(O) -	0/0
1032	ANJANGAON TO MAH/MP BORDER - [N24001007]MORTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	149.80	06/2019 -	06/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1033	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH ,	11/2017	392.33 -	392.33	196.99	03/2018 -	11/2019	20(O) -	0/0
1034	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019	76(O) -	0/0
1035	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	750.38	06/2014 -	03/2020	69(O) -	0/0
1036	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64(O) -	2/2
1037	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	52.00	- -	-	-	0/4
1038	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1039	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	259.50	- -	-	-	3/4
1040	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1041	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1042	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	83.11	- -	-	-	0/0
1043	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	.00	05/2019 -	05/2019	-	0/0
1044	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	529.62	05/2018 -	06/2020	25(O) -	0/0
1045	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	05/2018 -	06/2020	25(O) -	0/0
1046	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019	-	0/0
1047	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31(O) -	0/0
1048	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	203.78	03/2019 -	12/2020	21(O) -	0/0
1049	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	347.91	05/2018 -	05/2020	24(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1050	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019	24(O) -	0/0
1051	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	708.62	11/2016 -	05/2020	42(O) -	0/0
1052	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	226.24	06/2006 -	-	-	0/0
1053	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	3,424.19	01/2018 -	02/2019	-	0/0
1054	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1055	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	22.27	07/2018 -	-	-	0/0
1056	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	571.35	07/2019 -	07/2019	0(O) -	0/0
1057	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	762.75	07/2019 -	07/2019	0(O) -	0/0
1058	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	726.85	- -	-	-	0/0
1059	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	- -	-	-	0/0
1060	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	.00	- -	07/2021	-	0/0
1061	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	07/2021	-	0/0
1062	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6(O) -	0/0
1063	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8(O) -	0/0
1064	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	174.12	- -	05/2019	-	0/0
1065	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	219.09	05/2019 -	09/2019	4(O) -	0/0
1066	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	607.37	02/2020 -	05/2020	3(O) -	0/0
1067	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	02/2020	-1(O) -	0/0
1068	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1069	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2(O) -	0/0
1070	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5(O) -	0/0
1071	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	480.96	03/2017 -	11/2020	44(O) -	0/0
1072	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	248.60	03/2020 -	09/2019	-6(O) -	0/0
1073	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5(O) -	0/0
1074	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	71.72	- -	10/2020	- -	0/0
1075	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	55.06	- -	08/2021	- -	0/0
1076	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	212.24	- -	04/2021	- -	0/0
1077	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	7.51	- -	11/2020	- -	0/0
1078	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	12.80	- -	11/2020	- -	0/0
1079	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	5.00	- -	07/2021	- -	0/0
1080	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	642.13	288.84	- -	12/2020	- -	0/0
1081	SARSAM TO KOTHARI - [N24001002]MORTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	45.01	07/2019 -	07/2019	0(O) -	0/4
1082	AKOLA TO AKOT - [N24001003]MORTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	31.05	06/2019 -	06/2019	0(O) -	0/4
1083	AKOT TO ANJANGAON - [N24001006]MORTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	95.98	06/2019 -	06/2019	0(O) -	0/4
1084	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	86.79	05/2019 -	12/2019	7(O) -	0/0
1085	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	110.43	05/2019 -	12/2019	7(O) -	0/4
1086	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	169.08	05/2019 -	06/2019	1(O) -	0/4
1087	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	229.00	06/2019 -	10/2019	4(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1088	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	100.00	06/2019 -	06/2020	12(O) -	0/0
1089	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	171.75	06/2019 -	12/2019	6(O) -	0/0
1090	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	159.29	06/2019 -	12/2019	6(O) -	0/0
1091	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	252.90	06/2019 -	06/2019	0(O) -	0/0
1092	DAHEGAON TO KUHI - [N24001017]MORTH,MAHARASHTRA ,	01/2017	228.89 228.89	228.89	90.00	06/2019 -	06/2019	0(O) -	3/4
1093	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	254.60	06/2019 -	06/2019	0(O) -	0/0
1094	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	230.34	06/2019 -	08/2019	2(O) -	0/4
1095	AMD I TO SAONER - [N24001021]MORTH,MAHARASHTRA ,	01/2017	396.91 396.91	396.91	281.48	06/2019 -	08/2019	2(O) -	3/4
1096	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA ,	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12(O) -	1/4
1097	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	125.81	06/2019 -	12/2019	6(O) -	0/4
1098	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA ,	01/2017	457.52 457.52	457.52	184.31	07/2019 -	07/2020	12(O) -	2/4
1099	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA ,	01/2017	355.17 355.17	355.17	141.87	07/2019 -	12/2019	5(O) -	3/4
1100	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA ,	01/2017	376.19 376.19	376.19	23.03	05/2019 -	05/2020	12(O) -	1/4
1101	SHAH PUR PATGAON SECTION I - [N24001027]MORTH,MAHARASHTRA ,	01/2018	150.79 150.79	150.79	21.42	12/2019 -	12/2019	0(O) -	1/4
1102	PATGAON KHOPOLI SECTION I - [N24001028]MORTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	15.57	12/2019 -	12/2019	0(O) -	0/4
1103	AHMADPUR TO PIMPLA - [N24001029]MORTH,MAHARASHTRA ,	01/2017	422.38 422.38	422.38	136.58	08/2019 -	08/2019	0(O) -	2/4
1104	PIMPLA TO MANJAR SUMBHA - [N24001030]MORTH,MAHARASHTRA ,	01/2017	595.77 595.77	595.77	119.44	08/2019 -	08/2019	0(O) -	2/4
1105	MANJUSUMBA TO CHUMBALI - [N24001031]MORTH,MAHARASHTRA ,	01/2017	228.54 228.54	228.54	87.30	08/2019 -	08/2019	0(O) -	2/4
1106	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	126.78	05/2019 -	05/2020	12(O) -	0/4
1107	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MORTH,MAHARASHTRA ,	01/2017	486.19 486.19	486.19	174.29	07/2019 -	07/2019	0(O) -	2/4
1108	PARTUR TO MAJALGAON - [N24001034]MORTH,MAHARASHTRA ,	01/2017	420.57 420.57	420.57	121.39	07/2019 -	07/2019	0(O) -	2/4
1109	MANSAR TO SALAIKHURD - [N24001035]MORTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	70.13	12/2019 -	12/2019	0(O) -	0/4
1110	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	310.33	07/2019 -	07/2019	0(O) -	0/0
1111	KAIJ TO KUSALAM - [N24001037]MORTH,MAHARASHTRA ,	01/2017	554.78 554.78	554.78	136.90	07/2019 -	07/2019	0(O) -	2/4
1112	MAHAD TO RAIGAD FORT - [N24001038]MORTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	7.34	05/2020 -	05/2020	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1113	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA ,	01/2017	356.66 356.66	356.66	14.88	- -	- -	- -	0/4
1114	JAHIRABAD TO LATUR - [N24001040]MORTH,MAHARASHTRA ,	01/2017	461.96 461.96	461.96	116.43	11/2019 -	11/2019	0(O) -	2/4
1115	SHIROD SHAHPURER TO NANDED - [N24001041]MORTH,MAHARASHTRA ,	01/2017	211.34 211.34	211.34	94.83	07/2019 -	07/2019	0(O) -	2/4
1116	SALAIKHURD TO TIRORA - [N24001042]MORTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	36.22	12/2019 -	12/2019	0(O) -	0/4
1117	NILAJPHATA TO BHANDARA - [N24001043]MORTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	3.60	05/2020 -	05/2020	0(O) -	0/4
1118	KALMAB TO RALEGAON - [N24001044]MORTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	294.91	06/2019 -	06/2019	0(O) -	0/4
1119	JALGAON TO BHADGAON - [N24001045]MORTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	75.59	11/2019 -	11/2019	0(O) -	0/4
1120	RALEGAON TO RAMTIRTH - [N24001046]MORTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	100.69	07/2019 -	07/2019	0(O) -	0/4
1121	BHADGAON TO CHALISGAON - [N24001047]MORTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	120.00	11/2019 -	11/2019	0(O) -	0/0
1122	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	83.51	07/2019 -	07/2019	0(O) -	0/0
1123	KARAD TO VITA - [N24001049]MORTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	39.04	12/2019 -	12/2019	0(O) -	0/4
1124	VITA TO NAGAJ - [N24001050]MORTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019	0(O) -	0/4
1125	NALDURG TO AKKALKOT - [N24001051]MORTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	56.39	12/2019 -	12/2019	0(O) -	0/4
1126	SANGOLA TO JATH - [N24001052]MORTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	28.15	12/2019 -	12/2019	0(O) -	0/4
1127	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	68.97	06/2019 -	06/2020	12(O) -	0/4
1128	TASGAON TO SHIRDHON - [N24001054]MORTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	83.73	11/2019 -	11/2019	0(O) -	0/4
1129	HELWAK TO KARAD - [N24001055]MORTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	100.40	07/2019 -	07/2019	0(O) -	0/4
1130	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	224.01	07/2019 -	07/2019	0(O) -	0/0
1131	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	12.00	06/2019 -	06/2020	12(O) -	0/4
1132	KARWANDI TO RAJURI - [N24001058]MORTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	44.47	12/2019 -	12/2019	0(O) -	0/4
1133	SHIVUR TO YEOLA - [N24001059]MORTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	7.45	12/2019 -	12/2019	0(O) -	0/4
1134	PALPHATA TO PHULAMBARI - [N24001060]MORTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	37.23	12/2019 -	12/2019	0(O) -	0/4
1135	CHIKALI TO DHAD - [N24001061]MORTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	21.00	12/2019 -	12/2019	0(O) -	0/4
1136	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MORTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	58.66	12/2019 -	12/2019	0(O) -	0/4
1137	WADIGODRI TO DHANGRIIMPRI - [N24001063]MORTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	48.23	02/2020 -	02/2020	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1138	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MORTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	52.77	02/2020 -	02/2020	0(O) -	0/4
1139	PARBHANI TO GANGKHED - [N24001065]MORTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	9.85	12/2019 -	12/2019	0(O) -	0/4
1140	LATUR TO PANGAON - [N24001066]MORTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	60.48	12/2019 -	12/2019	0(O) -	0/4
1141	OMREGA TO AUSA - [N24001067]MORTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	72.24	12/2019 -	12/2019	0(O) -	0/4
1142	WASHIM TO DASTAPUR - [N24001068]MORTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	25.45	12/2019 -	12/2019	0(O) -	1/4
1143	NANDED TO JALKOT - [N24001069]MORTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	37.50	09/2019 -	09/2019	0(O) -	1/4
1144	DASTAPUR TO KARANJA - [N24001070]MORTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	58.15	12/2019 -	12/2019	0(O) -	2/4
1145	JALKOT TO TOGRI - [N24001071]MORTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	.00	08/2020 -	08/2020	0(O) -	0/4
1146	KHERDA TO NAGZARI - [N24001072]MORTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	27.50	12/2019 -	12/2019	0(O) -	0/4
1147	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	.00	08/2020 -	08/2020	0(O) -	0/0
1148	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	32.20	12/2019 -	12/2019	0(O) -	0/0
1149	OSMANNAGAR TO KUNDRAL - [N24001075]MORTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	44.02	08/2020 -	08/2020	0(O) -	0/4
1150	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	84.46	12/2019 -	12/2019	0(O) -	0/0
1151	KUNDRAL TO WAZAR - [N24001077]MORTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	90.75	12/2019 -	12/2019	0(O) -	2/4
1152	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	13.50	12/2019 -	12/2019	0(O) -	0/0
1153	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MORTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	64.97	06/2020 -	06/2020	0(O) -	1/4
1154	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	15.50	12/2019 -	12/2019	0(O) -	0/0
1155	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MORTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	31.30	12/2019 -	12/2019	0(O) -	1/4
1156	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	21.42	12/2019 -	12/2019	0(O) -	0/0
1157	CHIKLI TO TAKARKHED - [N24001083]MORTH,MAHARASHTRA ,	03/2018	393.10 393.10	393.10	83.97	12/2019 -	12/2019	0(O) -	2/4
1158	PAHUR TO BODHWAD - [N24001084]MORTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	29.23	05/2020 -	05/2020	0(O) -	0/4
1159	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	35.26	06/2019 -	12/2019	6(O) -	0/4
1160	BODHWAD TO STATE BORDER - [N24001086]MORTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	81.95	07/2019 -	07/2019	0(O) -	0/4
1161	MANGRUPHIR TO MAHAN - [N24001087]MORTH,MAHARASHTRA ,	03/2018	222.13 222.13	222.13	14.36	11/2019 -	11/2019	0(O) -	0/4
1162	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	35.69	12/2019 -	12/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1163	MALEGAON TO RISOD - [N24001089]MORTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	50.07	12/2019 -	12/2019	0(O) -	0/4
1164	KOLDE TO KHETIYA - [N24001090]MORTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	157.93	07/2019 -	07/2019	0(O) -	0/4
1165	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019	0(O) -	0/0
1166	SATARA TO MHASWAD - [N24001092]MORTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	167.18	07/2019 -	07/2019	0(O) -	0/4
1167	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	19.32	12/2019 -	12/2019	0(O) -	0/0
1168	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	14.94	03/2019 -	12/2019	9(O) -	0/0
1169	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	179.77	- -	-	-	0/0
1170	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	23.71	03/2019 -	12/2019	9(O) -	0/0
1171	SELDOH TO PANVAR - [N24001097]MORTH,MAHARASHTRA ,	07/2018	404.33 404.33	404.33	14.19	05/2020 -	05/2020	0(O) -	0/4
1172	WARDHA TO HINGAGHAT - [N24001098]MORTH,MAHARASHTRA ,	01/2018	216.90 216.90	216.90	20.00	12/2019 -	12/2019	0(O) -	1/4
1173	MHASWAD TO TEMBHURNI - [N24001099]MORTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	151.71	07/2019 -	07/2019	0(O) -	0/4
1174	AHMEDNAGAR TO BARAMATI - [N24001100]MORTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	301.50	08/2019 -	08/2019	0(O) -	0/4
1175	KURUDWADI TO PANDHARPUR - [N24001101]MORTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	136.17	07/2019 -	07/2019	0(O) -	0/4
1176	PANDHARPUR TO SANGOLA - [N24001102]MORTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	161.75	07/2019 -	07/2019	0(O) -	0/4
1177	SARAD VANI PIMPALGAON - [N24001103]MORTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	1,691.63	07/2019 -	07/2019	0(O) -	0/4
1178	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	145.91	06/2019 -	06/2020	12(O) -	2/4
1179	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	156.72	03/2019 -	-	-	0/4
1180	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	.00	03/2018 -	12/2019	21(O) -	0/4
1181	PANCHARAL TO MANDANGHAR - [N24001107]MORTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020	0(O) -	0/4
1182	CHALISGAON TO NANDGAON - [N24001108]MORTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	46.89	12/2019 -	12/2019	0(O) -	0/4
1183	KUSUMBA TO MALEGAON - [N24001109]MORTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	47.02	12/2019 -	12/2019	0(O) -	0/4
1184	BAMNI TO NAVEGAON - [N24001110]MORTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	24.29	04/2020 -	04/2020	0(O) -	1/4
1185	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	.00	04/2019 -	04/2020	12(O) -	0/4
1186	NASRATPUR TO BARASGAON - [N24001112]MORTH,MAHARASHTRA ,	07/2016	406.54 406.54	406.54	136.00	09/2019 -	09/2019	0(O) -	2/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1187	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	30.00	09/2018 -	04/2021	31(O) -	0/4
1188	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA ,	01/2017	1,202.52 1,202.52	1,202.52	652.90	12/2019 -	03/2020	3(O) -	1/4
1189	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA ,	01/2017	1,598.47 1,598.47	1,598.47	746.91	11/2019 -	03/2020	4(O) -	1/4
1190	GADCHIROLI TO MUL - [N24001116]MORTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	127.31	06/2019 -	06/2019	0(O) -	2/4
1191	MUL TO CHANDRAPUR - [N24001117]MORTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019	0(O) -	1/4
1192	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA ,	01/2017	362.96 362.96	362.96	29.83	06/2019 -	11/2019	5(O) -	0/4
1193	NAGBHID TO ARMORI - [N24001119]MORTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	173.91	07/2019 -	07/2019	0(O) -	0/4
1194	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	130.85	02/2019 -	02/2020	12(O) -	0/4
1195	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	78.81	11/2018 -	11/2019	12(O) -	0/4
1196	PAITHAN TO SHIRUR - [N24001122]MORTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	88.00	06/2019 -	06/2019	0(O) -	0/4
1197	SHIRUR TO KHARDA - [N24001123]MORTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	122.79	06/2019 -	06/2019	0(O) -	0/4
1198	AURANGABAD TO SILLOD - [N24001124]MORTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	79.30	06/2019 -	06/2019	0(O) -	0/4
1199	SILLOD TO FARDAPUR - [N24001125]MORTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	44.03	06/2019 -	06/2019	0(O) -	0/4
1200	FARDAPUR TO JALGAON - [N24001126]MORTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	66.10	06/2019 -	06/2019	0(O) -	0/4
1201	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	406.58	06/2019 -	06/2019	0(O) -	0/0
1202	BHOKAR TO SARSAM - [N24001128]MORTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	155.64	07/2019 -	07/2019	0(O) -	0/4
1203	BHOGAN KHURD TO KASHEDI - [N24001132]MORTH,MAHARASHTRA ,	09/2017	743.21 743.21	743.21	52.87	06/2021 -	06/2021	0(O) -	1/4
1204	PARSHURAM GHAT TO ARAWALI - [N24001133]MORTH,MAHARASHTRA ,	04/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019	-1(O) -	1/4
1205	KANTE TO WAKED - [N24001134]MORTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.02	1,230.02	609.61	11/2019 -	11/2019	0(O) -	1/4
1206	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	800.00	02/2019 -	02/2019	- -	0/0
1207	TALGAON TO KALMATH - [N24001136]MORTH,MAHARASHTRA ,	10/2016	904.70 904.70	904.70	604.05	03/2020 -	03/2020	0(O) -	2/4
1208	KALMATH TO ZARAP - [N24001137]MORTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.13	1,338.13	959.51	03/2020 -	03/2020	0(O) -	3/5
1209	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA ,	02/2017	205.72 205.72	205.72	26.42	06/2019 -	06/2020	12(O) -	1/4
1210	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA ,	02/2018	355.99 355.99	355.99	68.97	12/2019 -	12/2019	0(O) -	0/0
1211	WARDHA TO ARVI - [N24001150]MORTH,MAHARASHTRA ,	02/2018	313.58 313.58	313.58	8.86	04/2020 -	04/2020	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1212	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	93.52	10/2018 -	10/2021	36(O) -	1/4
1213	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	475.02	05/2018 -	09/2019	16(O) -	0/0
1214	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	27.90	- -	09/2021	- -	0/4
1215	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	37.86	05/2019 -	07/2019	2(O) -	0/0
1216	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019	105(O) -	0/0
1217	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110(O) -	0/0
1218	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	296.28	10/2010 -	06/2020	116(O) -	0/0
1219	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	.00	09/2019 -	09/2019	0(O) -	0/0
1220	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	.00	09/2019 -	09/2019	0(O) -	0/0
1221	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	.00	09/2019 -	09/2019	0(O) -	0/0
1222	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	.00	09/2019 -	09/2019	0(O) -	0/0
1223	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	.00	09/2019 -	09/2019	0(O) -	0/0
1224	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	.00	09/2019 -	09/2019	0(O) -	0/0
1225	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	.00	09/2019 -	09/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1226	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	.00	09/2019 -	09/2019	0(O) -	0/0
1227	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128(O) -	0/0
1228	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	303.71	08/2011 -	-	-	2/2
1229	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1230	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69(O) -	0/0
1231	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81(O) -	0/0
1232	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-	-	0/0
1233	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1234	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,275.00	- -	02/2020	- -	0/0
1235	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,294.47	.00	- -	-	-	0/0
1236	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	998.70	.00	- -	-	-	0/0
1237	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1238	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	187.25	08/2016 -	08/2019	36(O) -	0/4
1239	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	229.11	08/2016 -	08/2019	36(O) -	0/4
1240	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	153.61	08/2016 -	08/2019	36(O) -	0/4
1241	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	112.38	04/2017 -	-	-	1/4
1242	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	116.06	09/2018 -	-	-	0/4
1243	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1244	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	.00	09/2018 -	-	-	0/0
1245	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 -	-	-	0/4
1246	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	-	-	0/0
1247	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	.00	09/2018 -	-	-	0/2
1248	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	.00	09/2018 -	-	-	0/2
1249	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	9.21	09/2018 -	-	-	0/2
1250	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	6.75	09/2018 -	-	-	0/2
1251	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	3.27	09/2018 -	-	-	0/2
1252	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	4.55	09/2018 -	-	-	0/2
1253	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	-	-	0/2
1254	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/0
1255	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/0
1256	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,930.61	09/2014 -	-	-	0/0
1257	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,864.34	06/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1258	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1259	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	268.01	10/2016 -	-	-	0/0
1260	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1261	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	06/2019	29(O) -	0/0
1262	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	.00	-	04/2020	-	0/0
1263	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	-	11/2019	-	0/0
1264	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22(O) -	0/0
1265	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52(O) -	0/0
1266	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	.00	-	07/2019	-	0/0
1267	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	.00	08/2019 -	08/2019	0(O) -	0/0
1268	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	447.28	-	07/2020	-	0/0
1269	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43(O) -	0/0
1270	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	06/2019	14(O) -	0/0
1271	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1272	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.31	137.43	10/2017 -	-	-	0/0
1273	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	268.27	05/2016 -	-	-	0/0
1274	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1275	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41(O) -	0/0
1276	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1277	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	221.91	03/2020 -	03/2021	12(O) -	0/0
1278	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 -	11/2020	40(O) -	0/0
1279	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	34.36	- -	07/2020	- -	0/0
1280	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	- -	-	-	0/0
1281	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	.00	- -	05/2020	- -	0/0
1282	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	.00	- -	05/2020	- -	0/0
1283	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1284	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	.00	- -	08/2021	- -	0/0
1285	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	08/2021	- -	0/0
1286	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	29.45	- -	03/2020	- -	0/0
1287	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1288	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1289	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	06/2021	- -	0/0
1290	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	.00	- -	04/2021	- -	0/0
1291	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1292	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA - [N24000912]MORTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1293	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1294	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1295	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1296	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1297	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1298	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA - [N24000918]MORTH,ODISHA ,	07/2013	251.92 -	251.92	225.98	10/2015 -	-	-	0/0
1299	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA - [N24000919]MORTH,ODISHA ,	07/2013	265.35 -	265.35	247.56	10/2015 -	-	-	0/0
1300	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA - [N24000924]MORTH,ODISHA ,	03/2015	229.29 -	229.29	163.40	11/2015 -	-	-	0/0
1301	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	666.72	- -	06/2019	- -	0/0
1302	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	786.68	- -	-	-	0/0
1303	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	904.82	722.92	- -	06/2019	- -	0/0
1304	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.09	- -	03/2020	- -	0/0
1305	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	194.95	12/2017 -	12/2019	24(O) -	0/0
1306	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	642.01	- -	11/2017	-	0/0
1307	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	1,213.89	09/2019 -	09/2019	0(O) -	0/0
1308	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	1,004.18	- -	04/2020	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1309	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	76.83	03/2020 -	04/2020	1(O) -	0/0
1310	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	261.76	40.89	- -	01/2021	- -	0/0
1311	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	37.68	- -	06/2019	- -	0/0
1312	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	9.03	- -	01/2020	- -	0/0
1313	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB ,	03/2018	322.48 -	322.48	48.73	07/2020 -	07/2020	0(O) -	0/0
1314	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB ,	03/2018	173.24 -	173.24	10.97	06/2020 -	06/2020	0(O) -	0/0
1315	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD,PUNJAB ,	03/2018	293.10 -	293.10	10.26	08/2020 -	08/2020	0(O) -	0/0
1316	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB ,	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019	0(O) -	0/0
1317	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]PWD,PUNJAB ,	03/2018	170.57 -	170.57	8.14	11/2020 -	11/2020	0(O) -	0/0
1318	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1319	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1320	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1321	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1322	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1323	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1324	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1325	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.00	06/2018 -	07/2019	13(O) -	0/4
1326	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	297.72	09/2016 -	03/2019	-	0/0
1327	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	605.33	10/2017 -	04/2019	-	0/0
1328	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	02/2019	-	0/0
1329	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	834.75	04/2018 -	03/2019	-	0/0
1330	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	06/2019	68(O) -	0/0
1331	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70(O) -	0/4
1332	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	03/2019	-	0/0
1333	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	257.52	-	03/2019	-	0/0
1334	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3(O) -	0/0
1335	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5(O) -	0/0
1336	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	09/2019	3(O) -	0/0
1337	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	661.85	-	11/2019	-	0/0
1338	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1339	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	232.49	01/2019 -	04/2019	-	0/0
1340	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	174.79	-	05/2020	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1341	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	848.00	- -	12/2019	- -	0/0
1342	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1343	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	605.00	04/2020 -	11/2019	-5(O) -	0/0
1344	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	329.90	10/2017 -	11/2020	37(O) -	0/0
1345	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	12/2020	- -	0/0
1346	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	198.85	- -	09/2020	- -	0/0
1347	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1348	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	73.00	- -	-	-	0/0
1349	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	.00	- -	-	-	0/0
1350	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	.00	- -	-	-	0/0
1351	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD,RAJASTHAN ,	11/2017	187.82 -	187.82	35.82	04/2018 -	-	-	1/4
1352	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD,RAJASTHAN ,	10/2014	382.81 -	382.81	333.27	01/2015 -	-	-	3/4
1353	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD,RAJASTHAN ,	01/2017	179.32 -	179.32	92.66	11/2017 -	-	-	2/4
1354	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD,RAJASTHAN ,	03/2016	155.77 -	155.77	97.42	09/2016 -	-	-	3/4
1355	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD,RAJASTHAN ,	01/2012	378.07 478.73	478.73	188.98	01/2014 -	-	-	1/4
1356	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD,RAJASTHAN ,	10/2012	511.21 -	511.21	813.54	10/2013 -	-	-	3/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1357	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD,RAJASTHAN ,	03/2009	501.00 671.54	671.54	659.98	09/2013 -	-	-	3/4
1358	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD,RAJASTHAN ,	11/2017	163.95 -	163.95	42.04	04/2018 -	-	-	3/4
1359	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD,RAJASTHAN ,	02/2018	370.30 -	370.30	167.46	06/2018 -	-	-	1/4
1360	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD,RAJASTHAN ,	02/2018	341.79 -	341.79	88.38	05/2018 -	-	-	1/4
1361	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD,RAJASTHAN ,	12/2015	621.43 -	621.43	402.14	10/2016 -	-	-	3/4
1362	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD,RAJASTHAN ,	01/2017	163.54 -	163.54	84.10	07/2017 -	-	-	2/4
1363	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	196.76	08/2013 -	12/2019	76(O) -	0/0
1364	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	132.27	08/2013 -	-	-	0/0
1365	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82(O) 0	0/0
1366	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	388.00	78.33	10/2017 -	-	-	1/4
1367	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	78.78	11/2017 -	-	-	1/4
1368	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	77.39	- -	-	-	0/0
1369	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	30.70	11/2017 -	-	-	1/4
1370	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1371	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,330.29	12/2013 -	-	-	0/0
1372	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	326.23	06/2013 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1373	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	-	-	0/0
1374	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	-	-	0/0
1375	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1376	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1377	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1378	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1379	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	956.75	11/2017 -	07/2019	20(O) -	0/0
1380	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	96.48	12/2017 -	08/2019	20(O) -	0/0
1381	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1382	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	627.66	07/2008 -	-	-	0/0
1383	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	288.38	08/2018 -	03/2020	19(O) -	0/0
1384	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	405.31	07/2018 -	05/2020	22(O) -	0/0
1385	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	54.70	03/2020 -	03/2020	0(O) -	0/0
1386	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	405.31	07/2016 -	05/2020	46(O) -	0/0
1387	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	.00	08/2017 -	09/2020	37(O) -	0/0
1388	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	95.96	09/2017 -	11/2019	26(O) -	0/0
1389	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	.00	09/2017 -	08/2020	35(O) -	0/0
1390	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	84.22	- -	03/2020	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1391	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	- -	02/2021	- -	0/0
1392	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	32.77	- -	11/2020	- -	0/0
1393	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	31.45	- -	11/2020	- -	0/0
1394	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	633.55	.00	- -	-	-	0/0
1395	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,016.92	.00	- -	04/2021	- -	0/0
1396	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,065.96	.00	- -	-	-	0/0
1397	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019	39(O) -	0/0
1398	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1399	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	.00	02/2017 -	-	-	0/1
1400	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	.00	01/2017 -	-	-	0/0
1401	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	691.30	11/2018 -	07/2019	8(O) -	0/0
1402	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1403	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	.00	- -	-	-	0/0
1404	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	.00	- -	-	-	0/0
1405	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1406	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI, TELANGANA ,	03/2018	828.29 -	828.29	.00	-	-	-	0/0
1407	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD, TELANGANA ,	10/2016	298.32 -	298.32	62.22	02/2019 -	12/2019	10(O) -	0/0
1408	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD, TELANGANA ,	10/2016	248.83 -	248.83	79.02	03/2019 -	12/2019	9(O) -	0/0
1409	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD, TELANGANA ,	01/2017	244.54 -	244.54	122.31	05/2019 -	07/2019	2(O) -	0/0
1410	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]PWD, TELANGANA ,	01/2017	196.52 -	196.52	92.88	10/2019 -	10/2019	0(O) -	0/0
1411	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]PWD, TELANGANA ,	01/2017	283.00 -	283.00	121.47	12/2019 -	12/2019	0(O) -	0/0
1412	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD, TELANGANA ,	01/2017	359.27 -	359.27	200.24	05/2019 -	08/2019	3(O) -	0/0
1413	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD, TELANGANA ,	01/2017	300.00 -	300.00	83.83	05/2019 -	12/2019	7(O) -	0/0
1414	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]PWD, TELANGANA ,	01/2018	283.15 -	283.15	32.04	05/2020 -	05/2020	0(O) -	0/0
1415	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD, TELANGANA ,	01/2018	230.03 -	230.03	80.71	12/2019 -	12/2019	0(O) -	0/0
1416	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD, TELANGANA ,	02/2018	206.13 -	206.13	94.93	06/2020 -	06/2020	0(O) -	0/0
1417	REHABILITATION AND UPGRADEMENT OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD, TELANGANA ,	02/2018	294.13 -	294.13	23.54	11/2019 -	11/2019	0(O) -	0/0
1418	REHABILITATION AND UPGRADEMENT OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD, TELANGANA ,	02/2018	220.28 -	220.28	7.40	11/2019 -	11/2019	0(O) -	0/0
1419	REHABILITATION AND UPGRADEMENT OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTING - [N24000992]PWD, TELANGANA ,	02/2018	426.52 -	426.52	134.38	04/2020 -	04/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1420	REHABILITATION AND UPGRADE OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD, TELANGANA ,	03/2018	322.81 -	322.81	.34	09/2020 -	09/2020	0(O) -	0/0
1421	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD, TELANGANA ,	03/2018	626.76 -	626.76	46.62	07/2020 -	07/2020	0(O) -	0/0
1422	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD, TELANGANA ,	01/2017	605.08 -	605.08	213.00	10/2019 -	10/2019	0(O) -	0/0
1423	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD, TELANGANA ,	03/2018	192.67 -	192.67	.00	07/2019 -	07/2019	0(O) -	0/0
1424	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD, TELANGANA ,	01/2019	193.19 -	193.19	.00	- -	-	-	0/0
1425	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00	297.12	03/2018 -	-	-	3/4
1426	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1427	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1428	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	459.07	01/2014 -	09/2018	-	0/0
1429	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-	-	0/0
1430	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH, UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1431	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1432	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH ,	04/2014	351.34 -	351.34	433.68	01/2016 -	-	-	0/0
1433	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH ,	09/2015	368.73 -	368.73	232.93	09/2016 -	-	-	0/0
1434	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH ,	06/2014	301.04 -	301.04	207.94	01/2016 -	-	-	0/0
1435	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH ,	04/2014	495.78 -	495.78	633.24	01/2016 -	-	-	0/0
1436	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019	29(O) -	0/0
1437	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD, UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1438	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	839.63	03/2018 -	-	-	0/0
1439	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	01/2019	-	0/0
1440	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1441	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1442	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1443	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1444	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1445	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	86.63	08/2015 -	09/2019	49(O) -	0/0
1446	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	623.53	- -	-	-	0/0
1447	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	988.72	06/2019 -	06/2019	0(O) -	0/0
1448	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	623.35	04/2019 -	04/2019	-	0/0
1449	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	92.37	- -	-	-	0/0
1450	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1451	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	276.87	04/2019 -	04/2019	-	0/0
1452	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	529.65	04/2019 -	-	-	0/0
1453	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	748.59	- -	02/2020	-	0/0
1454	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	13.33	- -	07/2020	-	0/0
1455	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	278.92	- -	04/2020	-	0/0
1456	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1457	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	425.19	- -	-	-	0/0
1458	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1459	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8(O) -	0/0
1460	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5(O) -	0/0
1461	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2(O) -	0/0
1462	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	1,597.26	03/2020 -	03/2020	0(O) -	0/0
1463	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	410.09	- -	05/2020	- -	0/0
1464	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1465	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1466	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1467	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1468	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1469	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0
1470	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	-	-	0/0
1471	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1472	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	-	-	-	0/0
1473	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	1,025.80	46.29	-	-	-	0/0
1474	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	1,115.28	113.90	-	-	-	0/0
1475	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	.00	-	-	-	0/0
1476	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	.00	-	-	-	0/0
1477	REHABILITATION AND UPGRADEATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH ,	03/2016	208.50 -	208.50	102.98	11/2019	11/2019	0(O)	0/0
1478	REHABILITATION AND UPGRADEATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	67.87	03/2020	03/2020	0(O)	0/0
1479	REHABILITATION AND UPGRADEATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	125.09	09/2019	09/2019	0(O)	0/0
1480	REHABILITATION AND UPGRADEATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	171.00	01/2020	01/2020	0(O)	0/0
1481	REHABILITATION AND UPGRADEATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	132.45	10/2018	07/2019	9(O)	0/0
1482	REHABILITATION AND UPGRADEATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.00	454.41	03/2017	07/2019	28(O)	0/0
1483	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	86.63	08/2015	07/2019	47(O)	0/0
1484	REHABILITATION AND UPGRADEATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH ,	03/2016	249.50 -	249.50	190.10	05/2019	05/2019	-	0/0
1485	REHABILITATION AND UPGRADEATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD,UTTAR PRADESH ,	10/2016	239.63 -	239.63	197.77	02/2019	06/2019	4(O)	0/0
1486	REHABILITATION AND UPGRADEATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH ,	03/2016	599.34 -	599.34	376.71	01/2020	01/2020	0(O)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1487	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69(O) -	0/0
1488	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	278.01	-	10/2019	-	0/0
1489	4-LANNING OF CHUTMALPUR-GANESHUPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	507.87	-	02/2020	-	0/0
1490	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	722.46	07/2018 -	12/2019	17(O) -	0/0
1491	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	8.24	05/2018 -	-	-	0/4
1492	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	35.51	06/2018 -	-	-	1/4
1493	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	31.00	05/2018 -	-	-	1/4
1494	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019	0(O) -	0/0
1495	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019	0(O) -	0/0
1496	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019	0(O) -	0/0
1497	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6(O) -	0/0
1498	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019	0(O) -	0/0
1499	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019	0(O) -	0/0
1500	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019	0(O) -	0/0
1501	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	02/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1502	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.31	- -	-	-	0/0
1503	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1504	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1505	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	44.88	07/2018 -	-	-	0/5
1506	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24(O) -	0/0
1507	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76(O) -	0/0
1508	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82(O) -	0/0
1509	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63(O) -	0/0
1510	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71(O) -	0/0
1511	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1512	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
1513	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18(O) -	0/0
1514	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	3,059.39	- -	06/2019	-	0/0
1515	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13(O) -	0/0
1516	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13(O) -	0/0
1517	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	28.21	06/2018 -	-	-	0/0
1518	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0
1519	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL ,	08/2014	600.87 720.97	720.97	636.36	11/2017 05/2019	05/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1520	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]PWD, WEST BENGAL ,	08/2014	823.20 937.76	937.76	703.65	11/2017 06/2019	06/2019	19(O) -1	0/0
1521	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL ,	03/2016	271.17 291.20	291.20	79.24	11/2018 11/2019	11/2019	12(O) 0	0/0
1522	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD, WEST BENGAL ,	01/2017	396.86 396.86	396.86	175.31	09/2019 -	-	-	0/0
1523	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD, WEST BENGAL ,	03/2017	202.69 202.69	202.69	75.72	11/2019 -	11/2019	0(O) -	0/0
1524	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD, WEST BENGAL ,	02/2018	426.18 426.18	426.18	217.48	09/2020 -	09/2020	0(O) -	0/0
1525	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD, WEST BENGAL ,	02/2018	218.70 218.70	218.70	17.84	11/2020 -	11/2020	0(O) -	0/0
1526	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]PWD, WEST BENGAL ,	03/2018	254.30 254.30	254.30	19.76	10/2020 -	10/2020	0(O) -	0/0
1527	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL ,	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24(O) -	0/0
1528	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24(O) -	0/0
1529	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD, WEST BENGAL ,	04/2014	279.70 398.52	398.52	314.34	08/2017 07/2019	07/2019	23(O) 1	0/0
	Total		4,92,220.43 -	5,07,134.63	2,33,897.96				150/803
	SHIPPING AND PORTS								
1530	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL, KERALA ,	07/2016	1,799.00 -	1,799.00	21.00	05/2021 -	05/2021	0(O) -	0/0
1531	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL, KERALA ,	05/2016	970.00 -	970.00	109.97	05/2020 -	05/2020	0(O) -	0/0
1532	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1533	JAL MARG VIKAS PROJECT - [N25000072]IWA, MULTI STATE ,	01/2018	4,200.00 -	4,200.00	1,256.55	03/2023 -	03/2023	0(O) -	0/0
1534	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1535	ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
1536	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL, TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	275.98	275.58	12/2017 -	-	-	1/1
1537	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU ,	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29(O) -	0/0
	Total		10,757.29 -	11,199.74	3,046.68				1/1
	<u>TELECOMMUNICATIONS</u>								
1538	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL, DELHI ,	06/2016	418.26 -	418.26	367.03	06/2017 -	-	-	0/0
1539	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL, MAHARASHTRA , Central Sector Projects	08/2017	215.30 219.60	219.60	33.46	05/2018 07/2019	07/2019	14(O) 1	0/0
1540	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL, MAHARASHTRA , Central Sector Projects	01/2018	231.80 240.10	240.10	117.63	10/2018 09/2019	09/2019	11(O) 0	0/0
1541	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE ,	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58(O) -	0/0
1542	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI, MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,310.53 -	27,553.13	9,169.02				0/70
	<u>URBAN DEVELOPMENT</u>								
1543	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL, ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1544	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD, ANDHRA PRADESH ,	06/2014	157.84 -	169.16	163.98	03/2017 -	-	-	4/5
1545	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1546	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD, ANDHRA PRADESH ,	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5(O) -	0/7
1547	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1548	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	69.60	06/2017 -	10/2020	40(O) -	0/0
1549	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,763.15	03/2016 -	-	-	0/0
1550	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	293.53	10/2019 -	03/2021	17(O) -	0/7
1551	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	703.90	12/2015 -	-	-	0/0
1552	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019	0(O) -	3/7
1553	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	35.77	04/2019 -	06/2020	14(O) -	0/2
1554	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1555	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	41.33	05/2020 -	05/2020	0(O) -	0/0
1556	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	146.45	06/2019 -	06/2019	0(O) -	0/0
1557	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	10.36	- -	12/2020	- -	0/0
1558	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	5.96	- 08/2020	03/2021	- 0	0/0
1559	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	18.58	04/2018 -	-	-	0/0
1560	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	28.71	11/2019 -	11/2019	0(O) -	0/0
1561	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	.00	- -	-	-	0/0
1562	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
1563	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59(O) -	2/8
1564	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1565	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1566	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0
1567	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1568	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	80.06	03/2016 -	09/2020	54(O) -	1/6
1569	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1570	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1571	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1572	RESIDENTIAL QUARTERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	62.56	02/2020 -	09/2020	7(O) -	0/0
1573	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	86.04	10/2012 -	03/2020	89(O) -	1/6
1574	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29(O) -	0/0
1575	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 -	03/2020	0(O) -	2/7
1576	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	33.82	02/2023 -	02/2023	0(O) -	0/0
1577	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	32.89	02/2023 -	02/2023	0(O) -	0/0
1578	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	205.00	156.21	03/2012 -	06/2019	87(O) -	17/20
1579	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	5,873.51	03/2018 -	12/2019	21(O) -	0/0
1580	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1581	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	27.31	07/2020 09/2020	09/2020	2(O) 0	3/14
1582	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	2,568.80	11/2021 12/2021	12/2021	1(O) 1	0/0
1583	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67(O) -	0/10
1584	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0
1585	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	800.00	.00	06/2021 -	06/2021	0(O) -	0/0
1586	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	488.28	418.79	05/2017 -	09/2019	28(O) -	8/12

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1587	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	187.10	04/2019 -	12/2019	8(O) -	4/8
1588	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	59.36	05/2020 -	12/2020	7(O) -	1/5
1589	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1590	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 559.47	559.47	314.01	07/2019 12/2019	12/2019	5(O) 0	0/0
1591	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-	-	12/24
1592	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	127.69	10/2019 -	03/2020	5(O) -	1/6
1593	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/2
1594	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	12.00	- -	11/2021	- -	0/0
1595	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	35.79	03/2020 02/2017	05/2021	14(O) 14	0/5
1596	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1597	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1598	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1599	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1600	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020	0(O) -	0/0
1601	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1602	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1603	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38(O) -	10/16
1604	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	126.07	04/2018 -	07/2019	15(O) -	5/6

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(June 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		1,75,890.06 -	1,82,113.88	78,238.37				74/183
	<u>WATER RESOURCES</u>								
1605	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15(O) -	0/19
1606	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	12/2019	0(O) -	0/0
	Total		10,384.61 -	55,782.44	16,450.19				0/19
	<u>DEFENCE PRODUCTION</u>								
1607	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	167.69	134.86	05/2018 03/2019	-	-	7/10
1608	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	285.95	79.33	08/2020 -	08/2020	0(O) -	7/16
	Total		453.64 -	453.64	214.19				14/26
	Grand Total		19,17,796.07	23,05,860.33	9,35,021.39				2732/5349


Summary of projects in the Flash Report for the month of June, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1623
Number of Projects completed/dropped/frozen in Current Month	52
Number of Projects elevated to the status of Major project during the current month	10
Number of Projects Added in Current Month	27
Number of Projects in Current Month	1608

Brief Analysis

Project Status with respect to Original Schedule: Out of 1608 projects, 24 projects are ahead of schedule, 390 projects are on schedule 550 projects are delayed. 479 projects do not have fixed dates of commissioning. 165 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

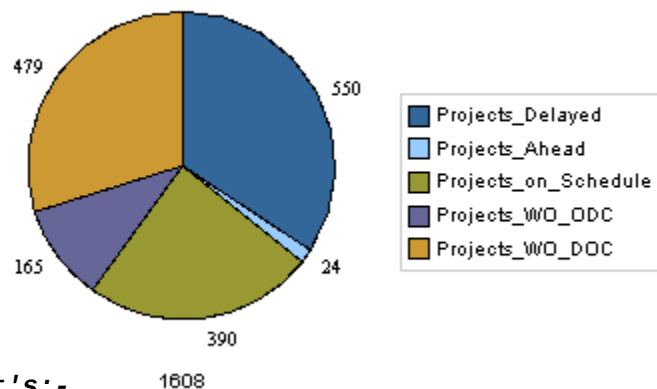


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1608 projects when sanctioned, was of the order of Rs. 1917796.07 crore but this was subsequently revised to Rs. 2305860.33 crore implying a cost overrun of 20.2%. The expenditure incurred on these projects till June, 2019 is Rs. 935021.39 crore, which is 40.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

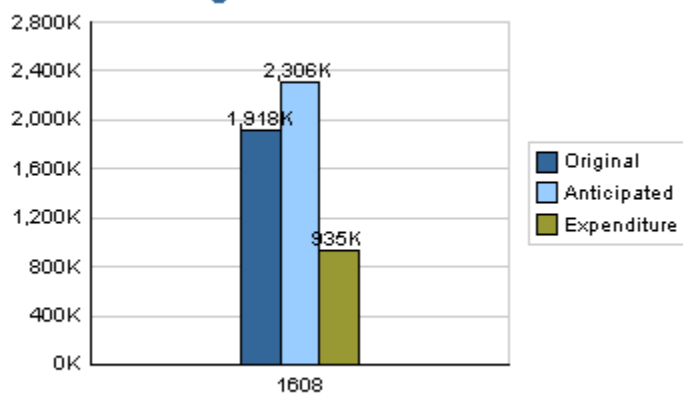

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

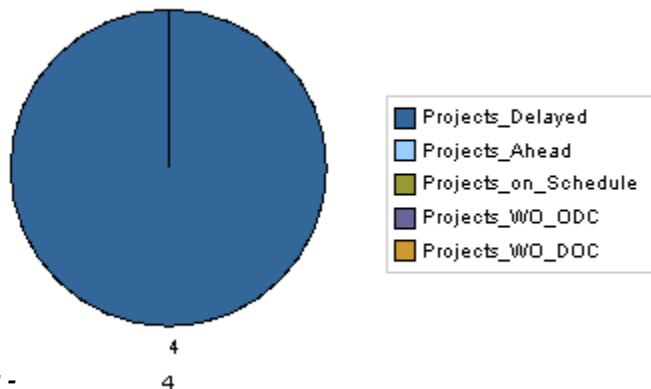

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till June, 2019 is Rs. 44910.74 crore, which is 55.9% of the anticipated cost of the projects.

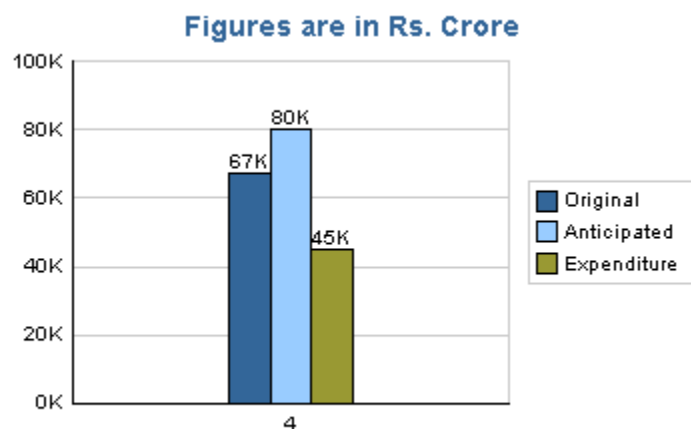

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

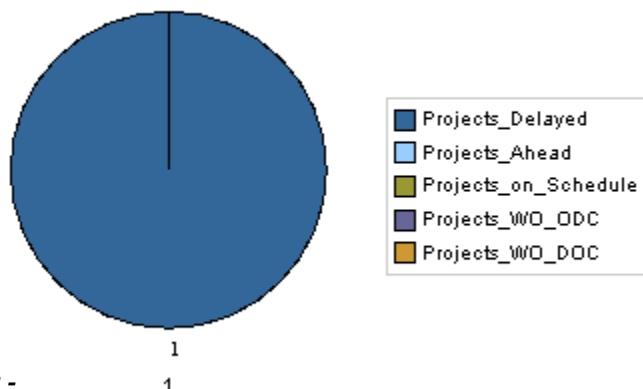


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 314.61 crore but this was subsequently anticipated to Rs. 441.33 crore implying a cost overrun of 40.3%. The expenditure incurred on these projects till June, 2019 is Rs. 85.79 crore, which is 19.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

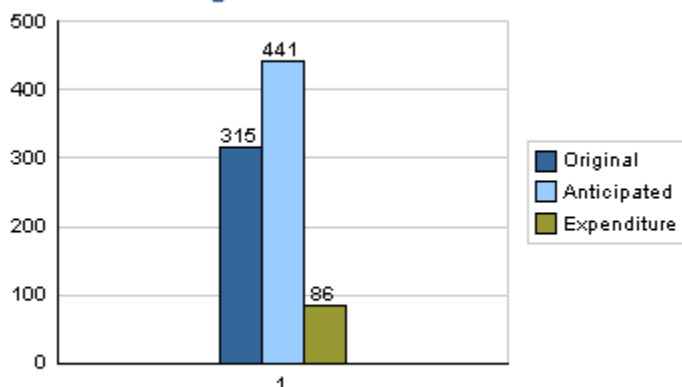

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	102
Number of Projects On Schedule	49
Number of Projects Delayed	30
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	22

Brief Analysis

Project Status with respect to Original Schedule: Out of 102 projects, 1 project is ahead of schedule, 49 projects are on schedule 30 projects are delayed. 22 projects do not have fixed dates of commissioning.

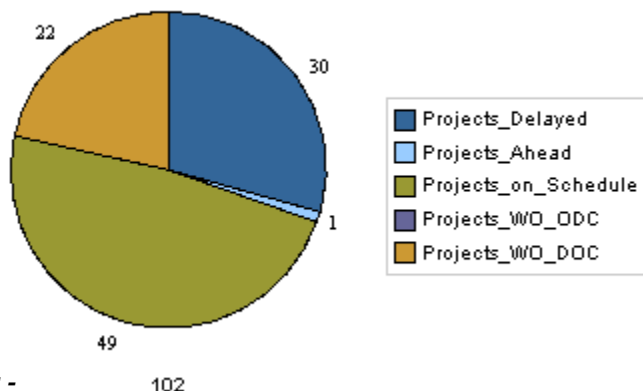


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 102 projects when sanctioned, was of the order of Rs. 101584.05 crore but this was subsequently anticipated to Rs. 102037.39 crore implying a cost overrun of .4%. The expenditure incurred on these projects till June, 2019 is Rs. 34533.21 crore, which is 33.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

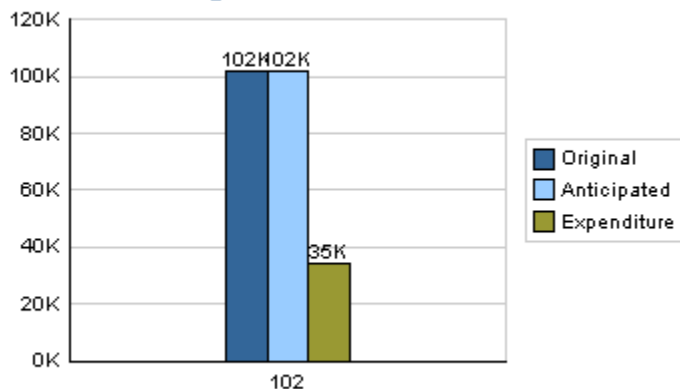

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	5
Number of Projects On Schedule	4
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project is delayed.

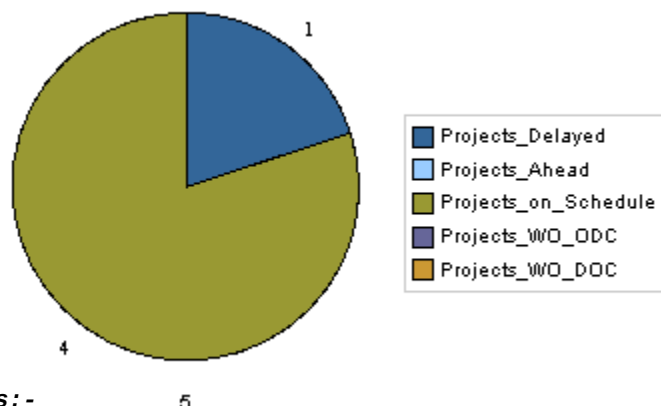


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1299.07 crore but this was subsequently anticipated to Rs. 1310.72 crore implying a cost overrun of .9%. The expenditure incurred on these projects till June, 2019 is Rs. 494.66 crore, which is 37.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

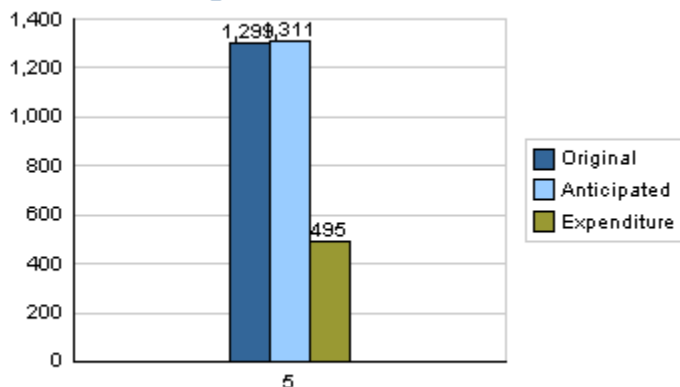

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	5
Number of Projects On Schedule	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 5 projects are on schedule

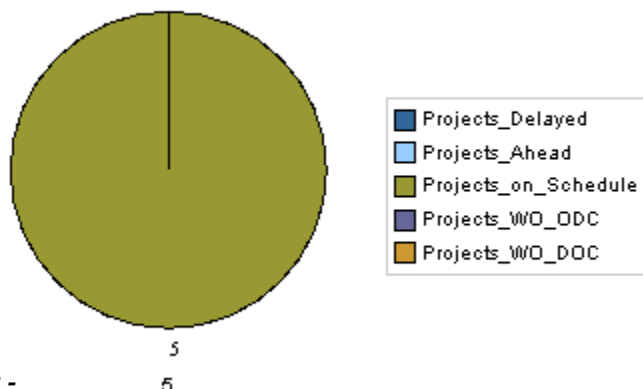


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore. The expenditure incurred on these projects till June, 2019 is Rs. 585.89 crore, which is 8.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

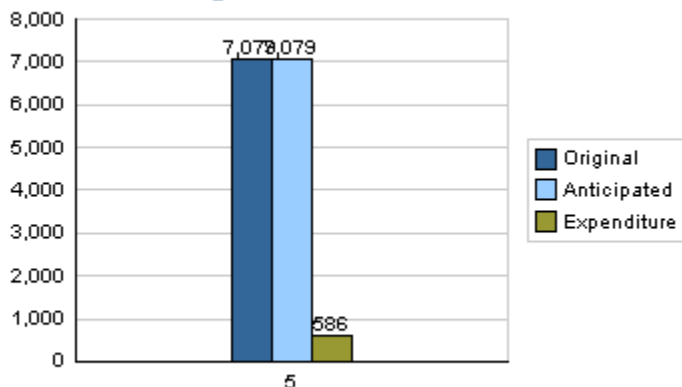

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	14
Number of Projects On Schedule	2
Number of Projects Delayed	9

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 14 projects, 2 projects are on schedule 9 projects are delayed. 3 projects do not have fixed dates of commissioning.

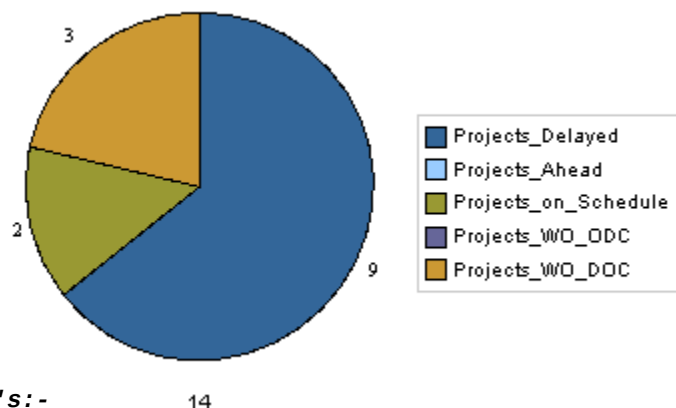


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 32793.01 crore but this was subsequently anticipated to Rs. 40195.41 crore implying a cost overrun of 22.6%. The expenditure incurred on these projects till June, 2019 is Rs. 23602.88 crore, which is 58.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

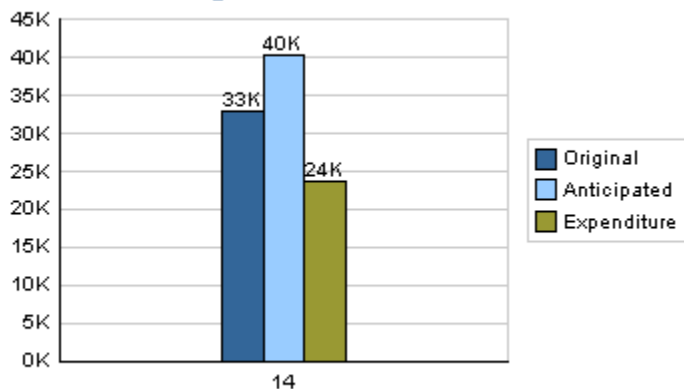

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	150
Number of Projects On Schedule	86
Number of Projects Delayed	44
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	12

Brief Analysis

Project Status with respect to Original Schedule: Out of 150 projects, 7 projects are ahead of schedule, 86 projects are on schedule 44 projects are delayed. 12 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

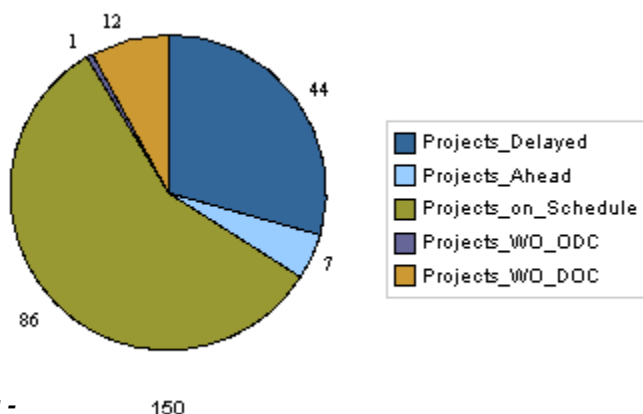


Total No Of Project's:-

150

Investment Scenario

Total original cost of implementation of 150 projects when sanctioned, was of the order of Rs. 247891.38 crore but this was subsequently anticipated to Rs. 255071.46 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till June, 2019 is Rs. 89795.86 crore, which is 35.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

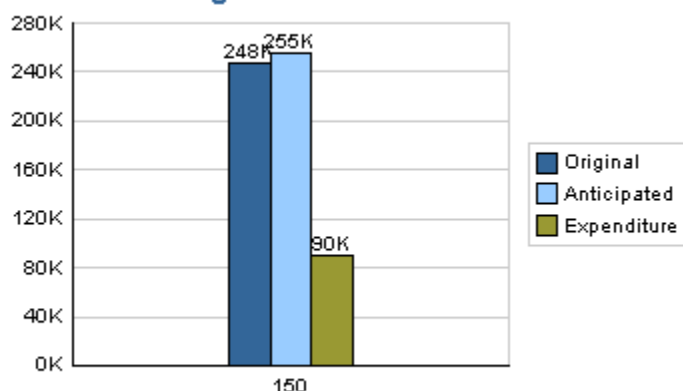

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	75
Number of Projects On Schedule	17
Number of Projects Delayed	52

Number of Projects Without Date Of Commissioning	6
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 75 projects, 17 projects are on schedule 52 projects are delayed. 6 projects do not have fixed dates of commissioning.

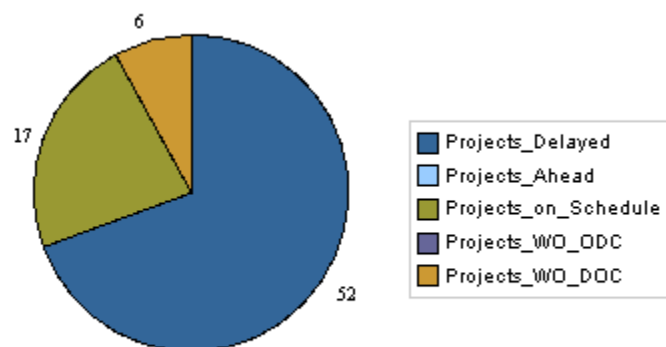


Total No Of Project's:-

75

Investment Scenario

Total original cost of implementation of 75 projects when sanctioned, was of the order of Rs. 277523.99 crore but this was subsequently anticipated to Rs. 351070.74 crore implying a cost overrun of 26.5%. The expenditure incurred on these projects till June, 2019 is Rs. 211507.55 crore, which is 60.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

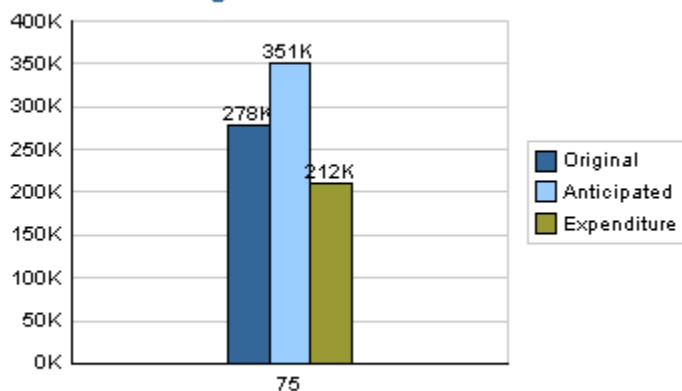

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

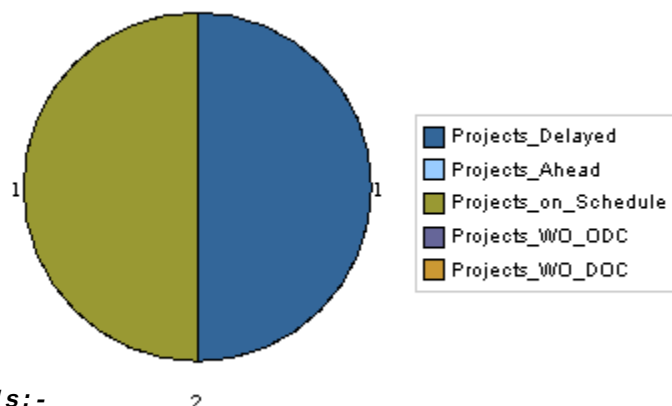


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 3272 crore but this was subsequently anticipated to Rs. 5281.3 crore implying a cost overrun of 61.4%. The expenditure incurred on these projects till June, 2019 is Rs. 3517.13 crore, which is 66.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

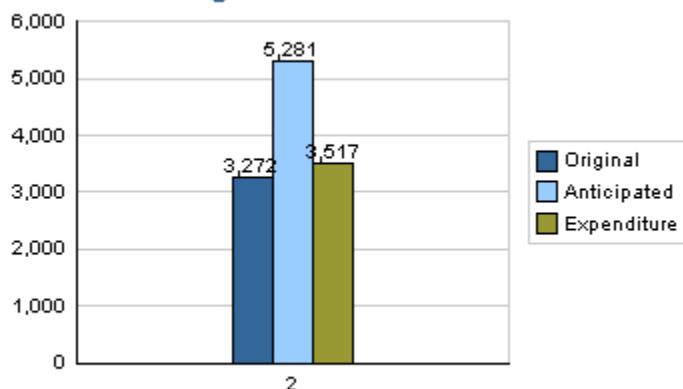

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	320
Number of Projects On Schedule	47
Number of Projects Delayed	138
Number of Projects Ahead	8
Number of Projects Without Original Date of Commissioning	65
Number of Projects Without Date Of Commissioning	62

Brief Analysis

Project Status with respect to Original Schedule: Out of 320 projects, 8 projects are ahead of schedule, 47 projects are on schedule 138 projects are delayed. 62 projects do not have fixed dates of commissioning. 65 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

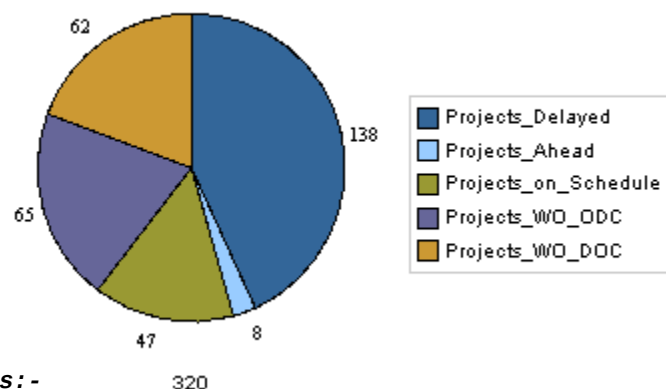


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 320 projects when sanctioned, was of the order of Rs. 464773.55 crore but this was subsequently anticipated to Rs. 670541.38 crore implying a cost overrun of 44.3%. The expenditure incurred on these projects till June, 2019 is Rs. 181731.32 crore, which is 27.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

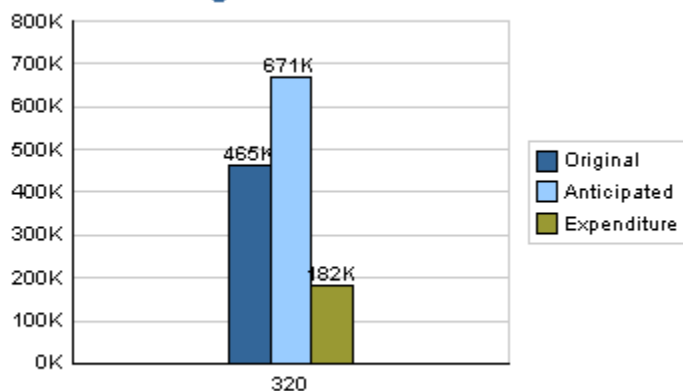

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	831
Number of Projects On Schedule	165
Number of Projects Delayed	227
Number of Projects Ahead	8
Number of Projects Without Original Date of Commissioning	90
Number of Projects Without Date Of Commissioning	341

Brief Analysis

Project Status with respect to Original Schedule: Out of 831 projects, 8 projects are ahead of schedule, 165 projects are on schedule 227 projects are delayed. 341 projects do not have fixed dates of commissioning. 90 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

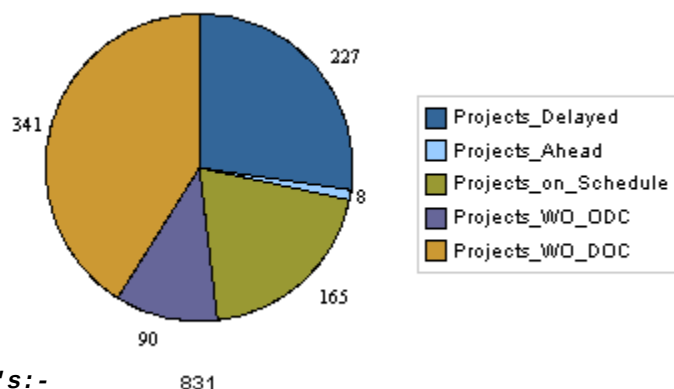

Investment Scenario

Total original cost of implementation of 831 projects when sanctioned, was of the order of Rs. 492220.43 crore but this was subsequently anticipated to Rs. 507134.63 crore implying a cost overrun of 3%. The expenditure incurred on these projects till June, 2019 is Rs. 233897.96 crore, which is 46.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

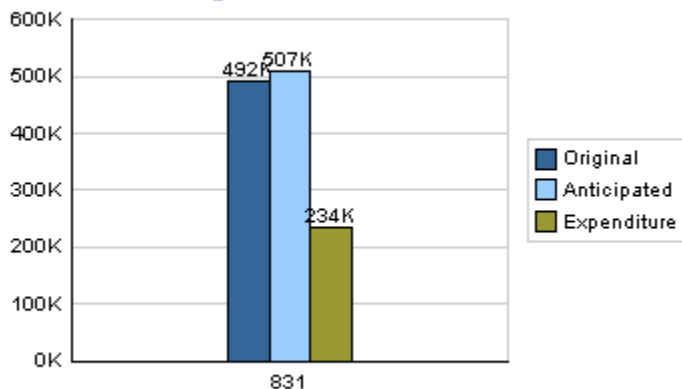

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	3
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule 1 project is delayed. 4 projects do not have fixed dates of commissioning.

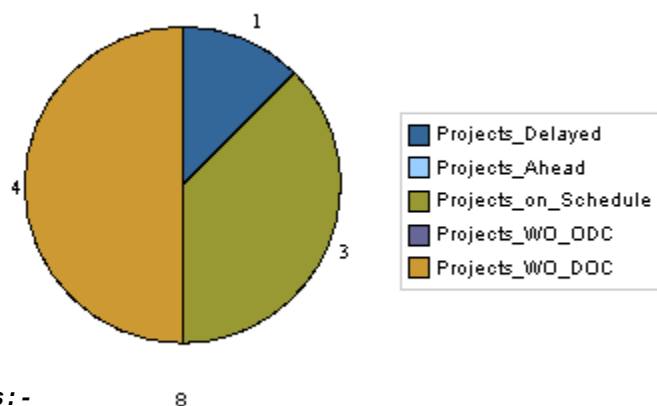


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 10757.29 crore but this was subsequently anticipated to Rs. 11199.74 crore implying a cost overrun of 4.1%. The expenditure incurred on these projects till June, 2019 is Rs. 3046.68 crore, which is 27.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

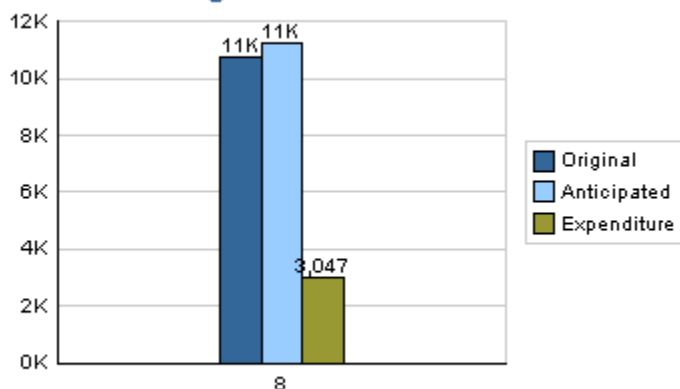

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	5
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed. 2 projects do not have fixed dates of commissioning.

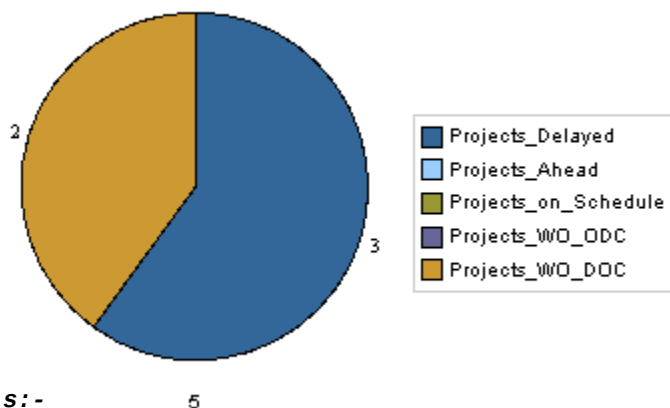


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 16310.53 crore but this was subsequently anticipated to Rs. 27553.13 crore implying a cost overrun of 68.9%. The expenditure incurred on these projects till June, 2019 is Rs. 9169.02 crore, which is 33.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

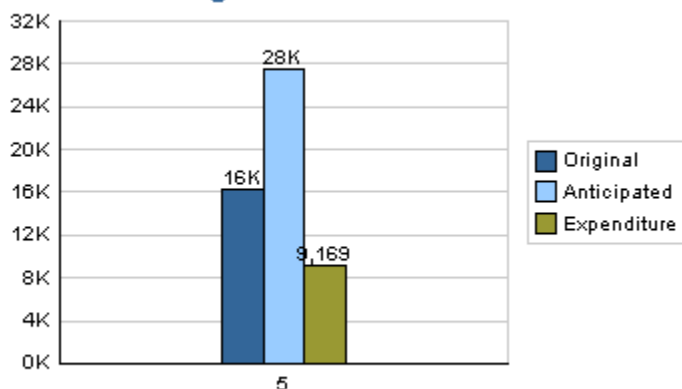

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	62
Number of Projects On Schedule	9
Number of Projects Delayed	26
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	24

Brief Analysis

Project Status with respect to Original Schedule: Out of 62 projects, 9 projects are on schedule 26 projects are delayed. 24 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

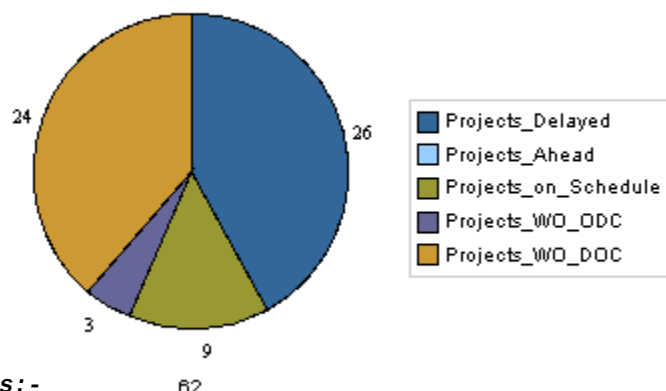


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 62 projects when sanctioned, was of the order of Rs. 175890.06 crore but this was subsequently anticipated to Rs. 182113.88 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till June, 2019 is Rs. 78238.37 crore, which is 43% of the anticipated cost of the projects.

Figures are in Rs. Crore

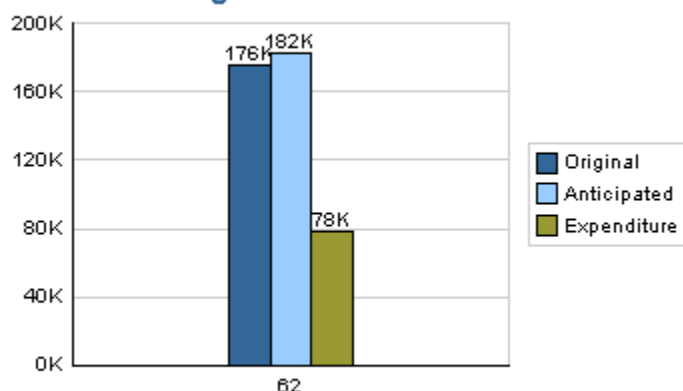

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.

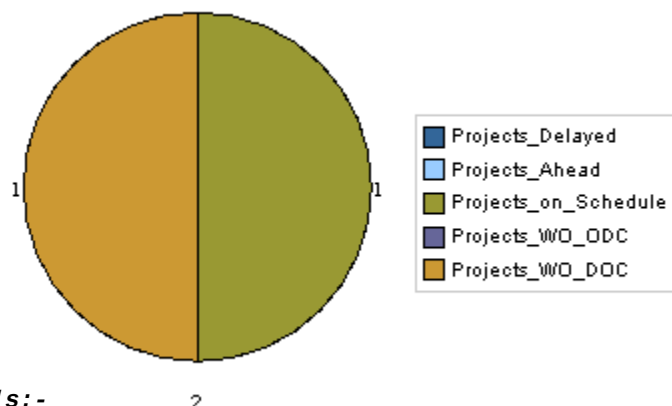


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 453.64 crore The expenditure incurred on these projects till June, 2019 is Rs. 214.19 crore, which is 47.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

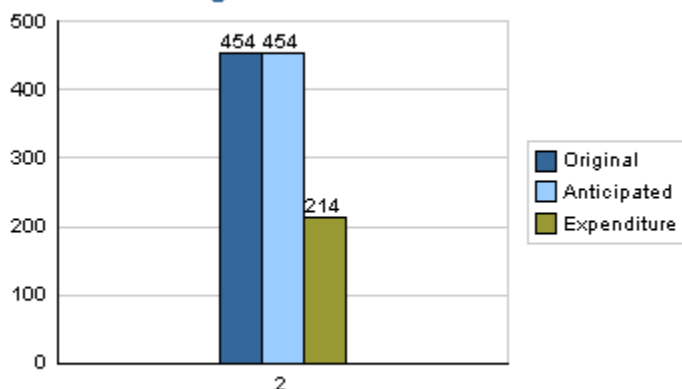

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (JUNE 2019)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,786.01	2,893.59	354.16
2	ANDHRA PRADESH	76	1,20,417.63	1,69,552.26	40,627.18
3	ARUNACHAL PRADESH	38	19,572.19	38,180.7	20,640.04
4	ASSAM	46	24,306.66	28,182.62	13,319.93
5	BIHAR	90	76,140.96	1,21,061.57	59,587.88
6	CHHATISGARH	36	74,436.64	85,988.61	42,378.17
7	D & N HAVELI	1	6,086.08	5,842.31	4,780.91
8	DELHI	23	55,482.27	62,957.5	41,514.59
9	GOA	12	5,779.51	5,789.94	2,136.8
10	GUJARAT	55	53,993.8	59,554.74	38,445.42
11	HARYANA	33	22,790.13	24,261.34	11,102.26
12	HIMACHAL PRADESH	12	16,702.17	26,812.7	11,889.06
13	JAMMU AND KASHMIR	12	24,323.57	49,772.57	32,478
14	JHARKHAND	48	65,190.64	69,228.28	25,743.36
15	KARNATAKA	63	71,493.59	74,471.44	17,550.67
16	KERALA	22	39,078.6	41,496.22	13,364.1
17	MADHYA PRADESH	74	84,643.15	91,734.75	39,600.02
18	MAHARASHTRA	254	2,35,175.32	2,44,487.65	94,749.19
19	MANIPUR	4	5,767.05	15,062.08	8,964.5
20	MEGHALAYA	6	2,760.77	7,854.31	975.79
21	MIZORAM	12	7,570.66	10,884.08	4,274.21
22	MULTI STATE	137	3,27,381.15	4,34,465.77	1,38,477.64
23	NAGALAND	21	13,711.07	14,384.55	1,579.01
24	ODISHA	97	1,06,664.83	1,09,523.39	42,237.25
25	PUNJAB	27	13,539.35	13,656.94	7,753.72
26	RAJASTHAN	62	47,167.18	53,718.94	31,547.35
27	SIKKIM	9	3,476.73	6,308.8	1,065.18
28	TAMIL NADU	67	1,15,852.79	1,34,404.28	63,913.2
29	TELANGANA	57	40,255.16	43,275.56	11,873.12
30	TRIPURA	5	1,466.46	1,628.65	862.24
31	UTTAR PRADESH	107	1,39,187.34	1,43,133.84	60,370.37
32	UTTARAKHAND	30	35,308.06	44,082.86	13,555.14
33	WEST BENGAL	63	59,288.55	71,207.49	37,310.93
TOTAL		1,608	19,17,796.07	23,05,860.33	9,35,021.39

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	13,711.00	12/2015 -	06/2020
	Total		14,951.00 -	23,420.00	19,495.74		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
3	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022
4	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	241.15	03/2012 -	03/2021
5	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	493.85	03/2017 -	03/2020
6	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	346.99	03/2010 -	03/2022
	<u>South-Eastern Coal Fields Limited</u>						
7	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	203.90	03/2015 -	03/2020
	<u>Western Coal Fields Limited</u>						
8	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	-
	Total		1,678.34 -	1,985.40	2,080.20		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	523.00	508.29	03/2018 -	-
	Total		505.58 -	523.00	508.29		
	<u>PETROLEUM</u>						
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>						
11	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,265.01	05/2013 12/2019	12/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,854.79 -	3,376.06	2,814.86		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
12	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	9/2002	3,919.59 -	9,997.11	7,399.82	09/2009 -	12/2021
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	9/2003	6,285.33 -	19,496.34	10,868.18	09/2010 -	-
	<u>National Thermal Power Corporation</u>						
14	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	1/2007	5,353.00 -	9,996.59	7,816.71	07/2012 -	09/2020
15	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	12,104.40	10/2017 03/2020	03/2020
	<u>Power Grid Corporation Of India Limited</u>						
16	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	2/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022
17	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	5/2005	1,779.29 -	2,187.32	2,237.45	11/2008 06/2019	08/2019
18	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
19	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194	5/2015	436.68 -	602.44	561.74	12/2016 -	07/2019
20	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) [N18000235	11/2016	330.00 -	332.00	331.46	11/2017 -	04/2019
	<u>Thdc India Limited</u>						
21	DHUKWAN SMALL HYDRO PROJECT - [N18000189	5/2011	195.42 -	294.60	292.85	02/2014 -	10/2019
22	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	7/2006	1,657.00 -	5,024.35	2,935.92	02/2016 -	06/2022
	Total		43,419.99 -	76,029.13	57,893.11		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
23	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	305.00	260.45	03/2019 12/2019	12/2019
	<u>East Central Railways</u>						
24	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	3/1999	1,033.07 -	3,376.00	3,180.37	- -	03/2021
25	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	4/2003	528.65 -	2,066.77	1,403.38	- -	03/2023
26	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	4/1997	324.73 -	1,156.41	1,028.71	03/2012 -	03/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
27	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	4/1991	329.39 -	1,483.14	815.41	- -	12/2021
28	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	4/1998	180.82 -	727.29	488.81	- -	09/2019
29	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	1/1991	332.15 -	559.91	541.07	07/2014 -	-
30	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	4/2013	213.01 -	400.17	378.41	- -	01/2020
31	SAKRI-HASANPUR ROAD (NL) - [N22000171	4/1999	325.00 -	729.92	349.60	- -	03/2021
32	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	4/1997	162.87 -	589.15	303.96	- -	03/2022
33	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	4/1996	477.88 283.95	749.00	672.82	03/2012 -	03/2020
	<u>East Coast Railway</u>						
34	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	3/2012	155.81 -	238.03	224.63	03/2020 -	03/2020
	<u>Eastern Railways</u>						
35	DEOGHAR - SULTANGANJ (INL), ER - [220100273	4/2000	607.09 -	1,026.30	637.72	02/2013 -	03/2024
36	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249	4/2011	166.89 -	166.89	246.00	- -	03/2025
37	BANDEL-BOINCHI 3RD LINE - [N22000221	4/2011	288.35 -	364.98	364.98	- -	03/2020
38	PIRPAINTI-BHAGALPUR - [N22000222	4/2011	261.38 -	444.81	444.81	- -	05/2019
39	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	4/2011	175.80 -	226.22	226.22	- -	-
	<u>Metropolitan Rapid Transport Projects</u>						
40	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
41	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	<u>North Central Railway</u>						
42	ETAWAH-MAINPURI (NL),NCR - [220100318	4/1997	120.00 -	346.00	345.51	12/2008 03/2015	03/2015
	<u>North East Frontier Railway</u>						
43	BHAIRABI SAIRONG, NL, NEFR - [N22000100	4/2008	2,393.47 -	5,021.45	2,933.84	03/2014 03/2022	03/2022
44	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	9/2006	385.20 -	1,532.00	606.19	03/2019 -	03/2020
45	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	4/2011	314.00 -	700.00	687.37	03/2019 -	03/2019
46	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	4/1999	819.23 -	1,871.00	1,082.01	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
47	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	9/2006	532.87 -	2,145.00	932.80	03/2019 -	03/2020
48	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	13,809.00	8,818.98	03/2011 -	03/2020
49	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	4/2000	1,180.19 -	3,500.00	3,257.97	12/2008 -	03/2019
	<u>North Eastern Railway</u>						
50	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	12/2022
	<u>North Western Railway</u>						
51	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	245.81	11/2019 -	05/2020
52	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	410.00	341.67	02/2019 -	12/2019
	<u>Northern Railway</u>						
53	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,010.00	644.09	07/2012 -	03/2024
	<u>Rail Vikas Nigam Ltd.</u>						
54	HARIDASPUR-PARADEEP(NL) - [220100285]	4/1996	1,185.64 -	1,844.47	1,709.83	12/2017 -	03/2020
55	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,200.00	1,100.58	03/2019 -	03/2020
56	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,500.00	1,197.11	03/2020 -	03/2020
57	BANASPAANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,120.00	977.00	03/2019 -	03/2021
58	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,950.00	1,803.73	03/2020 -	03/2020
59	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	668.38	03/2016 -	12/2020
60	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	385.00	381.48	03/2009 03/2009	12/2019
	<u>South Central Railway</u>						
61	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
	<u>South Eastern Railway</u>						
62	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019
	<u>Southern Railway</u>						
63	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020
64	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]	2/1999	257.00 257.00	257.00	268.31	03/2018 -	03/2018
65	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	2/1996	268.87 -	950.00	927.86	03/2005 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
66	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019
67	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	980.00	669.21	03/2020 -	03/2021
68	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	4/1999	198.68 -	556.64	303.72	- -	-
	<u>West Central Railway</u>						
69	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023
	<u>Western Railway</u>						
70	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	4/2006	117.36 196.95	202.35	404.70	03/2011 03/2017	03/2017
71	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,310.23	1,294.00	03/2020 03/2021	03/2021
	Total		31,870.88 -	83,413.48	57,743.63		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
72	SARAD VANI PIMPALGAON - [N24001103]	1/2017	250.46 -	250.46	1,691.63	07/2019 -	07/2019
73	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]	2/2017	406.51 -	406.51	406.58	06/2019 -	06/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
74	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	168.40	11/2018 -	-
75	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	182.19	01/2019 -	-
	<u>National Highways Authority Of India</u>						
76	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	280.00	472.00	02/2009 -	-
77	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.52	10/2013 -	-
78	KANDLA - MUNDRA PORT - [N24000175]	1/2011	953.88 -	953.88	976.79	07/2013 -	12/2018
79	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,330.29	12/2013 -	-
80	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
81	PATNA-MUZZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	885.31	02/2013 -	06/2019
82	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-
83	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
84	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	2,580.88	07/2015 -	03/2019
85	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-
86	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
87	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
88	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019
89	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	01/2019
90	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	839.63	03/2018 -	-
91	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	834.75	04/2018 -	03/2019
92	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]	9/2015	414.51 -	414.00	529.62	05/2018 -	06/2020
93	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	556.02	08/2016 -	02/2019
94	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]	10/2015	597.00 -	597.00	605.33	10/2017 -	04/2019
95	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	495.78	633.24	01/2016 -	-
96	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	351.34	433.68	01/2016 -	-
97	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-
98	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	2/2018	1,052.21 -	1,052.21	1,080.00	- -	01/2021
99	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	3/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020
100	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	605.84	722.46	07/2018 -	12/2019
101	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]	9/2016	1,244.10 -	1,244.10	1,275.00	- -	02/2020
102	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	762.75	07/2019 -	07/2019
103	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	571.35	07/2019 -	07/2019
104	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	627.66	07/2008 -	-
105	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	1,665.00	3,059.39	- -	06/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
107	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	3,424.19	01/2018 -	02/2019
108	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	12/2018
109	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	03/2019
110	NAGPUR - KONDHALI - [N24000472]	9/2005	168.00 -	168.00	226.24	06/2006 -	-
111	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-
112	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-
113	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	733.33	07/2014 -	06/2020
114	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	459.07	01/2014 -	09/2018
115	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019
116	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,864.34	06/2014 -	-
117	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020
118	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019
119	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019
120	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,930.61	09/2014 -	-
121	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,075.87	06/2014 -	-
122	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	566.60	11/2013 -	12/2018
123	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	843.67	07/2013 -	06/2019
124	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
125	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.73	03/2014 -	-
126	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019
127	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	1,509.10	3,187.21	09/2012 -	-
128	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019
129	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	04/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
130	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019
131	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019
132	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019
133	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	325.00	469.54	05/2013 -	-
134	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019
135	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
136	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]	2/2010	617.00 -	617.00	943.17	08/2012 -	12/2019
137	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	340.12	07/2009 -	-
138	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019
139	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020
140	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019
141	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	319.96	04/2009 -	07/2019
142	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	167.64	268.94	11/2008 -	-
143	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	195.35	11/2008 -	-
	<u>National Highways Development Project</u>						
144	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE [N24000251]	3/2015	297.00 -	297.00	306.64	04/2018 -	-
145	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 [N24000371]	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019
146	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020
	<u>Public Works Dept Of State</u>						
147	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019
148	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	8/2010	193.69 -	327.92	254.24	10/2010 -	12/2019
149	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	3/2012	207.03 -	389.45	275.19	05/2012 -	-
150	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	8/2010	195.04 -	377.99	296.28	10/2010 -	06/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
151	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]	10/2012	511.21 -	511.21	813.54	10/2013 -	-
152	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019
153	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]	9/2012	511.00 -	511.00	2,323.04	10/2013 -	06/2019
154	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]	4/2013	151.59 -	151.59	196.76	08/2013 -	12/2019
	Total		70,661.09 -	75,671.35	1,07,628.39		
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
155	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	275.98	275.58	12/2017 -	-
	<u>Mumbai Port Trust</u>						
156	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	1/2007	366.39 -	669.46	411.12	12/2010 -	-
	Total		610.89 -	945.44	686.70		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmdc)</u>						
157	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	15,729.80	05/2015 07/2020	07/2020
	Total		15,525.00 -	23,140.00	15,729.80		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
158	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	488.28	418.79	05/2017 -	09/2019
159	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	169.16	163.98	03/2017 -	-
	<u>Chennai Metro Rail Ltd</u>						
160	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-
	<u>Hindustan Steelwork Construction Limited</u>						
161	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
162	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	175.94	178.65	12/2015 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
163	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019
	Total		21,246.24 -	26,692.51	23,387.83		
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
164	POLAVARAM IRRIGATION PROJECT - [N30000002	2/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021
	Total		10,151.04 -	55,548.87	16,417.99		
	Grand Total		2,12,474.84	3,70,745.24	3,04,386.54		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64	203.82	117.55	03/2023	03/2021
	Total		1,186.64	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
2	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,649.57	12/2020	08/2020
3	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00	151.00	147.35	09/2019	06/2019
4	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00	324.00	147.63	06/2020	03/2020
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00	664.00	564.33	12/2020	02/2020
6	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58	384.58	73.31	04/2021	04/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	33.85	09/2022	06/2021
	Total		7,556.58	8,557.58	2,616.04		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
8	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	480.35	03/2024	03/2022
	<u>East Central Railways</u>						
9	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23	348.23	156.48	03/2021	12/2020
	<u>North Central Railway</u>						
10	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00	2,001.00	395.59	03/2021 03/2023	03/2021
	<u>North East Frontier Railway</u>						
11	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48	4,084.69	285.46	12/2015 06/2021	03/2020
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27	612.00	181.63	12/2021	03/2020
13	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32	2,182.00	571.56	03/2022	03/2020
	<u>North Eastern Railway</u>						

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
14	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42	1,295.42	249.27	03/2022 -	12/2019
15	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469	4/2016	600.00	366.71	9.10	01/2022 -	01/2020
	<u>Rail Vikas Nigam Ltd.</u>						
16	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78	723.78	.19	12/2025 -	03/2025
	Total		12,769.97 -	15,241.30	2,329.63		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
17	PARSHURAM GHAT TO ARAWALI - [N24001133	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
	<u>National Highways Authority Of India</u>						
18	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02	157.49	-	03/2020 -	02/2020
19	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19	254.00	248.60	03/2020 -	09/2019
20	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79	552.90	480.73	03/2020 -	09/2019
21	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32	503.10	.95	03/2020 -	11/2019
22	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50	172.16	107.13	03/2020 -	06/2019
23	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68	235.90	89.96	03/2020 -	06/2019
24	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00	894.00	605.00	04/2020 -	11/2019
	Total		4,113.64 -	3,752.69	2,187.52		
	Grand Total		25,626.83	27,755.39	7,250.74		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	186.88	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	308.29	03/2022 -	03/2022
4	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
5	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
6	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	258.98	08/2019 -	08/2019
7	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.13	03/2024 -	03/2024
8	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
9	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	87.14	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
10	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	437.89	03/2021 -	03/2021
11	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,546.73	03/2026 -	03/2026
12	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	82.60	03/2027 -	03/2027
13	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,111.70	03/2029 -	03/2029
	<u>Neyveli Lignite Corporation</u>						
14	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	6,531.52	11/2021 -	11/2021
15	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
16	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.88	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
17	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
18	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	255.65	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
19	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
	<u>Singareni Colliers Company Limited</u>						
20	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
21	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.60	03/2021 -	03/2021
22	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.59	03/2021 -	03/2021
23	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	67.40	03/2020 -	03/2020
24	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
25	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.94	03/2023 -	03/2023
26	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
27	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.29	03/2023 -	03/2023
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	88.29	03/2022 -	03/2022
29	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
30	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,057.87	03/2023 -	03/2023
31	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
32	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,902.94	03/2023 -	03/2023
33	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	80.33	03/2020 -	03/2020
34	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
35	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
36	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	115.41	03/2021 -	03/2021
37	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	26.61	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
38	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	258.40	03/2025 -	03/2025
39	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
40	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	150.04	03/2021 -	03/2021
41	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	18.45	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	168.92	03/2021 -	03/2021
43	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
44	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	175.30	03/2020 -	03/2020
45	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
46	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.81	03/2020 -	03/2020
47	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	119.73	03/2023 -	03/2023
48	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020
49	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
	Total		74,644.94 -	74,867.48	18,817.30		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
50	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	79.33	08/2020 -	08/2020
	Total		285.95 -	285.95	79.33		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
51	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	81.46	11/2019 -	11/2019
52	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	72.95	11/2019 -	11/2019
53	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	88.74	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
54	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	92.10	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	335.25		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
55	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
56	UTKAL D AND E COAL BLOCK - [N10000011	5/2016	534.00 -	534.00	316.08	01/2020 01/2020	01/2020
57	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
58	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	0.30	04/2021 04/2021	04/2021
59	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014	9/2017	166.62 -	166.62	134.98	06/2019 -	06/2019
60	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	5,540.00	102.61	04/2021 04/2021	04/2021
	Total		7,078.62 -	7,078.62	585.89		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
61	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364	7/2017	580.20 -	580.20	27.71	02/2021 -	02/2021
62	PUNE POL STORAGE DEPOT - [N16000313	8/2016	282.64 -	282.64	105.42	08/2020 -	08/2020
63	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365	12/2017	1,524.06 -	1,524.06	13.10	12/2021 -	12/2021
64	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341	8/2017	750.00 -	750.00	32.69	12/2020 -	12/2020
65	MMPL PIPELINE REROUTING PROJECT - [N16000261	4/2013	449.58 -	449.58	153.11	12/2019 -	12/2019
66	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346	9/2018	11,130.00 -	11,130.00	14.14	03/2023 -	03/2023
67	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260	2/2016	554.00 -	554.00	315.44	02/2020 -	02/2020
68	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347	10/2018	206.26 -	206.26	0.30	03/2021 -	03/2021
	<u>Chennai Petroleum Corporation Limited</u>						
69	RE-LIQUIFIED NATURAL GAS - [N16000301	8/2017	421.00 -	421.00	100.28	08/2020 -	08/2020
70	BS-VI PROJECTS - [N16000295	9/2017	1,858.00 -	1,858.00	848.87	12/2019 -	12/2019
	<u>Gas Authority Of India Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
71	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	42.87	10/2022 -	10/2022
72	LAYING OF VIJAI PUR-AURAIYA PIPELINE SECTION OF VIJAI PUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,237.86	12/2020 -	12/2020
73	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	0.99	08/2020 -	08/2020
74	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,248.16	12/2020 -	12/2020
75	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	45.20	07/2022 -	07/2022
76	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
77	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	116.05	04/2022 -	04/2022
78	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	988.14	12/2020 -	12/2020
79	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	-	02/2021 -	02/2021
80	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	40.86	10/2022 -	10/2022
81	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	58.27	10/2022 -	10/2022
82	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	157.26	12/2020 -	12/2020
83	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	25.83	07/2022 -	07/2022
84	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,327.89	12/2020 -	12/2020
85	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	935.94	12/2021 -	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
86	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	600.15	03/2021 -	03/2021
87	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
88	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	104.23	11/2019 -	11/2019
89	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,068.39	03/2020 -	03/2020
90	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,386.04	06/2020 -	06/2020
91	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021
92	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	58.20	11/2020 -	11/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
93	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	359.31	09/2019 -	09/2019
94	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	4,913.36	07/2020 -	07/2020
95	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
	<u>Indian Oil Corporation Limited</u>						
96	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	1,453.91	07/2019 -	07/2019
97	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	109.28	12/2021 -	12/2021
98	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	27.66	01/2021 -	01/2021
99	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	0.44	08/2020 -	08/2020
100	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	300.50	10/2019 -	10/2019
101	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
102	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,409.29	09/2019 -	09/2019
103	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	10.40	12/2021 -	12/2021
104	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	240.73	10/2021 -	10/2021
105	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
106	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	598.85	10/2019 -	10/2019
107	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	759.67	12/2020 -	12/2020
108	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	887.73	08/2021 -	08/2021
109	BS-VI PROJECT AT PARADIP - [N16000362]	5/2019	3,361.00 -	3,361.00	269.74	08/2021 -	08/2021
110	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	8.19	03/2021 -	03/2021
111	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
112	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
113	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	161.68	08/2020 -	08/2020
114	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	6.82	02/2020 -	02/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
115	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	7.18	10/2021 -	10/2021
116	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY [N16000284]	9/2016	208.35 -	208.35	105.30	07/2020 -	07/2020
117	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	36.68	12/2019 -	12/2019
118	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	6.64	06/2020 -	06/2020
119	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
120	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
121	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	125.80	03/2021 -	03/2021
122	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY [N16000324]	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020
123	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
124	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	6.71	01/2021 -	01/2021
125	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,498.18	11/2019 -	11/2019
126	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	13.11	01/2021 -	01/2021
127	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	132.24	09/2019 -	09/2019
128	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
129	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	460.33	09/2019 -	09/2019
130	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
131	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	374.07	09/2019 -	09/2019
132	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY [N16000353]	10/2018	598.00 -	598.00	13.44	02/2020 -	02/2020
133	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	101.40	02/2020 -	02/2020
134	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,824.73	09/2019 -	09/2019
Oil & Natural Gas Corporation Limited							
135	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	370.84	03/2022 -	03/2022
136	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION [N16000357]	2/2019	2,292.46 -	2,292.46	45.81	05/2021 -	05/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
137	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	833.51	11/2019 -	11/2019
138	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	406.35	11/2019 -	11/2019
139	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	434.78	12/2019 -	12/2019
140	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	145.01	05/2020 -	05/2020
141	HEERA REDEVELOPMENT - PHASE III - [N16000360]	5/2019	2,494.68 -	2,494.68	-	12/2021 -	12/2021
142	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	354.67	03/2026 -	03/2026
	<u>Oil India Limited</u>						
143	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	82.95	10/2020 -	10/2020
144	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	682.90	6.12	02/2020 -	02/2020
145	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	142.82	12/2019 -	12/2019
146	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	3.30	08/2020 -	08/2020
	Total		1,23,801.13 -	1,25,295.60	31,834.83		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
147	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,595.15	11/2019 -	11/2019
148	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	1,780.00	03/2023 -	03/2023
149	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
150	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	8,127.53	01/2020 -	01/2020
151	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
	<u>Power Grid Corporation Of India Limited</u>						
152	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	116.76	02/2020 02/2020	02/2020
153	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020
154	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020
155	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
156	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238	3/2017	283.72 -	283.72	187.60	11/2019 11/2019	11/2019
157	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236	3/2017	251.60 -	251.60	185.94	06/2019 -	06/2019
158	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245	3/2017	379.95 -	379.95	52.63	12/2019 12/2019	12/2019
159	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019
160	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247	2/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020
	<u>Satluj Jal Vidyut Nigam Limited</u>						
161	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	648.33	222.91	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
162	KHURJA SUPER THERMAL POWER PROJECT - [N18000272	3/2019	11,089.42 -	11,089.42	503.39	09/2023 -	09/2023
163	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	1,587.16	298.76	09/2020 -	09/2020
	Total		73,024.95 -	73,786.25	26,257.13		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
164	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
165	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
166	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
167	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	66.23	03/2023 -	03/2023
168	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,180.11	03/2023 -	03/2023
169	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	140.79	03/2023 -	03/2023
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
170	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
171	KOSI BRIDGE (NL), ECR - [220100304	4/2002	499.41 -	516.02	389.29	03/2020 -	03/2020
	<u>East Coast Railway</u>						
172	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	3,382.95	325.64	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
173	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	224.63	03/2020 -	03/2020
	<u>Eastern Railways</u>						
174	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	693.80	403.81	03/2020 -	03/2020
	<u>North Central Railway</u>						
175	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	395.59	03/2021 03/2023	03/2021
176	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 03/2020	03/2020
177	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.56	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
178	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	454.63	03/2021 -	03/2021
179	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.67	03/2021 -	03/2021
180	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.14	03/2020 -	03/2020
181	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
182	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.92	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
183	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
184	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
185	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	12/2022
	<u>Northern Railway</u>						
186	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
187	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	2,812.27	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
188	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
189	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	309.16	12/2024 -	12/2024
190	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,541.10	03/2023 -	03/2023
191	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	1,100.00	987.29	03/2020 -	03/2020
192	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	267.40	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
193	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	1,950.00	1,803.73	03/2020 -	03/2020
194	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.67	709.85	12/2023 -	12/2023
195	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,485.85	994.43	12/2020 -	12/2020
196	PALANPUR-SAMAKHAYALI (DL) - [N22000144	4/2013	1,548.66 -	1,548.66	1,140.64	12/2021 -	12/2021
197	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	1/1991	2,335.67 -	2,335.68	482.27	12/2024 -	12/2024
198	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99 -	7,000.00	366.38	12/2026 -	12/2026
199	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,082.32	902.37	12/2021 -	12/2021
200	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	1,500.00	1,197.11	03/2020 -	03/2020
	<u>South Central Railway</u>						
201	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	4/2010	704.31 -	1,352.74	269.07	03/2020 03/2020	03/2020
202	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
	<u>South East Central Railway</u>						
203	ANUPPUR-KATNI - [N22000485	4/2015	1,370.00 -	1,370.00	253.18	12/2021 12/2021	12/2021
204	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,908.51 -	2,686.63	393.46	03/2023 03/2023	03/2023
	<u>South Eastern Railway</u>						
205	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	1/1991	1,013.45 -	1,428.00	484.82	12/2021 -	12/2021
	<u>South Western Railway</u>						
206	ARSIKERE-TUMKUR - [N22000332	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
207	YELAHANKA-PENUKONDA - [N22000328	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
	<u>Southern Railway</u>						
208	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>Western Railway</u>						
209	CHOTTAUDEPUR-DHAR(NL) - [N22000138	4/2007	1,347.26 -	1,347.26	700.60	03/2022 03/2022	03/2022
210	SURENDRA NAGAR RAJKOT - [N22000392	4/2015	1,002.39 -	1,002.39	348.91	03/2021 03/2021	03/2021
	Total		1,97,744.34 -	2,53,733.44	45,092.11		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
211	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
212	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
213	BODHWAD TO STATE BORDER - [N24001086	1/2017	178.26 -	178.26	81.95	07/2019 -	07/2019
214	NALDURG TO AKKALKOT - [N24001051	2/2018	274.50 275.00	274.50	56.39	12/2019 -	12/2019
215	KALMATH TO ZARAP - [N24001137	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
216	WADIGODRI TO DHANGRIPIMPRI - [N24001063	3/2018	194.23 194.00	194.23	48.23	02/2020 -	02/2020
217	DEULGAON SAKARSHA TO MEHKAR - [N24001076	3/2018	219.91 -	219.91	84.46	12/2019 -	12/2019
218	TALGAON TO KALMATH - [N24001136	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
219	SILLOD TO FARDAPUR - [N24001125	2/2017	337.46 -	337.46	44.03	06/2019 -	06/2019
220	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
221	MALEGAON TO RISOD - [N24001089	2/2018	303.24 303.00	303.24	50.07	12/2019 -	12/2019
222	HELWAK TO KARAD - [N24001055	2/2017	416.99 -	416.99	100.40	07/2019 -	07/2019
223	PANCHARAL TO MANDANGHAR - [N24001107	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020
224	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
225	SARSAM TO KOTHARI - [N24001002	2/2016	545.64 -	545.64	45.01	07/2019 -	07/2019
226	KHAMGAON TO DEULGAON SAKARSHA - [N24001074	3/2018	249.29 -	249.29	32.20	12/2019 -	12/2019
227	JALKOT TO TOGRI - [N24001071	7/2018	299.92 300.00	299.92	-	08/2020 -	08/2020
228	KARAD TO VITA - [N24001049	1/2018	344.85 245.00	344.85	39.04	12/2019 -	12/2019
229	PALPHATA TO PHULAMBARI - [N24001060	3/2018	227.19 227.00	227.19	37.23	12/2019 -	12/2019
230	WARDHA TO HINGAGHAT - [N24001098	1/2018	216.90 217.00	216.90	20.00	12/2019 -	12/2019
231	MEHKAR TO AJISPUR - [N24001048	1/2017	232.77 -	232.77	83.51	07/2019 -	07/2019
232	KARASWADA TO BAMBOLIM - [N24001005	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
233	PARTUR TO MAJALGAON - [N24001034]	1/2017	420.57 -	420.57	121.39	07/2019 -	07/2019
234	BHANDARA TO GHOTITOK - [N24001018]	1/2017	392.83 393.00	392.83	254.60	06/2019 -	06/2019
235	PANDHARPUR TO SANGOLA - [N24001102]	7/2017	218.38 -	218.38	161.75	07/2019 -	07/2019
236	DAHEGAON TO KUHI - [N24001017]	1/2017	228.89 229.00	228.89	90.00	06/2019 -	06/2019
237	MAHAD TO RAIGAD FORT - [N24001038]	7/2018	237.40 -	237.40	7.34	05/2020 -	05/2020
238	KUSUMBA TO MALEGAON - [N24001109]	3/2018	243.45 244.00	243.45	47.02	12/2019 -	12/2019
239	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	52.87	06/2021 -	06/2021
240	BHADGAON TO CHALISGAON - [N24001047]	1/2018	259.55 260.00	259.55	120.00	11/2019 -	11/2019
241	AURANGABAD TO SILLOD - [N24001124]	2/2017	456.32 -	456.32	79.30	06/2019 -	06/2019
242	SHIRUR TO KHARDA - [N24001123]	2/2017	381.77 -	381.77	122.79	06/2019 -	06/2019
243	KOTHARI TO DHANORA - [N24001073]	9/2018	301.38 301.00	301.38	-	08/2020 -	08/2020
244	ANJANGAON TO MAH/MP BORDER - [N24001007]	1/2017	359.00 359.00	359.00	149.80	06/2019 -	06/2019
245	NILAJPHATA TO BHANDARA - [N24001043]	1/2018	420.63 421.00	420.63	3.60	05/2020 -	05/2020
246	KARWANDI TO RAJURI - [N24001058]	3/2018	276.95 277.00	276.95	44.47	12/2019 -	12/2019
247	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	44.02	08/2020 -	08/2020
248	NANDED TO JALKOT - [N24001069]	12/2017	456.93 457.00	456.93	37.50	09/2019 -	09/2019
249	PUNE TO MALE VILLAGE - [N24001078]	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
250	AHMADPUR TO PIMPLA - [N24001029]	1/2017	422.38 -	422.38	136.58	08/2019 -	08/2019
251	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
252	ARNI TO NAIGAINBANDI - [N24001093]	12/2017	309.94 310.00	309.94	19.32	12/2019 -	12/2019
253	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	58.15	12/2019 -	12/2019
254	SHAHAPUR PATGAON SECTION I - [N24001027]	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
255	NASRATPUR TO BARASGAON - [N24001112]	7/2016	406.54 407.00	406.54	136.00	09/2019 -	09/2019
256	MANSAR TO SALAIKHURD - [N24001035]	1/2018	418.36 -	418.36	70.13	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
257	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
258	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]	1/2017	486.19 -	486.19	174.29	07/2019 -	07/2019
259	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	3/2018	217.14 217.00	217.14	52.77	02/2020 -	02/2020
260	PATGAON KHOPOLI SECTION I - [N24001028]	1/2018	170.00 -	170.00	15.57	12/2019 -	12/2019
261	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
262	SATARA TO MHASWAD - [N24001092]	1/2017	653.46 -	653.46	167.18	07/2019 -	07/2019
263	NAGBHID TO ARMORI - [N24001119]	9/2016	269.05 -	269.05	173.91	07/2019 -	07/2019
264	MAJALGAON TO KAIJ - [N24001036]	1/2017	413.99 -	413.99	310.33	07/2019 -	07/2019
265	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
266	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	609.61	11/2019 -	11/2019
267	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	27.50	12/2019 -	12/2019
268	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]	2/2017	406.51 -	406.51	406.58	06/2019 -	06/2019
269	JALGAON TO NANDURA - [N24001088]	3/2018	177.84 177.00	177.84	35.69	12/2019 -	12/2019
270	MANJUSUMBA TO CHUMBALI - [N24001031]	1/2017	228.54 -	228.54	87.30	08/2019 -	08/2019
271	PAHUR TO BODHWAD - [N24001084]	1/2017	244.93 -	244.93	29.23	05/2020 -	05/2020
272	KUNDRAL TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	90.75	12/2019 -	12/2019
273	TASGAON TO SHIRDHON - [N24001054]	1/2017	195.64 196.00	195.64	83.73	11/2019 -	11/2019
274	AHMEDNAGAR TO BARAMATI - [N24001100]	1/2017	955.40 -	955.40	301.50	08/2019 -	08/2019
275	SANGOLA TO JATH - [N24001052]	1/2018	257.38 257.00	257.38	28.15	12/2019 -	12/2019
276	SALAIKHURD TO TIRORA - [N24001042]	1/2018	415.25 415.25	415.25	36.22	12/2019 -	12/2019
277	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	3/2018	336.21 336.00	336.21	58.66	12/2019 -	12/2019
278	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]	3/2018	294.87 295.00	294.87	31.30	12/2019 -	12/2019
279	PARBHANI TO GANGKHED - [N24001065]	3/2018	238.19 238.00	238.19	9.85	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
280	KOLDE TO KHETIYA - [N24001090]	1/2017	509.18 -	509.18	157.93	07/2019 -	07/2019
281	KAIJ TO KUSALAM - [N24001037]	1/2017	554.78 -	554.78	136.90	07/2019 -	07/2019
282	MORSHI TO MAH/MP BORDER - [N24001016]	1/2017	471.61 472.00	471.61	252.90	06/2019 -	06/2019
283	WASHIM TO DASTAPUR - [N24001068]	3/2018	165.51 -	165.51	25.45	12/2019 -	12/2019
284	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	2/2017	422.02 422.00	422.02	224.01	07/2019 -	07/2019
285	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
286	CHIKLI TO TAKARKHED - [N24001083]	3/2018	393.10 393.00	393.10	83.97	12/2019 -	12/2019
287	MUL TO CHANDRAPUR - [N24001117]	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019
288	KURUDWADI TO PANDHARPUR - [N24001101]	1/2017	307.63 -	307.63	136.17	07/2019 -	07/2019
289	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
290	AJANTHA TO BULDHANA - [N24001008]	2/2017	401.00 401.00	401.00	82.81	07/2019 -	07/2019
291	SELDOH TO PANVAR - [N24001097]	7/2018	404.33 404.00	404.33	14.19	05/2020 -	05/2020
292	PATRADEVI TO KARASWADA 4L - [N24001004]	3/2017	634.32 -	634.32	102.33	05/2020 -	05/2020
293	PAITHAN TO SHIRUR - [N24001122]	3/2017	341.80 -	341.80	88.00	06/2019 -	06/2019
294	JAHIRABAD TO LATUR - [N24001040]	1/2017	461.96 -	461.96	116.43	11/2019 -	11/2019
295	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	8.86	04/2020 -	04/2020
296	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
297	SHIVUR TO YEOLA - [N24001059]	3/2018	181.08 -	181.08	7.45	12/2019 -	12/2019
298	MHASWAD TO TEMBHURNI - [N24001099]	1/2017	488.60 -	488.60	151.71	07/2019 -	07/2019
299	PIMPLA TO MANJARSUMBHA - [N24001030]	1/2017	595.77 -	595.77	119.44	08/2019 -	08/2019
300	SHIROD SHAHPURER TO NANDED - [N24001041]	1/2017	211.34 -	211.34	94.83	07/2019 -	07/2019
301	VITA TO NAGAJ - [N24001050]	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019
302	RALEGAON TO RAMTIRTH - [N24001046]	1/2017	210.81 -	210.81	100.69	07/2019 -	07/2019
303	AKOLA TO AKOT - [N24001003]	1/2017	313.95 -	313.95	31.05	06/2019 -	06/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
304	SARAD VANI PIMPALGAON - [N24001103]	1/2017	250.46 -	250.46	1,691.63	07/2019 -	07/2019
305	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
306	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	24.29	04/2020 -	04/2020
307	JALGAON TO BHADGAON - [N24001045]	1/2018	307.54 308.00	307.54	75.59	11/2019 -	11/2019
308	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	64.97	06/2020 -	06/2020
309	CHIKALI TO DHAD - [N24001061]	3/2018	189.46 189.00	189.46	21.00	12/2019 -	12/2019
310	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	68.97	12/2019 -	12/2019
311	MANGRUPHIR TO MAHAN - [N24001087]	3/2018	222.13 222.00	222.13	14.36	11/2019 -	11/2019
312	LATUR TO PANGAON - [N24001066]	3/2018	336.47 336.00	336.47	60.48	12/2019 -	12/2019
313	KALMAB TO RALEGAON - [N24001044]	1/2017	467.78 -	467.78	294.91	06/2019 -	06/2019
314	AKOT TO ANJANGAON - [N24001006]	1/2017	245.77 246.00	245.77	95.98	06/2019 -	06/2019
315	OMREGA TO AUSA - [N24001067]	3/2018	272.04 272.00	272.04	72.24	12/2019 -	12/2019
316	FARDAPUR TO JALGAON - [N24001126]	2/2017	456.45 -	456.45	66.10	06/2019 -	06/2019
317	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
318	CHALISGAON TO NANDGAON - [N24001108]	3/2018	206.97 207.00	206.97	46.89	12/2019 -	12/2019
319	BHOKAR TO SARSAM - [N24001128]	2/2017	295.09 -	295.99	155.64	07/2019 -	07/2019
320	GADCHIROLI TO MUL - [N24001116]	12/2016	484.15 -	484.15	127.31	06/2019 -	06/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
324	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]	3/2018	253.44 -	253.44	-	07/2019 -	07/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
325	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
326	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
327	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
328	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
329	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
330	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	1,388.34	1,213.89	09/2019 -	09/2019
331	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	762.75	07/2019 -	07/2019
332	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
333	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	54.70	03/2020 -	03/2020
334	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
335	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541	1/2016	1,081.57 -	1,081.57	988.72	06/2019 -	06/2019
336	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	525.24	04/2020 -	04/2020
337	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
338	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	571.35	07/2019 -	07/2019
339	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	1,597.26	03/2020 -	03/2020
	<u>National Highways Development Project</u>						
340	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	957.54 -	957.54	412.39	02/2020 -	02/2020
341	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	207.68	01/2020 -	01/2020
	<u>Public Works Dept Of State</u>						
342	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
343	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	125.09	09/2019 -	09/2019
344	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	0.50	09/2021 -	09/2021
345	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	59.56	06/2020 -	06/2020
346	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996	1/2017	605.08 -	605.08	213.00	10/2019 -	10/2019
347	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942	3/2016	208.50 -	208.50	102.98	11/2019 -	11/2019
348	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896	1/2017	373.82 -	373.82	116.33	09/2019 -	09/2019
349	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	171.00	01/2020 -	01/2020
350	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
351	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	134.38	04/2020 -	04/2020
352	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	0.34	09/2020 -	09/2020
353	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882	2/2018	218.70 -	218.70	17.84	11/2020 -	11/2020
354	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997	3/2018	192.67 -	192.67	-	07/2019 -	07/2019
355	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
356	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884	3/2018	191.21 -	191.21	68.26	11/2019 -	11/2019
357	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
358	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	46.62	07/2020 -	07/2020
359	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	19.76	10/2020 -	10/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
360	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	67.87	03/2020 -	03/2020
361	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158	3/2018	159.97 -	159.97	-	06/2019 -	06/2019
362	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880	2/2018	426.18 -	426.18	217.48	09/2020 -	09/2020
363	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
364	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	121.47	12/2019 -	12/2019
365	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	7.40	11/2019 -	11/2019
366	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	23.54	11/2019 -	11/2019
367	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999	11/2016	230.34 -	230.34	167.64	10/2019 -	10/2019
368	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	376.71	01/2020 -	01/2020
369	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	80.71	12/2019 -	12/2019
370	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910	3/2018	170.57 -	170.57	8.14	11/2020 -	11/2020
371	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
372	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	94.93	06/2020 -	06/2020
373	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	32.04	05/2020 -	05/2020
374	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879	3/2017	202.69 -	202.69	75.72	11/2019 -	11/2019
375	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983	1/2017	196.52 -	196.52	92.88	10/2019 -	10/2019
	Total		67,781.75 -	68,446.00	22,015.53		
	SHIPPING AND PORTS						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Cochin Shipyard Ltd</u>						
376	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	21.00	05/2021 -	05/2021
377	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	109.97	05/2020 -	05/2020
	<u>Inland Waterways Authority Of India</u>						
378	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	4,200.00	1,256.55	03/2023 -	03/2023
	Total		6,969.00 -	6,969.00	1,387.52		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
379	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
380	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	0.60	09/2020 -	09/2020
	Total		1,081.36 -	1,081.36	32.20		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
381	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	1/2019	790.79 -	800.00	-	06/2021 -	06/2021
382	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
383	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	146.45	06/2019 -	06/2019
384	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	41.33	05/2020 -	05/2020
385	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	28.71	11/2019 -	11/2019
386	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
387	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	33.82	02/2023 -	02/2023
388	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	32.89	02/2023 -	02/2023
	<u>National Building Construcion Corporation Ltd</u>						
389	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		20,517.46 -	20,701.90	3,564.31		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
390	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Total		233.57 -	233.57	32.20		
	Grand Total		5,75,818.35	6,35,134.45	1,50,368.63		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

Costing Rs. 150 Crore and above							
						(June 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N02000044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63
	Total		27,271.00 -	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
9	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	09/2017	11.42
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	09/2017	5.85
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	-	114.60
	<u>South-Eastern Coal Fields Limited</u>						
12	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Western Coal Fields Limited</u>						
13	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
14	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
15	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		25,725.94 -	28,037.55			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
16	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	08/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
17	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
18	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45
19	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
20	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,727.30	09/2011 -	03/2020	116.96
	Total		1,718.00 -	3,727.30			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
21	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33
	<u>Gas Authority Of India Limited</u>						
22	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
23	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
24	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	08/2019	133.50
25	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
26	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	09/2015	4,199.00 -	5,060.00	03/2020 -	03/2020	20.50
	<u>Indian Oil Corporation Limited</u>						
27	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
28	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	12/2020 -	12/2020	66.09
29	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	08/2020	43.82
30	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
32	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	08/2019	26.44
33	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
34	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45
35	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
36	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2019	29.42
37	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
38	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
39	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	265.49	05/2020 -	05/2020	6.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
40	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48
41	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
42	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71
43	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17
	<u>Oil India Limited</u>						
44	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
45	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
46	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	02/2020	25.55
	Total		42,201.80 -	52,135.03			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
47	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
48	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
49	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
50	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	12/2020	96.99
51	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	06/2020	9.64
52	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55
53	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
54	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75
55	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	07/2019	33.47
56	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2018 -	06/2020	24.87

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
57	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16
58	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55
59	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
60	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
61	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>						
62	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,419.34	12/2009 06/2016	08/2019	197.14
	<u>Power Grid Corporation Of India Limited</u>						
63	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
64	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
65	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	08/2019	38.61
66	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
67	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	06/2019	14.60
68	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	07/2019	26.82
69	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	08/2019	27.92
70	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17
71	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [N180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	08/2019	22.93
72	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
73	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Satluj Jal Vidyut Nigam Limited</u>						
74	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	07/2019	37.96
75	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) [N18000235]	11/2016	330.00 -	332.00	11/2017 -	04/2019	.61
	<u>Thdc India Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
76	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75
77	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
78	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,55,595.63 -	2,29,659.43			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
79	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71
80	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44
81	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
82	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04
83	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
84	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
85	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	143.17
86	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>						
87	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
88	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	- -	03/2023	290.95
89	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73
90	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
91	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
92	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
93	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	- -	02/2023	36.67

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
94	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88	- -	03/2023	278.13
95	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	03/2024	323.32
96	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	03/2024	542.46
97	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	03/2024	32.26
98	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15
99	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	- -	03/2021	124.59
100	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	- -	03/2022	590.61
101	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	03/2024	338.91
102	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	03/2024	252.66
103	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,470.50	- -	03/2021	295.15
104	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2022	43.41
105	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	400.17	- -	01/2020	87.86
106	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
107	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
108	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
109	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	727.29	- -	09/2019	302.22
110	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	12/2021	350.27
	<u>East Coast Railway</u>						
111	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
112	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	12/2023	29.96
113	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
114	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
115	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
116	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
117	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
118	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,670.01	03/2019 12/2009	03/2025	40.47
119	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,026.30	02/2013 -	03/2024	69.05
120	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	1,106.62 -	1,536.44	12/2010 -	03/2020	38.84
121	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]	04/2010	277.28 -	328.75	03/2016 -	03/2025	18.56
122	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46
123	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2020	27.96
124	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	226.22	- -	-	28.68
125	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
126	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	506.42	03/2005 -	03/2025	2.40
127	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	319.75	- -	03/2025	7.49
128	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]	04/2003	337.96 -	381.75	- -	03/2025	12.96
129	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	726.95	02/2012 -	03/2025	45.40
130	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	04/2009	257.42 -	258.73	03/2014 -	03/2025	.51
131	MONIGRAM- NIMITITA - [N22000301]	04/2012	250.93 -	259.23	- -	03/2024	3.31
132	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	09/2021	6.48
133	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	575.65	03/2006 -	03/2025	41.44

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
134	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34 -	- -	03/2025	180.30
135	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10 -	- -	03/2025	51.19
136	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81 -	03/2022 -	03/2025	133.39
137	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	364.98 -	- -	03/2020	26.58
138	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	444.81 -	- -	05/2019	70.18
139	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL [N22000223]	04/2000	157.17 -	160.00 -	- -	-	1.80
140	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	1,218.71 -	03/2016 -	03/2025	31.96
141	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]	04/2010	174.56 -	175.99 -	- -	03/2025	.82
	<u>Indian Railway Construction Company Limited</u>						
142	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11 -	03/2022 -	12/2022	117.23
	<u>Metropolitan Rapid Transport Projects</u>						
143	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92 -	12/2006 -	-	224.37
144	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,973.73 -	03/2004 -	03/2021	500.22
145	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01 -	06/2013 -	-	48.06
146	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97 -	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
147	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00 -	12/2008 -	03/2015	188.33
148	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60 -	03/2022 -	12/2024	32.02
149	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00 -	03/2020 -	03/2020	1.69
	<u>North East Frontier Railway</u>						
150	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00 -	03/2019 -	03/2020	106.51
151	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45 -	03/2014 -	03/2022	109.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
152	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266	04/2000	1,180.19 -	3,500.00	12/2008 -	-	196.56
153	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
154	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
155	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
156	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
157	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	- -	03/2022	7.86
158	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95
159	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	- -	03/2022	71.62
160	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11
161	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
162	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
163	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	394.28	- -	03/2021	63.25
164	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
165	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	- -	-	128.39
166	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	700.00	03/2019 -	-	122.93
167	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
168	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
	<u>North Eastern Railway</u>						
169	KICHHA-KHATIMA (NL) - NER - [N220100317	04/2003	142.45 -	228.40	- -	-	60.34
170	HATHUA-BHATNI (N L) (NER) - [N220100319	04/2005	230.03 -	770.08	12/2022 -	12/2022	234.77
171	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
						(June 2019)	
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
172	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09 -	- -	-	358.99
173	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00 -	12/2021 -	12/2021	267.13
174	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31 -	01/2019 -	01/2020	61.80
175	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00 -	- -	-	.16
176	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35 -	04/2016 -	02/2020	.16
177	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00 -	01/2018 -	-	.15
178	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34 -	- -	-	18.56
	<u>North Western Railway</u>						
179	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41 -	02/2019 -	12/2021	116.16
180	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99 -	03/2020 -	04/2022	14.33
181	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04 -	- -	-	26.25
182	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55 -	12/2019 -	06/2020	41.64
183	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15 -	- -	-	95.85
184	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90 -	10/2018 -	10/2019	24.47
185	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54 -	- -	-	33.76
186	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22 -	- -	-	33.81
187	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02 -	11/2019 -	05/2020	14.35
188	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00 -	02/2019 -	12/2019	69.36
	<u>Northern Railway</u>						
189	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17 -	- -	03/2024	25.87
190	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]	04/2013	654.00 -	700.00 -	- -	03/2025	7.03
191	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00 -	12/2011 -	03/2021	141.81
192	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00 -	- -	03/2022	137.45

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
193	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63 -	- -	06/2020	57.68
194	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00 -	- -	03/2023	.08
195	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00 -	07/2012 -	03/2024	346.67
196	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00 -	11/2002 -	12/2021	1,017.96
197	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00 -	03/2023 -	03/2023	369.31
198	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	876.00 -	03/2016 -	03/2021	40.16
	<u>Rail Vikas Nigam Ltd.</u>						
199	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47 -	12/2017 -	03/2020	55.57
200	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00 -	03/2009 03/2009	12/2019	188.58
201	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00 -	12/2026 -	12/2026	135.93
202	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00 -	03/2023 -	03/2023	36.34
203	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48 -	03/2016 -	03/2025	7.78
204	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86 -	03/2014 -	12/2025	18.95
205	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32 -	12/2021 -	12/2021	10.94
206	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55 -	03/2016 -	12/2020	29.06
207	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67 -	12/2023 -	12/2023	9.32
208	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00 -	03/2019 -	03/2020	29.45
209	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00 -	03/2020 -	03/2020	173.31
210	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68 -	12/2024 -	12/2024	.00
211	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00 -	03/2020 -	03/2020	58.22
212	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00 -	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
213	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10	275.08	03/2012	-	60.77
	<u>South Central Railway</u>						
214	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20	2,120.16	03/2009	03/2023	102.85
215	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00	2,911.84	-	-	161.86
216	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95	2,200.00	03/2023	03/2024	18.47
217	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23	1,787.00	-	-	93.56
218	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00	1,599.39	-	-	92.93
219	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31	1,352.74	03/2020	03/2020	92.07
220	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36	1,050.00	02/2009	-	538.84
221	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00	2,542.75	03/2000	03/2021	47.58
222	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25	458.26	-	-	.00
223	KONDAPALLI-KOTHAGUDEM - [N22000364]	04/2013	723.00	997.09	-	-	37.91
224	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73	184.97	03/2022	03/2022	54.49
	<u>South East Central Railway</u>						
225	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	1,413.76	-	10/2019	268.37
226	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86	1,756.92	04/2020	12/2020	243.24
227	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51	2,686.63	03/2023	03/2023	40.77
228	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93	1,300.44	02/2019	06/2020	121.94
229	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	860.92	12/2021	03/2023	275.95
230	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00	1,226.51	12/2019	10/2019	40.65
231	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00	1,973.66	03/2021	12/2021	.03
	<u>South Eastern Railway</u>						
232	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69	426.00	-	03/2030	53.96

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
233	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [N220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2025	160.76
234	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	11/2019	153.41
235	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	- -	03/2025	131.89
236	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99
237	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161	04/2011	289.64 -	760.00	- -	-	162.39
238	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	03/2015 -	-	53.44
239	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	358.68	- -	06/2020	38.92
240	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	03/2020 -	06/2020	35.38
241	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
242	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
243	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
244	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	- -	12/2023	24.09
245	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	- -	12/2023	57.65
246	TORANAGALLU-RANJITPURA DL - [N22000298	04/2011	146.75 -	167.50	- -	12/2023	14.14
247	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	04/2013	327.25 -	367.77	- -	12/2023	12.38
248	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
249	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
250	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98
251	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	227.40 -	900.00	- -	-	295.78
252	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	582.83 -	2,300.00	- -	-	294.63

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
253	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
254	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	- -	-	79.80
255	ATTIPPATTU PUTTUR - [N22000184	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
256	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	2,300.00	- -	-	339.33
257	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
258	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
259	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	457.08	- -	-	69.20
260	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	- -	-	295.05
261	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	03/2020	173.71
262	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	951.24	- -	03/2020	2.07
263	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
264	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
265	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	950.00	03/2005 -	-	253.33
266	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
267	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35
268	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
269	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32
	<u>Western Railway</u>						
270	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18
271	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125	04/2006	117.36 196.95	202.35	03/2011 -	03/2017	72.42
272	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
						(June 2019)	
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
273	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
274	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
275	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70
	Total		1,81,516.40 -	4,00,102.03			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
276	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	-	3.72
	<u>Ministry Of Road Transport And Highways</u>						
277	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	- -	-	58.68
278	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
279	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
280	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26
281	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643	12/2013	319.80 320.00	320.00	05/2016 -	-	.06
282	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02
283	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
284	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
285	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	07/2019	.31
286	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.00	03/2017 -	07/2019	46.45
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
287	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
288	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]	02/2017	168.32 -	202.05	04/2017 -	02/2021	20.04
289	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]	02/2017	180.57 -	215.70	04/2017 -	02/2021	19.46
290	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]	02/2017	216.71 -	262.62	04/2017 -	02/2021	21.19
291	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]	02/2017	167.28 -	209.71	04/2017 -	02/2021	25.36
	<u>National Highways Authority Of India</u>						
292	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	07/2019	92.75
293	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
294	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
295	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
296	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2020	106.50
297	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58
298	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	12/2019	21.90
299	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
300	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
301	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
302	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
303	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
304	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
305	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
306	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
307	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
308	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
309	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
310	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
311	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	-	4.02
312	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
313	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
314	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
315	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
<u>National Highways Development Project</u>							
316	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	03/2017 -	08/2019	46.51
317	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
<u>Public Works Dept Of State</u>							
318	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
319	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
320	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
321	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 -	389.45	05/2012 -	-	88.11

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
322	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65
323	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	-	6.02
324	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2019	36.24
325	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	- -	-	1.75
326	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	02/2011 -	-	34.06
327	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 -	353.89	11/2015 -	06/2019	6.21
328	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	307.47	02/2018 -	-	40.84
329	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
330	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]	08/2014	600.87 720.97	720.97	11/2017 -	05/2019	19.99
331	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]	08/2014	823.20 937.76	937.76	11/2017 -	06/2019	13.92
332	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39
333	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51
334	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18
335	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]	04/2014	279.70 398.22	398.52	08/2017 -	07/2019	42.48
336	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]	01/2012	378.07 -	478.73	01/2014 -	-	26.62
337	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]	03/2009	501.00 -	671.54	09/2013 -	-	34.04

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
						(June 2019)	
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		33,028.53	48,641.44			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
338	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88
	<u>Mumbai Port Trust</u>						
339	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	-	82.72
	<u>Port Trust</u>						
340	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
341	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05
	<u>Rastrya Ispat Nigam Limited</u>						
342	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2021	42.39
	Total		15,868.00 -	23,628.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
343	MADHYA PRADESH ACCESS (LOT1) - [N26000110	08/2017	215.30 -	219.60	05/2018 -	07/2019	2.00
344	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	01/2018	231.80 -	240.10	10/2018 -	09/2019	3.58
	<u>Department Of Telecommunication</u>						
345	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,781.10 -	25,123.70			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
346	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85
347	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2021	30.58
348	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	06/2014	157.84 -	169.16	03/2017 -	-	7.17
349	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57
350	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
351	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	12/2019	1.85
352	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	01/2019	790.79 -	800.00	06/2021 -	06/2021	1.16
	<u>Chennai Metro Rail Ltd</u>						
353	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
354	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
355	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
356	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
357	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Kochi Metro Rail Corporation Ltd</u>						
358	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
359	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		29,058.09 -	35,281.91			
	<u>WATER RESOURCES</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 Crore and above							
(June 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Polavaram Project Authority</u>						
360	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		5,38,265.07	9,45,774.41			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00	6,840.00	5,784.74	09/2010	10/2021	133	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00	16,580.00	13,711.00	12/2015	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	10,993.00	12/2016	12/2020	48	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00	39,849.00	14,422.00	11/2020	11/2023	36	0	
	Total		67,120.00	80,348.00	44,910.74					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61	441.33	85.79	09/2018	06/2020	21	40.28	
	Total		314.61	441.33	85.79					
	<u>COAL</u>									
	<u>Central Coal Fields Limited</u>									
6	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87	179.87	163.23	03/2012	07/2019	88	0	
7	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51	163.51	106.41	03/2011	03/2021	120	0	
8	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68	264.68	179.87	03/2012	03/2021	108	0	
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85	510.85	359.23	03/2016	03/2021	60	0	
10	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	89.82	03/2014	03/2021	84	0	
11	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40	706.40	336.64	07/2012	03/2022	116	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Eastern Coal Fields Limited</u>									
12	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	460.96	03/2018 -	03/2020	24	0	1. Rehabilitation of PAFs : Progress of R & R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
	<u>Mahanadi Coal Fields Limited</u>									
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL, ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	0	
14	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	493.85	03/2017 -	03/2020	36	0	
15	JAGANNATH RE-ORGANISATION OC (6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12	0	
16	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	75.79	03/2018 -	03/2020	24	0	
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	241.15	03/2012 -	03/2021	108	0	
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	390.53	03/2013 -	03/2021	96	0	
19	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022	108	0	
20	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	346.99	03/2010 -	03/2022	144	0	
21	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	196.26	03/2019 -	03/2022	36	0	
	<u>Neyveli Lignite Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
22	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	709.06	439.27	06/2015 -	09/2019	51	-51.37	Due to unavailability of land, it was not possible to increase OB removal to the extent of 47.5 MM3 per annum as envisaged in Mining Plan to get 7.0 MTPA lignite exposures. Hence, it is required to keep Mine 1A expansion to 7.0 MTPA on hold till land is acquired and required OB removal capacity is attained. Land acquisition process was delayed due to lack of clarity about payment of compensation in the State land acquisition rules consequent to enactment of Acquisition, Rehabilitation and Resettlement Act, 2013 (Central Act 30 of 2013) and Land Acquisition Rehabilitation and resettlement (Amendment) Act 2015.
23	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,451.65	12/2015 -	12/2019	48	19.86	
	<u>Singareni Colliers Company Limited</u>									
24	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	0	
25	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	7.01	03/2015 -	03/2021	72	114.6	
26	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	53.00	03/2019 -	03/2022	36	0	
27	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	115.71	03/2015 -	07/2019	52	-32.3	
28	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	331.25	03/2012 -	03/2023	132	16.86	
29	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	232.81	03/2012 -	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
30	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.49	203.90	03/2015 -	03/2020	60	201.44	
31	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	
32	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	172.88	03/2016 -	03/2020	48	0	
33	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	207.04	03/2014 -	03/2021	84	0	
	<u>Western Coal Fields Limited</u>									
34	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	17.71	03/2023 -	03/2024	12	15.41	
35	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	115.28	03/2021 -	03/2024	36	12.85	
	Total		17,014.82 -	18,205.04	12,820.65					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
36	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	209.44	159.41	11/2016 -	08/2019	33	5.89	
	Total		197.79 -	209.44	159.41					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
37	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	23,140.00	15,729.80	05/2015 07/2020	07/2020	62	49.05	
	<u>Rastriya Ispat Nigam Limited</u>									
38	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	199.91	08/2018 07/2019	07/2019	11	0	No
39	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	390.25	07/2018 07/2019	07/2019	12	0	No
40	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,144.53	09/2018 09/2019	09/2019	12	0	No

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
41	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,277.76	12/2017 09/2019	09/2019	21	-12.53	No
42	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 488.40	488.40	254.29	10/2016 03/2021	03/2021	53	42.39	No
	<u>Steel Authority Of India Limited (Sail)</u>									
43	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	922.73	12/2017 06/2019	06/2019	18	0	
44	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	431.23	10/2017 06/2020	06/2020	32	0	
45	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	99.65	06/2019 06/2020	06/2020	12	0	
	Total		23,646.42 -	31,048.82	20,450.15					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
46	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	694.00	671.48	10/2018 -	11/2019	13	0	
47	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	5,245.96	3,283.70	08/2018 -	11/2019	15	14.33	
48	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	1,112.00	467.00	06/2019 -	06/2020	12	0	
49	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	3,288.96	816.62	02/2020 -	10/2020	8	-7.3	
50	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	0	
	<u>Gas Authority Of India Limited</u>									
51	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	03/2015	3,957.00 -	3,397.00	2,707.26	12/2018 -	06/2019	6	-14.15	
52	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	135.09	04/2018 -	08/2019	16	-38.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
53	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,291.18	12/2012 -	02/2022	110	4.61	
	<u>Hindustan Petroleum Corporation Limited</u>									
54	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	678.31	10/2014 08/2019	08/2019	58	133.5	
	<u>Indian Oil Corporation Limited</u>									
55	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	2,740.12	09/2017 -	07/2019	22	0	
56	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	07/2019	8	0	
57	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	244.44	08/2019 -	09/2019	1	0	
58	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	300.23	01/2019 -	12/2019	11	0	
59	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	21.97	06/2020 -	08/2020	2	0	
60	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	256.76	07/2018 -	10/2020	27	0	
61	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	38.51	02/2020 -	10/2020	8	0	
62	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	75.19	02/2020 -	10/2020	8	0	
63	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	444.28	12/2018 -	02/2021	26	33.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
64	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	163.02	44.00	04/2020 -	03/2021	11	0	
65	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	212.00	28.55	01/2021 -	04/2021	3	0	
66	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00 -	466.00	74.36	04/2021 -	07/2021	3	0	
67	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	466.43	25.99	10/2020 -	08/2021	10	0	
68	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA	05/2016	348.00 -	348.00	20.85	01/2021 -	10/2021	9	0	
69	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH	08/2017	318.80 -	318.80	37.30	08/2021 -	11/2021	3	0	
70	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL, ANDHRA PRADESH	04/2018	355.00 -	355.00	13.97	04/2022 -	02/2023	10	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
71	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN, KARNATAKA	10/2015	135.00 170.70	170.70	152.13	03/2019 -	08/2019	5	26.44	
72	BSVI UPGRADATION - [N16000257]MANGALORE REFIN, KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	643.05	12/2019 07/2020	07/2020	7	0	
73	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN, KARNATAKA	11/2017	581.00 -	621.00	66.19	03/2020 04/2020	09/2020	6	6.88	
	<u>Oil & Natural Gas Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
74	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 -	420.76	193.15	09/2018 07/2019	07/2019	10	0	
75	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,780.91	05/2019 10/2019	10/2019	5	-4.01	
76	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	345.92	139.45	01/2014 -	11/2019	70	70.45	
77	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81	-3.5	
78	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	1,683.06	1,265.01	05/2013 12/2019	12/2019	79	95.3	
79	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	5,296.93	4,748.30	04/2019 12/2019	12/2019	8	-12.72	
80	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	4,619.94	4,313.38	12/2017 03/2020	03/2020	27	0	
81	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 565.15	565.15	425.96	11/2019 03/2020	03/2020	4	3.48	
82	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	2,185.47	03/2019 05/2020	05/2020	14	0	
83	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,180.79	04/2018 05/2020	05/2020	25	1.77	
84	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	367.94	03/2019 -	05/2020	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
85	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 05/2021	05/2021	1	2.17	
86	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	2,670.11	06/2020 -	08/2021	14	0	
87	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 -	4,475.92	2,555.11	05/2021 12/2021	12/2021	7	11.71	
	<u>Oil India Limited</u>									
88	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	
89	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	224.72	03/2017 -	12/2019	33	24.47	
	Total		1,04,117.69 -	1,06,787.83	45,432.14					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
90	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,135.82	04/2020 -	12/2023	44	0	
	<u>National Hydro-Electric Power Corporation</u>									
91	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,399.82	09/2009 -	12/2021	147	155.05	
	<u>National Thermal Power Corporation</u>									
92	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	13,589.31	05/2018 06/2019	07/2019	14	33.47	
93	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	12,104.40	10/2017 03/2020	03/2020	29	7.55	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
94	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	11,322.86	01/2018 03/2020	03/2020	26	10.55	
95	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	6,271.59	07/2019 06/2020	06/2020	11	0	
96	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	9,298.78	12/2018 06/2020	06/2020	18	9.64	
97	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	9,645.00	02/2018 06/2020	06/2020	28	24.87	
98	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	9,996.59	7,816.71	07/2012 -	09/2020	98	86.75	
99	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,025.80	03/2013 12/2020	12/2020	93	96.99	
100	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	4,988.68	11/2020 06/2021	06/2021	7	0	
101	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	16,182.14	10/2011 08/2021	08/2021	118	145.16	
102	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	8,852.51	06/2019 09/2019	09/2021	27	5.55	
103	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	443.47	09/2019 02/2022	02/2022	29	15.23	
	<u>North East Electric Power Corporation</u>									
104	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,419.34	7,419.34	7,327.76	12/2009 08/2019	08/2019	116	197.14	
	<u>Power Grid Corporation Of India Limited</u>									
105	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	225.28	162.30	02/2016 04/2019	06/2019	40	14.6	
106	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	340.88	251.33	03/2018 03/2019	07/2019	16	26.82	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
107	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	1,429.38	1,011.38	01/2019 -	07/2019	6	0	Bhadla (PG) - Bhadla (RVPN) line alongwith 1x500 MVA ICT at Bhadla S/S commissioned in Apr'19. 2x500 MVA ICTs at Bhadla S/S commissioned in May'19. Progress of 765 KV Bhadla-Bikaner line is getting affected due to delay in forest clearance, awaited. ROW also being faced
108	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	562.25	392.96	03/2019 03/2019	07/2019	4	0	
109	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	407.79	04/2019 04/2019	07/2019	3	0	
110	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	84.17	06/2019 -	07/2019	1	0	
111	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,308.50	04/2019 -	07/2019	3	0	
112	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,237.45	11/2008 06/2019	08/2019	129	22.93	Implementation of balance 01 line (Edamon-Muvattupuzha line) was affected due to severe ROW problem (long pending) in Kerala. 1 Tower Erection is held up due to court case.
113	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 08/2019	08/2019	40	38.61	Severe ROW problem at Rajarhat area due to protest by political groups. Work in Rajarhat was on hold since Jan'17. Work of TL resumed in Jun'18 & substation resumed in Aug'18 after intervention from State and Distt. Admn. Presently, works of TL at 2 loc. in Distt. Pargana 24 South are held up.
114	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	190.80	07/2017 06/2019	08/2019	25	27.92	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
115	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	81.97	03/2018 03/2018	08/2019	17	0	Due to inclement weather conditions in hills, refusal of PTW for live line installation due to system constraints and shutdown requirement due to missing earth-wires etc.
116	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	430.71	04/2019 04/2019	08/2019	4	0	
117	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	153.70	02/2019 06/2019	08/2019	6	0	Work of downstream system yet to be taken up by UT Chandigarh. Underground cable laying done in 5 Kms. 05 locations under severe ROW. Land owners have taken stay from Hon'ble Court. Court hearing postponed & now scheduled on 24.07.19
118	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019	63	31.17	- Balance 400KV Madhugiri-Yelhanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the earlier contractor had expressed inability to continue the balance work. Balance work re-awarded in Dec'17. ROW issues in Bangalore (Urban) are being resolved with the help of State/ District admin. Work in progress in balance sections
119	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	548.30	10/2017 09/2019	09/2019	23	0	04 locs. under severe ROW problem. Line linked with Tehri Generation completion expected by December 2020

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
120	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4	0	Ajmer-Bikaner & LILO at Bikaner line: Physical work completed. Final checking in progress. Bikaner-Moga line: Defence aviation clearance received for revised route on 23.04.19. Forest clearance awaited. Some foundation abandoned & towers dismantled due to re-routing.
121	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	266.03	01/2019 09/2019	09/2019	8	0	
122	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	92.78	09/2018 09/2019	09/2019	12	0	Gen. delayed. Completion matching with BanaskanGen.
123	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2	0	LILO of existing Neyveli TS-II - Pondy cherry 400KV S/C at NNTPS Gen. Yd.: Line charged in Jun'18 by cross jumpering at dead end tower near NLC switchyard as associated bays was not ready (under scope of NLC).
124	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3	0	
125	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	117.15	06/2019 06/2019	10/2019	4	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
126	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 12/2019	12/2019	86	5.14	LILO at Navi Mumbai: All physical work completed in Mar'19. CEA clearance received (alongwith Navi Mumbai S/S) in May'19. Shutdown for connection from Maharashtra State utilities (MSETCL) is still awaited. State downstream system at Navi Mumbai to be implemented through TBCB. Matter critical. 02 Kms of line executed using underground cable. Work was affected due to water logging. Severe ROW problem was encountered at Navi Mumbai end, miscreants had burnt and damaged part of laid cable.
127	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	210.72	04/2016 03/2017	12/2019	44	0	
128	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 5,151.37	5,151.37	3,115.72	03/2018 12/2019	12/2019	21	0	
129	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	405.65	05/2017 06/2019	12/2019	31	0	
130	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12	90.82	Award have been delayed due to poor response & high prices quoted by bidders. Out of 113 Sub stations land for only 82 nos S/S available. Delay in land handover and forest clearance.
131	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
132	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	287.52	04/2018 01/2020	01/2020	21	0	Schedule extended due to corridor constraint at Jeerat (4th element). Work to be executed by WBSETCL on deposit basis. Awarded to JV of M/s Techno & Xian in Nov'18.
133	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	0	
134	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE	05/2014	522.29 -	546.36	465.21	11/2016 12/2019	03/2020	40	4.61	
135	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	808.63	513.85	01/2018 12/2019	03/2020	26	0	Implementation affected due to forest (Tiger reserve) clearance. Line passing through buffer zone of Tiger reserve area. Wildlife proposal cleared in NBWL. Stage-I issued on 18.10.18. Working permission received in Feb'19. Gen. Project commissioned. Alternate arrangements made for evacuation (through existing Punatsangchu ATS). No bottleneck in power flow.
136	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 12/2018	12/2020	24	34.61	Award was delayed due to poor response & high prices quoted by bidders. Delay in land handover and forest clearance.
137	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022	103	32.24	Balance 02 lines (linked to Gen. Proj.) to be completed matching with Gen. Proj. Lower Subhansiri HEP (schedule uncertain). Works presently stand-still over uncertainty of generation on a/c of local disturbance/ agitation against big dams.
	<u>Satluj Jal Vidyut Nigam Limited</u>									
138	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN, BIHAR	05/2015	436.68 -	602.44	561.74	12/2016 -	07/2019	31	37.96	
	<u>Thdc India Limited</u>									
139	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42 -	294.60	292.85	02/2014 -	10/2019	68	50.75	Cutting of trees may be expedited by Forest deptt.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
140	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	2,935.92	02/2016 -	06/2022	76	203.22	Renewal of lease for 3.0 Ha land at Asena Quarry and Transfer of additional 05 Ha. Forest land and permission for mining are pending. It needs to be expedited.
141	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,697.38	06/2013 -	12/2022	114	76.51	Approval of Gaddi Quarry and crusher plant is pending with District Administration/ GoUK.
	Total		1,83,618.66 -	2,42,602.99	1,65,331.62					
	<u>HEAVY INDUSTRY</u>									
	<u>Natrip Implementation Society</u>									
142	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	3,727.30	3,182.10	09/2011 06/2019	03/2020	102	116.96	
	Total		1,718.00 -	3,727.30	3,182.10					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>HII Infra Tech Services Limited</u>									
143	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2	0	
144	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2	0	
145	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5	0	
	<u>Hospital Services Consultancy Corporation</u>									
146	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7	0	
	<u>Hospital Services Consultancy Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
147	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	244.00	241.39	09/2018 -	06/2019	9	0	
148	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27	0	
149	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	0	
150	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC, PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	0	
151	NEIGRIHMS SHILLONG MEGHALAYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	0	
152	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	0	
153	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	0	
154	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	24.1	
	Total		4,937.67 -	5,037.45	2,079.73					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
155	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 -	305.00	260.45	03/2019 12/2019	12/2019	9	65.71	
156	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,211.41	03/2021 -	03/2022	12	63.44	
157	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	792.89	294.10	03/2021 -	03/2022	12	0	Acquisition of land in 37 villages.
158	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	1,272.19	256.28	03/2022 -	03/2023	12	0	
159	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	540.02	215.95	03/2022 -	03/2024	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
160	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	65.16	03/2022 -	03/2024	24	0	
161	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	48.42	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									
162	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	259.90	03/2019 -	12/2019	9	0	
163	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	0	
164	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	149.66	03/2019 -	02/2020	11	0	
165	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	436.07	03/2018 -	03/2020	24	0	
166	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	300.00	285.74	03/2019 -	03/2020	12	-13.37	
167	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	5.59	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
168	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	72.25	03/2019 -	12/2019	9	0	
169	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,156.41	1,028.71	03/2012 -	03/2020	96	256.11	
170	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	672.82	03/2012 -	03/2020	96	56.73	
171	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	446.51	03/2019 -	02/2021	23	0	
172	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	426.16	03/2020 -	03/2021	12	0	
173	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	390.91	03/2020 -	10/2021	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
174	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	785.87	457.46	03/2020 -	03/2022	24	43.41	
175	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	35.10	03/2021 -	03/2022	12	63.37	
176	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	15.39	03/2021 -	03/2022	12	62.06	
177	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	424.98	03/2020 -	12/2022	33	0	
	<u>East Coast Railway</u>									
178	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	116.91	11/2018 -	03/2021	28	15.45	
179	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	879.96	02/2019 -	03/2022	37	38.43	
180	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	349.23	12/2018 -	03/2022	39	0	
181	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	624.68	06/2021 -	03/2023	21	137.8	
182	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	125.30	10/2020 -	03/2023	29	0	
183	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	654.74	03/2020 -	03/2023	36	.07	
184	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	320.30	03/2022 -	03/2023	12	0	
185	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,354.80	03/2009 -	12/2023	177	29.96	
186	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	148.96	03/2022 -	03/2025	36	0	
	<u>Eastern Railways</u>									
187	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,536.44	815.11	12/2010 12/2017	03/2020	111	38.84	Govt. of West Bengal to deposit Rs. 189.96 Cr. for their balance share towards project Katwa- BWN G.C.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
188	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.47	11/2018 -	03/2021	28	0	
189	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,026.30	637.72	02/2013 -	03/2024	133	69.05	
190	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,670.01	847.87	03/2019 12/2009	03/2025	72	40.47	1. Acquisition of land in stretch of 7.008 KM between Kamarpukur and Mayanapur and pending over of 13.342 KM stretch possession to Railway. 2. Villagers of Vill.Bhadadighi, Hooghly District, are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non availability of land Land acquisition for the main project Tarkeshwar – Bishnupur including their all MM works are yet to be received from State Government.
191	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	575.65	148.40	03/2006 -	03/2025	228	41.44	Land is required for execution of the MM projects.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
192	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	307.25	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit the balance share of this cost shared project.
193	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	1,218.71	431.90	03/2016 -	03/2025	108	31.96	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 For Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to religious structures in alignment and Amghata to Nabadwipghat work is held up due to 41 nos. of unauthorized crossings.
194	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	328.75	165.55	03/2016 -	03/2025	108	18.56	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
195	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	182.35	03/2017 -	03/2025	96	-18.82	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non availability of land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
196	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	506.42	32.00	03/2005 -	03/2025	240	2.4	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahat (9.75 Km) New line-- Work could not be started due to non availability of land
197	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	726.95	150.36	02/2012 -	03/2025	157	45.4	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Diamond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
198	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	258.73	103.91	03/2014 -	03/2025	132	.51	226.542 acres of land required to be acquired for the MM work.
199	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
200	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 12/2020	12/2020	27	0	1- Agitation by Land loser.
201	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	619.50	03/2022 12/2022	12/2022	9	117.23	
202	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 1,700.43	1,700.43	48.00	03/2020 06/2023	06/2023	39	-67.3	
	<u>Metropolitan Rapid Transport Projects</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
203	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,973.73	1,394.89	03/2004 -	03/2021	204	500.22	Land acquisition for 4.067Ha. forest land & 0.67Ha. of Private land.
204	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 918.53	918.53	256.68	03/2014 03/2021	03/2021	84	-82.67	
205	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
	<u>North Central Railway</u>									
206	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	32.02	Delay in acquisition of land in Morena District of M.P.
	<u>North East Frontier Railway</u>									
207	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	285.46	12/2015 06/2021	03/2020	51	204.95	
208	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	271.06	03/2019 -	03/2020	12	106.51	
209	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	13,809.00	8,818.98	03/2011 -	03/2020	108	210.02	
210	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,532.00	606.19	03/2019 -	03/2020	12	297.72	
211	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	932.80	03/2019 -	03/2020	12	302.54	
212	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	3,000.00	756.82	03/2015 -	10/2021	79	28.95	
213	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 569.63	650.00	45.24	03/2020 03/2020	12/2021	21	14.11	
214	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	5,021.45	2,933.84	03/2014 03/2022	03/2022	96	109.8	
	<u>North Eastern Railway</u>									
215	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	256.42	01/2019 -	01/2020	12	61.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
216	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	116.58	04/2017 -	01/2020	33	-31.45	
217	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	4.89	04/2016 -	02/2020	46	.16	
218	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	3.12	12/2019 -	04/2021	16	-12.65	
219	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
220	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
	<u>North Western Railway</u>									
221	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	138.99	10/2018 -	10/2019	12	24.47	
222	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	341.67	02/2019 -	12/2019	10	69.36	
223	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	244.02	245.81	11/2019 -	05/2020	6	14.35	
224	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	199.54	12/2019 -	06/2020	6	41.64	
225	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	142.63	03/2020 -	06/2020	3	0	
226	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	510.24	02/2019 -	12/2021	34	116.16	
227	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	38.93	03/2020 -	04/2022	25	14.33	
228	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	33.39	08/2022 -	09/2022	1	0	
	<u>Northern Railway</u>									
229	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	189.71	12/2011 -	03/2021	111	141.81	
230	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 876.00	876.00	848.84	03/2016 -	03/2021	60	40.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
231	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	18,512.58	11/2002 -	12/2021	229	1017.96	
232	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE <u>Rail Vikas Nigam Ltd.</u>	03/1981	450.00 -	2,010.00	644.09	07/2012 -	03/2024	140	346.67	
233	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	381.48	03/2009 03/2009	12/2019	129	188.58	
234	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,709.83	12/2017 -	03/2020	27	55.57	
235	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,100.58	03/2019 -	03/2020	12	29.45	
236	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	668.38	03/2016 -	12/2020	57	29.06	
237	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	977.00	03/2019 -	03/2021	24	18.78	
238	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	982.53	12/2020 -	03/2021	3	0	
239	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	833.73	02/2015 -	12/2021	82	0	
240	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,235.96	03/2020 -	03/2022	24	0	
241	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	285.50	03/2022 -	12/2024	33	-20.46	
242	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	455.60	03/2023 -	12/2024	21	0	
243	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,110.08	03/2016 -	03/2025	108	7.78	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
244	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	842.61	03/2016 -	03/2025	108	0	
245	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	2,106.28	03/2014 -	12/2025	141	18.95	
246	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,458.67	12/2024 -	03/2026	15	0	
<u>South Central Railway</u>										
247	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	2,542.75	1,413.56	03/2000 -	03/2021	252	47.58	
248	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	102.85	
249	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	0	
250	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	0	
251	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	0	
252	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	18.47	
253	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	0	
254	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	0	
<u>South East Central Railway</u>										
255	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR, MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	626.21	02/2019 03/2020	06/2020	16	121.94	
256	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	511.86 1,756.92	1,756.92	1,645.84	04/2020 12/2020	12/2020	8	243.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
257	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 1,973.66	1,973.66	121.56	03/2021 12/2021	12/2021	9	.03	
258	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 403.00	860.92	39.80	12/2021 03/2023	03/2023	15	275.95	
	<u>South Eastern Railway</u>									
259	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019	35	153.41	
260	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	494.27	03/2020 -	06/2020	3	35.38	
261	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	332.04	03/2021 -	12/2021	9	0	
262	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FROM - [N22000398]SER,ODISHA	04/1995	524.43 -	939.00	184.33	12/2021 -	12/2024	36	79.05	
263	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	03/2025	216	160.76	
264	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	54.99	
265	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	130.97	
	<u>South Western Railway</u>									
266	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	37.96	
267	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-1.38	
268	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	15.84	
269	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	0	
270	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	0	
271	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
272	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
273	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	0	
	<u>Southern Railway</u>									
274	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	1391.3	
275	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	185.98	
276	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	23.72	
277	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	222.39	
278	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	55.57	
279	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									
280	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 1,763.93	1,763.93	624.49	03/2020 03/2022	03/2022	24	0	
281	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	154.63	03/2022 09/2022	09/2022	6	114.32	
282	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023	178	2360.35	
283	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 2,909.99	2,909.99	1,027.12	03/2021 03/2023	03/2023	24	585.35	
284	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	367.59	03/2022 03/2023	03/2023	12	0	
	<u>Western Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
285	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	809.07	596.89	03/2019 03/2020	03/2020	12	46.7	
286	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	1,310.23	1,294.00	03/2020 03/2021	03/2021	12	57.91	
287	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	663.29	81.64	03/2020 03/2021	03/2021	12	-4.13	
288	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	64.48	06/2020 06/2021	06/2021	12	-13.76	
289	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120	1.06	
290	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36	167.87	
291	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,338.15	3,860.40	1,577.87	03/2022 03/2023	03/2023	12	10.18	
292	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	665.69	03/2022 03/2023	03/2023	12	0	
	Total		1,72,020.18 -	2,55,911.58	1,02,257.61					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
293	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
294	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	326.63	249.26	04/2018 -	06/2019	14	0	
295	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	301.70	01/2017 -	06/2019	29	0	
296	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH	01/2016	386.09 -	386.09	153.98	05/2016 -	06/2019	37	0	
297	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	208.09	09/2016 -	06/2019	33	0	
298	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA	02/2017	322.48 322.00	322.48	169.08	05/2019 -	06/2019	1	0	
299	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH	10/2015	333.21 -	333.21	-	12/2015 -	06/2019	42	0	
300	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	621.43	387.00	06/2018 -	07/2019	13	0	
301	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 - [N24000971]MORTH,ANDHRA PRADESH	08/2016	574.19 -	574.19	-	07/2017 -	07/2019	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
302	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.00	454.41	03/2017 -	07/2019	28	46.45	
303	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	97.23	08/2017 -	08/2019	24	0	
304	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	169.76	08/2017 -	08/2019	24	0	
305	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA	01/2017	463.62 664.00	463.62	230.34	06/2019 -	08/2019	2	0	
306	AMD1 TO SAONER - [N24001021]MORTH,MAHARASHTRA	01/2017	396.91 396.91	396.91	281.48	06/2019 -	08/2019	2	0	
307	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	86.63	08/2015 -	09/2019	49	0	
308	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	43.79	09/2017 -	09/2019	24	0	
309	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	229.00	06/2019 -	10/2019	4	0	
310	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	.02	
311	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	179.81	11/2017 -	11/2019	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
312	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	29.83	06/2019 -	11/2019	5	0	
313	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	78.81	11/2018 -	11/2019	12	0	
314	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	.26	
315	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	0	
316	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	86.79	05/2019 -	12/2019	7	0	
317	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	110.43	05/2019 -	12/2019	7	0	
318	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	171.75	06/2019 -	12/2019	6	0	
319	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	159.29	06/2019 -	12/2019	6	0	
320	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	125.81	06/2019 -	12/2019	6	0	
321	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA	01/2017	355.17 355.17	355.17	141.87	07/2019 -	12/2019	5	0	
322	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	35.26	06/2019 -	12/2019	6	0	
323	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	14.94	03/2019 -	12/2019	9	0	
324	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	23.71	03/2019 -	12/2019	9	0	
325	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
326	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-11.07	
327	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH	11/2016	378.24 -	378.24	-	01/2018 -	01/2020	24	0	
328	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (-) [N24000938]MORTH,ANDHRA PRADESH	03/2018	297.12 294.00	297.12	119.08	07/2018 -	01/2020	18	0	
329	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	177.36	01/2018 -	01/2020	24	0	
330	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	60.76	08/2018 -	02/2020	18	0	
331	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	100.00	08/2018 -	02/2020	18	0	
332	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	130.85	02/2019 -	02/2020	12	0	
333	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	20.13	08/2018 -	03/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
334	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	652.90	12/2019 -	03/2020	3	0	
335	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	746.91	11/2019 -	03/2020	4	0	
336	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	-	04/2019 -	04/2020	12	0	
337	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	136.30	11/2018 -	05/2020	18	0	
338	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	23.03	05/2019 -	05/2020	12	0	
339	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	126.78	05/2019 -	05/2020	12	0	
340	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	100.00	06/2019 -	06/2020	12	0	
341	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	68.97	06/2019 -	06/2020	12	0	
342	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	12.00	06/2019 -	06/2020	12	0	
343	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	145.91	06/2019 -	06/2020	12	0	
344	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	26.42	06/2019 -	06/2020	12	0	
345	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	184.31	07/2019 -	07/2020	12	0	
346	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH	03/2018	244.95 245.00	244.95	75.36	08/2018 -	08/2020	24	0	
347	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
348	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	30.00	09/2018 -	04/2021	31	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
349	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	37.86	05/2019 -	07/2019	2	0	
350	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	194.11	174.80	05/2018 -	08/2019	15	0	
351	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	187.25	08/2016 -	08/2019	36	0	
352	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	229.11	08/2016 -	08/2019	36	0	
353	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	153.61	08/2016 -	08/2019	36	0	
354	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36	0	
355	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	94.49	01/2017 -	01/2020	36	11.57	
356	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	240.21	06/2018 -	03/2020	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
357	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	284.09	80.64	04/2017 -	02/2021	46	0	
358	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	202.05	42.83	04/2017 -	02/2021	46	20.04	
359	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	215.70	45.21	04/2017 -	02/2021	46	19.46	
360	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	262.62	31.11	04/2017 -	02/2021	46	21.18	
361	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	209.71	47.37	04/2017 -	02/2021	46	25.36	
362	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	93.52	10/2018 -	10/2021	36	-11.55	
363	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60	0	
	<u>National Highways Authority Of India</u>									
364	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	885.31	02/2013 -	06/2019	76	0	
365	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	843.67	07/2013 -	06/2019	71	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
366	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64	0	
367	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	0	
368	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019	133	4.99	
369	FOUR LANING OF BIAORA – DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	5	0	
370	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	273.20	256.25	02/2019 -	06/2019	4	0	
371	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	319.96	04/2009 -	07/2019	123	92.75	
372	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019	76	0	
373	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-11	
374	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	956.75	11/2017 -	07/2019	20	0	
375	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	574.28	448.92	07/2018 -	07/2019	12	0	
376	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019	24	0	
377	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	691.30	11/2018 -	07/2019	8	0	
378	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	712.41	03/2019 -	07/2019	4	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
379	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019	112	0	
380	TWO LANE WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	08/2019	20	0	
381	4 LANE OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	417.86	06/2016 -	08/2019	38	0	
382	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	09/2019	138	-28.84	
383	TWO LANE WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	479.20	475.02	05/2018 -	09/2019	16	0	
384	TWO LANE WITH PAVED SHOULDER OF SALASAR- NAGPUR - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	0	
385	FOUR LANE OF BAR-BILARA- JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	0	
386	FOUR LANE OF CHICHRA- KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITATION - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13	0	
387	4-LANE OF RAIPUR- KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTISGARH - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6	0	
388	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR BOBEDULLAGANJ ROAD IN THE STATE - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	244.90	219.09	05/2019 -	09/2019	4	0	
389	NALBARI TO BIJANI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019	136	0	
390	SIX LANE OF NELLORE- CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
391	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,154.18	12/2018 -	10/2019	10	0	
392	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	385.09	05/2018 -	10/2019	17	0	
393	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	0	
394	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,098.56	08/2018 -	11/2019	15	0	
395	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	0	
396	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7	0	
397	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6	0	
398	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8	0	
399	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	18.02	06/2017 -	11/2019	29	0	
400	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	0	
401	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	95.96	09/2017 -	11/2019	26	0	
402	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019	140	10.58	
403	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
404	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	0	
405	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	0	
406	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	0	
407	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	0	
408	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	0	
409	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019	39	21.9	
410	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	433.12	09/2017 -	12/2019	27	0	
411	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	0	
412	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	194.95	12/2017 -	12/2019	24	0	
413	CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	0	
414	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	722.46	07/2018 -	12/2019	17	0	
415	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	402.47	06/2018 -	01/2020	19	0	
416	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	192.02	08/2018 -	01/2020	17	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
417	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	0	
418	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	357.06	04/2018 -	02/2020	22	0	
419	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	0	
420	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020	100	106.5	
421	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	750.38	06/2014 -	03/2020	69	0	
422	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	288.38	08/2018 -	03/2020	19	0	
423	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	0	
424	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	76.83	03/2020 -	04/2020	1	.23	
425	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	347.91	05/2018 -	05/2020	24	0	
426	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	708.62	11/2016 -	05/2020	42	0	
427	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	405.31	07/2018 -	05/2020	22	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
428	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	607.37	02/2020 -	05/2020	3	0	
429	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	3.4	
430	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2	0	
431	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	687.88	03/2020 -	05/2020	2	13.97	
432	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	405.31	07/2016 -	05/2020	46	0	
433	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	0	
434	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	0	
435	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	529.62	05/2018 -	06/2020	25	-12	
436	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	06/2020	25	0	
437	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	1,167.42	238.96	03/2019 -	06/2020	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
438	SIX LANE OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	566.10	03/2020 -	06/2020	3	44.39	
439	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	256.47	09/2017 -	06/2020	33	0	
440	SIX LANE OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	513.98	03/2020 -	07/2020	4	41.54	
441	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	0	
442	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	10.58	
443	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	5.56	
444	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	5.7	
445	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	0	
446	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	-	09/2017 -	08/2020	35	0	
447	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	-	08/2017 -	09/2020	37	0	
448	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	0	
449	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	12.95	03/2019 -	11/2020	20	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
450	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	0	
451	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	480.96	03/2017 -	11/2020	44	1.06	
452	REHABILITATION AND UPGRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	0	
453	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	329.90	10/2017 -	11/2020	37	0	
454	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31	0	
455	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	203.78	03/2019 -	12/2020	21	0	
456	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	0	
457	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	301.68	06/2019 -	12/2020	18	0	
458	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	950.69	782.81	08/2019 -	12/2020	16	0	
459	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	221.91	03/2020 -	03/2021	12	10.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
460	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,532.62	-	03/2021 -	04/2021	1	0	
461	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-3.27	
462	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	0	
463	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	0	
	<u>National Highways Development Project</u>									
464	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019	29	46.51	
465	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	410.72	-	04/2015 -	08/2019	52	0	
466	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020	36	77.26	
	<u>Public Works Dept Of State</u>									
467	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	342.05	258.91	01/2017 -	06/2019	29	0	
468	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	511.00	2,323.04	10/2013 -	06/2019	68	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
469	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - [N24001147]PWD,UTTAR PRADESH	10/2016	239.63 -	239.63	197.77	02/2019 -	06/2019	4	0	
470	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	256.11	12/2015 06/2019	06/2019	42	0	
471	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	256.11	12/2015 06/2019	06/2019	42	0	
472	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 353.89	353.89	256.11	11/2015 06/2019	06/2019	43	6.21	
473	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	937.76	703.65	11/2017 06/2019	06/2019	19	13.92	
474	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.52	398.52	314.34	08/2017 07/2019	07/2019	23	42.48	
475	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	178.23	114.16	09/2018 -	07/2019	10	0	
476	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	244.54	122.31	05/2019 -	07/2019	2	0	
477	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	07/2019	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
478	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	86.63	08/2015 -	07/2019	47	0	
479	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70	0	
480	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	359.27	200.24	05/2019 -	08/2019	3	0	
481	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24	0	
482	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	09/2019	24	36.24	
483	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	143.16	10/2015 09/2019	09/2019	47	0	
484	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	0	
485	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	247.25	139.25	03/2019 -	09/2019	6	0	
486	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL	03/2016	271.17 291.20	291.20	79.24	11/2018 11/2019	11/2019	12	7.39	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
487	REHABILITATION AND UPGADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	73.09	02/2018 -	11/2019	21	0	
488	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	47.70	02/2018 -	11/2019	21	0	
489	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	15.22	03/2018 -	11/2019	20	0	
490	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	93.96	03/2018 -	11/2019	20	0	
491	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	115.54	02/2018 -	11/2019	21	0	
492	REHABILITATION AND UPGADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	0	
493	REHABILITATION AND UPGADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	356.56	06/2019 -	11/2019	5	0	
494	BALANCE WORK FOR REHABILITATION AND UPGADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	196.99	03/2018 -	11/2019	20	0	
495	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019	105	58.98	
496	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	69.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
497	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	151.59	196.76	08/2013 -	12/2019	76	0	
498	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	47.65	
499	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	0	
500	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	66.95	03/2018 -	12/2019	21	0	
501	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	62.22	02/2019 -	12/2019	10	0	
502	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	79.02	03/2019 -	12/2019	9	0	
503	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	83.83	05/2019 -	12/2019	7	0	
504	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	0	
505	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	100.10	07/2018 -	01/2020	18	0	
506	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	219.26	08/2017 -	02/2020	30	0	
507	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	173.16	07/2018 -	02/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
508	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54	0	
509	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	50.39	03/2018 -	04/2020	25	0	
510	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	0	
511	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	296.28	10/2010 -	06/2020	116	93.8	
512	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	14.37	08/2018 -	06/2020	22	0	
513	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	62.60	03/2017 -	06/2020	39	0	
514	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	4.45	08/2018 -	06/2020	22	0	
515	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	7.10	03/2018 -	07/2020	28	0	
516	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	-	08/2016 -	12/2020	52	0	
517	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
518	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	33.51	
519	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	11.18	
	Total		1,33,025.16 -	1,38,078.80	86,370.68					
	<u>SHIPPING AND PORTS</u>									
	<u>Kamarajar Port Limited</u>									
520	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-57.02	
	Total		600.00 -	257.90	1.45					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
521	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL, MAHARASHTRA	08/2017	215.30 219.60	219.60	33.46	05/2018 07/2019	07/2019	14	2	
522	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL, MAHARASHTRA	01/2018	231.80 240.10	240.10	117.63	10/2018 09/2019	09/2019	11	3.58	
	<u>Department Of Telecommunication</u>									
523	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	84.97	
	Total		13,781.10 -	25,123.70	8,548.09					
	<u>URBAN DEVELOPMENT</u>									
	<u>Bangalore Metro Rail Corporation Limited</u>									
524	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
525	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	156.21	03/2012 -	06/2019	87	0	
526	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	126.07	04/2018 -	07/2019	15	0	
527	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5	0	
528	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	488.28	418.79	05/2017 -	09/2019	28	25.85	
529	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38	0	
530	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59	0	
531	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
532	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	187.10	04/2019 -	12/2019	8	0	
533	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	314.01	07/2019 12/2019	12/2019	5	1.85	
534	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	86.04	10/2012 -	03/2020	89	0	
535	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	127.69	10/2019 -	03/2020	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
536	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	35.77	04/2019 -	06/2020	14	0	
537	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	80.06	03/2016 -	09/2020	54	0	
538	RESIDENTIAL QUARTERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	62.56	02/2020 -	09/2020	7	0	
539	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	27.31	07/2020 09/2020	09/2020	2	0	
540	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	0	
541	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	69.60	06/2017 -	10/2020	40	.57	
542	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	59.36	05/2020 -	12/2020	7	0	
543	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	293.53	10/2019 -	03/2021	17	30.58	
544	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 02/2017	05/2021	14	0	
	<u>Hindustan Steelwork Construction Limited</u>									
545	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
546	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	9.76	
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (June 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
547	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11,420.00	2,568.80	11/2021 12/2021	12/2021	1	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
548	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
549	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	5,873.51	03/2018 -	12/2019	21	0	
	Total		81,911.38 -	83,055.16	17,351.53					
	<u>WATER RESOURCES</u>									
	<u>Polavaram Project Authority</u>									
550	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	447.22	
	Total		10,151.04 -	55,548.87	16,417.99					
	Grand Total		8,14,174.52	10,46,384.21	5,25,399.68					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(June 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88	133
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63	48
	Total		27,271.00 -	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	<u>COAL</u>							
	<u>Neyveli Lignite Corporation</u>							
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86	48
	<u>Singareni Colliers Company Limited</u>							
6	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	-	114.60	72
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
9	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							
10	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
11	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
	Total		7,456.85 -	9,474.43				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
12	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	08/2019	5.89	33
	Total		197.79 -	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
13	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10	83
	Total		414.11 -	513.89				
	<u>HEAVY INDUSTRY</u>							
	<u>Natip Implementation Society</u>							
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]	04/2011	1,718.00 -	3,727.30	09/2011 -	03/2020	116.96	102
	Total		1,718.00 -	3,727.30				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
15	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33	15
	<u>Gas Authority Of India Limited</u>							
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61	110
	<u>Hindustan Petroleum Corporation Limited</u>							
17	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	08/2019	133.50	58
	<u>Indian Oil Corporation Limited</u>							
18	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98	26
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
19	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	08/2019	26.44	5
20	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88	6

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Oil & Natural Gas Corporation Limited</u>							
21	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45	70
22	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48	4
23	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30	79
24	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77	25
25	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17	1
26	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71	7
	<u>Oil India Limited</u>							
27	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47	33
	Total		25,847.77 -	30,331.66				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
28	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06	147
	<u>National Thermal Power Corporation</u>							
29	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23	29
30	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	12/2020	96.99	93
31	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75	98
32	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2018 -	06/2020	24.87	28
33	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55	29
34	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55	26
35	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	06/2020	9.64	18
36	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55	27

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
37	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	07/2019	33.47	14
38	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16	118
	<u>North East Electric Power Corporation</u>							
39	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,419.34	12/2009 06/2016	08/2019	197.14	116
	<u>Power Grid Corporation Of India Limited</u>							
40	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	06/2019	14.60	40
41	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	08/2019	27.92	25
42	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	07/2019	26.82	16
43	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61	40
44	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17	63
45	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	08/2019	38.61	40
46	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	08/2019	22.93	129
47	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14	86
48	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61	24
49	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82	12
50	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24	103
	<u>Satluj Jal Vidyut Nigam Limited</u>							
51	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	07/2019	37.96	31
	<u>Thdc India Limited</u>							
52	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75	68
53	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51	114
54	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22	76
	Total		1,33,344.83 -	1,92,329.16				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
55	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71	9
56	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44	12
	<u>Container Corporation Of India</u>							
57	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73	96
59	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	785.87	03/2020 -	03/2022	43.41	24
60	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11	96
61	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
62	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
	<u>East Coast Railway</u>							
63	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45	28
64	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07	36
65	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43	37
66	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
67	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,798.80	03/2009 -	12/2023	29.96	177
	<u>Eastern Railways</u>							
68	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL - [N22000244	04/2009	257.42 -	258.73	03/2014 -	03/2025	.51	132
69	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL [N22000228	04/2010	277.28 -	328.75	03/2016 -	03/2025	18.56	108
70	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
71	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE- PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	506.42	03/2005 -	03/2025	2.40	240

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
72	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	575.65	03/2006 -	03/2025	41.44	228
73	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	726.95	02/2012 -	03/2025	45.40	157
74	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,026.30	02/2013 -	03/2024	69.05	133
75	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	1,218.71	03/2016 -	03/2025	31.96	108
76	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	1,106.62 -	1,536.44	12/2010 -	03/2020	38.84	111
77	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,670.01	03/2019 12/2009	03/2025	40.47	72
78	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
79	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23	9
	<u>Metropolitan Rapid Transport Projects</u>							
80	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,973.73	03/2004 -	03/2021	500.22	204
81	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>							
82	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
83	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
84	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11	21
85	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
86	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
87	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95	79
88	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95	51
89	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02	108
	<u>North Eastern Railway</u>							
91	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16	46
92	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80	12
	<u>North Western Railway</u>							
93	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35	6
94	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47	12
95	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64	6
96	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	12/2019	69.36	10
97	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33	25
98	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	02/1997	410.08 -	886.41	02/2019 -	12/2021	116.16	34
	<u>Northern Railway</u>							
99	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81	111
100	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	876.00	03/2016 -	03/2021	40.16	60
101	NANGALDAM-TALWARA(NL),NR - [N220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67	140
102	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [N220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	12/2021	1,017.96	229
	<u>Rail Vikas Nigam Ltd.</u>							
103	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	188.58	129
104	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
105	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78	24
106	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45	12
107	HARIDASPUR-PARADEEP(NL) - [N220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57	27
108	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
109	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
	<u>South Central Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
110	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85	168
111	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47	12
112	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [N220100205]	04/1997	1,723.00 1.00	2,542.75	03/2000 -	03/2021	47.58	252
	<u>South East Central Railway</u>							
113	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95	15
114	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94	16
115	GONDIA-JABALPUR(GC),(SECR) - [N220100186]	02/1997	511.86 -	1,756.92	04/2020 -	12/2020	243.24	8
116	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	1,973.66	03/2021 -	12/2021	.03	9
	<u>South Eastern Railway</u>							
117	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323]	04/2012	148.77 -	377.00	12/2016 -	11/2019	153.41	35
118	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05	36
119	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
120	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [N220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2025	160.76	216
121	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	03/2020 -	06/2020	35.38	3
122	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
123	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96	36
124	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84	24
	<u>Southern Railway</u>							
125	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72	71
126	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39	12
127	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57	15
128	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30	9

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
129	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98	12
	<u>West Central Railway</u>							
130	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32	6
131	RAMGANJMUHDI-BHOPAL (NL), WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
132	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
133	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06	120
134	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70	12
135	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
136	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91	12
137	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18	12
	Total		81,236.13 -	1,73,802.32				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways</u>							
138	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02	41
139	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26	43
140	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.00	03/2017 -	07/2019	46.45	28
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
141	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
142	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]	02/2017	168.32 -	202.05	04/2017 -	02/2021	20.04	46
143	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]	02/2017	167.28 -	209.71	04/2017 -	02/2021	25.36	46

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
144	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683	02/2017	180.57 -	215.70	04/2017 -	02/2021	19.46	46
145	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684	02/2017	216.71 -	262.62	04/2017 -	02/2021	21.19	46
	<u>National Highways Authority Of India</u>							
146	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99	133
147	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58	140
148	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	07/2019	92.75	123
149	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
150	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
151	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
152	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
153	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
154	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54	4
155	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
156	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
157	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24	12
158	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
159	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	12/2019	21.90	39
160	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2020	106.50	100
	<u>National Highways Development Project</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
161	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	08/2019	46.51	29
162	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26	36
	<u>Public Works Dept Of State</u>							
163	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51	24
164	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18	24
165	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65	82
166	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39	12
167	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30	110
168	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2019	36.24	24
169	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	06/2019	6.21	43
170	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80	116
171	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	08/2017 -	07/2019	42.48	23
172	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	11/2017 -	06/2019	13.92	19
173	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98	105
	Total		19,392.26 -	24,611.08				
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmdc)</u>							
174	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05	62
	<u>Rastriya Ispat Nigam Limited</u>							
175	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2021	42.39	53

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(June 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		15,868.00	23,628.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
176	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	08/2017	215.30	219.60	05/2018	07/2019	2.00	14
177	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT [N26000113]	01/2018	231.80	240.10	10/2018	09/2019	3.58	11
	<u>Department Of Telecommunication</u>							
178	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00	24,664.00	07/2015	05/2020	84.97	58
	Total		13,781.10	25,123.70				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
179	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013	10/2019	132.80	70
180	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00	488.28	05/2017	09/2019	25.85	28
181	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017	10/2020	.57	40
182	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31	559.47	07/2019	12/2019	1.85	5
183	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21	1,592.00	10/2019	03/2021	30.58	17
	<u>Kochi Metro Rail Corporation Ltd</u>							
184	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79	5,687.79	07/2017	12/2019	9.77	29
	Total		7,948.75	9,092.53				
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
185	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04	55,548.87	03/2020	06/2021	447.22	15
	Total		10,151.04	55,548.87				
	Grand Total		3,44,942.24	5,89,333.11				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	05/2014 -	04/2018
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2018
3	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2019
4	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	10/2018
5	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Singareni Colliers Company Limited</u>				
6	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	03/2015 -	03/2019
7	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	06/2015 -	12/2015
8	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	03/2016 -	12/2016
9	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	07/2016 -	04/2017
10	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	03/2015 -	09/2017
11	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	03/2019 -	09/2017
12	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 -	-
14	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	- -	-
15	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA	08/2016	431.92 -	- -	-
16	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA	02/2018	412.70 -	- -	-
	<u>South-Eastern Coal Fields Limited</u>				
17	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	03/2016 -	-
18	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	03/2018 -	-
	<u>Western Coal Fields Limited</u>				
19	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	03/2018 -	03/2018
20	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	03/2019 -	03/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
21	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	03/2019 -	03/2019
22	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL, MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
	Total		8,737.65 -		
	<u>STEEL</u>				
	<u>Steel Authority Of India Limited (Sail)</u>				
23	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	04/2018 05/2019	05/2019
24	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93 -	04/2015 -	-
25	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL, JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		8,065.23 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
26	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
27	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				
28	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	12/2016 -	-
29	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	10/2015	607.06 -	10/2017 -	-
30	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	05/2015 -	-
31	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL, GUJARAT	10/2014	279.00 -	08/2018 -	-
32	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20 -	- -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR, KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>				
34	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN, KARNATAKA	05/2015	224.00 207.00	04/2019 06/2019	10/2018
	<u>Oil & Natural Gas Corporation Limited</u>				
35	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	03/2015 12/2019	05/2019
	<u>Oil India Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
36	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
37	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		11,527.56 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
38	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
39	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
40	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
41	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
42	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
	<u>Satluj Jal Vidyut Nigam Limited</u>				
43	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	11/2017 -	04/2019
	Total		20,880.38 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
44	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
45	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	-
	Total		681.15 -		
	<u>RAILWAYS</u>				
	<u>Container Corporation Of India</u>				
46	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
47	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
48	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
49	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
50	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>Eastern Railways</u>				
51	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	05/2010
52	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
53	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
54	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
	<u>Kolkata Metro Rail Corporation Limited</u>				
55	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
56	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
57	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	06/2013 -	-
58	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
59	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 314.09	12/2008 03/2015	03/2015
	<u>North East Frontier Railway</u>				
60	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 -	12/2008 -	03/2019
61	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019
62	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 -	03/2019 -	03/2019
63	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
	<u>North Eastern Railway</u>				
64	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
65	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
66	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
67	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
68	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
69	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>North Western Railway</u>				
70	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
71	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
72	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
73	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
74	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
75	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
76	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
77	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
78	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
79	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
80	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
81	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
82	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 997.09	- -	-
83	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South Eastern Railway</u>				
84	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
85	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>Southern Railway</u>				
86	ATTIPPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018
87	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-
88	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
89	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
90	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
91	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
92	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
93	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
94	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-
95	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-
96	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
97	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-
98	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-
99	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
100	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
	<u>Western Railway</u>				
101	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 -	03/2021 -	03/2019
102	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017
103	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
104	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
105	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
106	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
107	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		49,864.44 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
108	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
109	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
110	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Ministry Of Road Transport And Highways</u>				
111	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	02/2019
112	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
113	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
114	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
115	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
116	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
117	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
118	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
119	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
120	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
121	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
122	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
123	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
124	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
125	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
126	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
127	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
128	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
129	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-
130	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
131	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
132	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
133	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
134	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
135	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
136	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
137	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
138	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
139	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
140	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
141	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
142	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
143	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
144	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
145	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
146	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
147	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-
148	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-
149	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
150	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
151	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-
152	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-
153	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA	03/2016	165.06 -	12/2016 -	-
154	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA	08/2016	287.70 -	02/2017 -	-
155	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA	09/2016	295.67 -	02/2017 -	-
156	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA	12/2016	223.50 -	08/2018 -	-
157	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA	12/2016	206.88 -	04/2018 -	-
158	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA	03/2018	214.23 -	08/2018 -	-
159	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA	03/2018	199.16 -	08/2018 -	-
160	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA - [N24000918]MORTH,ODISHA	07/2013	251.92 -	10/2015 -	-
161	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA - [N24000919]MORTH,ODISHA	07/2013	265.35 -	10/2015 -	-
162	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA - [N24000924]MORTH,ODISHA	03/2015	229.29 -	11/2015 -	-
163	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH	09/2016	372.68 -	02/2017 -	-
164	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 -	-
165	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH	03/2016	995.09 995.00	05/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
166	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR	09/2018	1,478.40 -	- -	-
167	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MORTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 -	-
168	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA	01/2017	356.66 356.66	- -	-
169	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-
170	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
171	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	01/2019
172	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	10/2017
173	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	12/2015
174	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	-
175	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	-
176	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	06/2018 -	-
177	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
178	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
179	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
180	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	-
181	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
182	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
183	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
184	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
185	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
186	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
187	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
188	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
189	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
190	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
191	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
192	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
193	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
194	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
195	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
196	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
197	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
198	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
199	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
200	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
201	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
202	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
203	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-
204	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	-
205	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
206	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
207	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
208	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
209	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
210	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
211	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
212	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
213	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-
214	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
215	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
216	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
217	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
218	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
219	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
220	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
221	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
222	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
223	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
224	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
225	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
226	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
227	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-
228	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
229	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
230	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	- -	-
231	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	- -	-
232	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 -	- -	-
233	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 -	- -	-
234	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	-
235	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-
236	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
237	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
National Highways Authority Of India					

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
238	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019
239	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	02/2019
240	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	02/2019
241	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019
242	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019
243	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	03/2019
244	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	03/2019
245	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	03/2019
246	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2019
247	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	03/2019
248	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	03/2019
249	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	03/2019
250	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	04/2019
251	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2019
252	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	04/2019
253	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	04/2019
254	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	04/2019
255	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	04/2019
256	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	04/2019
257	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	05/2019
258	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	05/2019
259	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	05/2019
260	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	05/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
261	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	05/2019
262	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018
263	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2018
264	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2018
265	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2018
266	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	03/2019
267	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	05/2019
268	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
269	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
270	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
271	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
272	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
273	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
274	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
275	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
276	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
277	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
278	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
279	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
280	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
281	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
282	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
283	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
284	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
285	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
286	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
287	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
288	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
289	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
290	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
291	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
292	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
293	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
294	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
295	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
296	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
297	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-
298	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
299	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
300	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
301	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
302	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
303	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
304	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
305	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-
306	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
307	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
308	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
309	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
310	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
311	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-
312	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
313	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
314	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
315	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
316	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
317	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
318	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
319	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
320	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
321	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
322	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
323	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
324	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
325	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
326	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
327	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
328	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
329	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
330	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
331	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
332	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
333	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH-69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
334	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
335	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
336	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
337	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
338	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
339	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
340	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
341	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
342	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
343	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
344	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
345	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
346	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
347	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
348	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
349	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
350	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
351	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
352	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
353	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 -	- -	-
354	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
355	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
356	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
357	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-
358	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
359	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
360	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
361	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
362	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
363	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
364	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
365	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
366	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
367	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
368	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
369	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
370	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
371	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-
372	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-
373	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-
374	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
375	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- -	-
376	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-
377	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	- -	-
378	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
379	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI, HARYANA	03/2018	795.50 -	- -	-
380	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI, JHARKHAND	03/2018	1,005.08 -	- -	-
National Highways Development Project					
381	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHUDEAPAR BRIDGE - [N24000251]NHDP, GOA	03/2015	297.00 -	04/2018 -	-
382	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP, MAHARASHTRA	03/2015	168.30 -	- -	-
383	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP, MAHARASHTRA	01/2014	446.77 -	- -	-
384	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP, MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
385	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP, MADHYA PRADESH	08/2015	257.80 -	- -	-
Public Works Dept Of State					
386	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD, KARNATAKA	08/2016	367.44 -	01/2017 -	01/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
387	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA	08/2016	175.20 -	01/2017 -	01/2019
388	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	01/2019
389	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]PWD,GUJARAT	03/2016	223.67 -	02/2017 -	02/2017
390	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	02/2017
391	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	02/2017
392	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	03/2017
393	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	03/2017
394	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	03/2019 -	05/2019
395	REHABILITATION AND UPGRADATION OF TULSIPUR-BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	05/2019
396	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	05/2019
397	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	05/2019
398	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	06/2018
399	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	07/2018
400	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	08/2016
401	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	09/2017
402	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	10/2018
403	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	10/2018
404	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	11/2010

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
405	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 307.47	02/2018 -	11/2014
406	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	11/2017
407	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
408	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
409	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	-
410	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-
411	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
412	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
413	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
414	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
415	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
416	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
417	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
418	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
419	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
420	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
421	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
422	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
423	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
424	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
425	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
426	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
427	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
428	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD, WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-
429	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-
430	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD,GUJARAT	03/2016	208.34 -	02/2016 -	-
431	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD,GUJARAT	12/2017	867.97 -	11/2018 -	-
432	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]PWD,GUJARAT	03/2018	464.07 -	11/2018 -	-
433	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 -	05/2019 -	-
434	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD,GUJARAT	08/2017	962.43 -	03/2018 -	-
435	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
436	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD,RAJASTHAN	10/2014	382.81 -	01/2015 -	-
437	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD,RAJASTHAN	01/2017	179.32 -	11/2017 -	-
438	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD,RAJASTHAN	03/2016	155.77 -	09/2016 -	-
439	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD,RAJASTHAN	01/2012	378.07 478.73	01/2014 -	-
440	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD,RAJASTHAN	10/2012	511.21 -	10/2013 -	-
441	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD,RAJASTHAN	03/2009	501.00 671.54	09/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
442	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD,RAJASTHAN	11/2017	163.95 -	04/2018 -	-
443	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
444	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
445	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD,RAJASTHAN	12/2015	621.43 -	10/2016 -	-
446	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD,RAJASTHAN	01/2017	163.54 -	07/2017 -	-
447	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA	01/2019	193.19 -	- -	-
448	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR	03/2018	153.24 -	- -	-
	Total		2,09,917.69 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
449	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.00	12/2017 -	-
	<u>Mumbai Port Trust</u>				
450	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	-
	<u>Port Trust</u>				
451	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
452	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
	Total		3,188.29 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
453	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
454	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
455	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
456	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
457	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
458	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	- -	-
	<u>Chennai Metro Rail Ltd</u>				
459	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
460	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
461	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
462	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
463	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
464	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
465	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
466	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
467	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
468	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
469	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
470	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
471	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
472	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-
473	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(June 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
474	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
475	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Lucknow Metro Rail Corporation Limited</u>				
476	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Maharashtra Metro Rail Corporation Ltd.</u>				
477	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>National Building Construcion Corporation Ltd</u>				
478	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		72,298.45 -		
	<u>DEFENCE PRODUCTION</u>				
	<u>Goa Shipyard Limited</u>				
479	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA	12/2016	167.69 168.00	05/2018 03/2019	-
	Total		167.69 -		
	Grand Total		3,87,857.96		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
1	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	69.10	- -	03/2021	-	5/26
	Total		229.80 -	229.80	69.10				5/26
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation</u>								
2	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	601.02	85.04	- -	02/2020	-	0/0
3	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	582.99	112.97	- -	02/2020	-	0/0
4	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99	112.82	- -	02/2020	-	0/0
5	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	268.84	99.26	- -	04/2020	-	0/0
6	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	249.01	73.40	- -	05/2020	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>								
7	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	156.65	54.94	- -	02/2020	-	0/0
	Total		2,510.41 -	2,510.50	538.43				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
8	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]EJR,BIHAR	04/1998	180.82 -	727.29	488.81	- -	09/2019	-	0/0
9	HAIJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]EJR,BIHAR	04/2013	213.01 -	400.17	378.41	- -	01/2020	-	0/0
10	KODERMA-RANCHI VIA BARKAKANA (NL),EJR - [220100222]EJR,JHARKHAND	03/1999	1,033.07 3,031.00	3,376.00	3,180.37	- -	03/2021	-	0/0
11	KODERMA-TILAIYA (NL), EJR - [220100305]EJR,JHARKHAND	04/2002	459.91 -	459.91	456.83	- -	03/2021	-	0/0
12	SAKRI-HASANPUR ROAD (NL) - [N22000171]EJR,BIHAR	04/1999	325.00 -	729.92	349.60	- -	03/2021	-	0/0
13	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]EJR,BIHAR	04/2004	372.14 1,470.50	1,470.50	356.81	- -	03/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	1,483.14	815.41	- -	12/2021	-	0/0
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	589.15	303.96	- -	03/2022	-	0/0
16	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	2,614.36	375.63	- -	03/2022	-	0/0
17	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	126.80	- -	02/2023	-	0/0
18	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	2,066.77	1,403.38	- -	03/2023	-	0/0
19	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	2,396.88	.40	- -	03/2023	-	0/0
20	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	23.40	- 03/2023	03/2023	0(R3)	0/0
21	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	2,626.98	.28	- -	03/2024	-	0/0
22	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	2,860.55	1.14	- -	03/2024	-	0/0
23	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	549.75	15.47	- -	03/2024	-	0/0
24	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	1.91	- -	03/2024	-	0/0
25	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.21	- -	03/2024	-	0/0
26	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	926.09	24.16	- -	03/2024	-	0/0
27	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	2,393.23	17.20	- -	03/2024	-	0/0
28	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
29	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	.39	- -	03/2024	-	0/0
30	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	.60	- -	03/2024	-	0/0
	<u>Eastern Railways</u>								
31	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	364.98	364.98	- -	03/2020	-	0/0
32	BAZAR SAU-AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	140.00	- -	09/2021	-	0/0
33	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	259.23	243.97	- -	03/2024	-	0/0
34	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	9.31	- -	03/2025	-	0/0
35	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	10.73	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	175.99	71.37	- -	03/2025	-	0/0
37	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.12	- -	03/2025	-	0/0
38	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
39	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	319.75	52.09	- -	03/2025	-	0/0
40	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	381.75	70.22	- -	03/2025	-	0/0
41	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	246.00	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
42	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North Central Railway</u>								
43	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	19.07	- -	12/2022	-	0/0
	<u>North East Frontier Railway</u>								
44	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 373.87	394.28	272.88	- -	03/2021	-	0/0
45	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.67	- 03/2022	03/2022	0(R3)	0/0
46	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	0(R3)	0/0
	<u>Northern Railway</u>								
47	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	346.63	213.80	- -	06/2020	-	0/0
48	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	800.00	495.17	- -	03/2022	-	0/0
49	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	68.13	- -	03/2023	-	0/0
50	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,230.00	102.72	- -	03/2023	-	0/0
51	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	197.17	102.06	- -	03/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
52	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	205.22	1.79	-	03/2024	-	0/0
53	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00	700.00	-	-	03/2025	-	0/0
54	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00	1,239.00	-	-	03/2025	-	0/0
55	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00	400.00	-	-	03/2025	-	0/0
56	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00	876.00	-	-	03/2025	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
57	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	2,062.30	2,062.20	825.58	-	03/2022	-	0/2
	<u>South East Central Railway</u>								
58	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,413.76	1,413.76	1,309.02	- 10/2019	10/2019	0(R3)	0/0
	<u>South Eastern Railway</u>								
59	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	231.84	-	06/2020	-	0/0
60	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37	620.00	40.99	-	03/2025	-	0/0
61	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69	426.00	-	-	03/2030	-	0/0
	<u>South Western Railway</u>								
62	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01	1,801.01	44.36	-	12/2023	-	0/0
63	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	692.43	-	-	12/2023	-	0/0
64	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00	466.65	-	-	12/2023	-	0/0
65	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85	348.85	.35	-	12/2023	-	0/0
66	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	167.50	.34	-	12/2023	-	0/0
67	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	367.77	-	-	12/2023	-	0/0
68	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00	2,135.00	144.76	-	12/2024	-	0/0
	<u>Southern Railway</u>								
69	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41	450.00	151.50	-	03/2020	-	0/0
70	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 951.24	951.24	724.96	-	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
71	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	1,431.90	61.69	- 06/2022	-	-	0/0
	<u>Western Railway</u>								
72	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	87.81	- 03/2021	03/2021	0(R3)	0/0
	Total		34,843.10 -	60,197.52	14,501.95				0/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
73	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	128.92	- -	09/2020	-	0/4
74	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	434.06	126.58	- -	12/2020	-	2/4
75	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	27.90	- -	09/2021	-	0/4
	<u>National Highways Authority Of India</u>								
76	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	199.90	37.68	- -	06/2019	-	0/0
77	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	588.21	- -	06/2019	-	0/0
78	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	586.36	- -	06/2019	-	0/0
79	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	1,665.00	3,059.39	- -	06/2019	-	0/0
80	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	-	- -	07/2019	-	0/0
81	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	435.25	- -	08/2019	-	0/0
82	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	357.12	- -	08/2019	-	0/0
83	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	321.67	- -	09/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
84	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	417.19	262.83	- -	09/2019	-	0/0
85	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	845.24	788.62	- -	10/2019	-	0/0
86	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	720.00	278.01	- -	10/2019	-	0/0
87	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	834.64	140.44	- -	10/2019	-	0/0
88	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	752.28	-	- -	11/2019	-	0/0
89	4/2 LANNING WITH PS DAUSA-LALSOT- KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	688.70	661.85	- -	11/2019	-	0/0
90	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	447.75	179.17	- -	11/2019	-	0/0
91	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH	12/2017	328.67 -	328.67	176.29	- -	11/2019	-	0/0
92	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	1,167.45	99.74	- -	12/2019	-	0/0
93	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	364.56	208.94	- -	12/2019	-	0/0
94	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)- CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	458.03	158.64	- -	12/2019	-	0/0
95	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	1,100.19	848.00	- -	12/2019	-	0/0
96	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
97	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	814.04	367.27	- -	01/2020	-	0/0
98	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	829.97	75.08	- -	01/2020	-	0/0
99	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	196.05	9.03	- -	01/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
100	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	1,443.00	507.87	- -	02/2020	-	0/0
101	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	748.59	- -	02/2020	-	0/0
102	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,275.00	- -	02/2020	-	0/0
103	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	453.09	- -	03/2020	-	0/0
104	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	84.22	- -	03/2020	-	0/0
105	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	29.45	- -	03/2020	-	0/0
106	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	557.30	33.63	- -	03/2020	-	0/0
107	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	275.12	-	- -	03/2020	-	0/0
108	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	307.79	-	- -	03/2020	-	0/0
109	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	198.05	-	- -	03/2020	-	0/0
110	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	551.58	-	- -	03/2020	-	0/0
111	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	-	- -	04/2020	-	0/0
112	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	278.92	- -	04/2020	-	0/0
113	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	1,169.61	1,004.18	- -	04/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
114	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	174.79	- -	05/2020	-	0/0
115	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	1,232.21	410.09	- -	05/2020	-	0/0
116	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	-	- -	05/2020	-	0/0
117	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	-	- -	05/2020	-	0/0
118	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	181.78	-	- -	06/2020	-	0/0
119	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	13.33	- -	07/2020	-	0/0
120	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	-	- -	07/2020	-	0/0
121	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	447.28	- -	07/2020	-	0/0
122	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	34.36	- -	07/2020	-	0/0
123	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-- [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
124	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	960.24	-	- -	08/2020	-	0/0
125	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	234.67	- -	09/2020	-	0/0
126	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	1,103.88	198.85	- -	09/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
127	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	110.39	- -	10/2020	-	0/0
128	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	404.94	71.72	- -	10/2020	-	0/0
129	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	32.77	- -	11/2020	-	0/0
130	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	31.45	- -	11/2020	-	0/0
131	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	7.51	- -	11/2020	-	0/0
132	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	12.80	- -	11/2020	-	0/0
133	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	-	- -	12/2020	-	0/0
134	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	17.64	- -	12/2020	-	0/0
135	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	642.13	288.84	- -	12/2020	-	0/0
136	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
137	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	1,471.75	305.75	- -	01/2021	-	0/0
138	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	261.76	40.89	- -	01/2021	-	0/0
139	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	1,052.21	1,080.00	- -	01/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
140	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	2,702.05	-	-	01/2021	-	0/0
141	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI, TAMIL NADU	02/2018	1,166.26 -	1,166.26	-	-	02/2021	-	0/0
142	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	565.09	-	-	02/2021	-	0/0
143	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	1,029.96	-	-	03/2021	-	0/0
144	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA	01/2018	621.00 -	621.00	212.24	-	04/2021	-	0/0
145	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI, TAMIL NADU	03/2018	1,016.92 -	1,016.92	-	-	04/2021	-	0/0
146	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA	03/2018	806.11 -	806.11	-	-	04/2021	-	0/0
147	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 -	478.74	-	-	05/2021	-	0/0
148	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	503.88	-	-	06/2021	-	0/0
149	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	1,071.61	-	-	07/2021	-	0/0
150	4-LANNING OF TARSOD-FAGNE (FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	1,064.88	-	-	07/2021	-	0/0
151	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI, ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	-	-	07/2021	-	0/0
152	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI, ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	-	-	07/2021	-	0/0
153	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI, ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	-	-	07/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(June 2019)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
154	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	-	- -	07/2021	-	0/0
155	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	5.00	- -	07/2021	-	0/0
156	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	55.06	- -	08/2021	-	0/0
157	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	-	- -	08/2021	-	0/0
158	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	-	- -	08/2021	-	0/0
159	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	1,995.34	-	- -	11/2021	-	0/0
<u>National Highways Development Project</u>									
160	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	390.51	178.32	- -	03/2020	-	0/0
<u>Public Works Dept Of State</u>									
161	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	766.36	666.72	- -	06/2019	-	0/0
162	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	904.82	722.92	- -	06/2019	-	0/0
	Total		77,382.19 -	77,397.77	21,287.30				2/12
<u>URBAN DEVELOPMENT</u>									
<u>Central Public Works Department</u>									
163	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	10.36	- -	12/2020	-	0/0
164	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	5.96	- 08/2020	03/2021	7(R3)	0/0
165	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	348.77	12.00	- -	11/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		1,162.77	1,162.77	28.32				0/0
	Grand Total		1,16,128.27	1,41,498.36	36,425.10				7/40

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Eastern Coal Fields Limited</u>					
2	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL	02/2019	916.62 -	03/2027 -	03/2027	0/0
	<u>Neyveli Lignite Corporation</u>					
3	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
4	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Western Coal Fields Limited</u>					
6	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
7	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (SAIL)</u>					
8	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
9	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	06/2019 -	06/2020	0/0
10	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	03/2021 -	03/2021	0/0
11	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	10/2021	0/0
12	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH	12/2017	1,524.06 -	12/2021 -	12/2021	0/0
13	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
14	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00	12/2019	12/2019	0/0
15	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00	08/2020	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
16	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00	02/2020	02/2020	0/0
17	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53	07/2022	07/2022	0/0
18	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20	07/2022	07/2022	0/0
19	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25	10/2022	10/2022	0/0
20	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45	10/2022	10/2022	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
21	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH	08/2016	154.84	11/2019	11/2019	0/0
22	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26	06/2020	06/2020	0/0
23	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50	06/2020	06/2020	0/0
24	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00	04/2021	04/2021	0/0
	<u>Indian Oil Corporation Limited</u>					
25	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58	04/2021	04/2020	0/0
26	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00	06/2020	06/2020	0/0
27	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00	06/2020	08/2020	0/0
28	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00	12/2020	12/2020	0/0
29	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00	01/2021	01/2021	0/0
30	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00	01/2021	01/2021	0/0
31	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00	03/2021	03/2021	0/0
32	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00	03/2021	03/2021	0/0
33	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00	03/2021	03/2021	0/0
34	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00	01/2021	04/2021	0/0
35	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00	04/2021	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
36	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
37	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	09/2021 -	09/2021	0/0
38	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
39	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
40	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
41	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	04/2022	0/0
42	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
43	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	-	0/0
	<u>Indian Strategic Petroleum Reserves Ltd</u>					
44	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRIL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
45	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	05/2021 -	05/2021	0/0
46	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	04/2021 05/2021	05/2021	0/0
47	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	12/2021 -	12/2021	0/0
48	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 -	03/2022 -	03/2022	0/0
	<u>Oil India Limited</u>					
49	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
50	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	08/2020	0/0
51	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
52	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	12/2023	0/0
	<u>National Hydro-Electric Power Corporation</u>					
53	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
54	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>National Thermal Power Corporation</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
55	TALAIALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00	11/2019	11/2019	0/0
56	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC, UTTAR PRADESH	12/2018	587.44	09/2020	09/2020	0/0
57	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC, UTTAR PRADESH	03/2019	349.00	11/2020	11/2020	0/0
58	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
59	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL, MULTI STATE	03/2017	251.60	06/2019	06/2019	0/0
60	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38	01/2019	07/2019	0/0
61	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL, MULTI STATE	09/2016	562.25	03/2019 03/2019	07/2019	0/0
62	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24	04/2019 04/2019	07/2019	0/0
63	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL, MULTI STATE	03/2017	337.75	06/2019	07/2019	0/0
64	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00	04/2019	07/2019	0/0
65	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40	03/2018 03/2018	08/2019	0/0
66	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA	04/2016	844.64	04/2019 04/2019	08/2019	0/0
67	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400V - [N18000242]PGCIL, MULTI STATE	02/2017	322.30	02/2019 06/2019	08/2019	0/0
68	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59	05/2019	09/2019	0/0
69	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE - II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46	01/2019 09/2019	09/2019	0/0
70	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64	09/2018 09/2019	09/2019	0/0
71	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17	07/2019	09/2019	0/0
72	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPF AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14	06/2019	09/2019	0/0
73	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53	06/2019 06/2019	10/2019	0/0
74	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37	11/2019	11/2019	0/0
75	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL, MULTI STATE	03/2017	283.72	11/2019 11/2019	11/2019	0/0
76	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 374.63	04/2016 03/2017	12/2019	0/0
77	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95	12/2019 12/2019	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
78	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
79	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	12/2019	0/0
80	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 01/2020	01/2020	0/0
81	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 02/2020	02/2020	0/0
82	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
83	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	02/2020	0/0
84	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 12/2019	03/2020	0/0
85	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
86	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
87	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
88	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 12/2018	12/2020	0/0
	<u>Thdc India Limited</u>					
89	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	09/2023 -	09/2023	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
90	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	09/2019	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
91	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	06/2020	0/0
92	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	08/2020	0/0
93	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	10/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					
94	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	10/2019	0/0
95	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	02/2020	0/0
96	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	02/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
97	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	02/2020	0/0
98	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
99	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	- -	05/2020	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
100	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	06/2019	0/0
101	NEIGRIHMS SHILLONG MEGHALAYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	05/2018 -	09/2019	0/0
102	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	03/2019 -	10/2019	0/0
103	GERIATRICS BLOCK- AIIMS DELHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	- -	02/2020	0/0
104	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2020	0/0
105	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	10/2020	0/0
106	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
107	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
108	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 -	03/2019 12/2019	12/2019	0/0
109	AHMEDNAGAR-PARLI VAIJNATH (NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2022	0/0
110	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2022	0/0
111	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR, MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2022	0/0
112	WARDHA-NANDED MAHARASHTRA - [N22000231]CR, MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
113	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
114	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR, MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2023	0/0
115	DAUND - MANMAD (236 KM) - [N22000360]CR, MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
116	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
117	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR, MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
118	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
119	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
120	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
	<u>Container Corporation Of India</u>					
121	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2019	0/0
122	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
123	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	02/2020	0/0
124	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020	0/0
125	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2020	0/0
126	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
127	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
128	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
129	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
130	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	<u>East Central Railways</u>					
131	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	09/2019	0/0
132	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
133	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	01/2020	0/0
134	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	03/2012 -	03/2020	0/0
135	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	03/2020	0/0
136	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	03/2012 -	03/2020	0/0
137	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
138	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,031.00	- -	03/2021	0/0
139	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
141	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2021	0/0
142	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
143	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	- -	12/2021	0/0
144	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	03/2022	0/0
145	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
146	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	03/2020 -	03/2022	0/0
147	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2022	0/0
148	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	03/2021 -	03/2022	0/0
149	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	- -	02/2023	0/0
150	HAJIPUR-SUGAU LI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
151	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	03/2023	0/0
152	ARARIA-SUPAU LI (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- 03/2023	03/2023	0/0
153	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	03/2024	0/0
154	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	03/2024	0/0
155	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	03/2024	0/0
156	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
157	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	03/2024	0/0
158	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	03/2024	0/0
159	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	03/2024	0/0
160	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
161	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	03/2024	0/0
162	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	03/2024	0/0
163	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
164	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
	<u>East Coast Railway</u>					
165	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2020	0/0
166	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2021	0/0
167	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	03/2022	0/0
168	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	03/2022	0/0
169	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2022	0/0
170	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	03/2023	0/0
171	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 -	03/2023	0/0
172	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 -	03/2023	0/0
173	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	12/2023	0/0
174	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 -	03/2025	0/0
	<u>Eastern Railways</u>					
175	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	05/2010	0/0
176	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
177	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2020	0/0
178	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2020	0/0
179	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
180	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	09/2021	0/0
181	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
182	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
183	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
184	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
185	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
186	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
187	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
188	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
189	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
190	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
191	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
192	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
193	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
194	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
195	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
196	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
197	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
198	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
199	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
200	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
201	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
202	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
	<u>Indian Railway Construction Company Limited</u>					
203	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	09/2018 12/2020	12/2020	0/0
204	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	03/2022 12/2022	12/2022	0/0
205	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 1,700.43	03/2020 06/2023	06/2023	0/0
	<u>Kolkata Metro Rail Corporation Limited</u>					
206	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
207	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]JMTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 918.53	03/2014 03/2021	03/2021	0/0
209	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
210	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
211	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
212	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
213	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	12/2022	0/0
214	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 314.09	12/2008 03/2015	03/2015	0/0
215	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
	<u>North East Frontier Railway</u>					
216	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 -	12/2008 -	03/2019	0/0
217	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019	0/0
218	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 -	03/2019 -	03/2019	0/0
219	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 06/2021	03/2020	0/0
220	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	03/2020	0/0
221	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	03/2020	0/0
222	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2020	0/0
223	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 -	03/2019 -	03/2020	0/0
224	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
225	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
226	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
227	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
228	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
229	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
230	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 373.87	- -	03/2021	0/0
231	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
232	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	10/2021	0/0
233	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	03/2014 03/2022	03/2022	0/0
234	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- 03/2022	03/2022	0/0
235	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- 03/2022	03/2022	0/0
236	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
	<u>North Eastern Railway</u>					
237	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019	0/0
238	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2020	0/0
239	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	01/2020	0/0
240	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2020	0/0
241	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	02/2020	0/0
242	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
243	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
244	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
245	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
246	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
247	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
248	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
249	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
250	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
251	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
252	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
253	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
	<u>North Western Railway</u>					
254	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2019	0/0
255	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	02/2019 -	12/2019	0/0
256	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	05/2020	0/0
257	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2020	0/0
258	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2020	0/0
259	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	12/2021	0/0
260	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
261	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0
262	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
263	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
264	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	06/2020	0/0
265	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	03/2021	0/0
266	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 876.00	03/2016 -	03/2021	0/0
267	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	12/2021	0/0
268	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	- -	03/2022	0/0
269	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	03/2023	0/0
270	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
271	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
272	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0
273	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
274	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
275	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	03/2025	0/0
276	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	03/2025	0/0
277	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	03/2025	0/0
278	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	03/2025	0/0
	<u>National High Speed Rail Corporation Limited</u>					
279	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
280	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
281	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
282	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
283	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2020	0/0
284	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	03/2020	0/0
285	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	03/2020	0/0
286	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2020	0/0
287	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2020	0/0
288	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
289	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
290	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
291	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	12/2021	0/0
292	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
293	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2021	0/0
294	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
295	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
296	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
297	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
298	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
299	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2024	0/0
300	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
301	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
302	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
303	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
304	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2026	0/0
305	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2026	0/0
	<u>Railway Electrification</u>					
306	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	<u>South Central Railway</u>					
307	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2021	0/0
308	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
309	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2023	0/0
310	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2023	0/0
311	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2023	0/0
312	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
313	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
314	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
315	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
316	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
	<u>South East Central Railway</u>					
317	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,413.76	- 10/2019	10/2019	0/0
318	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	12/2019 10/2019	10/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
319	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.00	12/2021 12/2021	12/2021	0/0
	<u>South Eastern Railway</u>					
320	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 11/2019	11/2019	0/0
321	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	- -	06/2020	0/0
322	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 -	06/2020	0/0
323	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2021	0/0
324	TAMLUK DIGHA 88.9 KM WITH MM DESHPURAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL	01/1991	1,013.45 -	12/2021 -	12/2021	0/0
325	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2024	0/0
326	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	03/2025	0/0
327	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	03/2025	0/0
328	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
329	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	- -	03/2030	0/0
330	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 -	03/2003 -	03/2030	0/0
331	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
332	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
	<u>South Western Railway</u>					
333	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	03/2020	0/0
334	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	03/2020	0/0
335	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	03/2021	0/0
336	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
337	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
338	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
339	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
340	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
341	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
342	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
343	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
344	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
345	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
346	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	12/2024	0/0
	<u>Southern Railway</u>					
347	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018	0/0
348	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2019	0/0
349	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2020	0/0
350	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
351	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 951.24	- -	03/2020	0/0
352	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
353	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2021	0/0
354	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2021	0/0
355	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
356	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
357	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-	0/0
358	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
359	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
360	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
361	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
362	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
363	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
364	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-	0/0
365	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-	0/0
366	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
367	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-	0/0
368	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	- 06/2022	-	0/0
369	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-	0/0
370	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
371	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
	<u>Western Railway</u>					
372	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 -	03/2021 -	03/2019	0/0
373	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017	0/0
374	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	03/2019 03/2020	03/2020	0/0
375	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	03/2020 03/2021	03/2021	0/0
376	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2021	03/2021	0/0
377	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 03/2021	03/2021	0/0
378	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	03/2020 03/2021	03/2021	0/0
379	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 06/2021	06/2021	0/0
380	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	03/2012 03/2022	03/2022	0/0
381	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2022	03/2022	0/0
382	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	03/2019 03/2022	03/2022	0/0
383	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,338.15	03/2022 03/2023	03/2023	0/0
384	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
385	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
386	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
387	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
388	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
389	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
390	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	02/2019	0/0
391	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	06/2019	0/0
392	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	06/2019	0/0
393	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 -	06/2019	0/0
394	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 -	06/2019	0/0
395	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 -	06/2019	0/0
396	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	06/2019	0/0
397	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	06/2019	0/0
398	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	06/2019	0/0
399	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	06/2019	0/0
400	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 - [N24000971]MORTH,ANDHRA PRADESH	08/2016	574.19 -	07/2017 -	07/2019	0/0
401	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019	0/0
402	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	07/2019	0/0
403	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	07/2019	0/0
404	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	07/2019	0/0
405	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 -	08/2019	0/0
406	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 -	08/2019	0/0
407	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
408	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH	01/2017	263.45 -	09/2017 -	09/2019	0/0
409	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	11/2019	0/0
410	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
411	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
412	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
413	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
414	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	11/2019	0/0
415	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH	02/2017	429.43 -	11/2017 -	11/2019	0/0
416	BHADGAON TO CHALISGAON - [N24001047]MORTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	11/2019	0/0
417	WIDENING AND STRENGTHENING OF EXISTING SINGLE LANE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	12/2019	0/0
418	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
419	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
420	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
421	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2019	0/0
422	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	12/2019	0/0
423	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	12/2019	0/0
424	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2019	0/0
425	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	12/2019	0/0
426	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0
427	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	12/2019	0/0
428	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
429	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	12/2019	0/0
430	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	12/2019	0/0
431	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	12/2019	0/0
432	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	12/2019	0/0
433	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2019	0/0
434	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	12/2019	0/0
435	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2019	0/0
436	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA	02/2018	355.99 355.99	12/2019 -	12/2019	0/0
437	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	01/2020	0/0
438	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MORTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	01/2020	0/0
439	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH	01/2017	576.48 -	01/2018 -	01/2020	0/0
440	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
441	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH	03/2018	289.67 290.00	08/2018 -	02/2020	0/0
442	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH	01/2018	418.03 -	08/2018 -	02/2020	0/0
443	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH	03/2018	228.32 -	08/2018 -	03/2020	0/0
444	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
445	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 -	05/2020	0/0
446	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	06/2020	0/0
447	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	08/2020	0/0
448	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	08/2020	0/0
449	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
450	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
451	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
452	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
453	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
454	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
455	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
456	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
457	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
458	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
459	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
460	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
461	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
462	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
463	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
464	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
465	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
466	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
467	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
468	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
469	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
470	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
471	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
472	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
473	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
474	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
475	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
476	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
477	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
478	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
479	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
480	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
481	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
482	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
483	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
484	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-	0/0
485	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-	0/0
486	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
487	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
488	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
489	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
490	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
491	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
492	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
493	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
494	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
495	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
496	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
497	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA - [N24000918]MORTH,ODISHA	07/2013	251.92 -	10/2015 -	-	0/0
498	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA - [N24000919]MORTH,ODISHA	07/2013	265.35 -	10/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
499	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA - [N24000924]MORTH,ODISHA	03/2015	229.29 -	11/2015 -	-	0/0
500	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH	09/2016	372.68 -	02/2017 -	-	0/0
501	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 -	-	0/0
502	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH	03/2016	995.09 995.00	05/2016 -	-	0/0
503	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
504	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MORTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 -	-	0/0
505	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
506	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	07/2019	0/0
507	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	07/2019	0/0
508	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019	0/0
509	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019	0/0
510	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019	0/0
511	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019	0/0
512	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019	0/0
513	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019	0/0
514	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019	0/0
515	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019	0/0
516	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
517	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-	0/0
518	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-	0/0
519	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-	0/0
520	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-	0/0
521	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-	0/0
522	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
523	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
524	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
525	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-	0/0
526	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
527	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
528	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	- -	-	0/0
529	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	- -	-	0/0
530	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 -	- -	-	0/0
531	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 -	- -	-	0/0
532	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	-	0/0
533	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-	0/0
534	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-	0/0
535	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-	0/0
<u>National Highways Authority Of India</u>						
536	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019	0/0
537	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	02/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
538	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	02/2019	0/0
539	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
540	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019	0/0
541	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	03/2019	0/0
542	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	-	03/2019	0/0
543	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	03/2019	0/0
544	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2019	0/0
545	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	-	03/2019	0/0
546	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	-	03/2019	0/0
547	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	-	03/2019	0/0
548	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	04/2019	0/0
549	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2019	0/0
550	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	04/2019	0/0
551	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	04/2019	0/0
552	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	04/2019	0/0
553	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	04/2019	0/0
554	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	04/2019	0/0
555	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	05/2019	0/0
556	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	05/2019	0/0
557	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	-	05/2019	0/0
558	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	05/2019	0/0
559	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	05/2019	0/0
560	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	06/2019	0/0
561	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
562	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	06/2019	0/0
563	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	06/2019	0/0
564	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	06/2019	0/0
565	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	-	06/2019	0/0
566	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018	0/0
567	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2018	0/0
568	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2018	0/0
569	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2018	0/0
570	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	03/2019	0/0
571	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	-	05/2019	0/0
572	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
573	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	-	06/2019	0/0
574	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	-	06/2019	0/0
575	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	06/2019	0/0
576	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	-	06/2019	0/0
577	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019	0/0
578	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	06/2019	0/0
579	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	07/2019	0/0
580	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	07/2019	0/0
581	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	07/2019	0/0
582	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019	0/0
583	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2019	0/0
584	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	07/2019	0/0
585	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
586	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	07/2019	0/0
587	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	07/2019	0/0
588	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	07/2019	0/0
589	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 -	07/2019	0/0
590	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	08/2019	0/0
591	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	08/2019	0/0
592	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	08/2019	0/0
593	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	08/2019	0/0
594	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	08/2019	0/0
595	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0
596	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	09/2019	0/0
597	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	09/2019	0/0
598	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
599	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
600	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
601	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	09/2019	0/0
602	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	09/2019	0/0
603	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	09/2019	0/0
604	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
605	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	09/2019	0/0
606	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	09/2019	0/0
607	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	09/2019	0/0
608	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	10/2019	0/0
609	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	10/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
610	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	-	10/2019	0/0
611	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018	10/2019	0/0
612	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018	10/2019	0/0
613	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019	10/2019	0/0
614	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	-	10/2019	0/0
615	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	-	10/2019	0/0
616	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	-	11/2019	0/0
617	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018	11/2019	0/0
618	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019	11/2019	0/0
619	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	-	11/2019	0/0
620	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019	11/2019	0/0
621	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019	11/2019	0/0
622	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019	11/2019	0/0
623	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	-	11/2019	0/0
624	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020	11/2019	0/0
625	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020	11/2019	0/0
626	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017	11/2019	0/0
627	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017	11/2019	0/0
628	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017	11/2019	0/0
629	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	-	11/2019	0/0
630	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008	12/2019	0/0
631	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012	12/2019	0/0
632	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014	12/2019	0/0
633	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
634	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2019	0/0
635	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2019	0/0
636	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	12/2019	0/0
637	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	12/2019	0/0
638	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	12/2019	0/0
639	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	12/2019	0/0
640	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	-	12/2019	0/0
641	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	12/2019	0/0
642	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	-	12/2019	0/0
643	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	-	12/2019	0/0
644	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	-	12/2019	0/0
645	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	07/2018 -	12/2019	0/0
646	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	-	01/2020	0/0
647	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	-	01/2020	0/0
648	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	06/2018 -	01/2020	0/0
649	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	-	01/2020	0/0
650	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	08/2018 -	01/2020	0/0
651	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	10/2017 -	01/2020	0/0
652	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	-	01/2020	0/0
653	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	04/2018 -	02/2020	0/0
654	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	-	02/2020	0/0
655	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	-	02/2020	0/0
656	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT (APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	-	02/2020	0/0
657	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	02/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
658	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2020	0/0
659	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2020	0/0
660	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2020	0/0
661	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2020	0/0
662	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2020	0/0
663	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
664	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
665	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
666	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
667	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2020	0/0
668	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	03/2020	0/0
669	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	03/2020	0/0
670	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	03/2020	0/0
671	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	03/2020	0/0
672	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	03/2020	0/0
673	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	03/2020	0/0
674	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	04/2020	0/0
675	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
676	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
677	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	04/2020	0/0
678	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
679	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
680	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	05/2020	0/0
681	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
682	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	05/2020	0/0
683	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	05/2020	0/0
684	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	05/2020	0/0
685	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
686	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	05/2020	0/0
687	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
688	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	05/2020	0/0
689	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	05/2020	0/0
690	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	05/2020	0/0
691	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	05/2020	0/0
692	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	06/2020	0/0
693	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	06/2020	0/0
694	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 -	06/2020	0/0
695	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	06/2020	0/0
696	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 -	06/2020	0/0
697	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
698	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
699	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	06/2020	0/0
700	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
701	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
702	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	07/2020	0/0
703	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	07/2020	0/0
704	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	07/2020	0/0
705	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	08/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
706	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
707	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	08/2020	0/0
708	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
709	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
710	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	08/2020	0/0
711	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	08/2020	0/0
712	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	08/2020	0/0
713	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
714	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	09/2020	0/0
715	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
716	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0
717	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020	0/0
718	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	11/2020	0/0
719	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
720	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020	0/0
721	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
722	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	11/2020	0/0
723	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
724	FOUR LANINIG OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	11/2020	0/0
725	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	11/2020	0/0
726	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	11/2020	0/0
727	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	11/2020	0/0
728	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	12/2020	0/0
729	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
730	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
731	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
732	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	12/2020	0/0
733	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	-	12/2020	0/0
734	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	-	12/2020	0/0
735	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	-	12/2020	0/0
736	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	-	01/2021	0/0
737	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	-	01/2021	0/0
738	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	-	01/2021	0/0
739	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	-	01/2021	0/0
740	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	-	01/2021	0/0
741	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	-	02/2021	0/0
742	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	-	02/2021	0/0
743	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2021	0/0
744	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	-	03/2021	0/0
745	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	-	04/2021	0/0
746	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 -	04/2021	0/0
747	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDER - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	-	04/2021	0/0
748	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	-	04/2021	0/0
749	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
750	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	-	05/2021	0/0
751	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	-	06/2021	0/0
752	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	-	07/2021	0/0
753	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	-	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
754	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
755	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	07/2021	0/0
756	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	07/2021	0/0
757	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
758	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
759	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	08/2021	0/0
760	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
761	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	08/2021	0/0
762	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
763	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
764	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
765	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
766	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
767	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
768	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
769	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
770	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
771	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
772	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
773	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
774	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
775	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
776	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
777	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
778	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
779	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
780	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
781	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
782	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
783	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
784	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
785	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
786	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
787	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
788	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
789	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
790	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
791	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
792	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
793	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
794	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
795	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
796	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
797	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
798	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
799	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
800	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
801	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
802	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
803	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
804	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
805	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
806	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
807	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
808	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
809	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
810	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
811	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
812	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-	0/0
813	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
814	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
815	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
816	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
817	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
818	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-	0/0
819	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
820	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
821	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-	0/0
822	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
823	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
824	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
825	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
826	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
827	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
828	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
829	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
830	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
831	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
832	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
833	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
834	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
835	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
836	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
837	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
838	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
839	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
840	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
841	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
842	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
843	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
844	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
845	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
846	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
847	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
848	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
849	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
850	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
851	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-	0/0
852	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
853	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
854	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
855	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
856	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
857	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
858	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
859	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
860	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
861	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
862	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
863	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
864	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965,) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
865	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
866	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
867	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
868	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
869	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	-	0/0
870	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
871	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-	0/0
872	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
873	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-	0/0
874	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-	0/0
	<u>National Highways Development Project</u>					
875	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	08/2019	0/0
876	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	08/2019	0/0
877	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	01/2020 -	01/2020	0/0
878	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	02/2020	0/0
879	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	03/2020	0/0
880	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2020	0/0
881	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
882	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
	<u>Public Works Dept Of State</u>					
883	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA	08/2016	367.44 -	01/2017 -	01/2017	0/0
884	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA	08/2016	175.20 -	01/2017 -	01/2019	0/0
885	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	01/2019	0/0
886	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	02/2017	0/0
887	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	02/2017	0/0
888	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	03/2017	0/0
889	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	03/2017	0/0
890	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	03/2019 -	05/2019	0/0
891	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	05/2019	0/0
892	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	05/2019	0/0
893	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	05/2019	0/0
894	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	06/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
895	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	06/2019	0/0
896	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	06/2019	0/0
897	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	06/2019	0/0
898	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	06/2019	0/0
899	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	06/2019	0/0
900	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA	03/2018	159.97 -	06/2019 -	06/2019	0/0
901	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	07/2018	0/0
902	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	08/2016	0/0
903	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	09/2017	0/0
904	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	09/2020	0/0
905	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	10/2018	0/0
906	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	10/2018	0/0
907	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	11/2010	0/0
908	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 307.47	02/2018 -	11/2014	0/0
909	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	11/2017	0/0
910	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD, WEST BENGAL	03/2017	202.69 202.69	11/2019 -	11/2019	0/0
911	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	11/2020	0/0
912	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
913	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 353.89	11/2015 06/2019	06/2019	0/0
914	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0
915	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019	0/0
916	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	07/2019	0/0
917	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	05/2019 -	07/2019	0/0
918	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA	03/2018	192.67 -	07/2019 -	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
919	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	07/2019	0/0
920	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	07/2019	0/0
921	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	05/2019 -	08/2019	0/0
922	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	08/2017 -	08/2019	0/0
923	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2019	0/0
924	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 09/2019	09/2019	0/0
925	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	09/2019	0/0
926	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	09/2019	0/0
927	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	03/2019 -	09/2019	0/0
928	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	09/2019	0/0
929	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB	10/2017	1,069.59 -	10/2019 -	10/2019	0/0
930	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]PWD,TELANGANA	01/2017	196.52 -	10/2019 -	10/2019	0/0
931	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD,TELANGANA	01/2017	605.08 -	10/2019 -	10/2019	0/0
932	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD,BIHAR	11/2016	230.34 -	10/2019 -	10/2019	0/0
933	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL	03/2016	271.17 291.20	11/2018 11/2019	11/2019	0/0
934	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	02/2018 -	11/2019	0/0
935	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	02/2018 -	11/2019	0/0
936	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	11/2019	0/0
937	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	11/2019	0/0
938	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	11/2019	0/0
939	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	02/2018 -	11/2019	0/0
940	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	01/2019 -	11/2019	0/0
941	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	06/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
942	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	11/2019	0/0
943	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD,TELANGANA	02/2018	294.13 -	11/2019 -	11/2019	0/0
944	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD,TELANGANA	02/2018	220.28 -	11/2019 -	11/2019	0/0
945	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	03/2018 -	11/2019	0/0
946	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	12/2019	0/0
947	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	12/2019	0/0
948	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	12/2019	0/0
949	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	02/2013 09/2017	12/2019	0/0
950	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	12/2019	0/0
951	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	12/2019	0/0
952	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	02/2019 -	12/2019	0/0
953	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	03/2019 -	12/2019	0/0
954	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]PWD,TELANGANA	01/2017	283.00 -	12/2019 -	12/2019	0/0
955	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	05/2019 -	12/2019	0/0
956	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD,TELANGANA	01/2018	230.03 -	12/2019 -	12/2019	0/0
957	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	02/2014 -	12/2019	0/0
958	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	01/2020	0/0
959	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	01/2020	0/0
960	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	01/2020	0/0
961	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	02/2020	0/0
962	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	02/2020	0/0
963	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	03/2020	0/0
964	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	03/2020	0/0
965	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	04/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
966	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTING - [N24000992]PWD, TELANGANA	02/2018	426.52	04/2020	04/2020	0/0
967	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]PWD, TELANGANA	01/2018	283.15	05/2020	05/2020	0/0
968	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD, KARNATAKA	05/2018	171.60	05/2018	05/2020	0/0
969	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD, MIZORAM	08/2010	195.04	10/2010	06/2020	0/0
970	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD, MADHYA PRADESH	03/2018	166.21	08/2018	06/2020	0/0
971	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD, MADHYA PRADESH	01/2017	205.05	03/2017	06/2020	0/0
972	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD, MADHYA PRADESH	03/2018	217.22	08/2018	06/2020	0/0
973	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD, PUNJAB	03/2018	173.24	06/2020	06/2020	0/0
974	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD, TELANGANA	02/2018	206.13	06/2020	06/2020	0/0
975	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD, JHARKHAND	03/2018	212.99	06/2020	06/2020	0/0
976	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD, MADHYA PRADESH	02/2018	169.63	03/2018	07/2020	0/0
977	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD, PUNJAB	03/2018	322.48	07/2020	07/2020	0/0
978	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD, TELANGANA	03/2018	626.76	07/2020	07/2020	0/0
979	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD, PUNJAB	03/2018	293.10	08/2020	08/2020	0/0
980	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD, PUNJAB	03/2018	293.64	08/2020	08/2020	0/0
981	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD, PUNJAB	03/2018	293.64	08/2020	08/2020	0/0
982	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD, TELANGANA	03/2018	322.81	09/2020	09/2020	0/0
983	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]PWD, WEST BENGAL	03/2018	254.30	10/2020	10/2020	0/0
984	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]PWD, PUNJAB	03/2018	170.57	11/2020	11/2020	0/0
985	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD, BIHAR	05/2014	199.98	08/2016	12/2020	0/0
986	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD, KARNATAKA	02/2017	157.32	05/2019	05/2021	0/0
987	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27	08/2019	08/2021	0/0
988	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78	08/2019	08/2021	0/0
989	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]PWD, ASSAM	09/2018	160.00	09/2021	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
990	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
991	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
992	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
993	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
994	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
995	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
996	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
997	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
998	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
999	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
1000	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
1001	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-	0/0
1002	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
1003	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
1004	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
1005	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
1006	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-	0/0
1007	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-	0/0
1008	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 -	05/2019 -	-	0/0
1009	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA	01/2019	193.19 -	- -	-	0/0
1010	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR	03/2018	153.24 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Cochin Shipyard Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1011	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL,KERALA	05/2016	970.00 -	05/2020 -	05/2020	0/0
1012	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL,KERALA	07/2016	1,799.00 -	05/2021 -	05/2021	0/0
	<u>Inland Waterways Authority Of India</u>					
1013	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	4,200.00 -	03/2023 -	03/2023	0/0
	<u>Kamarajar Port Limited</u>					
1014	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	05/2020	0/0
	<u>Mumbai Port Trust</u>					
1015	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	-	0/0
	<u>Port Trust</u>					
1016	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
1017	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
1018	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 219.60	05/2018 07/2019	07/2019	0/0
1019	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	10/2018 09/2019	09/2019	0/0
	<u>Department Of Telecommunication</u>					
1020	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
1021	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Bangalore Metro Rail Corporation Limited</u>					
1022	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
1023	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	06/2019	0/0
1024	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
1025	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1026	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	07/2019 12/2019	12/2019	0/0
1027	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	03/2020	0/0
1028	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
1029	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 -	09/2020	0/0
1030	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	10/2020	0/0
1031	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	12/2020	0/0
1032	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- 08/2020	03/2021	0/0
1033	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	06/2021 -	06/2021	0/0
1034	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	11/2021	0/0
1035	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
1036	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-	0/0
1037	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	- -	-	0/0
	<u>Chennai Metro Rail Ltd</u>					
1038	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-	0/0
	<u>Hindustan Steelwork Construction Limited</u>					
1039	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1040	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1041	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
1042	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1043	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
1044	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1045	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
1046	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1047	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1048	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1049	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1050	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1051	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0
1052	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1053	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1054	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1055	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1056	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharastra Metro Rail Corporation Ltd.</u>					
1057	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 12/2021	12/2021	0/0
1058	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1059	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1060	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1061	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1062	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
1063	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1064	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (June 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		11,65,932.15 -			0/0
	Grand Total		11,65,932.15			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64	203.82	117.55	03/2023 -	03/2021
	Total		1,186.64 -	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
2	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,649.57	12/2020 -	08/2020
3	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00	151.00	147.35	09/2019 -	06/2019
4	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00	324.00	147.63	06/2020 -	03/2020
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL [N16000252]	5/2016	664.00	664.00	564.33	12/2020 -	02/2020
6	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58	384.58	73.31	04/2021 -	04/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	33.85	09/2022 -	06/2021
	Total		7,556.58 -	8,557.58	2,616.04		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
8	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	480.35	03/2024 -	03/2022
	<u>East Central Railways</u>						
9	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23	348.23	156.48	03/2021 -	12/2020
	<u>North Central Railway</u>						
10	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00	2,001.00	395.59	03/2021 03/2023	03/2021
	<u>North East Frontier Railway</u>						
11	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48	4,084.69	285.46	12/2015 06/2021	03/2020
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27	612.00	181.63	12/2021 -	03/2020

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
13	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32	2,182.00	571.56	03/2022 -	03/2020
	<u>North Eastern Railway</u>						
14	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42	1,295.42	249.27	03/2022 -	12/2019
15	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00	366.71	9.10	01/2022 -	01/2020
	<u>Rail Vikas Nigam Ltd.</u>						
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	0.19	12/2025 -	03/2025
	Total		12,769.97 -	15,241.30	2,329.63		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
17	PARSHURAM GHAT TO ARAWALI - [N24001133]	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
	<u>National Highways Authority Of India</u>						
18	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02	157.49	-	03/2020 -	02/2020
19	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19	254.00	248.60	03/2020 -	09/2019
20	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79	552.90	480.73	03/2020 -	09/2019
21	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32	503.10	0.95	03/2020 -	11/2019
22	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50	172.16	107.13	03/2020 -	06/2019
23	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68	235.90	89.96	03/2020 -	06/2019
24	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	605.00	04/2020 -	11/2019
	Total		4,113.64 -	3,752.69	2,187.52		
	Grand Total		25,626.83	27,755.39	7,250.74		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	186.88	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	308.29	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	87.14	03/2022 -	03/2022
5	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	258.98	08/2019 -	08/2019
6	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
7	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
8	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
9	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.13	03/2024 -	03/2024
	<u>Mahanadi Coal Fields Limited</u>						
10	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,546.73	03/2026 -	03/2026
11	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	437.89	03/2021 -	03/2021
12	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,111.70	03/2029 -	03/2029
13	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	82.60	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
14	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.88	09/2019 -	09/2019
15	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	6,531.52	11/2021 -	11/2021
16	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
17	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	255.65	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
19	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
20	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
21	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.29	03/2023 -	03/2023
22	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	88.29	03/2022 -	03/2022
23	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	80.33	03/2020 -	03/2020
24	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
25	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
26	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
27	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
28	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.60	03/2021 -	03/2021
29	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,902.94	03/2023 -	03/2023
30	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,057.87	03/2023 -	03/2023
31	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.94	03/2023 -	03/2023
32	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	67.40	03/2020 -	03/2020
33	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
34	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.59	03/2021 -	03/2021
35	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	115.41	03/2021 -	03/2021
36	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
37	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	26.61	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
38	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	175.30	03/2020 -	03/2020
39	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	150.04	03/2021 -	03/2021
41	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
42	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
43	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	18.45	03/2022 -	03/2022
44	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
45	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	258.40	03/2025 -	03/2025
46	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	168.92	03/2021 -	03/2021
47	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
48	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.81	03/2020 -	03/2020
49	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	119.73	03/2023 -	03/2023
	Total		74,644.94 -	74,867.48	18,817.30		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
50	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	79.33	08/2020 -	08/2020
	Total		285.95 -	285.95	79.33		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
51	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	72.95	11/2019 -	11/2019
52	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	88.74	11/2019 -	11/2019
53	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	81.46	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
54	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	92.10	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	335.25		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
55	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
56	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	5,540.00	102.61	04/2021 04/2021	04/2021
57	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014	9/2017	166.62 -	166.62	134.98	06/2019 -	06/2019
58	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
59	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	.30	04/2021 04/2021	04/2021
60	UTKAL D AND E COAL BLOCK - [N10000011	5/2016	534.00 -	534.00	316.08	01/2020 01/2020	01/2020
	Total		7,078.62 -	7,078.62	585.89		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
61	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260	2/2016	554.00 -	554.00	315.44	02/2020 -	02/2020
62	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346	9/2018	11,130.00 -	11,130.00	14.14	03/2023 -	03/2023
63	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364	7/2017	580.20 -	580.20	27.71	02/2021 -	02/2021
64	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365	12/2017	1,524.06 -	1,524.06	13.10	12/2021 -	12/2021
65	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347	10/2018	206.26 -	206.26	.30	03/2021 -	03/2021
66	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341	8/2017	750.00 -	750.00	32.69	12/2020 -	12/2020
67	PUNE POL STORAGE DEPOT - [N16000313	8/2016	282.64 -	282.64	105.42	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
68	MMPL PIPELINE REROUTING PROJECT - [N16000261] <u>Chennai Petroleum Corporation Limited</u>	4/2013	449.58 -	449.58	153.11	12/2019 -	12/2019
69	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	848.87	12/2019 -	12/2019
70	RE-LIQUIFIED NATURAL GAS - [N16000301] <u>Gas Authority Of India Limited</u>	8/2017	421.00 -	421.00	100.28	08/2020 -	08/2020
71	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
72	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	.99	08/2020 -	08/2020
73	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	-	02/2021 -	02/2021
74	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	935.94	12/2021 -	12/2021
75	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	40.86	10/2022 -	10/2022
76	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	42.87	10/2022 -	10/2022
77	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	25.83	07/2022 -	07/2022
78	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	58.27	10/2022 -	10/2022
79	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	45.20	07/2022 -	07/2022
80	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	988.14	12/2020 -	12/2020
81	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,248.16	12/2020 -	12/2020
82	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	157.26	12/2020 -	12/2020
83	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	116.05	04/2022 -	04/2022
84	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,327.89	12/2020 -	12/2020
85	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271] <u>Hindustan Petroleum Corporation Limited</u>	7/2015	2,881.40 -	2,000.00	1,237.86	12/2020 -	12/2020
86	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	678.31	10/2014 08/2019	08/2019
87	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	104.23	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
88	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
89	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
90	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	58.20	11/2020 -	11/2020
91	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021
92	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	600.15	03/2021 -	03/2021
93	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,068.39	03/2020 -	03/2020
94	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	4,913.36	07/2020 -	07/2020
95	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,386.04	06/2020 -	06/2020
96	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	407.00	359.31	09/2019 -	09/2019
<u>Indian Oil Corporation Limited</u>							
97	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
98	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
99	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
100	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	36.68	12/2019 -	12/2019
101	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
102	BS-VI PROJECT AT PARADIP - [N16000362]	5/2019	3,361.00 -	3,361.00	269.74	08/2021 -	08/2021
103	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
104	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	6.82	02/2020 -	02/2020
105	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	460.33	09/2019 -	09/2019
106	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	8.19	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
107	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,824.73	09/2019 -	09/2019
108	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
109	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	109.28	12/2021 -	12/2021
110	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	374.07	09/2019 -	09/2019
111	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	6.64	06/2020 -	06/2020
112	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	105.30	07/2020 -	07/2020
113	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	132.24	09/2019 -	09/2019
114	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	13.44	02/2020 -	02/2020
115	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	13.11	01/2021 -	01/2021
116	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
117	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
118	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	300.50	10/2019 -	10/2019
119	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	7.18	10/2021 -	10/2021
120	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	125.80	03/2021 -	03/2021
121	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	161.68	08/2020 -	08/2020
122	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	101.40	02/2020 -	02/2020
123	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	240.73	10/2021 -	10/2021
124	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	6.71	01/2021 -	01/2021
125	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	10.40	12/2021 -	12/2021
126	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	1,453.91	07/2019 -	07/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
127	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.49	10/2020 -	10/2020
128	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	.44	08/2020 -	08/2020
129	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,409.29	09/2019 -	09/2019
130	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]	5/2016	261.00 -	261.00	27.66	01/2021 -	01/2021
131	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
132	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	887.73	08/2021 -	08/2021
133	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,498.18	11/2019 -	11/2019
134	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	598.85	10/2019 -	10/2019
135	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	759.67	12/2020 -	12/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
136	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	643.05	12/2019 07/2020	07/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
137	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019
138	HEERA REDEVELOPMENT - PHASE III - [N16000360]	5/2019	2,494.68 -	2,494.68	-	12/2021 -	12/2021
139	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	2/2019	3,660.71 -	3,740.05	126.66	04/2021 05/2021	05/2021
140	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	370.84	03/2022 -	03/2022
141	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	45.81	05/2021 -	05/2021
142	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	434.78	12/2019 -	12/2019
143	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	193.15	09/2018 07/2019	07/2019
144	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	354.67	03/2026 -	03/2026
145	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	145.01	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
146	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	303.30	03/2023 03/2022	03/2022
147	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,180.79	04/2018 05/2020	05/2020
148	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,313.38	12/2017 03/2020	03/2020
149	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,265.01	05/2013 12/2019	12/2019
150	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	2,185.47	03/2019 05/2020	05/2020
151	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,780.91	05/2019 10/2019	10/2019
152	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,475.92	2,555.11	05/2021 12/2021	12/2021
153	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	833.51	11/2019 -	11/2019
154	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	406.35	11/2019 -	11/2019
155	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	565.15	425.96	11/2019 03/2020	03/2020
156	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,748.30	04/2019 12/2019	12/2019
	<u>Oil India Limited</u>						
157	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	82.95	10/2020 -	10/2020
158	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	3.30	08/2020 -	08/2020
159	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	682.90	6.12	02/2020 -	02/2020
160	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	142.82	12/2019 -	12/2019
	Total		1,61,325.34 -	1,63,828.28	58,381.23		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
161	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	11,322.86	01/2018 03/2020	03/2020
162	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,025.80	03/2013 12/2020	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
163	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,592.34	443.47	09/2019 02/2022	02/2022
164	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	9,645.00	02/2018 06/2020	06/2020
165	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	9,298.78	12/2018 06/2020	06/2020
166	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	1,780.00	03/2023 -	03/2023
167	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
168	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
169	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,595.15	11/2019 -	11/2019
170	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	4,988.68	11/2020 06/2021	06/2021
171	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	8,127.53	01/2020 -	01/2020
172	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,104.40	10/2017 03/2020	03/2020
173	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	16,182.14	10/2011 08/2021	08/2021
174	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	6,271.59	07/2019 06/2020	06/2020
	<u>North East Electric Power Corporation</u>						
175	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,419.34	7,327.76	12/2009 08/2019	08/2019
	<u>Power Grid Corporation Of India Limited</u>						
176	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	4,558.05	10/2012 12/2019	12/2019
177	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	7,922.74	11/2019 -	11/2019
178	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	38.90	05/2020 -	05/2020
179	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	933.96	02/2020 -	02/2020
180	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	92.78	09/2018 09/2019	09/2019
181	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,399.20	07/2020 -	07/2020
182	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	2,516.66	04/2020 -	04/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
183	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	52.63	12/2019 12/2019	12/2019
184	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	116.76	02/2020 02/2020	02/2020
185	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	266.03	01/2019 09/2019	09/2019
186	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	187.60	11/2019 11/2019	11/2019
187	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	185.94	06/2019 -	06/2019
188	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	287.52	04/2018 01/2020	01/2020
189	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	3,115.72	03/2018 12/2019	12/2019
190	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	540.12	06/2014 09/2019	09/2019
191	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,804.46	08/2013 03/2022	03/2022
192	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	548.30	10/2017 09/2019	09/2019
193	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,259.05	04/2016 08/2019	08/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
194	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	222.91	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
195	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	298.76	09/2020 -	09/2020
196	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	503.39	09/2023 -	09/2023
	Total		1,78,998.50 -	2,10,671.04	1,31,339.64		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
197	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,180.11	03/2023 -	03/2023
198	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	305.00	260.45	03/2019 12/2019	12/2019
199	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	66.23	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
200	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	140.79	03/2023 -	03/2023
201	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
202	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
203	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
204	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
205	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	389.29	03/2020 -	03/2020
206	ARARIA-SUPAUL (NL) - [N22000177]	4/2008	1,605.17 -	1,605.17	23.40	- 03/2023	03/2023
	<u>East Coast Railway</u>						
207	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	224.63	03/2020 -	03/2020
208	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	3,382.95	325.64	03/2022 -	03/2022
	<u>Eastern Railways</u>						
209	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	693.80	403.81	03/2020 -	03/2020
	<u>Indian Railway Construction Company Limited</u>						
210	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	1,700.43	48.00	03/2020 06/2023	06/2023
211	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,970.11	619.50	03/2022 12/2022	12/2022
212	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	4/2013	3,055.00 -	3,055.00	1,729.64	09/2018 12/2020	12/2020
	<u>Metropolitan Rapid Transport Projects</u>						
213	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	918.53	256.68	03/2014 03/2021	03/2021
	<u>North Central Railway</u>						
214	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 03/2020	03/2020
215	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.56	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
216	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	5,021.45	2,933.84	03/2014 03/2022	03/2022
217	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.67	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
218	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.92	03/2020 -	03/2020
219	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	454.63	03/2021 -	03/2021
220	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.14	03/2020 -	03/2020
221	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
222	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	4/2008	333.76 -	360.00	6.67	- 03/2022	03/2022
223	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	4/2010	221.42 -	380.00	38.18	- 03/2022	03/2022
	<u>North Eastern Railway</u>						
224	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	12/2022
225	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
226	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>Northern Railway</u>						
227	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
228	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	2,812.27	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
229	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
230	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	366.38	12/2026 -	12/2026
231	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,541.10	03/2023 -	03/2023
232	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	1,100.00	987.29	03/2020 -	03/2020
233	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,500.00	1,197.11	03/2020 -	03/2020
234	VIZIANAGARAM -SAMBALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.68	482.27	12/2024 -	12/2024
235	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) [N22000407]	3/2009	713.48 -	1,950.00	1,803.73	03/2020 -	03/2020
236	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	309.16	12/2024 -	12/2024
237	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	709.85	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
238	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	1,140.64	12/2021 -	12/2021
239	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	267.40	03/2021 -	03/2021
240	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	902.37	12/2021 -	12/2021
241	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	994.43	12/2020 -	12/2020
	<u>South Central Railway</u>						
242	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	1,352.74	269.07	03/2020 03/2020	03/2020
243	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
	<u>South East Central Railway</u>						
244	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	4/2005	383.79 -	1,413.76	1,309.02	- 10/2019	10/2019
245	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.92	1,645.84	04/2020 12/2020	12/2020
246	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	393.46	03/2023 03/2023	03/2023
247	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,226.51	1,034.58	12/2019 10/2019	10/2019
248	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	253.18	12/2021 12/2021	12/2021
249	JHARSUGUDA-BILASPUUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.66	121.56	03/2021 12/2021	12/2021
250	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	860.92	39.80	12/2021 03/2023	03/2023
	<u>South Eastern Railway</u>						
251	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	377.00	174.82	12/2016 11/2019	11/2019
252	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.82	12/2021 -	12/2021
	<u>South Western Railway</u>						
253	YELAHANKA-PENKONDA - [N22000328]	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
254	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
	<u>Southern Railway</u>						
255	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>West Central Railway</u>						
256	RAMGANJIMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,027.12	03/2021 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
257	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,247.64	154.63	03/2022 09/2022	09/2022
258	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	367.59	03/2022 03/2023	03/2023
259	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	1,763.93	624.49	03/2020 03/2022	03/2022
260	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	6,093.31	1,835.18	05/2008 03/2023	03/2023
	<u>Western Railway</u>						
261	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	3,860.40	1,577.87	03/2022 03/2023	03/2023
262	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	321.62	125.76	03/2012 03/2022	03/2022
263	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	700.60	03/2022 03/2022	03/2022
264	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	858.96	534.00	03/2019 03/2022	03/2022
265	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	87.81	- 03/2021	03/2021
266	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	665.69	03/2022 03/2023	03/2023
267	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	663.29	81.64	03/2020 03/2021	03/2021
268	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	64.48	06/2020 06/2021	06/2021
269	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	809.07	596.89	03/2019 03/2020	03/2020
270	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	348.91	03/2021 03/2021	03/2021
271	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,310.23	1,294.00	03/2020 03/2021	03/2021
	Total		2,35,339.01 -	3,03,061.40	63,975.65		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
272	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
273	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
274	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
275	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
276	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
277	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
278	DAHEGAON TO KUHI - [N24001017	1/2017	228.89 229.00	228.89	90.00	06/2019 -	06/2019
279	MORSHI TO MAH/MP BORDER - [N24001016	1/2017	471.61 472.00	471.61	252.90	06/2019 -	06/2019
280	AJANTHA TO BULDHANA - [N24001008	2/2017	401.00 401.00	401.00	82.81	07/2019 -	07/2019
281	ANJANGAON TO MAH/MP BORDER - [N24001007	1/2017	359.00 359.00	359.00	149.80	06/2019 -	06/2019
282	AKOT TO ANJANGAON - [N24001006	1/2017	245.77 246.00	245.77	95.98	06/2019 -	06/2019
283	KARASWADA TO BAMBOLIM - [N24001005	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019
284	PATRADEVI TO KARASWADA 4L - [N24001004	3/2017	634.32 -	634.32	102.33	05/2020 -	05/2020
285	AKOLA TO AKOT - [N24001003	1/2017	313.95 -	313.95	31.05	06/2019 -	06/2019
286	SARSAM TO KOTHARI - [N24001002	2/2016	545.64 -	545.64	45.01	07/2019 -	07/2019
287	MAJALGAON TO KAIJ - [N24001036	1/2017	413.99 -	413.99	310.33	07/2019 -	07/2019
288	PARTUR TO MAJALGAON - [N24001034	1/2017	420.57 -	420.57	121.39	07/2019 -	07/2019
289	MANTHA TALUKAS BORDER TO PARTUR - [N24001033	1/2017	486.19 -	486.19	174.29	07/2019 -	07/2019
290	MANJUSUMBA TO CHUMBALI - [N24001031	1/2017	228.54 -	228.54	87.30	08/2019 -	08/2019
291	PIMPLA TO MANJARSUMBHA - [N24001030	1/2017	595.77 -	595.77	119.44	08/2019 -	08/2019
292	AHMADPUR TO PIMPLA - [N24001029	1/2017	422.38 -	422.38	136.58	08/2019 -	08/2019
293	PATGAON KHOPOLI SECTION I - [N24001028	1/2018	170.00 -	170.00	15.57	12/2019 -	12/2019
294	SHAHPUR PATGAON SECTION I - [N24001027	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
295	BHANDARA TO GHOTITOK - [N24001018	1/2017	392.83 393.00	392.83	254.60	06/2019 -	06/2019
296	JALGAON TO BHADGAON - [N24001045	1/2018	307.54 308.00	307.54	75.59	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
297	NILAJPHATA TO BHANDARA - [N24001043]	1/2018	420.63 421.00	420.63	3.60	05/2020 -	05/2020
298	KALMAB TO RALEGAON - [N24001044]	1/2017	467.78 -	467.78	294.91	06/2019 -	06/2019
299	SALAIKHURD TO TIRORA - [N24001042]	1/2018	415.25 415.25	415.25	36.22	12/2019 -	12/2019
300	SHIROD SHAHPURER TO NANDED - [N24001041]	1/2017	211.34 -	211.34	94.83	07/2019 -	07/2019
301	MAHAD TO RAIGAD FORT - [N24001038]	7/2018	237.40 -	237.40	7.34	05/2020 -	05/2020
302	JAHIRABAD TO LATUR - [N24001040]	1/2017	461.96 -	461.96	116.43	11/2019 -	11/2019
303	KAJJ TO KUSALAM - [N24001037]	1/2017	554.78 -	554.78	136.90	07/2019 -	07/2019
304	MANSAR TO SALAIKHURD - [N24001035]	1/2018	418.36 -	418.36	70.13	12/2019 -	12/2019
305	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
306	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	64.97	06/2020 -	06/2020
307	PUNE TO MALE VILLAGE - [N24001078]	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
308	DEULGAON SAKARSHA TO MEHKAR - [N24001076]	3/2018	219.91 -	219.91	84.46	12/2019 -	12/2019
309	KUNDRAL TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	90.75	12/2019 -	12/2019
310	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]	3/2018	249.29 -	249.29	32.20	12/2019 -	12/2019
311	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	44.02	08/2020 -	08/2020
312	KOTHARI TO DHANORA - [N24001073]	9/2018	301.38 301.00	301.38	-	08/2020 -	08/2020
313	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	27.50	12/2019 -	12/2019
314	KURUDWADI TO PANDHARPUR - [N24001101]	1/2017	307.63 -	307.63	136.17	07/2019 -	07/2019
315	AHMEDNAGAR TO BARAMATI - [N24001100]	1/2017	955.40 -	955.40	301.50	08/2019 -	08/2019
316	MHASWAD TO TEMBHURNI - [N24001099]	1/2017	488.60 -	488.60	151.71	07/2019 -	07/2019
317	WARDHA TO HINGAGHAT - [N24001098]	1/2018	216.90 217.00	216.90	20.00	12/2019 -	12/2019
318	SELDOH TO PANVAR - [N24001097]	7/2018	404.33 404.00	404.33	14.19	05/2020 -	05/2020
319	ARNI TO NAIGAINBANDI - [N24001093]	12/2017	309.94 310.00	309.94	19.32	12/2019 -	12/2019
320	SATARA TO MHASWAD - [N24001092]	1/2017	653.46 -	653.46	167.18	07/2019 -	07/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
321	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
322	KOLDE TO KHETIYA - [N24001090]	1/2017	509.18 -	509.18	157.93	07/2019 -	07/2019
323	BHOKAR TO SARSAM - [N24001128]	2/2017	295.09 -	295.99	155.64	07/2019 -	07/2019
324	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]	2/2017	406.51 -	406.51	406.58	06/2019 -	06/2019
325	FARDAPUR TO JALGAON - [N24001126]	2/2017	456.45 -	456.45	66.10	06/2019 -	06/2019
326	SILLOD TO FARDAPUR - [N24001125]	2/2017	337.46 -	337.46	44.03	06/2019 -	06/2019
327	AURANGABAD TO SILLOD - [N24001124]	2/2017	456.32 -	456.32	79.30	06/2019 -	06/2019
328	SHIRUR TO KHARDA - [N24001123]	2/2017	381.77 -	381.77	122.79	06/2019 -	06/2019
329	PAITHAN TO SHIRUR - [N24001122]	3/2017	341.80 -	341.80	88.00	06/2019 -	06/2019
330	NAGBHID TO ARMORI - [N24001119]	9/2016	269.05 -	269.05	173.91	07/2019 -	07/2019
331	MUL TO CHANDRAPUR - [N24001117]	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019
332	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	8.86	04/2020 -	04/2020
333	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	68.97	12/2019 -	12/2019
334	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
335	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
336	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	609.61	11/2019 -	11/2019
337	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	52.87	06/2021 -	06/2021
338	GADCHIROLI TO MUL - [N24001116]	12/2016	484.15 -	484.15	127.31	06/2019 -	06/2019
339	NASRATPUR TO BARASGAON - [N24001112]	7/2016	406.54 407.00	406.54	136.00	09/2019 -	09/2019
340	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	24.29	04/2020 -	04/2020
341	KUSUMBA TO MALEGAON - [N24001109]	3/2018	243.45 244.00	243.45	47.02	12/2019 -	12/2019
342	CHALISGAON TO NANDGAON - [N24001108]	3/2018	206.97 207.00	206.97	46.89	12/2019 -	12/2019
343	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
344	SARAD VANI PIMPALGAON - [N24001103]	1/2017	250.46 -	250.46	1,691.63	07/2019 -	07/2019
345	PANDHARPUR TO SANGOLA - [N24001102]	7/2017	218.38 -	218.38	161.75	07/2019 -	07/2019
346	MALEGAON TO RISOD - [N24001089]	2/2018	303.24 303.00	303.24	50.07	12/2019 -	12/2019
347	JALGAON TO NANDURA - [N24001088]	3/2018	177.84 177.00	177.84	35.69	12/2019 -	12/2019
348	BODHWAD TO STATE BORDER - [N24001086]	1/2017	178.26 -	178.26	81.95	07/2019 -	07/2019
349	MANGRUPHIR TO MAHAN - [N24001087]	3/2018	222.13 222.00	222.13	14.36	11/2019 -	11/2019
350	PAHUR TO BODHWAD - [N24001084]	1/2017	244.93 -	244.93	29.23	05/2020 -	05/2020
351	CHIKLI TO TAKARKHED - [N24001083]	3/2018	393.10 393.00	393.10	83.97	12/2019 -	12/2019
352	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
353	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]	3/2018	294.87 295.00	294.87	31.30	12/2019 -	12/2019
354	JALKOT TO TOGRI - [N24001071]	7/2018	299.92 300.00	299.92	-	08/2020 -	08/2020
355	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	58.15	12/2019 -	12/2019
356	NANDED TO JALKOT - [N24001069]	12/2017	456.93 457.00	456.93	37.50	09/2019 -	09/2019
357	WASHIM TO DASTAPUR - [N24001068]	3/2018	165.51 -	165.51	25.45	12/2019 -	12/2019
358	OMREGA TO AUSA - [N24001067]	3/2018	272.04 272.00	272.04	72.24	12/2019 -	12/2019
359	LATUR TO PANGAON - [N24001066]	3/2018	336.47 336.00	336.47	60.48	12/2019 -	12/2019
360	PARBHANI TO GANGKHED - [N24001065]	3/2018	238.19 238.00	238.19	9.85	12/2019 -	12/2019
361	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	3/2018	217.14 217.00	217.14	52.77	02/2020 -	02/2020
362	WADIGODRI TO DHANGRIPIMPRI - [N24001063]	3/2018	194.23 194.00	194.23	48.23	02/2020 -	02/2020
363	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	3/2018	336.21 336.00	336.21	58.66	12/2019 -	12/2019
364	CHIKALI TO DHAD - [N24001061]	3/2018	189.46 189.00	189.46	21.00	12/2019 -	12/2019
365	PALPHATA TO PHULAMBARI - [N24001060]	3/2018	227.19 227.00	227.19	37.23	12/2019 -	12/2019
366	SHIVUR TO YEOLA - [N24001059]	3/2018	181.08 -	181.08	7.45	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
367	KARWANDI TO RAJURI - [N24001058]	3/2018	276.95 277.00	276.95	44.47	12/2019 -	12/2019
368	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI [N24001056]	2/2017	422.02 422.00	422.02	224.01	07/2019 -	07/2019
369	HELWAK TO KARAD - [N24001055]	2/2017	416.99 -	416.99	100.40	07/2019 -	07/2019
370	TASGAON TO SHIRDHON - [N24001054]	1/2017	195.64 196.00	195.64	83.73	11/2019 -	11/2019
371	SANGOLA TO JATH - [N24001052]	1/2018	257.38 257.00	257.38	28.15	12/2019 -	12/2019
372	NALDURG TO AKKALKOT - [N24001051]	2/2018	274.50 275.00	274.50	56.39	12/2019 -	12/2019
373	VITA TO NAGAJ - [N24001050]	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019
374	KARAD TO VITA - [N24001049]	1/2018	344.85 245.00	344.85	39.04	12/2019 -	12/2019
375	MEHKAR TO AJISPUR - [N24001048]	1/2017	232.77 -	232.77	83.51	07/2019 -	07/2019
376	BHADGAON TO CHALISGAON - [N24001047]	1/2018	259.55 260.00	259.55	120.00	11/2019 -	11/2019
377	RALEGAON TO RAMTIRTH - [N24001046]	1/2017	210.81 -	210.81	100.69	07/2019 -	07/2019
378	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
379	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
380	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
381	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
382	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
383	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
384	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
385	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]	4/2017	518.53 -	518.53	-	09/2019 -	09/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
386	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]	3/2018	253.44 -	253.44	-	07/2019 -	07/2019
387	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
388	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
389	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
390	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
<u>National Highways Authority Of India</u>							
391	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]	1/2016	1,081.57 -	1,081.57	988.72	06/2019 -	06/2019
392	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	762.75	07/2019 -	07/2019
393	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	1,213.89	09/2019 -	09/2019
394	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
395	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
396	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	1,597.26	03/2020 -	03/2020
397	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
398	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	54.70	03/2020 -	03/2020
399	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	525.24	04/2020 -	04/2020
400	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	571.35	07/2019 -	07/2019
<u>National Highways Development Project</u>							
401	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	207.68	01/2020 -	01/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
402	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 [N24000478]	12/2015	957.54 -	957.54	412.39	02/2020 -	02/2020
	<u>Public Works Dept Of State</u>						
403	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274	7/2015	333.21 333.21	333.21	256.11	12/2015 06/2019	06/2019
404	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301	3/2015	271.45 -	271.45	143.16	10/2015 09/2019	09/2019
405	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910	3/2018	170.57 -	170.57	8.14	11/2020 -	11/2020
406	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
407	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020
408	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
409	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
410	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896	1/2017	373.82 -	373.82	116.33	09/2019 -	09/2019
411	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	4/2014	279.70 398.22	398.52	314.34	08/2017 07/2019	07/2019
412	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884	3/2018	191.21 -	191.21	68.26	11/2019 -	11/2019
413	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	19.76	10/2020 -	10/2020
414	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999	11/2016	230.34 -	230.34	167.64	10/2019 -	10/2019
415	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997	3/2018	192.67 -	192.67	-	07/2019 -	07/2019
416	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996	1/2017	605.08 -	605.08	213.00	10/2019 -	10/2019
417	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	46.62	07/2020 -	07/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
418	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	.34	09/2020 -	09/2020
419	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	134.38	04/2020 -	04/2020
420	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	7.40	11/2019 -	11/2019
421	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	23.54	11/2019 -	11/2019
422	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	94.93	06/2020 -	06/2020
423	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	80.71	12/2019 -	12/2019
424	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	32.04	05/2020 -	05/2020
425	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	121.47	12/2019 -	12/2019
426	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983	1/2017	196.52 -	196.52	92.88	10/2019 -	10/2019
427	REHABILITATION AND UPGRADATION OF HARPALPUR-SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942	3/2016	208.50 -	208.50	102.98	11/2019 -	11/2019
428	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
429	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
430	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158	3/2018	159.97 -	159.97	-	06/2019 -	06/2019
431	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	.50	09/2021 -	09/2021
432	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	376.71	01/2020 -	01/2020
433	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	171.00	01/2020 -	01/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
434	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00	215.16	125.09	09/2019 -	09/2019
435	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]	10/2016	218.94 219.00	218.94	67.87	03/2020 -	03/2020
436	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]	3/2018	212.99 -	212.99	59.56	06/2020 -	06/2020
437	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]	2/2018	218.70 -	218.70	17.84	11/2020 -	11/2020
438	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]	2/2018	426.18 -	426.18	217.48	09/2020 -	09/2020
439	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]	3/2017	202.69 -	202.69	75.72	11/2019 -	11/2019
440	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	3/2016	271.17 291.20	291.20	79.24	11/2018 11/2019	11/2019
441	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]	8/2014	823.20 937.76	937.76	703.65	11/2017 06/2019	06/2019
442	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 -	353.89	256.11	11/2015 06/2019	06/2019
443	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]	7/2015	333.21 -	333.21	256.11	12/2015 06/2019	06/2019
	Total		70,426.90 -	71,365.24	24,024.25		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
444	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	21.00	05/2021 -	05/2021
445	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	109.97	05/2020 -	05/2020
	<u>Inland Waterways Authority Of India</u>						
446	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	4,200.00	1,256.55	03/2023 -	03/2023
	Total		6,969.00 -	6,969.00	1,387.52		
	<u>STEEL</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Mineral Development Corporation (Nmdc)</u>						
447	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	15,729.80	05/2015 07/2020	07/2020
448	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020
	<u>Rastriya Ispat Nigam Limited</u>						
449	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	254.29	10/2016 03/2021	03/2021
450	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,500.00	1,277.76	12/2017 09/2019	09/2019
451	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]	7/2015	465.85 -	465.85	390.25	07/2018 07/2019	07/2019
452	CENTRAL DISPATCH YARD - [N12000119]	8/2015	320.66 -	320.66	199.91	08/2018 07/2019	07/2019
453	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	1,144.53	09/2018 09/2019	09/2019
	<u>Steel Authority Of India Limited (Sail)</u>						
454	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	431.23	10/2017 06/2020	06/2020
455	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	99.65	06/2019 06/2020	06/2020
456	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	922.73	12/2017 06/2019	06/2019
457	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	.60	09/2020 -	09/2020
	Total		24,727.78 -	32,130.18	20,482.35		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
458	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	219.60	33.46	05/2018 07/2019	07/2019
459	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	240.10	117.63	10/2018 09/2019	09/2019
	Total		447.10 -	459.70	151.09		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
460	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	41.33	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(June 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
461	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	314.01	07/2019 12/2019	12/2019
462	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	1/2019	790.79 -	800.00	-	06/2021 -	06/2021
463	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	146.45	06/2019 -	06/2019
464	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
465	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]	1/2018	223.37 -	223.37	27.31	07/2020 09/2020	09/2020
466	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	28.71	11/2019 -	11/2019
467	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
468	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	2,568.80	11/2021 12/2021	12/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
469	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	33.82	02/2023 -	02/2023
470	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	32.89	02/2023 -	02/2023
	<u>National Building Construcion Corporation Ltd</u>						
471	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	Total		32,710.14 -	32,904.74	6,474.43		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
472	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Total		233.57 -	233.57	32.20		
	Grand Total		7,95,842.13	9,06,510.48	3,26,401.16		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
	Total		14,951.00 -	23,420.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
7	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	09/2017	11.42
8	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	09/2017	5.85
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	-	114.60
	<u>South-Eastern Coal Fields Limited</u>						
10	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						
11	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
12	BHANEAGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
13	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		19,818.83 -	20,957.14			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
14	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	08/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
15	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
16	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45
17	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
18	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33
	<u>Gas Authority Of India Limited</u>						
19	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
21	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
22	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
24	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
25	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
27	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
28	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
29	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
30	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71
	<u>Oil India Limited</u>						
31	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
32	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
33	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	02/2020	25.55
	Total		22,400.65 -	26,553.69			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
34	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
35	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
36	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
37	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	06/2020	9.64
38	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
39	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
40	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75
41	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2018 -	06/2020	24.87
42	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55
43	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
44	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
45	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
<u>Power Grid Corporation Of India Limited</u>							
46	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
47	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
48	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	08/2019	38.61
49	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
50	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	06/2019	14.60
51	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	07/2019	26.82
52	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	08/2019	27.92
53	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17
54	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
55	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
<u>Satluj Jal Vidyut Nigam Limited</u>							
56	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	07/2019	37.96
57	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) [N18000235]	11/2016	330.00 -	332.00	11/2017 -	04/2019	.61
<u>Thdc India Limited</u>							
58	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
59	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
60	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,26,683.39 -	1,75,569.28			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
61	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71
62	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44
63	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
64	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04
65	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2022	.01
66	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
67	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
68	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
69	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	- -	03/2023	290.95
70	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	163.78
71	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
72	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
73	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
74	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88	- -	03/2023	278.13
75	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	03/2024	323.32
76	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	03/2024	542.46
77	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	03/2024	32.26

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	-	03/2024	818.15
79	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	-	03/2021	124.59
80	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	-	03/2022	590.61
81	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	-	03/2024	338.91
82	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	03/2024	252.66
83	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2022	43.41
84	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	400.17	-	01/2020	87.86
85	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
86	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
87	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
88	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	727.29	-	09/2019	302.22
89	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	-	12/2021	350.27
	<u>East Coast Railway</u>						
90	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
91	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	12/2023	29.96
92	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
93	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07
94	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
95	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
96	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
97	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,670.01	03/2019 12/2009	03/2025	40.47
98	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,026.30	02/2013 -	03/2024	69.05

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
99	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	1,106.62 -	1,536.44	12/2010 -	03/2020	38.84
100	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]	04/2010	277.28 -	328.75	03/2016 -	03/2025	18.56
101	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46
102	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2020	27.96
103	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	226.22	- -	-	28.68
104	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
105	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	506.42	03/2005 -	03/2025	2.40
106	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	319.75	- -	03/2025	7.49
107	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA AND CHA - [N22000242]	04/2003	337.96 -	381.75	- -	03/2025	12.96
108	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	726.95	02/2012 -	03/2025	45.40
109	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	04/2009	257.42 -	258.73	03/2014 -	03/2025	.51
110	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	03/2024	3.31
111	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	09/2021	6.48
112	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	575.65	03/2006 -	03/2025	41.44
113	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30
114	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19
115	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
116	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	364.98	- -	03/2020	26.58
117	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	444.81	- -	05/2019	70.18
118	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]	04/2000	157.17 -	160.00	- -	-	1.80

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	1,218.71	03/2016 -	03/2025	31.96
120	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227	04/2010	174.56 -	175.99	-	03/2025	.82
	<u>Indian Railway Construction Company Limited</u>						
121	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
	<u>Metropolitan Rapid Transport Projects</u>						
122	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
123	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,973.73	03/2004 -	03/2021	500.22
124	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	-	48.06
125	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
126	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	346.00	12/2008 -	03/2015	188.33
127	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>						
128	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
129	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80
130	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	3,500.00	12/2008 -	-	196.56
131	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
132	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
133	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
134	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
135	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	-	03/2022	7.86
136	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
137	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	-	03/2022	71.62
138	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11
139	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
140	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
141	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2021	63.25
142	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
143	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
144	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	700.00	03/2019 -	-	122.93
145	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
146	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
	<u>North Eastern Railway</u>						
147	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
148	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08	12/2022 -	12/2022	234.77
149	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
150	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
151	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
152	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
153	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
154	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16
155	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
156	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
157	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	12/2021	116.16

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
158	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
159	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	- -	-	26.25
160	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
161	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15	- -	-	95.85
162	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47
163	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
164	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
165	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35
166	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	12/2019	69.36
	<u>Northern Railway</u>						
167	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	03/2024	25.87
168	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]	04/2013	654.00 -	700.00	- -	03/2025	7.03
169	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
170	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00	- -	03/2022	137.45
171	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	06/2020	57.68
172	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
173	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67
174	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
	<u>Rail Vikas Nigam Ltd.</u>						
175	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
176	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	85.99
177	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
178	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
181	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
182	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
183	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
184	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
185	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00	03/2020 -	03/2020	173.31
186	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
187	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2020	58.22
188	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						
189	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
190	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
191	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
192	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
193	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
194	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
195	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
196	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	2,542.75	03/2000 -	03/2021	2,54,175.00
197	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
	<u>South East Central Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
198	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94
199	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95
	<u>South Eastern Railway</u>						
200	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	- -	03/2030	53.96
201	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2025	564.94
202	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	11/2019	153.41
203	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
204	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99
205	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
206	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
207	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
208	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
209	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
210	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09
211	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
212	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
213	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
214	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
215	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
216	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98
217	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
218	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	-	-	294.63
219	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
220	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
221	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	- -	-	339.33
222	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
223	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
224	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
225	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
226	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
227	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
228	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	-	253.33
229	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
230	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
	<u>Western Railway</u>						
231	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18
232	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	202.35	03/2011 -	03/2017	2.74
233	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
234	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,39,348.20 -	2,70,176.49			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
235	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	-	3.72
	<u>Ministry Of Road Transport And Highways</u>						
236	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	- -	-	9.23
237	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
238	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642	03/2015	226.31 226.00	226.31	10/2017 -	-	.14
239	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00	157.30	06/2018 -	-	.19
240	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
241	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
242	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00	297.12	07/2018 -	01/2020	1.06
243	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	05/2020	.04
244	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	-	.01
245	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	12/2019	.10
246	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	12/2019	.03
247	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.15
248	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	10/2019	.01
249	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	06/2020	.02
250	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	12/2019	.05
251	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	12/2019	40.76
252	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	12/2019	.15
253	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	07/2019	.00

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
254	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00	407.19	06/2019 -	06/2020	.05
255	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00	227.19	12/2019 -	12/2019	.08
256	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00	189.46	12/2019 -	12/2019	.24
257	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00	336.21	12/2019 -	12/2019	.06
258	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00	194.23	02/2020 -	02/2020	.12
259	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00	217.14	02/2020 -	02/2020	.06
260	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00	238.19	12/2019 -	12/2019	.08
261	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00	336.47	12/2019 -	12/2019	.14
262	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00	272.04	12/2019 -	12/2019	.01
263	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00	301.38	08/2020 -	08/2020	.13
264	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00	344.25	08/2020 -	08/2020	.07
265	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00	225.25	12/2019 -	12/2019	.11
266	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	06/2020 -	06/2020	.01
267	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00	177.84	12/2019 -	12/2019	.47
268	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00	303.24	12/2019 -	12/2019	.08
269	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00	536.65	12/2019 -	12/2019	50.74
270	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00	244.04	03/2019 -	12/2019	.02
271	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00	264.41	03/2019 -	12/2019	.16
272	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00	381.08	05/2020 -	05/2020	26.19
273	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	07/2019 -	07/2019	.31
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
274	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]	02/2017	168.32 -	202.05	04/2017 -	02/2021	20.04

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
275	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683	02/2017	180.57 -	215.70	04/2017 -	02/2021	19.46
276	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684	02/2017	216.71 -	262.62	04/2017 -	02/2021	21.19
277	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685	02/2017	167.28 -	209.71	04/2017 -	02/2021	25.36
	<u>National Highways Authority Of India</u>						
278	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	07/2019	92.75
279	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
280	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
281	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
282	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2020	106.50
283	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58
284	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	12/2019	21.90
285	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
286	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
287	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609	09/2015	771.18 -	7,558.00	-	-	880.06
288	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
289	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
290	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
291	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
292	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
293	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
294	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
295	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
296	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
297	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	-	4.02
298	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
299	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
300	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
301	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
National Highways Development Project							
302	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	08/2019	46.51
303	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
Public Works Dept Of State							
304	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
305	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
306	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	05/2012 -	-	88.11
307	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
308	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2019	.12
309	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75
310	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
311	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
312	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00	215.16	09/2019 -	09/2019	.07
313	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00	240.30	01/2020 -	01/2020	.13
	Total		38,922.86 -	53,266.07			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
314	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	6.97
	<u>Mumbai Port Trust</u>						
315	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	-	82.72
	<u>Port Trust</u>						
316	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
317	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
318	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
319	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	09/2019	25.85

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(June 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
320	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2021	30.58
321	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	06/2014	157.84 -	169.16	03/2017 -	-	7.17
322	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.60
323	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126	01/2019	790.79 -	800.00	06/2021 -	06/2021	1.16
	<u>Chennai Metro Rail Ltd</u>						
324	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
325	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
326	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Kochi Metro Rail Corporation Ltd</u>						
327	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
328	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		28,016.42 -	34,022.73			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
329	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		4,31,500.93	7,10,708.02			

List of Delayed Projects w.r.t. Latest Schedule

Annexure - XIV

Costing Rs. 150 Crore and above (June 2019)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,784.74	09/2010 -	10/2021	133	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	13,711.00	12/2015 -	06/2020	54	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	10,993.00	12/2016 -	12/2020	48	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	14,422.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	44,910.74				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	85.79				
	<u>COAL</u>								
	<u>Central Coal Fields Limited</u>								
6	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	163.23	03/2012 -	07/2019	88	-
7	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120	-
8	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	179.87	03/2012 -	03/2021	108	-
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	359.23	03/2016 -	03/2021	60	-
10	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.82	03/2014 -	03/2021	84	-
11	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	336.64	07/2012 -	03/2022	116	-
	<u>Eastern Coal Fields Limited</u>								
12	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	460.96	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	-
14	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	493.85	03/2017 -	03/2020	36	-
15	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	75.79	03/2018 -	03/2020	24	-
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	241.15	03/2012 -	03/2021	108	-
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	390.53	03/2013 -	03/2021	96	-
19	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022	108	-
20	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	346.99	03/2010 -	03/2022	144	-
21	BASUNDHARA (WEST) OC EXTN (7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	196.26	03/2019 -	03/2022	36	-
	<u>Neyveli Lignite Corporation</u>								
22	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	709.06	439.27	06/2015 -	09/2019	51	-
23	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,451.65	12/2015 -	12/2019	48	-
	<u>Singareni Colliers Company Limited</u>								
24	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	-
25	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	7.01	03/2015 -	03/2021	72	-
26	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	53.00	03/2019 -	03/2022	36	-
27	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	115.71	03/2015 -	07/2019	52	-
28	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	331.25	03/2012 -	03/2023	132	-
29	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	232.81	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
30	JAGANNATHPOR OCP (3.00 MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	459.49	203.90	03/2015 -	03/2020	60	-
31	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
32	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	172.88	03/2016 -	03/2020	48	-
33	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	207.04	03/2014 -	03/2021	84	-
	<u>Western Coal Fields Limited</u>								
34	ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA	08/2015	288.90 -	333.43	17.71	03/2023 -	03/2024	12	-
35	KAMPTEE DEEP OC MINE - [N06000141]WCL, MAHARASHTRA	11/2015	277.65 -	313.34	115.28	03/2021 -	03/2024	36	-
	Total		17,014.82 -	18,205.04	12,820.65				
	<u>FERTILISERS</u>								
	<u>Rashtriya Chemical & Fertiliser Limited</u>								

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	209.44	159.41	11/2016 -	08/2019	33	-
	Total		197.79 -	209.44	159.41				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
37	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	694.00	671.48	10/2018 -	11/2019	13	-
38	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	5,245.96	3,283.70	08/2018 -	11/2019	15	-
39	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	1,112.00	467.00	06/2019 -	06/2020	12	-
40	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	3,288.96	816.62	02/2020 -	10/2020	8	-
41	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	-
	<u>Gas Authority Of India Limited</u>								
42	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	03/2015	3,957.00 -	3,397.00	2,707.26	12/2018 -	06/2019	6	-
43	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	135.09	04/2018 -	08/2019	16	-
44	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,291.18	12/2012 -	02/2022	110	-
	<u>Indian Oil Corporation Limited</u>								
45	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	2,740.12	09/2017 -	07/2019	22	-
46	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	07/2019	8	-
47	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	244.44	08/2019 -	09/2019	1	-
48	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	300.23	01/2019 -	12/2019	11	-
49	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	21.97	06/2020 -	08/2020	2	-
50	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	256.76	07/2018 -	10/2020	27	-
51	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	38.51	02/2020 -	10/2020	8	-
52	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	75.19	02/2020 -	10/2020	8	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
53	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	444.28	12/2018 -	02/2021	26	-
54	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	163.02	44.00	04/2020 -	03/2021	11	-
55	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	28.55	01/2021 -	04/2021	3	-
56	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	74.36	04/2021 -	07/2021	3	-
57	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	25.99	10/2020 -	08/2021	10	-
58	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	20.85	01/2021 -	10/2021	9	-
59	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	37.30	08/2021 -	11/2021	3	-
60	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	13.97	04/2022 -	02/2023	10	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
61	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 170.70	170.70	152.13	03/2019 -	08/2019	5	-
62	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	66.19	03/2020 04/2020	09/2020	6	5
	<u>Oil & Natural Gas Corporation Limited</u>								
63	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	345.92	139.45	01/2014 -	11/2019	70	-
64	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	367.94	03/2019 -	05/2020	14	-
65	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	2,670.11	06/2020 -	08/2021	14	-
	<u>Oil India Limited</u>								
66	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
67	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	224.72	03/2017 -	12/2019	33	-
	Total		67,252.10 -	69,165.38	19,189.04				
	<u>POWER</u>								

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Chenab Valley Power Projects [P] Limited</u>								
68	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,135.82	04/2020 -	12/2023	44	-
	<u>National Hydro-Electric Power Corporation</u>								
69	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,399.82	09/2009 -	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
70	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	13,589.31	05/2018 06/2019	07/2019	14	1
71	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	9,996.59	7,816.71	07/2012 -	09/2020	98	-
72	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	8,852.51	06/2019 09/2019	09/2021	27	24
	<u>Power Grid Corporation Of India Limited</u>								
73	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	225.28	162.30	02/2016 04/2019	06/2019	40	2
74	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	340.88	251.33	03/2018 03/2019	07/2019	16	4
75	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	1,429.38	1,011.38	01/2019 -	07/2019	6	-
76	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	562.25	392.96	03/2019 03/2019	07/2019	4	4
77	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	407.79	04/2019 04/2019	07/2019	3	3
78	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	84.17	06/2019 -	07/2019	1	-
79	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,308.50	04/2019 -	07/2019	3	-
80	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,237.45	11/2008 06/2019	08/2019	129	2
81	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	190.80	07/2017 06/2019	08/2019	25	2
82	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	81.97	03/2018 03/2018	08/2019	17	17
83	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	430.71	04/2019 04/2019	08/2019	4	4
84	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	153.70	02/2019 06/2019	08/2019	6	2

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
85	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,431.00	05/2019 -	09/2019	4	-
86	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	103.12	07/2019 -	09/2019	2	-
87	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	72.38	06/2019 -	09/2019	3	-
88	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	117.15	06/2019 06/2019	10/2019	4	4
89	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	210.72	04/2016 03/2017	12/2019	44	33
90	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	405.65	05/2017 06/2019	12/2019	31	6
91	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,211.92	12/2018 -	12/2019	12	-
92	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	272.00	02/2019 -	12/2019	10	-
93	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	-
94	EASTERN REGION STRENGTHENING SCHEME- XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	465.21	11/2016 12/2019	03/2020	40	3
95	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	513.85	01/2018 12/2019	03/2020	26	3
96	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,367.68	12/2018 12/2018	12/2020	24	24
	<u>Satluj Jal Vidyut Nigam Limited</u>								
97	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	561.74	12/2016 -	07/2019	31	-
	<u>Thdc India Limited</u>								
98	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	292.85	02/2014 -	10/2019	68	-
99	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	2,935.92	02/2016 -	06/2022	76	-
100	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,697.38	06/2013 -	12/2022	114	-
	Total		77,645.11 -	1,05,718.20	60,249.11				
	<u>HEAVY INDUSTRY</u>								
	<u>Natirp Implementation Society</u>								

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
101	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	3,727.30	3,182.10	09/2011 06/2019	03/2020	102	9
	Total		1,718.00 -	3,727.30	3,182.10				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>HII Infra Tech Services Limited</u>								
102	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2	-
103	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2	-
104	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5	-
	<u>Hospital Services Consultancy Corporation</u>								
105	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
106	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	244.00	241.39	09/2018 -	06/2019	9	-
107	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	290.71	05/2017 -	08/2019	27	-
108	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	-
109	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	-
110	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	-
111	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	-
112	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	-
113	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	-
	Total		4,937.67 -	5,037.45	2,079.73				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
114	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,211.41	03/2021 -	03/2022	12	-
115	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	792.89	294.10	03/2021 -	03/2022	12	-
116	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	256.28	03/2022 -	03/2023	12	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
117	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	215.95	03/2022 -	03/2024	24	-
118	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	65.16	03/2022 -	03/2024	24	-
119	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	48.42	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
120	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	259.90	03/2019 -	12/2019	9	-
121	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	-
122	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	149.66	03/2019 -	02/2020	11	-
123	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	436.07	03/2018 -	03/2020	24	-
124	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	300.00	285.74	03/2019 -	03/2020	12	-
125	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	5.59	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
126	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	72.25	03/2019 -	12/2019	9	-
127	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,156.41	1,028.71	03/2012 -	03/2020	96	-
128	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	672.82	03/2012 -	03/2020	96	-
129	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	446.51	03/2019 -	02/2021	23	-
130	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	426.16	03/2020 -	03/2021	12	-
131	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	390.91	03/2020 -	10/2021	19	-
132	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	785.87	457.46	03/2020 -	03/2022	24	-
133	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	35.10	03/2021 -	03/2022	12	-
134	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	15.39	03/2021 -	03/2022	12	-
135	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	424.98	03/2020 -	12/2022	33	-
	<u>East Coast Railway</u>								
136	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	116.91	11/2018 -	03/2021	28	-
137	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	879.96	02/2019 -	03/2022	37	-
138	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	349.23	12/2018 -	03/2022	39	-
139	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	624.68	06/2021 -	03/2023	21	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
140	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	125.30	10/2020 -	03/2023	29	-
141	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	654.74	03/2020 -	03/2023	36	-
142	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	320.30	03/2022 -	03/2023	12	-
143	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,354.80	03/2009 -	12/2023	177	-
144	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	148.96	03/2022 -	03/2025	36	-
	<u>Eastern Railways</u>								
145	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,536.44	815.11	12/2010 12/2017	03/2020	111	27
146	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.47	11/2018 -	03/2021	28	-
147	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,026.30	637.72	02/2013 -	03/2024	133	-
148	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,670.01	847.87	03/2019 12/2009	03/2025	72	183
149	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	575.65	148.40	03/2006 -	03/2025	228	-
150	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	307.25	03/2022 -	03/2025	36	-
151	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	1,218.71	431.90	03/2016 -	03/2025	108	-
152	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	328.75	165.55	03/2016 -	03/2025	108	-
153	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	182.35	03/2017 -	03/2025	96	-
154	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	506.42	32.00	03/2005 -	03/2025	240	-
155	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	726.95	150.36	02/2012 -	03/2025	157	-
156	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	258.73	103.91	03/2014 -	03/2025	132	-
157	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Metropolitan Rapid Transport Projects</u>								

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
158	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,973.73	1,394.89	03/2004 -	03/2021	204	-
159	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
	<u>North Central Railway</u>								
160	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
161	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	271.06	03/2019 -	03/2020	12	-
162	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	13,809.00	8,818.98	03/2011 -	03/2020	108	-
163	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,532.00	606.19	03/2019 -	03/2020	12	-
164	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	932.80	03/2019 -	03/2020	12	-
165	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	3,000.00	756.82	03/2015 -	10/2021	79	-
166	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 569.63	650.00	45.24	03/2020 03/2020	12/2021	21	21
	<u>North Eastern Railway</u>								
167	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	256.42	01/2019 -	01/2020	12	-
168	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	116.58	04/2017 -	01/2020	33	-
169	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	4.89	04/2016 -	02/2020	46	-
170	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	3.12	12/2019 -	04/2021	16	-
171	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
172	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
173	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	138.99	10/2018 -	10/2019	12	-
174	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	341.67	02/2019 -	12/2019	10	-
175	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	244.02	245.81	11/2019 -	05/2020	6	-
176	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	199.54	12/2019 -	06/2020	6	-
177	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	142.63	03/2020 -	06/2020	3	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
178	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	510.24	02/2019 -	12/2021	34	-
179	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	38.93	03/2020 -	04/2022	25	-
180	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	33.39	08/2022 -	09/2022	1	-
	<u>Northern Railway</u>								
181	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	189.71	12/2011 -	03/2021	111	-
182	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 876.00	876.00	848.84	03/2016 -	03/2021	60	-
183	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	18,512.58	11/2002 -	12/2021	229	-
184	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,010.00	644.09	07/2012 -	03/2024	140	-
	<u>Rail Vikas Nigam Ltd.</u>								
185	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	381.48	03/2009 03/2009	12/2019	129	129
186	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,709.83	12/2017 -	03/2020	27	-
187	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,100.58	03/2019 -	03/2020	12	-
188	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	668.38	03/2016 -	12/2020	57	-
189	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	977.00	03/2019 -	03/2021	24	-
190	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	982.53	12/2020 -	03/2021	3	-
191	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	833.73	02/2015 -	12/2021	82	-
192	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,235.96	03/2020 -	03/2022	24	-
193	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	285.50	03/2022 -	12/2024	33	-
194	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	455.60	03/2023 -	12/2024	21	-
195	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,110.08	03/2016 -	03/2025	108	-
196	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.50	842.61	03/2016 -	03/2025	108	-
197	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	2,106.28	03/2014 -	12/2025	141	-
198	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,458.67	12/2024 -	03/2026	15	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>South Central Railway</u>								
199	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	2,542.75	1,413.56	03/2000 -	03/2021	252	-
200	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	-
201	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	-
202	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	-
203	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	-
204	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	-
205	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	-
206	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	-
	<u>South East Central Railway</u>								
207	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	626.21	02/2019 03/2020	06/2020	16	3
	<u>South Eastern Railway</u>								
208	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	494.27	03/2020 -	06/2020	3	-
209	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	332.04	03/2021 -	12/2021	9	-
210	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	939.00	184.33	12/2021 -	12/2024	36	-
211	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	03/2025	216	216
212	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
213	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
214	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	-
215	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-
216	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	-
217	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	-
218	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	-
219	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
220	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
221	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	-
	<u>Southern Railway</u>								
222	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	-
223	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	-
224	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	-
225	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	-
226	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	-
227	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	Total		1,35,345.27 -	2,06,327.47	85,192.68				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
228	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	-
229	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	326.63	249.26	04/2018 -	06/2019	14	-
230	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	301.70	01/2017 -	06/2019	29	-
231	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH	01/2016	386.09 -	386.09	153.98	05/2016 -	06/2019	37	-
232	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	208.09	09/2016 -	06/2019	33	-
233	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA	02/2017	322.48 322.00	322.48	169.08	05/2019 -	06/2019	1	-
234	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH	10/2015	333.21 -	333.21	-	12/2015 -	06/2019	42	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
235	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	621.43	387.00	06/2018 -	07/2019	13	-
236	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 - [N24000971]MORTH,ANDHRA PRADESH	08/2016	574.19 -	574.19	-	07/2017 -	07/2019	24	-
237	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.00	454.41	03/2017 -	07/2019	28	-
238	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	97.23	08/2017 -	08/2019	24	-
239	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	169.76	08/2017 -	08/2019	24	-
240	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA	01/2017	463.62 664.00	463.62	230.34	06/2019 -	08/2019	2	-
241	AMD I TO SAONER - [N24001021]MORTH,MAHARASHTRA	01/2017	396.91 396.91	396.91	281.48	06/2019 -	08/2019	2	-
242	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	86.63	08/2015 -	09/2019	49	-
243	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	43.79	09/2017 -	09/2019	24	-
244	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	229.00	06/2019 -	10/2019	4	-
245	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	-
246	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	179.81	11/2017 -	11/2019	24	-
247	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	29.83	06/2019 -	11/2019	5	-
248	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	78.81	11/2018 -	11/2019	12	-
249	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	-
250	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	-
251	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	86.79	05/2019 -	12/2019	7	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
252	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	110.43	05/2019 -	12/2019	7	-
253	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	171.75	06/2019 -	12/2019	6	-
254	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	159.29	06/2019 -	12/2019	6	-
255	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	125.81	06/2019 -	12/2019	6	-
256	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA	01/2017	355.17 355.17	355.17	141.87	07/2019 -	12/2019	5	-
257	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	35.26	06/2019 -	12/2019	6	-
258	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	14.94	03/2019 -	12/2019	9	-
259	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	23.71	03/2019 -	12/2019	9	-
260	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	-
261	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-
262	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH	11/2016	378.24 -	378.24	-	01/2018 -	01/2020	24	-
263	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MORTH,ANDHRA PRADESH	03/2018	297.12 294.00	297.12	119.08	07/2018 -	01/2020	18	-
264	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	177.36	01/2018 -	01/2020	24	-
265	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	60.76	08/2018 -	02/2020	18	-
266	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	100.00	08/2018 -	02/2020	18	-
267	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	130.85	02/2019 -	02/2020	12	-
268	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	20.13	08/2018 -	03/2020	19	-
269	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	652.90	12/2019 -	03/2020	3	-
270	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	746.91	11/2019 -	03/2020	4	-
271	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	-	04/2019 -	04/2020	12	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
272	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	136.30	11/2018 -	05/2020	18	-
273	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	23.03	05/2019 -	05/2020	12	-
274	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	126.78	05/2019 -	05/2020	12	-
275	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	100.00	06/2019 -	06/2020	12	-
276	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	68.97	06/2019 -	06/2020	12	-
277	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	12.00	06/2019 -	06/2020	12	-
278	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	145.91	06/2019 -	06/2020	12	-
279	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	26.42	06/2019 -	06/2020	12	-
280	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	184.31	07/2019 -	07/2020	12	-
281	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH	03/2018	244.95 245.00	244.95	75.36	08/2018 -	08/2020	24	-
282	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12	-
283	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	30.00	09/2018 -	04/2021	31	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
284	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	37.86	05/2019 -	07/2019	2	-
285	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	194.11	174.80	05/2018 -	08/2019	15	-
286	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	187.25	08/2016 -	08/2019	36	-
287	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	229.11	08/2016 -	08/2019	36	-
288	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	153.61	08/2016 -	08/2019	36	-
289	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	198.00	195.67	10/2016 -	10/2019	36	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
290	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	94.49	01/2017 -	01/2020	36	-
291	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	240.21	06/2018 -	03/2020	21	-
292	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	284.09	80.64	04/2017 -	02/2021	46	-
293	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	202.05	42.83	04/2017 -	02/2021	46	-
294	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	215.70	45.21	04/2017 -	02/2021	46	-
295	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	262.62	31.11	04/2017 -	02/2021	46	-
296	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	209.71	47.37	04/2017 -	02/2021	46	-
297	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	93.52	10/2018 -	10/2021	36	-
298	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	211.21	03/2017 -	03/2022	60	-
<u>National Highways Authority Of India</u>									
299	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	885.31	02/2013 -	06/2019	76	-
300	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	843.67	07/2013 -	06/2019	71	-
301	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64	-
302	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	-
303	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	167.98	223.68	05/2008 -	06/2019	133	-
304	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	5	-
305	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	273.20	256.25	02/2019 -	06/2019	4	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
306	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	319.96	04/2009 -	07/2019	123	-
307	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,346.01	03/2013 -	07/2019	76	-
308	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-
309	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	956.75	11/2017 -	07/2019	20	-
310	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	574.28	448.92	07/2018 -	07/2019	12	-
311	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,497.56	07/2017 -	07/2019	24	-
312	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	691.30	11/2018 -	07/2019	8	-
313	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	712.41	03/2019 -	07/2019	4	-
314	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	217.61	451.15	04/2010 -	08/2019	112	-
315	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	08/2019	20	-
316	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	417.86	06/2016 -	08/2019	38	-
317	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	09/2019	138	-
318	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	475.02	05/2018 -	09/2019	16	-
319	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	-
320	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	-
321	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	502.91	08/2018 -	09/2019	13	-
322	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6	-
323	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	219.09	05/2019 -	09/2019	4	-
324	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	326.35	06/2008 -	10/2019	136	-
325	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
326	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,154.18	12/2018 -	10/2019	10	-
327	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	385.09	05/2018 -	10/2019	17	-
328	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	-
329	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,098.56	08/2018 -	11/2019	15	-
330	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	-
331	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7	-
332	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	241.69	05/2019 -	11/2019	6	-
333	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8	-
334	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	18.02	06/2017 -	11/2019	29	-
335	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	-
336	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	95.96	09/2017 -	11/2019	26	-
337	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	337.08	04/2008 -	12/2019	140	-
338	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	-
339	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	-
340	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	-
341	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	-
342	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	-
343	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	-
344	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	12/2019	39	-
345	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	433.12	09/2017 -	12/2019	27	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
346	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	-
347	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	194.95	12/2017 -	12/2019	24	-
348	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	-
349	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	605.84	722.46	07/2018 -	12/2019	17	-
350	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	804.97	402.47	06/2018 -	01/2020	19	-
351	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	323.72	192.02	08/2018 -	01/2020	17	-
352	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	-
353	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	726.67	357.06	04/2018 -	02/2020	22	-
354	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	-
355	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,978.72	11/2011 -	03/2020	100	-
356	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	750.38	06/2014 -	03/2020	69	-
357	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	707.82	288.38	08/2018 -	03/2020	19	-
358	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	-
359	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 -	756.27	76.83	03/2020 -	04/2020	1	-
360	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	505.00	347.91	05/2018 -	05/2020	24	-
361	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	923.04	708.62	11/2016 -	05/2020	42	-
362	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	641.17	405.31	07/2018 -	05/2020	22	-
363	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	904.16	607.37	02/2020 -	05/2020	3	-
364	4-LANNING OF WARDHA- BUTIBORI SECTION (KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
365	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2	-
366	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	687.88	03/2020 -	05/2020	2	-
367	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	405.31	07/2016 -	05/2020	46	-
368	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	-
369	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	-
370	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	529.62	05/2018 -	06/2020	25	-
371	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	06/2020	25	-
372	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	1,167.42	238.96	03/2019 -	06/2020	15	-
373	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	566.10	03/2020 -	06/2020	3	-
374	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	256.47	09/2017 -	06/2020	33	-
375	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	513.98	03/2020 -	07/2020	4	-
376	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	-
377	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	-
378	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	-
379	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	-
380	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	-
381	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	-	09/2017 -	08/2020	35	-
382	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	-	08/2017 -	09/2020	37	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
383	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	-
384	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	12.95	03/2019 -	11/2020	20	-
385	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	-
386	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	480.96	03/2017 -	11/2020	44	-
387	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	-
388	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	329.90	10/2017 -	11/2020	37	-
389	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	484.48	05/2018 -	12/2020	31	-
390	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	203.78	03/2019 -	12/2020	21	-
391	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	-
392	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	301.68	06/2019 -	12/2020	18	-
393	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	950.69	782.81	08/2019 -	12/2020	16	-
394	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	221.91	03/2020 -	03/2021	12	-
395	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,532.62	-	03/2021 -	04/2021	1	-
396	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-
397	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	-
398	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	-
	<u>National Highways Development Project</u>								

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
399	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	653.29	454.49	03/2017 -	08/2019	29	-
400	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	410.72	-	04/2015 -	08/2019	52	-
401	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	881.05	507.45	05/2017 -	05/2020	36	-
	<u>Public Works Dept Of State</u>								
402	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	342.05	258.91	01/2017 -	06/2019	29	-
403	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	511.00	2,323.04	10/2013 -	06/2019	68	-
404	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - [N24001147]PWD,UTTAR PRADESH	10/2016	239.63 -	239.63	197.77	02/2019 -	06/2019	4	-
405	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	178.23	114.16	09/2018 -	07/2019	10	-
406	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	244.54	122.31	05/2019 -	07/2019	2	-
407	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	07/2019	9	-
408	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	86.63	08/2015 -	07/2019	47	-
409	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	511.00	492.00	10/2013 -	08/2019	70	-
410	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	359.27	200.24	05/2019 -	08/2019	3	-
411	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	291.49	130.00	08/2017 -	08/2019	24	-
412	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	09/2019	24	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
413	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	-
414	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	247.25	139.25	03/2019 -	09/2019	6	-
415	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	73.09	02/2018 -	11/2019	21	-
416	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	47.70	02/2018 -	11/2019	21	-
417	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	15.22	03/2018 -	11/2019	20	-
418	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	93.96	03/2018 -	11/2019	20	-
419	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	115.54	02/2018 -	11/2019	21	-
420	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	-
421	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	356.56	06/2019 -	11/2019	5	-
422	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	196.99	03/2018 -	11/2019	20	-
423	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	789.85	03/2011 -	12/2019	105	-
424	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	-
425	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	151.59	196.76	08/2013 -	12/2019	76	-
426	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	27
427	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	-
428	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	66.95	03/2018 -	12/2019	21	-

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
429	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	62.22	02/2019 -	12/2019	10	-
430	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	79.02	03/2019 -	12/2019	9	-
431	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	83.83	05/2019 -	12/2019	7	-
432	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	-
433	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	100.10	07/2018 -	01/2020	18	-
434	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	219.26	08/2017 -	02/2020	30	-
435	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	173.16	07/2018 -	02/2020	19	-
436	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	298.00	09/2015 -	03/2020	54	-
437	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	50.39	03/2018 -	04/2020	25	-
438	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	-
439	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	296.28	10/2010 -	06/2020	116	-
440	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	14.37	08/2018 -	06/2020	22	-
441	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	62.60	03/2017 -	06/2020	39	-
442	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	4.45	08/2018 -	06/2020	22	-
443	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	7.10	03/2018 -	07/2020	28	-
444	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	-	08/2016 -	12/2020	52	-
445	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
446	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	-
447	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	-
	Total		1,30,380.01 -	1,35,159.56	84,361.96				
	<u>SHIPPING AND PORTS</u>								
	<u>Kamarajar Port Limited</u>								
448	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-
	Total		600.00 -	257.90	1.45				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
449	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Bangalore Metro Rail Corporation Limited</u>								
450	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
451	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 -	205.00	156.21	03/2012 -	06/2019	87	-
452	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL	10/2014	162.88 -	162.88	126.07	04/2018 -	07/2019	15	-
453	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD, ANDHRA PRADESH	01/2018	206.58 -	206.58	82.23	03/2019 -	08/2019	5	-
454	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB	02/2014	388.00 -	488.28	418.79	05/2017 -	09/2019	28	-
455	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38	-
456	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59	-
457	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-

Costing Rs. 150 Crore and above

(June 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	187.10	04/2019 -	12/2019	8	-
459	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	86.04	10/2012 -	03/2020	89	-
460	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	127.69	10/2019 -	03/2020	5	-
461	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	35.77	04/2019 -	06/2020	14	-
462	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	80.06	03/2016 -	09/2020	54	-
463	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	62.56	02/2020 -	09/2020	7	-
464	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	-
465	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	69.60	06/2017 -	10/2020	40	-
466	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	59.36	05/2020 -	12/2020	7	-
467	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	293.53	10/2019 -	03/2021	17	-
468	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	5.96	- 08/2020	03/2021	-	7
469	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 02/2017	05/2021	14	51
	<u>Hindustan Steelwork Construction Limited</u>								
470	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
471	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
472	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	<u>Nagpur Metro Rail Corporation Ltd</u>								
473	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	5,873.51	03/2018 -	12/2019	21	-
	Total		70,110.70 -	71,244.32	14,447.37				

Costing Rs. 150 Crore and above

(June 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
474	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	-
	Total		10,151.04 -	55,548.87	16,417.99				
	Grand Total		5,96,121.12	7,76,054.26	3,51,495.02				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
7	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2020	258.56	48
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	48
9	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
10	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2021	479.53	96
11	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
12	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2022	457.77	108
13	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
14	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
15	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2022	479.15	36
16	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2020	337.66	12
17	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
18	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
19	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2020	302.96	120
20	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2021	510.85	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
22	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2020	426.79	24
23	JAGANNATHPUR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
24	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2022	706.4	116
25	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
26	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2021	163.51	120
27	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	07/2019	179.87	88
28	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2021	264.68	108
29	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2021	162.46	84
30	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
31	KISTARAM OCP	SCCL	11/2010	03/2015	07/2019	242.29	52
32	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
33	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
34	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
35	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2022	172.08	144

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
36	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	08/2019	197.79	33

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
37	CNCI KOLKATA WEST BENGAL	HSCC	08/2016	09/2018	06/2019	244	9
38	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	09/2019	363.99	16
39	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	08/2019	293.65	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
40	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	09/2019	204.44	28
41	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	09/2019	152.95	19
42	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	10/2019	274.19	7
43	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	10/2019	272.19	7
44	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	03/2020	355.15	12
45	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	10/2020	414.11	83

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	03/2020	1718	102

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
48	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2020	906	8
49	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	03/2021	163.02	11
50	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
51	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
52	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	06/2020	1112	12
53	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	7
54	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	12/2019	429	11
55	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
56	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	12/2019	6068.8	8
57	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
58	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	03/2015	12/2018	06/2019	3957	6
59	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	79
61	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	58
62	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	11/2019	694	13
63	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	15
64	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	08/2019	327.78	16
65	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	10/2021	678	56
66	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2020	390.52	14
67	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
68	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	IOCL	07/2015	11/2018	07/2019	822.66	8
69	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2020	4619.94	27
70	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2020	3190.69	25
71	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2020	160.1	8
72	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
73	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	09/2020	581	6
74	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	12/2019	2465.15	81
75	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	12/2019	352.56	33
76	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	07/2019	3150	22
77	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497	26
78	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	07/2020	1810	7
79	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
80	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
81	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	ONGC	04/2017	09/2018	07/2019	420.76	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
82	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	24
83	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	09/2019	408.46	8
84	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
85	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	09/2019	175.64	12
86	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	12/2019	445.89	10
87	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	07/2019	12964.6	14
88	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2018	06/2020	9750.89	28
89	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
90	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	86
91	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	11638.55	26
92	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
93	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	40
94	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2019	374.63	44
95	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	06/2019	196.58	40
96	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	12/2023	8112.12	44
97	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	06/2020	9188.98	11
98	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	06/2020	12532.44	18
99	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	14366.58	27
100	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
101	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP	PGCIL	01/2015	03/2018	07/2019	268.8	16
102	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
103	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	08/2019	203.28	25
104	EASTERN REGION STRENGTHENING SCHEME- XII	PGCIL	05/2014	11/2016	03/2020	522.29	40

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
105	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
106	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	12/2019	5151.37	21
107	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	08/2019	197.4	17
108	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2019	1394.52	31
109	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	10/2019	195.42	68
110	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353	98
111	BUXAR THERMAL POWER PLANT (1320 MW)	SJVN	05/2015	12/2016	07/2019	436.68	31
112	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	114
113	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	08/2019	2496.9	116
114	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657	76
115	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	63
116	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	08/2019	1779.29	129
117	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	118
118	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	11846	29
119	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	06/2021	10598.98	7
120	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2020	808.63	26
121	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	01/2020	454.11	21
122	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	PGCIL	07/2016	01/2019	07/2019	1429.38	6
123	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	08/2019	322.3	6

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
124	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	03/2021	691.84	12
125	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	06/2021	700	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
126	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625	60
127	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
128	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229	15
129	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
130	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
131	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2020	346.32	12
132	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	02/2020	174	11
133	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
134	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
135	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	16
136	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
137	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760	15
138	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	02/2020	213	46
139	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
140	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	03/2026	16216	15
141	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
142	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
143	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	6
144	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
145	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	06/2023	5200	39
146	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
147	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2020	493.17	24
148	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	12/2019	305	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
149	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
150	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
151	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
152	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
153	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
154	RAMGANJMUHDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.6	24
155	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
156	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	129
157	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	21
158	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	12
159	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2020	1106.62	111
160	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	96
161	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
162	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2023	1160.48	156
163	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
164	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
165	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
166	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
167	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28
168	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	12
169	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
170	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
171	MAGRAHAT-DIAMOND HARBOUR WITH MM	ER	04/2009	02/2012	03/2025	499.96	157

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRHAT-KULPI NL						
172	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
173	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	9
174	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
175	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
176	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
177	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287	111
178	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
179	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
180	KADAPA-BANGALORE (NL), KADAPA- PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2132.77	120
181	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
182	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
183	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.5	12
184	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	204
185	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
186	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	96
187	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2023	2923.13	177
188	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	108
189	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
190	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
191	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
192	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2021	5300	84
193	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
194	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	12/2021	410.08	34

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
195	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140
196	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2021	2500	229
197	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
199	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2021	1723	252
200	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	8
201	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	03/2025	393.46	216
202	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
203	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2021	303.98	12
204	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2022	318.24	120
205	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	12
206	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
207	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
208	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2023	843.04	29
209	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
210	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	11/2019	148.77	35
211	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
212	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
213	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
214	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	02/2021	678.54	23
215	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2022	1763.93	24
216	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
217	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
218	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
219	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
220	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
221	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
222	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2025	2361.74	36
223	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	28
224	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	6
225	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
226	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
227	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
228	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	10/2019	236.93	12
229	AJMER-BANGURGRAM	NWR	04/2011	11/2019	05/2020	213.39	6
230	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	12/2019	242.09	10
231	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
232	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC	ECR	04/2009	03/2020	03/2022	548	24
233	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
234	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	63
235	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	12/2021	569.63	21
236	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
237	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2019	120.7	9
238	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
239	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
240	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
241	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
242	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2022	1491.47	33
243	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2022	1172.92	39
244	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2023	2063.03	24
245	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
246	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	36
247	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
248	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
249	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
250	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
251	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
252	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
253	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
254	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2021	1973	9
255	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	12
256	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288	9
257	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2020	3055	27

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
258	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	PWD	02/2017	05/2019	05/2021	157.32	24
259	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	PWD	01/2017	08/2017	08/2019	291.49	24
260	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	PWD	05/2018	05/2018	05/2020	171.6	24
261	CONSTRUCTION OF SILCHAR BYPASS ON NH-	PWD	11/2010	02/2014	12/2019	197.37	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	53 IN ASSAM						
262	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	PWD	11/2017	03/2018	11/2019	392.33	20
263	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	PWD	05/2013	08/2015	07/2019	164.54	47
264	REHABILITATION AND UPGRADE OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	07/2019	445.89	28
265	REHABILITATION AND UPGRADE OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	PWD	10/2016	10/2018	07/2019	176.94	9
266	PARLI PIMPLA DAHIGUDA	MORTH	02/2017	06/2019	06/2020	205.72	12
267	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	MORTH	08/2016	12/2017	12/2019	234.88	24
268	NASHIK TO PETH	MORTH	12/2015	11/2018	11/2019	289.6	12
269	AKKALKOT TO DHUDHNI	MORTH	04/2016	02/2019	02/2020	211.42	12
270	BARASGAON TO RAHATEE	MORTH	07/2016	09/2018	04/2021	289.11	31
271	KOLHA TO NASRATPUR	MORTH	04/2016	04/2019	04/2020	281.78	12
272	PEN TO KHOPOLI	MORTH	03/2018	03/2018	12/2019	301.39	21
273	MALEWADA TO CHIMUR	MORTH	10/2016	06/2019	06/2020	322.55	12
274	TALEGAON TO GONAPUR	MORTH	01/2018	03/2019	12/2019	264.41	9
275	NAIGAONBANDI TO MANGRULPIR	MORTH	12/2017	03/2019	12/2019	244.04	9
276	TAKARKHED TO JALNA	MORTH	09/2017	06/2019	12/2019	417.9	6
277	KARAD PATAN CHIPLUN GUHAGAR	MORTH	02/2017	06/2019	06/2020	407.19	12
278	KARAD TO TAGAON	MORTH	01/2017	06/2019	06/2020	537.81	12
279	DEORI TO AMGAON	MORTH	01/2017	05/2019	05/2020	409.62	12
280	WAKAN PALI KHOPOLI	MORTH	01/2017	05/2019	05/2020	376.19	12
281	MANGAON TO DIGHI PORT	MORTH	01/2017	07/2019	07/2020	457.52	12
282	NAGAJ TO VAIJAPUR	MORTH	01/2017	06/2019	12/2019	376.72	6
283	WADI TO ASOLA	MORTH	01/2017	09/2019	09/2020	363.82	12
284	MORSHI TO ACHALPUR	MORTH	01/2017	06/2019	12/2019	341.16	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
285	NANDGAON TO MORSHI	MORTH	01/2017	06/2019	12/2019	385.87	6
286	DIGRAS DARWAH KARANJA	MORTH	01/2017	06/2019	06/2020	391.06	12
287	SHEGAON TO DEORI PHATA	MORTH	02/2017	05/2019	12/2019	373.1	7
288	KHAMGAON TO SHEGAON	MORTH	02/2017	05/2019	12/2019	203.21	7
289	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	PWD	05/2014	08/2016	12/2020	199.98	52
290	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	PWD	01/2017	05/2019	12/2019	300	7
291	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	105
292	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	110
293	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	PWD	01/2013	02/2013	12/2019	182.28	82
294	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	116
295	FOUR LANNING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	05/2020	641.17	46
296	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
297	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	09/2020	1176.37	37
298	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	11/2020	476.56	40
299	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	11/2019	648.33	29
300	JUNAGADH BYPASS	NHAI	10/2017	10/2017	11/2019	232.49	25
301	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	01/2020	639.97	27
302	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	11/2020	964.17	37
303	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
304	4-LANNING OF OTTANCHATRAM BYPASS	NHAI	09/2017	09/2017	11/2019	244.27	26
305	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	08/2020	1227.87	35
306	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	MORTH	02/2015	03/2015	06/2019	383.4	51
307	REHABILITATION AND UPGRADATION OF NH-	PWD	03/2015	10/2015	09/2019	271.45	47

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH						
308	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	NHIDCL	03/2015	05/2018	08/2019	194.11	15
309	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	03/2020	394	21
310	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	MORTH	12/2015	06/2018	07/2019	621.43	13
311	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	09/2019	255.75	24
312	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	08/2019	445.89	29
313	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	36
314	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	PWD	10/2015	11/2015	06/2019	333.21	43
315	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	PWD	07/2014	01/2017	06/2019	342.05	29
316	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	09/2019	164.54	49
317	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	PWD	03/2015	08/2017	02/2020	511.83	30
318	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	PWD	12/2011	11/2017	09/2019	159.39	22
319	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	12/2019	191.08	52
320	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	03/2020	954.43	54
321	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	08/2019	410.72	52
322	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	PWD	09/2012	10/2013	06/2019	511	68
323	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	PWD	09/2012	10/2013	08/2019	511	70
324	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	08/2020	604	128
325	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2019	671.3	76
326	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	06/2019	575	71
327	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	06/2020	702.16	71
328	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	03/2020	486	118
329	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108	100
330	WIDENING OF KHED-SINNAR STRETCH OF	NHAI	05/2013	02/2014	06/2019	1348.2	64

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	PUNE NASHIK SECTION OF NH-50						
331	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2019	617	88
332	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	07/2019	1724.55	76
333	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	12/2019	1266.6	39
334	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
335	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	10/2019	1535	65
336	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
337	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2019	1078.84	76
338	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2020	998.79	82
339	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2019	1396.18	63
340	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	07/2019	972.5	24
341	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	05/2020	923.04	42
342	4-LANING OF GOA/KARNATAKA BORDER- KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
343	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	11/2019	1388	15
344	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	07/2019	199.81	123
345	DHARAMTUL TO SONAPUR, KM 205-183 (AS- 20)	NHAI	12/2003	05/2008	06/2019	160	133
346	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	PWD	07/2015	12/2015	06/2019	333.21	42
347	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	06/2019	333.21	42
348	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	PWD	04/2013	08/2013	12/2019	151.59	76
349	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	09/2019	245	138
350	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	08/2019	217.61	112
351	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2019	208	140
352	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	10/2019	225	136
353	HUNGUND-SURATHKAL AND MANGALORE-	NHAI	09/2010	06/2018	12/2019	946	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KNT/KERALA BORDER						
354	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	07/2019	478.51	69
355	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2020	942.69	69
356	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	12/2019	709	27
357	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	07/2019	1387.11	20
358	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	08/2019	563.92	20
359	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	06/2020	414.51	25
360	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2020	531.13	25
361	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	12/2020	593.26	31
362	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	12/2020	649.5	21
363	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	08/2019	602.95	38
364	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	07/2019	574.28	12
365	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	05/2020	505	24
366	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	12/2019	1083	18
367	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
368	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	07/2019	1423.96	8
369	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	10/2019	2136.97	10
370	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	10/2019	596.67	17
371	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
372	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	24
373	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	02/2020	726.67	22
374	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	09/2019	479.2	16
375	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
376	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	11/2020	701.4	20
377	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	11/2018	12/2019	229.37	13
378	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
379	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2020	707.82	19
380	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	05/2020	641.17	22
381	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	01/2020	804.97	19
382	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ	NHAI	05/2015	05/2017	06/2019	581.84	25
383	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	01/2020	323.72	17
384	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	06/2020	1167.42	15
385	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
386	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	NHAI	08/2016	05/2019	11/2019	248.97	6
387	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	NHIDCL	04/2016	10/2016	10/2019	198	36
388	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	NHAI	09/2016	08/2018	09/2019	767.03	13
389	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16
390	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	09/2019	400.25	6
391	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	11/2019	446.17	8
392	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	12/2019	605.84	17
393	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	MORTH	03/2014	05/2016	12/2019	191.5	43
394	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	MORTH	01/2015	04/2018	06/2019	326.63	14
395	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	MORTH	08/2013	06/2016	11/2019	171.96	41
396	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
397	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
398	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER	NHAI	03/2017	03/2020	05/2021	235.48	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	GANGA AT MUNGER GHAT NEAR MUNGE						
399	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	12
400	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
401	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
402	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	02/2021	284.09	46
403	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	02/2021	168.32	46
404	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
405	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	02/2021	216.71	46
406	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46
407	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
408	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
409	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
410	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
411	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MORTH	06/2017	06/2019	12/2019	282.08	6
412	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	PWD	10/2016	03/2019	12/2019	248.83	9
413	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	PWD	10/2016	02/2019	12/2019	298.32	10
414	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MORTH	01/2017	01/2018	01/2020	576.48	24
415	REHABILITATION AND UPGRADATION OF EEPURPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2	MORTH	08/2016	07/2017	07/2019	574.19	24
416	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MORTH	01/2017	09/2017	09/2019	263.45	24
417	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MORTH	11/2016	08/2017	08/2019	376.25	24
418	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	MORTH	03/2016	09/2016	06/2019	444.84	33
419	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	MORTH	01/2016	05/2016	06/2019	386.09	37
420	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MORTH	08/2016	01/2017	06/2019	350.61	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
421	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MORTH	01/2018	08/2018	02/2020	418.03	18
422	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	PWD	09/2016	09/2018	07/2019	178.23	10
423	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	MORTH	03/2018	11/2018	05/2020	504.19	18
424	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	MORTH	03/2018	07/2018	01/2020	297.12	18
425	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MORTH	03/2018	08/2018	02/2020	289.67	18
426	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	MORTH	03/2018	08/2018	08/2020	244.95	24
427	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MORTH	03/2018	08/2018	03/2020	228.32	19
428	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MORTH	02/2017	11/2017	11/2019	429.43	24
429	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MORTH	01/2017	08/2017	08/2019	319.28	24
430	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	MORTH	11/2016	01/2018	01/2020	378.24	24
431	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	MORTH	10/2015	12/2015	06/2019	333.21	42
432	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	PWD	01/2017	03/2019	09/2019	247.25	6
433	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	PWD	01/2016	07/2018	02/2020	809.16	19
434	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	PWD	09/2016	01/2019	11/2019	287.34	10
435	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	PWD	02/2018	03/2018	04/2020	279.44	25
436	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	254.17	21
437	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	PWD	11/2017	07/2018	01/2020	249.05	18
438	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	233.04	20
439	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	217.22	22
440	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	214.69	20
441	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	07/2019	279.7	23
442	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	PWD	01/2017	03/2017	06/2020	205.05	39
443	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF	PWD	06/2016	08/2019	08/2021	236.78	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	EXISTING LEVEL CROSSING GATE N						
444	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	PWD	03/2016	08/2019	08/2021	160.27	24
445	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	184.62	21
446	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	PWD	11/2017	02/2018	11/2019	235.91	21
447	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	PWD	02/2018	03/2018	07/2020	169.63	28
448	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	PWD	03/2016	11/2018	11/2019	271.17	12
449	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	166.21	22
450	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	PWD	08/2014	11/2017	06/2019	823.2	19
451	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	PWD	03/2018	03/2018	12/2019	162.56	21
452	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
453	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
454	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	RINL	07/2015	07/2018	07/2019	465.85	12
455	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	09/2019	2858	21
456	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	07/2019	320.66	11
457	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12
458	FORGED WHEEL PLANT	RINL	04/2014	09/2018	09/2019	1682.85	12
459	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
460	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	15525	62
461	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2021	343	53
462	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	06/2019	1154.18	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
463	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
464	MADHYA PRADESH ACCESS (LOT1)	BSNL	08/2017	05/2018	07/2019	215.3	14
465	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	BSNL	01/2018	10/2018	09/2019	231.8	11

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
466	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	12/2020	430	7
467	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
468	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
469	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	06/2019	205	87
470	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2020	216.69	67
471	NSG AT KOLKATA	CPWD	10/2014	04/2018	07/2019	162.88	15
472	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
473	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
474	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2020	197.33	14
475	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	09/2019	388	28
476	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	10/2019	156.57	38
477	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2019	270.83	59
478	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2020	171.86	54
479	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	17
480	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2020	165.23	89
481	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
482	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
483	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
484	CONSTRUCTION OF ITBP ROAD TO INDO-	CPWD	12/2008	12/2013	10/2019	114.26	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA						
485	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2020	496.18	40
486	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	12/2019	294	8

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
487	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	10151.04	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
7	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7080.41	1173.3
9	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3727.3	2009.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
12	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
13	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1683.06	821.27
14	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	4006.83	4475.92	469.09
15	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	3049.47	134.47
16	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
17	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS	IOCL	05/2016	12/2018	4497	6025	1528

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	PIPELINE						
18	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
19	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
20	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
21	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
23	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	682.9	138.99
24	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	345.92	142.98
25	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
26	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
27	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9997.11	6077.52
28	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	12865.92	1227.37
29	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
30	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
31	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
32	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6880.36	1769.03
33	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9072.36	4317.94
34	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
35	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
36	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
37	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
38	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4397.8	1906.22

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	BUXAR THERMAL POWER PLANT (1320 MW)	SJVN	05/2015	12/2016	436.68	602.44	165.76
40	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2018	9750.89	12176.28	2425.39
41	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
42	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	9996.59	4643.59
43	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1592.34	210.5
44	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15164.05	797.47
45	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13740.53	1208.09
46	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
47	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
48	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
49	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
50	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	5024.35	3367.35
51	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7419.34	4922.44
52	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
53	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
54	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3376	2342.93
55	KOTLIPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
56	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
57	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
58	HATHUA-BHATNI (N L) (NER)	NER	04/2005	12/2022	230.03	770.08	540.05
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
60	MANSI-PURNIA (EXTENSION OF MANSI-	ECR	04/1996	03/2012	477.88	749	271.12

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	SAHARSA) GAN ECR						
61	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.77	1538.12
62	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5021.45	2627.98
63	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
64	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	1106.62	1536.44	429.82
65	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
66	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
67	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
68	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
69	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
70	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
71	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
72	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	800	463.09
73	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
74	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	694	407
75	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
76	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
77	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
78	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
79	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	3000	673.48
80	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
81	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
82	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	13809	9354.83
84	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3798.8	875.67
85	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	3500	2319.81
86	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	589.15	426.28
87	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	358.68	100.48
88	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
89	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
90	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
91	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	410	167.91
92	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
93	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
94	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
95	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4079.15	1996.4
96	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
97	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	860.92	631.92
98	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
99	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	727.29	546.47
100	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
101	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
102	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
103	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
104	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
105	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
107	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1300.44	714.51
108	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
109	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
110	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
111	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1500	551.96
112	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	1950	1236.52
113	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1200	272.99
114	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
115	RUPSA BANGRIPOSTI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
116	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	1013.45	1428	414.55
117	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
118	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	2136.01	1265.05
119	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
120	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	2499.71	3382.95	883.24
121	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
122	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
123	KONDAPALLI-KOTHAGUDEM	SCR	04/2013	N.A.	723	997.09	274.09
124	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
125	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
126	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
127	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
128	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	923.52	1218.71	295.19

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	444.81	183.43
130	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
131	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
132	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	575.65	168.66
133	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3
134	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
135	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	700	386
136	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
137	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
138	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
139	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
140	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
141	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
142	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
143	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
144	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
145	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
146	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
147	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2300	1776.48
148	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
149	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	400.17	187.16
150	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	785.87	237.87
151	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
153	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
154	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	2614.36	2235.8
155	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	729.92	404.92
156	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
157	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
158	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	ECR	04/2008	N.A.	445.25	2860.55	2415.3
159	NAWADA-LAXMIPUR (NL)	ECR	04/2008	N.A.	620.57	2626.98	2006.41
160	ARA-BHABHUA ROAD (NL)	ECR	04/2008	N.A.	633.87	2396.88	1763.01
161	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
162	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
163	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
164	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	4874.58	8574.97	3700.39
165	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
166	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
167	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
168	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
169	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	876	251
170	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
171	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	809.07	257.56
172	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
173	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
174	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1103.04	229.33

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
176	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
177	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
178	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1310.23	480.49
179	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	980	676.02
180	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
181	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756.92	1245.06
182	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	2542.75	819.75
183	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
184	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
185	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
186	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
187	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2010	1560
188	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	886.41	476.33
189	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1156.41	831.68
190	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
191	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2973.73	2478.29
192	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
193	MM FROM PANSKURA-GHATAL NL	SER	04/2011	N.A.	276.69	426	149.31
194	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773
195	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
196	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	1352.74	648.43
197	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	305	120.94

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	726.95	226.99
199	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	693.8	151.62
200	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
201	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	3860.4	356.71
202	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
203	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	346	226
204	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1670.01	481.1
205	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1026.3	419.21
206	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
207	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
208	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
209	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
210	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
211	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	PWD	03/2012	05/2012	207.03	389.45	182.42
212	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
213	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
214	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
215	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
216	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
217	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
218	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
219	FOUR LANNING OF JHANSI-KHAJURAHO	NHAI	03/2017	03/2020	1184.71	1310	125.29

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C						
220	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
221	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
222	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	195.04	377.99	182.95
223	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	PWD	11/2010	02/2011	470.2	630.36	160.16
224	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	497.05	881.05	384
225	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	445.89	653.29	207.4
226	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653	207.11
227	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	PWD	03/2009	09/2013	501	671.54	170.54
228	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP.	PWD	01/2012	01/2014	378.07	478.73	100.66
229	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	279.7	398.52	118.82
230	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	PWD	08/2014	11/2017	823.2	937.76	114.56
231	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	PWD	08/2014	11/2017	600.87	720.97	120.1
232	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
233	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	193.69	327.92	134.23
234	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	624.41	992.67	368.26
235	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
236	ENORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
237	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
238	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	23140	7615

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
241	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
242	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79
243	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	5687.79	506
244	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
245	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
246	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
247	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	388	488.28	100.28
WATER RESOURCES							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
248	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	1,2320.00	1,7079.00	4759	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6840.00	3348	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	7080.41	1173.3	48
7	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
8	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	03/2020	1718.00	3727.30	2009.3	102

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	4475.92	469.09	7
11	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	345.92	142.98	70
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	1683.06	821.27	79

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	3049.47	134.47	110
14	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497.00	6025.00	1528	26
15	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	5245.96	657.67	15
16	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	723.40	413.59	58

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
17	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	6880.36	1769.03	24
18	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	1592.34	210.5	29
19	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353.00	9996.59	4643.59	98
20	BUXAR THERMAL POWER PLANT (1320 MW)	SJVN	05/2015	12/2016	07/2019	436.68	602.44	165.76	31
21	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	4397.80	1906.22	114
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	08/2019	2496.90	7419.34	4922.44	116
23	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657.00	5024.35	3367.35	76
24	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	639.46	151.97	63
25	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	08/2019	1779.29	2187.32	408.03	129
26	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	2,1312.11	12619.1	118
27	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2018	06/2020	9750.89	1,2176.28	2425.39	28
28	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9997.11	6077.52	147

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	5071.94	247.82	86
30	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	1,1638.55	1,2865.92	1227.37	26
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,4719.10	3588.91	103
32	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	1891.41	526.89	40
33	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	5867.38	2888.9	93
34	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	06/2020	1,2532.44	1,3740.53	1208.09	18
35	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	1,4366.58	1,5164.05	797.47	27
36	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	07/2019	1,2964.60	1,7304.00	4339.4	14
37	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9072.36	4317.94	12
38	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	1,1846.00	1,2739.82	893.82	29

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
39	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625.00	876.00	251	60
40	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288.00	4970.11	2682.11	9
41	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
42	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	809.07	257.56	12
43	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229.00	860.92	631.92	15
44	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
46	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2021	1723.00	2542.75	819.75	252
47	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	1756.92	1245.06	8
48	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	03/2025	393.46	1026.00	632.54	216
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2021	303.98	980.00	676.02	12
50	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	1310.23	480.49	12
51	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
52	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	11/2019	148.77	377.00	228.23	35
53	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
54	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	305.00	120.94	9
55	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12
56	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287.00	694.00	407	111
57	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.50	3712.50	1441	12
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	2973.73	2478.29	204
59	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
60	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1156.41	831.68	96
61	KHURDA ROAD-BOLANGIR(NL) ECR	ECOR	04/1994	03/2009	12/2023	2923.13	3798.80	875.67	177
62	JIRIBAM TO IMPHAL	NFR	04/2003	03/2011	03/2020	4454.17	1,3809.00	9354.83	108

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	(TUPUI)(NL)(NEFR)								
63	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
64	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
65	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1670.01	481.1	72
66	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1026.30	419.21	133
67	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
68	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
69	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	385.00	251.59	129
70	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	1928.07	1117.29	21
71	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	2072.50	1347.81	12
72	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2020	1106.62	1536.44	429.82	111
73	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	5021.45	2627.98	96
74	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	749.00	271.12	96
75	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	3860.40	356.71	12
76	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	726.95	226.99	157
77	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
78	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
79	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT	NFR	04/2006	03/2015	10/2021	2326.52	3000.00	673.48	79

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	(NEFR)								
80	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
81	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	12/2021	410.08	886.41	476.33	34
82	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450.00	2010.00	1560	140
83	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2021	2500.00	2,7949.00	25449	229
84	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
85	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	1218.71	295.19	108
86	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	810.02	108.41	28
87	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	939.00	414.57	36
88	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
89	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1200.00	272.99	12
90	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	1120.00	177.05	24
91	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	1247.64	665.51	6
92	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	1300.44	714.51	16
93	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
94	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
95	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
96	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	348.55	102.47	6

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
97	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
98	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
99	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	12/2019	242.09	410.00	167.91	10
100	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
101	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC	ECR	04/2009	03/2020	03/2022	548.00	785.87	237.87	24
102	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
103	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2019	120.70	1800.00	1679.3	9
104	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	575.65	168.66	228
105	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760.00	1182.31	422.31	15
106	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
107	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	07/2019	445.89	653.00	207.11	28
108	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	07/2019	199.81	385.13	185.32	123
109	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	1420.00	131.93	12
110	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	07/2019	279.70	398.52	118.82	23
111	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	PWD	08/2014	11/2017	06/2019	823.20	937.76	114.56	19
112	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	12/2019	1266.60	1544.00	277.4	39

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JUNE 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
113	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	992.67	368.26	105
114	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	327.92	134.23	110
115	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	377.99	182.95	116
116	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	08/2019	445.89	653.29	207.4	29
117	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	881.05	384	36
118	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108.00	2288.00	1180	100

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
119	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2021	343.00	488.40	145.4	53
120	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	1,5525.00	2,3140.00	7615	62

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
121	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
122	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
123	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	09/2019	388.00	488.28	100.28	28
124	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	5687.79	506	29
125	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	1592.00	372.79	17

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS
OF RS.100 CRORE AND ABOVE**

(JUNE 2019)

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
126	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	1,0151.04	5,5548.87	45397.8	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure - XVIII

Costing Rs. 150 Crore and above					(June 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	-	.00	56
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	-	.00	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2020	.00	118
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	-	.00	61
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	-	.00	30
10	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
11	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
12	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	-	.00	71
13	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	08/2020	.00	128
14	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2019	.00	88
15	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
16	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
17	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	-	.00	76
18	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	06/2020	.00	71

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (June 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
19	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2019	.00	81
20	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
21	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	-	.00	11
22	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	05/2020	.00	42
23	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	65
24	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	07/2019	.00	24
25	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	06/2020	.00	82
26	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
27	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	-	.00	0
28	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	12/2019	.00	76
29	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	-	.00	0
30	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
31	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
32	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	-	.00	0
33	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	64
34	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	11/2019	.00	15
35	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	12/2019	.00	63
36	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	-	.00	0
37	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
38	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (June 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	10/2019	.00	65
40	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	12/2019	21.90	39
41	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
42	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	06/2019	.00	5
43	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	37
44	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
45	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	-	.00	0
46	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	06/2019	.00	0
47	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	89
48	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
49	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	07/2019	.00	76
50	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
51	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	-	.00	13
52	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	29
53	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	-	.00	44
54	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
55	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	-	.00	0
56	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,159.00	06/2015	-	.00	0
57	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	03/2020	106.50	100
58	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	05/2019	-	.00	0
59	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0
60	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00	2,848.00	03/2014	12/2019	.00	69

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (June 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
61	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73	0
	Total		73,759.12 -	76,780.07				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
62	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88	0
	<u>Mumbai Port Trust</u>							
63	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	-	82.72	0
	Total		610.89 -	945.44				
	Grand Total		74,370.01	77,725.51				

State-Wise Ongoing Central Sector Project's List

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.06.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	9.77 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [7/2019]	401.00 (401.00) [401.00]	82.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	124.89 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	2.33 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	0.00 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
10	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [2/2020]	601.02 (-) [601.02]	85.04 (0.00) [-]
11	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [10/2019]	272.19 (-) [272.19]	140.58 (0.00) [7]
	<u>Petroleum</u>				
12	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
13	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	74.36 (0.00) [3]
14	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021	384.58	73.31

			(-) [4/2020]	(-) [384.58]	(0.00) [-12]
15	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [2/2021]	580.20 (-) [580.20]	27.71 (0.00) [0]
16	FIELD DEVELOPMENT OF NELL BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (7/2019) [7/2019]	420.76 (-) [420.76]	193.15 (0.00) [10]
17	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (-) [8/2021]	34,012.00 (-) [34,012.00]	2,670.11 (0.00) [14]
18	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	13.97 (0.00) [10]
19	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
20	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	14.78 (0.00) [0]
21	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	4,913.36 (0.00) [0]
22	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	359.31 (0.00) [0]
	<u>Railways</u>				
23	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
24	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
25	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
26	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (-) [3,631.00]	407.42 (0.00) [12]
27	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (-) [2,120.16]	412.87 (1,074.96) [168]
28	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (-) [3,382.95]	325.64 (883.24) [0]
29	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	5.59 (0.50) [21]
30	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
31	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,288.70]	667.03 (0.00) [36]
32	NANDYAL-YERRAGUNTLA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
33	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	709.85 (302.41) [0]
34	VIJAYAWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL	3/2012	3/2020	1,503.71	1,235.96

	(221 KM)		(-) [3/2022]	(-) [1,503.71]	(0.00) [24]
	<u>Road Transport And Highways</u>				
35	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [11/2019]	328.67 (-) [328.67]	176.29 (0.00) [-]
36	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	70.71 (0.00) [0]
37	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [3/2020]	557.30 (-) [557.30]	33.63 (0.00) [-]
38	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (-) [9/2019]	263.45 (-) [263.45]	43.79 (0.00) [24]
39	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (-) [11/2019]	429.43 (-) [429.43]	179.81 (0.00) [24]
40	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [12/2020]	314.43 (-) [314.43]	17.64 (0.00) [-]
41	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (-) [6/2019]	350.61 (-) [350.61]	301.70 (0.00) [29]
42	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (6/2019) [6/2019]	333.21 (353.89) [353.89]	256.11 (20.68) [43]
43	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (6/2019) [6/2019]	333.21 (333.21) [333.21]	256.11 (0.00) [42]
44	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (6/2019) [6/2019]	333.21 (-) [333.21]	256.11 (0.00) [42]
45	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (-) [6/2019]	333.21 (-) [333.21]	0.00 (0.00) [42]
46	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [4/2021]	1,532.62 (-) [1,532.62]	0.00 (0.00) [1]
47	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [11/2019]	648.33 (-) [648.33]	18.02 (0.00) [29]
48	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [5/2019]	1,134.97 (-) [1,134.97]	21.73 (0.00) [0]
49	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (-) [1/2020]	576.48 (-) [576.48]	177.36 (0.00) [24]
50	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (-) [0/0]	348.95 (-) [348.95]	144.95 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (-) [6/2019]	386.09 (-) [386.09]	153.98 (0.00) [37]
52	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2	8/2016	7/2017 (-) [7/2019]	574.19 (-) [574.19]	0.00 (0.00) [24]
53	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (-) [0/0]	290.15 (-) [290.15]	0.00 (0.00) [0]
54	REHABILITATION AND UPGRADATION OF EXISTING NH-	1/2014	11/2014	195.45	0.00

	565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T		(-) [0/0]	(-) [195.45]	(0.00) [0]
55	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/	565.09	0.00
			(-) [2/2021]	(-) [565.09]	(0.00) [-]
56	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016	995.09	401.90
			(-) [0/0]	(995.00) [995.09]	(0.00) [0]
57	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016	444.84	208.09
			(-) [6/2019]	(-) [444.84]	(0.00) [33]
58	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017	376.25	169.76
			(-) [8/2019]	(-) [376.25]	(0.00) [24]
59	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018	297.12	119.08
			(-) [1/2020]	(294.00) [297.12]	(0.00) [18]
60	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018	289.67	60.76
			(-) [2/2020]	(290.00) [289.67]	(0.00) [18]
61	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018	504.19	136.30
			(-) [5/2020]	(504.00) [504.19]	(0.00) [18]
62	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015	271.45	143.16
			(9/2019) [9/2019]	(-) [271.45]	(0.00) [47]
63	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017	319.28	97.23
			(-) [8/2019]	(-) [319.28]	(0.00) [24]
64	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020	648.32	0.95
			(-) [11/2019]	(-) [503.10]	(-145.22) [-4]
65	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018	244.95	75.36
			(-) [8/2020]	(245.00) [244.95]	(0.00) [24]
66	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017	372.68	0.00
			(-) [0/0]	(-) [372.68]	(0.00) [0]
67	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018	228.32	20.13
			(-) [3/2020]	(-) [228.32]	(0.00) [19]
68	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018	418.03	100.00
			(-) [2/2020]	(-) [418.03]	(0.00) [18]
69	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018	378.24	0.00
			(-) [1/2020]	(-) [378.24]	(0.00) [24]
70	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/	1,959.00	0.00
			(-) [7/2021]	(-) [1,959.00]	(0.00) [-]
71	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/	1,323.15	0.00
			(-) [7/2021]	(-) [1,323.15]	(0.00) [-]
72	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/	1,550.98	0.00
			(-) [7/2021]	(-) [1,550.98]	(0.00) [-]
73	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014	1,535.00	3,220.15
			(-) [10/2019]	(-) [1,535.00]	(0.00) [65]
74	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020	1,041.62	687.88
			(-)	(-)	(145.48)

			[5/2020]	[1,187.10]	[2]
75	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.52 (0.00) [0]
76	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
77	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	7/2015	7/2018 (7/2019) [7/2019]	465.85 (-) [465.85]	390.25 (0.00) [12]
78	CENTRAL DISPATCH YARD	8/2015	8/2018 (7/2019) [7/2019]	320.66 (-) [320.66]	199.91 (0.00) [11]
79	COKE OVEN BATTERY-5	12/2011	12/2017 (9/2019) [9/2019]	2,858.00 (-) [2,500.00]	1,277.76 (-358.00) [21]
80	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016 (3/2021) [3/2021]	343.00 (488.40) [488.40]	254.29 (145.40) [53]
	<u>Urban Development</u>				
81	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [8/2019]	206.58 (-) [206.58]	82.23 (0.00) [5]
82	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
83	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [169.16]	163.98 (11.32) [0]
84	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>Water Resources</u>				
85	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (-) [6/2021]	10,151.04 (-) [55,548.87]	16,417.99 (45,397.83) [15]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
86	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (8/2019) [8/2019]	2,496.90 (7,419.34) [7,419.34]	7,327.76 (4,922.44) [116]
87	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,868.18 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
88	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	0.00 (0.00) [0]
89	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	240.21 (0.00) [21]
90	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH- 229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59)	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	174.80 (0.00) [15]
91	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	182.19 (0.00) [0]
92	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [0/0]	210.50 (-) [210.50]	0.00 (0.00) [0]

93	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450)	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	69.97 (0.00) [0]
94	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN)	7/2015	/	189.91	0.00
			(-) [0/0]	(-) [189.91]	(0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/	259.52	0.00
			(-) [0/0]	(-) [259.52]	(0.00) [0]
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/	200.44	0.00
			(-) [0/0]	(-) [200.44]	(0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/	568.92	0.00
			(-) [0/0]	(-) [568.92]	(0.00) [0]
98	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/	188.78	0.00
			(-) [0/0]	(-) [188.78]	(0.00) [0]
99	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	94.49 (16.07) [36]
100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	128.92
			(-) [9/2020]	(-) [245.79]	(0.00) [-]
101	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2019]	198.00 (-) [198.00]	195.67 (0.00) [36]
102	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	53.23 (0.00) [0]
103	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM 16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	0.00
			(-) [0/0]	(-) [1,718.59]	(0.00) [0]
104	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM 16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	211.21 (0.00) [60]
105	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [2/2021]	167.28 (-) [209.71]	47.37 (42.43) [46]
106	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [2/2021]	216.71 (-) [262.62]	31.11 (45.91) [46]
107	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
108	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	126.58
			(-) [12/2020]	(-) [434.06]	(0.00) [-]
109	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [2/2021]	284.09 (-) [284.09]	80.64 (0.00) [46]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	37.30 (0.00) [0]
111	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	48.16 (0.00) [0]
112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	56.15 (0.00) [0]
113	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI	1/2017	4/2017	198.22	24.14

	ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.		(-) [0/0]	(-) [198.22]	(0.00) [0]
114	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [389.45]	275.19 (182.42) [0]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [215.70]	45.21 (35.13) [46]
116	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [2/2021]	168.32 (-) [202.05]	42.83 (33.73) [46]
117	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
118	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
119	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/	256.66	0.00
			(-) [0/0]	(-) [256.66]	(0.00) [0]
120	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/	175.06	0.00
			(-) [0/0]	(-) [175.06]	(0.00) [0]
121	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/	176.12	0.00
			(-) [0/0]	(-) [176.12]	(0.00) [0]
122	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/	199.02	0.00
			(-) [0/0]	(-) [199.02]	(0.00) [0]
123	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/	184.88	0.00
			(-) [0/0]	(-) [184.88]	(0.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
124	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
125	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
126	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
127	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	101.40 (0.00) [0]
128	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	460.33 (0.00) [0]
129	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CCGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	3.30 (0.00) [0]
130	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
131	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (-) [345.92]	139.45 (142.98) [70]
132	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF	6/2016	8/2019 (-)	423.00 (-)	244.44 (0.00)

	RAMNAGAR DEPOT		[9/2019]	[423.00]	[1]
133	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [682.90]	6.12 (138.99) [0]
134	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,498.18 (0.00) [0]
135	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	145.01 (15.64) [0]
136	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
137	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (-) [700.00]	687.37 (386.00) [0]
138	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	571.56 (-50.32) [-24]
139	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	454.63 (1,265.05) [0]
140	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	606.19 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
141	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [11/2010]	268.08 (-) [268.08]	188.71 (0.00) [0]
142	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [6/2018]	470.20 (-) [630.36]	344.32 (160.16) [0]
143	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
144	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [12/2015]	223.30 (-) [223.30]	61.56 (0.00) [0]
145	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	34.00 (0.00) [0]
146	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	347.18 (0.00) [0]
147	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [10/2017]	289.99 (-) [289.99]	4.48 (0.00) [0]
148	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
149	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	6.27 (0.00) [0]
150	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	48.09 (0.00) [0]
151	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [8/2019]	217.61 (-) [217.61]	451.15 (0.00) [112]
152	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN	11/2010	2/2014	197.37	88.86

	ASSAM		(-) [12/2019]	(-) [197.37]	(0.00) [70]
153	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.68 (7.98) [133]
154	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	292.25 (0.00) [0]
155	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	168.40 (0.00) [0]
156	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [818.00]	105.48 (0.00) [0]
157	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	6.62 (0.00) [0]
158	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	292.24 (0.00) [0]
159	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	120.86 (0.00) [0]
160	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [280.00]	472.00 (0.00) [0]
161	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
162	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
163	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [7/2019]	199.81 (-) [385.13]	319.96 (185.32) [123]
164	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [167.64]	268.94 (0.00) [0]
165	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2019]	208.00 (-) [230.00]	337.08 (22.00) [140]
166	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	326.35 (0.00) [136]
167	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [9/2019]	245.00 (-) [174.34]	224.28 (-70.66) [138]
168	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [11/2014]	218.31 (307.47) [307.47]	239.76 (89.16) [0]
169	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	BIHAR				
	Petroleum				
170	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	564.33 (0.00) [-10]
171	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	58.27 (0.00) [0]

172	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	125.80 (0.00) [0]
173	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	9.49 (0.00) [0]
174	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [7/2019]	822.66 (-) [822.66]	822.02 (0.00) [8]
175	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (-) [10/2019]	951.64 (-) [951.64]	300.50 (0.00) [0]
176	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	6.71 (0.00) [0]
177	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	8.19 (0.00) [0]
178	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [3/2020]	324.00 (-) [324.00]	147.63 (0.00) [-3]
	<u>Power</u>				
179	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (8/2021) [8/2021]	8,692.97 (21,312.11) [21,312.11]	16,182.14 (12,619.14) [118]
180	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (-) [9/2020]	5,353.00 (-) [9,996.59]	7,816.71 (4,643.59) [98]
181	BUXAR THERMAL POWER PLANT (1320 MW)	5/2015	12/2016 (-) [7/2019]	436.68 (-) [602.44]	561.74 (165.76) [31]
182	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (6/2019) [7/2019]	12,964.60 (17,304.00) [17,304.00]	13,589.31 (4,339.40) [14]
	<u>Railways</u>				
183	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [3/2023]	633.87 (-) [2,396.88]	0.40 (1,763.01) [-]
184	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (-) [1,605.17]	23.40 (0.00) [-]
185	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	1.91 (2,668.81) [-]
186	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	378.56 (-) [2,614.36]	375.63 (2,235.80) [-]
187	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
188	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [3/2024]	205.00 (-) [205.00]	5.21 (0.00) [-]
189	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [12/2021]	329.39 (-) [1,483.14]	815.41 (1,153.75) [-]
190	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [3/2024]	445.25 (-) [2,860.55]	1.14 (2,415.30) [-]
191	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (-)	213.01 (-)	378.41 (187.16)

			[1/2020]	[400.17]	[-]
192	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	1,403.38
			(-)	(-)	(1,538.12)
			[3/2023]	[2,066.77]	[-]
193	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	1,028.71
			(-)	(-)	(831.68)
			[3/2020]	[1,156.41]	[96]
194	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	457.46
			(-)	(-)	(237.87)
			[3/2022]	[785.87]	[24]
195	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	303.96
			(-)	(-)	(426.28)
			[3/2022]	[589.15]	[-]
196	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.67
			(3/2022)	(-)	(26.24)
			[3/2022]	[360.00]	[-]
197	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	390.91
			(-)	(1,200.20)	(0.00)
			[10/2021]	[1,200.20]	[19]
198	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	389.29
			(-)	(-)	(16.61)
			[3/2020]	[516.02]	[0]
199	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.39
			(-)	(-)	(0.00)
			[3/2024]	[192.56]	[-]
200	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	672.82
			(-)	(283.95)	(271.12)
			[3/2020]	[749.00]	[96]
201	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	24.16
			(-)	(-)	(715.09)
			[3/2024]	[926.09]	[-]
202	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	15.39
			(-)	(-)	(454.09)
			[3/2022]	[1,185.73]	[12]
203	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.60
			(-)	(-)	(0.00)
			[3/2024]	[281.30]	[-]
204	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.53
			(-)	(-)	(0.00)
			[3/2024]	[228.05]	[-]
205	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	541.07
			(-)	(-)	(227.76)
			[0/0]	[559.91]	[0]
206	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.28
			(-)	(-)	(2,006.41)
			[3/2024]	[2,626.98]	[-]
207	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	932.80
			(-)	(-)	(1,612.13)
			[3/2020]	[2,145.00]	[12]
208	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/	180.82	488.81
			(-)	(-)	(546.47)
			[9/2019]	[727.29]	[-]
209	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	424.98
			(-)	(-)	(0.00)
			[12/2022]	[1,491.47]	[33]
210	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	35.10
			(-)	(-)	(471.50)
			[3/2022]	[1,215.54]	[12]
211	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	349.60
			(-)	(-)	(404.92)
			[3/2021]	[729.92]	[-]

212	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2021]	372.14 (1,470.50) [1,470.50]	356.81 (1,098.36) [-]
213	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [2/2023]	380.00 (519.33) [519.33]	126.80 (139.33) [-]
214	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [3/2024]	678.62 (-) [2,393.23]	17.20 (1,714.61) [-]
	Road Transport And Highways				
215	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013 (-) [0/0]	351.54 (-) [351.54]	329.40 (0.00) [0]
216	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [12/2018]	511.54 (-) [511.54]	566.60 (0.00) [0]
217	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
218	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [6/2019]	575.00 (-) [575.00]	843.67 (0.00) [71]
219	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [6/2019]	581.84 (-) [581.84]	77.43 (0.00) [25]
220	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	0.00 (0.00) [0]
221	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015 (-) [0/0]	288.24 (-) [288.24]	241.00 (0.00) [0]
222	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (-) [0/0]	2,598.00 (-) [2,598.00]	0.00 (0.00) [0]
223	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	0.00 (-7.71) [14]
224	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [496.20]	0.00 (0.00) [0]
225	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [683.83]	473.00 (0.00) [0]
226	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	52.50 (0.00) [0]
227	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
228	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [553.30]	239.77 (0.00) [0]
229	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	99.74 (0.00) [-]
230	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [10/2020]	642.41 (-) [642.41]	110.39 (0.00) [-]
231	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [4/2020]	322.09 (-) [322.09]	77.53 (0.00) [24]

232	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	753.03 (0.00) [0]
233	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [814.04]	367.27 (0.00) [-]
234	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
235	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [4/2019]	1,041.10 (-) [1,041.10]	214.34 (0.00) [0]
236	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
237	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [6/2019]	671.30 (-) [671.30]	885.31 (0.00) [76]
238	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	517.08 (0.00) [0]
239	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
240	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
241	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [319.68]	0.00 (0.00) [0]
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [282.41]	67.52 (0.00) [0]
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [358.22]	188.71 (0.00) [0]
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	0.00 (0.00) [0]
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
248	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
249	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	102.51 (0.00) [54]
250	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	0.00 (0.00) [0]
251	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
252	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA -	8/2015	4/2019	399.54	195.59

	MOKAMA		(-) [10/2019]	(-) [399.54]	(0.00) [6]
253	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/	854.80	579.78
			(-) [3/2019]	(-) [854.80]	(0.00) [0]
254	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018	516.13	417.09
			(-) [0/0]	(-) [516.13]	(0.00) [0]
255	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020	672.89	0.00
			(-) [3/2020]	(-) [736.01]	(63.12) [0]
256	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016	199.98	0.00
			(-) [12/2020]	(-) [199.98]	(0.00) [52]
257	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019	230.34	167.64
			(-) [10/2019]	(-) [230.34]	(0.00) [0]
	<u>Urban Development</u>				
258	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017	496.18	69.60
			(-) [10/2020]	(496.00) [498.99]	(2.81) [40]
259	IRRIGATION WORK OF BAGMATI	10/2005	3/2015	956.00	651.21
			(-) [3/2021]	(-) [956.00]	(0.00) [72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
260	AMERA OC RCE	2/2015	3/2018	335.97	51.66
			(-) [0/0]	(-) [335.97]	(0.00) [0]
261	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020	316.10	67.40
			(-) [3/2020]	(-) [316.10]	(0.00) [0]
262	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016	198.59	169.15
			(-) [0/0]	(-) [198.59]	(0.00) [0]
263	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016	258.56	172.88
			(-) [3/2020]	(-) [258.56]	(0.00) [48]
264	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020	164.49	80.33
			(-) [3/2020]	(-) [164.49]	(0.00) [0]
265	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022	610.63	88.29
			(-) [3/2022]	(-) [610.63]	(0.00) [0]
266	DURGAPUR OPENCAST PROJECT	2/2015	3/2023	916.24	3.94
			(-) [3/2023]	(-) [916.24]	(0.00) [0]
267	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023	11,816.40	2,902.94
			(-) [3/2023]	(-) [11,816.40]	(0.00) [0]
268	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015	152.43	203.90
			(-) [3/2020]	(-) [459.49]	(307.06) [60]
269	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026	389.97	0.00
			(-) [3/2026]	(-) [389.97]	(0.00) [0]
270	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014	178.44	5.16
			(-) [3/2020]	(-) [178.44]	(0.00) [72]
271	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023	7,612.33	2,057.87
			(-)	(-)	(0.00)

			[3/2023]	[7,612.33]	[0]
272	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
273	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
274	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	207.04 (0.00) [84]
275	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.29 (0.00) [0]
276	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
277	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	1.09 (0.00) [0]
	<u>Power</u>				
278	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (3/2020) [3/2020]	11,846.00 (-) [12,739.82]	12,104.40 (893.82) [29]
279	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,595.15 (0.00) [0]
	<u>Railways</u>				
280	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (10/2019) [10/2019]	872.00 (1,226.51) [1,226.51]	1,034.58 (354.51) [-2]
281	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (12/2022) [12/2022]	2,288.00 (-) [4,970.11]	619.50 (2,682.11) [9]
282	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2021) [12/2021]	1,973.00 (1,973.66) [1,973.66]	121.56 (0.66) [9]
283	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (12/2020) [12/2020]	3,055.00 (-) [3,055.00]	1,729.64 (0.00) [27]
284	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2023]	1,160.00 (-) [1,160.83]	654.74 (0.83) [36]
285	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
286	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [3/2020]	1,402.02 (-) [1,100.00]	987.29 (-302.02) [0]
	<u>Road Transport And Highways</u>				
287	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,029.96]	0.00 (0.00) [-]
288	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [2/2020]	726.67 (-) [726.67]	357.06 (0.00) [22]
289	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	7.21 (0.00) [0]
290	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-)	596.67 (-)	385.09 (0.00)

			[10/2019]	[596.67]	[17]
291	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	178.85 (0.00) [0]
292	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	447.70 (0.00) [0]
	<u>Steel</u>				
293	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	6/2020 (-) [6/2020]	818.00 (-) [818.00]	31.60 (0.00) [0]
294	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	4/2015 (-) [0/0]	188.93 (-) [188.93]	136.74 (0.00) [0]
295	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2020) [7/2020]	15,525.00 (-) [23,140.00]	15,729.80 (7,615.00) [62]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
296	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,780.91 (-243.77) [5]
	<u>DELHI</u>				
	<u>Health And Family Welfare</u>				
297	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [9/2019]	204.44 (-) [204.44]	188.00 (0.00) [28]
298	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [8/2019]	293.65 (-) [293.65]	290.71 (0.00) [27]
299	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [2/2020]	156.56 (-) [156.65]	54.94 (0.09) [-]
300	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [10/2020]	414.11 (-) [513.89]	147.00 (99.78) [83]
	<u>Heavy Industry</u>				
301	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [9/2019]	1,554.00 (-) [1,554.00]	335.03 (0.00) [0]
	<u>Power</u>				
302	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (6/2019) [12/2019]	1,394.52 (-) [1,394.52]	405.65 (0.00) [31]
	<u>Railways</u>				
303	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [3/2023]	295.68 (-) [295.68]	68.13 (0.00) [-]
304	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [197.17]	102.06 (40.52) [-]
	<u>Road Transport And Highways</u>				
305	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/ (-) [0/0]	771.18 (-) [7,558.00]	261.77 (6,786.82) [0]
	<u>Telecommunications</u>				
306	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	367.03 (0.00) [0]
	<u>Urban Development</u>				
307	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN	6/2015	4/2019	197.33	35.77

	POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI		(-) [6/2020]	(-) [197.33]	(0.00) [14]
308	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	/	218.72	0.00
			(-) [0/0]	(-) [218.72]	(0.00) [0]
309	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015	884.30	703.90
			(-) [0/0]	(-) [884.30]	(0.00) [0]
310	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019	271.90	28.71
			(-) [11/2019]	(-) [271.90]	(0.00) [0]
311	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019	188.00	146.45
			(-) [6/2019]	(-) [188.00]	(0.00) [0]
312	DELHI MRTS PHASE-III	9/2011	3/2016	38,585.00	34,763.15
			(-) [0/0]	(-) [38,585.00]	(0.00) [0]
313	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	1,219.21	293.53
			(-) [3/2021]	(-) [1,592.00]	(372.79) [17]
314	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020	238.56	41.33
			(-) [5/2020]	(-) [238.56]	(0.00) [0]
315	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019	4,264.00	3,246.53
			(-) [11/2019]	(-) [4,439.23]	(175.23) [0]
316	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/	392.00	5.96
			(8/2020)	(-)	(0.00)
			[3/2021]	[392.00]	[-]
317	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/	422.00	10.36
			(-) [12/2020]	(-) [422.00]	(0.00) [-]
318	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/	2,694.00	0.00
			(-) [0/0]	(-) [2,694.00]	(0.00) [0]
319	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018	248.20	18.58
			(-) [0/0]	(-) [248.20]	(0.00) [0]
	<u>GOA</u>				
	<u>Defence Production</u>				
320	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020	285.95	79.33
			(-) [8/2020]	(286.00) [285.95]	(0.00) [0]
321	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018	167.69	134.86
			(3/2019) [0/0]	(168.00) [167.69]	(0.00) [0]
	<u>Health And Family Welfare</u>				
322	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/	249.01	73.40
			(-) [5/2020]	(-) [249.01]	(0.00) [-]
	<u>Road Transport And Highways</u>				
323	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/	280.16	209.47
			(-) [0/0]	(-) [290.59]	(10.43) [0]
324	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/	184.05	90.39
			(-) [0/0]	(-) [184.05]	(0.00) [0]
325	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/	936.40	310.25
			(-) [0/0]	(-) [936.40]	(0.00) [0]
326	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR	3/2015	/	298.33	212.33

	NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K		(-) [0/0]	(-) [298.33]	(0.00) [0]
327	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	306.64 (0.00) [0]
328	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [12/2019]	852.67 (852.67) [852.67]	108.04 (0.00) [0]
329	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [5/2020]	634.32 (634.32) [634.32]	102.33 (0.00) [0]
330	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	274.46 (0.00) [0]
331	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	235.30 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
332	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [6/2020]	11,459.00 (-) [16,580.00]	13,711.00 (5,121.00) [54]
	<u>Petroleum</u>				
333	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (-) [0/0]	588.20 (-) [588.20]	0.94 (0.00) [0]
334	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [9/2019]	3,380.00 (-) [3,380.00]	1,824.73 (0.00) [0]
335	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [8/2019]	327.78 (-) [200.00]	135.09 (-127.78) [16]
336	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	6.30 (0.00) [0]
337	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [10/2020]	906.00 (-) [906.00]	75.19 (0.00) [8]
338	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	105.30 (0.00) [0]
339	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [1,162.56]	354.67 (0.00) [0]
340	REPLACEMENT OF KV SECTION OF KSPL	10/2014	8/2018 (-) [0/0]	279.00 (-) [279.00]	200.05 (0.00) [0]
341	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [2/2021]	225.54 (-) [225.54]	0.00 (0.00) [0]
	<u>Power</u>				
342	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPF AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [9/2019]	193.14 (-) [193.14]	72.38 (0.00) [3]
343	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (9/2019) [9/2019]	175.64 (-) [175.64]	92.78 (0.00) [12]
344	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	11/2017 (-) [4/2019]	330.00 (-) [332.00]	331.46 (2.00) [0]
	<u>Railways</u>				

345	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	902.37 (106.70) [0]
346	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2021) [3/2021]	829.74 (1,215.34) [1,310.23]	1,294.00 (480.49) [12]
347	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (3/2017) [3/2017]	117.36 (196.95) [202.35]	404.70 (84.99) [0]
348	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (3/2020) [3/2020]	551.51 (809.07) [809.07]	596.89 (257.56) [12]
349	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2022) [3/2022]	318.24 (321.62) [321.62]	125.76 (3.38) [120]
350	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (3/2021) [3/2021]	691.84 (663.29) [663.29]	81.64 (-28.55) [12]
351	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	267.40 (0.00) [0]
352	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
353	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2021) [3/2021]	844.10 (844.10) [844.10]	87.81 (0.00) [-]
354	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	222.83 (0.00) [9]
355	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
356	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2021]	1,548.66 (-) [1,548.66]	1,140.64 (0.00) [0]
357	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2022) [3/2022]	320.66 (858.56) [858.96]	534.00 (538.30) [36]
358	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2021) [3/2021]	1,002.39 (1,002.39) [1,002.39]	348.91 (0.00) [0]
359	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (-) [3/2019]	1,037.15 (-) [160.00]	952.24 (-877.15) [0]
360	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
Road Transport And Highways					
361	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	262.83 (0.00) [-]
362	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [1/2020]	829.97 (-) [829.97]	75.08 (0.00) [-]
363	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [8/2020]	1,958.88 (-) [1,958.88]	1,116.85 (0.00) [2]
364	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,659.71 (0.00) [0]

365	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [12/2019]	364.56 (-) [364.56]	208.94 (0.00) [-]
366	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
367	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	0.00 (0.00) [-]
368	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [1/2021]	2,702.05 (-) [2,702.05]	0.00 (0.00) [-]
369	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	3.06 (0.00) [0]
370	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (-) [962.43]	45.70 (0.00) [0]
371	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	4.37 (0.00) [0]
372	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [8/2019]	998.18 (-) [998.18]	435.25 (0.00) [-]
373	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [9/2019]	723.64 (-) [723.64]	321.67 (0.00) [-]
374	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [10/2019]	834.64 (-) [834.64]	140.44 (0.00) [-]
375	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [8/2019]	763.08 (-) [763.08]	357.12 (0.00) [-]
376	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,187.21 (0.00) [0]
377	JUNAGADH BYPASS	10/2017	10/2017 (-) [11/2019]	232.49 (-) [232.49]	0.00 (0.00) [25]
378	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [12/2018]	953.88 (-) [953.88]	976.79 (0.00) [0]
379	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (-) [1,052.21]	1,080.00 (0.00) [-]
380	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [1/2021]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [-]
381	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [3/2019]	425.60 (-) [425.60]	0.00 (0.00) [0]
382	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	0.05 (0.00) [0]
383	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON	3/2016	2/2016 (-) [0/0]	208.34 (-) [208.34]	112.87 (0.00) [0]
384	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
385	WIDENING FROM TWO LANE TO FOUR LANE WITH	3/2016	2/2017	223.67	112.81

	PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE		(-) [2/2017]	(-) [223.67]	(0.00) [0]
	<u>Urban Development</u>				
386	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
387	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	72.95 (0.00) [0]
	<u>Health And Family Welfare</u>				
388	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [0/0]	505.58 (-) [523.00]	508.29 (17.42) [0]
	<u>Petroleum</u>				
389	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (-) [1/2021]	909.00 (-) [909.00]	13.11 (0.00) [0]
390	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [7/2019]	3,529.00 (-) [3,529.00]	1,453.91 (0.00) [0]
391	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	6.82 (0.00) [0]
392	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	58.20 (0.00) [0]
393	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (-) [2/2020]	598.00 (-) [598.00]	13.44 (0.00) [0]
394	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (-) [6/2021]	278.60 (-) [278.60]	0.00 (0.00) [0]
395	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	161.68 (0.00) [0]
396	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (-) [8/2020]	286.42 (-) [286.42]	0.99 (0.00) [0]
	<u>Railways</u>				
397	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	4/2013	/ (-) [3/2025]	400.00 (-) [400.00]	0.00 (0.00) [-]
398	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2020]	346.32 (-) [300.00]	285.74 (-46.32) [12]
399	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [3/2021]	287.00 (-) [694.00]	189.71 (407.00) [111]
	<u>Road Transport And Highways</u>				
400	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [8/2019]	602.95 (-) [602.95]	417.86 (0.00) [38]
401	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [7/2019]	574.28 (-) [574.28]	448.92 (0.00) [12]
402	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [9/2019]	639.79 (-) [552.90]	480.73 (-86.89) [-6]
403	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019	2,128.72	971.24

			(-) [4/2019]	(-) [2,128.72]	(0.00) [0]
404	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (-) [5/2019]	276.01 (-) [276.01]	155.40 (0.00) [0]
405	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [9/2019]	247.25 (-) [247.25]	139.25 (0.00) [6]
406	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [11/2019]	248.97 (-) [248.97]	241.69 (0.00) [6]
407	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [0/0]	1,484.30 (-) [1,484.30]	0.00 (0.00) [0]
408	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [5/2019]	1,004.67 (-) [1,004.67]	0.00 (0.00) [0]
409	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [118]
410	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
411	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
412	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [3/2020]	1,108.00 (-) [2,288.00]	3,978.72 (1,180.00) [100]
413	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [3/2020]	551.58 (-) [551.58]	0.00 (0.00) [-]
414	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [3/2020]	275.12 (-) [275.12]	0.00 (0.00) [-]
415	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI	3/2018	/ (-) [3/2020]	307.79 (-) [307.79]	0.00 (0.00) [-]
416	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [6/2020]	181.78 (-) [181.78]	0.00 (0.00) [-]
417	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [3/2020]	198.05 (-) [198.05]	0.00 (0.00) [-]
418	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [0/0]	795.50 (-) [795.50]	0.00 (0.00) [0]
419	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [0/0]	634.70 (-) [634.70]	0.00 (0.00) [0]
	HIMACHAL PRADESH				
	Petroleum				
420	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019 (-) [6/2019]	151.00 (-) [151.00]	147.35 (0.00) [-3]
	Power				
421	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2021]	3,919.59 (-) [9,997.11]	7,399.82 (6,077.52) [147]
	Railways				
422	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026	2,966.99	366.38

			(-) [12/2026]	(-) [7,000.00]	(4,033.01) [0]
	<u>Road Transport And Highways</u>				
423	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [6/2019]	273.20 (-) [273.20]	256.25 (0.00) [4]
424	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	704.29 (0.00) [15]
425	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016 (-) [4/2019]	1,916.79 (-) [1,916.79]	1,948.92 (0.00) [0]
426	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2019]	934.46 (-) [934.46]	452.30 (0.00) [0]
427	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH- 22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [5/2021]	478.74 (-) [478.74]	0.00 (0.00) [-]
428	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [7/2020]	1,273.71 (-) [1,273.71]	0.00 (0.00) [-]
429	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [11/2019]	447.75 (-) [447.75]	179.17 (0.00) [-]
430	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (-) [1,583.18]	234.67 (0.00) [-]
	<u>Urban Development</u>				
431	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [10/2019]	270.83 (-) [270.83]	199.91 (0.00) [59]
	<u>JAMMU AND KASHMIR</u>				
	<u>Power</u>				
432	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [12/2023]	8,112.12 (-) [8,112.12]	1,135.82 (0.00) [44]
	<u>Railways</u>				
433	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2021]	2,500.00 (27,949.00) [27,949.00]	18,512.58 (25,449.00) [229]
	<u>Road Transport And Highways</u>				
434	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (-) [1,471.75]	305.75 (0.00) [-]
435	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH- 1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	301.68 (0.00) [18]
436	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [10/2019]	2,136.97 (-) [2,136.97]	1,154.18 (0.00) [10]
437	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]
438	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	3,986.82 (0.00) [0]
439	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [3/2019]	1,987.00 (-) [1,987.00]	2,580.88 (0.00) [0]
440	SRINAGAR TO BANIHAL	6/2011	6/2014 (-)	1,100.70 (-)	2,075.87 (0.00)

			[0/0]	[1,100.70]	[0]
441	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [7/2019]	253.44 (-) [253.44]	0.00 (0.00) [0]
442	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	30.43 (0.00) [0]
443	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	0.00 (0.00) [0]
	JHARKHAND				
	Coal				
444	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	186.88 (0.00) [0]
445	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	90.13 (0.00) [0]
446	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2021]	163.51 (-) [163.51]	106.41 (0.00) [120]
447	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	87.14 (0.00) [0]
448	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
449	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2021]	162.46 (-) [162.46]	89.82 (0.00) [84]
450	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [4/2018]	289.45 (-) [289.45]	228.71 (0.00) [0]
451	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2022]	706.40 (-) [706.40]	336.64 (0.00) [116]
452	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [4/2019]	1,230.27 (-) [1,230.27]	354.29 (0.00) [0]
453	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2018]	339.88 (-) [339.88]	12.08 (0.00) [0]
454	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.24 (0.00) [0]
455	NORTH URIMARI OCP (3.0 MTY)	12/2007	3/2012 (-) [7/2019]	179.87 (-) [179.87]	163.23 (0.00) [88]
456	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2018]	269.82 (-) [269.82]	180.52 (0.00) [0]
457	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2021]	510.85 (-) [510.85]	359.23 (0.00) [60]
458	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2021]	264.68 (-) [264.68]	179.87 (0.00) [108]
	Petroleum				
459	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	17.78 (0.00) [0]

460	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	40.86 (0.00) [0]
461	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	42.87 (0.00) [0]
462	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	658.62 (-) [910.23]	303.30 (251.61) [-12]
463	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	4/2011	5/2015 (-) [0/0]	191.96 (-) [191.96]	76.28 (0.00) [0]
	Power				
464	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (9/2019) [9/2021]	14,366.58 (-) [15,164.05]	8,852.51 (797.47) [27]
465	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,268.00 (314.04) [0]
466	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2023]	18,668.00 (-) [18,668.00]	1,780.00 (0.00) [0]
	Railways				
467	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2021]	1,724.20 (-) [1,724.20]	332.04 (0.00) [9]
468	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	156.48 (0.00) [-3]
469	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (3,031.00) [3,376.00]	3,180.37 (2,342.93) [-]
470	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2021]	459.91 (-) [459.91]	456.83 (0.00) [-]
471	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	/ (-) [6/2020]	258.20 (358.68) [358.68]	231.84 (100.48) [-]
472	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (11/2019) [11/2019]	148.77 (-) [377.00]	174.82 (228.23) [35]
	Road Transport And Highways				
473	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [6/2019]	239.68 (-) [235.90]	89.96 (-3.78) [-9]
474	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [6/2019]	165.50 (-) [172.16]	107.13 (6.66) [-9]
475	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [0/0]	1,005.08 (-) [1,005.08]	0.00 (0.00) [0]
476	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [7/2019]	997.15 (-) [997.15]	712.41 (0.00) [4]
477	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
478	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [1/2020]	323.72 (-) [323.72]	192.02 (0.00) [17]
479	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015	1,479.00	740.26

			(-) [0/0]	(-) [1,479.00]	(0.00) [0]
480	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [6/2020]	212.99 (-) [212.99]	59.56 (0.00) [0]
481	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
482	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [12/2019]	458.03 (-) [458.03]	158.64 (0.00) [-]
	Steel				
483	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	2/2014	9/2017 (-) [0/0]	4,749.00 (-) [4,749.00]	110.95 (0.00) [0]
484	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (6/2019) [6/2019]	1,154.18 (-) [1,154.18]	922.73 (0.00) [18]
485	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (6/2020) [6/2020]	1,034.01 (-) [1,034.01]	431.23 (0.00) [32]
486	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (6/2020) [6/2020]	262.87 (-) [262.87]	99.65 (0.00) [12]
	Urban Development				
487	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [9/2020]	171.86 (-) [171.86]	80.06 (0.00) [54]
488	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
489	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
490	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
491	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	KARNATAKA				
	Petroleum				
492	BSVI UPGRADATION	9/2016	12/2019 (7/2020) [7/2020]	1,810.00 (1,810.00) [1,810.00]	643.05 (0.00) [7]
493	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (6/2019) [10/2018]	224.00 (207.00) [185.00]	164.61 (-39.00) [0]
494	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	606.89 (93.00) [0]
495	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (-) [8/2019]	135.00 (170.70) [170.70]	152.13 (35.70) [5]
496	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	0.30 (0.00) [0]
497	SEA WATER DESALINATION PLANT	11/2017	3/2020 (4/2020) [9/2020]	581.00 (-) [621.00]	66.19 (40.00) [6]
498	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012	993.00	1,549.85

			(-) [0/0]	(-) [1,693.00]	(700.00) [0]
	Power				
499	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [12/2019]	445.89 (-) [445.89]	272.00 (0.00) [10]
	Railways				
500	ARSIKERE-TUMKUR	3/2015	3/2020 (-) [3/2020]	578.00 (-) [578.00]	509.07 (0.00) [0]
501	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2023]	986.30 (-) [986.30]	297.70 (0.00) [93]
502	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
503	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [367.77]	0.00 (40.52) [-]
504	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [692.43]	0.00 (134.43) [-]
505	GADAG-WADI NL	4/2013	12/2018 (-) [12/2024]	2,841.84 (-) [2,841.84]	113.63 (0.00) [72]
506	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,900.00]	1,541.10 (773.00) [0]
507	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [3/2021]	1,156.94 (-) [1,140.93]	786.13 (-16.01) [12]
508	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [2,135.00]	144.76 (-180.00) [-]
509	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (-) [889.52]	438.39 (244.74) [36]
510	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	28.51 (0.00) [93]
511	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
512	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
513	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [1,801.01]	44.36 (0.00) [-]
514	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (-) [348.85]	0.35 (0.00) [-]
	Road Transport And Highways				
515	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (-) [6/2020]	1,167.42 (-) [1,167.42]	238.96 (0.00) [15]
516	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	0.00 (0.00) [0]
517	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-)	1,655.01 (-)	1,867.51 (0.00)

			[12/2020]	[1,655.01]	[52]
518	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/ (-) [0/0]	720.69 (-) [720.69]	99.03 (0.00) [0]
519	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [11/2020]	701.40 (-) [701.40]	29.48 (0.00) [20]
520	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	12.95 (0.00) [20]
521	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]
522	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [5/2020]	171.60 (-) [171.60]	0.86 (0.00) [24]
523	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [11/2019]	1,388.00 (-) [1,388.00]	1,098.56 (0.00) [15]
524	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	525.24 (0.00) [0]
525	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [12/2019]	946.00 (-) [946.00]	818.53 (0.00) [18]
526	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [10/2018]	325.86 (-) [325.86]	62.54 (0.00) [0]
527	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [2/2017]	175.50 (-) [175.50]	86.54 (0.00) [0]
528	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [6/2019]	159.97 (-) [159.97]	0.00 (0.00) [0]
529	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [8/2016]	471.16 (-) [471.16]	128.32 (0.00) [0]
530	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
531	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	566.10 (440.84) [3]
532	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [7/2020]	831.58 (-) [1,177.00]	513.98 (345.42) [4]
533	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,177.80]	0.00 (0.00) [0]
534	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [1,995.34]	0.00 (0.00) [-]
535	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
536	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
537	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [12/2019]	709.00 (-) [709.00]	433.12 (0.00) [27]

538	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [12/2020]	950.69 (-) [950.69]	782.81 (0.00) [16]
539	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [3/2017]	396.96 (-) [396.96]	113.98 (0.00) [0]
540	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [3/2017]	314.90 (-) [314.90]	104.40 (0.00) [0]
541	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [1/2017]	367.44 (-) [367.44]	61.95 (0.00) [0]
542	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [2/2017]	329.01 (-) [329.01]	135.50 (0.00) [0]
543	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [10/2018]	191.60 (-) [191.60]	26.24 (0.00) [0]
544	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [8/2019]	291.49 (-) [291.49]	130.00 (0.00) [24]
545	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [9/2017]	166.67 (-) [166.67]	117.05 (0.00) [0]
546	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [1/2019]	175.20 (-) [175.20]	113.38 (0.00) [0]
547	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [1/2019]	297.30 (-) [297.30]	0.00 (0.00) [0]
548	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGECHARA SECTION	1/2018	7/2018 (-) [7/2018]	159.70 (-) [159.70]	21.16 (0.00) [0]
549	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [5/2019]	165.67 (-) [165.67]	87.63 (0.00) [0]
550	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [5/2019]	159.12 (-) [159.12]	96.22 (0.00) [0]
	Urban Development				
551	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
552	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
553	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
554	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [9/2020]	246.31 (-) [246.31]	62.56 (0.00) [7]
	KERALA				
	Petroleum				
555	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [6/2020]	1,112.00 (-) [1,112.00]	467.00 (0.00) [12]
556	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [0/0]	607.06 (-) [714.25]	354.84 (107.19) [0]
557	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE	2/2016	2/2020	3,313.00	816.62

	BSVI MS AT KOCHI REFINERY		(-) [10/2020]	(-) [3,288.96]	(-24.04) [8]
558	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (-) [11/2019]	4,588.29 (-) [5,245.96]	3,283.70 (657.67) [15]
559	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	14.14 (0.00) [0]
	Railways				
560	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (2,815.62) [2,815.62]	262.37 (1,249.62) [0]
561	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (189.24) [189.24]	6.72 (0.00) [0]
562	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (252.96) [252.96]	8.50 (0.00) [0]
563	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
564	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (6/2022) [0/0]	1,431.90 (1,431.90) [1,431.90]	61.69 (0.00) [0]
565	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (828.50) [828.50]	0.08 (-171.50) [0]
	Road Transport And Highways				
566	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [10/2019]	845.24 (-) [845.24]	788.62 (0.00) [-]
567	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [1/2020]	804.97 (-) [804.97]	402.47 (0.00) [19]
568	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,124.11]	256.47 (0.00) [33]
569	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,424.77]	0.00 (0.00) [0]
570	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [9/2019]	255.75 (348.00) [348.43]	290.12 (92.68) [24]
571	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [88]
	Shipping And Ports				
572	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	5/2016	5/2020 (-) [5/2020]	970.00 (-) [970.00]	109.97 (0.00) [0]
573	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA	7/2016	5/2021 (-) [5/2021]	1,799.00 (-) [1,799.00]	21.00 (0.00) [0]
	Urban Development				
574	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
575	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	86.04 (0.00) [89]
576	KOCHI METRO RAIL PROJECT	7/2012	7/2017	5,181.79	5,188.00

			(-) [12/2019]	(-) [5,687.79]	(506.00) [29]
	MADHYA PRADESH				
	Coal				
577	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	112.60 (0.00) [0]
578	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
579	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
580	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2021]	1,186.64 (-) [203.82]	117.55 (-982.82) [-24]
581	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	18.45 (0.00) [0]
582	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	94.84 (0.00) [0]
583	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	255.65 (0.00) [0]
584	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	47.59 (0.00) [0]
585	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	26.61 (0.00) [0]
586	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	115.41 (0.00) [0]
587	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
	Petroleum				
588	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [8/2020]	236.00 (-) [236.00]	21.97 (0.00) [2]
	Power				
589	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [1,587.16]	298.76 (-517.05) [0]
590	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (3/2020) [3/2020]	11,638.55 (-) [12,865.92]	11,322.86 (1,227.37) [26]
591	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [1/2020]	9,870.51 (-) [11,148.86]	8,127.53 (1,278.35) [0]
	Railways				
592	ANUPPUR-KATNI	4/2015	12/2021 (12/2021) [12/2021]	1,370.00 (1,370.00) [1,370.00]	253.18 (0.00) [0]
593	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.85 (-) [1,485.85]	994.43 (0.00) [0]
594	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (10/2019) [10/2019]	383.79 (1,413.76) [1,413.76]	1,309.02 (1,029.97) [-]

595	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (3/2020) [6/2020]	585.93 (737.72) [1,300.44]	626.21 (714.51) [16]
596	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (6/2021) [6/2021]	700.00 (603.69) [603.69]	64.48 (-96.31) [12]
597	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (3/2022) [3/2022]	1,763.93 (1,763.93) [1,763.93]	624.49 (0.00) [24]
598	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (9/2022) [9/2022]	582.13 (1,247.64) [1,247.64]	154.63 (665.51) [6]
599	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (3/2023) [3/2023]	2,478.23 (-) [2,478.23]	367.59 (0.00) [12]
600	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [2/2020]	174.00 (-) [174.00]	149.66 (0.00) [11]
601	RAMGANJMUHDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2023) [3/2023]	424.60 (2,909.99) [2,909.99]	1,027.12 (2,485.39) [24]
602	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2023) [3/2023]	3,503.69 (3,338.15) [3,860.40]	1,577.87 (356.71) [12]
	Road Transport And Highways				
603	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [11/2019]	191.21 (-) [191.21]	68.26 (0.00) [0]
604	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (-) [1/2020]	249.05 (-) [249.05]	100.10 (0.00) [18]
605	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [6/2019]	359.00 (359.00) [359.00]	149.80 (0.00) [0]
606	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	0.00 (0.00) [0]
607	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (-) [11/2019]	392.33 (-) [392.33]	196.99 (0.00) [20]
608	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [3/2019]	227.49 (-) [227.49]	100.96 (0.00) [0]
609	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]
610	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [0/0]	990.61 (-) [990.61]	0.00 (0.00) [0]
611	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
612	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2020]	390.51 (-) [390.51]	178.32 (0.00) [-]
613	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	5/2015 (-) [0/0]	704.26 (-) [704.26]	5.21 (0.00) [0]
614	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [6/2020]	205.05 (-) [205.05]	62.60 (0.00) [39]

615	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (-) [6/2019]	1,583.79 (-) [1,583.79]	1,568.11 (0.00) [5]
616	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [8/2020]	960.24 (-) [960.24]	0.00 (0.00) [-]
617	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	439.07 (0.00) [0]
618	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [12/2018]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
619	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [6/2019]	928.83 (-) [928.83]	588.21 (0.00) [-]
620	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [5/2019]	794.30 (-) [794.30]	492.23 (0.00) [0]
621	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [3/2019]	795.76 (-) [795.76]	564.36 (0.00) [0]
622	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [6/2019]	810.22 (-) [810.22]	586.36 (0.00) [-]
623	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	274.24 (0.00) [27]
624	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	0.00 (0.00) [0]
625	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (-) [2/2020]	957.54 (-) [957.54]	412.39 (0.00) [0]
626	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [5/2020]	497.05 (-) [881.05]	507.45 (384.00) [36]
627	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
628	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,342.77 (0.00) [0]
629	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (-) [1/2020]	628.45 (-) [628.45]	207.68 (0.00) [0]
630	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [8/2019]	410.72 (-) [410.72]	0.00 (0.00) [52]
631	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [7/2020]	169.63 (-) [169.63]	7.10 (0.00) [28]
632	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [7/2019]	178.23 (-) [178.23]	114.16 (0.00) [10]
633	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (-) [11/2019]	287.34 (-) [287.34]	148.65 (0.00) [10]
634	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [11/2019]	877.79 (-) [877.79]	356.56 (0.00) [5]
635	REHABILITATION AND UPGRADATION OF INTERMEDIATE	11/2017	2/2018	235.91	73.09

	LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID		(-) [11/2019]	(-) [235.91]	(0.00) [21]
636	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [2/2020]	809.16 (-) [809.16]	173.16 (0.00) [19]
637	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
638	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [3/2020]	954.43 (-) [954.43]	298.00 (0.00) [54]
639	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [2/2020]	511.83 (-) [511.83]	219.26 (0.00) [30]
640	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	254.17 (-) [254.17]	115.54 (0.00) [21]
641	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	233.04 (-) [233.04]	93.96 (0.00) [20]
642	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [4/2020]	279.44 (-) [279.44]	50.39 (0.00) [25]
643	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	166.21 (-) [166.21]	14.37 (0.00) [22]
644	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	184.62 (-) [184.62]	47.70 (0.00) [21]
645	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	214.69 (-) [214.69]	15.22 (0.00) [20]
646	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	217.22 (-) [217.22]	4.45 (0.00) [22]
647	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [12/2019]	162.56 (-) [162.56]	66.95 (0.00) [21]
648	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [9/2019]	373.82 (-) [373.82]	116.33 (0.00) [0]
	Urban Development				
649	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	33.82 (0.00) [0]
650	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	32.89 (0.00) [0]
	MAHARASHTRA				
	Coal				
651	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	17.71 (44.53) [12]
652	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	254.72 (0.00) [0]
653	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	168.92 (0.00) [0]
654	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-)	727.28 (-)	258.40 (0.00)

			[3/2025]	[727.28]	[0]
655	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	119.73 (221.74) [0]
656	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2019]	304.52 (-) [304.52]	153.29 (0.00) [0]
657	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	413.13 (0.00) [0]
658	GOKUL	11/2014	3/2018 (-) [3/2018]	267.67 (-) [267.67]	208.78 (0.00) [0]
659	KAMPTTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2024]	277.65 (-) [313.34]	115.28 (35.69) [36]
660	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	319.81 (0.00) [0]
661	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	175.30 (0.00) [0]
662	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2019]	295.56 (-) [295.56]	123.60 (0.00) [0]
663	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	213.24 (0.00) [0]
664	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	121.74 (0.00) [0]
	Fertilisers				
665	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	92.10 (0.00) [0]
666	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (-) [8/2019]	197.79 (-) [209.44]	159.41 (11.65) [33]
	Health And Family Welfare				
667	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [2/2020]	582.99 (-) [582.99]	112.97 (0.00) [-]
668	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [10/2019]	274.19 (-) [274.19]	169.93 (0.00) [7]
	Petroleum				
669	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	58.33 (0.00) [0]
670	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (-) [11/2019]	968.61 (-) [1,033.95]	833.51 (65.34) [0]
671	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	27.66 (0.00) [0]
672	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	28.55 (0.00) [3]
673	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	20.85 (0.00) [9]

674	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2019) [12/2019]	861.79 (-) [1,683.06]	1,265.01 (821.27) [79]
675	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (3/2020) [3/2020]	546.15 (565.15) [565.15]	425.96 (19.00) [4]
676	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (-) [11/2019]	511.30 (-) [511.30]	406.35 (0.00) [0]
677	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,292.46]	45.81 (0.00) [0]
678	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (12/2021) [12/2021]	4,006.83 (-) [4,475.92]	2,555.11 (469.09) [7]
679	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (-) [4,619.94]	4,313.38 (0.00) [27]
680	HEERA REDEVELOPMENT - PHASE III	5/2019	12/2021 (-) [12/2021]	2,494.68 (-) [2,494.68]	0.00 (0.00) [0]
681	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	315.44 (0.00) [0]
682	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019) [5/2019]	2,059.63 (2,665.65) [2,665.65]	1,906.55 (606.02) [0]
683	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	887.73 (0.00) [0]
684	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2020) [5/2020]	3,190.69 (-) [3,247.19]	2,180.79 (56.50) [25]
685	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	153.11 (0.00) [0]
686	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (-) [3/2022]	3,228.80 (-) [3,228.80]	370.84 (0.00) [0]
687	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (12/2019) [12/2019]	6,068.80 (-) [5,296.93]	4,748.30 (-771.87) [8]
688	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	2/2019	4/2021 (5/2021) [5/2021]	3,660.71 (3,740.05) [3,740.05]	126.66 (79.34) [1]
689	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [3/2020]	4,199.00 (5,060.00) [5,060.00]	2,068.39 (861.00) [0]
690	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	2,185.47 (0.00) [14]
691	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	434.78 (0.00) [0]
692	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	105.42 (0.00) [0]
	Power				
693	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]

	Railways				
694	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (12/2019) [12/2019]	184.06 (-) [305.00]	260.45 (120.94) [9]
695	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2022]	2,271.50 (-) [3,712.50]	2,211.41 (1,441.00) [12]
696	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2021]	495.44 (1,781.98) [2,973.73]	1,394.89 (2,478.29) [204]
697	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	66.23 (205.27) [0]
698	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	713.48 (-) [1,950.00]	1,803.73 (1,236.52) [0]
699	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
700	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
701	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (-) [2,449.91]	140.79 (0.00) [0]
702	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2022]	792.89 (-) [792.89]	294.10 (0.00) [12]
703	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	65.16 (0.00) [24]
704	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2019]	305.00 (-) [305.00]	259.90 (0.00) [9]
705	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
706	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (3/2021) [3/2021]	5,300.00 (918.53) [918.53]	256.68 (-4,381.47) [84]
707	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2022]	3,627.47 (3,627.00) [3,627.47]	480.35 (0.00) [-24]
708	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
709	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (3/2023) [3/2023]	1,908.51 (2,686.63) [2,686.63]	393.46 (778.12) [0]
710	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
711	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
712	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
713	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (3/2023) [3/2023]	229.00 (403.00) [860.92]	39.80 (631.92) [15]

714	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	48.42 (0.00) [12]
715	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,272.19]	256.28 (0.00) [12]
716	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,180.11 (0.00) [0]
717	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	215.95 (0.00) [24]
	Road Transport And Highways				
718	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [5/2019]	2,288.18 (-) [2,288.18]	0.00 (0.00) [0]
719	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [5/2019]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
720	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [7/2019]	972.50 (-) [972.50]	1,497.56 (0.00) [24]
721	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	55.06 (0.00) [-]
722	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [4/2021]	621.00 (-) [621.00]	212.24 (0.00) [-]
723	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [5/2020]	923.04 (-) [923.04]	708.62 (0.00) [42]
724	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
725	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,071.61]	0.00 (0.00) [-]
726	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [11/2019]	446.17 (-) [446.17]	38.95 (0.00) [8]
727	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [8/2020]	1,098.06 (-) [1,160.64]	1,082.97 (62.58) [5]
728	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	726.85 (0.00) [0]
729	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	0.00 (0.00) [0]
730	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [9/2019]	400.25 (-) [400.25]	64.89 (0.00) [6]
731	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [7/2021]	1,064.88 (-) [1,064.88]	0.00 (0.00) [-]
732	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [11/2020]	1,059.73 (-) [1,071.00]	480.96 (11.27) [44]
733	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [5/2020]	1,030.44 (-) [1,065.51]	1,027.16 (35.07) [2]

734	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (-) [1,043.28]	1,094.73 (54.94) [5]
735	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (-) [5/2020]	505.00 (-) [505.00]	347.91 (0.00) [24]
736	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [8/2019]	422.38 (422.38) [422.38]	136.58 (0.00) [0]
737	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [8/2019]	955.40 (-) [955.40]	301.50 (0.00) [0]
738	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [2/2020]	211.42 (-) [211.42]	130.85 (0.00) [12]
739	AKOLA TO AKOT	1/2017	6/2019 (-) [6/2019]	313.95 (-) [313.95]	31.05 (0.00) [0]
740	AKOT TO ANJANGAON	1/2017	6/2019 (-) [6/2019]	245.77 (246.00) [245.77]	95.98 (0.00) [0]
741	AMDNI TO SAONER	1/2017	6/2019 (-) [8/2019]	396.91 (396.91) [396.91]	281.48 (0.00) [2]
742	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2020]	426.06 (426.00) [426.06]	64.97 (0.00) [0]
743	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [12/2019]	309.94 (310.00) [309.94]	19.32 (0.00) [0]
744	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [6/2019]	456.32 (-) [456.32]	79.30 (0.00) [0]
745	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	22.27 (0.00) [0]
746	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [4/2020]	241.69 (242.00) [241.69]	24.29 (0.00) [0]
747	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	30.00 (0.00) [31]
748	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [11/2019]	259.55 (260.00) [259.55]	120.00 (0.00) [0]
749	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [6/2019]	392.83 (393.00) [392.83]	254.60 (0.00) [0]
750	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2021]	743.21 (743.21) [743.21]	52.87 (0.00) [0]
751	BHOKAR TO SARSAM	2/2017	7/2019 (-) [7/2019]	295.09 (-) [295.99]	155.64 (0.90) [0]
752	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [7/2019]	178.26 (-) [178.26]	81.95 (0.00) [0]
753	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [12/2019]	206.97 (207.00) [206.97]	46.89 (0.00) [0]
754	CHIKALI TO DHAD	3/2018	12/2019	189.46	21.00

			(-) [12/2019]	(189.00) [189.46]	(0.00) [0]
755	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [10/2019]	548.03 (548.00) [548.03]	229.00 (0.00) [4]
756	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2019]	393.10 (393.10) [393.10]	83.97 (0.00) [0]
757	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	156.72 (0.00) [0]
758	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	5.00 (0.00) [-]
759	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (-) [12/2020]	649.50 (-) [649.50]	203.78 (0.00) [21]
760	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [11/2020]	291.53 (-) [291.53]	7.51 (0.00) [-]
761	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [9/2019]	244.90 (-) [244.90]	219.09 (0.00) [4]
762	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH- 53 (OLD NH-6)	3/2018	/ (-) [11/2020]	289.21 (-) [289.21]	12.80 (0.00) [-]
763	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (-) [12/2020]	593.26 (-) [593.26]	484.48 (0.00) [31]
764	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
765	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [6/2020]	531.13 (-) [531.13]	163.10 (0.00) [25]
766	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	52.00 (0.00) [0]
767	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
768	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [2/2020]	247.02 (-) [157.49]	0.00 (-89.53) [-1]
769	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (-) [6/2020]	414.51 (-) [414.00]	529.62 (-0.51) [25]
770	DAHEGAON TO KUHI	1/2017	6/2019 (-) [6/2019]	228.89 (228.89) [228.89]	90.00 (0.00) [0]
771	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [12/2019]	182.63 (-) [182.63]	58.15 (0.00) [0]
772	DEORI TO AMGAON	1/2017	5/2019 (-) [5/2020]	409.62 (410.00) [409.62]	126.78 (0.00) [12]
773	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	84.46 (0.00) [0]
774	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM	3/2017	3/2020 (-)	296.19 (-)	248.60 (-42.19)

	723.000)		[9/2019]	[254.00]	[-6]
775	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [12/2019]	336.21 (336.00) [336.21]	58.66 (0.00) [0]
776	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [2/2020]	217.14 (217.00) [217.14]	52.77 (0.00) [0]
777	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [6/2020]	391.06 (391.00) [391.06]	100.00 (0.00) [12]
778	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [6/2019]	456.45 (-) [456.45]	66.10 (0.00) [0]
779	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
780	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [642.13]	288.84 (0.00) [-]
781	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [2/2019]	1,871.34 (-) [1,871.34]	3,424.19 (0.00) [0]
782	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [5/2020]	904.16 (-) [904.16]	607.37 (0.00) [3]
783	GADCHIROLI TO MUL	12/2016	6/2019 (-) [6/2019]	484.15 (-) [484.15]	127.31 (0.00) [0]
784	HELWAK TO KARAD	2/2017	7/2019 (-) [7/2019]	416.99 (-) [416.99]	100.40 (0.00) [0]
785	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [12/2019]	294.87 (295.00) [294.87]	31.30 (0.00) [0]
786	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [12/2019]	355.17 (355.17) [355.17]	141.87 (0.00) [5]
787	INDAPUR TO VADPALE	1/2017	12/2019 (-) [3/2020]	1,202.52 (1,202.52) [1,202.52]	652.90 (0.00) [3]
788	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [11/2019]	461.96 (461.96) [461.96]	116.43 (0.00) [0]
789	JALGAON TO BHADGAON	1/2018	11/2019 (-) [11/2019]	307.54 (308.00) [307.54]	75.59 (0.00) [0]
790	JALGAON TO NANDURA	3/2018	12/2019 (-) [12/2019]	177.84 (177.00) [177.84]	35.69 (0.00) [0]
791	JALKOT TO TOGRI	7/2018	8/2020 (-) [8/2020]	299.92 (300.00) [299.92]	0.00 (0.00) [0]
792	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (356.66) [356.66]	14.88 (0.00) [0]
793	KAIJ TO KUSALAM	1/2017	7/2019 (-) [7/2019]	554.78 (554.78) [554.78]	136.90 (0.00) [0]
794	KALMAB TO RALEGAON	1/2017	6/2019 (-) [6/2019]	467.78 (-) [467.78]	294.91 (0.00) [0]

795	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (1,338.13) [1,338.13]	959.51 (0.00) [0]
796	KANTE TO WAKED	3/2016	11/2019 (-) [11/2019]	1,230.02 (1,230.02) [1,230.02]	609.61 (0.00) [0]
797	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [6/2020]	407.19 (407.00) [407.19]	12.00 (0.00) [12]
798	KARAD TO TAGAON	1/2017	6/2019 (-) [6/2020]	537.81 (538.00) [537.81]	68.97 (0.00) [12]
799	KARAD TO VITA	1/2018	12/2019 (-) [12/2019]	344.85 (245.00) [344.85]	39.04 (0.00) [0]
800	KARWANDI TO RAJURI	3/2018	12/2019 (-) [12/2019]	276.95 (277.00) [276.95]	44.47 (0.00) [0]
801	KATOL TO WARUD	1/2017	6/2019 (-) [8/2019]	463.62 (664.00) [463.62]	230.34 (0.00) [2]
802	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [12/2019]	249.29 (-) [249.29]	32.20 (0.00) [0]
803	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [12/2019]	203.21 (203.00) [203.21]	86.79 (0.00) [7]
804	KHERDA TO NAGZARI	3/2018	12/2019 (-) [12/2019]	181.30 (-) [181.30]	27.50 (0.00) [0]
805	KOLDE TO KHETIYA	1/2017	7/2019 (-) [7/2019]	509.18 (-) [509.18]	157.93 (0.00) [0]
806	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [4/2020]	281.78 (282.00) [281.78]	0.00 (0.00) [12]
807	KOTHARI TO DHANORA	9/2018	8/2020 (-) [8/2020]	301.38 (301.00) [301.38]	0.00 (0.00) [0]
808	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [6/2019]	406.51 (-) [406.51]	406.58 (0.00) [0]
809	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [12/2019]	225.25 (225.00) [225.25]	90.75 (0.00) [0]
810	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [7/2019]	307.63 (-) [307.63]	136.17 (0.00) [0]
811	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [12/2019]	243.45 (244.00) [243.45]	47.02 (0.00) [0]
812	LATUR TO PANGAON	3/2018	12/2019 (-) [12/2019]	336.47 (336.00) [336.47]	60.48 (0.00) [0]
813	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [5/2020]	237.40 (-) [237.40]	7.34 (0.00) [0]
814	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [7/2019]	413.99 (-) [413.99]	310.33 (0.00) [0]
815	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019	256.15	15.50

			(-) [12/2019]	(-) [256.15]	(0.00) [0]
816	MALEGAON TO RISOD	2/2018	12/2019 (-) [12/2019]	303.24 (303.00) [303.24]	50.07 (0.00) [0]
817	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2020]	322.55 (-) [322.55]	145.91 (0.00) [12]
818	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [7/2020]	457.52 (457.52) [457.52]	184.31 (0.00) [12]
819	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [11/2019]	222.13 (222.13) [222.13]	14.36 (0.00) [0]
820	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [8/2019]	228.54 (228.54) [228.54]	87.30 (0.00) [0]
821	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [12/2019]	418.36 (-) [418.36]	70.13 (0.00) [0]
822	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [7/2019]	486.19 (486.19) [486.19]	174.29 (0.00) [0]
823	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [7/2019]	232.77 (-) [232.77]	83.51 (0.00) [0]
824	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [6/2019]	322.48 (322.00) [322.48]	169.08 (0.00) [1]
825	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [7/2019]	488.60 (-) [488.60]	151.71 (0.00) [0]
826	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2019]	341.16 (341.00) [341.16]	159.29 (0.00) [6]
827	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [6/2019]	471.61 (472.00) [471.61]	252.90 (0.00) [0]
828	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [7/2019]	162.34 (-) [162.34]	32.80 (0.00) [0]
829	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [12/2019]	376.72 (377.00) [376.72]	125.81 (0.00) [6]
830	NAGBHID TO ARMORI	9/2016	7/2019 (-) [7/2019]	269.05 (-) [269.05]	173.91 (0.00) [0]
831	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	226.24 (0.00) [0]
832	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [7/2019]	546.00 (-) [546.00]	571.35 (0.00) [0]
833	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [7/2019]	591.66 (-) [591.66]	762.75 (0.00) [0]
834	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2019]	244.04 (244.00) [244.04]	14.94 (0.00) [9]
835	NALDURG TO AKKALKOT	2/2018	12/2019 (-)	274.50 (275.00)	56.39 (0.00)

			[12/2019]	[274.50]	[0]
836	NANDED TO JALKOT	12/2017	9/2019 (-) [9/2019]	456.93 (457.00) [456.93]	37.50 (0.00) [0]
837	NANDGAON TO MORSHI	1/2017	6/2019 (-) [12/2019]	385.87 (386.00) [385.87]	171.75 (0.00) [6]
838	NASHIK TO PETH	12/2015	11/2018 (-) [11/2019]	289.60 (-) [289.60]	78.81 (0.00) [12]
839	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [9/2019]	406.54 (406.54) [406.54]	136.00 (0.00) [0]
840	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [5/2020]	420.63 (421.00) [420.63]	3.60 (0.00) [0]
841	OMREGA TO AUSA	3/2018	12/2019 (-) [12/2019]	272.04 (272.00) [272.04]	72.24 (0.00) [0]
842	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [8/2020]	344.25 (344.00) [344.25]	44.02 (0.00) [0]
843	PAHUR TO BODHWAD	1/2017	5/2020 (-) [5/2020]	244.93 (-) [244.93]	29.23 (0.00) [0]
844	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [6/2019]	341.80 (-) [341.80]	88.00 (0.00) [0]
845	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [12/2019]	227.19 (227.00) [227.19]	37.23 (0.00) [0]
846	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [5/2020]	381.08 (302.00) [381.08]	13.00 (0.00) [0]
847	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [7/2019]	218.38 (-) [218.38]	161.75 (0.00) [0]
848	PANVEL-INDAPUR	12/2011	6/2014 (-) [3/2020]	942.69 (-) [942.69]	750.38 (0.00) [69]
849	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [12/2019]	238.19 (238.00) [238.19]	9.85 (0.00) [0]
850	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2020]	205.72 (205.72) [205.72]	26.42 (0.00) [12]
851	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [11/2019]	983.14 (983.14) [983.14]	655.15 (0.00) [-1]
852	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [7/2019]	420.57 (420.57) [420.57]	121.39 (0.00) [0]
853	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [12/2019]	170.00 (-) [170.00]	15.57 (0.00) [0]
854	PEN TO KHOPOLI	3/2018	3/2018 (-) [12/2019]	301.39 (302.00) [301.39]	0.00 (0.00) [21]
855	PIMPLA TO MANJARUMBHA	1/2017	8/2019 (-) [8/2019]	595.77 (595.77) [595.77]	119.44 (0.00) [0]

856	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [12/2019]	223.46 (-) [223.46]	21.42 (0.00) [0]
857	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [12/2019]	228.31 (-) [228.31]	13.50 (0.00) [0]
858	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [7/2019]	1,724.55 (-) [1,724.55]	2,346.01 (0.00) [76]
859	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [7/2019]	210.81 (-) [210.81]	100.69 (0.00) [0]
860	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	259.50 (0.00) [0]
861	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	83.11 (0.00) [0]
862	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (-) [12/2019]	536.65 (356.00) [536.65]	42.25 (0.00) [0]
863	RISOD TO HINGOLI	2/2018	12/2019 (-) [12/2019]	355.99 (355.99) [355.99]	68.97 (0.00) [0]
864	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [11/2019]	362.96 (362.96) [362.96]	29.83 (0.00) [5]
865	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [12/2019]	415.25 (415.25) [415.25]	36.22 (0.00) [0]
866	SANGOLA TO JATH	1/2018	12/2019 (-) [12/2019]	257.38 (257.00) [257.38]	28.15 (0.00) [0]
867	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [7/2019]	250.46 (-) [250.46]	1,691.63 (0.00) [0]
868	SARSAM TO KOTHARI	2/2016	7/2019 (-) [7/2019]	545.64 (-) [545.64]	45.01 (0.00) [0]
869	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	179.77 (0.00) [0]
870	SATARA TO MHASWAD	1/2017	7/2019 (-) [7/2019]	653.46 (-) [653.46]	167.18 (0.00) [0]
871	SELDOH TO PANVAR	7/2018	5/2020 (-) [5/2020]	404.33 (404.33) [404.33]	14.19 (0.00) [0]
872	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [12/2019]	150.79 (150.79) [150.79]	21.42 (0.00) [0]
873	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [12/2019]	373.10 (373.00) [373.10]	110.43 (0.00) [7]
874	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [7/2019]	211.34 (211.34) [211.34]	94.83 (0.00) [0]
875	SHIRUR TO KHARDA	2/2017	6/2019 (-) [6/2019]	381.77 (-) [381.77]	122.79 (0.00) [0]
876	SHIVUR TO YEOLA	3/2018	12/2019	181.08	7.45

			(-) [12/2019]	(-) [181.08]	(0.00) [0]
877	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [6/2019]	337.46 (-) [337.46]	44.03 (0.00) [0]
878	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (-) [404.94]	71.72 (0.00) [-]
879	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [5/2019]	290.73 (-) [290.73]	174.12 (0.00) [0]
880	TAKARKHED TO JALNA	9/2017	6/2019 (-) [12/2019]	417.90 (418.00) [417.90]	35.26 (0.00) [6]
881	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [12/2019]	264.41 (264.00) [264.41]	23.71 (0.00) [9]
882	TALGAON TO KALMATH	10/2016	3/2020 (-) [3/2020]	904.70 (904.70) [904.70]	604.05 (0.00) [0]
883	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [11/2019]	195.64 (196.00) [195.64]	83.73 (0.00) [0]
884	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [7/2019]	422.02 (422.00) [422.02]	224.01 (0.00) [0]
885	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [3/2020]	1,598.47 (1,598.47) [1,598.47]	746.91 (0.00) [4]
886	VITA TO NAGAJ	3/2018	12/2019 (-) [12/2019]	304.58 (305.00) [304.58]	9.16 (0.00) [0]
887	WADI TO ASOLA	1/2017	9/2019 (-) [9/2020]	363.82 (363.82) [363.82]	92.10 (0.00) [12]
888	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [2/2020]	194.23 (194.00) [194.23]	48.23 (0.00) [0]
889	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [5/2020]	376.19 (376.19) [376.19]	23.03 (0.00) [12]
890	WAKED TO TALEGAON	2/2016	2/2019 (-) [2/2019]	1,244.75 (1,245.00) [1,244.75]	800.00 (0.00) [0]
891	WARDHA TO ARVI	2/2018	4/2020 (-) [4/2020]	313.58 (313.58) [313.58]	8.86 (0.00) [0]
892	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [12/2019]	216.90 (216.90) [216.90]	20.00 (0.00) [0]
893	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [12/2019]	165.51 (-) [165.51]	25.45 (0.00) [0]
894	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
895	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [6/2019]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [64]
	<u>Shipping And Ports</u>				
896	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS	1/2007	12/2010	366.39	411.12

	AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB		(-) [0/0]	(-) [669.46]	(303.07) [0]
	<u>Telecommunications</u>				
897	MADHYA PRADESH ACCESS (LOT1)	8/2017	5/2018 (7/2019) [7/2019]	215.30 (219.60) [219.60]	33.46 (4.30) [14]
898	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (9/2019) [9/2019]	231.80 (240.10) [240.10]	117.63 (8.30) [11]
	<u>Urban Development</u>				
899	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2020) [9/2020]	223.37 (-) [223.37]	27.31 (0.00) [2]
900	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
901	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	5,873.51 (0.00) [21]
902	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (12/2021) [12/2021]	11,420.00 (-) [11,420.00]	2,568.80 (0.00) [1]
903	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	6/2010	3/2012 (-) [6/2019]	205.00 (-) [205.00]	156.21 (0.00) [87]
	<u>Water Resources</u>				
904	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2019]	233.57 (-) [233.57]	32.20 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
905	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
906	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	8,818.98 (9,354.83) [108]
	<u>Road Transport And Highways</u>				
907	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	93.52 (-59.80) [36]
	<u>Urban Development</u>				
908	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
909	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
910	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.67 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
911	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [7/2019]	306.28 (-) [306.28]	37.86 (0.00) [2]
912	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-)	479.20 (-)	475.02 (0.00)

			[9/2019]	[479.20]	[16]
913	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	<u>Urban Development</u>				
914	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
915	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (-) [5,021.45]	2,933.84 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
916	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	296.28 (182.95) [116]
917	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
918	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
919	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
920	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
921	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
922	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
923	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
924	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
925	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
926	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	789.85 (368.26) [105]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
927	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	20.86 (0.00) [0]
928	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	150.04 (0.00) [0]
929	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	58.04 (0.00) [0]
	<u>Heavy Industry</u>				
930	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	4/2011	9/2011 (6/2019)	1,718.00 (3,727.30)	3,182.10 (2,009.30)

			[3/2020]	[3,727.30]	[102]
	Petroleum				
931	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
932	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (3,027.90) [3,027.90]	759.67 (1,204.90) [0]
933	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	142.82 (0.00) [0]
934	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	935.94 (0.00) [0]
935	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,248.16 (0.00) [0]
936	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,327.89 (0.00) [0]
937	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	600.15 (0.00) [0]
938	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [10/2019]	890.00 (-) [887.00]	598.85 (-3.00) [0]
939	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (-) [2/2022]	2,915.00 (2,915.00) [3,049.47]	2,291.18 (134.47) [110]
940	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [12/2020]	2,881.40 (-) [2,000.00]	1,237.86 (-881.40) [0]
941	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,386.04 (0.00) [0]
942	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	1,649.57 (1,017.00) [-4]
943	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (-) [10/2020]	690.00 (-) [690.00]	256.76 (0.00) [27]
944	PARADIP-RAIPUR- RANCHI PIPELINE	8/2009	12/2016 (-) [0/0]	1,793.00 (-) [1,793.00]	1,788.86 (0.00) [0]
945	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	3/2015	12/2018 (-) [6/2019]	3,957.00 (-) [3,397.00]	2,707.26 (-560.00) [6]
946	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	82.95 (0.00) [0]
947	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [12/2019]	352.56 (-) [438.84]	224.72 (86.28) [33]
948	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (8/2019) [8/2019]	309.81 (723.40) [723.40]	678.31 (413.59) [58]
	Power				
949	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [2/2020]	198.49 (-) [198.49]	83.31 (0.00) [5]
950	COMPREHENSIVE SCHEME FOR THE STRENGTHENING	12/2014	12/2018	4,754.42	1,211.92

	OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P		(-) [12/2019]	(-) [9,072.36]	(4,317.94) [12]
951	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	38.90 (0.00) [0]
952	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (4/2019) [6/2019]	196.58 (-) [225.28]	162.30 (28.70) [40]
953	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (8/2019) [8/2019]	1,364.52 (-) [1,891.41]	1,259.05 (526.89) [40]
954	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (12/2019) [3/2020]	522.29 (-) [546.36]	465.21 (24.07) [40]
955	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	1,399.20 (0.00) [0]
956	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (6/2019) [10/2019]	235.53 (-) [235.53]	117.15 (0.00) [4]
957	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (6/2019) [8/2019]	322.30 (-) [322.30]	153.70 (0.00) [6]
958	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (3/2018) [8/2019]	197.40 (-) [197.40]	81.97 (0.00) [17]
959	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [9/2019]	3,519.59 (-) [3,519.59]	2,431.00 (0.00) [4]
960	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	2,516.66 (0.00) [0]
961	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	7,922.74 (0.00) [0]
962	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	933.96 (0.00) [0]
963	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	185.94 (0.00) [0]
964	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (12/2018) [12/2020]	5,111.33 (-) [6,880.36]	1,367.68 (1,769.03) [24]
965	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (-) [14,719.10]	12,804.46 (3,588.91) [103]
966	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (11/2019) [11/2019]	283.72 (-) [283.72]	187.60 (0.00) [0]
967	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (3/2019) [7/2019]	562.25 (-) [562.25]	392.96 (0.00) [4]
968	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [7/2019]	3,654.00 (-) [3,654.00]	3,308.50 (0.00) [3]
969	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (4/2019) [7/2019]	608.24 (-) [608.24]	407.79 (0.00) [3]
970	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019)	203.28 (-)	190.80 (56.75)

			[8/2019]	[260.03]	[25]
971	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (12/2019) [12/2019]	379.95 (-) [379.95]	52.63 (0.00) [0]
972	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-) [7/2019]	337.75 (-) [337.75]	84.17 (0.00) [1]
973	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (9/2019) [9/2019]	487.49 (-) [639.46]	540.12 (151.97) [63]
974	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2019) [12/2019]	4,824.12 (-) [5,071.94]	4,558.05 (247.82) [86]
975	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP	1/2015	3/2018 (3/2019) [7/2019]	268.80 (-) [340.88]	251.33 (72.08) [16]
976	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [9/2019]	871.62 (-) [871.62]	548.30 (0.00) [23]
977	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (9/2019) [9/2019]	408.46 (-) [408.46]	266.03 (0.00) [8]
978	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (12/2019) [12/2019]	5,151.37 (5,151.37) [5,151.37]	3,115.72 (0.00) [21]
979	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (12/2019) [3/2020]	808.63 (-) [808.63]	513.85 (0.00) [26]
980	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (3/2017) [12/2019]	374.63 (374.63) [374.63]	210.72 (0.00) [44]
981	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (2/2020) [2/2020]	195.05 (-) [195.05]	116.76 (0.00) [0]
	<u>Railways</u>				
982	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	2,812.27 (0.00) [0]
983	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2020]	288.35 (-) [364.98]	364.98 (76.63) [-]
984	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.12 (-200.00) [-]
985	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (1,352.74) [1,352.74]	269.07 (648.43) [0]
986	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [1,787.00]	2.46 (863.77) [0]
987	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [0/0]	175.80 (-) [226.22]	226.22 (50.42) [0]
988	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	233.84 (1,211.86) [0]
989	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [381.75]	70.22 (43.79) [-]
990	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-)	523.52 (-)	2.28 (1,776.48)

			[0/0]	[2,300.00]	[0]
991	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	256.42 (182.31) [12]
992	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	106.55 (651.22) [0]
993	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [5/2010]	595.51 (-) [160.00]	102.25 (-435.51) [0]
994	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2022) [3/2022]	1,347.26 (1,347.26) [1,347.26]	700.60 (0.00) [0]
995	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	665.69 (0.00) [12]
996	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [296.43]	182.35 (-68.74) [96]
997	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR	4/2013	/ (-) [3/2025]	1,239.00 (-) [1,239.00]	0.00 (0.00) [-]
998	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2022]	336.91 (791.39) [800.00]	495.17 (463.09) [-]
999	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,026.30]	637.72 (419.21) [133]
1000	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [12/2022]	2,030.50 (-) [2,030.50]	19.07 (0.00) [-]
1001	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1002	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1003	GAYA-CHATRA (NL)	4/2008	/ (-) [3/2024]	415.67 (-) [549.75]	15.47 (134.08) [-]
1004	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (12/2020) [12/2020]	511.86 (1,756.92) [1,756.92]	1,645.84 (1,245.06) [8]
1005	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1006	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	137.90 (932.64) [33]
1007	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL	4/2000	/ (-) [0/0]	157.17 (-) [160.00]	77.29 (2.83) [0]
1008	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [2/2021]	678.54 (678.54) [678.54]	446.51 (0.00) [23]
1009	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2020]	542.18 (-) [693.80]	403.81 (151.62) [0]
1010	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	10.73 (88.07) [-]

1011	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [770.08]	277.14 (540.05) [0]
1012	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2021]	1,614.59 (-) [1,870.41]	914.00 (255.82) [24]
1013	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.47 (0.00) [28]
1014	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [3/2025]	166.89 (-) [166.89]	246.00 (0.00) [-]
1015	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [3/2021]	625.00 (876.00) [876.00]	848.84 (251.00) [60]
1016	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2024]	2,132.77 (-) [2,132.77]	331.17 (0.00) [120]
1017	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [1,218.71]	431.90 (295.19) [108]
1018	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [3/2025]	174.56 (-) [175.99]	71.37 (1.43) [-]
1019	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2023]	2,063.03 (-) [2,063.03]	675.97 (0.00) [24]
1020	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [2,200.00]	252.81 (343.05) [12]
1021	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (457.08) [457.08]	360.07 (186.94) [0]
1022	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [575.65]	148.40 (168.66) [228]
1023	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (3/2023) [3/2023]	247.66 (-) [6,093.31]	1,835.18 (5,845.65) [178]
1024	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [258.73]	103.91 (1.31) [132]
1025	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2019]	120.70 (-) [1,800.00]	170.47 (1,679.30) [9]
1026	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [726.95]	150.36 (226.99) [157]
1027	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [259.23]	243.97 (8.30) [-]
1028	MUNEERABAD-MAHABOONNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2021]	1,723.00 (1.00) [2,542.75]	1,413.56 (819.75) [252]
1029	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	121.92 (246.16) [0]
1030	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (-) [2,010.00]	644.09 (1,560.00) [140]
1031	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI	4/2010	3/2005	494.54	32.00

	NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL		(-) [3/2025]	(-) [506.42]	(11.88) [240]
1032	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	68.14 (228.78) [0]
1033	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [3/2021]	241.52 (373.87) [394.28]	272.88 (152.76) [-]
1034	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [3/2019]	1,798.00 (-) [1,798.00]	0.00 (0.00) [0]
1035	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1036	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2019]	1,180.19 (-) [3,500.00]	3,257.97 (2,319.81) [0]
1037	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	38.93 (85.99) [25]
1038	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [444.81]	444.81 (183.43) [0]
1039	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	307.25 (1,221.83) [36]
1040	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1041	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,079.15]	184.67 (1,996.40) [0]
1042	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	2,062.30 (-) [2,062.20]	825.58 (-0.10) [-]
1043	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [319.75]	52.09 (22.28) [-]
1044	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [328.75]	165.55 (51.47) [108]
1045	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
1046	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	9.31 (811.34) [-]
1047	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1048	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1049	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	4/2013	/ (-) [3/2025]	876.00 (-) [876.00]	0.00 (0.00) [-]
1050	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [3/2020]	860.43 (-) [860.43]	697.21 (0.00) [0]
	<u>Road Transport And Highways</u>				
1051	4 LANING OF NAGPUR-BETUL	2/2011	8/2014	2,498.76	2,531.46

			(-) [0/0]	(-) [2,498.76]	(0.00) [0]
1052	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	3,070.11 (1,016.78) [0]
1053	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
1054	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,294.47]	0.00 (0.00) [0]
1055	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [998.70]	0.00 (0.00) [0]
1056	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [8/2020]	604.00 (-) [604.00]	423.83 (0.00) [128]
1057	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [12/2019]	754.00 (-) [754.00]	1,363.43 (0.00) [81]
1058	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	1,275.00 (0.00) [-]
1059	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	303.71 (0.00) [0]
1060	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2019]	2,848.00 (-) [2,848.00]	1,159.10 (0.00) [69]
	Shipping And Ports				
1061	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	4,200.00 (-) [4,200.00]	1,256.55 (0.00) [0]
	Telecommunications				
1062	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	8,397.00 (11,330.00) [58]
1063	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	NAGALAND				
	Railways				
1064	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1065	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [3,000.00]	756.82 (673.48) [79]
	Road Transport And Highways				
1066	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
1067	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
1068	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	3.27 (0.00) [0]
1069	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	116.06 (0.00) [0]

1070	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
1071	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	112.38 (0.00) [0]
1072	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
1073	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	0.00 (0.00) [0]
1074	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]
1075	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	4.55 (0.00) [0]
1076	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
1077	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
1078	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
1079	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	6.75 (0.00) [0]
1080	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	9.21 (0.00) [0]
1081	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	187.25 (0.00) [36]
1082	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	229.11 (0.00) [36]
1083	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	153.61 (0.00) [36]
1084	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1085	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	241.15 (0.00) [108]
1086	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2022]	172.08 (-) [172.08]	346.99 (0.00) [144]
1087	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2022]	479.15 (-) [479.15]	196.26 (0.00) [36]
1088	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	493.85 (0.00) [36]
1089	GARJANBAHAL OCP	11/2014	3/2021 (-)	1,375.38 (-)	437.89 (0.00)

			[3/2021]	[1,375.38]	[0]
1090	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2021]	479.53 (-) [479.53]	390.53 (0.00) [96]
1091	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	82.60 (0.00) [0]
1092	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2020]	337.66 (-) [337.66]	183.98 (0.00) [12]
1093	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2022]	457.77 (-) [457.77]	539.59 (0.00) [108]
1094	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	75.79 (0.00) [24]
1095	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2020]	302.96 (-) [302.96]	302.96 (0.00) [120]
1096	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,111.70 (0.00) [0]
1097	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,546.73 (0.00) [0]
	<u>Mines</u>				
1098	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	102.61 (0.00) [0]
1099	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	31.92 (0.00) [0]
1100	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.30 (0.00) [0]
1101	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	316.08 (0.00) [0]
	<u>Petroleum</u>				
1102	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	32.69 (0.00) [0]
1103	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	0.00 (0.00) [0]
1104	BS-VI PROJECT AT PARADIP	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	269.74 (0.00) [0]
1105	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	109.28 (0.00) [0]
1106	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	45.20 (0.00) [0]
1107	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	25.83 (0.00) [0]
1108	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	988.14 (0.00) [0]
1109	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021	5,654.00	240.73

			(-) [10/2021]	(-) [5,654.00]	(0.00) [0]
1110	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [12/2019]	429.00 (-) [429.00]	300.23 (0.00) [11]
1111	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	36.68 (0.00) [0]
1112	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	7.18 (0.00) [0]
1113	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (-) [7/2019]	3,150.00 (-) [3,150.00]	2,740.12 (0.00) [22]
	<u>Power</u>				
1114	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (6/2020) [6/2020]	12,532.44 (-) [13,740.53]	9,298.78 (1,208.09) [18]
1115	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (4/2019) [8/2019]	844.64 (-) [844.64]	430.71 (0.00) [4]
	<u>Railways</u>				
1116	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [1,120.00]	977.00 (177.05) [24]
1117	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2023]	843.04 (-) [843.04]	125.30 (0.00) [29]
1118	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2022]	1,172.92 (-) [1,172.92]	349.23 (0.00) [39]
1119	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
1120	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (6/2023) [6/2023]	5,200.00 (1,700.43) [1,700.43]	48.00 (-3,499.57) [39]
1121	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,709.83 (658.83) [27]
1122	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2023]	1,547.38 (1,547.38) [1,547.38]	320.30 (0.00) [12]
1123	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2021]	701.61 (-) [810.02]	116.91 (108.41) [28]
1124	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2019]	133.41 (207.00) [385.00]	381.48 (251.59) [129]
1125	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [12/2023]	2,923.13 (-) [3,798.80]	1,354.80 (875.67) [177]
1126	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2025]	2,361.74 (2,361.74) [2,361.74]	148.96 (0.00) [36]
1127	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [6/2020]	969.83 (1,312.96) [1,312.96]	494.27 (343.13) [3]
1128	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	4/1995	12/2021 (-) [12/2024]	524.43 (-) [939.00]	184.33 (414.57) [36]

1129	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2020]	155.81 (-) [238.03]	224.63 (82.22) [0]
1130	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2020]	948.04 (-) [1,500.00]	1,197.11 (551.96) [0]
1131	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2022]	1,111.99 (-) [1,539.28]	879.96 (427.29) [37]
1132	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (-) [1,202.70]	833.73 (0.00) [82]
1133	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2023]	810.78 (-) [1,928.07]	624.68 (1,117.29) [21]
1134	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (-) [2,335.68]	482.27 (0.01) [0]
	<u>Road Transport And Highways</u>				
1135	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [4/2020]	1,282.94 (-) [1,282.94]	0.00 (0.00) [-]
1136	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [8/2019]	2,510.04 (-) [2,510.04]	0.00 (0.00) [0]
1137	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
1138	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016 (-) [0/0]	319.80 (320.00) [320.00]	268.27 (0.20) [0]
1139	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016 (-) [0/0]	319.80 (-) [319.80]	268.01 (0.00) [0]
1140	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [7/2019]	1,069.65 (-) [1,069.65]	0.00 (0.00) [-]
1141	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,930.61 (0.00) [0]
1142	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [7/2020]	1,008.96 (-) [1,008.96]	447.28 (0.00) [-]
1143	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	0.00 (0.00) [-]
1144	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [11/2020]	476.56 (-) [476.56]	0.00 (0.00) [40]
1145	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
1146	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [5/2020]	953.09 (-) [953.09]	0.00 (0.00) [-]
1147	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [5/2020]	668.86 (-) [668.86]	0.00 (0.00) [-]
1148	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	0.00 (0.00) [-]

1149	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [6/2019]	342.05 (-) [342.05]	258.91 (0.00) [29]
1150	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	0.00 (0.00) [0]
1151	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	0.00 (0.00) [-]
1152	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2021]	1,288.07 (-) [1,420.00]	221.91 (131.93) [12]
1153	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [7/2020]	686.65 (-) [686.65]	34.36 (0.00) [-]
1154	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [3/2020]	686.65 (-) [686.65]	29.45 (0.00) [-]
1155	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [0/0]	417.51 (-) [417.51]	0.00 (0.00) [0]
1156	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	258.91 (-0.05) [0]
1157	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [0/0]	999.00 (-) [999.00]	0.00 (0.00) [0]
1158	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [11/2019]	171.96 (172.00) [172.00]	88.30 (0.04) [41]
1159	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1160	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1161	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,864.34 (0.00) [0]
1162	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	0.00 (0.00) [-]
1163	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [12/2019]	191.50 (192.00) [192.00]	136.19 (0.50) [43]
1164	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1165	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [6/2019]	326.63 (327.00) [326.63]	249.26 (0.00) [14]
1166	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1167	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [9/2019]	159.39 (-) [159.39]	210.29 (0.00) [22]
1168	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [12/2019]	191.08 (-) [191.08]	99.98 (0.00) [52]
1169	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED	3/2015	10/2017	226.31	137.43

	SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900		(-) [0/0]	(226.00) [226.31]	(0.00) [0]
1170	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA	3/2015	11/2015 (-) [0/0]	229.29 (-) [229.29]	163.40 (0.00) [0]
1171	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA	7/2013	10/2015 (-) [0/0]	251.92 (-) [251.92]	225.98 (0.00) [0]
1172	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA	7/2013	10/2015 (-) [0/0]	265.35 (-) [265.35]	247.56 (0.00) [0]
1173	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1174	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1175	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1176	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1177	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1178	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1179	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	<u>Steel</u>				
1180	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (5/2019) [5/2019]	3,127.30 (-) [3,127.30]	2,872.84 (0.00) [0]
	<u>Urban Development</u>				
1181	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	6/2021 (-) [6/2021]	790.79 (-) [800.00]	0.00 (9.21) [0]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1182	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	88.74 (0.00) [0]
1183	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	81.46 (0.00) [0]
	<u>Health And Family Welfare</u>				
1184	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [8/2020]	703.00 (-) [703.00]	184.93 (0.00) [2]
1185	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [9/2019]	152.95 (-) [152.95]	118.23 (0.00) [19]
	<u>Railways</u>				
1186	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [205.22]	1.79 (0.00) [-]
	<u>Road Transport And Highways</u>				
1187	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/	1,169.61	1,004.18

			(-) [4/2020]	(-) [1,169.61]	(0.00) [-]
1188	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/	847.02	786.68
			(-) [0/0]	(-) [847.02]	(0.00) [0]
1189	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/	889.24	722.92
			(-) [6/2019]	(-) [904.82]	(15.58) [-]
1190	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019	1,388.34	1,213.89
			(-) [9/2019]	(-) [1,388.34]	(0.00) [0]
1191	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020	754.54	76.83
			(-) [4/2020]	(-) [756.27]	(1.73) [1]
1192	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/	766.36	666.72
			(-) [6/2019]	(-) [766.36]	(0.00) [-]
1193	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017	447.29	194.95
			(-) [12/2019]	(-) [447.29]	(0.00) [24]
1194	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/	261.76	40.89
			(-) [1/2021]	(-) [261.76]	(0.00) [-]
1195	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	453.09
			(-) [3/2020]	(-) [479.00]	(0.00) [-]
1196	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019	1,069.59	629.87
			(-) [10/2019]	(-) [1,069.59]	(0.00) [0]
1197	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/	196.05	9.03
			(-) [1/2020]	(-) [196.05]	(0.00) [-]
1198	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/	199.90	37.68
			(-) [6/2019]	(-) [199.90]	(0.00) [-]
1199	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020	170.57	8.14
			(-) [11/2020]	(-) [170.57]	(0.00) [0]
1200	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020	173.24	10.97
			(-) [6/2020]	(-) [173.24]	(0.00) [0]
1201	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020	322.48	48.73
			(-) [7/2020]	(-) [322.48]	(0.00) [0]
1202	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	28.24
			(-) [8/2020]	(-) [293.64]	(0.00) [0]
1203	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	28.24
			(-) [8/2020]	(-) [293.64]	(0.00) [0]
1204	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020	293.10	10.26
			(-) [8/2020]	(-) [293.10]	(0.00) [0]
1205	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/	892.17	642.01
			(-) [11/2017]	(-) [892.17]	(0.00) [0]
	<u>Urban Development</u>				
1206	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017	388.00	418.79
			(-) [9/2019]	(-) [488.28]	(100.28) [28]
1207	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE	1/2018	5/2020	430.00	59.36

	1C AT IIT ROPAR, PUNJAB		(-) [12/2020]	(-) [430.00]	(0.00) [7]
1208	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [12/2019]	294.00 (-) [294.00]	187.10 (0.00) [8]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1209	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2020]	12,320.00 (17,079.00) [17,079.00]	10,993.00 (4,759.00) [48]
	<u>Coal</u>				
1210	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	175.30 (0.00) [0]
1211	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Petroleum</u>				
1212	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1213	LPG BP PROJECT JODHPUR	3/2018	/ (-) [3/2021]	229.80 (-) [229.80]	69.10 (0.00) [-]
	<u>Power</u>				
1214	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (-) [7/2019]	1,429.38 (-) [1,429.38]	1,011.38 (0.00) [6]
	<u>Railways</u>				
1215	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,103.04]	4.25 (229.33) [0]
1216	AJMER-BANGURGRAM	4/2011	11/2019 (-) [5/2020]	213.39 (-) [244.02]	245.81 (30.63) [6]
1217	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.54]	0.00 (277.54) [0]
1218	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [12/2019]	242.09 (281.03) [410.00]	341.67 (167.91) [10]
1219	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2020]	246.08 (-) [348.55]	199.54 (102.47) [6]
1220	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [12/2021]	410.08 (780.98) [886.41]	510.24 (476.33) [34]
1221	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	33.39 (0.00) [1]
1222	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2020]	420.18 (-) [420.18]	142.63 (0.00) [3]
1223	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	436.07 (0.00) [24]
1224	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1225	THIYAT HAMIRA-SANU	4/2013	10/2018 (-)	236.93 (-)	138.99 (57.97)

			[10/2019]	[294.90]	[12]
	Road Transport And Highways				
1226	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [4/2019]	597.00 (-) [597.00]	605.33 (0.00) [0]
1227	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [4/2019]	320.30 (-) [320.30]	232.49 (0.00) [0]
1228	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [2/2019]	530.07 (-) [530.07]	556.02 (0.00) [0]
1229	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [11/2019]	688.70 (-) [688.70]	661.85 (0.00) [-]
1230	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [8/2020]	1,031.95 (-) [1,031.95]	367.00 (0.00) [-]
1231	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [3/2019]	822.90 (-) [822.90]	834.75 (0.00) [0]
1232	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP.	10/2012	10/2013 (-) [0/0]	511.21 (-) [511.21]	813.54 (0.00) [0]
1233	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	0.00 (0.00) [0]
1234	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC.	12/2015	10/2016 (-) [0/0]	621.43 (-) [621.43]	402.14 (0.00) [0]
1235	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE.	3/2016	9/2016 (-) [0/0]	155.77 (-) [155.77]	97.42 (0.00) [0]
1236	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [0/0]	163.95 (-) [163.95]	42.04 (0.00) [0]
1237	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	73.00 (0.00) [0]
1238	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1239	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	3/2009	9/2013 (-) [0/0]	501.00 (671.54) [671.54]	659.98 (170.54) [0]
1240	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [12/2020]	1,308.73 (-) [1,308.73]	0.00 (0.00) [-]
1241	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	216.17 (0.00) [5]
1242	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	0.00 (0.00) [3]
1243	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [11/2020]	964.17 (-) [964.17]	329.90 (0.00) [37]
1244	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [3/2019]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1245	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP.	1/2012	1/2014 (-)	378.07 (478.73)	188.98 (100.66)

			[0/0]	[478.73]	[0]
1246	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC.	10/2014	1/2015 (-) [0/0]	382.81 (-) [382.81]	333.27 (0.00) [0]
1247	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [8/2019]	511.00 (-) [511.00]	492.00 (0.00) [70]
1248	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [6/2019]	511.00 (-) [511.00]	2,323.04 (0.00) [68]
1249	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1250	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1251	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [12/2019]	1,100.19 (-) [1,100.19]	848.00 (0.00) [-]
1252	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	174.79 (0.00) [-]
1253	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [11/2019]	894.00 (-) [894.00]	605.00 (0.00) [-5]
1254	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR	9/2014	9/2016 (-) [3/2019]	425.19 (-) [425.19]	297.72 (0.00) [0]
1255	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [3/2019]	275.90 (-) [275.90]	257.52 (0.00) [0]
1256	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1257	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	571.06 (0.00) [3]
1258	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE	1/2017	7/2017 (-) [0/0]	163.54 (-) [163.54]	84.10 (0.00) [0]
1259	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN	1/2017	11/2017 (-) [0/0]	179.32 (-) [179.32]	92.66 (0.00) [0]
1260	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	0.00 (0.00) [0]
1261	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	167.46 (0.00) [0]
1262	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	198.85 (0.00) [-]
1263	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	88.38 (0.00) [0]
1264	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1265	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [6/2019]	383.40 (-) [383.40]	224.68 (0.00) [51]

1266	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1267	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [7/2019]	621.43 (-) [621.43]	387.00 (0.00) [13]
1268	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	35.82 (0.00) [0]
	<u>Urban Development</u>				
1269	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [0/0]	189.00 (-) [189.00]	0.00 (0.00) [0]
1270	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (12/2019) [12/2019]	549.31 (559.47) [559.47]	314.01 (10.16) [5]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1271	SEVOK RANGPO, NEFR	4/2008	12/2015 (6/2021) [3/2020]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
1272	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (9/2017) [12/2019]	182.28 (269.14) [269.14]	185.49 (86.86) [82]
1273	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (-) [151.59]	196.76 (0.00) [76]
1274	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	132.27 (0.00) [0]
1275	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
1276	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	30.70 (0.00) [0]
1277	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	78.78 (0.00) [0]
1278	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1279	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [388.00]	78.33 (0.00) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1280	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	14,422.00 (0.00) [36]
1281	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2021]	3,492.00 (-) [6,840.00]	5,784.74 (3,348.00) [133]
	<u>Coal</u>				
1282	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [9/2019]	1,458.17 (-) [709.06]	439.27 (-749.11) [51]
1283	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [12/2019]	5,907.11 (7,080.41) [7,080.41]	6,451.65 (1,173.30) [48]

	<u>Mines</u>				
1284	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (-) [6/2019]	166.62 (-) [166.62]	134.98 (0.00) [0]
	<u>Petroleum</u>				
1285	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	6.64 (0.00) [0]
1286	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	848.87 (0.00) [0]
1287	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	25.99 (0.00) [10]
1288	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2021]	4,497.00 (6,025.00) [6,025.00]	444.28 (1,528.00) [26]
1289	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1290	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (-) [5/2020]	390.52 (-) [390.52]	367.94 (0.00) [14]
1291	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [10/2021]	678.00 (-) [678.00]	5.57 (0.00) [56]
1292	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	100.28 (0.00) [0]
1293	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.00 (0.00) [0]
	<u>Power</u>				
1294	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (6/2019) [8/2019]	1,779.29 (2,187.32) [2,187.32]	2,237.45 (408.03) [129]
1295	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [9/2019]	186.17 (-) [186.17]	103.12 (0.00) [2]
	<u>Railways</u>				
1296	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [3/2018]	257.00 (257.00) [257.00]	268.31 (0.00) [0]
1297	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1298	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (-) [3/2020]	931.98 (951.24) [951.24]	724.96 (19.26) [-]
1299	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	303.72 (357.96) [0]
1300	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1301	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [0/0]	495.74 (-) [734.01]	445.91 (238.27) [0]
1302	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2021]	760.00 (-) [1,182.31]	406.32 (422.31) [15]

1303	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	151.50 (285.59) [-]
1304	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [3/2022]	1,700.00 (-) [1,003.00]	167.73 (-697.00) [0]
1305	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2020]	724.69 (-) [2,072.50]	1,386.59 (1,347.81) [12]
1306	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	108.34 (44.41) [71]
1307	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]
1308	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [950.00]	927.86 (681.13) [0]
1309	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [0/0]	582.83 (-) [2,300.00]	241.39 (1,717.17) [0]
1310	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [900.00]	62.50 (672.60) [0]
1311	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2021]	303.98 (-) [980.00]	669.21 (676.02) [12]
1312	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	Road Transport And Highways				
1313	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [0/0]	485.00 (-) [485.00]	406.68 (0.00) [0]
1314	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHT 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1315	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [11/2019]	244.27 (-) [244.27]	95.96 (0.00) [26]
1316	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [8/2020]	1,227.87 (-) [1,227.87]	0.00 (0.00) [35]
1317	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1318	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1319	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [0/0]	600.00 (-) [600.00]	326.23 (0.00) [0]
1320	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [4/2021]	1,016.92 (-) [1,016.92]	0.00 (0.00) [-]
1321	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [7/2019]	1,387.11 (-) [1,387.11]	956.75 (0.00) [20]
1322	FOUR LANING OF MADURAI- CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [11/2020]	628.71 (-) [628.71]	31.45 (0.00) [-]

1323	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,065.96]	0.00 (0.00) [0]
1324	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [2/2021]	1,166.26 (-) [1,166.26]	0.00 (0.00) [-]
1325	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [5/2020]	641.17 (-) [641.17]	405.31 (0.00) [46]
1326	FOUR LANING OF CHETTikulAM TO NATHAM SECTION OF NH-785 FROM CHETTikulUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [11/2020]	505.35 (-) [505.35]	32.77 (0.00) [-]
1327	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [9/2020]	1,176.37 (-) [1,176.37]	0.00 (0.00) [37]
1328	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2020]	707.82 (-) [707.82]	288.38 (0.00) [19]
1329	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	54.70 (0.00) [0]
1330	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [5/2020]	641.17 (-) [641.17]	405.31 (0.00) [22]
1331	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1332	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2020]	379.90 (-) [379.90]	84.22 (0.00) [-]
1333	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,330.29 (0.00) [0]
1334	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1335	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	627.66 (0.00) [0]
1336	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [0/0]	374.00 (-) [374.00]	237.00 (0.00) [0]
1337	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [633.55]	0.00 (0.00) [0]
1338	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [8/2019]	563.92 (-) [563.92]	96.48 (0.00) [20]
	<u>Shipping And Ports</u>				
1339	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017 (-) [5/2020]	600.00 (258.00) [257.90]	1.45 (-342.10) [29]
1340	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017 (-) [0/0]	244.50 (258.00) [275.98]	275.58 (31.48) [0]
1341	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006 (-) [0/0]	150.00 (-) [600.00]	139.80 (450.00) [0]
1342	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008 (-) [0/0]	2,427.40 (-) [2,427.40]	831.21 (0.00) [0]

	<u>Urban Development</u>				
1343	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [3/2020]	209.00 (-) [209.00]	127.69 (0.00) [5]
1344	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1345	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.77 (4,458.00) [0]
1346	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [11/2021]	348.77 (-) [348.77]	12.00 (0.00) [-]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1347	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	2.11 (0.00) [0]
1348	KOYAGUDEM OPENCASE PROJECT	10/2015	3/2018 (-) [3/2020]	426.79 (-) [426.79]	0.72 (0.00) [24]
1349	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [9/2017]	447.06 (-) [473.22]	69.93 (26.16) [0]
1350	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1351	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	53.00 (0.00) [36]
1352	KAKATIYAKHANI OPENCASE-2 PROJECT	5/2015	3/2019 (-) [9/2017]	397.09 (-) [442.42]	78.30 (45.33) [0]
1353	KALYANIKHANI OPENCASE PROJECT	7/2012	7/2016 (-) [4/2017]	417.33 (-) [384.32]	86.94 (-33.01) [0]
1354	KISTARAM OCP	11/2010	3/2015 (-) [7/2019]	242.29 (-) [164.04]	115.71 (-78.25) [52]
1355	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	170.60 (0.00) [0]
1356	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	331.25 (70.65) [132]
1357	RAMPURAM SHAFT BLOCK	8/2016	/ (-) [0/0]	431.92 (-) [431.92]	0.00 (0.00) [0]
1358	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	7.01 (186.52) [72]
1359	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [12/2016]	430.45 (-) [415.37]	181.91 (-15.08) [0]
1360	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [12/2015]	365.01 (-) [365.01]	132.04 (0.00) [0]
1361	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2019]	209.78 (-) [209.78]	154.02 (0.00) [0]
1362	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012	249.03	232.81

			(-) [3/2024]	(-) [448.86]	(199.83) [144]
1363	SRAVANAPALLI OPENCASCT PROJECT	2/2018	/	412.70	0.00
			(-) [0/0]	(-) [412.70]	(0.00) [0]
1364	SRP OC-II EXPANSION PROJECT	11/2016	/	272.73	0.00
			(-) [0/0]	(-) [272.73]	(0.00) [0]
	<u>Petroleum</u>				
1365	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022	611.00	1.68
			(-) [4/2022]	(-) [611.00]	(0.00) [0]
	<u>Power</u>				
1366	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (6/2021) [6/2021]	10,598.98 (-) [10,598.98]	4,988.68 (0.00) [7]
	<u>Railways</u>				
1367	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2020]	632.68 (-) [816.55]	668.38 (183.87) [57]
1368	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	281.85 (0.00) [0]
1369	KONDAPALLI-KOTHAGUDEM	4/2013	/	723.00	0.00
			(-) [0/0]	(997.09) [997.09]	(274.09) [0]
1370	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/	458.25	3.83
			(-) [0/0]	(-) [458.26]	(0.01) [0]
1371	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	3.67 (65.24) [0]
1372	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2023]	1,160.48 (-) [1,160.48]	288.38 (0.00) [156]
1373	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92
			(-) [0/0]	(-) [2,911.84]	(1,799.84) [0]
1374	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	309.16 (0.00) [0]
	<u>Road Transport And Highways</u>				
1375	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [12/2019]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [39]
1376	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [5/2020]	283.15 (-) [283.15]	32.04 (0.00) [0]
1377	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [7/2020]	626.76 (-) [626.76]	46.62 (0.00) [0]
1378	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	0.00 (0.00) [0]
1379	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1380	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/	857.62	0.00
			(-) [0/0]	(-) [857.62]	(0.00) [0]
1381	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM	3/2018	/	802.65	0.00

	135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K		(-) [0/0]	(-) [802.65]	(0.00) [0]
1382	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/	950.63	0.00
			(-) [0/0]	(-) [950.63]	(0.00) [0]
1383	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO	3/2018	/	828.29	0.00
	TELANGANA/MAHARASHT		(-) [0/0]	(-) [828.29]	(0.00) [0]
1384	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018	1,423.96	691.30
			(-) [7/2019]	(-) [1,423.96]	(0.00) [8]
1385	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019	192.67	0.00
			(-) [7/2019]	(-) [192.67]	(0.00) [0]
1386	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019	605.08	213.00
			(-) [10/2019]	(-) [605.08]	(0.00) [0]
1387	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020	426.52	134.38
			(-) [4/2020]	(-) [426.52]	(0.00) [0]
1388	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016	270.00	19.84
			(-) [0/0]	(-) [270.00]	(0.00) [0]
1389	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019	294.13	23.54
			(-) [11/2019]	(-) [294.13]	(0.00) [0]
1390	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019	220.28	7.40
			(-) [11/2019]	(-) [220.28]	(0.00) [0]
1391	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020	322.81	0.34
			(-) [9/2020]	(-) [322.81]	(0.00) [0]
1392	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017	295.47	0.00
			(-) [0/0]	(-) [313.27]	(17.80) [0]
1393	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019	248.83	79.02
			(-) [12/2019]	(-) [248.83]	(0.00) [9]
1394	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019	298.32	62.22
			(-) [12/2019]	(-) [298.32]	(0.00) [10]
1395	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019	230.03	80.71
			(-) [12/2019]	(-) [230.03]	(0.00) [0]
1396	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020	206.13	94.93
			(-) [6/2020]	(-) [206.13]	(0.00) [0]
1397	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/	193.19	0.00
			(-) [0/0]	(-) [193.19]	(0.00) [0]
1398	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019	196.52	92.88
			(-) [10/2019]	(-) [196.52]	(0.00) [0]
1399	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019	283.00	121.47
			(-) [12/2019]	(-) [283.00]	(0.00) [0]
1400	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019	244.54	122.31
			(-) [7/2019]	(-) [244.54]	(0.00) [2]
1401	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-	1/2017	5/2019	359.27	200.24
			(-)	(-)	(0.00)

	RAVULAPALLY SECT		[8/2019]	[359.27]	[3]
1402	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [12/2019]	300.00 (-) [300.00]	83.83 (0.00) [7]
	<u>Urban Development</u>				
1403	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (2/2017) [5/2021]	209.84 (-) [209.84]	35.79 (0.00) [14]
	<u>TRIPURA</u>				
	<u>Railways</u>				
1404	AGARTALA-AKHAURA NL	4/2012	3/2020 (3/2020) [12/2021]	569.63 (569.63) [650.00]	45.24 (80.37) [21]
	<u>Road Transport And Highways</u>				
1405	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	297.12 (0.00) [0]
	<u>Urban Development</u>				
1406	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1407	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1408	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Coal</u>				
1409	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	6,531.52 (0.80) [0]
	<u>Health And Family Welfare</u>				
1410	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [6/2020]	785.00 (-) [785.00]	244.66 (0.00) [2]
1411	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	99.26 (0.00) [-]
	<u>Petroleum</u>				
1412	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	9/2019 (-) [9/2019]	204.00 (-) [204.00]	132.24 (0.00) [0]
1413	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	10.40 (0.00) [0]
1414	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	374.07 (0.00) [0]
1415	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	116.05 (0.00) [0]
1416	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	0.44 (0.00) [0]
1417	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	13.10 (0.00) [0]
1418	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY	8/2016	11/2019 (-) [11/2019]	154.84 (-) [154.84]	104.23 (0.00) [0]

1419	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	37.30 (0.00) [3]
	Power				
1420	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-) [9/2020]	587.44 (-) [587.44]	250.00 (0.00) [0]
1421	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (-) [11/2020]	349.00 (-) [349.00]	125.00 (0.00) [0]
1422	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (-) [10/2019]	195.42 (-) [294.60]	292.85 (99.18) [68]
1423	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [9/2023]	11,089.42 (-) [11,089.42]	503.39 (0.00) [0]
1424	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2018 (6/2020) [6/2020]	9,750.89 (-) [12,176.28]	9,645.00 (2,425.39) [28]
1425	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (6/2020) [6/2020]	9,188.98 (-) [9,188.98]	6,271.59 (0.00) [11]
	Railways				
1426	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1427	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2020]	600.00 (-) [366.71]	9.10 (-233.29) [-24]
1428	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1429	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	982.53 (0.00) [3]
1430	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	7.64 (111.84) [0]
1431	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1432	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1433	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (3/2015) [3/2015]	120.00 (314.09) [346.00]	345.51 (226.00) [0]
1434	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	4/2013	/ (-) [3/2025]	654.00 (-) [700.00]	0.00 (46.00) [-]
1435	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1436	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [2/2020]	213.00 (-) [213.35]	4.89 (0.35) [46]
1437	JHANSI BINA DOUBLING	9/2016	3/2021 (3/2023) [3/2021]	2,001.00 (-) [2,001.00]	395.59 (0.00) [0]
1438	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-)	4,329.53 (-)	3.56 (0.00)

			[3/2023]	[4,329.53]	[0]
1439	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1440	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [12/2019]	528.57 (-) [528.57]	72.25 (0.00) [9]
1441	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [1,200.00]	1,100.58 (272.99) [12]
1442	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (3/2020) [3/2020]	668.70 (680.00) [680.00]	330.00 (11.30) [0]
1443	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	455.60 (0.00) [21]
1444	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1445	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,345.00]	0.00 (2.00) [0]
1446	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [1/2020]	622.50 (427.00) [426.74]	116.58 (-195.76) [33]
1447	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	426.16 (0.00) [12]
1448	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [12/2019]	1,295.42 (-) [1,295.42]	249.27 (0.00) [-27]
1449	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	3.12 (-149.01) [16]
1450	UNCHAHAH-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,230.00]	102.72 (1.00) [-]
1451	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [750.56]	285.50 (-193.04) [33]
	<u>Road Transport And Highways</u>				
1452	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	232.93 (0.00) [0]
1453	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
1454	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	433.68 (0.00) [0]
1455	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	633.24 (0.00) [0]
1456	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [9/2018]	291.36 (-) [291.36]	459.07 (0.00) [0]
1457	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	207.94 (0.00) [0]
1458	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-)	2,016.00 (-)	1,996.00 (0.00)

			[11/2019]	[2,016.00]	[7]
1459	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/	1,120.57	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,120.57]	[0]
1460	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/	1,668.00	748.59
			(-)	(-)	(0.00)
			[2/2020]	[1,668.00]	[-]
1461	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016	611.65	728.24
			(-)	(-)	(0.00)
			[0/0]	[611.65]	[0]
1462	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/	1,408.00	13.33
			(-)	(-)	(0.00)
			[7/2020]	[1,408.00]	[-]
1463	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/	1,737.00	278.92
			(-)	(-)	(0.00)
			[4/2020]	[1,737.00]	[-]
1464	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/	1,404.50	92.37
			(-)	(-)	(0.00)
			[0/0]	[1,404.50]	[0]
1465	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]	3/2016	4/2019	1,587.49	276.87
			(-)	(-)	(0.00)
			[4/2019]	[1,587.49]	[0]
1466	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/	1,396.74	227.26
			(-)	(-)	(0.00)
			[0/0]	[1,396.74]	[0]
1467	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019	1,657.20	2,345.00
			(-)	(-)	(0.00)
			[1/2019]	[1,657.20]	[0]
1468	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020	2,064.99	1,597.26
			(-)	(-)	(382.01)
			[3/2020]	[2,447.00]	[0]
1469	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT- MUZAFFARN	12/2017	/	207.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[207.00]	[0]
1470	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019	676.73	623.35
			(-)	(-)	(0.00)
			[4/2019]	[676.73]	[0]
1471	BAREILY-SITAPUR (NH-24)	3/2011	9/2013	1,046.00	805.19
			(-)	(-)	(0.00)
			[0/0]	[1,046.00]	[0]
1472	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/	972.77	0.00
			(-)	(-)	(0.00)
			[0/0]	[972.77]	[0]
1473	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/	534.55	425.19
			(-)	(-)	(0.00)
			[0/0]	[534.55]	[0]
1474	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/	305.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[305.00]	[0]
1475	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/	1,117.84	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,117.84]	[0]
1476	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/	450.68	397.62
			(-)	(-)	(0.00)
			[0/0]	[450.68]	[0]
1477	CONSTRUCTION OF RING ROAD FOR RAE BARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016	282.41	155.53
			(-)	(-)	(0.00)
			[0/0]	[282.41]	[0]
1478	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019	1,081.57	988.72
			(-)	(-)	(0.00)
			[6/2019]	[1,081.57]	[0]

1479	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/	1,232.21	410.09
			(-)	(-)	(0.00)
			[5/2020]	[1,232.21]	[-]
1480	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020	1,989.00	842.34
			(-)	(-)	(0.00)
			[5/2020]	[1,989.00]	[2]
1481	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018	785.78	839.63
			(-)	(-)	(0.00)
			[0/0]	[785.78]	[0]
1482	ETAWAH CHAKERI	3/2013	9/2015	1,573.00	1,998.25
			(-)	(-)	(0.00)
			[0/0]	[1,573.00]	[0]
1483	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/	670.50	0.00
			(-)	(-)	(0.00)
			[0/0]	[670.50]	[0]
1484	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/	809.07	0.00
			(-)	(-)	(0.00)
			[0/0]	[809.07]	[0]
1485	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/	925.40	0.00
			(-)	(-)	(0.00)
			[0/0]	[925.40]	[0]
1486	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018	667.00	549.07
			(-)	(-)	(0.00)
			[0/0]	[667.00]	[0]
1487	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018	667.00	464.05
			(-)	(-)	(0.00)
			[0/0]	[667.00]	[0]
1488	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018	1,027.53	601.13
			(-)	(-)	(0.00)
			[0/0]	[1,027.53]	[0]
1489	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018	815.28	520.89
			(-)	(-)	(0.00)
			[0/0]	[815.28]	[0]
1490	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017	261.09	240.96
			(-)	(-)	(0.00)
			[0/0]	[261.09]	[0]
1491	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020	1,373.28	571.96
			(-)	(-)	(0.00)
			[11/2020]	[1,373.28]	[8]
1492	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020	1,184.71	563.15
			(-)	(-)	(125.29)
			[8/2020]	[1,310.00]	[5]
1493	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019	899.00	529.65
			(-)	(-)	(0.00)
			[0/0]	[899.00]	[0]
1494	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013	1,141.00	1,715.42
			(-)	(-)	(0.00)
			[0/0]	[1,141.00]	[0]
1495	MEERUT-BULANDSHAHR	1/2016	/	683.24	623.53
			(-)	(-)	(0.00)
			[0/0]	[683.24]	[0]
1496	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/	326.99	0.00
			(-)	(327.00)	(0.00)
			[0/0]	[326.99]	[0]
1497	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/	1,025.80	46.29
			(-)	(-)	(0.00)
			[0/0]	[1,025.80]	[0]
1498	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/	1,115.28	113.90
			(-)	(-)	(0.00)
			[0/0]	[1,115.28]	[0]
1499	REHABILITATION AND UPGRADATION OF ALLAHABAD -	10/2016	2/2019	239.63	197.77

	MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-		(-) [6/2019]	(-) [239.63]	(0.00) [4]
1500	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [11/2019]	208.50 (-) [208.50]	102.98 (0.00) [0]
1501	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [7/2019]	445.89 (653.00) [653.00]	454.41 (207.11) [28]
1502	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [1/2020]	599.34 (-) [599.34]	376.71 (0.00) [0]
1503	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [5/2019]	249.50 (-) [249.50]	190.10 (0.00) [0]
1504	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [9/2019]	215.16 (215.00) [215.16]	125.09 (0.00) [0]
1505	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [1/2020]	240.30 (240.00) [240.30]	171.00 (0.00) [0]
1506	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [3/2020]	218.94 (219.00) [218.94]	67.87 (0.00) [0]
1507	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [7/2019]	176.94 (177.00) [176.94]	132.45 (0.00) [9]
1508	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [8/2019]	445.89 (-) [653.29]	454.49 (207.40) [29]
1509	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1510	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1511	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [7/2019]	164.54 (165.00) [164.54]	86.63 (0.00) [47]
1512	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [9/2019]	164.54 (-) [164.54]	86.63 (0.00) [49]
	<u>Steel</u>				
1513	FORGED WHEEL PLANT	4/2014	9/2018 (9/2019) [9/2019]	1,682.85 (-) [1,682.85]	1,144.53 (0.00) [12]
	<u>Urban Development</u>				
1514	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	32.00 (0.00) [0]
1515	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Petroleum</u>				
1516	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [10/2020]	160.10 (-) [160.10]	38.51 (0.00) [8]
	<u>Power</u>				
1517	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.16 (274.07) [0]

1518	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	222.91 (0.00) [0]
1519	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (5,867.38) [5,867.38]	4,025.80 (2,888.90) [93]
1520	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2022]	1,657.00 (-) [5,024.35]	2,935.92 (3,367.35) [76]
1521	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2022]	2,491.58 (-) [4,397.80]	1,697.38 (1,906.22) [114]
	<u>Railways</u>				
1522	HARIDWAR-LAKSAR	4/2012	/ (-) [6/2020]	219.83 (-) [346.63]	213.80 (126.80) [-]
1523	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1524	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2026]	16,216.00 (-) [16,216.00]	1,458.67 (0.00) [15]
	<u>Road Transport And Highways</u>				
1525	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	35.51 (0.00) [0]
1526	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	31.00 (0.00) [0]
1527	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [12/2019]	605.84 (-) [605.84]	722.46 (0.00) [17]
1528	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	507.87 (0.00) [-]
1529	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	8.24 (0.00) [0]
1530	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	44.88 (0.00) [0]
1531	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1532	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [10/2019]	720.00 (-) [720.00]	278.01 (0.00) [-]
1533	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [7/2019]	478.51 (-) [478.00]	409.17 (-0.51) [69]
1534	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	59.44 (0.00) [0]
1535	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [283.51]	126.38 (0.00) [0]
1536	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	62.79 (0.00) [0]
1537	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE	12/2017	12/2019 (-)	200.34 (-)	31.00 (0.00)

	WITH PAVED S		[12/2019]	[200.34]	[0]
1538	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [12/2019]	282.08 (-) [282.08]	77.05 (0.00) [6]
1539	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	88.00 (0.00) [0]
1540	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	144.27 (0.00) [0]
1541	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [12/2019]	234.88 (-) [208.89]	118.26 (-25.99) [24]
1542	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.31 (0.00) [0]
1543	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1544	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1545	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Coal</u>				
1546	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	308.29 (0.00) [0]
1547	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.00 (0.00) [0]
1548	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2019]	2,661.73 (-) [2,661.73]	258.98 (0.00) [0]
1549	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1550	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	460.96 (0.00) [24]
1551	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.00 (0.00) [0]
	<u>Health And Family Welfare</u>				
1552	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [6/2019]	244.00 (-) [244.00]	241.39 (0.00) [9]
1553	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [2/2020]	651.99 (-) [651.99]	112.82 (0.00) [-]
1554	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2020]	355.15 (-) [355.15]	148.84 (0.00) [12]
	<u>Petroleum</u>				
1555	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,696.00]	33.85 (-16.00) [-15]
1556	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019	2,934.40	1,409.29

			(-) [9/2019]	(-) [2,934.40]	(0.00) [0]
1557	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	157.26 (0.00) [0]
1558	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1559	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (-) [11/2019]	694.00 (-) [694.00]	671.48 (0.00) [13]
1560	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [3/2021]	163.02 (-) [163.02]	44.00 (0.00) [11]
	<u>Power</u>				
1561	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (1/2020) [1/2020]	454.11 (-) [454.11]	287.52 (0.00) [21]
1562	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,592.34]	443.47 (210.50) [29]
	<u>Railways</u>				
1563	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (-) [2,373.00]	485.04 (1,345.60) [324]
1564	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (12/2017) [3/2020]	1,106.62 (-) [1,536.44]	815.11 (429.82) [111]
1565	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [9/2021]	255.64 (-) [272.20]	140.00 (16.56) [-]
1566	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	4/2011	/ (-) [0/0]	289.64 (-) [760.00]	0.13 (470.36) [0]
1567	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1568	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1569	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1570	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [3/2025]	393.46 (154.30) [1,026.00]	182.49 (632.54) [216]
1571	MM FROM PANSKURA-GHATAL NL	4/2011	0/0 (-) [3/2030]	276.69 (-) [426.00]	0.00 (149.31) [-]
1572	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (3/2022) [3/2022]	221.42 (-) [380.00]	38.18 (158.58) [-]
1573	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (-) [614.00]	271.06 (316.68) [12]
1574	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	181.63 (9.73) [-21]
1575	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	2,106.28 (435.44) [141]

1576	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [2,913.50]	842.61 (-0.01) [108]
1577	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1578	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,110.08 (307.50) [108]
1579	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	1/1991	12/2021 (-) [12/2021]	1,013.45 (-) [1,428.00]	484.82 (414.55) [0]
1580	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,670.01]	847.87 (481.10) [72]
1581	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
Road Transport And Highways					
1582	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [12/2019]	1,083.00 (-) [1,083.00]	26.64 (0.00) [18]
1583	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2020]	998.79 (-) [998.79]	1,775.04 (0.00) [82]
1584	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [12/2019]	1,078.84 (-) [1,078.84]	2,173.80 (0.00) [76]
1585	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [12/2019]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [63]
1586	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2020]	361.15 (-) [361.15]	144.71 (0.00) [-]
1587	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	28.21 (0.00) [0]
1588	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (11/2019) [11/2019]	271.17 (291.20) [291.20]	79.24 (20.03) [12]
1589	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [8/2021]	160.27 (213.97) [213.97]	20.11 (53.70) [24]
1590	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [12/2019]	229.37 (-) [229.37]	78.31 (0.00) [13]
1591	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [8/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [24]
1592	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [10/2020]	254.30 (254.30) [254.30]	19.76 (0.00) [0]
1593	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (-) [767.03]	502.91 (0.00) [13]
1594	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [6/2020]	702.16 (-) [702.16]	733.33 (0.00) [71]
1595	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	636.36 (120.10) [0]

1596	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	703.65 (114.56) [19]
1597	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/	1,261.98	0.00
			(-) [0/0]	(-) [1,261.98]	(0.00) [0]
1598	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (7/2019) [7/2019]	279.70 (398.52) [398.52]	314.34 (118.82) [23]
1599	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (-) [0/0]	396.86 (396.86) [396.86]	175.31 (0.00) [0]
1600	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1601	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/	1,665.00	3,059.39
			(-) [6/2019]	(-) [1,665.00]	(0.00) [-]
1602	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [11/2019]	202.69 (202.69) [202.69]	75.72 (0.00) [0]
1603	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [11/2020]	218.70 (218.70) [218.70]	17.84 (0.00) [0]
1604	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [9/2020]	426.18 (426.18) [426.18]	217.48 (0.00) [0]
	<u>Steel</u>				
1605	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [9/2020]	263.36 (-) [263.36]	0.60 (0.00) [0]
	<u>Urban Development</u>				
1606	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [10/2019]	156.57 (-) [156.57]	156.13 (0.00) [38]
1607	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1608	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	126.07 (0.00) [15]
	Total			19,17,796.07 (3,78,867.20) [23,05,860.33]	9,35,021.39 (3,88,064.26)

North-East Central Sector Project's Details

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.06.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (8/2019) [8/2019]	2,496.90 (7,419.34) [7,419.34]	7,327.76 (4,922.44) [116]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,868.18 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	0.00 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	240.21 (0.00) [21]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	174.80 (0.00) [15]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	182.19 (0.00) [0]
7	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [0/0]	210.50 (-) [210.50]	0.00 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	69.97 (0.00) [0]
9	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	0.00 (0.00) [0]
10	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	0.00 (0.00) [0]
11	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	0.00 (0.00) [0]
12	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	0.00 (0.00) [0]
13	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	0.00 (0.00) [0]
14	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	94.49 (16.07) [36]
15	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM	4/2016	/	245.79	128.92

	21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37		(-) [9/2020]	(-) [245.79]	(0.00) [-]
16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2019]	198.00 (-) [198.00]	195.67 (0.00) [36]
17	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	53.23 (0.00) [0]
18	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	0.00 (0.00) [0]
19	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	211.21 (0.00) [60]
20	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [2/2021]	167.28 (-) [209.71]	47.37 (42.43) [46]
21	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [2/2021]	216.71 (-) [262.62]	31.11 (45.91) [46]
22	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
23	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [12/2020]	434.06 (-) [434.06]	126.58 (0.00) [-]
24	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [2/2021]	284.09 (-) [284.09]	80.64 (0.00) [46]
25	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	37.30 (0.00) [0]
26	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	48.16 (0.00) [0]
27	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	56.15 (0.00) [0]
28	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	24.14 (0.00) [0]
29	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSponding TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [389.45]	275.19 (182.42) [0]
30	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [215.70]	45.21 (35.13) [46]
31	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [2/2021]	168.32 (-) [202.05]	42.83 (33.73) [46]
32	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
33	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
34	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	0.00 (0.00) [0]
35	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM	2/2017	/ (-)	175.06 (-)	0.00 (0.00)

	20.0		[0/0]	[175.06]	[0]
36	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (-) [0/0]	176.12 (-) [176.12]	0.00 (0.00) [0]
37	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (-) [0/0]	199.02 (-) [199.02]	0.00 (0.00) [0]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (-) [0/0]	184.88 (-) [184.88]	0.00 (0.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
39	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
40	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
41	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
42	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	101.40 (0.00) [0]
43	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	460.33 (0.00) [0]
44	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	3.30 (0.00) [0]
45	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
46	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (-) [345.92]	139.45 (142.98) [70]
47	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	244.44 (0.00) [1]
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [682.90]	6.12 (138.99) [0]
49	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,498.18 (0.00) [0]
50	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	145.01 (15.64) [0]
51	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
52	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (-) [700.00]	687.37 (386.00) [0]
53	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	571.56 (-50.32) [-24]
54	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-)	870.96 (-)	454.63 (1,265.05)

			[3/2021]	[2,136.01]	[0]
55	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	606.19 (1,146.80) [12]
	Road Transport And Highways				
56	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [11/2010]	268.08 (-) [268.08]	188.71 (0.00) [0]
57	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [6/2018]	470.20 (-) [630.36]	344.32 (160.16) [0]
58	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
59	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [12/2015]	223.30 (-) [223.30]	61.56 (0.00) [0]
60	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	34.00 (0.00) [0]
61	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	347.18 (0.00) [0]
62	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [10/2017]	289.99 (-) [289.99]	4.48 (0.00) [0]
63	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
64	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	6.27 (0.00) [0]
65	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	48.09 (0.00) [0]
66	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [8/2019]	217.61 (-) [217.61]	451.15 (0.00) [112]
67	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
68	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.68 (7.98) [133]
69	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	292.25 (0.00) [0]
70	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	168.40 (0.00) [0]
71	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [818.00]	105.48 (0.00) [0]
72	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	6.62 (0.00) [0]
73	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	292.24 (0.00) [0]
74	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200	5/2015	5/2018 (-)	454.89 (-)	120.86 (0.00)

	TO KM		[0/0]	[454.89]	[0]
75	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [280.00]	472.00 (0.00) [0]
76	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
77	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
78	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [7/2019]	199.81 (-) [385.13]	319.96 (185.32) [123]
79	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [167.64]	268.94 (0.00) [0]
80	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2019]	208.00 (-) [230.00]	337.08 (22.00) [140]
81	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	326.35 (0.00) [136]
82	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [9/2019]	245.00 (-) [174.34]	224.28 (-70.66) [138]
83	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [11/2014]	218.31 (307.47) [307.47]	239.76 (89.16) [0]
84	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
85	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
86	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	8,818.98 (9,354.83) [108]
	<u>Road Transport And Highways</u>				
87	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	93.52 (-59.80) [36]
	<u>Urban Development</u>				
88	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
89	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
90	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.67 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
91	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [7/2019]	306.28 (-) [306.28]	37.86 (0.00) [2]

92	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [9/2019]	479.20 (-) [479.20]	475.02 (0.00) [16]
93	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	Urban Development				
94	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	MIZORAM				
	Railways				
95	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (-) [5,021.45]	2,933.84 (2,627.98) [96]
	Road Transport And Highways				
96	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	296.28 (182.95) [116]
97	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
98	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
99	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
100	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
101	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
102	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
103	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
104	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
105	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
106	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	789.85 (368.26) [105]
	NAGALAND				
	Railways				
107	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
108	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [3,000.00]	756.82 (673.48) [79]
	Road Transport And Highways				
109	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]

110	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
111	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	3.27 (0.00) [0]
112	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	116.06 (0.00) [0]
113	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
114	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	112.38 (0.00) [0]
115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	0.00 (0.00) [0]
117	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]
118	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	4.55 (0.00) [0]
119	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
120	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
121	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	6.75 (0.00) [0]
123	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	9.21 (0.00) [0]
124	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	187.25 (0.00) [36]
125	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	229.11 (0.00) [36]
126	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	153.61 (0.00) [36]
127	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	SIKKIM				
	Railways				
128	SEVOK RANGPO, NEFR	4/2008	12/2015 (6/2021) [3/2020]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [51]
	Road Transport And Highways				
129	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI	1/2013	2/2013	182.28	185.49

	ROAD IN SOUTH SIKKIM		(9/2017) [12/2019]	(269.14) [269.14]	(86.86) [82]
130	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (-) [151.59]	196.76 (0.00) [76]
131	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	132.27 (0.00) [0]
132	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
133	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	30.70 (0.00) [0]
134	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	78.78 (0.00) [0]
135	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
136	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [388.00]	78.33 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Railways</u>				
137	AGARTALA-AKHAURA NL	4/2012	3/2020 (3/2020) [12/2021]	569.63 (569.63) [650.00]	45.24 (80.37) [21]
	<u>Road Transport And Highways</u>				
138	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	297.12 (0.00) [0]
	<u>Urban Development</u>				
139	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
140	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
141	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			78,631.59 (9,868.78) [1,22,485.79]	51,680.90 (43,854.20)
