

**296th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 Crores and above)
JUNE, 2010**



Guru Govind Singh Refinery



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-6
Summary of Projects	7-16
Graph	17-26
Sector wise analysis of projects	27-54

EXECUTIVE SUMMARY

The 296th Flash Report for June' 2010, that contains information on the status of 594 projects in the Central Sector, each costing Rs. 150 Crores and above. Since April' 2010, Flash report is prepared for the central sector projects costing Rs 150 Crores and above. During June' 2010, five projects have reported completion and have been dropped from the monitor of this Ministry. During June' 2010, three projects, one project of Coal, and two projects of Petroleum sector have shown considerable improvement over the completion schedule reported earlier.

The online submission of the implementation Status Report of the ongoing projects has not been provided/updated regularly by some of the project agencies leading to under utilization of online computerized monitoring system (OCMS) developed by this Ministry for effective monitoring. Only 404 out of 594 projects were updated either by the concerned project agencies online or the data has been entered locally by the staff of this Ministry. The information regarding 190 projects were not updated/received by this Ministry. Sector-wise number of ongoing projects along with status of online reporting is given below:

S. No.	Sector	Projects on monitor	Reported Online	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	135	122	40
2.	RAILWAYS	135	69	7
3.	POWER	83	67	2
4.	PETROLEUM	78	65	21
5.	COAL	39	37	2
6.	TELECOMMUNICATION	58	24	5
7.	STEEL	21	8	1
8.	SHIPPING & PORTS	22	10	2
9.	CIVIL AVIATION	8	-	-
10.	FERTILISERS	6	-	-
11.	ATOMIC ENERGY	4	-	1
12.	URBAN DEVELOPMENT	2	2	1
13.	MINES	1	-	-
14.	HEALTH & FW	1	-	-
15.	WATER RESOURCES	1	-	-
Total		594	404	82

2. Eighty two (82) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1 to 24 months in respect of projects relating to Atomic Energy, Coal, Steel, Petroleum, Power, Railways, Road

Transport and Highways, Shipping & Ports, Telecommunications and Urban Development sectors.

3. In the **Atomic Energy sector**, Kaiga Units 3 and 4, Project (NPCIL) has shown additional delay of 2 months due to the continued problem of non availability of fuel.
4. In the **Coal sector**, Manikpur OC expansion project has reported additional delay of 12 months whereas Kakatiya Longwal project has reported considerable improvement over the completion schedule reported earlier. However no specific reason has been reported by the project authorities.
5. In the **Steel Sector**, Expansion of Salem Steel Plant has reported additional delay of 2 months due to delay in supply of equipments.
6. In the **Petroleum Sector**, 19 projects have reported additional delays in the range of 1-23 months, whereas two projects have shown considerable improvement over the completion schedule reported earlier. Jagdishpur-Haldia pipeline project of GAIL has reported improvement of 10 months due to revival of fertilizer plants and availability of gas at Haldia landfall point. Installation of facilities for improvement in diesel quality (IOCL) has reported improvement of 4 months due to availability of raw material. Development of B22 Cluster Fields has reported additional delay of 1 month due to pending court cases. Additional Gas Processing Facility at Hazira has reported additional delay of 1 month due to late issue of Notice inviting tenders (NIT). VKPL Upgradation and Laying of Spurline to Bhilwara has reported additional delay of 1 month due to delay in tender process, inclement weather conditions and queries by vendors. MSQ Improvement project and Heera Reconstruction has reported additional delay of 2 month and 9 months respectively due to delay in installation and drilling work by the contractor. Additional Gas processing units at (ONGC) Uran, Mumbai has reported additional delay of 2 months due to delay in tender process. MSQ Upgradation Project at Gawahati Refinery and Upgradation Project at Digboi Refinery have reported additional delay of 3 months each due to poor response to consultancy bids, frequent bands and insufficient transportation of material/equipment. MSQ Upgradation Project at Barauni Refinery has reported additional delay of 3 months due to backing out of reputed PSU consultants in last moment, slow progress by M/S BHEL in power plant jobs and delay by BPCL in supply of compressor package by 11 month. Integrated offshore crude Oil handling facilities at Paradip has reported additional delay of 3 months due to slow progress of the work by the contractor. Development of C-Series Fields have reported additional delays of 5 months due to sinking of jacket in sea during transportation from Abudhavi. MNW – NF Bridge Project at Hazira (ONGC) has reported additional delays of 5 months due to adverse weather conditions. Bawana-Nangal Pipeline Project has reported additional delays of 6 months due to abnormally high demand of land and crops compensation by farmers of UP and Punjab. Residue upgradation and MS/HSD quality improvement project, Diesel Hydro Treatment Project BRPL Dhaligaon and Dahej-Vijaypur Pipe Line Project (Phase-II) – have reported additional delay of 2 months, 3 months and 6 months respectively, however no reasons have been provided by the project authorities. Mumbai High South redevelopment PH-2 has reported additional delay of 23 months due to detailed engineering and delay in procurement activities.
7. In the **Power Sector**, 2 projects have reported additional delays in the range of 2-4 months. KORBA STPP Stage-III has reported additional delay of 2 months, due to slow progress of work and delay in supply of equipments. BARH STPP, 3x660 MW has reported additional

delay of 4 months due to continued delay in supply of material by M/s Power Machine, Russia.

8. In the **Road Transport and Highways Sector**, 40 projects have reported additional delay in the range of 1-24 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, Termination of contracts due to poor performance and delay in land acquisition in forest clearance , slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such delays.
9. In the **Railway Sector**, 7 projects have shown additional delays in the range of 3-30 months. Raichur- Guntakal of SCR has reported additional delay of 5 months due to delay in approval of Engineers Supports Partnership (ESP) and land acquisition. Rajatgarh-Barrang (LD) ECOR, have shown delays of 6 months respectively due to slow progress of work by the contractor. Bilaspur- Urukura (DL), Bharuch – Samini- Dahej (GC), Utratia-Zafrabad, Conversion of 1500 Volts DC Traction to 25 KV AC WR and Abohar-Fazilka have reported additional delays of 4 months, 3 months, 12 months and 6 months respectively, however, no specific reasons have been given by the project authorities.
10. In the **Shipping & Ports Sector**, 2 projects have shown additional delays in the range of 2-3 months. Rail connectivity to ICTT at Vallarpadam project has shown additional delay of 3 months due to slow progress by the contractor Development & Operation of an International Container project has shown additional delay of 2 months however, no specific reason has been given by the project authorities.
10. In the **Telecommunication Sector**, 5 projects have shown additional delays of 2 – 3 months. East-West Transmission Corridor Strengthening Scheme has reported additional delay of 3 months due to Non resolution of funding issue with the World Bank and Ministry of Finance. Convergent Billing and CRM-MTNL, Expansion of Existing 2G & 3G GSM N/W by 750 K GSM Equipment of 3125K and GSM Equipment of 1625K lines have reported additional delays of 3 months, 3 months, and 2 months respectively, however, no specific reasons have been given by the project authorities.
11. In the **Urban Development Sector**, Bangalore Metro Rail Project has reported additional delay of 9 months but no specific reason has been reported by the concerned project authority.

Status as on 01.07.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the following tables.



09/09/2010

(Pankaj Jain)

**Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation**

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	135	7
2	Road Transport & Highways	135	40
3	Power	83	2
4	Petroleum	78	21
5	Telecommunications	58	5
6	Coal	39	2
7	Shipping & Ports	22	2
8	Steel	21	1
9	Civil Aviation	8	0
10	Fertilisers	6	0
11	Atomic Energy	4	1
12	Urban Development	2	1
13	Mines	1	0
14	Health & Family Welfare	1	0
15	Water Resources	1	0
	Total	594	82

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Power</u>				
4	LOWER SUBANSIRI H.E.P (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100221]	6,285.33	09/2010	4,097.17
<u>Telecommunications</u>				
5	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	.00	12/2008	175.77
6	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13


Summary of projects on the Flash Report for the month of June, 2010

I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 150 Cr. & above) Previous Month	579
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Previous Month	1
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Current month	5
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	21
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	594

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 594 projects, 15 projects are ahead of schedule, 105 projects are on schedule and 300 projects are delayed. Of the balance, 114 projects do not have fixed dates of commissioning while 60 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

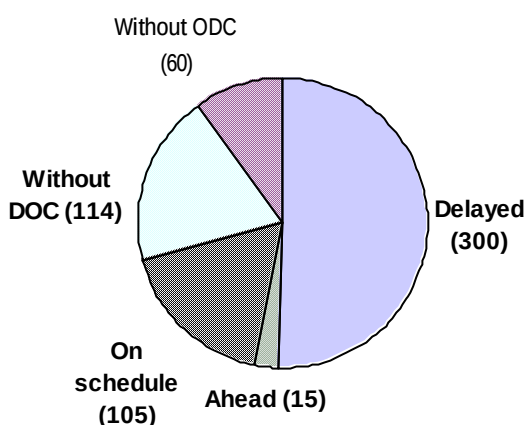

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 594 projects when sanctioned, was of the order of Rs. 624323.66 crore but this was subsequently revised to Rs. 696818.59 crore implying a cost overrun of 11.61%. The expenditure incurred on these projects till June, 2010 is Rs. 290436.56 crore, which is 41.68% of the revised cost of the projects.

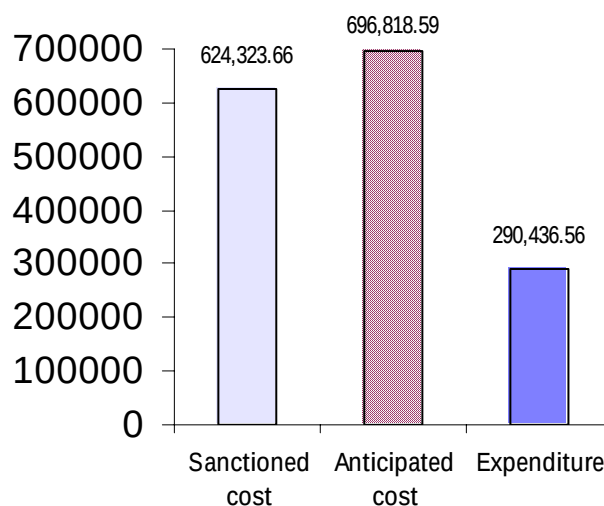

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	579
No of Projects Completed/Dropped/Frozen in Previous Month	1
No of Projects Completed/Dropped/Frozen in Current Month	5
No of Projects added in Current Month	21
No of Projects in Current Month	594

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original	300	15	105	60	114	594	50.51
Latest Approved	334	19	118	55	73	594	56.23

III. (A) Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	490	492,124.39	532,067.58	215,957.04	40.60	39,943.19	8.10
Latest Approved	104	132,199.27	164,751.01	74,479.52	45.20	32,551.74	24.60
Total	594	624,323.66	696,818.59	290,436.56	41.68	72494.93	11.61

III. (B) Delayed Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	300	303,783.53	372,518.40	184,666.36	49.60	68,734.87	22.60
Latest Approved	334	66,390.45	390,498.33	207,217.52	53.10	324,107.88	488.20

IV. Additional Delayed Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Latest Approved	82	83,889.77	97,701.85	50,642.22	51.80	13,812.08	16.50
Total	82	83,889.77	97,701.85	50,642.22	51.83	13812.08	16.46

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
LOWER SUBANSIRI H.E.P (NHPC)	09/2003	6,285.33	09/2010	6,285.33	12/2012	4,097.17
<u>Telecommunications</u>						
DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES	02/2007	463.61	12/2009	488.76	06/2010	106.13
EXPANSION OF 750K GSM LINES	10/2006	.00	12/2008	278.16	01/2010	175.77
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO.-4	05/2007	248.94	08/2009	248.94	06/2010	164.48
<u>Petroleum</u>						
CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)	04/2003	1,635.00	05/2006	2,147.79	06/2012	2,095.36

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
Telecommunications					
GSM equipment of 1700000Lines (2G) 234100 lines 3(	10/2008	677.75	10/2009	677.75	9/2010
FTTH BO-3474 /08-09 in Mumbai	9/2011	389.86	9/2011	389.86	9/2011
ERP implementation in BSNL on Turnkey basis	10/2009	384.00	10/2010	384.00	11/2010
Expn of existing 2G & 3G GSM N/W by 750k	10/2008	180.53	6/2010	180.53	9/2010
GSM equipment of 1867000Lines (2G) 383000 lines 3(	8/2008	868.00	8/2009	868.00	9/2010
GSM equipment of 614000Lines (2G) 150000lines 3(G)	1/2009	315.19	1/2010	315.19	8/2010
GSM equipment of 1900000Lines (2G) 335500lines 3(G)	1/2009	848.70	1/2010	848.70	9/2010
Provision of data network for CWG delhi	11/2009	488.76	10/2010	488.76	10/2010
GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph	9/2009	577.35	9/2010	577.35	8/2010
GSM equipment of 1100000Lines (2G) UP East Phase	9/2009	624.75	9/2010	624.75	8/2010
GSM equipment of 1500000Lines (2G) 264700lines 3(G)	1/2009	922.91	1/2010	922.91	8/2010
GSM equipment of 375000Lines (2G) 75000lines 3(G)	6/2008	170.23	6/2009	167.20	8/2010
GSM equipment of 945000Lines (2G) 225000lines 3(G)	10/2007	366.00	10/2008	529.32	8/2010
GSM equipment of 1900000Lines (2G) 401700 lines 3(	1/2009	760.20	1/2010	810.37	8/2010
GSM equipment of 849862Lines (2G) 150138 lines 3(G)	2/2008	584.33	2/2009	584.33	8/2010
GSM equipment of 200000Lines (2G) UP(West)Phase V.	10/2008	336.84	10/2009	336.84	8/2010
GSM equipment of 4,50,000 Lines (2G) Haryana (Phas	9/2008	216.54	9/2009	216.54	8/2010
GSM equipment of 975000Lines (2G) 325000 lines 3(G)	2/2009	625.53	2/2010	625.53	8/2010
GSM equipment of 900000Lines (2G) PunjabPhase V.2	9/2008	241.49	9/2009	241.49	9/2010
GSM equipment of 799000Lines (2G) 101000 lines 3(G)	3/2008	328.13	3/2009	328.13	8/2010
GSM equipment of 1625000Lines (2G) 325000 lines 3(	11/2009	916.70	11/2010	916.70	8/2010

VII. Milestones (Cumulative due & achieved)

Total	1938
Achieved up to month	744

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	07/2010	08/2010	1
<u>Coal</u>						
KAKATIYA LAONGWALL	453.63	453.63	N.A.	03/2013	12/2012	-3
MANIKPUR OC EXPANTION	321.42	321.50	03/2013	03/2013	03/2014	12
<u>Steel</u>						
EXPANSION OF SALEM STEEL PLANT	1,902.00	1,902.00	N.A.	06/2010	08/2010	2
<u>Petroleum</u>						
JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	7,596.18	6,652.22	01/2013	01/2013	03/2012	-10
INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL)	1,876.00	3,153.00	04/2009	06/2010	02/2010	-4
DEVELOPMENT OF B-22 CLUSTER FIELDS	1,552.63	2,920.82	02/2009	04/2012	05/2012	1
ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA	370.11	370.11	04/2011	06/2012	07/2012	1
VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI	463.32	463.32	N.A.	05/2011	06/2011	1
BNPL SPURLINE (UTTRANCHAL & PUNJAB)	540.92	540.92	N.A.	05/2011	06/2011	1
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT	5,693.00	6,898.00	01/2010	08/2010	10/2010	2
MSQ IMPROVMENT PROJECT	293.60	293.60	12/2009	07/2010	09/2010	2
ADDITIONAL GAS PROCESSING UNITS AT URAN	1,797.35	1,797.35	12/2011	09/2012	11/2012	2
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON	1,431.91	1,675.72	09/2009	06/2010	09/2010	3
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY	372.00	325.00	02/2010	06/2010	09/2010	3
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY	356.00	300.00	02/2010	06/2010	09/2010	3
MSQ UPGRADATION PROJECT AT BARAUNI REFINERY	1,492.00	1,505.00	04/2010	06/2010	09/2010	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
Integrated offshore crude Oil handling facilities at Paradip	1,492.33	1,492.33	06/2012	03/2012	06/2012	3
DEVELOPMENT OF C-SERIES FIELDS	3,195.16	2,800.00	12/2008	10/2010	03/2011	5
MNW-NF BRIDGE PROJECT	175.21	162.12	03/2009	12/2010	05/2011	5
BAWANA NANGAL PIPE LINE PROJECT	1,816.07	1,816.07	10/2010	10/2010	04/2011	6
DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)	4,429.38	2,800.00	10/2010	10/2010	04/2011	6
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I	1,512.00	975.00	10/2011	10/2010	04/2011	6
HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	2,305.30	2,305.30	06/2010	06/2010	03/2011	9
MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	1,252.75	8,813.41	06/2009	04/2011	03/2013	23
Power						
KORBA STPP STAGE-III	2,448.50	2,448.49	02/2010	08/2010	10/2010	2
BARH STPP(3X660MW) NTPC	8,692.97	8,692.97	11/2010	12/2013	04/2014	4
Railways						
BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	200.80	200.80	N.A.	09/2010	12/2010	3
BILASPUR-URKURA (DL)	151.52	273.00	N.A.	11/2010	03/2011	4
RAICHUR-GUNTAKAL(DL)(SCR)	136.62	221.90	12/2007	07/2010	12/2010	5
RAJATGARH-BARANG(LD),ECOR	166.16	243.40	N.A.	06/2010	12/2010	6
ABOHAR- FAZILKA	86.44	209.57	03/2009	02/2010	08/2010	6
UTRATIA-ZAFRABAD (LINE DOUBLING)	325.00	496.03	03/2010	12/2011	12/2012	12
CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	273.67	1,160.52	N.A.	06/2010	12/2012	30
Road Transport & Highways						
AMRITSAR-WAGHA BORDER	205.88	205.88	06/2010	06/2010	07/2010	1
VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)	467.93	467.93	03/2005	06/2010	08/2010	2
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5	480.00	480.00	11/2007	06/2010	08/2010	2
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120	323.36	323.36	03/2008	06/2010	08/2010	2
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	507.49	507.49	03/2008	05/2010	07/2010	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1	263.00	263.00	02/2009	05/2010	07/2010	2
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	225.00	225.00	10/2008	10/2010	12/2010	2
NEW MANGALORE PORT NH-17 AND 48	196.50	196.50	06/2008	06/2010	08/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418	205.92	205.92	08/2009	06/2010	08/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251	194.80	194.80	08/2009	06/2010	08/2010	2
MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS- 2/BOT/AP-6),NH-7	360.42	360.42	11/2009	05/2010	07/2010	2
COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358	106.00	193.00	08/2006	05/2010	08/2010	3
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	318.00	207.56	08/2004	06/2010	09/2010	3
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	629.00	629.00	11/2010	06/2010	09/2010	3
SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	151.30	151.30	10/2008	12/2010	03/2011	3
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3	239.19	239.19	09/2009	06/2010	09/2010	3
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463	243.64	243.64	08/2009	05/2010	08/2010	3
PONDICHERY - TINDIVANAU NH-66	285.00	285.00	07/2010	07/2010	10/2010	3
BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4	565.00	565.00	07/2010	07/2010	10/2010	3
THANJAUR-TRICHY,NH- 67(NHAI)	280.00	280.00	06/2009	06/2010	10/2010	4
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293	208.46	208.46	08/2009	06/2010	10/2010	4
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376	243.38	243.38	09/2008	06/2010	10/2010	4
KURALI-KIRATPUR, NH-21	309.00	309.00	06/2010	06/2010	10/2010	4
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	193.09	193.09	03/2008	07/2010	12/2010	5
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80	166.27	166.27	03/2008	07/2010	12/2010	5

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI	441.00	441.00	07/2010	07/2010	12/2010	5
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31	205.73	205.73	07/2004	06/2010	12/2010	6
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	359.00	359.00	03/2009	06/2010	12/2010	6
DARBHANGA- MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI)	291.80	291.80	06/2008	06/2010	12/2010	6
SILIGURI TO ISLAMPUR (WB-7)	225.00	225.00	07/2008	06/2010	12/2010	6
RINGBUNDS TO JHAJHANPUR (BR-6)	340.00	340.00	06/2008	06/2010	12/2010	6
ASSAM/WB BORDER TO GAIRKATTA (WB-1)	221.82	221.82	11/2008	06/2010	12/2010	6
BARA TO ORAI, NH-2, 25	465.00	465.00	04/2009	06/2010	12/2010	6
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS- 1/BOT/MP-2),NH7	407.60	407.60	06/2010	06/2010	12/2010	6
AURANG-RAIPUR, NH-6, KM.232 TO KM.281	190.00	190.00	01/2009	05/2010	12/2010	7
NAGPUR-KONDHALI,NH- 6(NHAI)	168.00	168.00	12/2008	05/2010	12/2010	7
GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500	579.00	579.00	04/2009	05/2010	01/2011	8
JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25	158.06	158.06	08/2005	06/2010	03/2011	9
BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	230.00	230.00	06/2005	12/2010	12/2011	12
MAIBANG TO LUNDING (AS- 24), KM.111.000 TO KM.126.450	155.04	155.04	11/2008	12/2010	12/2012	24
Shipping & Ports						
DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA	2,118.00	2,118.00	11/2004	08/2010	10/2010	2
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	245.67	298.17	04/2009	03/2010	06/2010	3
Telecommunications						
GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3	1,799.94	1,799.94	09/2009	06/2010	08/2010	2
GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M	908.30	916.70	08/2009	06/2010	08/2010	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME	803.70	803.76	06/2009	09/2010	12/2010	3
CONVERGENT BILLING AND CRM-MTNL(DELHI)	249.00	229.41	02/2007	12/2010	03/2011	3
EXPANSION OF EXISTING 2G&3G GSM NW BY 750 KPE NO	180.53	180.53	12/2009	06/2010	09/2010	3
<u>Urban Development</u>						
BANGALORE METRO RAIL PROJECT	6,395.00	11,609.00	12/2011	06/2012	03/2013	9

Number of projects reporting additional delay = 82


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

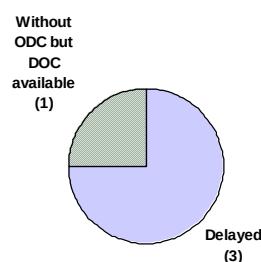

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till June, 2010 is Rs. 18410.25 Crores.

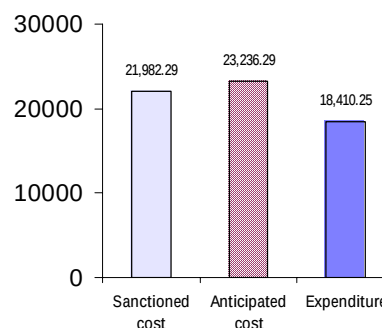


2. Sector: - Civil Aviation

Number of Projects	8
Number of Projects on schedule	3
Number of Projects Delayed	2
Number of Projects Wo_Doc_Original	2
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule, 2 projects are delayed and 2 projects are original date of commissioning and 1 projects are Wo_Odc_original.

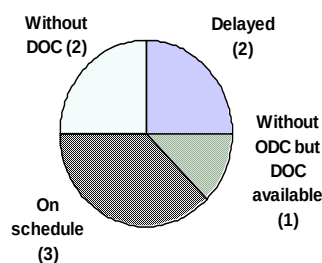

Investment Scenario

The total cost of implementation of 8 projects when sanctioned, was of the order of Rs. 5142.67 Crores but this was subsequently revised to Rs. 5142.67 Crores. The expenditure incurred on these projects till June, 2010 is Rs 1688.49 Crores.

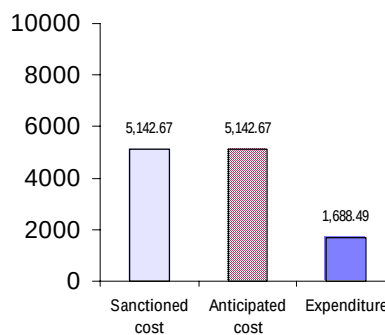


3. Sector: - Coal

Number of Projects	39
Number of Projects on schedule	8
Number of Projects Delayed	21
Number of Projects Ahead	3
Number of Projects Wo_ODC_Original	6
Number of Projects Wo_DOC_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 39 projects, 8 projects are on schedule, 21 projects are delayed and 3 projects are ahead and 1 Project W_Odc_Original .

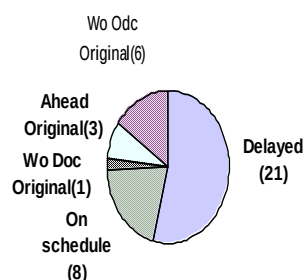

Investment Scenario

The total cost of implementation of 39 projects when sanctioned, was of the order of Rs. 24242.02 Crores but this was subsequently revised to Rs. 26295.92 Crores. The expenditure incurred on these projects till June, 2010 is Rs 9541.83 Crores

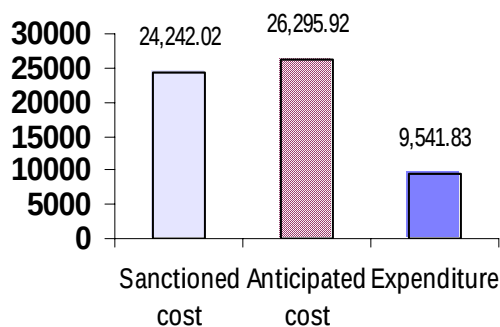


4. Sector: - Petroleum

Number of Projects	78
Number of Projects on schedule	22
Number of Projects Delayed	43
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	1
Number of Projects Without original date of commissioning	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 22 projects are on schedule, 43 projects are delayed and 3 projects are ahead and 1 projects is without date of commissioning and 9 Project is Without original date of commissioning.

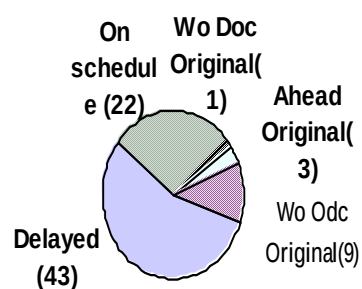

Investment Scenario

The total cost of implementation of 82 projects when sanctioned, was of the order of Rs. 154318.74 Crores but this was subsequently revised to Rs. 172142.54 Crores. The expenditure incurred on these projects till June, 2010 is Rs. 58893.73 Crores.

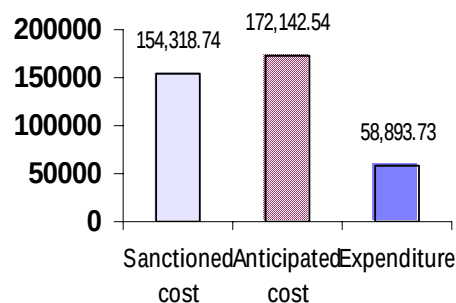


5. Sector: - Power


Number of Projects	83
Number of Projects on schedule	46
Number of Projects Delayed	32
Number of Projects Wo_Doc_Original	4
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 83 projects, 46 projects are on schedule, 32 projects are delayed, 4 projects are without date of commissioning and 1 project is without original date of commissioning

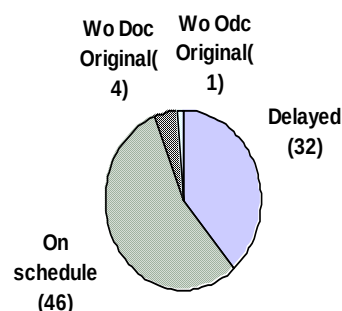

Investment Scenario

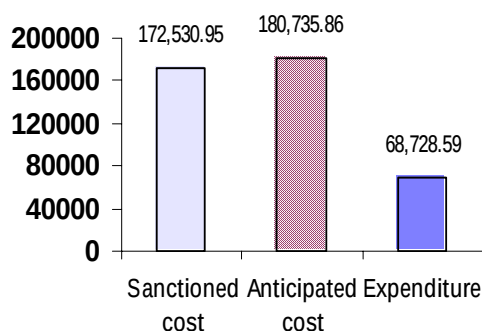


The total cost of implementation of 83 projects when sanctioned, was of the order of Rs. 172530.95 Crores but this was subsequently revised to Rs. 180735.86 Crores. The expenditure incurred on these projects till June, 2010 is Rs. 68728.59 Crores.

6. Sector: - Railways

Number of Projects	135
Number of Projects on schedule	6
Number of Projects Delayed	37
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	49
Number of Projects Wo_Odc_Original	41


Brief Analysis

Project Status with out respect Original Schedule: Out of 135 projects, 6 projects are on schedule, 37 projects are delayed, 2 projects is ahead. 49 projects are Without date of commissioning and 41 projects are without original date of commissioning.



Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs. 51007.64 Crores but this was subsequently revised to Rs. 103651.54 Crores. The expenditure incurred on these projects till June, 2010 is Rs. 40686.33 Crores.

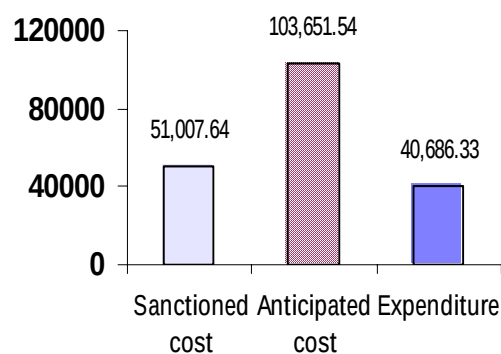


7. Sector: - Road Transport and Highways

Number of Projects	135
Number of Projects on schedule	4
Number of Projects Delayed	121
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	8


Brief Analysis

Project Status with respect to Original Schedule: Out of 135 projects, 4 projects are on schedule, 121 projects are delayed, 2 projects are ahead and 8 projects are without date of commissioning.

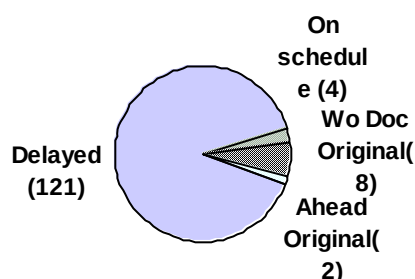

Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs 41863.55 Crores but this was subsequently revised to Rs. 42136.98 Crores. The expenditure incurred on these projects till June, 2010 is Rs. 35141.65 Crores.

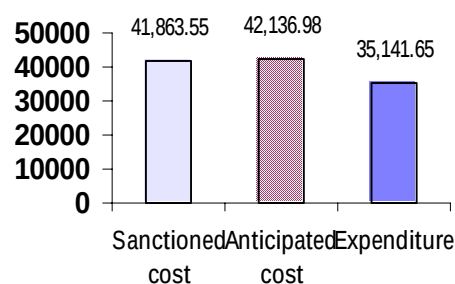


8. Sector: - Shipping and Ports

Number of Projects	22
Number of Projects on schedule	9
Number of Projects Delayed	8
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 9 projects are on schedule, 8 projects are delayed, 2 projects are ahead and 3 projects are without date of commissioning.



Investment Scenario

The total cost of implementation of 22 projects when sanctioned, was of the order of Rs.24047.63 Crores but this was subsequently revised to Rs. 24630.99 Crores. The expenditure incurred on these projects till June, 2010 is Rs. 3636.22 Crores.

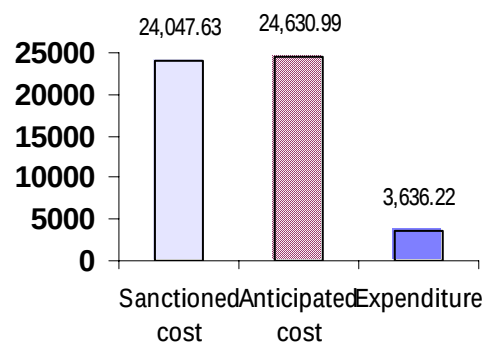


9. Sector: - Steel

Number of Projects	21
Number of Projects on schedule	1
Number of Projects Delayed	10
Number of Projects Wo_Odc_Original	10


Brief Analysis

Project Status with respect to Original Schedule: Out of 21 projects, 1 projects are on schedule, 10 projects are delayed and 10 projects are Wo_Odc_Original.

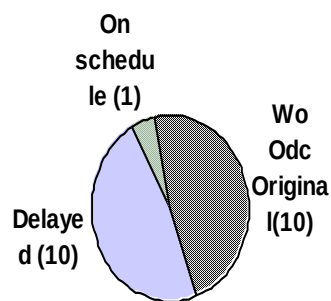

Investment Scenario

The total cost of implementation of 29 projects when sanctioned, was of the order of Rs.44492.92 Crores but this was subsequently revised to Rs. 52744.90 Crores. The expenditure incurred on these projects till June, 2010 is Rs. 22880.17 Crores.

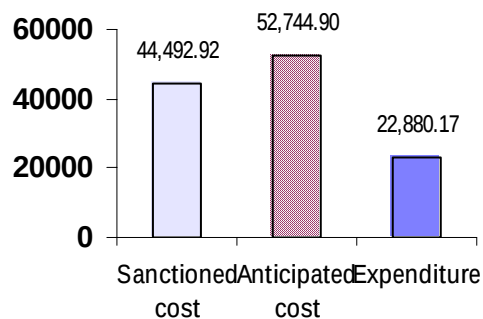


10. Sector: - Telecommunications

Number of Projects	58
Number of Projects Delayed	44
Number of Projects Ahead	3
Number of Projects on Schedule	2
Number of Projects Wo_Doc_Original	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 58 projects, 44 projects are delayed and 9 projects are with out date of commissioning, 3 Projects are ahead and 2 projects are on schedule.

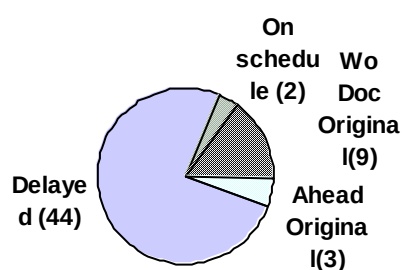

Investment Scenario

The total cost of implementation of 58 projects when sanctioned, was of the order of Rs 27675.46 Crores but this was subsequently revised to Rs. 27693.47 Crores. The expenditure incurred on these projects till June, 2010 is Rs 9385.98 Crores.

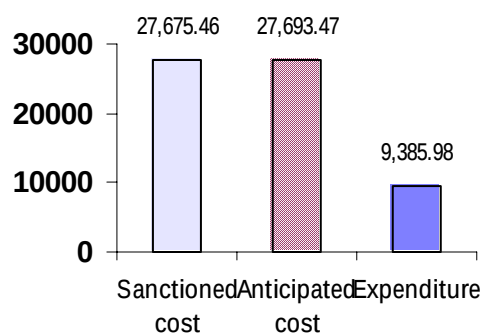

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	23,236.29
Civil Aviation	8	5,142.67	5,081.67	5,142.67
Coal	39	24,242.02	25,614.14	26,295.92
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,091.51	4,091.51
Steel	21	44,492.92	46,020.92	52,744.90
Petroleum	78	154,318.74	167,385.43	172,142.54
Power	83	172,530.95	174,345.03	180,735.86
Health & Family Welfare	1	71.18	422.60	443.15
Railways	135	51,007.64	63,348.29	103,651.54
Road Transport & Highways	135	41,863.55	41,863.55	42,136.98
Shipping & Ports	22	24,047.63	24,047.63	24,630.99
Telecommunications	58	27,675.46	27,496.93	27,693.47
Urban Development	2	15,071.00	16,763.36	27,368.36
Water Resources	1	542.90	542.90	1,187.00
Grand total	594	592,397.87	624,323.66	696,818.59

(Jun,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,536.00	10/2009 09/2007	08/2010	35(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	486.37	-	04/2011	-	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	13,002.00	12/2008	06/2011	30(O)	61/119
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,440.88	09/2010	09/2011	12(O)	8/80
Total			21,982.29	23,236.29	18,465.25				140/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	239.59	-	06/2010	-	1/24
6	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	143.97	06/2010	06/2010	0(O)	0/0
7	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]	06/2009	213.35	213.35	112.00	09/2010	11/2010	2(O)	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]	08/2008	1,273.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0
9	Extension of Secondary Runway(K2) - [N04000056]	08/2008	230.00	230.00	188.12	01/2011	01/2011	0(O)	0/0
10	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	579.26	05/2011	08/2011	3(O)	0/0
11	C/o new Airport-SH: E/W in cutting and filling geogrid - [N04000050]	01/2009	264.29	264.29	10.02	01/2011	-	-	0/0
12	GAGAN PROJECT - [N04000065]	09/2008	393.60	393.60	160.29	06/2013	-	-	0/0
Total			5,142.67	5,142.67	1,688.49				1/24
<u>Coal</u>									
13	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,443.24	06/2009	09/2010	15(O)	59/26
14	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	484.88	03/2009	03/2011	24(O)	0/0
15	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,985.97	06/2009	06/2011	24(O)	41/24
16	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	59.60	03/2010	03/2012	24(O)	0/4
17	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	997.01	03/2010	03/2012	24(O)	3/7
18	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66	341.63	101.25	03/2011	03/2012	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]	10/2006	249.03	249.03	37.64	03/2012	03/2012	0(O)	0/42
20	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	0.59	03/2012	03/2012	0(O)	0/0
21	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	248.03	03/2012	03/2012	0(O)	0/0
22	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.57	418.57	89.44	-	03/2012	-	0/27
23	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]	03/2010	181.91	181.19	0.07	-	03/2012	-	0/34
24	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	882.57	08/2012	08/2012	0(O)	0/0
25	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34	779.26	102.38	03/2013	09/2012	-6(O)	2/22
26	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63	453.63	48.86	-	12/2012	-	0/44
27	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88	741.56	135.35	03/2010	03/2013	36(O)	0/1
28	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	553.05	03/2011 03/2013	03/2013	0(R3)	0/4
29	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04	437.34	136.41	03/2012	03/2013	12(O)	0/1
30	MAGADH OC (CCL) - [N06000015]	07/2006	469.78	706.40	16.17	07/2012	03/2013	8(O)	0/1
31	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78	467.78	11.42	-	03/2013	-	0/83
32	KANIHA OCP - [N06000035]	12/2007	457.77	457.77	51.40	03/2012	03/2013	12(O)	0/0
33	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93	479.53	183.34	03/2013	03/2013	0(O)	0/0
34	BINA EXTN. PROJ - [N06000019]	11/2006	168.97	168.97	140.50	03/2014	11/2013	-4(O)	1/1
35	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53	1,943.66	886.62	03/2010	03/2014	48(O)	2/6
36	CHURCHA UG - [N06000046]	06/2008	462.35	462.35	243.97	06/2014	03/2014	-3(O)	0/0
37	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	3.14	03/2010	03/2014	48(O)	0/0
38	PENGANGA OC - [N06000066]	10/2008	339.77	339.77	-	-	03/2014	-	0/1
39	KARTALI (EAST) OC - [N06000076]	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
40	MANIKPUR OC EXPANTION - [N06000081]	11/2009	321.42	321.50	211.51	03/2013	03/2014	12(O)	0/0
41	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18	287.17	-	11/2009 01/2012	03/2015	38(R3)	0/0
42	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87	395.87	14.20	03/2013	03/2015	24(O)	0/0
43	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
44	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
45	JAGANNATHPOR OC - [N06000075]	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
46	RKP OCP PHASE-I - [N06000079]	03/2010	201.58	209.78	0.18	-	03/2015	-	0/31
47	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04	1,143.54	27.23	03/2014	03/2016	24(O)	1/1
48	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	134.87	03/2014	03/2016	24(O)	0/0
49	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	6.04	03/2015	03/2016	12(O)	0/0
50	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]	11/2009	158.59	198.59	89.06	03/2016	03/2016	0(O)	0/0
51	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07 254.60	254.60	215.84	06/2009	-	-	36/21
Total			24,242.02	26,295.92	9,541.83				145/381
Fertilisers									
52	THAL AMMONIA REVAMP PROJECT - [N08000003]	01/2009	488.75	488.75	-	03/2011	03/2011	0(O)	0/0
53	CAPACITY ENHANCEMENT OF VIJAIPUR-I - [N08000007]	09/2008	325.00	325.00	-	07/2011	07/2011	0(O)	0/0
54	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]	09/2008	438.00	438.00	-	07/2011	07/2011	0(O)	0/0
55	PANIPATH - AMMONIA PLANT FEEDSTOCK PLANT - [N08000004]	01/2010	1,292.84	1,292.84	-	10/2012	10/2012	0(O)	0/0
56	BATHINDA - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000005]	01/2010	1,294.19	1,294.19	-	10/2012	10/2012	0(O)	0/0
57	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]	01/2010	1,478.63	1,478.63	-	10/2012	10/2012	0(O)	0/0
Total			5,317.41	5,317.41	.00				0/0
Mines									
58	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	18/111
Total			4,091.51	4,091.51	3,316.00				18/111
Steel									
59	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	436.54	278.89	-	06/2010	-	1/1
60	BILADILLA IRON ORE DEPOSITE-11B - [N12000017]	01/2009	295.89	295.89	213.74	10/2009	06/2010	8(O)	0/0
61	Deve. of Bailadilla Iron Ore Deposit-II(B)(NMD) - [N12000018]	01/2003	295.89	607.17	213.89	10/2009	06/2010	8(O)	2/21
62	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	97.14	-	06/2010	-	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
63	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	42.02	06/2010	06/2010	0(O)	0/0
64	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	235.61	06/2009	07/2010	13(O)	0/0
65	REBUILDING OF BLAST FURNACE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	594.63	-	07/2010	-	2/1
66	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	120.71	-	07/2010	-	0/0
67	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	84.40	12/2009	08/2010	8(O)	0/0
68	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,592.38	-	08/2010	-	2/6
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	80.00	02/2010	08/2010	6(O)	0/0
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	114.32	02/2010	01/2011	11(O)	0/0
71	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	193.61	-	04/2011	-	0/2
72	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	111.28	232.93	53.11	-	05/2011	-	0/1
73	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	6,203.00	10/2009	06/2011	20(O)	0/126
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	12.00	10/2009	06/2011	20(O)	0/0
75	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	7,995.06	-	06/2011	-	0/6
76	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	4.04	09/2010	12/2011	15(O)	0/0
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,793.00	1,114.89	-	12/2011	-	0/7
78	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	8,128.00	2,506.34	02/2011	03/2013	25(O)	0/0
79	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	6,713.00	1,130.39	-	03/2013	-	0/8
Total			44,492.92	52,744.90	22,880.17				7/180
Petroleum									
80	CRUDE OIL RECEIPT FACILITIES,KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.00	09/2009	12/2009	3(O)	0/0
81	MSQ UPGRADEATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	750.71	12/2009	01/2010	1(O)	0/0
82	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00	3,153.00	2,710.18	04/2009	02/2010	2(R1)	36/36
83	INST. OF FCC GASOLINE DESULPHUN UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	186.58	12/2009	02/2010	2(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
84	CHAINSA-JHAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77 571.64	565.00	411.82	09/2009 03/2010	03/2010	0(R3)	0/0
85	BINA DESPATCH TERMINAL - [N16000078]	05/2007	490.71 639.11	639.11	578.54	12/2009 03/2010	03/2010	0(R3)	0/0
86	BINA KOTA PIPE LINE PROJECT - [N16000079]	07/2007	405.82 -	405.82	354.06	12/2009 03/2010	03/2010	0(R3)	0/0
87	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	14,439.00 -	15,292.00	12,054.37	11/2009 11/2009	05/2010	6(R1)	61/101
88	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66 350.00	389.00	350.96	06/2008 -	05/2010	23(O)	0/0
89	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60 -	289.60	198.16	05/2010 -	05/2010	0(O)	0/0
90	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46 -	643.46	489.52	- -	05/2010	-	0/2
91	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92 -	1,493.49	678.77	06/2006 05/2008	07/2010	26(R1)	0/2
92	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY - [N16000026]	10/2006	638.90 1,030.00	1,030.00	738.04	04/2009 -	07/2010	15(O)	0/0
93	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]	11/2007	396.13 -	396.13	183.41	10/2009 06/2010	07/2010	1(R3)	0/0
94	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31 4,803.00	3,760.00	3,232.20	11/2009 04/2010	08/2010	4(R3)	0/0
95	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]	06/2006	1,431.91 -	1,675.72	1,382.20	09/2009 -	09/2010	12(O)	0/0
96	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00 -	325.00	204.05	02/2010 -	09/2010	7(O)	0/0
97	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00 -	300.00	192.36	02/2010 -	09/2010	7(O)	0/0
98	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00 -	1,505.00	936.39	04/2010 -	09/2010	5(O)	0/0
99	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60 -	293.60	166.42	12/2009 -	09/2010	9(O)	0/0
100	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47 -	900.47	635.71	09/2009 -	09/2010	12(O)	0/0
101	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]	09/2009	2,591.80 3,941.41	3,941.41	2,720.30	12/2009 -	09/2010	9(O)	0/0
102	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA - [N16000017]	06/2005	1,007.83 -	1,077.00	712.81	12/2009 12/2009	10/2010	10(R1)	18/49
103	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00 6,898.00	6,898.00	5,462.74	01/2010 06/2010	10/2010	4(R3)	0/0
104	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07 -	281.07	1.13	10/2010 -	10/2010	0(O)	0/0
105	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]	01/2009	605.40 605.40	605.40	218.00	12/2010 12/2010	12/2010	0(R3)	12/17
106	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]	06/2008	304.40 -	304.40	111.39	12/2010 -	12/2010	0(O)	0/0
107	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]	07/2009	238.68 196.25	196.25	2.28	- -	01/2011	-	1/7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	CAPACITY AUGMENTATION OF AGRA& FERROZABAD REGION - [N16000074]	07/2009	199.57 -	199.57	0.74	- -	01/2011	-	8/5
109	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00 -	224.00	99.05	12/2010 -	02/2011	2(O)	0/0
110	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	600.00	525.82	03/2007 -	03/2011	48(O)	3/3
111	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,200.00	988.06	03/2007 -	03/2011	48(O)	6/6
112	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	371.05	145.95	03/2006 -	03/2011	60(O)	6/6
113	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	2,800.00	2,753.44	12/2008 12/2008	03/2011	27(R3)	0/0
114	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30 -	2,305.30	2,031.18	06/2010 06/2010	03/2011	9(R3)	0/0
115	NORTH TAPTI GAS FIELD DEV. - [N16000085]	07/2008	589.70 -	755.76	-	03/2011 -	03/2011	0(O)	0/0
116	North Tapti Gas Field Development - [N16000096]	01/2010	589.70 755.56	755.56	-	03/2011 -	03/2011	0(O)	0/0
117	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07 1,816.07	1,816.07	237.79	10/2010 04/2011	04/2011	0(R3)	0/0
118	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]	11/2007	4,429.38 4,403.00	2,800.00	1,087.47	10/2010 04/2011	04/2011	0(R3)	0/0
119	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00 1,434.00	975.00	535.65	10/2011 04/2011	04/2011	0(R3)	0/0
120	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93 1,167.00	1,167.00	17.86	11/2011 04/2011	04/2011	0(R3)	0/0
121	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70 -	706.70	440.60	04/2010 -	04/2011	12(O)	0/0
122	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08 -	305.08	52.15	04/2011 -	04/2011	0(O)	0/0
123	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82 2,218.01	2,218.01	1,234.69	03/2005 05/2011	05/2011	0(R3)	0/0
124	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40 -	330.40	0.39	05/2010 -	05/2011	12(O)	0/0
125	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21 -	162.12	58.19	03/2009 -	05/2011	26(O)	0/0
126	BNPL superlines(Uttranchal & Punjab) - [N16000091]	12/2009	540.92 -	540.92	-	05/2011 -	05/2011	0(O)	0/0
127	VKPL Upgradation and Laying of Superlines - [N16000092]	12/2009	463.32 -	463.32	-	05/2011 -	05/2011	0(O)	0/0
128	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]	12/2009	463.32 -	463.32	-	- -	06/2011	-	3/3
129	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]	12/2009	540.92 -	540.92	-	- -	06/2011	-	6/5
130	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00 -	267.00	72.99	- -	08/2011	-	0/1
131	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00 -	3,597.00	144.73	09/2011 -	09/2011	0(O)	0/0
132	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00 -	3,284.00	94.43	09/2011 -	09/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
133	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00 -	820.00	359.51	12/2011 -	12/2011	0(O)	0/0
134	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00 -	349.00	40.73	08/2011 -	12/2011	4(O)	0/0
135	HYDROCRACKER REVAMP & SETTING - [N16000081]	02/2008	825.00 -	825.00	62.54	12/2011 -	12/2011	0(O)	0/0
136	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	06/2007	736.65 -	736.65	154.37	12/2011 -	12/2011	0(O)	0/0
137	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,163.64	-	12/2011 -	12/2011	0(O)	0/0
138	Additional Development of D-1 Field - [N16000097]	01/2010	2,163.64 -	2,163.64	-	12/2011 -	12/2011	0(O)	0/0
139	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02 -	740.02	298.68	03/2010 03/2012	03/2012	0(R1)	0/0
140	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]	06/2009	3,032.00 348.00	348.00	6.03	- -	03/2012	-	5/7
141	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	07/2009	7,596.18 6,652.22	6,652.22	0.50	01/2013 -	03/2012	-10(O)	0/0
142	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 5,633.44	5,633.44	0.61	03/2010 08/2010	04/2012	20(R1)	0/0
143	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29 -	6,326.40	859.50	05/2010 -	05/2012	24(O)	0/0
144	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63 2,920.82	2,920.82	78.13	02/2009 09/2010	05/2012	20(R1)	0/0
145	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21 -	1,436.21	-	07/2010 -	05/2012	22(O)	0/0
146	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]	12/2009	1,492.33 -	1,492.33	22.57	06/2012 -	06/2012	0(O)	0/0
147	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11 -	370.11	8.53	04/2011 -	07/2012	15(O)	0/0
148	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]	07/2008	288.04 288.04	288.04	-	08/2012 -	08/2012	0(O)	0/0
149	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93 -	6,855.93	536.22	09/2012 -	09/2012	0(O)	0/0
150	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]	08/2009	1,793.00 -	1,793.00	9.39	09/2012 -	09/2012	0(O)	0/0
151	Construction of six Effluent Treatment Plants (ETP) - [N16000099]	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
152	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	29,777.00	3,676.04	03/2012 -	11/2012	8(O)	0/0
153	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35 -	1,797.35	9.77	12/2011 -	11/2012	11(O)	0/0
154	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]	06/2009	4,543.43 5,014.25	5,014.25	6.58	- -	12/2012	-	8/7
155	De-bottlenecking of SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	1.55	- -	12/2012	-	0/0
156	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75 8,813.41	8,813.41	4,573.26	06/2009 03/2013	03/2013	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
157	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	211.94	03/2013	03/2013	0(O)	0/0
	Total		154,318.74	172,142.54	58,893.73				173/257
			-						
	<u>Power</u>								
158	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72	877.06	215.38	07/2006	03/2010	44(O)	2/5
			-			-			
159	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,016.74	978.64	09/2007	05/2010	32(O)	8/36
			-			-			
160	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45	947.96	757.21	12/2007	06/2010	30(O)	7/18
			1,007.16			-			
161	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52	227.52	114.42	06/2010	06/2010	0(O)	0/0
			-			-			
162	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34	241.27	142.26	06/2008	08/2010	26(O)	8/20
			-			-			
163	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69	477.69	287.96	09/2010	09/2010	0(O)	0/0
			-			-			
164	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49	290.49	269.78	04/2010	09/2010	5(O)	0/0
			-			-			
165	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10	262.10	137.19	09/2010	09/2010	0(O)	0/0
			-			-			
166	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50	2,448.49	1,973.00	02/2010	10/2010	8(O)	5/24
			-			-			
167	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33	5,135.33	4,000.00	10/2010	10/2010	0(O)	11/40
			-			-			
168	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72	340.72	130.20	11/2010	11/2010	0(O)	0/0
			-			-			
169	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55	261.55	131.53	11/2010	11/2010	0(O)	0/0
			-			-			
170	KOTESHWAR HEP(THDC) - [180100184]	04/2000	1,301.56	2,398.39	1,888.32	04/2005	12/2010	68(O)	2/22
			-			-			
171	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63	1,405.63	1,477.56	08/2010	12/2010	4(O)	0/0
			-			-			
172	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.G.R.) - [180100260]	12/2005	3,779.46	3,779.46	3,379.61	09/2009	12/2010	15(O)	15/30
			-			-			
173	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96	975.96	603.79	10/2009	12/2010	14(O)	2/20
			-			-			
174	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01	611.02	643.73	08/2010	12/2010	4(O)	0/0
			-			-			
175	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23	5,221.23	2,418.12	07/2010	12/2010	5(O)	3/20
			-			-			
176	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76	417.76	257.17	12/2010	12/2010	0(O)	0/0
			-			-			
177	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36	408.36	286.44	12/2010	12/2010	0(O)	0/0
			-			-			
178	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89	230.89	30.84	01/2011	01/2011	0(O)	0/0
			-			-			

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
179	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92	768.92	1,142.73	03/2007	02/2011	47(O)	1/25
180	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29	1,724.79	1,141.80	11/2009	02/2011	15(O)	0/0
181	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26	621.28	452.32	02/2011	02/2011	0(O)	0/1
182	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44	2,570.44	1,728.00	08/2010	02/2011	6(O)	13/26
183	URI-II - [N18000023]	10/2006	238.25	1,724.79	1,141.80	-	05/2011	-	0/0
184	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	3,002.00	05/2011	05/2011	0(O)	0/0
185	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,304.52	1,057.65	10/2010	06/2011	8(O)	0/0
186	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24	557.25	347.89	01/2010	06/2011	17(O)	0/22
187	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	75.36	06/2011	06/2011	0(O)	0/0
188	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	117.67	06/2011	06/2011	0(O)	0/0
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	335.65	07/2011	07/2011	0(O)	0/0
190	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	336.21	07/2011	07/2011	0(O)	0/0
191	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	196.10	07/2011	07/2011	0(O)	0/0
192	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,061.38	726.76	09/2009	08/2011	23(O)	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	119.99	08/2011	08/2011	0(O)	0/0
194	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	1,896.65	1,572.42	11/2008	09/2011	34(O)	25/38
195	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97	328.97	116.46	09/2011	09/2011	0(O)	0/0
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48	520.48	171.48	11/2011	11/2011	0(O)	0/0
197	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66	509.66	65.29	11/2011	11/2011	0(O)	0/0
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69	317.69	13.52	11/2011	11/2011	0(O)	0/0
199	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19	184.19	36.36	11/2011	11/2011	0(O)	0/0
200	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39	8,323.39	6,745.00	12/2009	12/2011	24(O)	33/56

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
201	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01	623.44	15.03	01/2012	01/2012	0(O)	0/0
202	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96	664.96	62.23	02/2012	02/2012	0(O)	0/0
203	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50	409.50	4.51	02/2012	02/2012	0(O)	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29	410.29	75.23	02/2012	02/2012	0(O)	0/0
205	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57	353.57	102.90	07/2010	02/2012	19(O)	0/0
206	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32	1,347.32	284.25	02/2012	02/2012	0(O)	0/0
207	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15	4,527.15	3,183.00	04/2009	03/2012	35(O)	19/41
208	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03	2,047.03	845.95	01/2012	03/2012	2(O)	2/10
209	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35	4,375.35	1,119.00	07/2011	03/2012	8(O)	0/0
210	System Strengthening -X of SR - [N18000086]	12/2009	276.61	276.61	14.46	04/2012	04/2012	0(O)	0/0
211	765KV System for central part of Northern Region Grid - [N18000079]	11/2009	1,075.12	1,075.12	78.26	05/2012	05/2012	0(O)	0/0
212	765KV System for Central part of Northern Region G - [N18000078]	07/2009	1,736.36	1,736.36	-	06/2012	06/2012	0(O)	0/0
213	System Strengthening -XII of SR - [N18000085]	02/2010	232.34	232.34	4.56	06/2012	06/2012	0(O)	0/0
214	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]	12/2008	573.99	573.99	99.49	08/2012	08/2012	0(O)	0/10
215	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95	2,360.95	1,095.12	08/2012	08/2012	0(O)	0/0
216	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33	7,075.33	3,723.73	08/2012	08/2012	0(O)	0/0
217	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]	12/2009	1,216.83	1,216.83	87.87	08/2012	08/2012	0(O)	0/0
218	MOUDA STPP - [N18000048]	11/2007	5,459.28	6,010.89	1,074.00	02/2012	10/2012	8(O)	0/0
219	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12	4,824.12	598.95	10/2012	10/2012	0(O)	0/0
220	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00	5,915.00	737.00	11/2012	11/2012	0(O)	0/0
221	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81	6,230.81	617.00	11/2012	11/2012	0(O)	0/0
222	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]	03/2010	4,672.99	4,672.99	11.89	11/2012	11/2012	0(O)	0/0
223	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	358.42	7.78	12/2008 09/2010	12/2012	27(R1)	0/15

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
224	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
225	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	1,002.37	12/2012	12/2012	0(O)	0/0
226	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]	02/2010	2,144.00	2,144.00	126.48	12/2012	12/2012	0(O)	0/0
227	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,919.59	2,814.65	09/2009	03/2013	42(O)	1/20
228	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	870.00	03/2013	03/2013	0(O)	5/31
229	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	1,190.31	05/2013 05/2009	05/2013	48(R3)	63/36
230	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	976.00	08/2013	08/2013	0(O)	0/0
231	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	1,125.80	08/2013	08/2013	0(O)	0/0
232	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,680.00	11/2010	04/2014	41(O)	15/51
233	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	3,124.76	245.87	07/2010	12/2014	53(O)	0/0
234	Transm System for development of Pooling stn. in N - [N18000077]	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
235	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	111.02	07/2014	03/2015	8(O)	0/8
236	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	323.11	07/2014	01/2016	18(O)	0/0
237	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
238	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]	02/2010	215.86	215.86	-	06/2012	-	-	0/0
239	Northern Region Transmission Strengthening Scheme - [N18000083]	03/2012	965.58	965.58	64.66	11/2012	-	-	0/0
240	MAUDA Transmission System - [N18000084]	02/2010	469.38	469.38	9.84	10/2012	-	-	0/0
Total			172,530.95	180,735.86	68,728.59				246/659
Health & Family Welfare									
241	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	477.33	03/1999 03/2005	-	-	7/16
Total			71.18	443.15	477.33				7/16
Railways									
242	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50 246.50	246.50	-	03/2009 03/2009	11/2009	8(R3)	0/0
243	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74	224.51	41.39	-	12/2009	-	0/0
244	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	264.46	03/2006	01/2010	46(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
245	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	556.48	03/1995 -	03/2010	180(O)	0/0
246	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21 157.76	265.00	265.33	03/1998 -	03/2010	144(O)	0/0
247	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 459.55	579.37	574.82	- -	03/2010	-	0/0
248	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	789.84	03/2001 -	03/2010	108(O)	0/0
249	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 281.20	325.00	296.49	- -	03/2010	-	0/0
250	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 -	1,010.00	1,002.75	03/2003 -	03/2010	84(O)	0/0
251	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 -	665.00	-	- 11/2008	03/2010	16(R1)	0/0
252	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	503.16	482.13	- -	03/2010	-	0/0
253	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	762.21	06/2007 -	03/2010	33(O)	0/0
254	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	228.09	198.33	- -	03/2010	-	0/0
255	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 546.49	610.07	724.45	- 02/2009	03/2010	13(R1)	0/0
256	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	-	- 03/2009	03/2010	12(R1)	0/0
257	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 -	227.52	235.44	03/2008 03/2009	03/2010	12(R1)	0/0
258	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	-	03/2008 06/2008	03/2010	21(R3)	0/0
259	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	405.60	213.29	- -	03/2010	-	0/0
260	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53 320.66	464.50	500.63	03/1996 06/2009	06/2010	12(R1)	0/0
261	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	296.20	259.66	04/2003 03/2010	06/2010	3(R1)	0/0
262	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	824.18	12/2006 -	06/2010	42(O)	0/0
263	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
264	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44 -	209.57	196.47	03/2009 -	08/2010	17(O)	0/0
265	DEOGHAR-DUMKA NEW BG LINE (DOUBL.) (ER) - [220100264]	02/1999	180.73 320.66	358.00	309.87	12/2006 12/2008	11/2010	23(R3)	0/0
266	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	-	02/2015 -	11/2010	-51(O)	0/0
267	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	153.41	03/2004 -	12/2010	81(O)	0/0
268	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 492.98	724.31	684.47	- -	12/2010	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
269	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 479.20	762.33	244.42	- 12/2009	12/2010	12(R1)	0/0
270	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	243.40	-	- 02/2009	12/2010	22(R1)	0/0
271	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	211.90	-	- 03/2009	12/2010	21(R1)	0/0
272	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	221.90	115.11	12/2007 03/2010	12/2010	9(R1)	0/0
273	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 716.64	718.30	-	03/2008 08/2008	12/2010	28(R1)	0/0
274	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
275	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	-	- -	12/2010	-	0/0
276	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,103.20	3,727.00	- -	12/2010	-	0/1
277	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	355.51	- -	02/2011	-	0/0
278	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	475.17	379.16	02/2010 -	02/2011	12(O)	0/0
279	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 -	810.78	100.00	- 03/2011	02/2011	-1(R3)	0/0
280	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	356.87	120.72	- 03/2010	03/2011	12(R1)	0/0
281	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 284.27	488.76	285.80	06/1999 -	03/2011	141(O)	0/0
282	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	456.45	247.29	06/2004 -	03/2011	81(O)	0/0
283	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	436.60	05/2008 -	03/2011	34(O)	0/0
284	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00 214.09	214.09	158.52	12/2009 -	03/2011	15(O)	0/0
285	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	341.81	- 06/2009	03/2011	21(R3)	0/0
286	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	452.35	266.35	- -	03/2011	-	0/0
287	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	70.43	- -	03/2011	-	0/0
288	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0
289	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	348.78	314.22	- -	03/2011	-	0/0
290	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
291	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	245.15	34.57	12/2010 -	03/2011	3(O)	0/0
292	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
293	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.38	03/2011 -	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
294	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97	196.97	107.09	03/2011	03/2011	0(O)	0/0
295	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50	252.50	-	02/2010	11/2011	21(O)	0/0
296	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44	1,103.47	660.70	-	12/2011	-	0/0
297	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64	735.10	-	-	12/2011	27(R1)	0/0
298	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00	727.52	458.53	-	03/2012	-	0/0
299	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81	234.45	150.71	-	03/2012	-	0/0
300	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41	341.41	169.50	-	03/2012	-	0/0
301	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59	495.74	66.36	-	03/2012	-	0/0
302	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90	324.90	-	03/2010	03/2012	24(O)	0/0
303	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69	501.69	45.90	03/2010	03/2012	24(O)	0/0
304	TAMLUK DIGHA - [N22000097]	03/1984	293.97	293.97	311.22	06/2005	04/2012	82(O)	0/0
305	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68	730.00	275.47	-	07/2012	-	0/0
306	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77	540.96	474.40	03/1994	12/2012	225(O)	0/0
307	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67	1,160.52	484.07	-	12/2012	-	0/0
308	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00	981.00	340.69	03/2009	12/2012	45(O)	0/0
309	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47	1,480.71	445.84	10/2007	12/2012	62(O)	0/0
310	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20	687.20	-	03/2010	12/2012	33(O)	0/0
311	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00	496.03	88.04	03/2010	12/2012	33(O)	0/0
312	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84	410.08	105.58	-	03/2013	-	0/0
313	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00	1,029.00	557.47	-	03/2013	-	0/0
314	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70	1,556.23	261.35	-	03/2013	-	0/0
315	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00	3,230.01	1,892.49	04/2008	03/2014	27(R1)	0/0
316	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00	1,655.80	505.20	12/2008	03/2014	63(O)	0/0
317	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00	160.48	91.01	-	03/2014	-	0/0
318	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00	390.00	0.78	-	03/2014	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
319	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00	5,300.00	98.20	03/2014	03/2014	0(O)	0/0
320	AGARTALA SABROOM - [N22000099]	04/2008	813.34	813.34	84.20	03/2014	03/2014	0(O)	0/0
321	BHAIRABI SAIRONG - [N22000100]	04/2008	619.34	2,429.41	0.78	04/2014	03/2014	-1(O)	0/0
322	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66	324.66	129.93	-	03/2015	-	0/0
323	SEVOK RANGPO - [N22000102]	04/2008	1,339.48	1,339.48	1.42	12/2015	12/2015	0(O)	0/0
324	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56	3,123.52	200.98	03/2011	03/2016	60(O)	0/0
325	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	16,000.00	6,757.61	03/2001	12/2017	201(O)	0/0
326	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43	617.63	386.41	-	-	-	0/0
327	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00	318.66	452.61	03/1999	-	-	0/0
328	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80	285.93	231.63	-	-	-	0/0
329	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00	170.00	111.69	03/2002	-	-	0/0
330	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00	968.60	0.43	-	-	-	0/0
331	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00	880.00	421.71	-	-	-	0/0
332	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00	456.00	470.63	-	-	-	0/0
333	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00	511.86	413.02	03/1998	-	-	0/0
334	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40	563.25	548.92	03/2004	-	-	0/0
335	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]	04/1996	157.00	465.00	105.18	-	-	-	0/0
336	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55	712.00	363.60	-	-	-	0/0
337	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74	429.49	363.58	02/2009	-	-	0/0
338	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00	337.82	49.69	-	-	-	0/0
339	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22	268.00	-	12/1999	-	-	0/0
340	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00	661.72	510.14	-	-	-	0/0
341	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32	497.47	82.45	-	-	-	0/0
342	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42	154.30	106.79	03/2007	-	-	0/0
343	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00	363.26	0.27	07/2008	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
344	KODERMA-RANCHI VIA BARKAKHANA (NL), ECR - [220100222]	03/1999	491.19	1,099.20	711.79	07/2005	-	-	0/0
345	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76	219.94	190.49	-	-	-	0/0
346	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00	550.00	63.26	-	-	-	0/0
347	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00	497.63	477.14	-	-	-	0/0
348	BIDAR-GULBARGA, SCR(NL) - [220100254]	02/1999	242.42	369.70	151.69	-	-	-	0/0
349	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15	381.17	80.12	05/2009	-	-	0/0
350	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10	320.10	108.05	-	-	-	0/0
351	KHAGARIA-KUSHESHVAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23	162.87	72.90	-	-	-	0/0
352	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00	548.96	396.22	-	-	-	0/0
353	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00	695.00	9.41	-	-	-	0/0
354	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00	1,300.00	0.29	-	-	-	0/0
355	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90	325.17	311.98	03/2005	-	-	0/0
356	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38	700.00	97.09	12/2008	-	-	0/0
357	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91	418.17	52.53	03/2011	-	-	0/0
358	RAMGANJMUHDI-BHOPAL (NL), WCR - [220100314]	04/2001	727.13	1,225.00	140.34	-	-	-	0/0
359	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67	165.67	0.15	-	-	-	0/0
360	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73	230.03	45.76	-	-	-	0/0
361	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	585.93	102.78	-	-	-	0/0
362	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45	573.12	555.49	-	-	-	0/0
363	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56	671.82	1.05	-	-	-	0/0
364	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92	261.70	0.08	02/2006	-	-	0/0
365	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]	09/2007	404.19	900.00	47.91	-	-	-	0/0
366	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17	900.00	199.95	-	-	-	0/0
367	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00	255.96	129.45	-	-	-	0/0
368	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00	227.40	13.30	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
369	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 456.00	582.83	28.22	- -	-	-	0/0
370	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00 300.00	529.88	25.49	- -	-	-	0/0
371	BHAKURA DAMODAR - [N22000098]	03/1998	282.70 -	325.17	24.32	07/2008 -	-	-	0/0
372	KISHANGANJ JALALGARH - [N22000101]	04/2008	282.92 -	333.76	0.71	- -	-	-	0/0
373	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]	04/1993	100.41 -	949.22	15.65	12/2009 -	-	-	0/0
374	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 254.07	675.00	315.61	- 12/2011	-	-	0/0
375	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	353.08 353.08	1,010.00	64.83	- 12/2012	-	-	0/0
376	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	194.84	- 12/2012	-	-	0/0
	Total		51,007.64 -	103,651.54	40,686.33				0/1
Road Transport & Highways									
377	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93 -	440.93	641.40	12/2006 -	12/2009	36(O)	0/0
378	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39 -	534.39	716.15	05/2007 -	12/2009	31(O)	0/0
379	TOVARAMKURCHI-MADURAI,NH45B (NHAI) - [N24000054]	04/2000	263.00 -	263.00	317.74	08/2008 -	12/2009	16(O)	0/0
380	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00 -	450.00	876.61	07/2008 -	01/2010	18(O)	0/0
381	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00 -	261.00	286.30	08/2008 -	03/2010	19(O)	0/0
382	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00 -	320.00	636.10	05/2009 -	04/2010	11(O)	0/0
383	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40 -	372.40	-	07/2004 -	06/2010	71(O)	0/0
384	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75 -	399.75	-	03/2005 -	06/2010	63(O)	0/0
385	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78 -	479.54	423.50	11/2007 -	06/2010	31(O)	0/0
386	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00 -	305.00	428.90	06/2008 -	06/2010	24(O)	0/0
387	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27 -	263.27	-	02/2004 -	06/2010	76(O)	0/0
388	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]	03/2005	445.00 -	445.00	795.85	07/2010 -	06/2010	-1(O)	0/0
389	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00 -	196.65	-	08/2004 -	07/2010	71(O)	0/0
390	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00 -	310.00	392.26	04/2008 -	07/2010	27(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
391	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	342.80	03/2008	07/2010	28(O)	0/0
392	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	411.79	02/2009	07/2010	17(O)	0/0
393	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]	12/2003	360.42	360.42	478.40	11/2009	07/2010	8(O)	0/0
394	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	667.80	03/2010	07/2010	4(O)	0/0
395	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	212.23	06/2010	07/2010	1(O)	0/0
396	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	141.71	08/2006	08/2010	48(O)	0/0
397	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	452.11	03/2005	08/2010	65(O)	0/0
398	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	817.60	11/2007	08/2010	33(O)	0/0
399	MADURAI -KANNIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.90	03/2008	08/2010	29(O)	0/0
400	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	192.50	06/2008	08/2010	26(O)	0/0
401	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	196.11	06/2008	08/2010	26(O)	0/0
402	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	197.40	08/2009	08/2010	12(O)	0/0
403	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	254.50	08/2009	08/2010	12(O)	0/0
404	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	167.40	08/2009	08/2010	12(O)	0/0
405	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	-	08/2004	09/2010	73(O)	0/0
406	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	317.24	03/2005	09/2010	66(O)	0/0
407	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	876.87	11/2010	09/2010	-2(O)	0/0
408	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	276.90	06/2008	09/2010	27(O)	0/0
409	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	232.40	10/2008	09/2010	23(O)	0/0
410	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	216.60	09/2009	09/2010	12(O)	0/0
411	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	232.40	09/2009	09/2010	12(O)	0/0
412	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	243.00	09/2009	09/2010	12(O)	0/0
413	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	184.60	09/2009	09/2010	12(O)	0/0
414	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	298.42	09/2010	09/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	284.10	10/2008	10/2010	24(O)	0/0
416	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	310.30	10/2008	10/2010	24(O)	0/0
417	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	373.30	10/2008	10/2010	24(O)	0/0
418	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	291.80	10/2008	10/2010	24(O)	0/0
419	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	330.60	10/2008	10/2010	24(O)	0/0
420	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	474.30	04/2008	10/2010	30(O)	0/0
421	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	550.82	06/2009	10/2010	16(O)	0/0
422	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	190.60	08/2009	10/2010	14(O)	0/0
423	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	249.80	09/2008	10/2010	25(O)	0/0
424	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	473.22	06/2010	10/2010	4(O)	0/0
425	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	232.00	10/2009	10/2010	12(O)	0/0
426	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.55	07/2010	10/2010	3(O)	0/0
427	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	831.21	07/2010	10/2010	3(O)	0/0
428	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	422.12	03/2005	12/2010	69(O)	0/0
429	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	244.30	07/2004	12/2010	77(O)	0/0
430	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	-	04/2007	12/2010	44(O)	0/0
431	GARHMUKTRESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00	275.00	-	09/2007	12/2010	39(O)	0/0
432	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	129.40	03/2008	12/2010	33(O)	0/0
433	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	96.05	03/2008	12/2010	33(O)	0/0
434	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	291.50	05/2008	12/2010	31(O)	0/0
435	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68	340.68	259.50	03/2008	12/2010	33(O)	0/0
436	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	560.71	03/2009	12/2010	21(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
437	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	204.68	01/2009	12/2010	23(O)	0/0
438	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81	199.81	28.34	04/2009	12/2010	20(O)	0/0
439	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64	167.64	39.49	11/2008	12/2010	25(O)	0/0
440	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00	242.00	310.50	12/2008	12/2010	24(O)	0/0
441	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00	227.00	295.20	12/2008	12/2010	24(O)	0/0
442	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	412.70	06/2008	12/2010	30(O)	0/0
443	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	178.00	10/2008	12/2010	26(O)	0/0
444	SAGAR - RAJMARG CHORAHA,KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	281.90	10/2008	12/2010	26(O)	0/0
445	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43	203.43	108.10	10/2008	12/2010	26(O)	0/0
446	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	165.90	07/2008	12/2010	29(O)	0/0
447	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	461.20	06/2008	12/2010	30(O)	0/0
448	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	254.27	06/2009	12/2010	18(O)	0/0
449	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	12/2010	21(O)	0/0
450	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	179.90	11/2008	12/2010	25(O)	0/0
451	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]	03/2005	168.00	168.00	305.42	12/2008	12/2010	24(O)	0/0
452	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	33.65	04/2009	12/2010	20(O)	0/0
453	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	256.70	12/2009	12/2010	12(O)	0/0
454	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]	12/2003	407.60	407.60	181.40	06/2010	12/2010	6(O)	0/0
455	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	12/2010	5(O)	0/0
456	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	542.98	07/2010	12/2010	5(O)	0/0
457	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]	03/2005	557.00	557.00	505.00	02/2010	12/2010	10(O)	0/0
458	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	88.78	02/2004	12/2010	82(O)	0/0
459	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	444.84	08/2010	12/2010	4(O)	0/0
460	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	287.00	05/2010	12/2010	7(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
461	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	677.94	04/2009	01/2011	21(O)	0/0
462	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	173.20	06/2008	01/2011	31(O)	0/0
463	TRICHY - DINDIGUL NH-45 - [N24000099]	03/2005	576.00	576.00	254.40	07/2010	01/2011	6(O)	0/0
464	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	526.99	01/2011	01/2011	0(O)	0/0
465	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	334.80	01/2011	01/2011	0(O)	0/0
466	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	108.30	09/2007	02/2011	41(O)	0/0
467	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	135.90	09/2007	03/2011	42(O)	0/0
468	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	153.30	08/2005	03/2011	67(O)	0/0
469	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	230.10	07/2005	03/2011	68(O)	0/0
470	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	269.50	07/2005	03/2011	68(O)	0/0
471	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	190.60	10/2008	03/2011	29(O)	0/0
472	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00	227.00	240.80	10/2008	03/2011	29(O)	0/0
473	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	280.00	136.00	02/2009	03/2011	25(O)	0/0
474	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94	332.94	147.14	09/2008	03/2011	30(O)	0/0
475	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]	12/2003	198.00	198.00	110.90	11/2008	03/2011	28(O)	0/0
476	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30	151.30	104.00	10/2008	03/2011	29(O)	0/0
477	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	244.40	03/2008	03/2011	36(O)	0/0
478	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	131.40	06/2008	03/2011	33(O)	0/0
479	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	503.60	10/2009	03/2011	17(O)	0/0
480	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	121.30	09/2010	03/2011	6(O)	0/0
481	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00	200.00	62.69	04/2009	04/2011	24(O)	0/0
482	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	577.13	05/2010	05/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
483	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	-	09/2007	06/2011	45(O)	0/0
484	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	61.17	09/2008	06/2011	33(O)	0/0
485	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHA) - [240106304]	12/2003	251.03	251.03	205.60	10/2008	06/2011	32(O)	0/0
486	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91	229.91	150.30	10/2008	06/2011	32(O)	0/0
487	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	70.60	05/2008	06/2011	37(O)	0/0
488	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	247.40	03/2010	06/2011	15(O)	0/0
489	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	-	04/2004	10/2011	90(O)	0/0
490	DAKOPA TO NAGAON (NH-36)(NHA) - [240106288]	12/2003	225.00	225.00	187.80	06/2008	10/2011	40(O)	0/0
491	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	107.00	06/2005	12/2011	78(O)	0/0
492	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHA) - [240106290]	12/2003	195.00	195.00	91.36	06/2008	12/2011	42(O)	0/0
493	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHA) - [240106293]	12/2003	237.80	237.80	107.60	06/2008	12/2011	42(O)	0/0
494	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	314.50	09/2008	12/2011	39(O)	0/0
495	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	180.80	06/2008	12/2011	42(O)	0/0
496	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	140.20	04/2008	12/2011	44(O)	0/0
497	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	143.30	06/2008	12/2011	42(O)	0/0
498	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	93.82	04/2008	03/2012	47(O)	0/0
499	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	128.60	04/2008	03/2012	47(O)	0/0
500	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	177.32	02/2010	03/2012	25(O)	0/0
501	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
502	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	38.63	05/2010	08/2012	27(O)	0/0
503	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	155.04	28.24	11/2008	12/2012	49(O)	0/0
504	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	34.47	09/2007	12/2012	63(O)	0/0
505	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	24.16	07/2009	12/2012	41(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
506	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	73.64	04/2010	12/2012	32(O)	0/0
507	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00	276.00	360.00	04/2008	-	-	0/0
508	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]	12/2003	300.00	300.00	-	10/2008	-	-	0/0
509	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	568.50	03/2009	-	-	0/0
510	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	-	12/2008	-	-	0/0
511	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80	402.80	-	03/2009	-	-	0/0
	Total		41,863.55	42,136.98	35,141.65				0/0
	Shipping & Ports								
512	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	406.28	03/2010	03/2010	0(O)	0/0
513	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	193.47	06/2007 01/2009	06/2010	17(R1)	0/0
514	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	297.76	04/2009	06/2010	14(O)	0/0
515	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	374.37	07/2010	07/2010	0(O)	0/0
516	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA - [N25000046]	11/2004	2,118.00	2,118.00	-	11/2004	10/2010	71(O)	0/0
517	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	815.90	10/2008	11/2010	25(O)	0/0
518	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	274.64	11/2010	11/2010	0(O)	0/0
519	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
520	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
521	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	101.53	12/2005	01/2011	61(O)	0/0
522	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	1,140.00	0.16	02/2011	02/2011	0(O)	0/0
523	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	755.50	0.73	03/2011	03/2011	0(O)	0/0
524	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	211.22	04/2011	04/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
525	Acquisition of two nos. of 120 B.P - [N25000042]	04/2009	2,908.48	2,908.48	58.18	03/2011	06/2011	3(O)	0/0
526	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	374.36	04/2011	12/2011	8(O)	0/0
527	Acquisition of Two nos. of 3060 DWT - [N25000043]	04/2009	2,770.32	2,770.42	55.41	09/2011	12/2011	3(O)	0/0
528	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
529	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]	03/2009	3,500.00	3,500.00	-	01/2012	01/2012	0(O)	0/0
530	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
531	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.63	10/2008	-	-	0/0
532	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
533	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]	03/2008	375.00	375.00	-	01/2009	-	-	0/0
	Total		24,047.63	24,630.99	3,636.22				0/0
	Telecommunications								
534	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	08/2009	32(O)	0/0
535	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	10/2009	46(O)	0/0
536	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	15(O)	0/0
537	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.24	12/2004	02/2010	62(O)	0/0
538	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	483.54	475.59	12/2008	03/2010	15(O)	0/0
539	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	161.35	02/2008	05/2010	27(O)	0/0
540	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	94.14	10/2007 12/2009	07/2010	7(R3)	0/0
541	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	558.30	12/2008	08/2010	20(O)	0/0
542	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	144.63	03/2009	08/2010	17(O)	0/0
543	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	172.03	12/2008	08/2010	20(O)	0/0
544	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	54.65	09/2009	08/2010	11(O)	0/0
545	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	455.01	03/2009	08/2010	17(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
546	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	150.12	03/2009	08/2010	17(O)	0/0
547	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	165.56	08/2009	08/2010	12(O)	0/0
548	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	529.32	213.42	09/2009	08/2010	11(O)	0/0
549	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	336.81	105.16	01/2009	08/2010	19(O)	0/0
550	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph - [N26000079]	09/2009	577.35	577.35	69.44	09/2010	08/2010	-1(O)	0/0
551	GSM equipment of 4,50,000 Lines (2G) Haryana (Phas - [N26000080]	09/2008	216.54	216.54	80.84	09/2009	08/2010	11(O)	0/0
552	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]	10/2008	336.84	336.84	21.40	10/2009	08/2010	10(O)	0/0
553	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]	02/2009	625.53	625.53	463.60	02/2010	08/2010	6(O)	0/0
554	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]	09/2009	624.75	624.75	138.09	09/2010	08/2010	-1(O)	0/0
555	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]	06/2008	170.23	167.20	159.81	06/2009	08/2010	14(O)	0/0
556	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]	10/2007	366.00	529.32	284.85	10/2008	08/2010	22(O)	0/0
557	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]	02/2008	584.33	584.33	582.09	02/2009	08/2010	18(O)	0/0
558	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]	03/2008	328.13	328.13	185.10	03/2009	08/2010	17(O)	0/0
559	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]	11/2009	916.70	916.70	165.56	11/2010	08/2010	-3(O)	0/0
560	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]	01/2009	760.20	810.37	579.17	01/2010	08/2010	7(O)	0/0
561	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]	01/2009	922.91	922.91	123.27	01/2010	08/2010	7(O)	0/0
562	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]	01/2009	315.19	315.19	68.99	01/2010	08/2010	7(O)	0/0
563	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53	180.53	30.30	12/2009	09/2010	9(O)	0/0
564	Execution of telecom network requirement of defence - [N26000065]	05/2006	1,077.00	1,077.00	841.00	03/2009	09/2010	18(O)	0/0
565	Expn of existing 2G & 3G GSM N/W by 750k - [N26000077]	10/2008	180.53	180.53	30.30	06/2010	09/2010	3(O)	0/0
566	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]	09/2008	241.49	241.49	78.78	09/2009	09/2010	12(O)	0/0
567	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]	08/2008	868.00	868.00	175.00	08/2009	09/2010	13(O)	0/0
568	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]	10/2008	677.75	677.75	239.96	10/2009	09/2010	11(O)	0/0
569	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]	01/2009	848.70	848.70	399.04	01/2010	09/2010	8(O)	0/0
570	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
571	Implementation of FTTH, the state of the art Acces - [N26000073]	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
572	Provision of data network for CWG delhi - [N26000076]	11/2009	488.76	488.76	-	10/2010	10/2010	0(O)	0/0
573	Procurement of DXC equipment - [N26000074]	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
574	Procurement of 24 F OF cable. - [N26000075]	02/2008	199.00	199.00	-	03/2010	11/2010	8(O)	0/0
575	ERP implementation in BSNL on Turnkey basis - [N26000096]	10/2009	384.00	384.00	12.01	10/2010	11/2010	1(O)	0/0
576	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]	06/2006	803.70	803.76	599.26	06/2009	12/2010	18(O)	1/20
577	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007 12/2009	12/2010	12(R3)	0/0
578	Procurement of 2.5G DWDM equipment - [N26000066]	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
579	Procurement of 10G (40 chl) DWDM equipment - [N26000067]	08/2006	590.10	590.10	-	03/2009	12/2010	21(O)	0/0
580	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
581	Procurement of STM-1 SDH equipment - [N26000069]	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
582	Procurement of STM-16 ADM equipment - [N26000070]	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
583	Procurement of STM-16 ADM equipment - [N26000071]	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
584	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	64.30	02/2007	03/2011	49(O)	0/0
585	FTTH BO-3474 /08-09 in Mumbai - [N26000078]	09/2011	389.86	389.86	2.09	09/2011	09/2011	0(O)	0/0
586	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
587	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	160.00	92.45	06/2006	-	-	0/0
588	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
589	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	-	-	0/0
590	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]	11/2008	350.00	350.00	-	-	-	-	0/0
591	CENTRALISED TRANSMISSION NMS - [N26000064]	08/2009	300.00	300.00	-	-	-	-	0/0
Total			27,675.46	27,693.47	9,385.98				1/20
<u>Urban Development</u>									
592	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,676.00	15,759.36	14,727.76	06/2010	09/2010	3(O)	0/8
593	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	11,609.00	2,831.74	12/2011 03/2013	03/2013	0(R3)	6/6
Total			15,071.00	27,368.36	17,559.50				6/14

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Water Resources</u>									
594	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
			-			-			
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			592,397.87	696,818.59	290,436.56				744/1938
