

**344th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
June 2014**



NHPC - PARBATI H.E.P. STAGE -III



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English & Hindi	1 -25
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	26-26
Summary of Projects	27-42
Trend and Graphical Analysis of Projects	43-55
Sector wise analysis of projects	56-56
List of All Ongoing Projects	57-89
Sector wise Graph	90-100
ANNEXURE	101-101
Central Sector Projects	102-102
List of Projects Having Expenditure More than cost	103-112
List of Projects with out Original date of Commissioning	113-114
List of Projects with out date of Commissioning	115-128
List of Projects Ahead of Schedule	129-129
List of On schedule Projects Original Schedule	130-135
List of Delayed Projects w.r.t Original Schedule	136-158
List of Projects without Milestones	159-181
List of Projects Having Time and cost overrun w.r.t original	182-186
List of Projects Having cost overrun w.r.t original	187-197
List of On schedule Projects w.r.t. Latest Schedule	198-204
List of Projects Ahead of Schedule w.r.t Latest Schedule	205-206
List of Delayed Projects w.r.t Latest Schedule	207-220
List of Projects Having cost overrun w.r.t Revised original	221-230

कार्यकारी सारांश

1. जून, 2014 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 729 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जून, 2014 के दौरान 9 परियोजनाओं (पेट्रोलियम तथा विद्युत प्रत्येक में 3 परियोजनाएं, सड़क में दो परियोजनाएं तथा रेलवे क्षेत्र में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 729 परियोजनाओं में से, 290 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 52 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 52 परियोजनाओं में से, 25 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	290	37	7	2
2.	सड़क परिवहन एवं राजमार्ग	136	92	8	4
3.	विद्युत	99	56	17	11
4.	पेट्रोलियम	76	45	7	3
5.	कोयला	59	31	4	3
6.	इस्पात	20	15	7	2
7.	पोत परिवहन एवं पत्तन	19	3	0	0
8.	दूरसंचार	11	4	2	0
9.	नागर विमानन	8	2	0	0
10.	शहरी विकास	5	1	0	0
11.	परमाणु ऊर्जा	4	4	0	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		729	290	52	25

3. 729 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ₹ 9,35,003.47 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 11,08,382.70 करोड़ होने की संभावना है जो ₹ 1,73,379.23 करोड़ (मूल लागत का 18.50%) की समग्र लागत वृद्धि को दर्शाता है। जून, 2014 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,46,208.61 करोड़ है जो परियोजनाओं की अनुमानित लागत का 49.30% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (30.06.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		लागत-वृद्धि (% में)
				मूल	अनुमानित	
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी-बलूरघाट से नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.18	1810.82
3	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1423.98	1172.55
4	अकोला-खण्डवा जीसी अकोला-अकोट	रेलवे	04/2008	184.26	2000.00	985.42
5	बंगलोर सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	रेलवे	02/1999	138.00	1382.78	902.01

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (30.06.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	कुसमुण्डा एक्सपे. (ओसीपी) (एसईसीएल) (15-50) एमटीवाई	कोयला	06/2008	1188.31	7612.33	6424.02
3	जिरीबाम से इंफाल (टीयूपीयूआई) (एनएल) (एनईएफआर)	रेलवे	04/2003	727.56	5996.00	5268.44
4	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
5	बाढ़ एसटीपीपी (3X660 मेवा.) एनटीपीसी	विद्युत	12/2003	8692.97	13737.00	5044.03

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 729 परियोजनाओं में से, 6 परियोजनाएं समय से पहले चल रही हैं, 110 समय पर तथा 290 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 271 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 23 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 300 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 290 विलंबित परियोजनाओं में से, 60 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 72 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 87 परियोजनाओं में 25

से 60 माह तक का विलंब हुआ तथा 71 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ ।
अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (30.06.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटवा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	09/2014	246
2	फ्रैट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	11/2002	12/2017	181
4	बेलापुर-सीवूड-यूरान इलेक्ट्रीफाइड डबल लाईन (एमटीपी)	रेलवे	03/1996	03/2004	03/2016	144
5	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल, 2014 में इस मंत्रालय के प्रबोधन पर 727 परियोजनाओं में से 235 परियोजनाओं के संबंध में लागतवृद्धि तथा 282 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है; जबकि जून 2014 के दौरान 729 परियोजनाओं में से 214 परियोजनाओं के संबंध में लागतवृद्धि तथा 290 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है । अप्रैल 2014 की तुलना में लागतवृद्धि की सूचना देने वाली परियोजनाओं की संख्या 32% से घटकर 29% हो गई है जबकि समयवृद्धि की सूचना देने वाली परियोजनाओं की संख्या में मामूली वृद्धि 39% से 40% हो गई है (अनुबंध 6 (क) तथा 6(ख) ।

7. विद्युत क्षेत्र परियोजना 'बाढ़ एसटीपीपी (3X660 मेवा.), एनटीपीसी' में अप्रैल 2014 माह में 8693.00 करोड़ रुपए के अनुमानित लागत की सूचना दी गई है, जिसे परियोजना एजेंसी द्वारा जून 2014 माह में बढ़ाकर 13737.00 करोड़ रुपए कर दिया गया है। जो मुख्य रूप से रसियन कंपनी अर्थात् मेसर्स टीपीई तथा पावर मशीन द्वारा धीमी प्रगति, निधि की कमी तथा प्रतिबद्धताओं का पालन न करने के कारण 5040.03 करोड़ रुपए (अप्रैल 2014 माह में केवल 0.03 करोड़ रुपए से) की लागतवृद्धि को दर्शाता है। 'रेलवे की बेलापुर-सीवूड-यूरान इलेक्ट्रीफाइड डबल लाइन (एमटीपी)' परियोजना के लिए परियोजना प्राधिकारी ने शुरू करने की अनुमानित तारीख दिसंबर 2014 से बदलकर मार्च 2016 कर दिया है इसलिए अप्रैल 2014 की तुलना में समयवृद्धि 129 माह से बढ़कर 144 माह हो गई है।

8. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

9. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (30.06.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		संचयी व्यय (रु. करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी-बलूरघाट से नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रैट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

एन.आर.: सूचित नहीं ।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं। पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (30.06.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	विरमगम-बिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	155.66	एन.आर.	200.42
2	शापुर-सरादिया और सोमनाथ-कोडिनार के लिए राजकोटवेरावल, वंशजालिया से जतलसर नए एमएम के साथ (जीसी)	रेलवे	04/1994	320.66	एन.आर.	462.18
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	688.63
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8805.00
5	दल्ली-रजहारा रौघट (दल्ली-रजहारा जगदलपुर के भाग), एनएल, आरवीएनएल	रेलवे	04/1995	304.00	एन.आर.	138.39

एन.आर.: सूचित नहीं।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (30.06.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेडापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

एन.आर.: सूचित नहीं ।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

11. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- i) दूरसंचार क्षेत्र में, 11 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में 1 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजनाएं 'टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन, बीएसएनएल' में विक्रेता से संबंधित विभिन्न मुद्दों में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'उत्तरांचल में 283000 लाईनों (2जी) तथा 75000 लाईनों (3 जी) का

जीएसएम उपकरण, बीएसएनएल' में भूमि अधिग्रहण तथा स्थल को किराए पर लेने में हुए विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

ii) कोयला क्षेत्र में, 59 परियोजनाओं में से 31 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 3-48 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 3 मेगा परियोजनाएं हैं । परियोजना 'टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट), एनएलसी' में उपस्करों के निर्माण में विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'अदरियाला शाफ्ट परियोजना, एससीसीएल' में उपस्करों की आपूर्ति में विलंब के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'काकटिया लॉगवाल, एससीसीएल' में टीपीओ (प्रौद्योगिकी प्रदाता सह ऑपरेटर) के चयन में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जो लॉगवाल के प्रवेश के लिए जिम्मेदार है; तथा परियोजना 'मुनीडीह X/सीम यूजी, बीसीसीएल' में 48 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

iii) इस्पात क्षेत्र में, 20 परियोजनाओं में से 15 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 2-5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 मेगा परियोजनाएं हैं । परियोजना 'इसको इस्पात संयंत्र का विस्तार, सेल' में मृदा संबंधी समस्या के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'राउरकेला इस्पात संयंत्र का विस्तार, सेल' में कार्य आवंटन में परिवर्तन के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'कोक ओवन बैटरी सं.4 चरण-II आरआईएनएल' तथा '1.2 एमटीपीए पेलेट संयंत्र परियोजना, दोनीमलाई, एनएमडीसी' में क्रमशः 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'अन्य संबंधित सुविधाओं के साथ 45 एमवीए साफ्ट की स्थापना, सेल' तथा 'आरएसपी के एसपीपी में अतिरिक्त हीट ट्रीटमेंट सुविधाओं की स्थापना, सेल' प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'बीएसपी, भिलाई, छत्तीसगढ़ में कोक ओवन बैटरी-9 का कोल्ड रिपेयर, सेल' में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

iv) रेलवे क्षेत्र में, 290 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 9-69 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 मेगा परियोजनाएं हैं । परियोजनाएं 'मुनीराबाद-महबूबनगर (एनएल), एससीआर', 'बेलापुर-सीवूड-यूरान इलेक्ट्रीफाइड डबल लाईन (एमटीपी), एमआरटीपी' तथा 'गुलबर्गा-बीदर (एनएल), एससीआर' में निधि की कमी के कारण क्रमशः 9, 15 तथा 69 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बारानगर से बराकपुर तथा दक्षिणेश्वर तक मेट्रो रेलवे के निर्माण हेतु नए कार्य (एमटीपी), आरवीएनएल' में वन संबंधी अनुमति तथा राज्य सरकार के युटिलिटीज के स्थानांतरण में विलंब के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'चंपाझरन-बिमलगढ़ डबलिंग एक्सटेंशन, एसईआर', 'दुधनोई-मेंदीपतर से नई बीजी लाईन, एनईएफआर' तथा 'अमबारी फलकाटा से नई मायानगरी, एनईएफआर' प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

v) पेट्रोलियम क्षेत्र में, 77 परियोजनाओं में से 46 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 1-9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 3 मेगा परियोजनाएं हैं । परियोजनाएं 'बीपीसीआर/एचपीसीआर से यूरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण हेतु पाईपलाइन, बीपीसीएल' तथा 'सेंट्रल गैस गैदरिंग स्टेशन तथा ऑफटेक प्वाइंट, ऑयल' प्रत्येक में सिविल कार्यों में धीमी प्रगति के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं '6 ईटीपीएस का निर्माण, ओएनजीसी' तथा 'पोलिप्रोपीलेन यूनिट, मेंगलोर रिफाइनरी' में सिविल कार्यों में धीमी प्रगति के कारण क्रमशः 3 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'कोनबन जीजीएस तथा पाईपलाइन ग्रिड परियोजना, त्रिपुरा का उन्नयन, ओएनजीसी' में आरओयू समस्या के कारण 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'मंगलौर में स्ट्रेटजिक कूड ऑयल स्टोरेज परियोजना, आईएसपीआरएल' तथा 'पदुर में स्ट्रेटजिक कूड ऑयल स्टोरेज परियोजना, आईएसपीआरएल' प्रत्येक 8 में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन

परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) सड़क क्षेत्र में, 136 परियोजनाओं में से 92 परियोजनाएं विलंबित हैं । माह के दौरान, 8 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 4 मेगा परियोजनाएं हैं । परियोजनाएं 'हैदराबाद-बंगलौर सेक्शन का उन्नयन, एनएचआई' तथा 'चेन्नई-एन्नोर पोर्ट संपर्क से पर्याप्त सड़क संपर्क का विकास, एनएचआई' प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'बेवार-पाली-पिंदवारा, एनएचआई' तथा 'कोटा बाईपास, आरजे-4, एनएच-76, एनएचआई' में क्रमशः 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'सूरत-दहिसर (छह लेन) 263 किमी. से 502 किमी., एनएचआई' तथा 'जम्मू-उधमपुर 27.5 किमी. से 67.00 किमी. एनएचआई' प्रत्येक में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'चांदीखोल-जगतपुर-भुवनेश्वर की छह लेनिंग, एनएचआई' तथा 'पीएस मोतिहारी-रक्सौल के साथ 2 लेनिंग, एनएचआई' में क्रमशः 6 तथा 12 के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

vii) विद्युत क्षेत्र में, 99 परियोजनाओं में से 56 परियोजनाएं विलंबित हैं । माह के दौरान 17 परियोजनाओं के संबंध में 1-27 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 11 मेगा परियोजनाएं हैं । परियोजनाएं 'आंध्र प्रदेश के कृष्ण पट्टनम में आईएसजीएस परियोजनाओं के साथ जुड़ी हुई साझा प्रणाली, पीजीसीआईएल' तथा 'दक्षिणी क्षेत्र ग्रिड में प्रणाली सुदृढीकरण-XIII, पीजीसीआईएल' प्रत्येक में आरओडब्ल्यू समस्याओं के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'डीवीसी तथा मैथूब आरबीसी के साथ 765 कि.वा. पूलिंग स्टेशन तथा नेटवर्क, पीजीसीआईएल' में माओवादी समस्या के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'उड़ीसा-भाग-ए में चरण-1 जनरेशन परियोजना हेतु पारेषण प्रणाली, पीजीसीआईएल' तथा 'एसआर ग्रिड की प्रणाली सुदृढीकरण XII, पीजीसीआईएल' प्रत्येक में आरओडब्ल्यू समस्याओं के कारण से प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'उड़ीसा भाग-सी में चरण-I जनरेशन परियोजना हेतु पारेषण प्रणाली, पीजीसीआईएल' में वन संबंधी अनुमति मिलने में विलंब के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पश्चिमी क्षेत्र की सुदृढीकरण योजना-V पीजीसीआईएल' तथा 'छत्तीसगढ़ में आईपीपीएस जनरेशन परियोजनाओं हेतु डब्ल्यूआर के

पश्चिमी भाग में पारेषण सुदृढीकरण, पीजीसीआईएल' में आरओडब्ल्यू समस्याओं के कारण प्रत्येक में 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'एसआर की प्रणाली सुदृढीकरण-XI, पीजीसीआईएल' में बार-बार बंद के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'छत्तीसगढ़ में आईपीपी परियोजनाओं हेतु रायपुर-वर्धा कॉरिडोर में प्रणाली सुदृढीकरण, पीजीसीआईएल' तथा 'मुंद्रा अल्ट्रा मेगा पावर परियोजना के साथ जुड़े पारेषण प्रणाली, पीजीसीआईएल' में वन संबंधी अनुमति मिलने में विलंब के कारण क्रमशः 5 तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं पूर्वोत्तर क्षेत्र सुदृढीकरण योजना-III, पीजीसीआईएल' तथा 'छत्तीसगढ़ में आईपीपी जनरेशन परियोजना हेतु चंपा तथा रायगढ़ में पूलिंग स्टेशनों की स्थापना, पीजीसीआईएल' प्रत्येक में क्रमशः भूमि अधिग्रहण तथा निविदा की समाप्ति के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XX पीजीसीआईएल' में आरओडब्ल्यू समस्याओं के कारण 27 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'दक्षिण क्षेत्र-XV की प्रणाली सुदृढीकरण, पीजीसीआईएल', कोस्टल इनर्जन प्राइवेट लिमिटेड तथा इंद-बराथ पावर (मद्रास) लिमिटेड के साथ जुड़ी साझा प्रणाली, पीजीसीआईएल' तथा 'बाढ़-II टीपीएस के साथ इमिडिएट इवैक्यूएशन सिस्टम, पीजीसीआईएल' में क्रमशः 1, 3 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

12. दिनांक 30.06.2014 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
13. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for June 2014 contains information on the status of the 729 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During June 2014, 9 projects (3 projects each in Petroleum and Power, 2 projects in Roads and 1 project in Railways Sector) have reported completion.

2. During the reference month, out of 729 projects, 290 projects are delayed with respect to original schedule and 52 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 52 projects, 25 are Mega Projects costing ₹ 1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	290	37	7	2
2.	ROAD TRANSPORT AND HIGHWAYS	136	92	8	4
3.	POWER	99	56	17	11
4.	PETROLEUM	76	45	7	3
5.	COAL	59	31	4	3
6.	STEEL	20	15	7	2
7.	SHIPPING AND PORTS	19	3	0	0
8.	TELECOMMUNICATIONS	11	4	2	0
9.	CIVIL AVIATION	8	2	0	0
10.	URBAN DEVELOPMENT	5	1	0	0
11.	ATOMIC ENERGY	4	4	0	0
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		729	290	52	25

3. Total original cost of implementation of the 729 projects was ₹ 9,35,003.47 crore and their anticipated completion cost is likely to be ₹ 11,08,382.70 crore, which reflects overall cost overruns of ₹ 1,73,379.23 crore (18.50 % of original cost). The expenditure incurred on these projects till June 2014 is ₹ 5,46,208.61 crore, which is 49.30 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as follows:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 30-06 -2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		COST OVERRUNS (in %)
				ORIGINAL	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	RAILWAYS	03/1981	37.68	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	RAILWAYS	04/1983	36.80	703.18	1810.82
3	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	111.90	1423.98	1172.55
4	AKOLA-KHANDWA GC AKOLA-AKOT	RAILWAYS	04/2008	184.26	2000.00	985.42
5	BANGLORE SATYAMANGALAM (NL)(SWR)	RAILWAYS	02/1999	138.00	1382.78	902.01

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute terms are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 30-06-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	2500.00	20000.00	17500.00
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	COAL	06/2008	1188.31	7612.33	6424.02
3	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	5996.00	5268.44
4	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6395.00	11609.00	5214.00
5	BARH STPP(3X660MW) NTPC	POWER	12/2003	8692.97	13737.00	5044.03

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 729 projects, 6 projects are ahead of schedule, 110 are on schedule and 290 are delayed with respect to original schedule. However, the number of delayed projects decreases to 271 if delay is calculated on the basis of latest schedule of completion. Further, 23 projects have been sanctioned without any commissioning schedule/date and for 300 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 290 delayed projects, 60 projects have overall delay in the range of 1 to 12 months, 72 projects have delay in

the range of 13 to 24 months, 87 projects have delay in the range of 25 to 60 months and 71 projects have delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 30-06-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	RAILWAYS	04/1986	03/1994	09/2014	246
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	RAILWAYS	03/1984	03/1995	03/2015	240
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	11/2002	12/2017	181
4	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	RAILWAYS	03/1996	03/2004	03/2016	144
5	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	03/2005	12/2016	141

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2014, out of 727 projects on the monitor of this Ministry, 235 projects reported cost overruns and 282 projects reported time overruns; while during June 2014, out of 729 projects, 214 projects reported cost overruns and 290 projects reported time overruns. In comparison to April 2014, number of projects reporting cost overruns has gone down from 32% to 29% whereas projects reporting time overruns have marginally increased to 40% from 39% (Annexure 6 (a) & 6 (b)).

7. Power sector project “Barh STPP (3x 660 MW), NTPC” reported anticipated cost of Rs. 8693.00 crore in the month of April 2014, which has been increased to Rs. 13737.00 crore by the project agency in the month of June 2014, thereby showing cost overrun to the tune of Rs. 5044.03 crore (from mere 0.03 crore in the month of April 2014) mainly due to slow progress, fund constraints and non-adherence of commitments by Russian companies i.e. M/s TPE and

Power Machine. For the project “Belapur-Seawood-Uran Electrified Double Line (MTP)” of Railways, the project authority has changed the anticipated date of commissioning from December 2014 to March 2016 thereby increasing time overruns from 129 months to 144 months, as compared to April 2014.

8. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

9. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as follows:-

List of 5 Earliest Projects without Milestones (as on 30-06-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.

5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.
---	--	----------	---------	--------	---------	--------	---------	---------	------

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as follows:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 30-06-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	VIRAMGAM-BHILDI(WR),GC	RAILWAYS	04/1990	155.66	N.R.	200.42
2	RAJKOTVERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	N.R.	462.18
3	PEDAPALLI-KARIMNAGAR- NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	688.63
4	UDHAMPUR-SRINAGAR- BARAMULLA (NL),NR	RAILWAYS	03/1995	2500.00	2500.00	8805.00
5	DALLI-RAJHARA- RAOGHAT(PART OF DALLI- RAJHARA- JAGDALPUR),NL,RVNL	RAILWAYS	04/1995	304.00	N.R.	138.39

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing or updating revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 30.06.2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM- TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM- BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI- KARIMNAGAR-	Railways	12/1994	N.R.	N.R.	03/2012

	NIZAMABAD NL(SCR)					
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of delays/additional delays are as under:-

i) In the **Telecommunication Sector**, out of 11 projects, 4 projects are delayed. During the month, 2 projects have reported additional delays of 1 and 3 months. The projects ‘ERP Implementation in BSNL on Turnkey Basis, BSNL’ has reported additional delay of 1 month due to delay in various issues related to vendor; and the project ‘GSM Equipment of 283000 Lines (2G) and 75000 Lines (3G) in Uttranchal, BSNL’ has reported additional delay of 3 months due to delay in land acquisition and hiring of site.

ii) In the **Coal Sector**, out of 59 projects, 31 projects are delayed. During the month, 4 projects have reported additional delay in the range of 3-48 months, out of which 3 are Mega projects. The project ‘TPS-II Expansion (1470MW TO 1970MW), NLC’ has reported additional delay of 3 months due to delay in equipment’s erection; the project ‘Adriyala Shaft Project, SCCL’ has reported additional delay of 5 months due to delay in supply of equipments; the project ‘Kakatiya Longwall, SCCL’ has reported additional delay of 12 months due to delay in selection of TPO (Technology Provider cum Operator) which is responsible for induction of longwall; and the project ‘Moonidih XV Seam UG, BCCL’ has reported additional delay of 48 months (however, no specific reasons have been reported by the project authority for the delay in this project).

iii) In the **Steel Sector**, out of 20 projects, 15 projects are delayed. During the month, 7 projects have reported additional delays in the range of 2-5 months, out of which 2 are Mega projects. The project ‘Expansion of IISCO Steel Plant, SAIL’ has reported additional delay of 2 months due to soil related problem; the project ‘Expansion of Rourkela Steel Plant, SAIL’ has reported additional delay of 3 months due to change of scope of work; the projects ‘Coke Oven Battery No. 4 Phase-II RINL’ and ‘1.2 MTPA Pellet Plant Project, Donimalai, NMDC’ have reported additional delays of 2 and 3 months respectively; the projects ‘Installation of 45 MVA Saft with other Associated Facilities, SAIL’ and ‘Installation of Additional Heat Treatment Facilities in SPP at RSP, SAIL’ have reported additional delays of 4 months each; and the project ‘Cold Repair of Coke

Oven Battery-9 at BSP, Bhilai, Chattisgarh, SAIL’ has reported additional delay of 5 months (however, no specific reasons have been reported by the project authorities for the delay in these projects).

iv) In the **Railway Sector**, out of 290 projects, 37 projects are delayed. During the month, 7 projects have reported additional delays in the range of 9-69 months, out of which 2 are Mega projects. The projects ‘Muneerabad-Mahaboobnagar (NL), SCR’ , ‘Belapur-Seawood-Uran Electrified Double Line (MTP), MRTTP’ and ‘Gulbarga-Bidar, (NL), SCR’ have reported additional delays of 9, 15 and 69 months respectively due to fund constraints; the project ‘New Work for Construction of Metro Railway from Baranagar to Barrackpore and Dakshineswar (MTP), RVNL’ has reported additional delay of 24 months due to delay in forest clearance and shifting of utilities of State Government; and the projects ‘Champajharan-Bimalgarh Doubling Extension, SER’ , ‘New BG Line from Dudhnoi-Mendipatar, NEFR’ and ‘Ambari Falakata to New Maynaguri, NEFR’ have reported additional delays of 12 months each (however, no specific reasons have been reported by the project authorities for the delay in these projects).

v) In the **Petroleum Sector**, out of 77 projects, 46 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-9 months, out of which 3 are Mega projects. The projects ‘Pipeline for Transfer of LPG from BPCR/HPCR to Uran LPG Plant, BPCL’ and ‘Central Gas Gathering Station and Offtake Point, OIL’ have reported additional delays of 1 month each due to slow progress in civil works; the projects ‘Construction of 6 ETPS, ONGC’ and ‘Polypropylene Unit, Mangalore Refinery’ have reported additional delays of 3 and 4 months respectively due to slow progress in civil works; the project ‘UP-Gradation of Konaban GGS and Pipeline Grid Project, Tripura, ONGC’ has reported additional delay of 9 months due to ROU problem; and the projects ‘Strategic Crude Oil Storage Project at Mangalore, ISPRL’ and ‘Strategic Crude Oil Storage Project at Padur, ISPRL’ have reported additional delays of 4 months each (however, no specific reasons have been reported by the project authority for the delay in these projects).

vi) In the **Road Sector**, out of 136 projects, 92 projects are delayed. During the month 8 projects have reported additional delays in the range of 1-12 months, out of which 4 are Mega projects. The projects ‘Ugradation of Hyderabad-Bangalore Section, NHAI’ and ‘Development of Adiquate Road Connectivity to Chennai- Ennore Port Connectivity, NHAI’ have reported additional delays of 1 month each; the projects ‘Beawar-Pali-Pindwara, NHAI’ and ‘Kota Bypass,RJ-4, NH-76, NHAI’ have reported

additional delays of 2 and 3 months respectively; the projects ‘Surat- Dahisar(Six Lane) KM 263 to KM 502, NHAI’ and ‘Jammu-Udhampur KM.27.5 to KM.67.00, NHAI’ have reported additional delays of 5 months each; and the projects ‘SIX LANNING OF Chandikhol-Jagatpur-Bhubaneswar, NHAI’ and ‘2-Lanning with PS Motihari-Raxaul, NHAI’ have reported additional delays of 6 and 12 months respectively (however, no specific reasons have been reported by the project authority for the delay in these project).

vii) In the **Power Sector**, out of 99 projects, 56 projects are delayed. During the month 17 projects have reported additional delays in the range of 1-27 months, out of which 11 are Mega projects. The projects ‘Common System Associated with ISGS Projects in Krishna pattnam of Andhra Pradesh, PGCIL’ and ‘System Strengthening-XVIII in Southern Region Grid, PGCIL’ have reported additional delays of 1 month each due to ROW problems; the project ‘765 KV Pooling Station and Network with DVC and Maithob RBC, PGCIL’ has reported additional delay of 2 months due to maoist problem; the projects ‘Transmission System for Phase-I Generation Project in Orissa - Part-A, PGCIL’ and ‘Sytem Strengthening XIII of SR Grid, PGCIL’ have reported additional delays of 2 months each due to ROW problems; the project ‘Transmission System for Phase-I Generathon Project in Orissa Part-C, PGCIL’ has reported additional delay of 2 months due to delay in forest clearance; the projects ‘Western Region Strengthening Scheme-V, PGCIL’ and ‘Transmission System Strengthening in Western Part of WR for IPPS Generation Projects in Chhattisgarh, PGCIL’ have reported additional delays of 2 and 3 months respectively due to ROW problems; the project ‘System Strengthening -XII of SR, PGCIL’ has reported additional delay of 3 months due to frequent bandhs; the projects ‘System Strengthening in Raipur-Wardha Corridor for IPP Projects in Chhattisgarh, PGCIL’ and ‘Transmission System Associated with Mundra Ultra Mega Power Project, PGCIL’ have reported additional delays of 5 and 9 months respectively due to delay in forest clearance; the projects ‘Eastern Region Strengthening Scheme-III, PGCIL’ and ‘Establishment of Pooling Stations at Champa and Raigarh for IPP Generation Project in Chhattisgarh, PGCIL’ have reported additional delays of 6 months each due to delay in land acquisition and termination of contract respectively; the project ‘Northern Region System Strenghtening Scheme-XIX, PGCIL’ has reported additional delay of 27 months due to ROW problems; and the projects ‘Sytem Strengthening of Southern Region – XIV, PGCIL’ , ‘Common System Associated with Coastal Energen Private Limited and Ind-Barath Power (Madras) Limited, PGCIL’ and ‘Immediate Evacuation System with Barh-II TPS, PGCIL’ have reported additional delays of 1, 3 and 4 months respectively (however, no specific reason has been reported by the project authority for the delay in these projects).


12. The status as on 30.06.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

13. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	290	7
2	ROAD TRANSPORT AND HIGHWAYS	136	8
3	POWER	99	17
4	PETROLEUM	76	7
5	COAL	59	4
6	STEEL	20	7
7	SHIPPING AND PORTS	19	0
8	TELECOMMUNICATIONS	11	2
9	CIVIL AVIATION	8	0
10	URBAN DEVELOPMENT	5	0
11	ATOMIC ENERGY	4	0
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	729	52

Sectoral break up of on-going infrastructure projects.

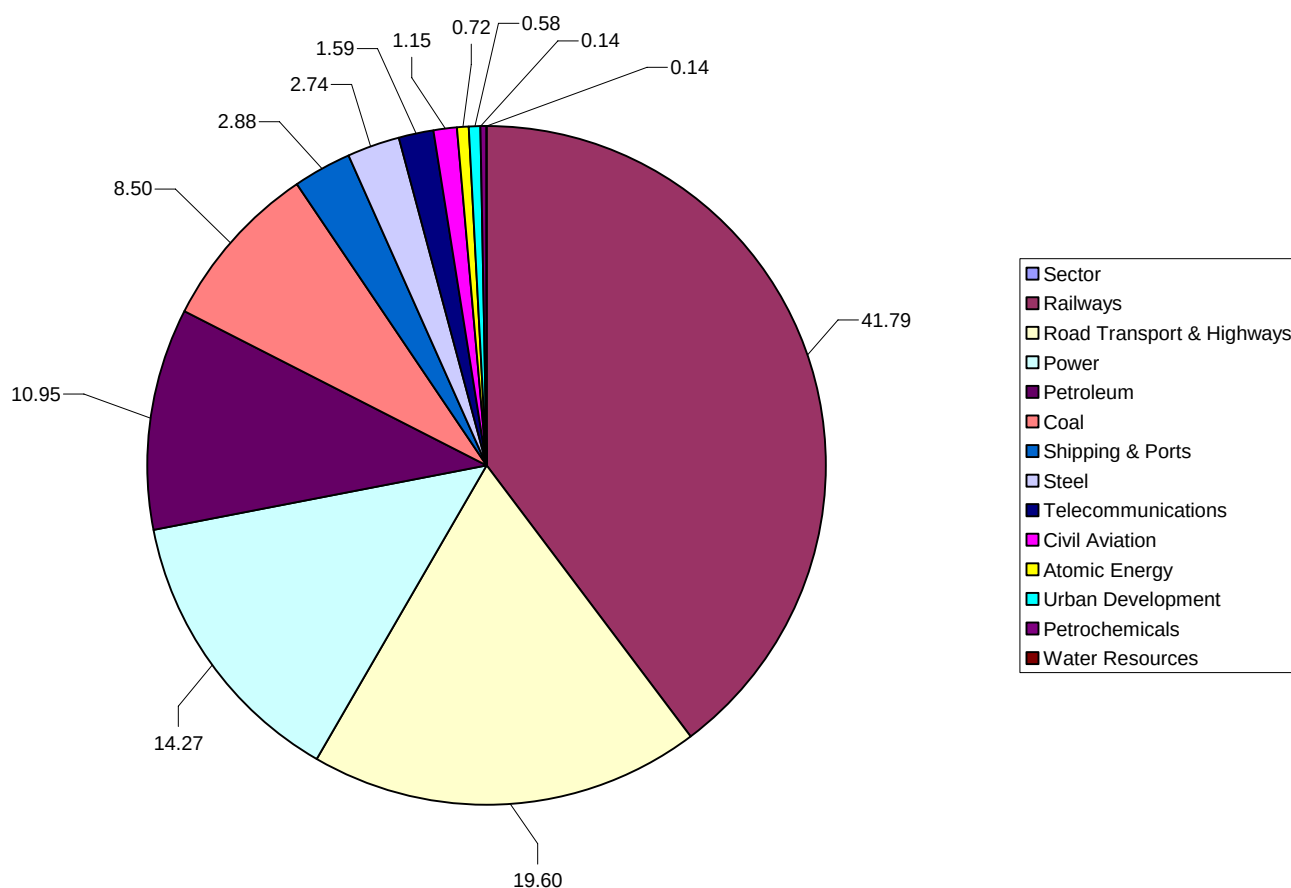

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2014			
	<u>COAL</u>			
1	BINA EXTN. PROJ(6.0 MTPA) (NORTHERN COAL FIELDS LIMITED) - [N06000019]	168.97	03/2014	67.53
	<u>POWER</u>			
2	PARBATI H.E.P. STAGE -III (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100250]	2,304.56	10/2010	2349.46
	June,2014			
	<u>PETROLEUM</u>			
3	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000039]	5,713.03	05/2010	3918.86
4	DEVELOPMENT OF B-46 CLUSTER FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000046]	1,436.21	07/2010	1165.53
5	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000060]	7,133.39	09/2012	2795.5
	<u>POWER</u>			
6	MOUDA STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000048]	5,459.28	08/2012	4056
7	VINDHYACHAL STTP STAGE-IV (NATIONAL THERMAL POWER CORPORATION) - [N18000072]	5,915.00	10/2012	N.A.
8	RIHAND STTP STAGE-III (2X500MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000073]	6,230.81	10/2012	4357
	<u>RAILWAYS</u>			
9	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000083]	156.00	-	424.43
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106236]	166.27	03/2008	200.4
11	CHITRADURGA-TUMKUR(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000157]	839.00	-	692.5


Summary of projects in the Flash Report for the month of June, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	735
Number of Projects completed/dropped/frozen in Current Month	9
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	4
Number of Projects in Current Month	729


Brief Analysis

Project Status with respect to Original Schedule: Out of 729 projects, 6 projects are ahead of schedule, 110 projects are on schedule and 290 projects are delayed. Of the balance, 300 projects do not have fixed dates of commissioning while 23 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

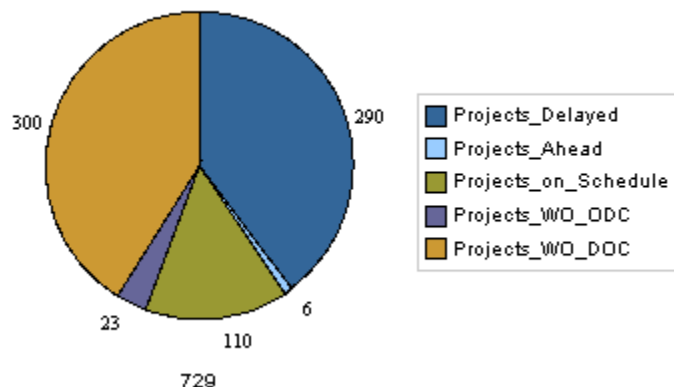

Investment Scenario

Total original cost of implementation of 729 projects when sanctioned, was of the order of Rs. 935003.47 crore but this was subsequently revised to Rs. 1108382.7 crore implying a cost overrun of 18.5%. The expenditure incurred on these projects till June, 2014 is Rs. 546208.61 crore, which is 49.3% of the revised cost of the projects.

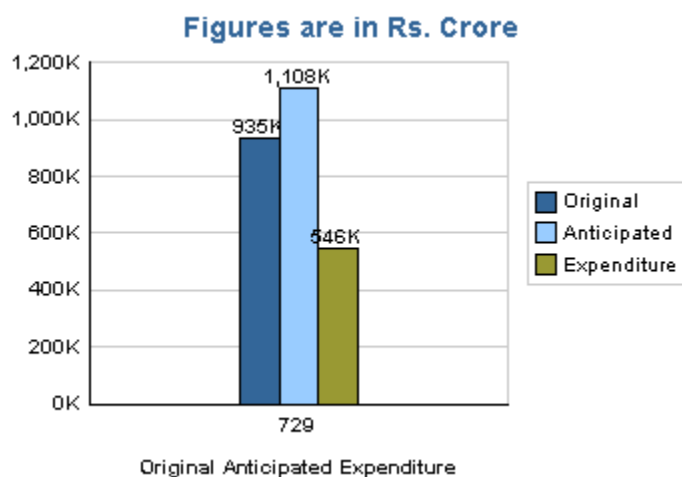

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	735
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects elevated to status of Major project during the current months	1
No of Projects added in Current Month	4
No of Projects in Current Month	729

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	290	6	110	23	300	729	39.78
Latest Approved (Date)	271	14	122	23	300	729	37.17

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	604	8,18,323.19	8,90,900.81	4,13,078.46	46.40	72,577.62	8.90
Project with Revision in Cost	125	1,65,773.91	2,17,481.89	1,33,130.15	61.20	51,707.98	31.20
Total	729	9,84,097.10	11,08,382.70	5,46,208.61	49.28	124285.6	12.63
Original Cost of All Projects							
Original Cost	729	9,35,003.47	11,08,382.70	5,46,208.61	49.30	1,73,379.23	18.50

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	290	497,453.91	598,654.31	396,858.89	66.30	101,200.40	20.30
Latest Approved (RCE)	271	508,436.53	575,640.89	386,673.76	67.20	67,204.36	13.20

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	58	81,437.44	89,246.50	72,469.67	81.20	7,809.06	9.60

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,035.5	6,926.8	14.8	3	4,086.1	4,977.5	21.8
3	COAL	59	41,532.1	51,354.2	23.6	8	9,767.8	20,187.6	106.7
4	STEEL	20	65,959.3	72,144.4	9.4	6	24,000.9	30,216.1	25.9
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	76	183,112.7	191,919.8	4.8	17	51,017.4	66,284.0	29.9
7	POWER	99	231,756.8	246,995.6	6.6	12	35,453.3	50,692.1	43.0
8	RAILWAYS	290	162,934.0	274,846.1	68.7	142	69,404.8	181,809.8	162.0
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.4	104,296.5	1.9	8	2,649.0	4,651.6	75.6
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	9	8,629.0	11,916.7	38.1
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	2	6,509.2	11,782.1	81.0
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		729	935,003.5	1,108,382.7	18.5	214	235,577.9	417,052.8	77.0

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	24,561.0	29,968.8	22.0	9	11,299.4	17,574.1	55.5
2	ARUNACHAL PRADESH	3	9,356.2	9,356.2	0.0	0	0.0	0.0	0.0
3	ASSAM	38	24,556.9	38,943.7	58.6	14	12,253.0	26,729.0	118.1
4	BIHAR	46	33,802.8	46,815.8	38.5	15	20,573.6	33,968.7	65.1
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	15.8
6	GUJARAT	31	37,705.2	38,694.3	2.6	6	2,786.3	4,095.7	47.0
7	HARYANA	10	4,757.4	6,907.4	45.2	3	1,633.6	3,783.5	131.6
8	HIMACHAL PRADESH	5	13,457.4	18,070.4	34.3	2	5,574.0	10,187.0	82.8
9	JAMMU AND KASHMIR	6	11,799.1	30,702.5	160.2	2	4,738.7	23,642.0	398.9
10	KARNATAKA	34	78,767.4	92,965.8	18.0	18	14,297.2	28,833.8	101.7
11	KERALA	12	22,610.7	25,135.4	11.2	5	5,480.4	8,005.2	46.1
12	MADHYA PRADESH	18	24,606.2	26,088.8	6.0	5	3,061.7	4,963.7	62.1
13	MAHARASHTRA	46	73,310.2	85,861.6	17.1	16	21,478.9	35,788.1	66.6
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	724.1
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	MIZORAM	2	988.1	3,307.1	234.7	2	988.1	3,307.1	234.7
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	187.8
18	ODISHA	34	61,113.8	68,005.7	11.3	12	33,433.6	40,325.5	20.6
19	PUNJAB	4	1,680.2	1,653.2	-1.6	0	0.0	0.0	0.0
20	RAJASTHAN	25	25,638.7	25,695.9	0.2	5	2,337.2	2,880.5	23.2
21	SIKKIM	2	1,648.9	3,684.9	123.5	1	1,339.5	3,375.4	152.0
22	TAMIL NADU	40	54,818.7	71,711.4	30.8	21	31,836.2	48,728.9	53.1
23	TRIPURA	6	2,966.3	4,409.2	48.6	3	2,129.4	3,606.7	69.4
24	UTTAR PRADESH	26	14,361.5	17,036.6	18.6	8	2,768.5	5,491.8	98.4
25	WEST BENGAL	38	57,186.3	65,301.4	14.2	9	22,482.8	30,597.9	36.1
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	DELHI	4	41,531.3	41,531.3	0.0	0	0.0	0.0	0.0
28	CHHATISGARH	24	57,805.7	65,314.3	13.0	6	2,585.1	10,093.7	290.5
29	JHARKHAND	29	21,317.1	21,927.5	2.9	4	1,301.4	2,083.6	60.1
30	UTTARAKHAND	7	9,501.0	13,063.9	37.5	5	7,496.0	11,058.9	47.5
31	TELANGANA	22	9,563.3	12,332.1	29.0	5	1,473.0	4,241.8	188.0
32	MULTI STATE	187	204,107.8	225,495.4	10.5	35	20,317.3	44,859.0	120.8
Total		729	935,003.5	1,108,382.7	18.5	214	235,577.9	417,052.8	77.0

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 75
2	CIVIL AVIATION	8	6,035.5	6,926.8	14.8	2	653.7	653.7	7 - 71
3	COAL	59	41,532.1	51,354.2	23.6	31	26,843.9	37,085.7	24 - 120
4	STEEL	20	65,959.3	72,144.4	9.4	15	64,701.5	70,655.4	4 - 71
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	76	183,112.7	191,919.8	4.8	45	127,800.0	138,088.3	3 - 110
7	POWER	99	231,756.8	246,995.6	6.6	56	135,181.9	149,427.8	1 - 106
8	RAILWAYS	290	162,934.0	274,846.1	68.7	37	29,667.7	80,673.3	3 - 246
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.4	104,296.5	1.9	92	65,761.2	67,736.2	2 - 120
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	3	1,889.9	3,270.0	5 - 99
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	4	2,018.2	1,843.9	37 - 68
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		729	935,003.5	1,108,382.7	18.5	290	497,453.9	598,654.3	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	24,561.0	29,968.8	22.0	8	17,332.3	20,539.0	11 - 71
2	ARUNACHAL PRADESH	3	9,356.2	9,356.2	0.0	3	9,356.2	9,356.2	13 - 99
3	ASSAM	38	24,556.9	38,943.7	58.6	29	15,644.2	23,475.8	21 - 120
4	BIHAR	46	33,802.8	46,815.8	38.5	12	22,014.1	32,223.9	4 - 98
5	GOA	1	335.6	388.5	15.8	0	0.0	0.0	-
6	GUJARAT	31	37,705.2	38,694.3	2.6	11	24,598.1	24,536.8	6 - 30
7	HARYANA	10	4,757.4	6,907.4	45.2	3	1,875.1	3,055.1	40 - 55
8	HIMACHAL PRADESH	5	13,457.4	18,070.4	34.3	2	8,446.7	11,139.6	73 - 106
9	JAMMU AND KASHMIR	6	11,799.1	30,702.5	160.2	6	11,799.1	30,702.5	6 - 181
10	KARNATAKA	34	78,767.4	92,965.8	18.0	6	16,777.3	17,020.6	20 - 48
11	KERALA	12	22,610.7	25,135.4	11.2	5	17,074.0	17,774.0	5 - 58
12	MADHYA PRADESH	18	24,606.2	26,088.8	6.0	8	3,545.9	3,658.7	5 - 74
13	MAHARASHTRA	46	73,310.2	85,861.6	17.1	17	27,858.7	34,577.8	3 - 144
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	72 - 72
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	1	536.0	536.0	11 - 11
16	MIZORAM	2	988.1	3,307.1	234.7	2	988.1	3,307.1	35 - 103
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	24 - 24
18	ODISHA	34	61,113.8	68,005.7	11.3	19	52,496.3	55,728.8	4 - 84
19	PUNJAB	4	1,680.2	1,653.2	-1.6	1	705.0	705.0	21 - 21
20	RAJASTHAN	25	25,638.7	25,695.9	0.2	7	17,752.0	17,305.7	2 - 76
21	SIKKIM	2	1,648.9	3,684.9	123.5	2	1,648.9	3,684.9	15 - 71
22	TAMIL NADU	40	54,818.7	71,711.4	30.8	15	36,540.7	45,969.7	6 - 99
23	TRIPURA	6	2,966.3	4,409.2	48.6	3	1,996.4	3,236.9	31 - 120
24	UTTAR PRADESH	26	14,361.5	17,036.6	18.6	11	5,608.5	7,089.5	13 - 93
25	WEST BENGAL	38	57,186.3	65,301.4	14.2	14	30,514.3	34,623.8	3 - 141
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	-
27	DELHI	4	41,531.3	41,531.3	0.0	1	2,494.0	2,494.0	8 - 8
28	CHHATISGARH	24	57,805.7	65,314.3	13.0	16	43,036.4	49,771.8	5 - 120
29	JHARKHAND	29	21,317.1	21,927.5	2.9	14	11,091.8	11,680.0	3 - 132
30	UTTARAKHAND	7	9,501.0	13,063.9	37.5	5	7,754.2	11,207.0	26 - 79
31	TELANGANA	22	9,563.3	12,332.1	29.0	5	1,898.8	3,098.7	24 - 47
32	MULTI STATE	187	204,107.8	225,495.4	10.5	62	104,493.1	111,713.0	1 - 246
	Total	729	935,003.5	1,108,382.7	18.5	290	497,453.9	598,654.3	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 75
2	CIVIL AVIATION	8	6,035.5	6,926.8	14.8	2	653.7	653.7	7 - 71
3	COAL	59	41,532.1	51,354.2	23.6	30	25,655.6	29,473.4	24 - 84
4	STEEL	20	65,959.3	72,144.4	9.4	13	63,507.0	69,149.7	4 - 71
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	76	183,112.7	191,919.8	4.8	44	124,559.0	131,449.3	3 - 110
7	POWER	99	231,756.8	246,995.6	6.6	54	132,316.3	146,017.2	1 - 106
8	RAILWAYS	290	162,934.0	274,846.1	68.7	36	29,342.7	79,556.8	3 - 246
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.4	104,296.5	1.9	82	63,808.8	65,658.7	2 - 120
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	1	1,228.0	2,158.2	58 - 58
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	3	1,634.2	1,459.9	37 - 68
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		729	935,003.5	1,108,382.7	18.5	270	485,641.2	574,796.9	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,625.0	6,926.8	4.6	2	2,660.6	2,962.5	11.3
3	COAL	59	51,328.6	51,354.2	0.0	4	1,431.8	1,716.6	19.9
4	STEEL	20	70,209.4	72,144.4	2.8	1	14,443.0	16,408.0	13.6
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	76	192,588.0	191,919.8	-0.3	6	36,616.6	40,179.2	9.7
7	POWER	99	233,458.4	246,995.6	5.8	10	32,017.0	45,554.2	42.3
8	RAILWAYS	290	183,746.5	274,846.1	49.6	129	72,788.5	164,341.0	125.8
9	ROAD TRANSPORT AND HIGHWAYS	136	102,859.7	104,296.5	1.4	8	2,992.3	4,651.6	55.5
10	SHIPPING AND PORTS	19	17,488.0	18,600.6	6.4	6	4,617.6	5,941.7	28.7
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	74,052.2	79,266.2	7.0	1	6,395.0	11,609.0	81.5
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		729	984,097.1	1,108,382.7	12.6	174	198,022.9	327,899.1	65.6

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	CIVIL AVIATION	8	6,035.46	6,926.79	14.77	1	1,808.00	2,015.00	13- 13
3	COAL	59	41,532.08	51,354.22	23.65	1	1,188.31	7,612.33	120- 120
4	STEEL	20	65,959.26	72,144.44	9.38	5	9,557.89	13,808.07	37- 71
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	76	183,112.71	191,919.84	4.81	5	12,438.19	21,985.78	20- 110
7	POWER	99	231,756.78	246,995.55	6.58	1	1,657.00	2,978.86	79- 79
8	RAILWAYS	290	162,933.96	274,846.09	68.69	12	9,597.46	21,820.47	0- 144
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,296.49	1.93	3	580.65	705.74	59- 80
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	5	5,400.70	7,558.41	10- 99
11	TELECOMMUNICATIONS	11	5,295.83	5,199.48	-1.82	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		729	935003.47	1108382.7	18.54	33	42228.2	78484.66	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 75
2	CIVIL AVIATION	8	6,035.46	6,926.79	14.77	0	0.00	0.00	0- 0
3	COAL	59	41,532.08	51,354.22	23.65	6	9,127.17	19,498.95	24- 120
4	STEEL	20	65,959.26	72,144.44	9.38	4	23,538.89	29,522.85	33- 71
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	76	183,112.71	191,919.84	4.81	14	48,053.07	62,605.36	12- 110
7	POWER	99	231,756.78	246,995.55	6.58	8	32,287.84	45,988.78	10- 87
8	RAILWAYS	290	162,933.96	274,846.09	68.69	32	24,097.25	75,102.87	3- 246
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,296.49	1.93	8	2,649.01	4,651.57	40- 93
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	2	1,378.00	2,758.16	58- 99
11	TELECOMMUNICATIONS	11	5,295.83	5,199.48	-1.82	1	149.15	158.72	63- 63
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		729	935003.47	1108382.7	18.54	77	157943.38	263234.26	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	10/2007	5,713.03	05/2010	8,813.41	04/2014	3,918.86
2	DEVELOPMENT OF B-46 CLUSTER FIELD	06/2007	1,436.21	07/2010	1,456.96	05/2014	1,165.53
3	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II	01/2009	7,133.39	09/2012	7,133.39	04/2014	2,795.50
	<u>POWER</u>						
4	MOUDA STTP	11/2008	5,459.28	08/2012	6,010.89	03/2014	4,056.00
5	RIHAND STTP STAGE-III (2X500MW)	01/2009	6,230.81	10/2012	6,230.81	03/2014	4,357.00
6	VINDHYACHAL STTP STAGE-IV	01/2009	5,915.00	10/2012	5,915.00	N.A.	.00
	<u>RAILWAYS</u>						
7	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	09/1996	156.00	N.A.	407.98	06/2014	424.43
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
8	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	12/2003	166.27	03/2008	193.10	02/2008	200.40
9	CHITRADURGA-TUMKUR(NH-4)	03/2011	839.00	N.A.	839.00	06/2014	692.50

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	555.52	3/2021	555.52	3/2021
2	KAPURIA UG(PSLW)	8/2011	988.35	4/2017	988.35	4/2017
3	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	1,055.05	3/2018	1,055.05	3/2018
4	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU	4/2012	364.75	10/2014	364.75	10/2014

Milestones (Cumulative due & achieved)		
Total	3487	
Achieved up to month	1391	

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,027.59	06/2009	06/2014	09/2014	3
2	ADRIYALA SHAFT PROJECT SCCL	212.34	1,228.39	03/2013	10/2014	03/2015	5
3	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
4	MOONIDIH XV SEAM UG BCCL	1,230.27	1,230.27	04/2015	04/2015	04/2019	48
	<u>STEEL</u>						
5	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	09/2008	06/2014	08/2014	2
6	EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	12/2011	07/2014	09/2014	2
7	EXPANSION OF ROURKELA STEEL PLANT SAIL	11,812.00	11,812.00	03/2013	09/2014	12/2014	3
8	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) NMDC	572.00	572.00	04/2013	09/2014	12/2014	3
9	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES SAIL	187.33	187.33	10/2013	08/2014	12/2014	4
10	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP SAIL	160.48	160.48	09/2014	09/2014	01/2015	4
11	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH SAIL	332.65	332.65	08/2014	08/2014	01/2015	5
	<u>PETROLEUM</u>						
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT BPCL	246.81	276.83	04/2012	06/2014	07/2014	1
13	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT OIL	144.02	204.29	06/2012	06/2014	07/2014	1
14	CONSTRUCTION OF 6 ETPS ONGC	302.26	240.95	09/2012	12/2014	03/2015	3
15	POLYPROPYLENE UNIT MANGALORE REFIN	1,803.78	1,803.78	07/2012	06/2014	10/2014	4
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE ISPRL	732.00	1,227.00	10/2011	06/2015	10/2015	4

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR ISPRL	993.00	1,693.00	01/2012	06/2015	10/2015	4
18	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA ONGC	288.04	253.66	08/2012	06/2014	03/2015	9
	<u>POWER</u>						
19	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) PGCIL	1,637.34	1,637.34	08/2014	08/2014	09/2014	1
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	297.33	08/2014	08/2014	09/2014	1
21	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID PGCIL	1,263.26	1,263.26	11/2014	11/2014	12/2014	1
22	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC PGCIL	7,075.33	7,075.33	08/2012	06/2014	08/2014	2
23	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A PGCIL	2,074.86	2,074.86	03/2013	09/2014	11/2014	2
24	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C PGCIL	2,569.25	2,569.25	03/2014	12/2014	02/2015	2
25	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	09/2014	11/2014	2
26	WESTERN REGION STRENGTHENING SCHEME-V PGCIL	477.69	477.69	09/2010	06/2014	09/2014	3
27	SYSTEM STRENGTHENING -XII OF SR PGCIL	232.34	232.34	06/2012	06/2014	09/2014	3
28	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L PGCIL	1,940.13	1,940.13	09/2014	12/2014	03/2015	3
29	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH PGCIL	2,127.51	2,127.51	07/2014	12/2014	03/2015	3
30	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS PGCIL	901.77	901.77	08/2014	08/2014	12/2014	4
31	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,422.85	1,422.85	01/2015	01/2015	06/2015	5
32	EASTERN REGION STRENGTHENING SCHEME-III PGCIL	1,272.80	1,272.80	11/2012	06/2015	12/2015	6


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
33	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH PGCIL	1,961.87	1,961.87	05/2014	09/2014	03/2015	6
34	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	03/2015	12/2015	9
35	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX PGCIL	410.29	410.29	02/2012	12/2013	03/2016	27
	<u>RAILWAYS</u>						
36	MUNEERABAD-MAHABOBNAGAR(NL),SCR SCR	218.24	645.00	N.A.	03/2014	12/2014	9
37	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION SER	149.90	184.91	03/2015	12/2015	12/2016	12
38	NEW BG LINE FROM DUDHNOI-MENDIPATAR NEFR	175.43	247.75	N.A.	03/2014	03/2015	12
39	AMBARI FALAKATA TO NEW MAYNAGURI NEFR	312.12	312.12	N.A.	03/2016	03/2017	12
40	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) MRTP	401.81	1,814.10	03/2004	12/2014	03/2016	15
41	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24
42	GULBARGA-BIDAR,SCR(NL) SCR	242.42	844.00	N.A.	05/2009	02/2015	69
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
43	UGRADATION OF HYDERABAD-BANGALORE SECTION NHAI	680.00	680.00	N.A.	06/2014	07/2014	1
44	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY NHAI	600.00	600.00	06/2013	06/2014	07/2014	1
45	BEAWAR-PALI-PINDWARA NHAI	2,388.00	2,388.00	06/2014	06/2014	08/2014	2
46	KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	06/2014	09/2014	3
47	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 NHAI	1,693.75	1,693.75	08/2011	06/2014	12/2014	6
48	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 NHAI	1,813.76	1,813.76	07/2013	06/2014	12/2014	6
49	SIX LANEING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR NHAI	1,047.00	1,047.00	06/2014	06/2014	12/2014	6


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
50	2-LANNING WITH PS MOTIHARI-RAXAUL NHAI	375.09	375.09	04/2014	03/2014	03/2015	12
	<u>TELECOMMUNICATIONS</u>						
51	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS BSNL	384.00	384.00	10/2010	12/2014	01/2015	1
52	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL BSNL	149.15	158.72	06/2009	06/2014	09/2014	3

Graphical Presentation of All Projects w.r.t. Original Schedule

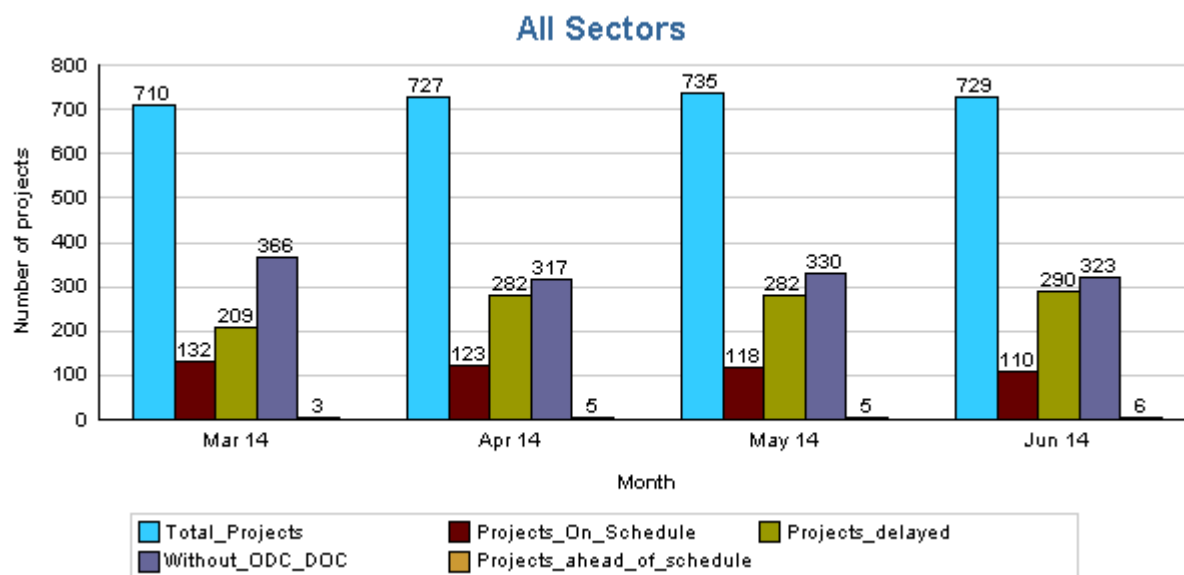

Break-up of 290 Delayed projects in June 2014

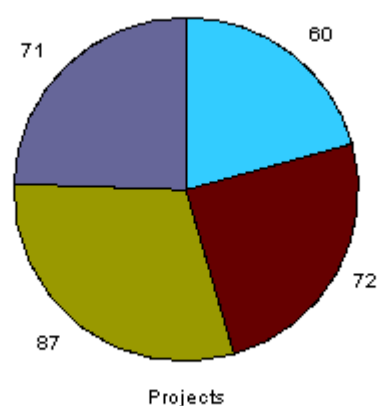


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of All Projects w.r.t. Revised Schedule

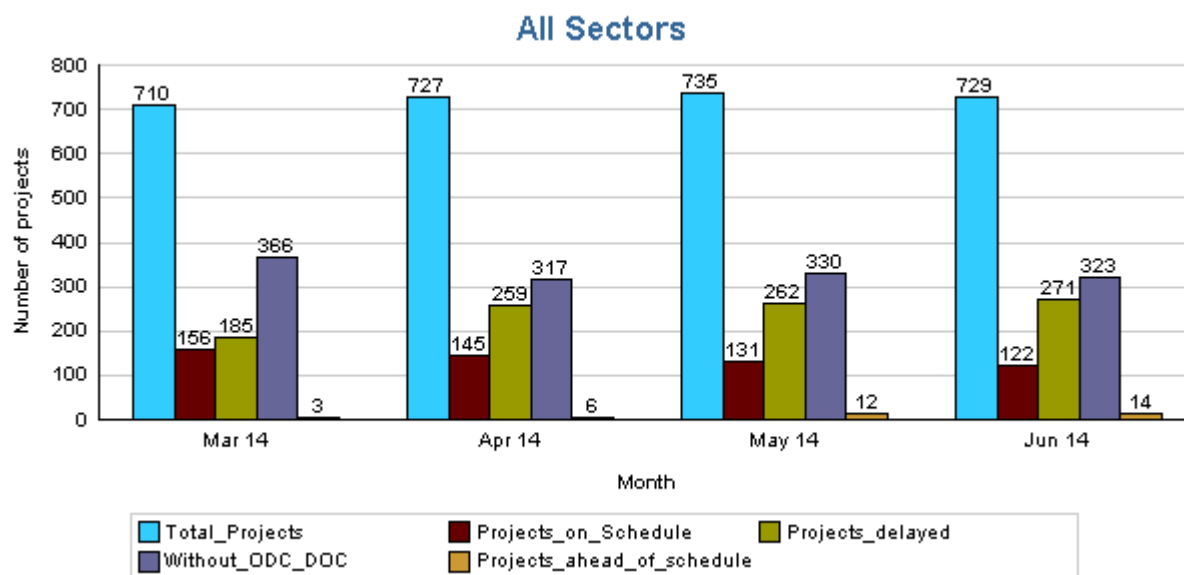


Break-up of 271 Delayed projects in June 2014

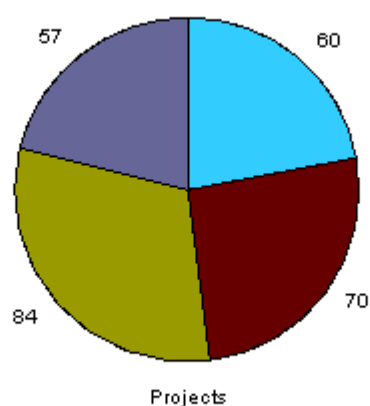


Delay in Months



Graphical Presentation of URBAN DEVELOPMENT Sector

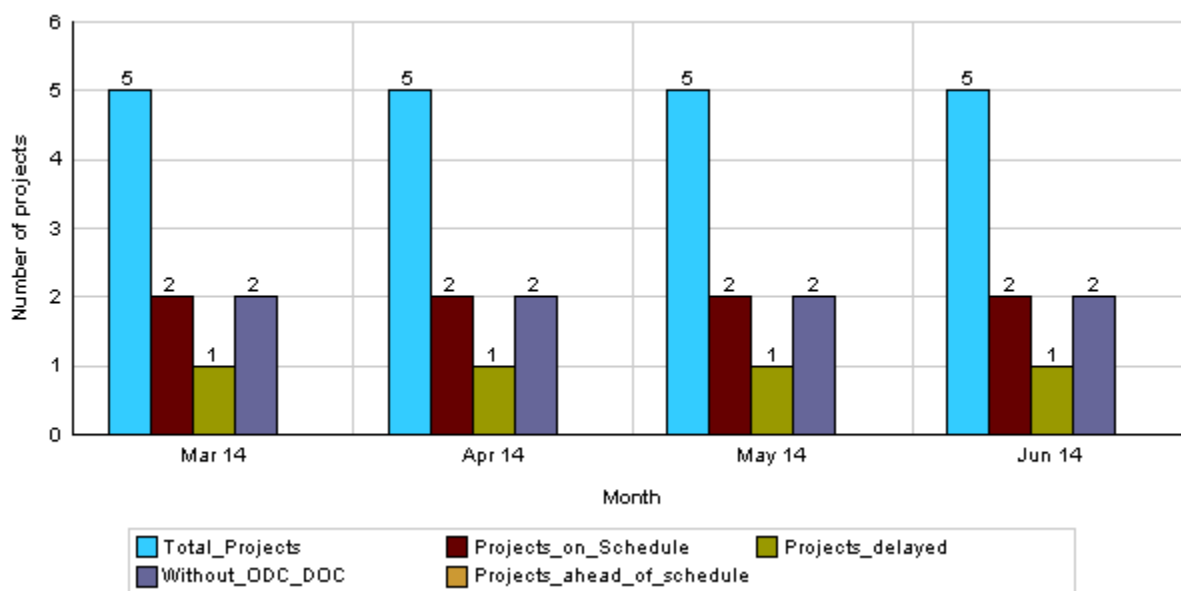


Break-up of 1 Delayed projects in June 2014

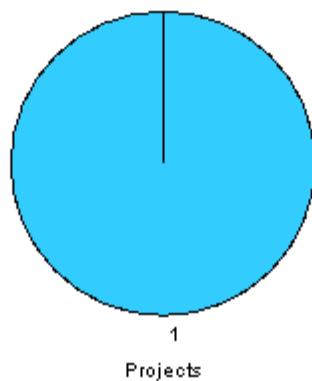


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	1	0	0	0

Graphical Presentation of TELECOMMUNICATIONS Sector

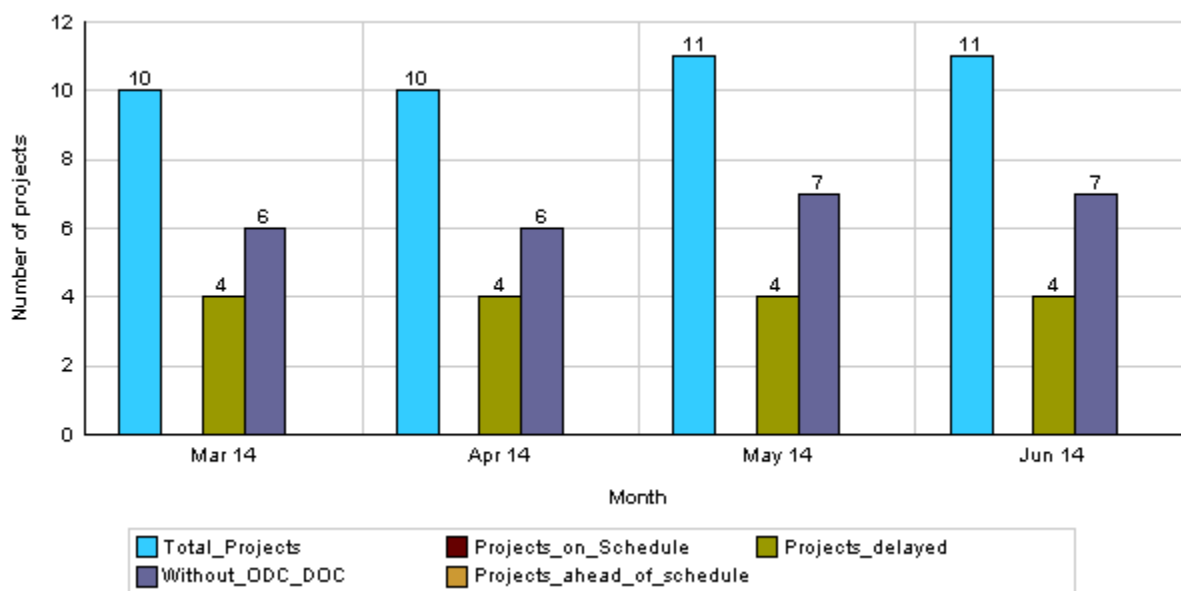


Break-up of 4 Delayed projects in June 2014




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	0	0	0	0

Graphical Presentation of SHIPPING AND PORTS Sector

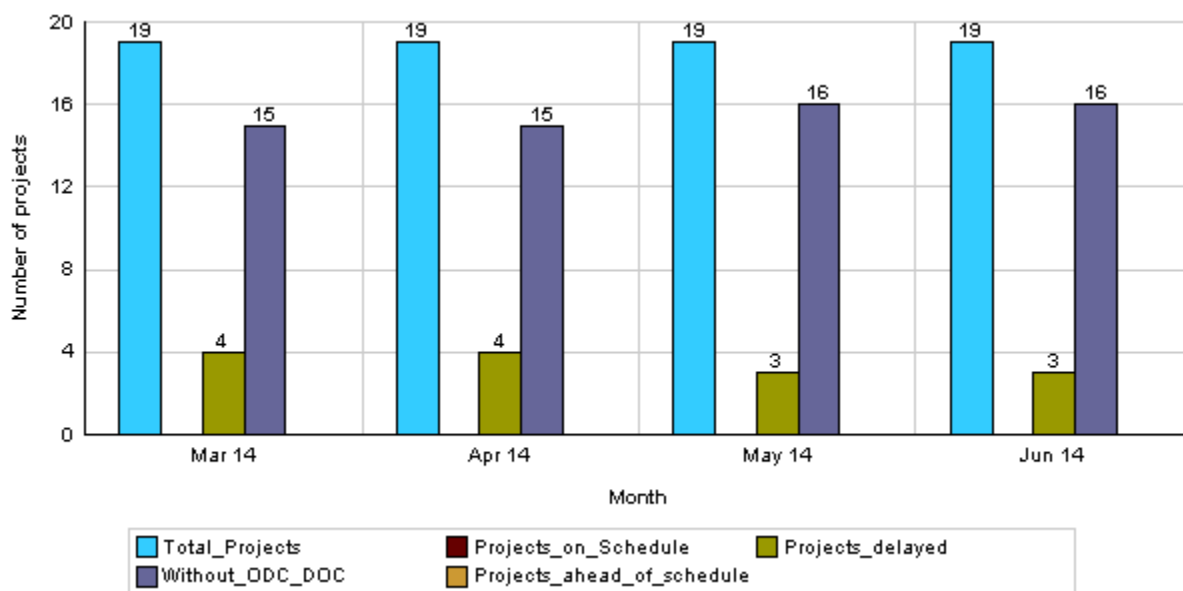


Break-up of 3 Delayed projects in June 2014

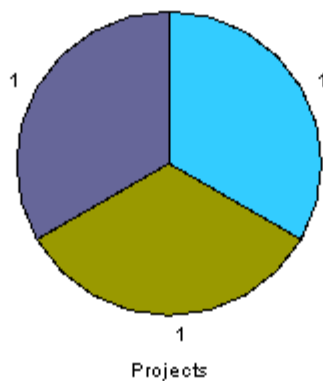


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

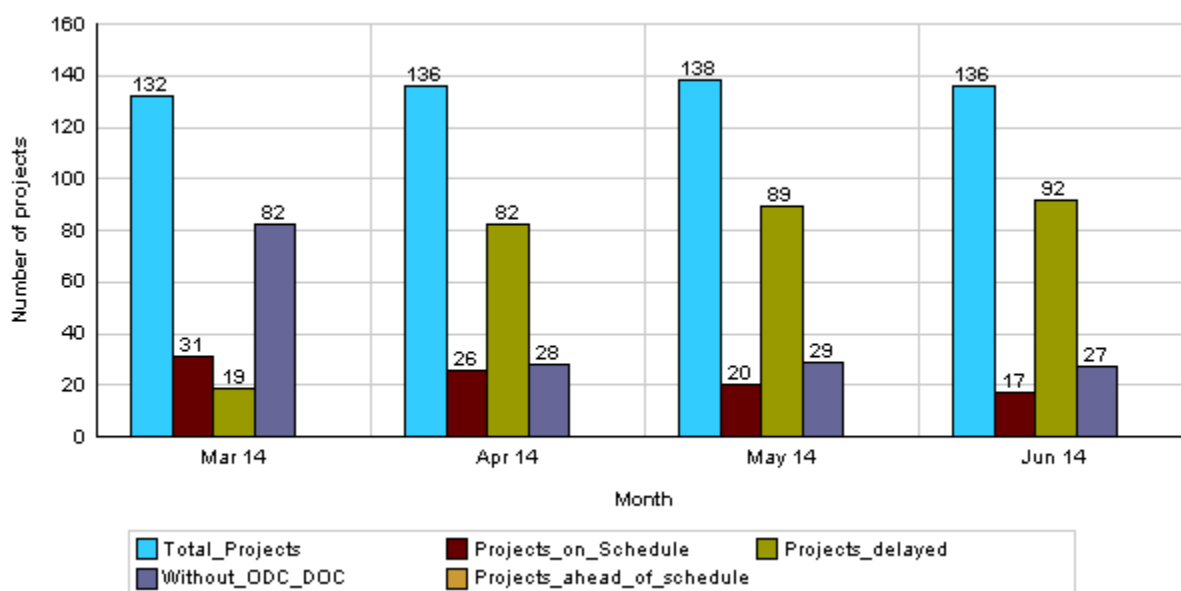


Break-up of 92 Delayed projects in June 2014

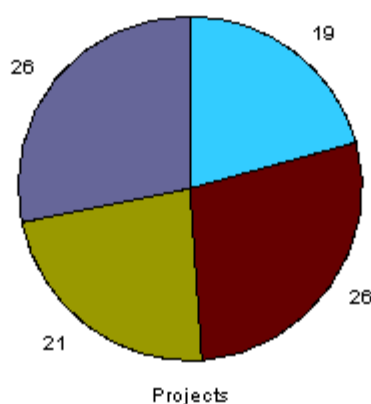


Delay in Months

Legend: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of RAILWAYS Sector

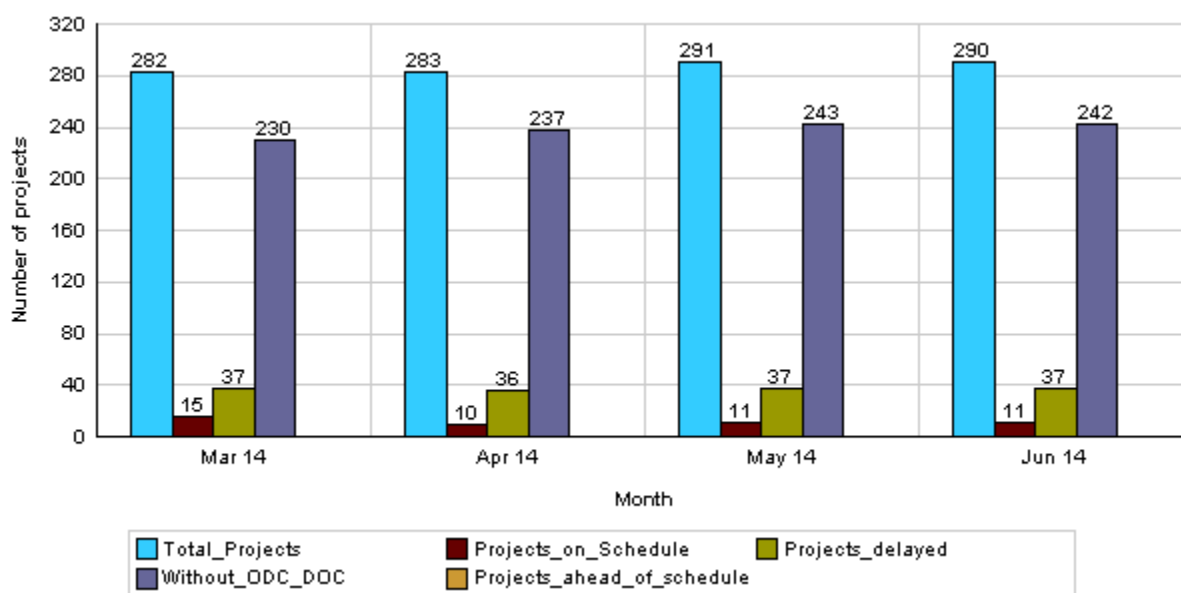


Break-up of 37 Delayed projects in June 2014

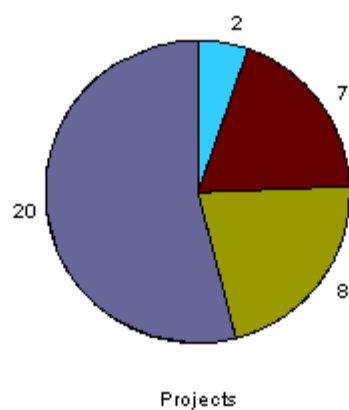


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of POWER Sector

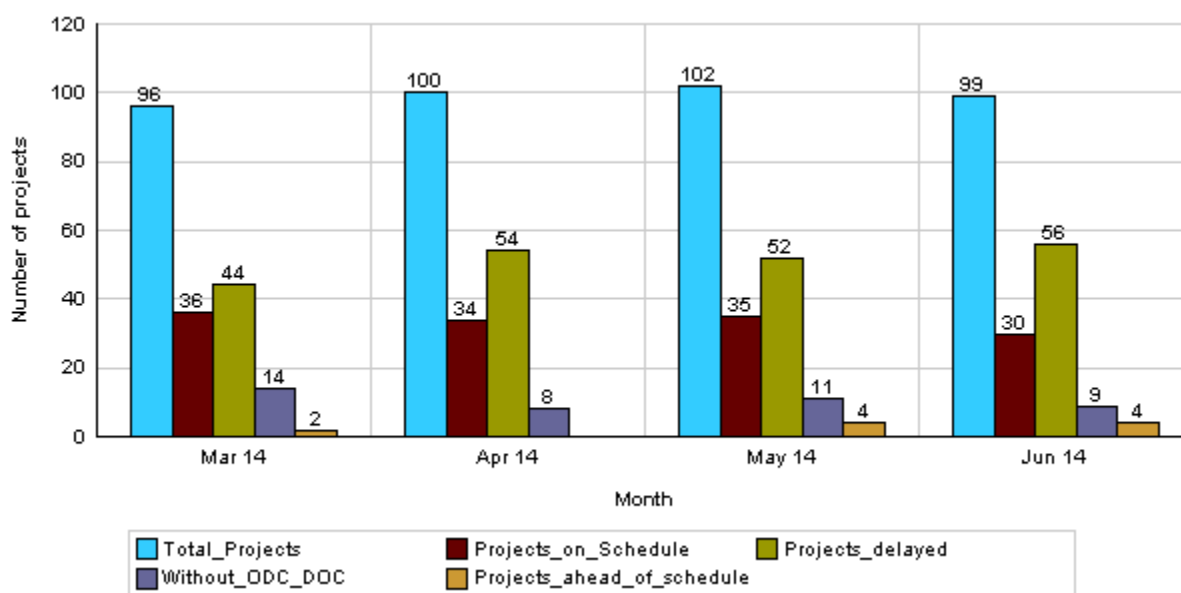


Break-up of 56 Delayed projects in June 2014

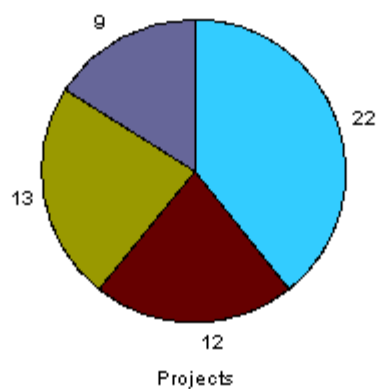


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	22	12	13	9

Graphical Presentation of PETROLEUM Sector

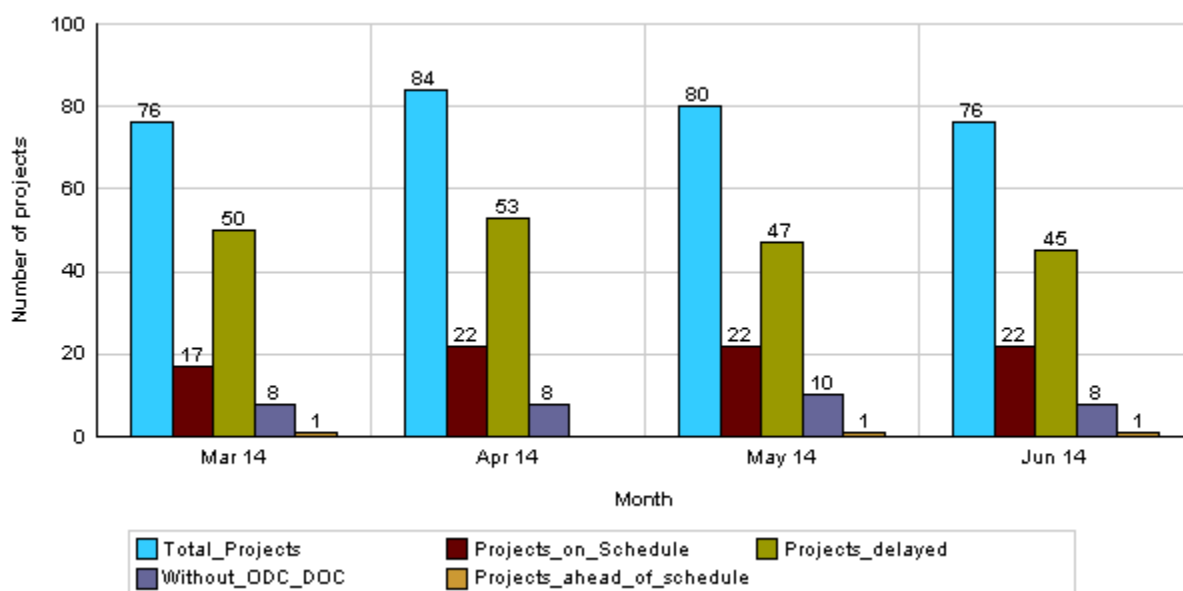


Break-up of 45 Delayed projects in June 2014

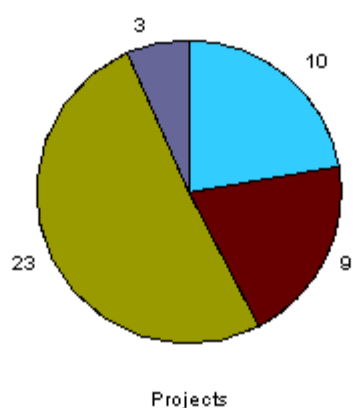

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	10	9	23	3

Graphical Presentation of STEEL Sector

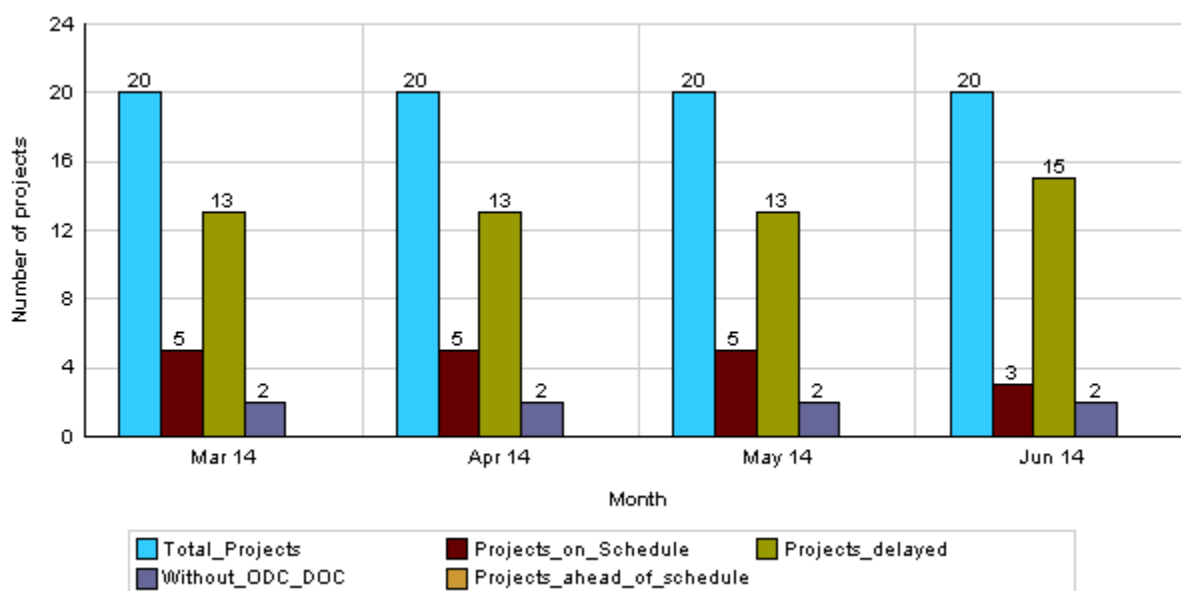


Break-up of 15 Delayed projects in June 2014




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	2	6	5	2

Graphical Presentation of COAL Sector

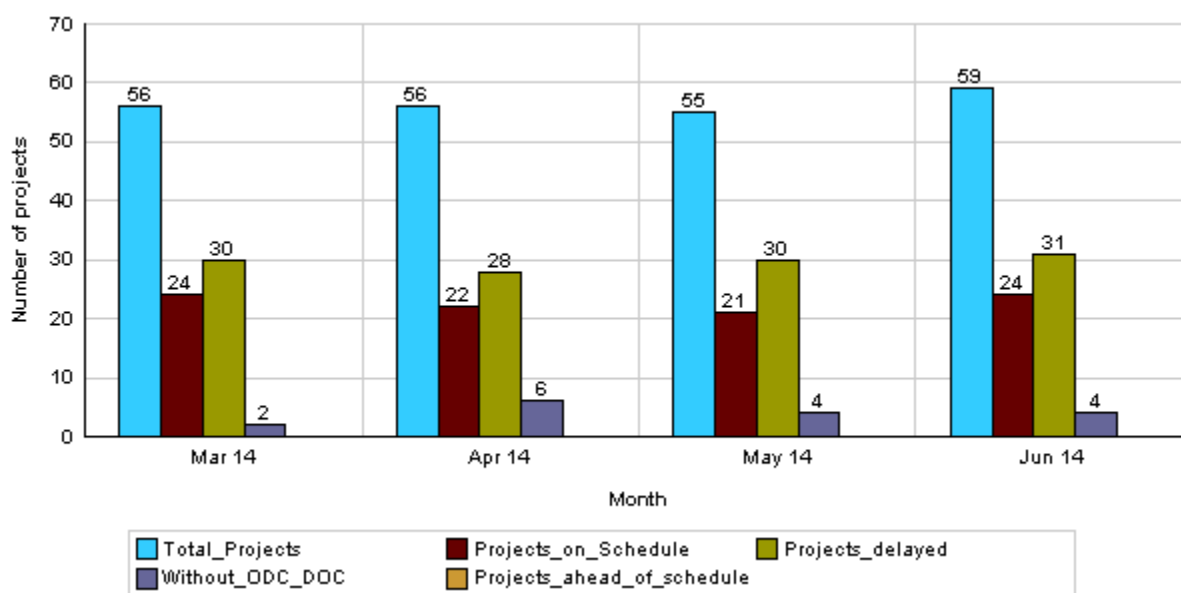


Break-up of 31 Delayed projects in June 2014

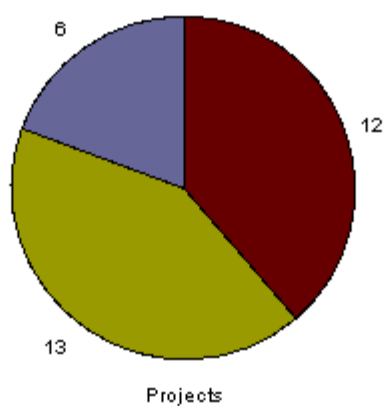


Delay in Months: 1-12 (light blue), 13-24 (dark red), 25-60 (olive green), MORE THAN 60 (purple)

Graphical Presentation of CIVIL AVIATION Sector

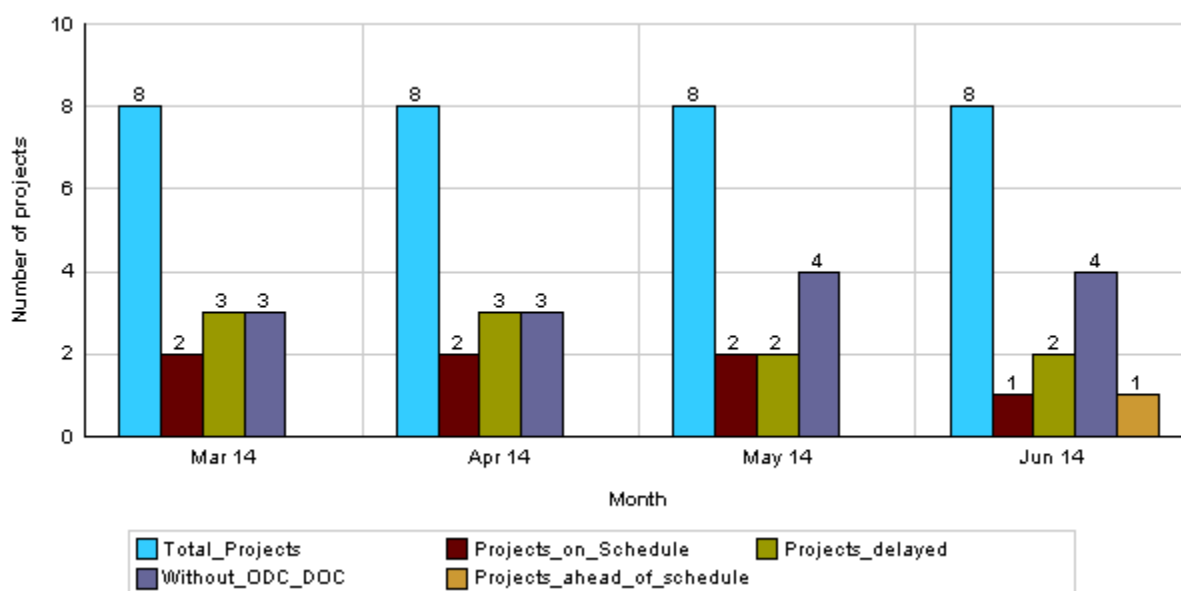


Break-up of 2 Delayed projects in June 2014

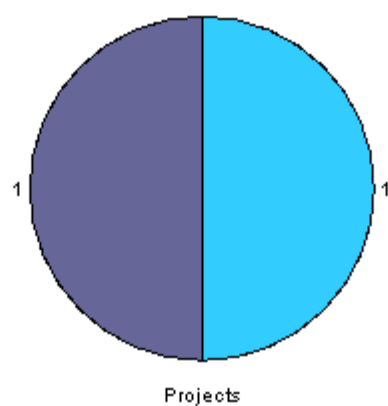


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

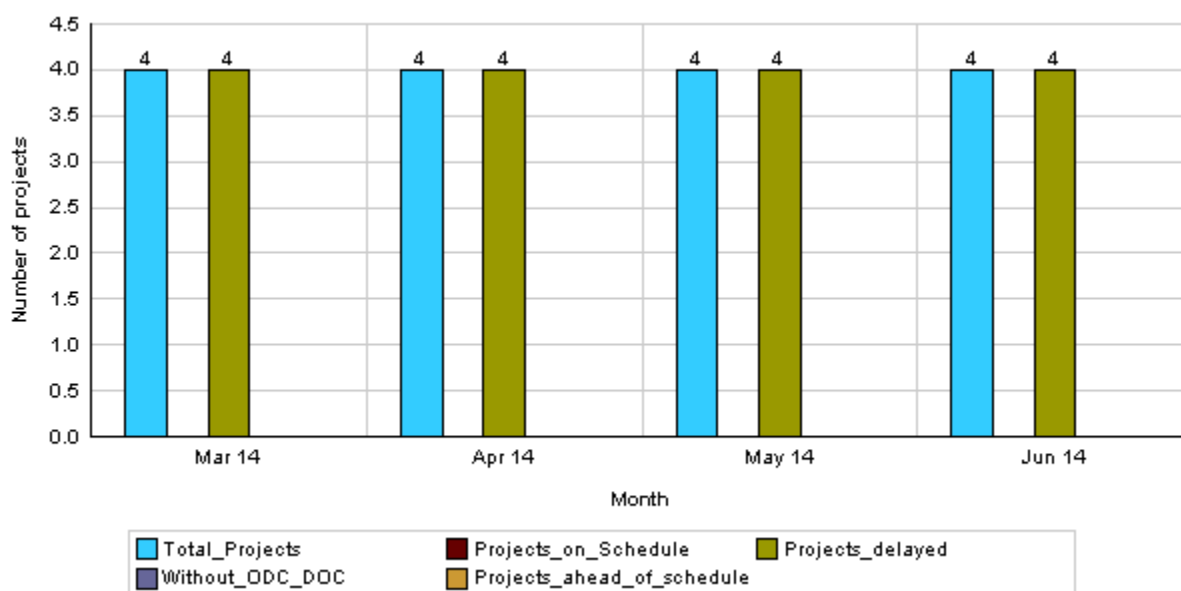

Break-up of 4 Delayed projects in June 2014

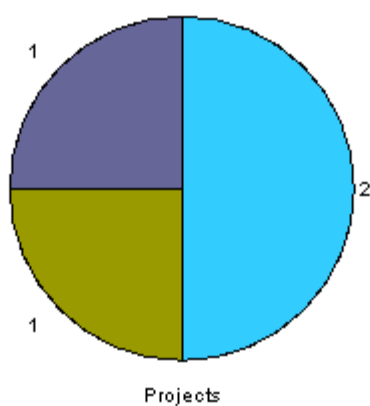

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	2	1	1	1

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	40,442.00	46,726.00	25,376.17
CIVIL AVIATION	8	6,035.46	6,624.95	6,926.79	5,823.27
COAL	59	41,532.08	51,328.63	51,354.22	18,493.21
STEEL	20	65,959.26	70,209.44	72,144.44	60,649.78
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	7,780.06
PETROLEUM	76	183,112.71	192,587.98	191,919.84	94,770.02
POWER	99	231,756.78	233,458.42	246,995.55	135,672.22
RAILWAYS	290	162,933.96	183,746.48	274,846.09	84,181.60
ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	102,859.69	104,296.49	91,608.16
SHIPPING AND PORTS	19	15,617.12	17,487.95	18,600.58	8,395.88
TELECOMMUNICATIONS	11	5,295.83	5,295.83	5,199.48	1,770.48
URBAN DEVELOPMENT	5	73,993.32	74,052.22	79,266.22	11,652.27
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	729	935,003.47	984,097.10	1,108,382.70	546,208.61

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(June 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,702.00	12/2008 -	03/2015	75(O) -	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,564.17	09/2010 -	03/2015	54(O) -	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,110.00	12/2016 -	03/2017	3(O) -	4/69
	Total		40,442.00 -	46,726.00	25,376.17				60/329
	<u>CIVIL AVIATION</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	2,573.92	2,573.92	05/2011 -	03/2013	-	0/2
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.81	01/2011 04/2013	12/2016	71(O) 44(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	280.74	05/2012 -	04/2014	-	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	2,015.00	1,939.20	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	264.84	03/2015 -	02/2015	-1(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	486.72	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,926.79	5,823.27				0/2
	<u>COAL</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	03/2015	24(O) 30(R)	19/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	87.18	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	664.21	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	95.88	03/2020 -	03/2020	0(O) -	0/3

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	155.48	03/2012 -	03/2016	48(O) -	4/5
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	100.27	03/2011 -	03/2017	72(O) -	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	139.74	03/2010 -	03/2016	72(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	57.78	03/2016 -	03/2016	0(O) -	0/6
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	181.71	03/2017 -	03/2017	0(O) -	3/11
23	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	255.25	03/2015 -	03/2015	0(O) -	0/3
24	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	610.33	-	03/2022 -	03/2022	0(O) -	0/0
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	272.43	03/2014 -	03/2016	24(O) -	2/9
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,541.93	03/2014 -	03/2016	24(O) -	6/13
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,553.35	03/2014 -	03/2016	24(O) -	10/16
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.30	03/2015 -	03/2015	0(O) -	1/13
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	117.27	03/2013 -	03/2015	24(O) -	2/7
31	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2015	0(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72(O) -	0/1
35	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	103.88	12/2012 -	03/2016	39(O) -	11/44
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.12	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	119.98	03/2013 -	03/2015	24(O) -	3/9
38	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	988.35	6.84	04/2017 -	04/2017	0(O) -	0/0
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	44.81	03/2014 -	03/2017	36(O) -	0/2
40	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
41	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	30.30	03/2018 -	03/2018	0(O) -	0/4

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
43	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	392.24	03/2013 -	03/2014	-	0/2
44	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	129.04	03/2010 -	03/2017	84(O) -	8/10
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	754.54	03/2013 03/2023	03/2023	120(O) 0(R)	0/16
46	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44(O) -	0/3
47	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.52	03/2014 -	03/2016	24(O) -	1/6
48	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36(O) -	4/6
49	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2019	48(O) -	0/0
50	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	-	0/0
51	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	341.57	12/2015 -	04/2018	28(O) -	5/33
52	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36(O) -	0/2
53	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	6.84	03/2021 -	03/2021	0(O) -	0/0
54	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.73	03/2012 -	03/2017	60(O) -	0/2
55	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	0.46	03/2015 -	03/2015	0(O) -	1/1
56	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.56	03/2014 -	03/2016	24(O) -	0/1
57	PURNADIDH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	121.62	03/2013 -	03/2015	24(O) -	0/3
58	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	38.70	03/2014 -	03/2016	24(O) -	0/0
59	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	221.41	03/2016 -	03/2016	0(O) -	0/2
60	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	226.56	03/2012 -	03/2015	36(O) -	24/27
61	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
62	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.14 -	430.14	65.57	03/2016 -	03/2016	0(O) -	6/48
63	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	06/2015	0(O) -	2/51
64	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	99.22	03/2015 -	03/2015	0(O) -	8/31
65	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	71.57	03/2012 -	-	-	24/42
66	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	21.25	03/2018 -	03/2018	0(O) -	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.14	03/2016 -	03/2016	0(O) -	0/12
68	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	139.29	03/2012 -	03/2016	48(O) -	0/2
69	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,991.89	06/2009 -	09/2014	63(O) -	19/23
70	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,415.43	03/2012 -	08/2014	29(O) -	24/39
71	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	57.87	10/2014 -	10/2014	0(O) -	0/10
	Total		41,532.08 -	51,354.22	18,493.21				212/789
	<u>STEEL</u>								
72	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	395.07	04/2013 09/2014	12/2014	20(O) 3(R)	17/18
73	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	10.55	05/2016 -	05/2016	0(O) -	0/3
74	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	349.64	260.63	12/2009 08/2010	06/2013	-	1/1
75	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	343.58	294.54	01/2010 02/2011	11/2013	-	3/3
76	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	309.56	05/2013 01/2015	01/2015	20(O) 0(R)	13/20
77	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	312.99	09/2009 05/2012	12/2014	63(O) 31(R)	1/1
78	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	373.28	12/2011 01/2015	01/2015	37(O) 0(R)	15/20
79	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.73	09/2008 12/2013	08/2014	71(O) 8(R)	3/4
80	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	111.54	08/2014 -	01/2015	5(O) -	2/4
81	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	111.90	11/2013 -	06/2015	19(O) -	2/4
82	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,938.98	03/2013 -	03/2015	24(O) -	29/35
83	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,734.82	12/2011 -	07/2014	31(O) -	18/24
84	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,238.22	12/2012 -	03/2015	27(O) -	14/20
85	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,000.18	12/2011 -	09/2014	33(O) -	23/29
86	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,872.97	10/2009 10/2012	09/2014	59(O) 23(R)	66/67
87	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	11,220.39	03/2013 -	12/2014	21(O) -	17/20

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	130.22	10/2013 -	12/2014	14(O) -	1/5
89	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	18.86	09/2014 -	01/2015	4(O) -	0/2
90	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	97.07	06/2015 -	06/2015	0(O) -	2/3
91	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	57.28	12/2014 -	12/2014	0(O) -	0/2
	Total		65,959.26 -	72,144.44	60,649.78				227/285
	<u>PETROCHEMICALS</u>								
92	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	8,920.00	7,780.06	04/2012 -	-	-	22/29
	Total		5,460.61 -	8,920.00	7,780.06				22/29
	<u>PETROLEUM</u>								
93	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	113.00	06/2012 -	07/2014	25(O) -	0/3
94	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	2,182.31	06/2012 -	05/2015	35(O) -	0/0
95	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018	0(O) -	0/0
96	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24(O) -	0/0
97	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24(O) -	0/0
98	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.17	03/2013 03/2014	03/2015	24(O) 12(R)	0/5
99	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,MULTI STATE	08/2011	586.00 -	586.00	182.89	08/2015 -	08/2015	0(O) -	0/12
100	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	540.92	338.71	07/2012 07/2012	-	-	6/7
101	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	151.39	06/2012 09/2013	07/2014	25(O) 10(R)	0/0
102	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	450.13	09/2011 -	12/2015	51(O) -	0/0
103	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	169.76	08/2013 -	09/2014	13(O) -	0/5
104	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	104.80	09/2012 -	03/2015	30(O) -	0/0
105	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
106	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	589.37	05/2013 06/2014	03/2015	22(O) 9(R)	0/5

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
107	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54(O) -	0/0
108	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	933.65	- -	08/2015	- -	0/12
109	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,728.25	04/2006 06/2012	06/2015	110(O) 36(R)	0/0
110	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,855.00	08/2010 03/2012	05/2015	57(O) 38(R)	0/10
111	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
112	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	287.14	05/2014 -	05/2015	12(O) -	0/9
113	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	3,068.29	12/2008 04/2013	05/2015	77(O) 25(R)	0/0
114	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
115	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 -	04/2015	0(O) -	0/0
116	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	248.72	12/2014 -	12/2014	0(O) -	0/8
117	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,015.77	01/2014 -	12/2015	23(O) -	0/9
118	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	10/2014	0(O) -	0/0
119	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,916.30	09/2011 05/2012	12/2014	39(O) 31(R)	6/76
120	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	07/2014	34(O) 28(R)	56/59
121	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	42.24	09/2017 -	09/2017	0(O) -	0/0
122	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	2.92	- -	-	-	0/0
123	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	178.68	10/2011 06/2014	08/2014	34(O) 2(R)	0/9
124	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	2,595.82	05/2015 -	05/2015	0(O) -	0/17
125	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	2.31	07/2016 -	07/2016	0(O) -	0/0
126	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	595.67	03/2015 -	03/2015	0(O) -	0/12
127	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	0.27	02/2016 -	02/2016	0(O) -	0/0
128	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016	0(O) -	0/0
129	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	2,563.75	12/2015 -	05/2016	5(O) -	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	94.80	03/2014 -	03/2015	12(O) -	0/5
131	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0
132	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	6.18	10/2010 -	12/2014	50(O) -	0/0
133	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	312.00	286.76	01/2012 -	07/2013	-	0/1
134	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,403.30	12/2012 -	-	-	0/14
135	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.26	139.50	03/2015 -	03/2015	0(O) -	0/64
136	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	20.79	01/2016 -	12/2015	-1(O) -	0/0
137	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	11/2012	666.00 701.00	701.00	245.50	11/2015 -	11/2015	0(O) -	18/29
138	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	138.83	06/2014 -	12/2014	6(O) -	0/0
139	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23(O) -	0/0
140	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	80.22	12/2014 -	12/2014	0(O) -	0/0
141	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 12,160.26	12,160.26	11,441.51	01/2012 -	09/2014	32(O) -	0/108
142	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
143	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	251.53	07/2015 -	12/2015	5(O) -	0/0
144	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	26,052.00	11/2012 11/2013	12/2014	25(O) 13(R)	72/100
145	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	994.83	09/2012 -	12/2015	39(O) -	6/7
146	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,738.16	02/2014 -	08/2014	6(O) -	0/0
147	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	257.90	04/2012 -	07/2014	27(O) -	0/0
148	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	33.26	07/2016 -	07/2016	0(O) -	0/5
149	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,200.35	05/2014 -	05/2015	12(O) -	0/5
150	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017	0(O) -	0/0
151	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	978.32	07/2012 -	10/2014	27(O) -	0/31
152	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	11/2015	11(O) -	0/0
153	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	686.58	85.47	04/2015 -	04/2015	0(O) -	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
154	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	599.48	12/2014 -	03/2015	3(O) -	0/0
155	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	-	02/2016 -	02/2016	0(O) -	0/0
156	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	193.65	11/2015 -	11/2015	0(O) -	0/0
157	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	1,913.10	9.50	05/2016 -	05/2016	0(O) -	0/0
158	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	589.19	11/2015 -	11/2015	0(O) -	13/25
159	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	648.92	04/2012 -	12/2013	-	0/0
160	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	864.97	10/2011 -	10/2015	48(O) -	0/0
161	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,255.25	01/2012 -	10/2015	45(O) -	0/0
162	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	971.42	10/2011 -	12/2014	38(O) -	0/0
163	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	- -	04/2015	- -	0/0
164	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	03/2015	31(O) -	0/5
165	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	17.48	03/2015 -	03/2015	0(O) -	0/5
166	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 462.79	462.79	85.74	10/2014 -	10/2015	12(O) -	0/0
167	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.56	03/2012 -	03/2015	36(O) -	13/20
168	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	536.65	12/2013 03/2014	09/2015	21(O) 18(R)	62/69
	Total		183,112.71 -	191,919.84	94,770.02				252/761
	POWER								
169	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,356.86	08/2012 -	08/2014	24(O) -	0/11
170	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	206.14	- 03/2015	-	-	5/17
171	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	03/2016	0(O) -	0/0
172	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	58.96	10/2014 -	10/2014	0(O) -	0/7
173	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	8,238.60	7,658.00	08/2013 -	03/2015	19(O) -	15/20
174	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	13,737.00	10,086.00	12/2009 -	03/2017	87(O) -	22/46

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
175	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,575.00	07/2011 -	08/2016	61(O) -	6/34
176	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	140.75	12/2015 -	12/2015	0(O) -	2/20
177	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,364.50	09/2014 -	03/2015	6(O) -	7/20
178	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	557.43	06/2015 -	06/2015	0(O) -	0/0
179	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	1,421.95	08/2014 -	09/2014	1(O) -	7/20
180	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.47	06/2014 -	06/2014	0(O) -	0/20
181	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
182	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	20.63	10/2014 -	10/2014	0(O) -	2/2
183	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	845.43	11/2012 -	12/2015	37(O) -	2/13
184	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	17.04	05/2016 -	04/2016	-1(O) -	0/0
185	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
186	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
187	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,460.45	05/2014 -	03/2015	10(O) -	2/8
188	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,254.00	09/2017 -	09/2017	0(O) -	11/39
189	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	669.00	08/2014 -	12/2014	4(O) -	1/15
190	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	-	07/2016 -	07/2016	0(O) -	0/0
191	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATTISGARH	08/2011	1,391.97 -	1,391.97	1,398.15	12/2013 -	08/2014	8(O) -	2/7
192	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	65.27	11/2016 -	03/2016	-8(O) -	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
193	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	1,007.16	941.81	12/2007 12/2009	-	-	2/11
194	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	2,496.90	2,991.34	12/2009 03/2017	03/2017	87(O) 0(R)	11/29
195	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 -	3,642.04	3,489.64	01/2016 -	11/2016	10(O) -	1/6
196	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	7,220.00	5,958.00	04/2009 -	05/2015	73(O) -	2/9
197	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	4,520.00	12/2016 -	12/2016	0(O) -	18/23
198	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,878.15	09/2008 -	03/2013	-	15/23
199	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,677.00	05/2017 -	05/2017	0(O) -	13/37
200	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	130.00	08/2017 -	08/2017	0(O) -	0/9
201	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	2,693.00	09/2016 -	09/2016	0(O) -	18/23
202	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	8,604.10	08/2013 -	06/2015	22(O) -	0/16
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	397.02	07/2013 -	03/2015	20(O) -	2/11
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	283.37	02/2012 -	03/2016	49(O) -	1/13
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	413.16	11/2011 -	-	-	2/14
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	-	06/2016 -	06/2016	0(O) -	0/0
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,047.82	04/2013 -	12/2014	20(O) -	0/11
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	358.12	11/2014 -	11/2014	0(O) -	2/12
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	38.79	03/2016 -	03/2016	0(O) -	0/0
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	310.29	03/2015 -	03/2015	0(O) -	4/15
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	120.22	04/2015 -	05/2015	1(O) -	0/16
213	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	667.64	11/2012 -	06/2014	19(O) -	0/11
214	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	3,919.59	4,534.79	09/2009 -	07/2018	106(O) -	2/12
215	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	573.99	876.27	08/2013 -	09/2014	13(O) -	21/37
216	RAMPUR HEP(412 MW) - [N18000024]SJVN,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	3,161.88	01/2012 -	-	-	19/28
217	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	2,715.00	11/2016 -	11/2016	0(O) -	16/19

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
218	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	09/2016 -	09/2016	0(O) -	0/0
219	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	0/0
220	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,877.35	09/2010 -	12/2018	99(O) -	0/0
221	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	2,129.61	08/2012 -	09/2014	25(O) -	1/5
222	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	333.88	06/2016 -	12/2015	-6(O) -	0/20
223	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	185.39	06/2012 -	09/2014	27(O) -	0/3
224	SYSTEM STRENGTHENING - XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	735.08	12/2014 -	11/2014	-1(O) -	2/2
225	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	133.04	03/2014 -	08/2014	5(O) -	3/7
226	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	451.33	08/2014 -	05/2015	9(O) -	2/18
227	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,001.99	08/2012 -	12/2014	28(O) -	0/11
228	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	-	08/2014 -	08/2016	24(O) -	0/0
229	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	798.03	02/2015 -	02/2015	0(O) -	1/14
230	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	694.18	11/2014 -	12/2014	1(O) -	0/16
231	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	728.92	01/2015 -	06/2015	5(O) -	4/19
232	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	230.77	08/2014 -	09/2014	1(O) -	7/20
233	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	293.42	06/2014 -	11/2014	5(O) -	8/20
234	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,146.00	03/2013 -	03/2017	48(O) -	0/14
235	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,061.38	1,513.20	09/2009 -	03/2016	78(O) -	1/5
236	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDC,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	735.81	07/2010 02/2016	02/2017	79(O) 12(R)	1/15
237	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	163.82	01/2014 -	09/2014	8(O) -	3/15
238	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,074.06	08/2014 -	06/2015	10(O) -	2/19

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
239	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,630.21	10/2014 -	06/2015	8(O) -	3/18
240	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,923.18	10/2012 -	12/2015	38(O) -	0/11
241	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	31(O) -	0/4
242	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	- -	-	-	0/0
243	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,777.00	12/2012 -	06/2015	30(O) -	0/11
244	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	-	- -	-	-	0/0
245	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	545.65	01/2015 -	12/2015	11(O) -	2/20
246	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,MULTI STATE	02/2012	324.33 -	324.33	188.96	08/2014 -	08/2014	0(O) -	9/20
247	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	-	10/2016 -	10/2016	0(O) -	0/0
248	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,196.87	10/2014 -	10/2014	0(O) -	3/16
249	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	76.40	05/2016 -	05/2016	0(O) -	0/0
250	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	418.10	02/2014 -	03/2015	13(O) -	5/17
251	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	-	10/2013 -	06/2014	8(O) -	2/8
252	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,030.76	12/2013 -	05/2014	-	4/13
253	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	296.91	11/2013 -	03/2015	16(O) -	7/20
254	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,568.64	03/2013 -	11/2014	20(O) -	5/15
255	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,463.37	03/2014 -	02/2015	11(O) -	5/15
256	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,197.40	12/2013 -	12/2014	12(O) -	2/8
257	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	68.90	01/2013 -	06/2015	29(O) -	5/18

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
258	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,243.16	11/2013 -	06/2015	19(O) -	5/16
259	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,219.87	11/2012 -	03/2015	28(O) -	0/13
260	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,881.83	07/2014 -	03/2015	8(O) -	3/14
261	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	623.44	777.57	07/2013 -	-	-	21/25
262	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	368.72 -	913.63	610.46	07/2006 12/2015	02/2015	103(O) -10(R)	2/13
263	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
264	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	1,056.00	08/2015 -	08/2015	0(O) -	17/18
265	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	488.66	07/2014 -	07/2018	48(O) -	1/1
266	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	490.59	09/2010 -	09/2014	48(O) -	0/5
267	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	2,127.69	06/2015 -	12/2015	6(O) -	3/27
	Total		231,756.78 -	246,995.55	135,672.22				372/1253
	RAILWAYS								
268	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTPT,TELANGANA	04/2012	632.68 -	816.55	17.54	04/2012 -	03/2016	47(O) -	0/0
269	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	184.06	2.99	- -	-	-	0/0
270	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	681.02	03/2014 -	03/2017	36(O) -	0/0
271	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
272	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	403.29	12/2009 03/2011	12/2014	60(O) 45(R)	0/0
273	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	2.00	- -	-	-	0/0
274	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	64.32	03/2013 -	03/2013	-	0/0
275	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	310.61	- -	-	-	0/0
276	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	20.99	- -	-	-	0/0
277	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
278	AKKANAPET-MEDAK - [N22000285]SCOR,TELANGANA	04/2012	153.00 -	153.00	-	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
279	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
280	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	485.00	417.14	03/2011 03/2011	03/2011	-	0/0
281	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
282	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	114.44	- -	-	-	0/0
283	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	87.44	- -	03/2017	-	0/0
284	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	725.00	573.95	06/1999 03/2011	03/2011	-	0/0
285	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.78	- -	-	-	0/0
286	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
287	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
288	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
289	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
290	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
291	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	52.07	- -	-	-	0/0
292	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	54.46	- -	-	-	0/0
293	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	8.23	- -	-	-	0/0
294	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	202.11	12/2012 -	12/2014	24(O) -	0/0
295	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	1,382.78	1.65	- -	-	-	0/0
296	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	1.76	- -	-	-	0/0
297	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	481.56	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
298	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,106.62	235.59	12/2010 03/2011	03/2011	-	0/0
299	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	11.83	- -	-	-	0/0
300	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
301	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.10	376.57	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
302	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	337.50	0.21	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
303	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	923.23	-	- -	-	-	0/0
304	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	858.67	0.73	- -	-	-	0/0
305	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
306	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	175.62	04/2014 -	03/2017	35(O) -	0/0
307	BHANUPALI-BILASPUK BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.79	- -	-	-	0/0
308	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.30	03/2011 -	-	-	0/0
309	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	80.74	- -	-	-	0/0
310	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69(O) -	0/0
311	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	484.61	2.17	03/2012 -	-	-	0/0
312	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
313	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.30	- -	-	-	0/0
314	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	267.37	34.08	- -	-	-	0/0
315	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,500.00 -	4,996.19	3,237.27	04/2008 03/2014	12/2017	116(O) 45(R)	0/0
316	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
317	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	59.57	03/2015 -	12/2016	21(O) -	0/0
318	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.17	- -	-	-	0/0
319	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	60.81	- -	-	-	0/0
320	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	568.50	- -	12/2014	- -	0/0
321	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0
322	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	462.24	- -	-	-	0/0
323	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.04	- -	-	-	0/0
324	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	494.92	3.62	- -	-	-	0/0
325	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	106.98	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
326	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
327	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
328	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.15	- -	-	-	0/0
329	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
330	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
331	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	88.29	- -	-	-	0/0
332	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	150.95	- -	-	-	0/0
333	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
334	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	1,242.25	972.61	03/2007 -	03/2017	120(O) -	0/0
335	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	267.98	- -	-	-	0/0
336	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
337	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	164.02	- -	-	-	0/0
338	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	533.38	110.73	12/2011 02/2012	02/2012	-	0/0
339	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	142.11	12/2012 -	-	-	0/0
340	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	388.67	92.56	12/2015 -	03/2016	3(O) -	0/0
341	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	406.92	152.23	- -	-	-	0/0
342	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	3.97	- -	-	-	0/0
343	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	205.00	5.20	- -	-	-	0/0
344	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	245.99	- -	03/2014	-	0/0
345	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	165.16	84.91	03/2015 -	03/2015	0(O) -	0/0
346	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
347	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	143.02	- -	-	-	0/0
348	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 607.09	607.09	549.05	12/2012 12/2012	02/2013	-	0/0

Sector Wise Details (June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
349	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	2.00	- -	-	-	0/0
350	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	2.43	02/2019 -	02/2019	0(O) -	0/0
351	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	651.17	7.22	- -	-	-	0/0
352	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
353	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	914.98	778.24	- -	12/2012	-	0/0
354	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	400.00	03/2016 -	03/2016	0(O) -	0/0
355	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	10/2014	31(O) 10(R)	0/0
356	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
357	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
358	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	227.22	12/2008 -	09/2014	69(O) -	0/0
359	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	272.47	06/2013 06/2013	03/2015	21(O) 21(R)	0/0
360	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
361	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240(O) -	0/0
362	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	0.31	- -	-	-	0/0
363	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	296.40	02/2011 02/2011	03/2013	-	0/0
364	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.92	- -	-	-	0/0
365	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
366	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	611.03	139.35	12/2011 11/2013	11/2013	-	0/0
367	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	261.70	146.24	02/2006 -	-	-	0/0
368	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	863.23 -	1,075.11	831.65	- -	03/2012	-	0/0
369	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
370	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	52.92	- -	-	-	0/0
371	GUDUR-DURGARA JAPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
372	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	468.11	- 05/2009	02/2015	- 69(R)	0/0
373	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	586.81	03/1994 -	09/2014	246(O) -	0/0
374	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	10.00	- -	-	-	0/0
375	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.92	02/2020 -	02/2020	0(O) -	0/0
376	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]JER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
377	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]JECR,BIHAR	04/2013	213.01 -	213.01	-	- -	-	-	0/0
378	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]JECR,BIHAR	04/2003	528.65 528.65	324.66	198.23	- -	-	-	0/0
379	HANSDIHA-GODDA NL - [N22000236]JER,MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
380	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]JER,MULTI STATE	04/2010	172.03 -	172.03	5.84	- -	-	-	0/0
381	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	319.13	- 09/2009	-	-	0/0
382	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	0.34	- -	-	-	0/0
383	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
384	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	884.92	- -	01/2013	-	0/0
385	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	159.02	- -	03/2014	-	0/0
386	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	64.98	03/2015 -	03/2015	0(O) -	0/0
387	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
388	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	47.50	- -	-	-	0/0
389	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]JER,MULTI STATE	04/2010	157.94 -	157.94	41.67	- -	-	-	0/0
390	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	445.40	180.42	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
391	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]JER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
392	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	108.42	- -	-	-	0/0
393	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	185.35	01/1999 -	-	-	0/0
394	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	653.46	241.37	03/2014 -	03/2014	-	0/0
395	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	141.28	- -	-	-	0/0

Sector Wise Details									
(June 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
396	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	839.47	06/2007 -	06/2007	-	0/0
397	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	1,043.56	738.56	03/2012 08/2012	-	-	0/0
398	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	14.00	- -	-	-	0/0
399	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	201.17	209.83	- -	-	-	0/0
400	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 238.56	740.00	562.57	03/2012 03/2012	12/2012	-	0/0
401	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	2,262.95	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
402	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	178.92	-	12/2014	-	0/0
403	KAKINADA-PITHAPURAM - [N22000314]SECR,ANDHRA PRADESH	03/1999	215.06 -	215.06	0.01	- -	-	-	0/0
404	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	205.13	- -	-	-	0/0
405	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	53.67	- -	-	-	0/0
406	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	3.71	- -	-	-	0/0
407	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,708.41	1,578.17	- -	03/2015	-	0/0
408	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
409	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	538.69	- -	03/2014	-	1/1
410	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	800.00	775.20	- -	10/2012	-	0/0
411	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	140.11	12/2012 -	03/2016	39(O) -	0/0
412	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	1,022.64	742.15	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
413	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	188.81	03/2017 -	03/2017	0(O) -	0/0
414	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	1,054.35	0.66	- -	-	-	0/0
415	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 162.87	162.87	129.14	- -	-	-	0/0
416	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	280.13	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
417	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 470.21	1,995.25	312.36	- -	12/2014	-	0/0
418	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	826.57	32.82	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
419	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	2.22	- -	03/2015	- -	0/0
420	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 768.87	768.87	553.53	- 03/2010	03/2010	-	0/0
421	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 2,957.21	2,957.21	1,805.36	07/2005 -	-	-	0/0
422	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	418.17	226.59	- -	-	-	0/0
423	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
424	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	341.41	296.34	03/2012 03/2013	03/2013	-	0/0
425	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	1,045.20	0.03	- -	-	-	0/0
426	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
427	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
428	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
429	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	406.99	141.31	- -	-	-	0/0
430	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	441.98	05/2008 03/2011	-	-	0/0
431	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	69.11	03/2014 -	03/2014	-	0/0
432	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	364.06	0.30	- -	-	-	0/0
433	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,185.44	4,277.33	03/2009 -	03/2017	96(O) -	0/0
434	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	0.92	07/2008 -	07/2008	-	0/0
435	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	14.22	- -	-	-	0/0
436	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.53	- -	-	-	0/0
437	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	119.45	- -	-	-	0/0
438	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	472.00	199.32	- -	02/2013	-	0/0
439	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 900.05	900.05	829.03	12/2011 12/2011	03/2013	-	0/0
440	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 671.82	791.59	1.49	- -	-	-	0/0
441	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.45	- -	03/2016	- -	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
442	MANSI-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	100.80	- -	-	-	0/0
443	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	477.88	456.82	03/2012 03/2013	03/2013	-	0/0
444	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
445	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	1.58	01/1999 -	-	-	0/0
446	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.65	- -	-	-	0/0
447	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	1,383.45	425.59	- -	-	-	0/0
448	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	0.91	- -	-	-	0/0
449	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
450	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	466.48	0.25	01/1999 -	-	-	0/0
451	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
452	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	-	- -	-	-	0/0
453	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
454	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	390.60	2.11	- -	-	-	0/0
455	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,708.74	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
456	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	286.45	- -	12/2014	-	0/0
457	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	645.00	286.45	- -	-	-	0/0
458	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	545.64	0.54	- -	-	-	0/0
459	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
460	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	0.02	- -	-	-	0/0
461	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	169.82	24.33	- -	-	-	0/0
462	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	1.13	- -	-	-	0/0
463	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	883.00	696.74	02/2009 -	03/2012	-	0/0
464	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	1,036.78	393.57	07/2012 -	-	-	0/0
465	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
466	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
467	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	532.87	49.21	- -	-	-	0/0
468	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	189.84	- -	03/2018	- -	0/0
469	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	242.22	37.02	- -	-	-	0/0
470	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	4,083.02	4.37	- -	-	-	0/0
471	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	229.26	- -	03/2015	- -	0/0
472	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	03/2016	- -	0/0
473	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	221.42	21.13	- -	-	-	0/0
474	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.18	254.77	- -	03/2015	- -	0/0
475	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
476	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	46.37	- -	03/2017	- -	0/0
477	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	18.71	- -	03/2017	- -	0/0
478	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	1,418.21	1,039.97	- -	-	-	0/0
479	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	9.23	03/2015 -	03/2017	24(O) -	0/0
480	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,582.40	12/2008 -	03/2017	99(O) -	0/0
481	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	66.46	03/2014 -	03/2016	24(O) -	0/0
482	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.51	441.33	03/2016 -	03/2016	0(O) -	0/0
483	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	94.53	03/2016 -	06/2016	3(O) -	0/0
484	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	439.52	03/2016 -	03/2016	0(O) -	0/0
485	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,117.11	430.50	03/2008 06/2008	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
486	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
487	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 293.74	293.74	139.18	12/2010 12/2010	12/2010	-	0/0
488	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	260.16	225.58	- -	05/2014	-	0/0
489	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	2,169.50	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
490	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 495.68	925.30	688.95	- -	02/2014	-	0/0
491	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	203.00	200.37	- -	03/2014	-	0/0
492	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	261.38	17.75	- -	-	-	0/0
493	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
494	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	248.07	18.72	03/2015 -	03/2015	0(O) -	0/0
495	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
496	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
497	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
498	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
499	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	1,122.00	843.56	- -	03/2013	-	0/6
500	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	289.93	280.67	12/2007 03/2010	-	-	0/0
501	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,383.02	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
502	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	308.27	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
503	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	913.48	459.31	- -	-	-	0/0
504	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	609.61	03/2013 -	03/2014	-	0/0
505	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	240.22	- -	-	-	0/0
506	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.40	381.74	06/2004 -	06/2015	132(O) -	0/0
507	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 915.70	3,019.17	2,843.22	- -	03/2015	- -	0/0
508	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.12	- -	-	-	0/0
509	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	788.72	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
510	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	28.54	- -	-	-	0/0
511	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	387.37	03/2012 -	-	-	0/0
512	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	285.67	-	-	-	0/0
513	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	755.54	2.89	- -	-	-	0/0
514	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	32.81	- 12/2017	12/2017	- 0(R)	0/0
515	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	21.45	- -	-	-	0/0
516	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	246.91	- -	-	-	0/0
517	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	345.69	- -	-	-	0/0
518	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	230.97	03/2010 -	-	-	0/0
519	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	14.00	- -	-	-	0/0
520	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	14.73	- -	-	-	0/0
521	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
522	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	86.75	12/2015	03/2017	15(O) -	0/0
523	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.58	- -	-	-	0/0
524	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.47	- -	-	-	0/0
525	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.81	- -	-	-	0/0
526	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	61.56	- -	-	-	0/0
527	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	-	-	0/0
528	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.15	- -	-	-	0/0
529	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	128.17	02/2015 -	02/2015	0(O) -	0/0
530	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.57	- -	-	-	0/0
531	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	502.17	03/2014 -	03/2014	-	0/0
532	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	810.78	134.62	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
533	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	460.73	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
534	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	171.02	148.69	06/2013 -	12/2014	18(O) -	0/0
535	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17 -	365.17	1.30	- -	-	-	0/0
536	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,188.91	678.79	- 12/2009	02/2012	-	0/0
537	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	236.93	-	- -	-	-	0/0
538	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU	09/2006	456.00 456.00	820.00	193.26	- -	-	-	0/0
539	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	125.00 125.00	420.00	61.41	- -	-	-	0/0
540	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	167.73	96.40	03/2012 -	-	-	0/0
541	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU	09/1995	100.00 100.00	900.00	581.28	- -	-	-	0/0
542	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	3,176.10	3,499.66	12/2006 08/2010	08/2010	-	0/0
543	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	167.50	0.15	- -	-	-	0/0
544	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	913.00 -	1,801.01	0.70	- -	-	-	0/0
545	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181(O) -	0/0
546	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	1,389.62	872.89	03/2014 -	03/2014	-	0/0
547	UNCHAHAH-AMETHI - [N22000294]NR, UTTAR PRADESH	04/2012	380.00 -	380.00	1.29	- -	-	-	0/0
548	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,116.53	309.20	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
549	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	- -	-	-	0/0
550	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR, MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
551	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	548.01	200.94	- 03/2010	-	-	0/0
552	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	685.17	120.40	- -	-	-	0/0
553	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	279.40	205.88	- -	04/2014	-	0/0
554	WARDHA-NANDED MAHARASHTRA - [N22000231]CR, MAHARASHTRA	04/2008	499.30 -	2,501.05	71.25	- -	-	-	0/0
555	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	297.85 -	297.85	5.67	- -	-	-	0/0
556	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
557	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		162,933.96 -	274,846.09	84,181.60				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
558	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	356.80	08/2013 -	02/2015	18(O) -	0/0
559	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
560	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	360.60	10/2014 -	10/2014	0(O) -	0/0
561	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	263.80	07/2014 -	07/2014	0(O) -	0/0
562	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.40	05/2013 -	05/2013	-	0/0
563	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	09/2014	10(O) -	0/0
564	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	436.30	04/2014 -	09/2014	5(O) -	0/0
565	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,440.00	10/2014 -	10/2014	0(O) -	0/0
566	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	52.72	07/2014 -	07/2014	0(O) -	0/0
567	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	137.70	01/2014 -	12/2015	23(O) -	0/0
568	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
569	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	742.80	02/2014 -	02/2014	-	0/0
570	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	329.50	04/2014 -	03/2015	11(O) -	0/0
571	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	170.80	05/2014 -	05/2014	-	0/0
572	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	708.20	09/2014 -	03/2015	6(O) -	0/3
573	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,662.00	08/2014 -	07/2015	11(O) -	0/0
574	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,380.00	06/2013 -	06/2013	-	0/3
575	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	12/2016	39(O) -	0/0
576	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	934.80	08/2013 -	08/2013	-	0/3
577	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
578	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	459.10	02/2014 -	09/2015	19(O) -	0/0

Sector Wise Details									
(June 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
579	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,560.00	08/2013 -	12/2014	16(O) -	0/0
580	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,717.00	08/2013 -	06/2015	22(O) -	0/0
581	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	365.20	08/2013 -	12/2015	28(O) -	0/0
582	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	192.10	10/2015 -	10/2015	0(O) -	0/0
583	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.70	07/2013 -	03/2015	20(O) -	0/0
584	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,709.00	09/2014 -	09/2014	0(O) -	0/0
585	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	286.70	09/2007 07/2011	06/2015	93(O) 47(R)	0/0
586	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	115.90	12/2015 -	12/2015	0(O) -	0/3
587	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,190.00	11/2012 -	08/2014	21(O) -	0/0
588	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
589	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	377.70	09/2013 -	12/2015	27(O) -	0/0
590	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12(O) -	0/0
591	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,147.00	06/2014 -	08/2014	2(O) -	0/0
592	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	656.90	-	07/2014	-	2/2
593	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	65.35	01/2013 -	12/2015	35(O) -	0/0
594	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19(O) -	0/0
595	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	310.70	06/2008 -	03/2015	81(O) -	0/0
596	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	267.10	06/2008 -	03/2015	81(O) -	0/0
597	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.40	06/2005 -	06/2015	120(O) -	0/0
598	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	217.61	444.00	04/2010 01/2016	03/2015	59(O) -10(R)	0/0
599	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	06/2016	76(O) -	0/0
600	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	888.40	03/2013 -	12/2014	21(O) -	0/0
601	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38(O) -	0/0
602	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0
603	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19(O) -	0/0
604	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
605	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	512.70	04/2015 -	04/2015	0(O) -	0/0
606	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	664.90	05/2010 -	12/2014	55(O) -	0/0
607	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	743.10	07/2013 -	08/2014	13(O) -	0/0
608	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	07/2014	13(O) -	0/0
609	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	779.70	- -	05/2013	-	1/1
610	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	268.70	06/2008 -	06/2014	72(O) -	0/0
611	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.40	05/2008 01/2015	10/2014	77(O) -3(R)	0/0
612	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	309.10	09/2010 -	08/2014	47(O) -	0/0
613	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	844.60	09/2015 -	09/2015	0(O) -	0/0
614	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	519.50	09/2008 -	12/2014	75(O) -	0/0
615	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	272.10	11/2016 -	11/2016	0(O) -	0/0
616	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	506.20	08/2015 -	08/2015	0(O) -	0/0
617	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	603.80	10/2013 -	11/2015	25(O) -	0/0
618	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	186.00	09/2008 -	12/2014	75(O) -	0/0
619	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	2,034.00	08/2013 06/2014	09/2014	13(O) 3(R)	0/0
620	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,492.00	09/2012 -	12/2014	27(O) -	2/3
621	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	327.40	04/2008 01/2015	10/2014	78(O) -3(R)	0/0
622	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	273.00	04/2008 01/2015	12/2014	80(O) -1(R)	0/0
623	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72(O) -	0/0
624	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	280.00	357.00	02/2009 -	12/2014	70(O) -	0/0
625	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	238.30	07/2009 -	12/2014	65(O) -	0/0
626	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	125.00	09/2007 -	03/2015	90(O) -	0/0
627	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	316.60	10/2013 -	12/2015	26(O) -	0/0
628	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	01/2013	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
629	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
630	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	605.90	05/2013 -	12/2015	31(O) -	0/0
631	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20(O) -	0/0
632	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	695.40	02/2013 -	02/2013	-	0/0
633	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,982.00	12/2012 -	12/2012	-	0/0
634	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,141.00	07/2013 -	12/2014	17(O) -	0/0
635	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	664.90	01/2014 -	12/2014	11(O) -	0/0
636	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	891.70	07/2013 -	11/2014	16(O) -	0/0
637	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	07/2014	26(O) -	0/0
638	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	284.90	10/2008 -	09/2014	71(O) -	0/0
639	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	682.00	07/2014 -	12/2015	17(O) -	0/0
640	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,190.00	- -	06/2015	-	2/3
641	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	587.30	07/2012 -	07/2014	24(O) -	0/0
642	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	280.13	168.30	11/2008 12/2014	09/2014	70(O) -3(R)	0/0
643	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	134.10	04/2009 12/2014	03/2015	71(O) 3(R)	0/0
644	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 167.64	167.64	121.30	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
645	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 200.00	200.00	198.40	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
646	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,270.00	06/2013 -	03/2015	21(O) -	0/0
647	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	590.40	03/2013 -	12/2015	33(O) -	0/0
648	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	311.80	06/2008 -	06/2014	72(O) -	0/0
649	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	284.80	10/2014 -	10/2014	0(O) -	0/0
650	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	325.40	04/2008 01/2015	12/2014	80(O) -1(R)	0/0
651	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	275.80	06/2008 09/2014	09/2014	75(O) 0(R)	0/0
652	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
653	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	540.60	06/2015 -	05/2016	11(O) -	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
654	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	551.30	09/2013 -	09/2013	-	0/0
655	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,121.00	02/2010 -	12/2014	58(O) -	0/0
656	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O) -	0/0
657	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	717.30	09/2014 -	10/2015	13(O) -	0/0
658	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40(O) -	0/0
659	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	0(O) -	0/0
660	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.00	06/2014 -	12/2015	18(O) -	0/0
661	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	920.80	03/2014 -	08/2014	5(O) -	0/0
662	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	12/2014	22(O) -	0/0
663	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,341.00	07/2012 -	07/2012	-	0/0
664	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,207.00	03/2013 -	12/2014	21(O) -	0/0
665	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	474.20	01/2014 -	08/2014	7(O) -	0/0
666	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	03/2012	-	0/0
667	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,136.00	07/2015 -	06/2016	11(O) -	0/0
668	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	376.40	10/2008 -	12/2014	74(O) -	0/0
669	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	341.60	06/2015 -	06/2015	0(O) -	0/0
670	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	268.10	09/2014 -	09/2014	0(O) -	0/0
671	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,162.00	11/2013 -	11/2013	-	0/0
672	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	823.90	03/2013 -	12/2014	21(O) -	0/0
673	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	963.50	05/2014 -	09/2014	4(O) -	0/0
674	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	262.30	09/2007 03/2014	12/2014	87(O) 9(R)	0/0
675	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
676	SIX LANEING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	281.40	06/2014 -	12/2014	6(O) -	0/0
677	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	09/2014	9(O) -	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
678	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,284.00	12/2013 -	09/2014	9(O) -	0/0
679	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.00	05/2014 -	05/2015	12(O) -	0/0
680	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.00	08/2012 -	03/2016	43(O) -	0/0
681	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	09/2014	78(O) -4(R)	0/0
682	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	12/2014	6(O) -	0/0
683	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40(O) -	2/2
684	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,376.00	11/2013 -	11/2013	-	0/0
685	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11(O) -	0/0
686	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	146.50	05/2013 -	12/2014	19(O) -	0/0
687	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	383.20	-	07/2014	-	2/2
688	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,056.00	03/2014 -	12/2015	21(O) -	0/0
689	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	-	-	-	0/0
690	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	63.89	11/2012 -	12/2014	25(O) -	0/0
691	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015	0(O) -	0/0
692	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	-	-	-	0/0
693	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		102,321.44 -	104,296.49	91,608.16				14/28
	<u>SHIPPING AND PORTS</u>								
694	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	211.30	04/2011 11/2011	11/2011	-	0/0
695	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
696	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	47.32	01/2013 06/2013	06/2013	-	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
697	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
698	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	81.40	12/2011 10/2012	10/2012	-	0/0
699	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 04/2014	04/2014	-	0/0
700	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0
701	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,005.88	12/2010 09/2012	10/2015	58(O) 37(R)	0/0
702	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
703	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
704	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
705	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
706	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99(O) 0(R)	0/0
707	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
708	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
709	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
710	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
711	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0
712	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	18,600.58	8,395.88				0/1
	<u>TELECOMMUNICATIONS</u>								
713	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	09/2014	68(O) -	0/0
714	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 01/2015	01/2015	51(O) 0(R)	0/0

Sector Wise Details

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
715	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	930.60	828.48	11/2010 12/2012	09/2013	-	0/0
716	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	336.84	-	10/2009 -	-	-	0/0
717	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	85.96	06/2009 -	09/2014	63(O) -	0/0
718	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
719	GSM EQUIPMENT OF 4,50,000 LINES (2G) HARYANA (PHASE V.2) TELECOM CIRCLE - [N26000080]BSNL,HARYANA	09/2008	216.54 -	216.54	-	09/2009 -	-	-	0/0
720	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
721	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEPON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
722	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
723	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	37(O) -	0/0
	Total		5,295.83 -	5,199.48	1,770.48				0/0
	<u>URBAN DEVELOPMENT</u>								
724	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
725	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
726	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
727	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016	0(O) -	0/0
728	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8(O) -	0/0
	Total		73,993.32 -	79,266.22	11,652.27				3/3
	<u>WATER RESOURCES</u>								
729	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		935,003.47	1,108,382.70	546,208.61				1163/3487

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

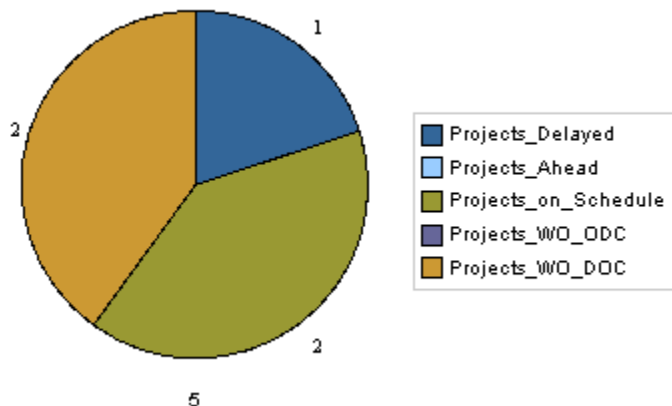

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 73993.32 crore but this was subsequently revised to Rs. 79266.22 crore implying a cost overrun of 7.1%. The expenditure incurred on these projects till June, 2014 is Rs. 11652.27 crore, which is 14.7% of the revised cost of the projects.

Figures are in Rs. Crore

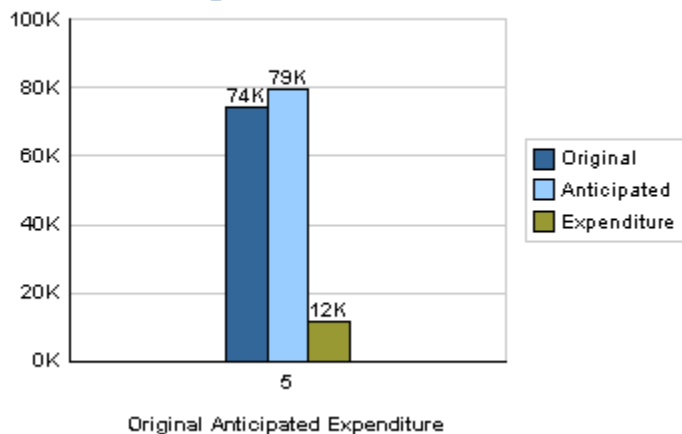

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	11
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 11 projects, 4 projects are delayed .7 projects do not have fixed dates of commissioning.

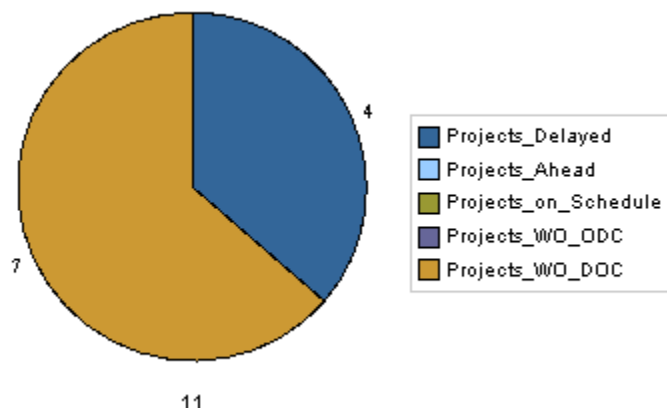

Investment Scenario

Total original cost of implementation of 11 projects when sanctioned, was of the order of Rs. 5295.83 crore but this was subsequently revised to Rs. 5199.48 crore implying a cost overrun of -1.8%. The expenditure incurred on these projects till June, 2014 is Rs. 1770.48 crore, which is 34.1% of the revised cost of the projects.

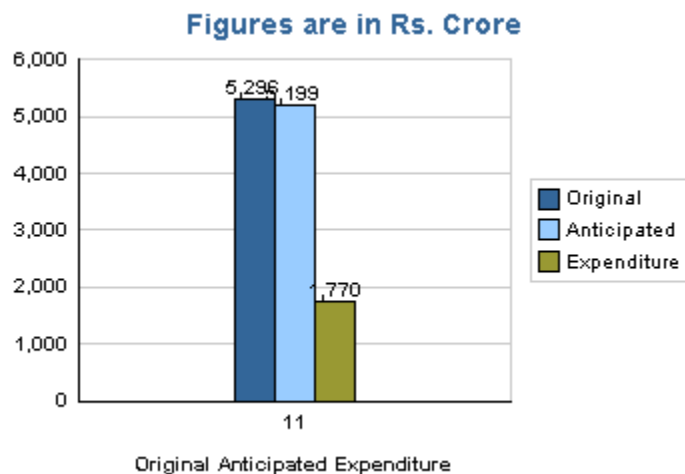

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects **19**

Number of Projects Delayed **3**

Number of Projects Without Date Of Commissioning **16**


Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 3 projects are delayed .16 projects do not have fixed dates of commissioning.

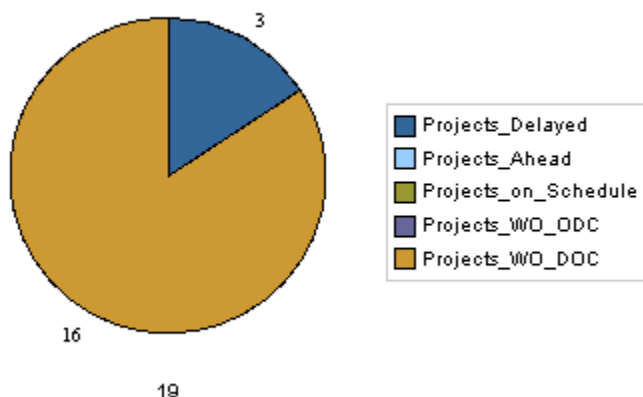

Investment Scenario

Total original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 18600.58 crore implying a cost overrun of 19.1%. The expenditure incurred on these projects till June, 2014 is Rs. 8395.88 crore, which is 45.1% of the revised cost of the projects.

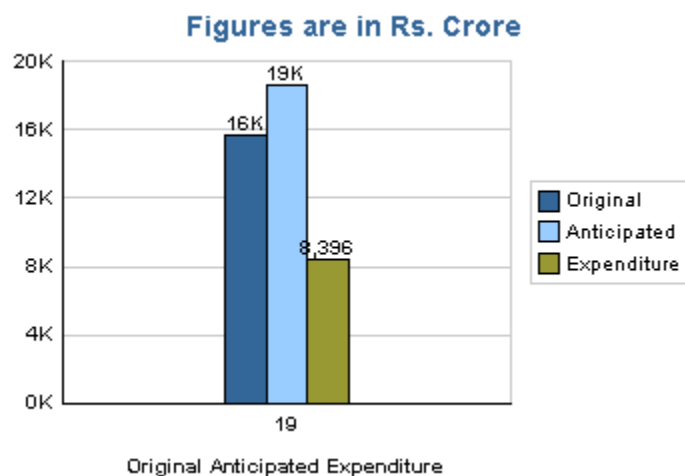

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHW


Current Status:

Number of Projects	136
Number of Projects On Schedule	17
Number of Projects Delayed	92

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	24


Brief Analysis

Project Status with respect to Original Schedule: Out of 136 projects, 17 projects are on schedule and 92 projects are delayed .24 projects do not have fixed dates of commissioning.3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

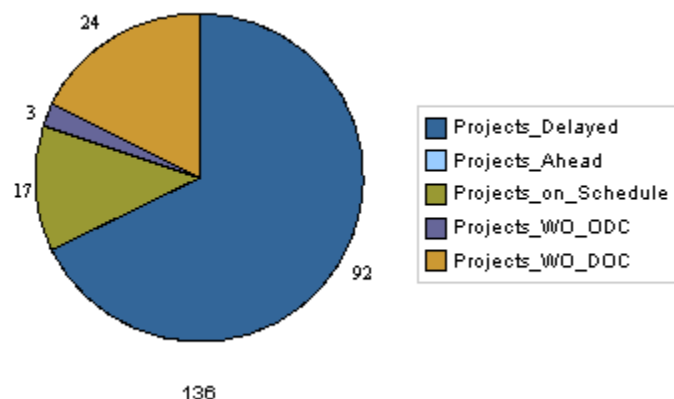

Investment Scenario

Total original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 102321.44 crore but this was subsequently revised to Rs. 104296.49 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till June, 2014 is Rs. 91608.16 crore, which is 87.8% of the revised cost of the projects.

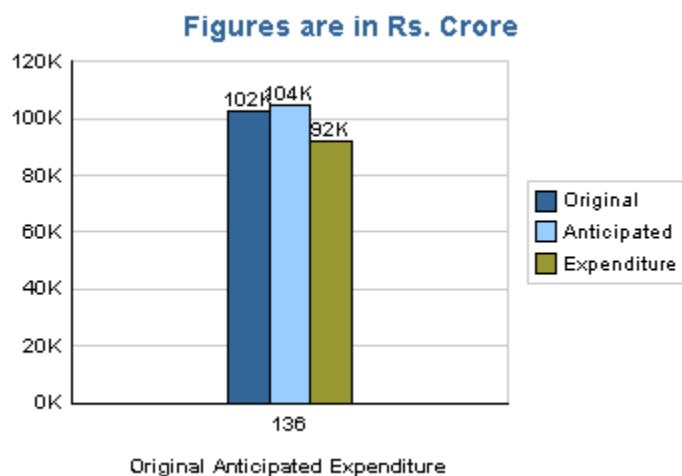

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	290
Number of Projects On Schedule	11
Number of Projects Delayed	37

Number of Projects Without Original Date of Commissioning	17
Number of Projects Without Date Of Commissioning	225

Brief Analysis


Project Status with respect to Original Schedule: Out of 290 projects, 11 projects are on schedule and 37 projects are delayed .225 projects do not have fixed dates of commissioning.17 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

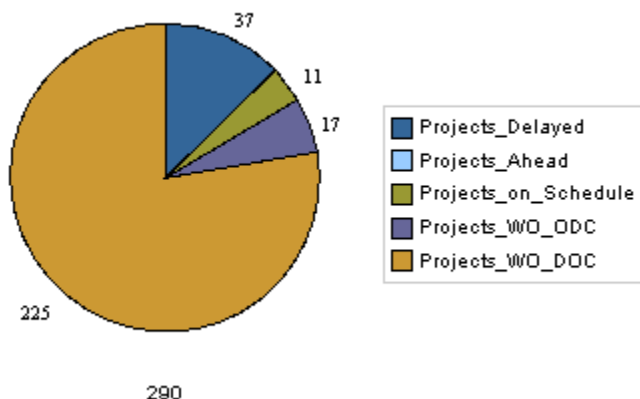

Investment Scenario

Total original cost of implementation of 290 projects when sanctioned, was of the order of Rs. 162933.96 crore but this was subsequently revised to Rs. 274846.09 crore implying a cost overrun of 68.7%. The expenditure incurred on these projects till June, 2014 is Rs. 84181.6 crore, which is 30.6% of the revised cost of the projects.

Figures are in Rs. Crore

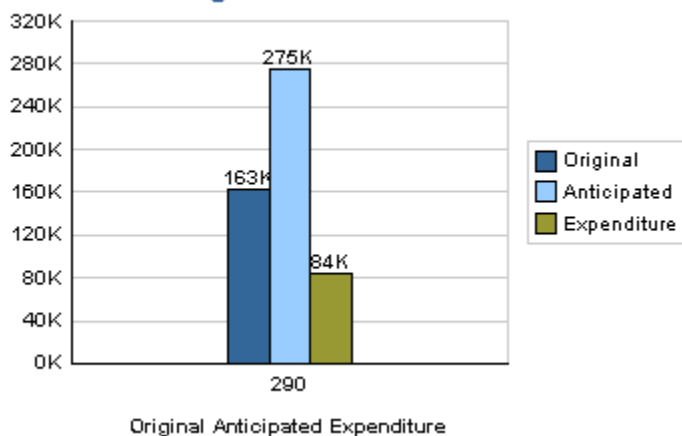

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	99
Number of Projects On Schedule	30
Number of Projects Delayed	56
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8

Brief Analysis


Project Status with respect to Original Schedule: Out of 99 projects, 4 projects are ahead of schedule, 30 projects are on schedule and 56 projects are delayed .8 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

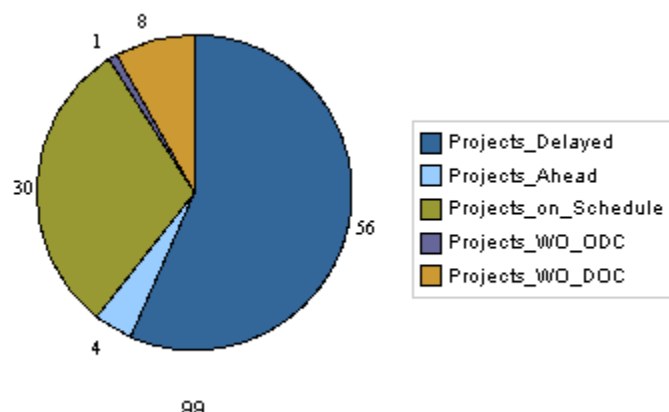

Investment Scenario

Total original cost of implementation of 99 projects when sanctioned, was of the order of Rs. 231756.78 crore but this was subsequently revised to Rs. 246995.55 crore implying a cost overrun of 6.6%. The expenditure incurred on these projects till June, 2014 is Rs. 135672.22 crore, which is 54.9% of the revised cost of the projects.

Figures are in Rs. Crore

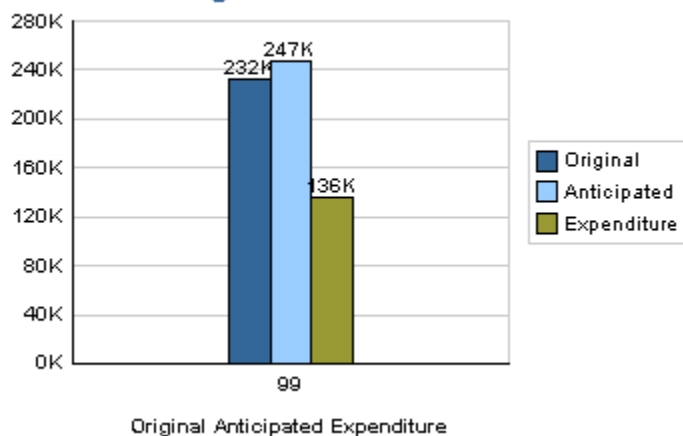

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	76
Number of Projects On Schedule	22
Number of Projects Delayed	45
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 76 projects, 1 project are ahead of schedule, 22 projects are on schedule and 45 projects are delayed .6 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

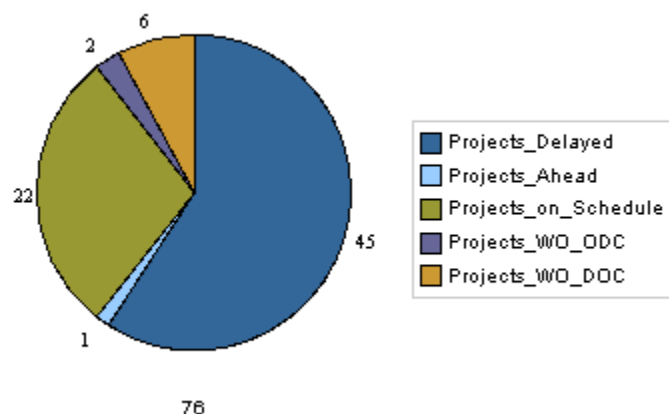

Investment Scenario

Total original cost of implementation of 76 projects when sanctioned, was of the order of Rs. 183112.71 crore but this was subsequently revised to Rs. 191919.84 crore implying a cost overrun of 4.8%. The expenditure incurred on these projects till June, 2014 is Rs. 94770.02 crore, which is 49.4% of the revised cost of the projects.

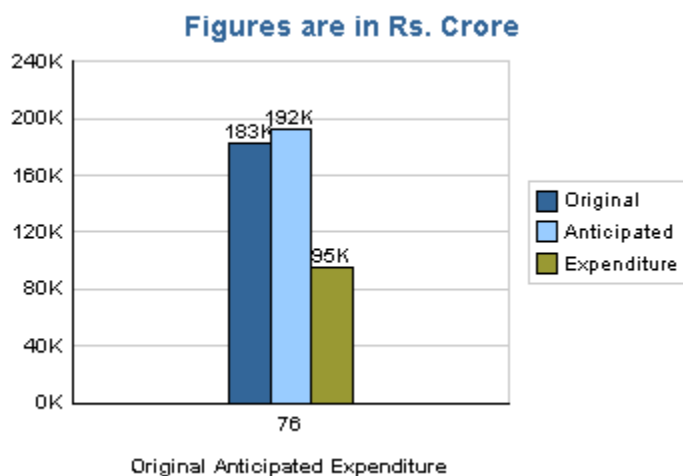

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	20
Number of Projects On Schedule	3
Number of Projects Delayed	15

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 3 projects are on schedule and 15 projects are delayed .2 projects do not have fixed dates of commissioning.

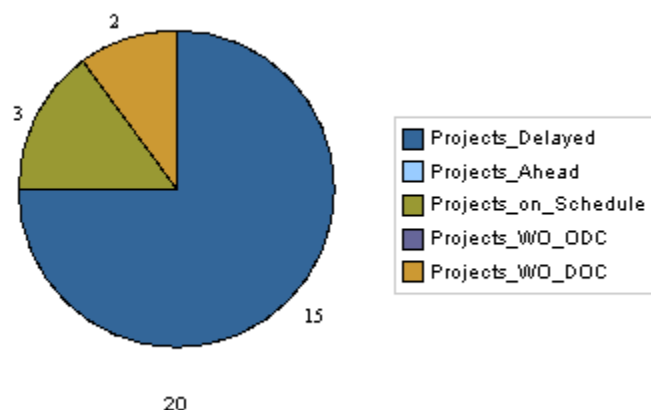

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 65959.26 crore but this was subsequently revised to Rs. 72144.44 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till June, 2014 is Rs. 60649.78 crore, which is 84.1% of the revised cost of the projects.

Figures are in Rs. Crore

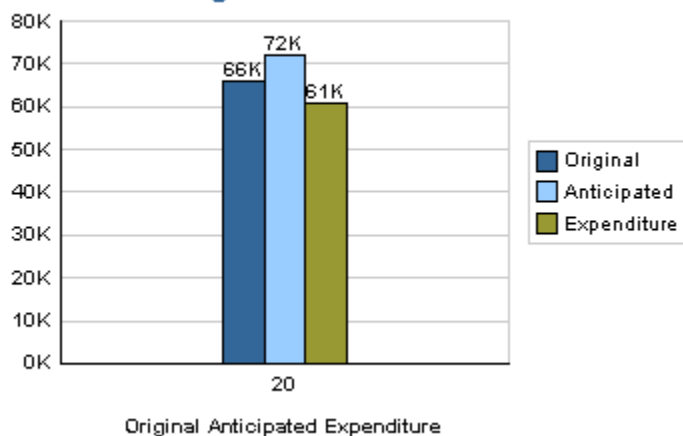

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	59
Number of Projects On Schedule	24
Number of Projects Delayed	31

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 59 projects, 24 projects are on schedule and 31 projects are delayed .4 projects do not have fixed dates of commissioning.

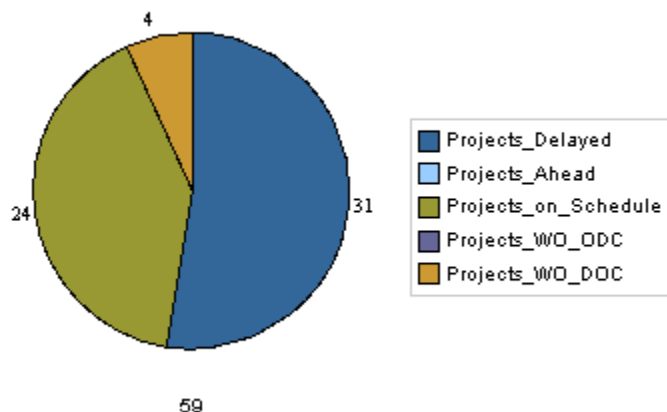

Investment Scenario

Total original cost of implementation of 59 projects when sanctioned, was of the order of Rs. 41532.08 crore but this was subsequently revised to Rs. 51354.22 crore implying a cost overrun of 23.6%. The expenditure incurred on these projects till June, 2014 is Rs. 18493.21 crore, which is 36% of the revised cost of the projects.

Figures are in Rs. Crore

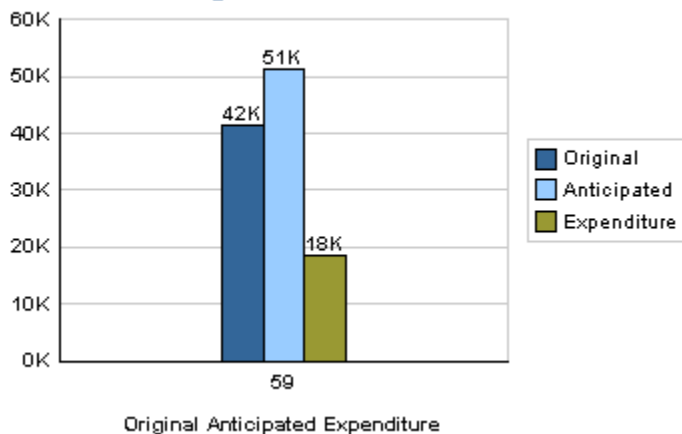

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	8
Number of Projects On Schedule	1
Number of Projects Delayed	2
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 1 project are ahead of schedule, 1 project are on schedule and 2 projects are delayed .4 projects do not have fixed dates of commissioning.

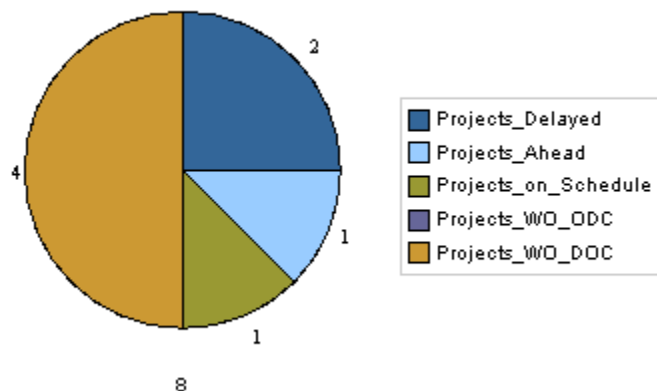

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6926.79 crore implying a cost overrun of 14.8%. The expenditure incurred on these projects till June, 2014 is Rs. 5823.27 crore, which is 84.1% of the revised cost of the projects.

Figures are in Rs. Crore

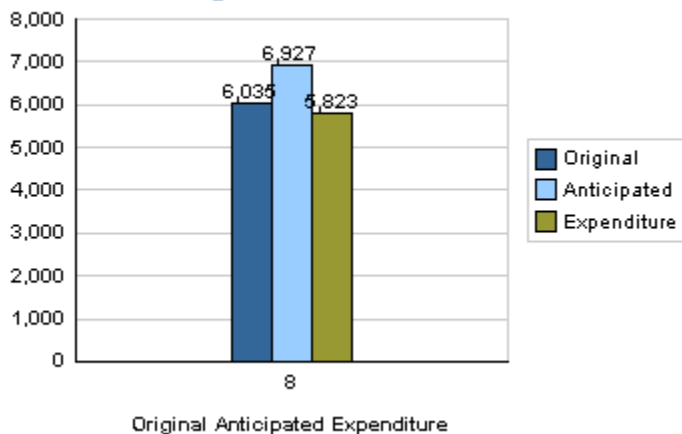

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

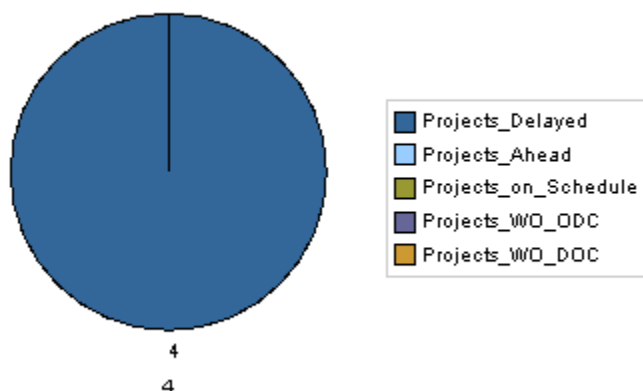

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till June, 2014 is Rs. 25376.17 crore, which is 54.3% of the revised cost of the projects.

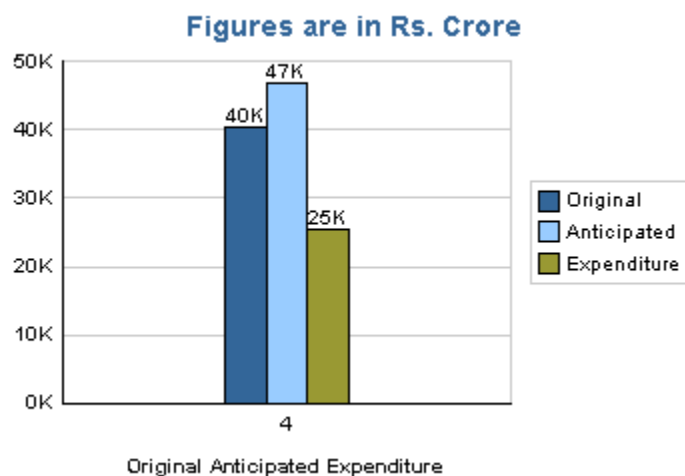

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDHRA PRADESH	22	24,560.99	29,968.77	20,353.28
2	ARUNACHAL PRADESH	3	9,356.22	9,356.22	10,744.96
3	ASSAM	38	24,556.86	38,943.74	31,368.1
4	BIHAR	46	33,802.78	46,815.8	32,917.64
5	CHANDIGARH	1	452	452	264.84
6	CHHATISGARH	24	57,805.7	65,314.32	28,033.26
7	DELHI	4	41,531.33	41,531.33	9,438.4
8	GOA	1	335.61	388.53	280.74
9	GUJARAT	32	38,022.88	38,935.23	13,217.42
10	HARYANA	10	4,757.42	6,907.4	7,266.07
11	HIMACHAL PRADESH	5	13,457.44	18,070.4	13,967.56
12	JAMMU AND KASHMIR	6	11,799.13	30,702.5	15,366.54
13	JHARKHAND	29	21,317.05	21,927.46	11,711.32
14	KARNATAKA	34	78,767.44	92,965.75	28,864.8
15	KERALA	12	22,610.65	25,135.43	10,017.66
16	MADHYA PRADESH	18	24,606.22	26,088.81	8,445.29
17	MAHARASHTRA	46	73,310.22	85,861.64	38,050.74
18	MANIPUR	1	727.56	5,996	2,262.95
19	MEGHALAYA	3	4,845.02	4,845.02	951.57
20	MIZORAM	2	988.06	3,307.11	786.08
21	MULTI STATE	187	2,04,107.77	2,25,495.41	95,604.71
22	NAGALAND	2	5,124	6,720.57	9.23
23	ODISHA	34	61,113.78	68,005.65	47,057.98
24	PUNJAB	4	1,680.2	1,653.16	2,519.92
25	RAJASTHAN	25	25,638.72	25,695.93	13,224.85
26	SIKKIM	2	1,648.94	3,684.88	364.56
27	TAMIL NADU	40	54,818.67	71,711.37	47,311.32
28	TELANGANA	22	9,563.31	12,332.13	3,244.14
29	TRIPURA	6	2,966.26	4,409.22	2,847.41
30	UTTAR PRADESH	26	14,361.52	17,036.56	11,397.03
31	UTTARAKHAND	7	9,501.04	13,063.93	3,903.37
32	WEST BENGAL	38	57,186.32	65,301.38	34,517.67
TOTAL		729	9,35,321.11	11,08,623.65	5,46,311.41

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	17,702
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	4,564.17
3	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,534.79
4	KOLDAM HEP (NTPC)	POWER	10/2002	4,527.15	-	5,958
5	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,877.35
6	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	2,991.34
7	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	10,086
8	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,513.2
9	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	POWER	03/2005	596.45	-	941.81
10	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	200.94
11	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	688.95
12	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	2500	8,805
13	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
14	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	884.92

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	155	775.2
16	NANDYAL-YERRAGUNTLA(NL), SCR	RAILWAYS	03/1996	155.74	429.49	696.74
17	KANPUR-KASGANJ-MATHURA(GC), NER	RAILWAYS	03/1997	677.97	1062.36	1,578.17
18	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,500	-	3,237.27
19	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	194.07	381.74
20	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	441.98
21	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	233	501.69	738.56
22	KATIHAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	742.15
23	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	468.11
24	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	RAILWAYS	03/2002	625.3	408.76	839.47
25	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	100	581.28
26	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	843.56
27	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,582.4
28	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3156.32	3,499.66

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	296.4
30	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	238.56	562.57
31	HARIDASPUR-PARADEEP(NL)	RAILWAYS	04/1996	301.64	-	319.13
32	RAJATGARH-BARANG(LD), ECOR	RAILWAYS	04/1999	166.16	-	308.27
33	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.53	2,262.95
34	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	2,843.22
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	280.13
36	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	280.67
37	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	262.3
38	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	186
39	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	243.4
40	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	267.1
41	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	310.7
42	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	519.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	284.9
44	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	376.4
45	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	CIVIL AVIATION	08/2008	1,942.51	2325	2,573.92
46	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	1,248.89
47	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	16,000.18
48	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,855
49	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	PETROLEUM	07/2009	238.68	-	286.76
50	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	7,780.06
51	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	PETROLEUM	08/2009	246.81	-	257.9
52	RAMPUR HEP(412 MW)	POWER	01/2007	2,047.03	-	3,161.88
53	KISHANGANGA HEP	POWER	07/2007	2,238.67	-	3,489.64
54	WESTERN REGION STRENGTHENING SCHEME-V	POWER	12/2007	477.69	-	490.59
55	BONGAIGAON THERMAL POWER PROJECT	POWER	01/2008	4,375.35	-	4,575
56	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	-	876.27

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	7,658
58	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	-	777.57
59	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	POWER	08/2011	1,391.97	-	1,398.15
60	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	POWER	01/2011	368.72	-	610.46
61	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	PETROLEUM	08/2008	144.02	-	151.39
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	114.01	332.92	456.82
63	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	798.47
64	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	404.19	425.59
65	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	343.17	778.24
66	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	170	417.14
67	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	609.61
68	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.3
69	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	1676.31	4,277.33
70	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	459.31

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.65
72	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	788.72
73	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	246.91
74	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	267.98
75	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	462.24
76	NEW BG LINE FROM DUDHNOI-MENDIPATAR	RAILWAYS	04/1999	175.43	-	229.26
77	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	972.61
78	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	568.5
79	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	1,039.97
80	PANVEL PEN DOUBLING	RAILWAYS	04/2006	191	-	225.58
81	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	286.45
82	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2
83	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	209.83
84	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	273
86	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	311.8
87	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
88	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	327.4
89	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	275.8
90	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	325.4
91	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	211.4
92	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	268.7
93	BRAHMPUTRA BRIDGE, NH NO-31	ROAD TRANSPORT AND HIGHWAYS	12/2003	217.61	309.56	444
94	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,121
95	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	309.1
96	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	664.9
97	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,341
98	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,492

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826
100	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,128
101	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
102	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
103	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
104	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
105	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,982
106	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,376
107	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
108	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
109	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	888.4
110	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,190
111	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,190
112	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	743.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
114	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	779.7
115	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,270
116	4 LANING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,662
117	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	656.9
118	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	605.9
119	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.4
120	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,380
121	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	934.8
122	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,162
123	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	1141	2,034
124	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,284
125	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	823.9
126	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	664.9

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
128	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	742.8
129	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	920.8
130	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	824.7
131	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
132	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	459.1
133	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	622.1
134	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	963.5
135	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	695.4
136	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,717
137	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,560
138	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,709
139	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	360.6
140	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

List of Projects Without Original Date of Commissioning

(June 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL, MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	-	04/2015	-	0/0
2	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	933.65	-	08/2015	-	0/12
	Total		11,865.00 -	11,865.00	935.01				0/12
	<u>POWER</u>								
3	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO, TRIPURA	07/2012	296.87 -	296.87	206.14	-	03/2015	-	0/17
	Total		296.87 -	296.87	206.14				0/17
	<u>RAILWAYS</u>								
4	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 377.32	645.00	286.45	-	12/2014	-	0/0
5	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	470.21 470.21	1,995.25	312.36	-	12/2014	-	0/0
6	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	568.50	-	12/2014	-	0/0
7	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE	04/2008	2,050.00 -	2,050.00	178.92	-	12/2014	-	0/0
8	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	468.11	-	05/2009	69(R1)	0/0
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NEFR, WEST BENGAL	04/1983	36.80 274.41	703.18	254.77	-	03/2015	-	0/0
10	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	1,708.41	1,578.17	-	03/2015	-	0/0
11	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR, ASSAM	01/2004	915.70 915.70	3,019.17	2,843.22	-	03/2015	-	0/0
12	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR, BIHAR	04/2008	282.92 282.92	359.86	2.22	-	03/2015	-	0/0
13	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR, MULTI STATE	04/1999	175.43 -	247.75	229.26	-	03/2015	-	0/0
14	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 -	258.20	1.45	-	03/2016	-	0/0

(June 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	03/2016	-	0/0
16	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	46.37	- -	03/2017	-	0/0
17	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	18.71	- -	03/2017	-	0/0
18	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	87.44	- -	03/2017	-	0/0
19	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	32.81	- 12/2017	12/2017	0(R3)	0/0
20	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	189.84	- -	03/2018	-	0/0
	Total		7,535.95 -	14,973.45	7,246.93				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
21	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	656.90	- -	07/2014	-	2/2
22	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	383.20	- -	07/2014	-	2/2
23	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,190.00	- -	06/2015	-	2/3
	Total		1,831.00 -	1,831.00	2,230.10				6/7
	Grand Total		21,528.82	28,966.32	10,618.18				6/36

List of Projects Without Date of Commissioning

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	04/2014
	Total		4,712.12 -		
	<u>COAL</u>				
5	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	03/2013 -	03/2014
6	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
8	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		1,846.57 -		
	<u>STEEL</u>				
9	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	12/2009 08/2010	06/2013
10	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	01/2010 02/2011	11/2013
	Total		462.00 -		
	<u>PETROCHEMICALS</u>				
11	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
12	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	01/2012 -	07/2013
13	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	-
15	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
16	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	07/2012 07/2012	-
17	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
	Total		5,621.00 -		
	<u>POWER</u>				
18	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
19	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	12/2013 -	05/2014
20	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	12/2007 12/2009	-
21	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	01/2012 -	-
22	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	11/2011 -	-
23	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	07/2013 -	-
24	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	- -	-
25	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	- -	-
	Total		12,271.62 -		
	<u>RAILWAYS</u>				
26	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	06/2007
27	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
28	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 768.87	- 03/2010	03/2010
29	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 08/2010	08/2010
30	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 293.74	12/2010 12/2010	12/2010
31	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011
32	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011
33	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 03/2011	03/2011

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
34	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
35	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	02/2012
36	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012
37	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012
38	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	863.23 -	- -	03/2012
39	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	- -	03/2012
40	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	- -	03/2012
41	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 155.00	- -	10/2012
42	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	238.56 238.56	03/2012 03/2012	12/2012
43	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 343.17	- -	12/2012
44	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	- -	01/2013
45	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 607.09	12/2012 12/2012	02/2013
46	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 218.19	- -	02/2013
47	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 900.05	12/2011 12/2011	03/2013
48	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	- -	03/2013
49	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013
50	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013
51	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013
52	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	03/2013
53	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
54	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	12/2013
55	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 495.68	- -	02/2014
56	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	- -	03/2014
57	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71 -	- -	03/2014
58	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 230.03	- -	03/2014

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
59	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	03/2014
60	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014
61	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	03/2014
62	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014
63	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
64	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014
65	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014
66	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	- -	05/2014
67	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
68	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
69	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
70	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
71	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
72	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
73	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
74	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
75	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-
76	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-
77	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
78	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 2,957.21	07/2005 -	-
79	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 03/2011	-
80	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-
81	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
82	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 162.87	- -	-
83	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
84	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-
85	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-
86	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 528.65	- -	-
87	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-
88	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
89	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-
90	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	- -	-
91	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 671.82	- -	-
92	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
93	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-
94	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-
95	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-
96	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-
97	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
98	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
99	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
100	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
101	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
102	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
103	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
104	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
105	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-
106	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
107	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
108	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
110	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
111	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
112	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
113	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-
114	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
115	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
116	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-
117	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
118	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
119	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
120	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
121	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
122	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
123	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
124	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
125	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
126	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
127	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-
128	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
129	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
130	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-
131	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
132	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
133	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
134	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
135	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
136	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-
137	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
138	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
139	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
140	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
141	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
142	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
143	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
144	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
145	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
146	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-
147	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
148	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
149	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
150	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
151	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
152	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
153	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
154	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
155	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-
156	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-
157	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-
158	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
159	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
160	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
161	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
162	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-
163	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-
164	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-
165	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
166	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-
167	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
168	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
169	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
170	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
171	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
172	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
173	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
174	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
175	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
176	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
177	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
178	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
179	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
180	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
181	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
182	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
183	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
184	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
185	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
186	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
187	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
188	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
189	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
190	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
191	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
192	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
193	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-
194	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
195	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
196	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
197	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
198	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
199	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
200	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
201	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	- -	-
202	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	- -	-
203	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	- -	-
204	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	- -	-
205	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
206	GUDUR-DURGARA JAPATNAM - [N22000265]SCOR, ANDHRA PRADESH	04/2011	283.54 -	- -	-
207	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR, UTTAR PRADESH	04/2012	377.44 -	- -	-
208	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR, PUNJAB	04/2009	396.04 -	- -	-
209	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	- -	-
210	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	- -	-
211	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR, MULTI STATE	04/2013	1,239.00 -	- -	-
212	ROHTAK-MEHAM HANSI - [N22000272]NR, HARYANA	04/2012	287.00 -	- -	-
213	BHANUPALI-BILASPUR BERI NL - [N22000273]NR, HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
214	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91 -	- -	-
215	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 -	- -	-
216	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00 -	- -	-
217	SHIMOGA-HARIHAR NL - [N22000278]SWR, KARNATAKA	04/2011	562.74 -	- -	-
218	RAYADURGA-TUMKUR NL - [N22000279]SWR, MULTI STATE	04/2007	970.34 -	- -	-
219	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	341.05 -	- -	-
220	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	- -	-
221	CUMBUM-PRODDATUR - [N22000282]SCOR, ANDHRA PRADESH	04/2013	829.00 -	- -	-
222	MUDKHED-PARBHANI - [N22000283]SCOR, MAHARASHTRA	04/2011	390.60 -	- -	-
223	AKKANAPET-MEDAK - [N22000285]SCOR, TELANGANA	04/2012	153.00 -	- -	-
224	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR, ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
225	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR, MULTI STATE	04/2010	337.49 -	- -	-
226	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	- -	-
227	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR, MULTI STATE	04/2010	338.54 -	- -	-
228	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR, MULTI STATE	04/2008	162.96 -	- -	-
229	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR, HARYANA	04/2013	400.00 -	- -	-
230	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR, MULTI STATE	04/2013	876.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
232	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
233	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
234	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
235	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
236	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
237	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
238	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
239	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
240	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
241	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
242	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
243	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
244	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
245	KAKINADA-PITHAPURAM - [N22000314]SECR,ANDHRA PRADESH	03/1999	215.06 -	- -	-
246	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
247	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
248	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
249	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	-
250	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-
	Total		110,042.31 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
251	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
252	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
253	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
254	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013
255	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013
256	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	05/2013
257	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013
258	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
259	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013
260	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
261	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
262	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
263	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013
264	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
265	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
266	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014
267	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014
268	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
269	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
270	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
271	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
272	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-
273	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
274	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		16,070.95 -		
	<u>SHIPPING AND PORTS</u>				
275	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010
276	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
277	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
278	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
279	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012
280	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012
281	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
282	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013
283	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
284	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
285	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
286	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
287	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
288	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 04/2014	04/2014
289	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
290	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-
	Total		13,727.25 -		
	TELECOMMUNICATIONS				
291	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012
292	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013
293	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013
294	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-
295	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEAPON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
296	GSM EQUIPMENT OF 4,50,000 LINES (2G) HARYANA (PHASE V.2) TELECOM CIRCLE - [N26000080]BSNL,HARYANA	09/2008	216.54 -	09/2009 -	-
297	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-
	Total		3,277.68 -		
	<u>URBAN DEVELOPMENT</u>				
298	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
299	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>WATER RESOURCES</u>				
300	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		180,544.19		

List of Projects Ahead of Schedule w.r.t. Original Schedule

(June 2014)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	264.84	03/2015 -	02/2015
	Total		452.00 -	452.00	264.84		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	333.88	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	333.88		
	<u>PETROLEUM</u>						
3	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	20.79	01/2016 -	12/2015
	Total		607.06 -	607.06	20.79		
	<u>POWER</u>						
4	SYSTEM STRENGTHENING - XIX IN SOUTHERN REGIONAL GRID - [N18000137]	9/2012	1,935.35 -	1,935.35	735.08	12/2014 -	11/2014
5	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	65.27	11/2016 -	03/2016
6	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	17.04	05/2016 -	04/2016
	Total		4,615.77 -	4,615.77	817.39		
	Grand Total		7,183.57	7,183.57	1,436.90		

List of On Schedule Projects w.r.t. Original Schedule

(June 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		217.60 -	217.60	.04		
	<u>COAL</u>						
2	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	255.25	03/2015 -	03/2015
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	664.21	03/2016 03/2016	03/2016
4	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	76.30	03/2015 -	03/2015
5	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015
6	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	99.22	03/2015 -	03/2015
7	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	221.41	03/2016 -	03/2016
8	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	30.30	03/2018 -	03/2018
9	JALAGAM VENGALA RAO OCP-II - [N06000094	7/2011	447.06 -	447.06	29.03	03/2015 -	03/2015
10	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	21.25	03/2018 -	03/2018
11	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
12	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
13	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
14	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	95.88	03/2020 -	03/2020
15	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.14 -	430.14	65.57	03/2016 -	03/2016
16	KALYANIKHANI OPENCAST PROJECT - [N06000101	7/2012	417.33 -	417.33	2.12	07/2016 -	07/2016
17	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100	6/2012	365.01 -	365.01	6.56	06/2015 -	06/2015
18	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	57.78	03/2016 -	03/2016
19	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110	4/2012	364.75 -	364.75	57.87	10/2014 -	10/2014
20	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015

(June 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
22	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	87.18	03/2016 -	03/2016
23	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
24	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	52.14	03/2016 -	03/2016
25	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	181.71	03/2017 -	03/2017
	Total		12,841.57 -	12,470.23	2,020.40		
	<u>PETROLEUM</u>						
26	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	595.67	03/2015 -	03/2015
27	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	193.65	11/2015 -	11/2015
28	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
29	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 -	10/2014
30	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10 -	1,913.10	9.50	05/2016 -	05/2016
31	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	2.31	07/2016 -	07/2016
32	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
33	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	-	02/2016 -	02/2016
34	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	42.24	09/2017 -	09/2017
35	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
36	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	17.48	03/2015 -	03/2015
37	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
38	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	139.50	03/2015 -	03/2015
39	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	85.47	04/2015 -	04/2015
40	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	0.27	02/2016 -	02/2016
41	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	33.26	07/2016 -	07/2016
42	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	80.22	12/2014 -	12/2014
43	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	182.89	08/2015 -	08/2015

(June 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	245.50	11/2015 -	11/2015
45	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,595.82	05/2015 -	05/2015
46	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	589.19	11/2015 -	11/2015
47	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	248.72	12/2014 -	12/2014
	Total		37,219.66 -	36,366.67	5,154.18		
	<u>POWER</u>						
48	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	798.03	02/2015 -	02/2015
49	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	188.96	08/2014 -	08/2014
50	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
51	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	358.12	11/2014 -	11/2014
52	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	2,693.00	09/2016 -	09/2016
53	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
55	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
56	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
57	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	76.40	05/2016 -	05/2016
58	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	38.79	03/2016 -	03/2016
59	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	1,254.00	09/2017 -	09/2017
60	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	557.43	06/2015 -	06/2015
61	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	140.75	12/2015 -	12/2015
62	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]	2/2014	378.71 -	378.71	-	10/2016 -	10/2016
63	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
64	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016

(June 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
65	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
66	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	09/2016 -	09/2016
67	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
68	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	130.00	08/2017 -	08/2017
69	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,677.00	05/2017 -	05/2017
70	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	20.63	10/2014 -	10/2014
71	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	58.96	10/2014 -	10/2014
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	310.29	03/2015 -	03/2015
73	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,056.00	08/2015 -	08/2015
74	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	2,715.00	11/2016 -	11/2016
75	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	4,520.00	12/2016 -	12/2016
76	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	43.47	06/2014 -	06/2014
77	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	1,196.87	10/2014 -	10/2014
	Total		77,881.87 -	77,881.87	17,833.70		
	<u>RAILWAYS</u>						
78	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	128.17	02/2015 -	02/2015
79	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	441.33	03/2016 -	03/2016
80	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	400.00	03/2016 -	03/2016
81	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	2.43	02/2019 -	02/2019
82	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
83	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	165.16	84.91	03/2015 -	03/2015
84	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	188.81	03/2017 -	03/2017
85	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	18.72	03/2015 -	03/2015

(June 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
87	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	64.98	03/2015 -	03/2015
88	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	439.52	03/2016 -	03/2016
	Total		15,688.03 -	20,708.19	1,771.89		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
89	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
90	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	506.20	08/2015 -	08/2015
91	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	192.10	10/2015 -	10/2015
92	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
93	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	268.10	09/2014 -	09/2014
94	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	1,440.00	10/2014 -	10/2014
95	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	512.70	04/2015 -	04/2015
96	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	115.90	12/2015 -	12/2015
97	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	263.80	07/2014 -	07/2014
98	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	360.60	10/2014 -	10/2014
99	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	844.60	09/2015 -	09/2015
100	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
101	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	272.10	11/2016 -	11/2016
102	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	341.60	06/2015 -	06/2015
103	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,709.00	09/2014 -	09/2014
104	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	52.72	07/2014 -	07/2014
105	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	284.80	10/2014 -	10/2014
	Total		18,658.30 -	18,658.30	8,913.75		
	<u>STEEL</u>						
106	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	237.09	57.28	12/2014 -	12/2014

(June 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	97.07	06/2015 -	06/2015
108	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	10.55	05/2016 -	05/2016
	Total		795.81 -	795.81	164.90		
	<u>URBAN DEVELOPMENT</u>						
109	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
110	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	8,699.49		
	Grand Total		228,292.98	232,088.81	44,558.35		

List of Delayed Projects w.r.t. Original and Revised Schedule

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,702.00	12/2008 -	03/2015	75	31.12	Slippage of commitments by M/s Atoms troy Export (ASE), Russian Federation.
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,564.17	09/2010 -	03/2015	54	62.57	NR
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11	0	Delay in supply of major equipments.
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,110.00	12/2016 -	03/2017	3	0	Delay in supply of major equipments.
	Total		40,442.00 -	46,726.00	25,376.17					
	<u>CIVIL AVIATION</u>									
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	0	Delay in supply of equipments.
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.81	01/2011 04/2013	12/2016	71	0	1. Adverse weather condition. 2. Delay in diversion of roads
	Total		653.74 -	653.74	277.81					
	<u>COAL</u>									
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,415.43	03/2012 -	08/2014	29	34.63	1. Contractual issues. 2. Delay in civil works and erection of equipments
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,991.89	06/2009 -	09/2014	63	49.09	1. Contractual issues. 2. Delay in equipment erection.
9	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	03/2015	24	478.5	1. Contractual issues. 2. Adverse geo-mining conditions
10	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	0	1. Land acquisition. 2. Rehabilitation & resettlement problems
11	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	119.98	03/2013 -	03/2015	24	0	1. Environmental clearance. 2. Coal evacuation problems.
12	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	117.27	03/2013 -	03/2015	24	0	Environmental clearance.

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
13	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	226.56	03/2012 -	03/2015	36	0	1. Land acquisition 2. Rehabilitation & resettlement problems
14	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36	0	Environmental clearance
15	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	121.62	03/2013 -	03/2015	24	0	1. Rehabilitation & resettlement problems. 2. Law & order problems. 3.Environmental clearance
16	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,553.35	03/2014 -	03/2016	24	0	1. Rehabilitation & resettlement problems. 2. Delay in tendering of major HEMM.
17	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,541.93	03/2014 -	03/2016	24	0	1. Rehabilitation & resettlements problems. 2. Delay in tendering of major HEMM.
18	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44	50.37	Law & order problems.
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	139.74	03/2010 -	03/2016	72	0	Rehabilitation & resettlement issues.
20	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	272.43	03/2014 -	03/2016	24	0	Contractual issues
21	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	103.88	12/2012 -	03/2016	39	0	1. Land acquisition. 2. Rehabilitation & resettlement problems. 3. Contractual issues. 4. Adverse geo-mining conditions.
22	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	38.70	03/2014 -	03/2016	24	0	1. Law & order problems. 2. Contractual issues.
23	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.56	03/2014 -	03/2016	24	0	Land acquisition
24	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	155.48	03/2012 -	03/2016	48	0	1. Environmental clearance. 2. Delay in forest land diversion.
25	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	0	1. Rehabilitation & resettlement problems. 2. Environmental clearance.
26	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.52	03/2014 -	03/2016	24	.02	Environmental clearance.
27	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60	0	Contractual issues
28	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	139.29	03/2012 -	03/2016	48	0	Environmental clearance.
29	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	129.04	03/2010 -	03/2017	84	0	Coal evacuation problem

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
30	ASHOK EXPN.OCP -CCL (10 MTY) - [N060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	100.27	03/2011 -	03/2017	72	-27.57	1. Law & order problems. 2. Environmental clearance. 3. Coal evacuation problems.
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72	0	Contractual issues.
32	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	0	1. Land acquisition. 2. Rehabilitation & resettlement problems
33	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.73	03/2012 -	03/2017	60	0	Rehabilitation & resettlement problems
34	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	44.81	03/2014 -	03/2017	36	0	1. Rehabilitation & resettlement problems. 2. Environmental clearance.
35	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	341.57	12/2015 -	04/2018	28	0	Delay in opening and evaluation of bids
36	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2019	48	0	NA
37	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	754.54	03/2013 03/2023	03/2023	120	540.6	1. Rehabilitation & resettlement problems. 2. Environmental clearance.
	Total		26,843.94 -	37,085.68	15,996.69					
	STEEL									
38	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,734.82	12/2011 -	07/2014	31	0	Packages approved at different times
39	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.73	09/2008 12/2013	08/2014	71	100.63	NR
40	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,872.97	10/2009 10/2012	09/2014	59	41.41	Poor mobilization by contractors
41	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,000.18	12/2011 -	09/2014	33	13.61	1. Soil related problems. 2. Delay in approval of engineering design from railway authorities
42	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	312.99	09/2009 05/2012	12/2014	63	-6.25	Re-tendering and lack of consultants
43	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	11,220.39	03/2013 -	12/2014	21	0	NR
44	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	395.07	04/2013 09/2014	12/2014	20	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
45	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	130.22	10/2013 -	12/2014	14	0	NR
46	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	373.28	12/2011 01/2015	01/2015	37	105.2	1. Maoist activities, 2. Fire incident.
47	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	309.56	05/2013 01/2015	01/2015	20	0	Re-tendering and construction delays
48	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	111.54	08/2014 -	01/2015	5	0	NR
49	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	18.86	09/2014 -	01/2015	4	0	NR
50	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,938.98	03/2013 -	03/2015	24	0	NR
51	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,238.22	12/2012 -	03/2015	27	0	NR
52	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	111.90	11/2013 -	06/2015	19	0	NR
	Total		64,701.45 -	70,655.41	59,929.71					
	PETROLEUM									
53	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	07/2014	34	-24.1	NR
54	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	113.00	06/2012 -	07/2014	25	-38.7	ROW problem at site due to intervention of local villagers
55	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	257.90	04/2012 -	07/2014	27	12.16	Forest clearance and High Court permission for cutting mangroves were obtained in Dec'12.
56	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	151.39	06/2012 09/2013	07/2014	25	41.85	1.Delay in release of drawings by EPC contractor, 2. Delay in Soil filling and frequent bands.
57	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,738.16	02/2014 -	08/2014	6	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
58	GAS TURBINE GENERATION SET - [N18000146]OIL, ASSAM	07/2009	216.88 -	216.88	178.68	10/2011 06/2014	08/2014	34	0	1. Short supply of materials. 2. Delay in finalization of Bop vendor for ventilation system.
59	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN, KARNATAKA	08/2008	12,412.00 12,160.26	12,160.26	11,441.51	01/2012 -	09/2014	32	-2.03	Project has been delayed due to slow construction progress for CPP by BHEL & slow construction progress in Unit package - Coke Handling by M/s Torpor & Utility package - Raw Water by M/s Aqua fill Polymers.
60	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	169.76	08/2013 -	09/2014	13	-18.75	1. Delay in award of work. 2. Slow progress by the contractors
61	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN, KARNATAKA	05/2009	1,803.78 -	1,803.78	978.32	07/2012 -	10/2014	27	0	1. Project is delayed due to poor progress of piping works by M/s Simplex and inadequate deployment of skilled manpower. 2. Poor manpower mobilization by Electrical & Instrumentation contractor.
62	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC, MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20	104.84	Delay in award of work for project facilities (well platforms & pipelines, hiring of FPSO)
63	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, HARYANA	11/2007	281.07 -	281.07	6.18	10/2010 -	12/2014	50	0	No potential customers coming up in Sultanpur-Jhajjar- Hissar section. Anchor Load DFR Customers (RIL SEZ, TATA Power etc.) shelved off their projects. Presently the project is on hold
64	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 -	32,710.00	26,052.00	11/2012 11/2013	12/2014	25	9.85	1. Law & order at site, 2. Delay in construction of Power Plant by BHEL, 3. Delay in remobilization of manpower after cyclone.
65	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,916.30	09/2011 05/2012	12/2014	39	-33.8	In the terrain where horizontal boring is being carried out, a very hard rock strata was encountered. This strata was encountered after a progress of about 35-40 mtr and at that stage, there was no option but to continue with the same technique. No alternative technique can be adopted for further job.

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
66	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	971.42	10/2011 -	12/2014	38	54.46	Completion delayed primarily because the rectification of rock wedge failure in cavern A1 took more time and Zones of poor geology encountered during excavation of balance bench.
67	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	138.83	06/2014 -	12/2014	6	0	NR
68	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.17	03/2013 03/2014	03/2015	24	-3.5	Local problems and court cases by tea gardener.
69	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.56	03/2012 -	03/2015	36	-28.67	Hard rocks & restricted ROU provided by forest deptt. caused delay in construction progress.
70	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	03/2015	31	-11.94	Construction activities hampered due to ROU related issues. Marshy and highly undulating terrain resulting in poor progress in pipeline laying work.
71	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	104.80	09/2012 -	03/2015	30	-20.28	Slow progress in civil work and fabrication work due to less resource mobilization.
72	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	589.37	05/2013 06/2014	03/2015	22	-11.62	Increase in scope of work and delay in procurement of steel and fabrication of legs by the contractor.
73	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	94.80	03/2014 -	03/2015	12	0	1. Clubbing of project facilities alongwith C-26 Cluster development project. 2. slow progress by the contractor
74	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	599.48	12/2014 -	03/2015	3	0	Desalter and air coolers not received at site.
75	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	3,068.29	12/2008 04/2013	05/2015	77	15.5	1. Two decks sunk into international waters which necessitated re- fabrication of the decks. 2. Delay in taking up drilling of all planned wells due to subsurface studies and re-prioritization of locations

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
76	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,855.00	08/2010 03/2012	05/2015	57	84.68	1. Contract terminated as contractor failed to submit PBG insurance. 2. Splitting of facility into three packages, scope optimization in view of the price rise in oil field services/equipments and preparation of fresh bid packages. 3. Increased facility.
77	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	2,182.31	06/2012 -	05/2015	35	7.76	Delay in installation of well platforms due to delay in material supply and punch through location
78	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	287.14	05/2014 -	05/2015	12	0	NR
79	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,200.35	05/2014 -	05/2015	12	-44.37	Contractor did not take up the work as per scope.
80	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,728.25	04/2006 06/2012	06/2015	110	536.46	Non-cooperation by equipments suppliers, sub-contractors and consultant, delay in availability of subsea manifold and prolonged repairing work and complications in well G-1-9 and well control activities.
81	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	536.65	12/2013 03/2014	09/2015	21	17.25	Progress is affected due to slow progress in construction activities
82	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 462.79	462.79	85.74	10/2014 -	10/2015	12	49.38	Delay in getting statutory approvals.
83	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	864.97	10/2011 -	10/2015	48	67.62	Order for Mangalore-Padur pipeline is yet to be placed. Recommendation awaited from EIL
84	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,255.25	01/2012 -	10/2015	45	70.49	Order for Mangalore-Padur pipeline is yet to be placed. Recommendations awaited from EIL.
85	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	11/2015	11	0	One of the bidder M/s Drillmech filed writ petition in Guwahati High Court against deviation in process of evaluation for award of LOA. Matter currently sub judice.

(June 2014) All Cost/ Expenditure in Rs. crore										
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
86	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63	25.71	1. Delay in finalization of tender due to representation by bidders in IEM and further in High Court and Supreme Court. 2. Scope optimization and preparation of new bid package during re-tendering. 3. Drilling of wells and re-prioritization of locations in view of geological surprises.
87	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	0	Execution of JHPL project would be synchronized with gas availability from various domestic sources/ customer readiness. Revival pkg. approved for Sindri and Gorakhpur fertilizer plant . HFCL revival plan is under consideration for the units at Haldia, Durgapur, and Barauni. Project activities will start after signing of GSA/ GTA by consumers.
88	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	450.13	09/2011 -	12/2015	51	0	1. Delay in preparation of drawing and additional model testing of Hull form in Austria . 2. Shortage of skilled manpower at contractor's end. 3. Inadequate ancillary/sub-contractors at the location. 4. Lack of planning to match resources to work targets. 5. Change in delivery location.
89	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	994.83	09/2012 -	12/2015	39	0	Works regularly hampered at many locations due to frequent interruptions by activists. Station works at various locations are not progressing due to poor deployment of resources & financial crunch faced by contractors.
90	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,015.77	01/2014 -	12/2015	23	0	1. Slow progress by the contractor in laying of pipelines. 2 Delay in conversion work of Sagar Samrat to MOPU. 3. Delay in drilling of some wells due to non-availability of light rig.

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
91	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	251.53	07/2015 -	12/2015	5	0	NR
92	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	2,563.75	12/2015 -	05/2016	5	0	NR
93	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	0	1. Revision in scope of work. 2. Closure of original tender due to high quoted price.
94	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24	0	1.Preparation of TBP and cost estimation takes too much time. 2. Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and layout of control rooms etc. 3. Preparation of pre-bid replies in view of the quantum and complexities
95	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24	0	1. Preparation of TBP and cost estimation 2. Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and lay out of control rooms etc. 3. Preparation of pre-bid replies in view of the quantum and complexities.
96	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23	0	1. Preparation of TBP and cost estimation 2. Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and lay out of control rooms etc. 3. Preparation of pre-bid replies in view of the quantum and complexities
97	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54	0	Project site shifted to new location at Madhuban for which land in under possession of OIL.
	Total		127,799.99 -	138,088.26	85,979.43					
	POWER									

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
98	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	-	10/2013 -	06/2014	8	0	ROW problem
99	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	31	0	NR
100	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	667.64	11/2012 -	06/2014	19	0	Severe ROW Problem.
101	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,356.86	08/2012 -	08/2014	24	0	1. Environmental clearance, 2. Law & order problems.
102	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,398.15	12/2013 -	08/2014	8	0	Forest clearance
103	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	133.04	03/2014 -	08/2014	5	0	NR
104	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	490.59	09/2010 -	09/2014	48	0	ROW Problem.
105	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	573.99	876.27	08/2013 -	09/2014	13	0	Law & order, adverse weather & geo-mining condition.
106	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	2,129.61	08/2012 -	09/2014	25	9.32	Law & order problems.
107	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	185.39	06/2012 -	09/2014	27	0	ROW Problem.
108	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	1,421.95	08/2014 -	09/2014	1	0	NR
109	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	230.77	08/2014 -	09/2014	1	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
110	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	163.82	01/2014 -	09/2014	8	0	Delay due to type testing of GIS equipment of substation.
111	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,568.64	03/2013 -	11/2014	20	0	Non- availability of shut down by OPTCL.
112	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	293.42	06/2014 -	11/2014	5	0	ROW Problem.
113	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,001.99	08/2012 -	12/2014	28	0	Contractual issues.
114	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,197.40	12/2013 -	12/2014	12	0	Environmental clearance awaited.
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,047.82	04/2013 -	12/2014	20	0	ROW Problem
116	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	669.00	08/2014 -	12/2014	4	0	NR
117	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	694.18	11/2014 -	12/2014	1	0	NR
118	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,463.37	03/2014 -	02/2015	11	0	Non- availability of shut down by OPTCL.
119	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	368.72 -	913.63	610.46	07/2006 12/2015	02/2015	103	147.78	Ban on mining, inadequate infrastructure.
120	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	8,238.60	7,658.00	08/2013 -	03/2015	19	12.23	Delay in supply of materials by BHEL.
121	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,219.87	11/2012 -	03/2015	28	0	Environmental clearance awaited.
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	397.02	07/2013 -	03/2015	20	0	Environmental clearance awaited.
123	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,460.45	05/2014 -	03/2015	10	0	Contract termination due to poor performance

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
124	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGY PRIVATE LIMITED AND INDBARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,364.50	09/2014 -	03/2015	6	0	NR
125	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	296.91	11/2013 -	03/2015	16	0	Environmental clearance awaited.
126	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	1,881.83	07/2014 -	03/2015	8	0	Delay in forest clearance & ROW problems.
127	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	418.10	02/2014 -	03/2015	13	0	ROW Problem.
128	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	7,220.00	5,958.00	04/2009 -	05/2015	73	59.48	Right Bank slide, Seepage problem in main dam.
129	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 -	1,746.65	451.33	08/2014 -	05/2015	9	0	Environmental clearance awaited
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	120.22	04/2015 -	05/2015	1	0	NR
131	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	8,604.10	08/2013 -	06/2015	22	0	ROW Problem.
132	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,777.00	12/2012 -	06/2015	30	0	ROW Problem
133	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	68.90	01/2013 -	06/2015	29	0	Land acquisition
134	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,243.16	11/2013 -	06/2015	19	0	Land acquisition

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
135	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,074.06	08/2014 -	06/2015	10	0	Forest clearance awaited.
136	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	728.92	01/2015 -	06/2015	5	0	NR
137	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,630.21	10/2014 -	06/2015	8	0	Land acquisition
138	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,923.18	10/2012 -	12/2015	38	0	Environmental clearance
139	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	545.65	01/2015 -	12/2015	11	0	Wild life clearance awaited from state WL Board
140	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	845.43	11/2012 -	12/2015	37	0	Land acquisition
141	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	2,127.69	06/2015 -	12/2015	6	0	NR
142	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,061.38	1,513.20	09/2009 -	03/2016	78	0	Cash problem of civil contractor.
143	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	283.37	02/2012 -	03/2016	49	0	NR
144	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,575.00	07/2011 -	08/2016	61	0	Contractual issues, law & order problem.
145	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	-	08/2014 -	08/2016	24	0	NR
146	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 -	3,642.04	3,489.64	01/2016 -	11/2016	10	62.69	Employment issue.
147	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	735.81	07/2010 02/2016	02/2017	79	79.77	Ban on mining activity

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
148	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 -	2,496.90	2,991.34	12/2009 03/2017	03/2017	87	0	Adverse geo-mining & contractual issues.
149	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	12/2003	8,692.97 -	13,737.00	10,086.00	12/2009 -	03/2017	87	58.02	1. Delay in supply of equipments, 2. Slow progress by implementing agencies.
150	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,146.00	03/2013 -	03/2017	48	29.14	Adverse weather condition (flash flood & heavy rainfall)
151	PARBATI HEP (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	3,919.59	4,534.79	09/2009 -	07/2018	106	0	Cash problem of contractor.
152	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, UTTARAKHAND	08/2008	2,491.58 -	3,745.08	488.66	07/2014 -	07/2018	48	50.31	Rehabilitation & resettlement issues
153	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,877.35	09/2010 -	12/2018	99	0	Stoppage of work due to agitation by AASU
	Total		135,181.91 -	149,427.76	108,277.78					
	<u>RAILWAYS</u>									
154	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	308.27	02/2009 02/2009	08/2014	66	73.33	Contractual issues
155	KHURDA ROAD - BARANG 3RD LINE (DL) (ECR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	276.00	280.13	03/2009 03/2009	08/2014	65	106.88	Contractual issues
156	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	608.02	586.81	03/1994 -	09/2014	246	282.96	Delayed due to occurrence of crack in pier
157	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	09/2001	120.00 245.39	245.39	227.22	12/2008 -	09/2014	69	104.49	NR
158	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	10/2014	31	44.03	NR
159	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	432.72	403.29	12/2009 03/2011	12/2014	60	300.67	Land acquisition
160	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 2,363.00	2,363.00	1,383.02	03/2009 12/2012	12/2014	69	156.57	NR
161	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 207.52	207.52	202.11	12/2012 -	12/2014	24	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
162	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	171.02	148.69	06/2013 -	12/2014	18	0	NR
163	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240	60.58	Increase in scope of work.
164	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	445.40	180.42	03/2007 03/2007	03/2015	96	13.2	1. Land acquisition , 2. Fund constraints.
165	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR, BIHAR	09/2001	492.98 -	1,022.64	742.15	12/2010 12/2010	03/2015	51	107.44	Fund constraints
166	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, TAMIL NADU	04/2006	495.74 -	495.74	272.47	06/2013 06/2013	03/2015	21	0	NR
167	- [220100214]SER, JHARKHAND	04/1997	194.07 194.07	596.40	381.74	06/2004 -	06/2015	132	207.31	Law & order problems.
168	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 2,921.00	2,921.00	2,169.50	10/2007 12/2012	12/2015	98	367.76	NR
169	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	16.41	NR
170	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRT, MAHARASHTRA	03/1996	401.81 495.44	1,814.10	376.57	03/2004 12/2010	03/2016	144	351.48	Fund constraints
171	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	66.46	03/2014 -	03/2016	24	0	NR
172	KATAKHAL TO BHAIRABI - [N22000126]NEFR, ASSAM	04/1998	227.90 227.90	331.40	140.11	12/2012 -	03/2016	39	45.41	Fund constraints
173	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	388.67	92.56	12/2015 -	03/2016	3	25.6	Delayed due to acute sand problem & foundation problem
174	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRT, TELANGANA	04/2012	632.68 -	816.55	17.54	04/2012 -	03/2016	47	29.06	NR
175	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	460.73	06/2005 07/2011	06/2016	132	265.5	1. Rehabilitation & resettlement issues 2. Fund constraints.
176	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	94.53	03/2016 -	06/2016	3	0	Encroachment along the proposed alignment

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
177	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	481.56	03/2005 12/2008	12/2016	141	1172.55	1. Rehabilitation & resettlement issues 2. Fund constraints.
178	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,708.74	03/2014 03/2016	12/2016	33	32.32	NR
179	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	184.91	59.57	03/2015 -	12/2016	21	23.36	NR
180	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	2,483.04	1,582.40	12/2008 -	03/2017	99	238.75	1. Fund constraints, 2. Land acquisition.
181	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	5,996.00	2,262.95	03/2011 03/2014	03/2017	72	724.12	Fund constraints
182	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,116.53	309.20	03/2010 03/2017	03/2017	84	243.55	Court cases
183	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	1,741.00	681.02	03/2014 -	03/2017	36	114.06	Fund constraints
184	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	2,393.48	175.62	04/2014 -	03/2017	35	286.46	Environmental clearance awaited
185	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	3,375.42	86.75	12/2015 -	03/2017	15	151.99	Wild life clearance awaited.
186	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	2,446.57	9.23	03/2015 -	03/2017	24	187.83	Change in original alignment.
187	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	5,185.44	4,277.33	03/2009 -	03/2017	96	209.34	Fund constraints
188	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	1,242.25	972.61	03/2007 -	03/2017	120	38.8	Fund constraints
189	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181	700	NR
190	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,500.00 -	4,996.19	3,237.27	04/2008 03/2014	12/2017	116	233.08	Fund constraints
	Total		29,667.67 -	80,673.29	34,770.32					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
191	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	311.80	06/2008 -	06/2014	72	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
192	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00	268.70	06/2008 -	06/2014	72	0	NR
193	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	07/2014	26	0	NR
194	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	07/2014	13	0	NR
195	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	587.30	07/2012 -	07/2014	24	0	NR
196	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45	309.10	09/2010 -	08/2014	47	0	NR
197	AMRITSAR-PATHANKOT - [N24000147]NHAI, PUNJAB	05/2010	705.00 -	705.00	2,190.00	11/2012 -	08/2014	21	0	NR
198	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	743.10	07/2013 -	08/2014	13	0	NR
199	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	920.80	03/2014 -	08/2014	5	0	NR
200	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	474.20	01/2014 -	08/2014	7	0	NR
201	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,147.00	06/2014 -	08/2014	2	0	NR
202	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 241.28	280.13	168.30	11/2008 12/2014	09/2014	70	80.68	NR
203	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	284.90	10/2008 -	09/2014	71	-8.95	NR
204	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	09/2014	78	0	NR
205	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	275.80	06/2008 09/2014	09/2014	75	0	NR
206	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	2,034.00	08/2013 06/2014	09/2014	13	0	NR
207	SIX LANNING OF HOSUR-KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	09/2014	9	0	NR
208	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,284.00	12/2013 -	09/2014	9	0	NR
209	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
210	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	09/2014	10	0	NR
211	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	963.50	05/2014 -	09/2014	4	0	NR
212	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	436.30	04/2014 -	09/2014	5	0	NR
213	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	327.40	04/2008 01/2015	10/2014	78	0	NR
214	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	211.40	05/2008 01/2015	10/2014	77	0	NR
215	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	891.70	07/2013 -	11/2014	16	0	NR
216	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	262.30	09/2007 03/2014	12/2014	87	-1.84	NR
217	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	186.00	09/2008 -	12/2014	75	30.1	NR
218	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 361.00	280.00	357.00	02/2009 -	12/2014	70	0	NR
219	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 167.64	167.64	121.30	11/2008 12/2014	12/2014	73	0	NR
220	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 200.00	200.00	198.40	04/2009 12/2014	12/2014	68	0	NR
221	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94	519.50	09/2008 -	12/2014	75	0	NR
222	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	251.03	376.40	10/2008 -	12/2014	74	0	NR
223	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	273.00	04/2008 01/2015	12/2014	80	0	NR
224	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	325.40	04/2008 01/2015	12/2014	80	0	NR
225	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 331.23	363.74	238.30	07/2009 -	12/2014	65	85.58	NR
226	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00 -	557.00	1,121.00	02/2010 -	12/2014	58	0	NR
227	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	664.90	05/2010 -	12/2014	55	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
228	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	1,509.10	2,492.00	09/2012 -	12/2014	27	0	NR
229	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	0	NR
230	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40	0	NR
231	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20	0	NR
232	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	888.40	03/2013 -	12/2014	21	0	NR
233	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19	0	NR
234	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	193.45	63.89	11/2012 -	12/2014	25	0	NR
235	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,207.00	03/2013 -	12/2014	21	0	NR
236	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,141.00	07/2013 -	12/2014	17	0	NR
237	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	12/2014	22	0	NR
238	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	146.50	05/2013 -	12/2014	19	0	NR
239	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	823.90	03/2013 -	12/2014	21	0	NR
240	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	664.90	01/2014 -	12/2014	11	0	NR
241	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	12/2014	6	0	NR
242	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	998.79	1,560.00	08/2013 -	12/2014	16	0	NR
243	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	281.40	06/2014 -	12/2014	6	0	NR
244	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	356.80	08/2013 -	02/2015	18	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
245	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	134.10	04/2009 12/2014	03/2015	71	92.75	NR
246	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	267.10	06/2008 -	03/2015	81	0	NR
247	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	310.70	06/2008 -	03/2015	81	0	NR
248	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	125.00	09/2007 -	03/2015	90	82.12	NR
249	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	217.61	444.00	04/2010 01/2016	03/2015	59	0	NR
250	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	106.5	NR
251	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,270.00	06/2013 -	03/2015	21	0	NR
252	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	329.50	04/2014 -	03/2015	11	0	NR
253	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.70	07/2013 -	03/2015	20	0	NR
254	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19	0	NR
255	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	708.20	09/2014 -	03/2015	6	0	NR
256	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.00	05/2014 -	05/2015	12	0	NR
257	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.40	06/2005 -	06/2015	120	0	NR
258	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	286.70	09/2007 07/2011	06/2015	93	33.7	NR
259	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0	NR
260	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,717.00	08/2013 -	06/2015	22	0	NR
261	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,662.00	08/2014 -	07/2015	11	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
262	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	459.10	02/2014 -	09/2015	19	0	NR
263	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	717.30	09/2014 -	10/2015	13	0	NR
264	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	603.80	10/2013 -	11/2015	25	0	NR
265	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0	NR
266	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	605.90	05/2013 -	12/2015	31	0	NR
267	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,056.00	03/2014 -	12/2015	21	0	NR
268	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	65.35	01/2013 -	12/2015	35	0	NR
269	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	377.70	09/2013 -	12/2015	27	0	NR
270	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	590.40	03/2013 -	12/2015	33	0	NR
271	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	365.20	08/2013 -	12/2015	28	0	NR
272	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	137.70	01/2014 -	12/2015	23	0	NR
273	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	682.00	07/2014 -	12/2015	17	0	NR
274	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	316.60	10/2013 -	12/2015	26	0	NR
275	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.00	06/2014 -	12/2015	18	0	NR
276	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12	0	NR
277	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.00	08/2012 -	03/2016	43	0	NR
278	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	540.60	06/2015 -	05/2016	11	0	NR
279	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	06/2016	76	2.29	NR
280	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,136.00	07/2015 -	06/2016	11	0	NR

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
281	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	12/2016	39	0	NR
282	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	NR
	Total		65,761.19 -	67,736.24	63,763.53					
	<u>SHIPPING AND PORTS</u>									
283	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99	300	Land acquisition.
284	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0	NR
285	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,005.88	12/2010 09/2012	10/2015	58	75.75	Scrutiny of technical bid is in progress.
	Total		1,889.87 -	3,270.03	1,252.40					
	<u>TELECOMMUNICATIONS</u>									
286	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	37	-16.01	Delay in supply by one of the vendor M/s Gemini, the PO placed 2707 BTS on the firm terminated by office of CGM STP. Presently the case is sub judice.
287	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	85.96	06/2009 -	09/2014	63	6.42	The project is delayed due to difficulty in acquisition /hiring of site.
288	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	09/2014	68	0	1. Municipal permission issue 2. Electric connection issue 3. Delay in permission to lay optical fiber cable from local bodies 4. Non availability of suitable sites 5. Security issue for working staff in remote area and frequent strikes.

(June 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
289	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 01/2015	01/2015	51	0	1. Issue related to change of business process. 2. Integration issue with CDR system 3. Procurement of additional server storage 4. Issues related to vendor.
	Total		2,018.15 -	1,843.90	549.84					
	<u>URBAN DEVELOPMENT</u>									
290	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	0	NR
	Total		2,494.00 -	2,494.00	685.21					
	Grand Total		497,453.91	598,654.31	396,858.89					

List of Projects Without Milestones w.r.t. Original Schedule

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	04/2014	0/0
4	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	10/2014	0/0
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	02/2015	0/0
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015	0/0
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	12/2016	0/0
	Total		4,092.95 -			0/0
	<u>COAL</u>					
8	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014	0/0
9	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	03/2016	0/0
10	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	04/2017	0/0
11	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	03/2018 -	03/2018	0/0
12	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2019	0/0
13	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	03/2021 -	03/2021	0/0
14	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	03/2022 -	03/2022	0/0
	Total		4,933.22 -			0/0
	<u>PETROLEUM</u>					
15	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013	0/0
16	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	04/2012 -	07/2014	0/0
17	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	06/2012 09/2013	07/2014	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00	02/2014	08/2014	0/0
19	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06	10/2014	10/2014	0/0
20	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07	10/2010	12/2014	0/0
21	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00	12/2014	12/2014	0/0
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011	12/2014	0/0
23	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75	06/2014	12/2014	0/0
24	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26	09/2012	03/2015	0/0
25	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00	12/2014	03/2015	0/0
26	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50	04/2015	04/2015	0/0
27	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00	-	04/2015	0/0
28	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82	04/2015	04/2015	0/0
29	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	12/2008 04/2013	05/2015	0/0
30	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	06/2012	05/2015	0/0
31	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	04/2006 06/2012	06/2015	0/0
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 462.79	10/2014	10/2015	0/0
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011	10/2015	0/0
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012	10/2015	0/0
35	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00	12/2014	11/2015	0/0
36	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36	11/2015	11/2015	0/0
37	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
38	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18	01/2013	12/2015	0/0
39	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65	09/2011	12/2015	0/0
40	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00	07/2015	12/2015	0/0
41	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06	01/2016	12/2015	0/0
42	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07	02/2016	02/2016	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
43	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	02/2016 -	02/2016	0/0
44	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	04/2016 -	04/2016	0/0
45	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
46	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	05/2016 -	05/2016	0/0
47	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0
48	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	07/2016 -	07/2016	0/0
49	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2016	0/0
50	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2016	0/0
51	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 -	03/2017	0/0
52	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	09/2012 -	03/2017	0/0
53	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	09/2017 -	09/2017	0/0
54	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
55	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	12/2018 -	12/2018	0/0
56	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
57	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
	Total		92,272.92 -			0/0
	<u>POWER</u>					
58	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	09/2014	0/0
59	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	06/2015 -	06/2015	0/0
60	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
61	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	12/2015 -	12/2015	0/0
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	03/2016 -	03/2016	0/0
63	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	11/2016 -	03/2016	0/0
64	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	03/2016 -	03/2016	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
65	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	05/2016 -	04/2016	0/0
66	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
67	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	05/2016 -	05/2016	0/0
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	06/2016 -	06/2016	0/0
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	06/2016 -	06/2016	0/0
70	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	07/2016 -	07/2016	0/0
71	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	08/2014 -	08/2016	0/0
72	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	09/2016 -	09/2016	0/0
73	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	10/2016 -	10/2016	0/0
74	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	11/2016	0/0
75	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	12/2018	0/0
76	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	- -	-	0/0
77	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	- -	-	0/0
	Total		23,818.73 -			0/0
	<u>RAILWAYS</u>					
78	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	06/2007	0/0
79	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
80	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 768.87	- 03/2010	03/2010	0/0
81	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 08/2010	08/2010	0/0
82	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 293.74	12/2010 12/2010	12/2010	0/0
83	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011	0/0
84	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
85	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 03/2011	03/2011	0/0
86	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
87	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	02/2012	0/0
88	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
89	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
90	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	863.23 -	- -	03/2012	0/0
91	HARNOUT - SET. UP OF W/S TO UND. POH OF UP TO 50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
92	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
93	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 155.00	- -	10/2012	0/0
94	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	238.56 238.56	03/2012 03/2012	12/2012	0/0
95	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 343.17	- -	12/2012	0/0
96	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	- -	01/2013	0/0
97	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 607.09	12/2012 12/2012	02/2013	0/0
98	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 218.19	- -	02/2013	0/0
99	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 900.05	12/2011 12/2011	03/2013	0/0
100	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013	0/0
101	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
102	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
103	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	03/2013	0/0
104	GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
105	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	12/2013	0/0
106	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 495.68	- -	02/2014	0/0
107	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	- -	03/2014	0/0
108	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 230.03	- -	03/2014	0/0
109	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	03/2013 -	03/2014	0/0
110	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
111	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN	04/2008	516.23 -	03/2014 -	03/2014	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
112	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
113	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
114	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014	0/0
115	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014	0/0
116	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	- -	05/2014	0/0
117	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
118	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
119	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	09/2014	0/0
120	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	12/2008 -	09/2014	0/0
121	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	03/2012 12/2013	10/2014	0/0
122	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	- -	12/2014	0/0
123	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	12/2014	0/0
124	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 470.21	- -	12/2014	0/0
125	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
126	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	12/2012 -	12/2014	0/0
127	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2014	0/0
128	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	12/2014	0/0
129	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	12/2014	0/0
130	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	02/2015	0/0
131	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
132	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
133	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2015	0/0
134	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2015	0/0
135	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
136	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	12/2010 12/2010	03/2015	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
137	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 915.70	- -	03/2015	0/0
138	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	03/2015	0/0
139	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	- -	03/2015	0/0
140	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
141	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2015	0/0
142	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
143	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
144	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	06/2004 -	06/2015	0/0
145	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
146	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
147	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	03/2004 12/2010	03/2016	0/0
148	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
149	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
151	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	12/2012 -	03/2016	0/0
152	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
153	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
154	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	03/2016	0/0
155	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	03/2016	0/0
156	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	04/2012 -	03/2016	0/0
157	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	06/2016	0/0
158	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
159	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
160	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	03/2014 03/2016	12/2016	0/0
161	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
162	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2017	0/0
163	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
164	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
165	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2017	0/0
166	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2017	0/0
167	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
168	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
169	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	03/2009 -	03/2017	0/0
170	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	03/2007 -	03/2017	0/0
171	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	- -	03/2017	0/0
172	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	- -	03/2017	0/0
173	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR, ASSAM	04/2011	312.12 -	- -	03/2017	0/0
174	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
175	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
176	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
177	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,500.00 -	04/2008 03/2014	12/2017	0/0
178	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	- 12/2017	12/2017	0/0
179	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	- -	03/2018	0/0
180	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
181	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
182	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
183	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
184	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
185	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
186	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
187	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
188	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
189	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
190	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-	0/0
191	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-	0/0
192	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
193	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 2,957.21	07/2005 -	-	0/0
194	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 03/2011	-	0/0
195	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
196	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
197	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 162.87	- -	-	0/0
198	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-	0/0
199	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-	0/0
200	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-	0/0
201	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 528.65	- -	-	0/0
202	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-	0/0
203	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
204	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-	0/0
205	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	- -	-	0/0
206	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 671.82	- -	-	0/0
207	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
208	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-	0/0
209	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-	0/0
210	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-	0/0
211	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
212	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
213	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
214	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
215	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
216	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
217	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
218	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
219	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
220	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-	0/0
221	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
222	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
223	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
224	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
225	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
226	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
227	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
228	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-	0/0
229	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
230	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
231	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-	0/0
232	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
233	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
234	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
235	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
236	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
237	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
238	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
239	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
240	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
241	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
242	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-	0/0
243	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
244	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
245	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-	0/0
246	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
247	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
248	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
249	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
250	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
251	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-	0/0
252	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
253	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
254	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
255	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
256	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
257	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
258	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
259	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
260	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
261	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
262	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
263	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
264	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
265	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
266	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-	0/0
267	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
268	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
269	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
270	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
271	AGARTALA-AKHAURA NL - [N22000195]NEFR, TRIPURA	04/2012	252.00 -	- -	-	0/0
272	DIMAPUR-TIZIT NL - [N22000196]NEFR, NAGALAND	04/2013	4,274.00 -	- -	-	0/0
273	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
274	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
275	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
276	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
277	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR, MEGHALAYA	04/2010	4,083.02 -	- -	-	0/0
278	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
279	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-	0/0
280	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-	0/0
281	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR, ASSAM	04/2012	246.07 -	- -	-	0/0
282	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
283	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
284	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-	0/0
285	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
286	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
287	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
288	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
289	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
290	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
291	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
292	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
293	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
294	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
295	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
296	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
297	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
298	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
299	BARIAPUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
300	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
301	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
302	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
303	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
304	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
305	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
306	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
307	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
308	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-	0/0
309	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-	0/0
310	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
311	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
312	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
313	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
314	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
315	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
316	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
317	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
318	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
319	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
320	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
321	GUDUR-DURGARAJPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
322	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
323	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
324	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
325	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
326	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
327	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
328	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
329	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
330	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
331	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
332	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
333	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
334	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
335	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
336	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
337	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
338	AKKANAPET-MEDAK - [N22000285]SCOR,TELANGANA	04/2012	153.00 -	- -	-	0/0
339	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
340	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
341	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
342	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
343	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
344	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
345	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
346	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
347	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
348	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
349	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
350	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
351	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
352	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
353	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
354	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
355	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
356	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
357	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
358	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
359	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
360	KAKINADA-PITHAPURAM - [N22000314]SECR,ANDHRA PRADESH	03/1999	215.06 -	- -	-	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
361	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
362	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0
363	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
364	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	-	0/0
365	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-	0/0
	Total		161,909.25 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
366	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012	0/0
367	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012	0/0
368	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012	0/0
369	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013	0/0
370	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013	0/0
371	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013	0/0
372	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
373	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
374	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013	0/0
375	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013	0/0
376	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0
377	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
378	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0
379	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
380	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	06/2014	0/0
381	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	06/2014	0/0
382	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	07/2014	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
383	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	07/2014	0/0
384	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	07/2014	0/0
385	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	07/2014	0/0
386	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	07/2014	0/0
387	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	08/2014	0/0
388	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	08/2014	0/0
389	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	08/2014	0/0
390	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	08/2014	0/0
391	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	08/2014	0/0
392	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	08/2014	0/0
393	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	11/2008 12/2014	09/2014	0/0
394	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	09/2014	0/0
395	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	09/2014	0/0
396	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 09/2014	09/2014	0/0
397	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	08/2013 06/2014	09/2014	0/0
398	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	09/2014	0/0
399	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	09/2014	0/0
400	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	09/2014	0/0
401	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	09/2014	0/0
402	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	09/2014	0/0
403	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
404	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	09/2014	0/0
405	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	09/2014	0/0
406	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	10/2014	0/0
407	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 01/2015	10/2014	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
408	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00	10/2014	10/2014	0/0
409	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	10/2014	10/2014	0/0
410	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50	10/2014	10/2014	0/0
411	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00	10/2014	10/2014	0/0
412	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88	07/2013	11/2014	0/0
413	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47	09/2007	12/2014	0/0
414	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00	09/2008	12/2014	0/0
415	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00	02/2009	12/2014	0/0
416	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64	11/2008	12/2014	0/0
417	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00	04/2009	12/2014	0/0
418	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94	09/2008	12/2014	0/0
419	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03	10/2008	12/2014	0/0
420	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96	04/2008	12/2014	0/0
421	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00	04/2008	12/2014	0/0
422	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00	07/2009	12/2014	0/0
423	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00	02/2010	12/2014	0/0
424	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00	05/2010	12/2014	0/0
425	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37	10/2011	12/2014	0/0
426	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00	04/2013	12/2014	0/0
427	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00	03/2013	12/2014	0/0
428	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00	05/2013	12/2014	0/0
429	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45	11/2012	12/2014	0/0
430	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55	03/2013	12/2014	0/0
431	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76	07/2013	12/2014	0/0
432	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30	02/2013	12/2014	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
433	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2014	0/0
434	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	12/2014	0/0
435	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	12/2014	0/0
436	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2014	0/0
437	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	12/2014	0/0
438	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	12/2014	0/0
439	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	02/2015	0/0
440	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 12/2014	03/2015	0/0
441	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	03/2015	0/0
442	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	03/2015	0/0
443	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	09/2007 -	03/2015	0/0
444	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	03/2015	0/0
445	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2015	0/0
446	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2015	0/0
447	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2015	0/0
448	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2015	0/0
449	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	03/2015	0/0
450	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
451	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2015	0/0
452	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	06/2015	0/0
453	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 07/2011	06/2015	0/0
454	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	06/2015	0/0
455	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	06/2015	0/0
456	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
457	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	07/2015	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
458	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
459	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	09/2015	0/0
460	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
461	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
462	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
463	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	11/2015	0/0
464	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
465	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	12/2015	0/0
466	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	12/2015	0/0
467	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2015	0/0
468	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	12/2015	0/0
469	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2015	0/0
470	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2015	0/0
471	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	12/2015	0/0
472	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2015	0/0
473	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	12/2015	0/0
474	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	12/2015	0/0
475	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	12/2015	0/0
476	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2016	0/0
477	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2016	0/0
478	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
479	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	06/2016	0/0
480	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
481	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
482	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
483	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
484	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
485	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
486	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
487	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
488	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0
489	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
490	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
	Total		91,141.35 -			0/0
	<u>SHIPPING AND PORTS</u>					
491	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
492	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
493	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0
494	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
495	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0
496	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012	0/0
497	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013	0/0
498	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0
499	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
500	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
501	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0
502	ACQUISTION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
503	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 04/2014	04/2014	0/0
504	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014	0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
505	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
506	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2015	0/0
507	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
508	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		15,462.28 -			0/0
	<u>TELECOMMUNICATIONS</u>					
509	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012	0/0
510	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013	0/0
511	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
512	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	06/2014	0/0
513	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	06/2009 -	09/2014	0/0
514	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	09/2014	0/0
515	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 01/2015	01/2015	0/0
516	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-	0/0
517	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GEPOE EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-	0/0
518	GSM EQUIPMENT OF 4,50,000 LINES (2G) HARYANA (PHASE V.2) TELECOM CIRCLE - [N26000080]BSNL,HARYANA	09/2008	216.54 -	09/2009 -	-	0/0
519	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-	0/0
	Total		5,295.83 -			0/0
	<u>URBAN DEVELOPMENT</u>					
520	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
521	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0
522	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
523	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		67,598.32 -			0/0

			(June 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>WATER RESOURCES</u>					
524	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		467,067.75			0/0

List of Ongoing Projects having Time and Cost Overrun w.r.t Original Schedule

(June 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12	75
	Total		16,663.00 -	22,947.00				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50	24
4	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60	120
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	09/2014	49.09	63
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63	29
	Total		9,127.17 -	42,445.95				
	<u>PETROLEUM</u>							
9	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	07/2014	41.85	25
10	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	07/2014	12.16	27
11	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	462.79	10/2014 -	10/2015	49.38	12
12	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	04/2006 -	06/2015	536.46	110
13	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	09/2015	17.25	21
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	12/2014	54.46	38
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45

(June 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
17	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2015	7.76	35
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63
19	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	05/2015	15.50	77
20	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
21	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68	57
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85	25
	Total		48,053.07 -	105,051.31				
	<u>POWER</u>							
23	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79
24	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.04	01/2016 -	11/2016	62.69	10
25	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32	25
26	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31	48
27	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14	48
28	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48	73
29	BARH STPP STAGE -II - [N18000047	02/2008	7,341.04 -	8,238.60	08/2013 -	03/2015	12.23	19
30	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	13,737.00	12/2009 -	03/2017	58.02	87
	Total		32,287.84 -	151,040.09				
	<u>RAILWAYS</u>							
31	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67	60
32	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141
33	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49	69
34	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65
35	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	184.91	03/2015 -	12/2016	23.36	21

(June 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
36	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	09/2014	282.96	246
37	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66
38	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03	31
39	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.40	06/2004 -	06/2015	207.31	132
40	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
41	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50	132
42	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60	3
43	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
44	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20	96
45	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	03/2016	351.48	144
46	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,022.64	12/2010 -	03/2015	107.44	51
47	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
48	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46	35
49	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
50	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06	47
51	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
52	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12	72
53	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75	99
54	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06	36
55	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83	24
56	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80	120
57	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
58	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99	15

(June 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
59	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	12/2017	233.08	116
60	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34	96
61	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
62	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,012.84	03/2014 -	12/2016	32.32	33
	Total		24,097.25 -	226,142.96				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
63	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10	75
64	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	09/2014	80.68	70
65	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58	65
66	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75	71
67	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12	90
68	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	06/2016	2.29	76
69	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93
70	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50	40
	Total		2,649.01 -	230,794.53				
	<u>SHIPPING AND PORTS</u>							
71	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00	99
72	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75	58
	Total		1,378.00 -	233,552.69				
	<u>STEEL</u>							
73	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	08/2014	100.63	71
74	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20	37
75	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	09/2014	41.41	59

(June 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
76	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	09/2014	13.61	33
	Total		23,538.89 -	263,075.54				
	<u>TELECOMMUNICATIONS</u>							
77	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	06/2009 -	09/2014	6.42	63
	Total		149.15 -	263,234.26				
	Grand Total		157,943.38	1,538,284.33				

List of Ongoing Projects having Cost Overrun w.r.t. to Original Schedule

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,573.92	05/2011 -	03/2013	32.50
4	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77
	Total		4,086.12 -	27,924.45			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	09/2014	49.09
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
8	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
9	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50
10	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		9,767.76 -	48,112.09			
	<u>PETROCHEMICALS</u>						
14	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		5,460.61 -	57,032.09			
	<u>PETROLEUM</u>						
15	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	2,735.65	04/2006 -	06/2015	536.46
16	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	05/2015	15.50
17	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
18	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68
19	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85
20	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
21	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2015	7.76
22	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	09/2015	17.25
23	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
24	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
25	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	07/2014	12.16
26	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
27	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	462.79	10/2014 -	10/2015	49.38
28	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	12/2014	54.46
29	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
30	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49
31	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	06/2012 -	07/2014	41.85
	Total		51,017.38 -	123,316.10			
	<u>POWER</u>						
32	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48
33	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	13,737.00	12/2009 -	03/2017	58.02

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
34	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
35	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
36	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
37	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
38	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.04	01/2016 -	11/2016	62.69
39	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
40	BARH STPP STAGE -II - [N18000047	02/2008	7,341.04 -	8,238.60	08/2013 -	03/2015	12.23
41	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32
42	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	07/2013 -	-	48.08
43	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	01/2011	368.72 -	913.63	07/2006 02/2015	02/2015	147.78
	Total		35,453.31 -	174,008.18			
	<u>RAILWAYS</u>						
44	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	09/2014	282.96
45	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
46	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
47	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
48	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
49	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
50	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.18	- -	03/2015	1,810.82
51	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
52	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
53	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	03/2016	351.48
54	AHMEDNAGAR-PARLI VAIJNATH(NL) CR [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	01/2013	337.26
56	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
57	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
58	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	10/2012	414.30
59	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
60	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
61	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,708.41	- -	03/2015	151.99
62	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	12/2017	233.08
63	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	12/2014	195.55
64	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20
65	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.40	06/2004 -	06/2015	207.31
66	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
67	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
68	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
69	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
70	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,022.64	12/2010 -	03/2015	107.44
71	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
72	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	02/2015	248.16
73	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255]	03/2002	863.23 -	1,075.11	- -	03/2012	24.55
74	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	06/2007	35.57
75	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	900.00	- -	-	800.00
76	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
77	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,045.20	- -	-	216.73

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75
79	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,176.10	12/2006 -	08/2010	202.58
80	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
81	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	1,382.78	- -	-	902.01
82	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
83	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
84	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	12/2014	324.33
85	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
86	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
87	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12
88	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
89	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
90	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
91	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	-	160.32
92	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
93	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
94	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49
95	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
96	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
97	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
98	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53
99	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
100	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
101	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
102	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
103	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
104	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
105	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
106	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
107	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
109	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
110	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
111	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
112	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	- -	03/2018	115.17
113	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
114	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
115	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	12/2016	32.32
116	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03
117	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50
118	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06
119	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
120	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
121	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
122	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2014	81.45

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
124	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113	04/2008	653.19 -	653.46	03/2014 -	03/2014	0.04
125	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
126	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
127	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	484.61	03/2012 -	-	52.28
128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
129	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
130	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
131	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34
132	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
133	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	- -	-	184.87
134	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63
135	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
136	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152	04/2013	456.00 -	855.16	- -	-	87.54
137	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153	04/2010	739.65 -	872.22	- -	-	17.92
138	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	218.39	- -	-	2.34
139	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
140	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	553.63 -	651.17	- -	-	17.62
141	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	184.91	03/2015 -	12/2016	23.36
142	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60
143	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	175.69 -	325.00	- -	-	84.98

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
144	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	285.07 -	378.56	- -	-	32.80
145	ATTIPPATTU-PUTTUR - [N22000184	04/2008	446.87 -	528.00	- -	-	18.16
146	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	1,200.00	- -	-	129.22
147	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
148	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
149	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188	04/1999	271.24 -	520.00	- -	-	91.71
150	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	04/2008	822.39 -	1,280.83	- -	-	55.74
151	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	346.15	- -	-	28.14
152	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192	04/1999	175.43 -	247.75	- -	03/2015	41.22
153	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
154	ERODE-PALANI - [N22000199	04/2008	288.57 -	603.22	- -	-	109.04
155	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	-	173.71
156	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	247.00 -	951.24	- -	12/2014	285.12
157	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	222.95	- -	-	16.29
158	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	165.82 -	545.64	- -	-	229.06
159	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJBHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,418.21	- -	-	171.08
160	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	- -	-	47.95
161	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
162	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02
163	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	499.30 -	2,501.05	- -	-	400.91
164	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
165	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	182.06 -	184.06	- -	-	1.10

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
166	PANVEL PEN DOUBLING - [N22000255]	04/2006	191.00 -	260.16	- -	05/2014	36.21
167	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
168	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	645.00	- -	-	259.03
169	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
170	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
171	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
172	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
173	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
174	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
175	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
176	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
177	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
178	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
179	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
180	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
181	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
182	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
183	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
184	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
185	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	201.17	- -	-	0.08
	Total		69,404.75 -	355,817.94			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
186	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10
187	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
188	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	09/2014	80.68
189	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
190	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58
191	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	06/2016	2.29
192	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
193	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,649.01 -	360,469.51			
	SHIPPING AND PORTS						
194	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
195	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
196	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75
197	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
198	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST - [N25000037	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
199	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
200	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVEEN COCHIN [N25000048	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
201	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
202	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	372,386.17			
	STEEL						
203	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	09/2014	41.41
204	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
205	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	08/2014	100.63
206	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	09/2014	13.61
207	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09
208	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	08/2006	260.00 -	349.64	12/2009 -	06/2013	34.48
	Total		24,000.89 -	402,602.24			
	<u>TELECOMMUNICATIONS</u>						
209	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058	01/2009	149.15 -	158.72	06/2009 -	09/2014	6.42
210	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE [N26000088	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
211	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE [N26000090	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	404,083.69			
	<u>URBAN DEVELOPMENT</u>						
212	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
213	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX, MUMBAI - [N28000048	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	415,865.77			
	<u>WATER RESOURCES</u>						
214	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	417,052.77			
	Grand Total		235,577.86	3,181,618.00			

List of Projects on schedule w.r.t. Latest Schedule

(June 2014)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		217.60 -	217.60	.04		
	<u>COAL</u>						
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	6/2008	1,188.31 -	7,612.33	754.54	03/2013 03/2023	03/2023
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	664.21	03/2016 03/2016	03/2016
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	181.71	03/2017 -	03/2017
5	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	255.25	03/2015 -	03/2015
6	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	76.30	03/2015 -	03/2015
7	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015
8	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	99.22	03/2015 -	03/2015
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	221.41	03/2016 -	03/2016
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	95.88	03/2020 -	03/2020
11	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	65.57	03/2016 -	03/2016
12	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	2.12	07/2016 -	07/2016
13	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	6.56	06/2015 -	06/2015
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	57.78	03/2016 -	03/2016
15	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.03	03/2015 -	03/2015
16	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
17	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	30.30	03/2018 -	03/2018
18	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015

(June 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]	4/2012	364.75 -	364.75	57.87	10/2014 -	10/2014
20	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	21.25	03/2018 -	03/2018
21	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
22	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
23	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
24	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	87.18	03/2016 -	03/2016
25	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
26	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	52.14	03/2016 -	03/2016
	Total		14,029.88 -	20,082.56	2,774.94		
	<u>PETROLEUM</u>						
27	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	3/2010	3,241.03 -	6,638.94	2,192.69	03/2013 11/2014	11/2014
28	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	595.67	03/2015 -	03/2015
29	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	248.72	12/2014 -	12/2014
30	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	182.89	08/2015 -	08/2015
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	245.50	11/2015 -	11/2015
32	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	589.19	11/2015 -	11/2015
33	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,595.82	05/2015 -	05/2015
34	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	80.22	12/2014 -	12/2014
35	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	193.65	11/2015 -	11/2015
36	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
37	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 -	10/2014
38	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10 -	1,913.10	9.50	05/2016 -	05/2016

(June 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
39	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	2.31	07/2016 -	07/2016
40	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
41	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	-	02/2016 -	02/2016
42	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	42.24	09/2017 -	09/2017
43	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
44	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
45	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	139.50	03/2015 -	03/2015
46	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	85.47	04/2015 -	04/2015
47	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	0.27	02/2016 -	02/2016
48	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	33.26	07/2016 -	07/2016
49	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	17.48	03/2015 -	03/2015
	Total		40,460.69 -	43,005.61	7,346.87		
	POWER						
50	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	2,496.90	2,991.34	12/2009 03/2017	03/2017
51	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	798.03	02/2015 -	02/2015
52	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
53	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	43.47	06/2014 -	06/2014
54	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	1,196.87	10/2014 -	10/2014
55	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	188.96	08/2014 -	08/2014

(June 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
56	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	358.12	11/2014 -	11/2014
57	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	2,693.00	09/2016 -	09/2016
58	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	140.75	12/2015 -	12/2015
59	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
60	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	130.00	08/2017 -	08/2017
61	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,677.00	05/2017 -	05/2017
62	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	20.63	10/2014 -	10/2014
63	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	58.96	10/2014 -	10/2014
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	310.29	03/2015 -	03/2015
65	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,056.00	08/2015 -	08/2015
66	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	2,715.00	11/2016 -	11/2016
67	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	09/2016 -	09/2016
68	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
71	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
72	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	76.40	05/2016 -	05/2016
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	38.79	03/2016 -	03/2016
74	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	1,254.00	09/2017 -	09/2017
75	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	557.43	06/2015 -	06/2015

(June 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166	2/2014	378.71 -	378.71	-	10/2016 -	10/2016
77	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
78	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
79	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
80	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	4,520.00	12/2016 -	12/2016
	Total		80,378.77 -	80,378.77	20,825.04		
	<u>RAILWAYS</u>						
81	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29	128.17	02/2015 -	02/2015
82	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	4/2010	3,951.98 -	4,259.48	439.52	03/2016 -	03/2016
83	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112	4/2008	829.74 -	829.74	64.98	03/2015 -	03/2015
84	DELANG-PURI DOUBLING - [N22000320	3/2011	165.16 -	165.16	84.91	03/2015 -	03/2015
85	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245	4/2010	423.66 -	423.66	188.81	03/2017 -	03/2017
86	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
87	PLASSEY-JIAGANJ DOUBLING - [N22000220	4/2011	248.07 -	248.07	18.72	03/2015 -	03/2015
88	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	2.43	02/2019 -	02/2019
89	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
90	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	400.00	03/2016 -	03/2016
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	4/2010	2,913.51 -	2,913.51	441.33	03/2016 -	03/2016
92	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	4/2006	325.00 -	1,116.53	309.20	03/2010 03/2017	03/2017
	Total		16,013.03 -	21,824.72	2,081.09		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						

(June 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
93	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	167.64	121.30	11/2008 12/2014	12/2014
94	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	200.00	198.40	04/2009 12/2014	12/2014
95	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	275.80	06/2008 09/2014	09/2014
96	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,709.00	09/2014 -	09/2014
97	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI [N24000211]	7/2012	356.40 -	356.40	52.72	07/2014 -	07/2014
98	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	506.20	08/2015 -	08/2015
99	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	360.60	10/2014 -	10/2014
100	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
101	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) [N24000232]	11/2013	1,916.79 -	1,916.79	272.10	11/2016 -	11/2016
102	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	192.10	10/2015 -	10/2015
103	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
104	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	268.10	09/2014 -	09/2014
105	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC [N24000226]	10/2011	1,565.00 -	1,565.00	1,440.00	10/2014 -	10/2014
106	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	512.70	04/2015 -	04/2015
107	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	115.90	12/2015 -	12/2015
108	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	263.80	07/2014 -	07/2014
109	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	844.60	09/2015 -	09/2015
110	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	341.60	06/2015 -	06/2015
111	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	284.80	10/2014 -	10/2014
112	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
	Total		19,250.94 -	19,250.94	9,509.25		
	SHIPPING AND PORTS						

(June 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
113	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	139.80	03/2006 06/2014	06/2014
114	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		661.87 -	1,111.87	246.52		
	<u>STEEL</u>						
115	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	1/2007	295.89 -	607.17	373.28	12/2011 01/2015	01/2015
116	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]	2/2011	898.55 -	898.55	309.56	05/2013 01/2015	01/2015
117	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	237.09	57.28	12/2014 -	12/2014
118	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	97.07	06/2015 -	06/2015
119	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	10.55	05/2016 -	05/2016
	Total		1,990.25 -	2,301.53	847.74		
	<u>TELECOMMUNICATIONS</u>						
120	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]	10/2009	384.00 -	384.00	29.45	10/2010 01/2015	01/2015
	Total		384.00 -	384.00	29.45		
	<u>URBAN DEVELOPMENT</u>						
121	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
122	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	8,699.49		
	Grand Total		238,377.17	253,547.74	52,360.43		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

						(June 2014)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
1	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 241.28	280.13	168.30	11/2008 12/2014	09/2014
	Total		155.04 -	280.13	168.30		
	<u>CIVIL AVIATION</u>						
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	264.84	03/2015 -	02/2015
	Total		452.00 -	452.00	264.84		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	333.88	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	333.88		
	<u>PETROLEUM</u>						
4	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	20.79	01/2016 -	12/2015
	Total		607.06 -	607.06	20.79		
	<u>POWER</u>						
5	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	1/2011	368.72	913.63	610.46	07/2006 12/2015	02/2015
6	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]	9/2012	1,935.35 -	1,935.35	735.08	12/2014 -	11/2014
7	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	65.27	11/2016 -	03/2016
8	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	17.04	05/2016 -	04/2016
	Total		4,984.49 -	5,529.40	1,427.85		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
9	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	273.00	04/2008 01/2015	12/2014

(June 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
10	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	09/2014
11	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	327.40	04/2008 01/2015	10/2014
12	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 230.00	208.00	325.40	04/2008 01/2015	12/2014
13	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	211.40	05/2008 01/2015	10/2014
14	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 309.56	217.61	444.00	04/2010 01/2016	03/2015
	Total		1,204.73 -	1,204.73	2,072.40		
	Grand Total		8,912.06	9,582.06	4,288.06		

List of Delayed Projects w.r.t. Latest Schedule

(June 2014)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,702.00	12/2008 -	03/2015	75	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,564.17	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,110.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	25,376.17				
	<u>CIVIL AVIATION</u>								
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.81	01/2011 04/2013	12/2016	71	44
	Total		653.74 -	653.74	277.81				
	<u>COAL</u>								
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,415.43	03/2012 -	08/2014	29	-
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,991.89	06/2009 -	09/2014	63	-
9	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	03/2015	24	30
10	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
11	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	119.98	03/2013 -	03/2015	24	-
12	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	117.27	03/2013 -	03/2015	24	-
13	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	226.56	03/2012 -	03/2015	36	-
14	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36	-
15	PURNADIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND	07/2008	210.98 -	210.98	121.62	03/2013 -	03/2015	24	-
16	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,553.35	03/2014 -	03/2016	24	-
17	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,541.93	03/2014 -	03/2016	24	-
18	MAGADH OC 20 MTY (CCL) - [N06000015]JCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	139.74	03/2010 -	03/2016	72	-
20	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	272.43	03/2014 -	03/2016	24	-
21	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	103.88	12/2012 -	03/2016	39	-
22	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	38.70	03/2014 -	03/2016	24	-
23	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.56	03/2014 -	03/2016	24	-
24	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	155.48	03/2012 -	03/2016	48	-
25	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
26	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.52	03/2014 -	03/2016	24	-
27	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60	-
28	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	139.29	03/2012 -	03/2016	48	-
29	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	129.04	03/2010 -	03/2017	84	-
30	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	100.27	03/2011 -	03/2017	72	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72	-
32	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
33	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.73	03/2012 -	03/2017	60	-
34	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	44.81	03/2014 -	03/2017	36	-
35	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	341.57	12/2015 -	04/2018	28	-
36	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2019	48	-
	Total		25,655.63 -	29,473.35	15,242.15				
	STEEL								
37	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,734.82	12/2011 -	07/2014	31	-
38	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.73	09/2008 12/2013	08/2014	71	8
39	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,872.97	10/2009 10/2012	09/2014	59	23
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,000.18	12/2011 -	09/2014	33	-
41	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	312.99	09/2009 05/2012	12/2014	63	31

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,220.39	03/2013 -	12/2014	21	-
43	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	395.07	04/2013 09/2014	12/2014	20	3
44	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	130.22	10/2013 -	12/2014	14	-
45	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	111.54	08/2014 -	01/2015	5	-
46	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	18.86	09/2014 -	01/2015	4	-
47	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,938.98	03/2013 -	03/2015	24	-
48	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,238.22	12/2012 -	03/2015	27	-
49	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	111.90	11/2013 -	06/2015	19	-
	Total		63,507.01 -	69,149.69	59,246.87				
	<u>PETROLEUM</u>								
50	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	07/2014	34	28
51	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 -	678.02	113.00	06/2012 -	07/2014	25	-
52	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL, MAHARASHTRA	08/2009	246.81 -	276.83	257.90	04/2012 -	07/2014	27	-
53	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 -	204.29	151.39	06/2012 09/2013	07/2014	25	10
54	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, MULTI STATE	08/2010	8,140.00 -	8,140.00	6,738.16	02/2014 -	08/2014	6	-
55	GAS TURBINE GENERATION SET - [N18000146]OIL, ASSAM	07/2009	216.88 -	216.88	178.68	10/2011 06/2014	08/2014	34	2
56	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN, KARNATAKA	08/2008	12,412.00 12,160.26	12,160.26	11,441.51	01/2012 -	09/2014	32	-
57	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	169.76	08/2013 -	09/2014	13	-
58	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN, KARNATAKA	05/2009	1,803.78 -	1,803.78	978.32	07/2012 -	10/2014	27	-
59	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, HARYANA	11/2007	281.07 -	281.07	6.18	10/2010 -	12/2014	50	-
60	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 -	32,710.00	26,052.00	11/2012 11/2013	12/2014	25	13
61	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,916.30	09/2011 05/2012	12/2014	39	31

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	971.42	10/2011 -	12/2014	38	-
63	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	138.83	06/2014 -	12/2014	6	-
64	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.17	03/2013 03/2014	03/2015	24	12
65	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.56	03/2012 -	03/2015	36	-
66	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	03/2015	31	-
67	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	104.80	09/2012 -	03/2015	30	-
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	589.37	05/2013 06/2014	03/2015	22	9
69	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	94.80	03/2014 -	03/2015	12	-
70	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	599.48	12/2014 -	03/2015	3	-
71	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	3,068.29	12/2008 04/2013	05/2015	77	25
72	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,855.00	08/2010 03/2012	05/2015	57	38
73	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	2,182.31	06/2012 -	05/2015	35	-
74	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	287.14	05/2014 -	05/2015	12	-
75	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,200.35	05/2014 -	05/2015	12	-
76	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,728.25	04/2006 06/2012	06/2015	110	36
77	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	536.65	12/2013 03/2014	09/2015	21	18
78	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 462.79	462.79	85.74	10/2014 -	10/2015	12	-
79	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	864.97	10/2011 -	10/2015	48	-
80	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,255.25	01/2012 -	10/2015	45	-
81	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	11/2015	11	-
82	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63	45
83	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
84	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	450.13	09/2011 -	12/2015	51	-
85	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	994.83	09/2012 -	12/2015	39	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,015.77	01/2014 -	12/2015	23	-
87	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	251.53	07/2015 -	12/2015	5	-
88	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	2,563.75	12/2015 -	05/2016	5	-
89	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
90	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24	-
91	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24	-
92	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23	-
93	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54	-
	Total		124,558.96 -	131,449.32	83,786.74				
	<u>POWER</u>								
94	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	-	10/2013 -	06/2014	8	-
95	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	31	-
96	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	667.64	11/2012 -	06/2014	19	-
97	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,356.86	08/2012 -	08/2014	24	-
98	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,398.15	12/2013 -	08/2014	8	-
99	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	133.04	03/2014 -	08/2014	5	-
100	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	490.59	09/2010 -	09/2014	48	-
101	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	573.99	876.27	08/2013 -	09/2014	13	-
102	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	2,129.61	08/2012 -	09/2014	25	-
103	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	185.39	06/2012 -	09/2014	27	-
104	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	1,421.95	08/2014 -	09/2014	1	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
105	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	230.77	08/2014 -	09/2014	1	-
106	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	163.82	01/2014 -	09/2014	8	-
107	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,568.64	03/2013 -	11/2014	20	-
108	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	293.42	06/2014 -	11/2014	5	-
109	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,001.99	08/2012 -	12/2014	28	-
110	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,197.40	12/2013 -	12/2014	12	-
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,047.82	04/2013 -	12/2014	20	-
112	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	669.00	08/2014 -	12/2014	4	-
113	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	694.18	11/2014 -	12/2014	1	-
114	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,463.37	03/2014 -	02/2015	11	-
115	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	8,238.60	7,658.00	08/2013 -	03/2015	19	-
116	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,219.87	11/2012 -	03/2015	28	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	397.02	07/2013 -	03/2015	20	-
118	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,460.45	05/2014 -	03/2015	10	-
119	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,364.50	09/2014 -	03/2015	6	-
120	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	296.91	11/2013 -	03/2015	16	-
121	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,881.83	07/2014 -	03/2015	8	-
122	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	418.10	02/2014 -	03/2015	13	-
123	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	7,220.00	5,958.00	04/2009 -	05/2015	73	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
124	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	451.33	08/2014 -	05/2015	9	-
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	120.22	04/2015 -	05/2015	1	-
126	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	8,604.10	08/2013 -	06/2015	22	-
127	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,777.00	12/2012 -	06/2015	30	-
128	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	68.90	01/2013 -	06/2015	29	-
129	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,243.16	11/2013 -	06/2015	19	-
130	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,074.06	08/2014 -	06/2015	10	-
131	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	728.92	01/2015 -	06/2015	5	-
132	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,630.21	10/2014 -	06/2015	8	-
133	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,923.18	10/2012 -	12/2015	38	-
134	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	545.65	01/2015 -	12/2015	11	-
135	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	845.43	11/2012 -	12/2015	37	-
136	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	2,127.69	06/2015 -	12/2015	6	-
137	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,061.38	1,513.20	09/2009 -	03/2016	78	-
138	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	283.37	02/2012 -	03/2016	49	-
139	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 -	4,375.35	4,575.00	07/2011 -	08/2016	61	-
140	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	-	08/2014 -	08/2016	24	-
141	KISHANGANGA HEP - [N18000031]NHPC, JAMMU AND KASHMIR	07/2007	2,238.67 -	3,642.04	3,489.64	01/2016 -	11/2016	10	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
142	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	735.81	07/2010 02/2016	02/2017	79	12
143	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	13,737.00	10,086.00	12/2009 -	03/2017	87	-
144	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,146.00	03/2013 -	03/2017	48	-
145	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	3,919.59	4,534.79	09/2009 -	07/2018	106	-
146	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	488.66	07/2014 -	07/2018	48	-
147	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,877.35	09/2010 -	12/2018	99	-
	Total		132,316.29 -	146,017.23	104,675.98				
	<u>RAILWAYS</u>								
148	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	308.27	02/2009 02/2009	08/2014	66	66
149	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	280.13	03/2009 03/2009	08/2014	65	65
150	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	586.81	03/1994 -	09/2014	246	-
151	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	227.22	12/2008 -	09/2014	69	-
152	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	10/2014	31	10
153	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	403.29	12/2009 03/2011	12/2014	60	45
154	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,383.02	03/2009 12/2012	12/2014	69	24
155	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]JER,WEST BENGAL	04/1999	207.52 207.52	207.52	202.11	12/2012 -	12/2014	24	-
156	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.02	148.69	06/2013 -	12/2014	18	-
157	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240	-
158	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	445.40	180.42	03/2007 03/2007	03/2015	96	96
159	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	1,022.64	742.15	12/2010 12/2010	03/2015	51	51
160	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]JMRTP,TAMIL NADU	04/2006	495.74 -	495.74	272.47	06/2013 06/2013	03/2015	21	21
161	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.40	381.74	06/2004 -	06/2015	132	-
162	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	2,169.50	10/2007 12/2012	12/2015	98	36
163	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
164	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	401.81 495.44	1,814.10	376.57	03/2004 12/2010	03/2016	144	63
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	66.46	03/2014 -	03/2016	24	-
166	KATAKHAL TO BHAIRABI - [N22000126]NEFR, ASSAM	04/1998	227.90 227.90	331.40	140.11	12/2012 -	03/2016	39	-
167	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	388.67	92.56	12/2015 -	03/2016	3	-
168	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	17.54	04/2012 -	03/2016	47	-
169	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	460.73	06/2005 07/2011	06/2016	132	59
170	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	94.53	03/2016 -	06/2016	3	-
171	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	481.56	03/2005 12/2008	12/2016	141	96
172	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,708.74	03/2014 03/2016	12/2016	33	9
173	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	184.91	59.57	03/2015 -	12/2016	21	-
174	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	2,483.04	1,582.40	12/2008 -	03/2017	99	-
175	JIRIBAM TO IMPHAL (TUPUI) (NL), NEFR - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	5,996.00	2,262.95	03/2011 03/2014	03/2017	72	36
176	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	1,741.00	681.02	03/2014 -	03/2017	36	-
177	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	2,393.48	175.62	04/2014 -	03/2017	35	-
178	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	3,375.42	86.75	12/2015 -	03/2017	15	-
179	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	2,446.57	9.23	03/2015 -	03/2017	24	-
180	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	5,185.44	4,277.33	03/2009 -	03/2017	96	-
181	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	1,242.25	972.61	03/2007 -	03/2017	120	-
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181	-
183	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,500.00 -	4,996.19	3,237.27	04/2008 03/2014	12/2017	116	45
	Total		29,342.67 -	79,556.76	34,461.12				
	ROAD TRANSPORT AND HIGHWAYS								

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
184	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	311.80	06/2008 -	06/2014	72	-
185	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00	268.70	06/2008 -	06/2014	72	-
186	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	07/2014	26	-
187	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	07/2014	13	-
188	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	587.30	07/2012 -	07/2014	24	-
189	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45	309.10	09/2010 -	08/2014	47	-
190	AMRITSAR-PATHANKOT - [N24000147]NHAI, PUNJAB	05/2010	705.00 -	705.00	2,190.00	11/2012 -	08/2014	21	-
191	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	743.10	07/2013 -	08/2014	13	-
192	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	920.80	03/2014 -	08/2014	5	-
193	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	474.20	01/2014 -	08/2014	7	-
194	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,147.00	06/2014 -	08/2014	2	-
195	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	284.90	10/2008 -	09/2014	71	-
196	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 - 1,141.00	1,141.00	2,034.00	08/2013 06/2014	09/2014	13	3
197	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	09/2014	9	-
198	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,284.00	12/2013 -	09/2014	9	-
199	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11	-
200	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	09/2014	10	-
201	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	963.50	05/2014 -	09/2014	4	-
202	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	436.30	04/2014 -	09/2014	5	-
203	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	891.70	07/2013 -	11/2014	16	-
204	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	262.30	09/2007 03/2014	12/2014	87	9
205	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	186.00	09/2008 -	12/2014	75	-
206	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 361.00	280.00	357.00	02/2009 -	12/2014	70	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
207	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	519.50	09/2008 -	12/2014	75	-
208	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	376.40	10/2008 -	12/2014	74	-
209	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	238.30	07/2009 -	12/2014	65	-
210	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,121.00	02/2010 -	12/2014	58	-
211	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	664.90	05/2010 -	12/2014	55	-
212	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,492.00	09/2012 -	12/2014	27	-
213	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	-
214	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40	-
215	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20	-
216	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	888.40	03/2013 -	12/2014	21	-
217	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19	-
218	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	63.89	11/2012 -	12/2014	25	-
219	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,207.00	03/2013 -	12/2014	21	-
220	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,141.00	07/2013 -	12/2014	17	-
221	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	12/2014	22	-
222	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	146.50	05/2013 -	12/2014	19	-
223	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	823.90	03/2013 -	12/2014	21	-
224	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	664.90	01/2014 -	12/2014	11	-
225	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	12/2014	6	-
226	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,560.00	08/2013 -	12/2014	16	-
227	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	281.40	06/2014 -	12/2014	6	-
228	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	356.80	08/2013 -	02/2015	18	-
229	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	134.10	04/2009 12/2014	03/2015	71	3
230	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	267.10	06/2008 -	03/2015	81	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
231	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	310.70	06/2008 -	03/2015	81	-
232	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	125.00	09/2007 -	03/2015	90	-
233	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	-
234	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,270.00	06/2013 -	03/2015	21	-
235	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	329.50	04/2014 -	03/2015	11	-
236	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.70	07/2013 -	03/2015	20	-
237	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19	-
238	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	708.20	09/2014 -	03/2015	6	-
239	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.00	05/2014 -	05/2015	12	-
240	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.40	06/2005 -	06/2015	120	-
241	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	286.70	09/2007 07/2011	06/2015	93	47
242	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	-
243	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,717.00	08/2013 -	06/2015	22	-
244	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,662.00	08/2014 -	07/2015	11	-
245	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	459.10	02/2014 -	09/2015	19	-
246	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	717.30	09/2014 -	10/2015	13	-
247	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	603.80	10/2013 -	11/2015	25	-
248	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	-
249	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	605.90	05/2013 -	12/2015	31	-
250	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,056.00	03/2014 -	12/2015	21	-
251	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	65.35	01/2013 -	12/2015	35	-
252	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	377.70	09/2013 -	12/2015	27	-
253	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	590.40	03/2013 -	12/2015	33	-
254	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	365.20	08/2013 -	12/2015	28	-

(June 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
255	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	137.70	01/2014 -	12/2015	23	-
256	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	682.00	07/2014 -	12/2015	17	-
257	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	316.60	10/2013 -	12/2015	26	-
258	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.00	06/2014 -	12/2015	18	-
259	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12	-
260	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.00	08/2012 -	03/2016	43	-
261	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	540.60	06/2015 -	05/2016	11	-
262	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	06/2016	76	-
263	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,136.00	07/2015 -	06/2016	11	-
264	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	12/2016	39	-
265	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	-
	Total		63,808.78 -	65,658.74	60,927.33				
	<u>SHIPPING AND PORTS</u>								
266	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,005.88	12/2010 09/2012	10/2015	58	37
	Total		1,228.00 -	2,158.16	1,005.88				
	<u>TELECOMMUNICATIONS</u>								
267	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	37	-
268	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	85.96	06/2009 -	09/2014	63	-
269	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	09/2014	68	-
	Total		1,634.15 -	1,459.90	520.39				
	<u>URBAN DEVELOPMENT</u>								
270	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	685.21				

(June 2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Grand Total		485,641.23	574,796.89	386,205.65				

List of ongoing projects having cost overrun w.r.t. to revised schedule

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,573.92	05/2011 -	03/2013	32.50
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77
	Total		2,278.12 -	25,909.45			
	<u>COAL</u>						
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		1,431.79 -	27,626.04			
	<u>PETROCHEMICALS</u>						
9	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	36,546.04			
	<u>PETROLEUM</u>						
10	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68
11	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070]	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
13	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR [N16000099]	03/2009	317.64 -	240.95	09/2012 -	03/2015	-24.14
14	WAX PROJECT [N16000101]	06/2010	576.60 -	676.05	12/2013 -	09/2015	17.25
15	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT [N16000138]	08/2009	246.81 -	276.83	04/2012 -	07/2014	12.16
16	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT [N18000149]	08/2008	144.02 -	204.29	06/2012 -	07/2014	41.85
	Total		34,549.53 -	76,966.16			
	<u>POWER</u>						
17	KOLDAM HEP (NTPC) [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48
18	BARH STPP(3X660MW) NTPC [180100242]	12/2003	8,692.97 -	13,737.00	12/2009 -	03/2017	58.02
19	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
20	TAPOVAN-VISHNUGAD HEP (4X130MW) [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
21	KISHANGANGA HEP [N18000031]	07/2007	2,238.67 -	3,642.04	01/2016 -	11/2016	62.69
22	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
23	BARH STPP STAGE -II [N18000047]	02/2008	7,341.04 -	8,238.60	08/2013 -	03/2015	12.23
24	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32
25	TRIPURA GAS BASED POWER PROJECT [N18000071]	07/2009	421.01 -	623.44	07/2013 -	-	48.08
26	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) [N18000119]	01/2011	368.72 -	913.63	07/2006 02/2015	02/2015	147.78
	Total		32,017.02 -	122,520.31			
	<u>RAILWAYS</u>						
27	VIRAMGAM-BHILDI(WR),GC [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
28	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
29	AMRAVATI-NARKHER NL(CR) [220100118]	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
30	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
31	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	703.18	- -	03/2015	1,810.82
32	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
33	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
34	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,814.10	03/2004 -	03/2016	351.48
35	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
36	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	01/2013	337.26
37	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
38	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	10/2012	414.30
39	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
40	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
41	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,708.41	- -	03/2015	151.99
42	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	12/2017	233.08
43	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	12/2014	195.55
44	HOWRAH-AMTA-CHAMPADANGA NL (SER) [220100208]	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20
45	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.40	06/2004 -	06/2015	207.31
46	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
47	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
48	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240]	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
49	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
50	KATI HAR - JOGBANI (GC)(NEFR) [220100247]	09/2001	492.98 -	1,022.64	12/2010 -	03/2015	107.44
51	ANGAMALI-SABARIMALA (N.L.)(SR) [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
52	GULBARGA-BIDAR,SCR(NL) [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	02/2015	248.16

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	863.23 -	1,075.11	- -	03/2012	24.55
54	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	06/2007	35.57
55	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	900.00	- -	-	800.00
56	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
57	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75
58	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,176.10	12/2006 -	08/2010	202.58
59	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
60	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	1,382.78	- -	-	902.01
61	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
62	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
63	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	12/2014	324.33
64	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
65	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
66	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12
67	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
68	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	-	160.32
69	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
70	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	472.00	- -	02/2013	116.33
71	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	- -	12/2013	52.67
72	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
73	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
74	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 -	810.78	- -	-	11.53

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
75	RAICHUR-GUNTAKAL(DL)(SCR) - [N220100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
76	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
77	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]	04/2006	378.56 -	791.59	- -	-	109.11
78	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
79	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N220000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
80	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
81	BHOPAL BINA 3D LINE DOUBLING - [N220000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
82	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N220000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
83	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
84	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
85	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]	09/2006	125.00 -	420.00	- -	-	236.00
86	TIDIVANAM-NAGARI (NL) - [N220000085]	09/2006	456.00 -	820.00	- -	-	79.82
87	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086]	09/2006	200.00 -	430.33	- -	03/2018	115.17
88	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087]	09/2006	300.00 -	532.87	- -	-	77.62
89	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
90	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	12/2016	32.32
91	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N220000094]	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03
92	TAMLUK DIGHA,LINE DOUBLING (SER) - [N220000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50
93	AGARTALA SABROOM, NL, NEFR - [N220000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06
94	BHAIRABI SAIRONG, NL, NEFR - [N220000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
95	KISHANGANJ JALALGARH, NL, NEFR - [N220000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
96	SEVOK RANGPO, NEFR - [N220000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
97	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N220000107]	04/2007	482.00 -	874.57	03/2013 -	03/2014	81.45

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
99	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.46	03/2014 -	03/2014	0.04
100	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
101	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
102	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
103	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
104	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34
105	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
106	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
107	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
108	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
109	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
110	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
111	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
112	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2016	23.36
113	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
114	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
115	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
116	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
117	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
118	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
120	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
121	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
122	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	247.75	- -	03/2015	41.22
123	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
124	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
125	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
126	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	12/2014	285.12
127	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
128	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	545.64	- -	-	229.06
129	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,418.21	- -	-	171.08
130	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	-	47.95
131	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
132	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
133	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
134	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
135	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
136	PANVEL PEN DOUBLING - [N22000255]	04/2006	191.00 -	260.16	- -	05/2014	36.21
137	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
138	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	645.00	- -	-	259.03
139	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
140	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
141	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
142	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
143	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
144	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
145	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
146	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
147	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
148	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
149	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
150	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
151	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
152	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
153	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
154	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
155	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	201.17	- -	-	0.08
	Total		63,389.31 -	286,861.35			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
156	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10
157	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75
158	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	09/2014	80.68
159	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
160	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58
161	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	06/2016	2.29
162	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
163	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		2,649.01 -	291,512.92			
	<u>SHIPPING AND PORTS</u>						
164	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75
165	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
166	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
167	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
168	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
169	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		4,174.13 -	297,454.62			
	<u>STEEL</u>						
170	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	09/2014	13.61
	Total		14,443.00 -	313,862.62			
	<u>TELECOMMUNICATIONS</u>						
171	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	09/2014	6.42
172	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
173	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	315,344.07			
	<u>URBAN DEVELOPMENT</u>						
174	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
	Total		6,395.00 -	326,953.07			

(June 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>WATER RESOURCES</u>						
175	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	328,140.07			
	Grand Total		185,387.40	2,472,643.72			
