

**365th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
March 2016**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

कार्यकारी सारांश

1. मार्च, 2016 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 1076 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। मार्च 2016 के दौरान, 2 परियोजनाओं (इस्पात क्षेत्र और पेट्रोलियम क्षेत्र में प्रत्येक में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 1076 परियोजनाओं में से, 343 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 57 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 57 परियोजनाओं में से, 14 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	सड़क परिवहन एवं राजमार्ग	414	126	27	4
2.	रेलवे	298	31	0	0
3.	विद्युत	111	64	11	7
4.	कोयला	88	42	7	0
5.	पेट्रोलियम	68	38	7	3
6.	इस्पात	33	15	0	0
7.	शहरी विकास	31	13	3	0
8.	स्वास्थ्य और परिवार कल्याण	9	4	1	0
9.	पोत परिवहन एवं पत्तन	8	2	1	0
10.	नागर विमानन	4	1	0	0
11.	परमाणु ऊर्जा	4	4	0	0
12.	खान	3	0	0	0
13.	दूरसंचार	2	2	0	0
14.	उर्वरक	1	0	0	0
15.	पेट्रोरसायन	1	0	0	0
16.	भारी उद्योग	1	1	0	0
कुल		1076	343	57	14

3. 1076 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹ 12,38,517.07 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 13,93,627.86 करोड़ होने की संभावना है, जो ₹ 1,55,110.79 करोड़

(मूल लागत का 12.52%) की समग्र लागत वृद्धि को दर्शाता है। मार्च, 2016 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,75,677.42 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 41.31% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31-03-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	लागत वृद्धि (%)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर भाविनी), 500 मेगावाट (	09/2003	3492.00	5677.00	62.57
	नागर विमानन				
1	विभिन्न हवाई अड्डों पर सं 56. फायर निविदाओं की एयरफील्ड आपूर्ति	10/2012	217.60	244.10	12.18
	कोयला				
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	87.58
3	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	16.86
4	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	12.97
5	हिंगुला ओसी-II विस्तार चरण-III (15 एमटीवाई)	11/2008	479.53	479.63	0.02
	उर्वरक				
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ थ्रोम्बे	10/2014	197.79	209.44	5.89
	भारी उद्योग				
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
	पेट्रोरसायन				
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9965.00	82.49

	पेट्रोलियम				
1	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
2	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
3	मणिपुर, इम्फाल में पॉल डिपोट का निर्माण	08/2010	103.02	171.04	66.03
4	कोरबा में टॉप मार्केटिंग	01/2011	141.86	232.00	63.54
5	उरान चाकन/शिकरापुर एलपीजी पाइपलाइन	12/2009	309.81	462.79	49.38
	विद्युत				
1	तुरीअल हाइड्रो इलेक्ट्रिक परियोजना (60 मेवा.)	07/1998	368.72	1381.71	274.73
2	सुबनसिरी लोअर एचईपी(8X250 मेगावाट) एनएचपीसी	09/2003	6285.33	18063.89	187.40
3	कार्मेग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	147.51
4	त्रिपुरा गैर आधारित विद्युत परियोजना	07/2009	421.01	1007.57	139.32
5	रघुनाथपुर थर्मल पावर स्टेशन फेज-I	04/2007	4122.00	9606.82	133.06
	रेलवे				
1	गजोल-इटाहार सहित इकलाखी-बेलूरघाट से नई बीजी लाइन (एनएल) एनईएफआर	04/1983	36.80	1336.57	3531.98
2	बांकुड़ा - दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
3	ललितपुर-सतना-रीवा-सिंगरौली एनएल, (एनसीआर)	09/1998	247.66	3500.00	1313.23
4	अकोला-खंडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
5	बंगलोर - सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
	सड़क परिवहन एवं राजमार्ग				
1	पानीपत जालंधर 6 लेन,) 96 किमी . 387.1 किमी (.)	05/2009	1108.00	2288.00	106.50
2	अरुणाचल प्रदेश पैकेज के तहत अरुणाचल प्रदेश में यूपिया-एचओजे सेक्शन की दो लेनिंग (20.40किमी.)	12/2009	104.00	201.00	93.27
3	मैबंग से लुमडिंग, 83.400 किमी से 111.000 किमी	12/2003	199.81	385.13	92.75
4	मैबंग से लुमडिंग, (एस-24)	12/2003	155.04	280.13	80.68

	111.000 किमी से .126.450 किमी . -एनएच54				
5	अरुणाचल प्रदेश के तहत अरुणाचल प्रदेश में खोंसा-टीस्सा-लुम्डिंग (एनएच-52बी) (42.50 किमी.)	12/2011	156.63	276.00	76.21
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
3	कोचीन पोर्ट्स के बल्लापाड़म में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	66.82
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	5.66
इस्पात					
1	सिंटर मशीन की रिक्विजिटिंग - 1 और 2	12/2009	343.00	488.40	42.39
2	गुलबर्गा में मेडिकल कॉलेज और आस्पताल का निर्माण	05/2005	768.88	1070.97	39.29
3	प्रधानमंत्री ग्राम सड़क योजना चरण-VIII के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	206.71	17.79
4	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	175.94	17.50
5	प्रधानमंत्री ग्राम सड़क योजना चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	12.04
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53
2	बिहटा में आईआईटी पटना के आवास के लिए आवासीय और अन्य परिसरों	02/2012	171.10	202.00	18.06

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार है:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31-03-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	लागत वृद्धि (रु. करोड़)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर भाविनी), 500 मेगावाट (	09/2003	3492.00	5677.00	2185.00
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं 56. फायर निविदाओं की एयरफील्ड आपूर्ति	10/2012	217.60	244.10	26.50
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	227.17
3	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	70.65
4	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	55.82
5	हिंगुला ओसी-II विस्तार चरण-III (15 एमटीवाई)	11/2008	479.53	479.63	0.10
उर्वरक					
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ थोम्बे	10/2014	197.79	209.44	11.65
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोरसायन					
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9965.00	4504.39
पेट्रोलियम					
1	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00

2	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
3	बी-127 क्षेत्रों का एकीकृत विकास	12/2011	2059.63	2665.65	606.02
4	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	495.00
5	रिंग सागर सम्राट से मोबाइल ऑफशोर यूनिट का परिवर्तन (एमओपीएस)	03/2011	861.79	1256.72	394.93
विद्युत					
1	सुबानसिरी लोअर एच.ई.पी (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	18063.89	11778.56
2	बाढ़ एसटीपीपी (3X660मेवा.), एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	रघुनाथपुर थर्मल पावर स्टेशन चरण-	04/2007	4122.00	9606.82	5484.82
4	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) द्वितीय	09/2002	3919.59	8398.76	4479.17
5	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	3683.06
रेलवे					
1	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	2500.00	20000.00	17500.00
2	जिरीबाम इंफाल (तुपुई) (एनएल) (एनईएफआर)	04/2003	727.56	6570.75	5843.19
3	लुमडिंग-सिलचर जिरीबाम, बदरपुर-बरायग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
4	बोगीबिल और लिंक लाइन एनईएफआर में ब्रह्मपुत्र पुल	09/1997	1500.00	4996.19	3496.19
5	ललितपुर-सतना-रीवा-सिंगरौली एनएल, (एनसीआर)	09/1998	247.66	3500.00	3252.34
सड़क परिवहन एवं राजमार्ग					
1	पानीपत से जालंधर 6 लेन 96 किमी .387.1 किमी	05/2009	1108.00	2288.00	1180.00
2	मैबंग से लुमडिंग (एएस-25) 83.400 किमी से 111.000 किमी	12/2003	199.81	385.13	185.32
3	हरंगार्जों से मैबंग, एनएच-54	12/2003	196.00	331.23	135.23
4	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी से 126.450 किमी	12/2003	155.04	280.13	125.09

	-एनएच54				
5	एलडब्ल्यूई के तहत एनएच-202 पर सड़क पहुंच सहित वेनकटपुरम के समीप गोदवारी नदी पुल का निर्माण	03/2011	218.31	339.82	121.51
	पोत परिवहन एवं पत्तन				
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
3	कोचीन पोर्ट्स के बल्लापाड़म में आईसीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	164.16
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	13.83
	इस्पात				
1	गुलबर्गा में पैरामेडिकल और संबद्ध स्वास्थ्य संस्थान का निर्माण	05/2005	768.88	1070.97	302.09
2	सिंटर मशीन की रिवैम्पिंग - 1 और 2	12/2009	343.00	488.40	145.40
3	प्रधानमंत्री ग्राम सड़क योजना चरण-VIII के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	206.71	31.22
4	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	175.94	26.21
5	प्रधानमंत्री ग्राम सड़क योजना चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	24.39
	शहरी विकास				
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00
2	बिहटा में आईआईटी पटना के आवास के लिए आवासीय और अन्य परिसरों	02/2012	171.10	202.00	30.90

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 1076 परियोजनाओं में से, 6 परियोजनाएं समय से पहले चल रही हैं, 258 समय पर, 343 विलंबित तथा 241 परियोजनाएं लागत वृद्धि दर्शाती हैं तथा 83 परियोजनाएं समय तथा लागत वृद्धि दोनों दर्शाती हैं। तथापि, विलंबित परियोजनाओं की संख्या में 304 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है। इसके अलावा, 36 परियोजनाएं किसी आरंभ संबंधी तारीख के बिना स्वीकृत की गई हैं तथा 433 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है। 343 विलंबित परियोजनाओं में से, 65 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 62 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 146 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 70 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31-03-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत की तारीख	अनुमानित लागत की तारीख	समय वृद्धि (माह में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (आईएलएनपीसी)	12/2001	12/2008	05/2016	89
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर भाविनि), 500 एमडब्ल्यूई(	09/2003	09/2010	09/2016	72
3	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	12/2019	36
4	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	11/2018	35
नागर विमानन					
1	पाक्यांग सिक्किम हवाई अड्डे में नए हवाई अड्डे का निर्माण	01/2009	01/2011	09/2017	80
कोयला					
1	रामागुंडम ओसी-II विस्तार	12/2009	03/2012	03/2023	132
2	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	07/2012	03/2021	104
3	कुल्दा ओसीपी (महानदी कोलफील्ड्स लिमिटेड)	01/2005	03/2010	03/2017	84
4	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
5	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
स्वास्थ्य एवं परिवार कल्याण					

1	एम्स-रायबरेली-हाउसिंग	10/2013	11/2013	06/2016	31
2	एलजीबीआरआईएमएच तेजपुर-, असम	07/2012	12/2014	03/2016	15
3	सफदरजंग अस्पताल का पुनर्विकास और अदर्स -सुपर स्पेशियलिटी ब्लॉक	09/2013	12/2015	06/2016	6
4	सफदरजंग अस्पताल का पुनर्विकास और अन्य -इमरजेंसी ब्लॉक	11/2013	01/2016	04/2016	3
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
पेट्रोलियम					
1	कोच्ची-कूटनाइ बंगलौर मंगलौर पाइपलाइन परियोजना	06/2009	12/2012	02/2019	74
2	फुप्लुर-हल्दिया पाइपलाइन परियोजना चरण -I	07/2009	01/2013	12/2018	71
3	12 ऑफशोर सप्लाई वेसेल्स (ओएसवी) का निर्माण	06/2007	09/2011	10/2016	61
4	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना) भिलवाड़ा तथा चित्तौड़गढ़ के लिए	12/2009	06/2011	03/2016	57
5	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	04/2016	54
विद्युत					
1	तुरीअल हाइड्रो इलेक्ट्रिक प्रोजेक्ट (60मेवा.)	07/1998	07/2006	10/2016	123
2	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
3	कुडनकुलम एपीपी ट्रांस प्रणाली (पीजीसीआईएल)	05/2005	11/2008	12/2016	97
4	बाढ़ एसटीपीपी (3X660मेवा.), एनटीपीसी	02/2005	01/2011	05/2018	88
5	तीस्ता लो डैम एचईपी, स्टेज IV (4X40 मेगावाट) (एनएचपीसी)	09/2005	09/2009	09/2016	84
रेलवे					
1	गोंदिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
2	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	11/2002	12/2017	181
3	बांकुड़ा - दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	06/2005	12/2019	174

5	बेलापुर-सीवुड-उरान विद्युतीकृत डबल लाइन (एमटीपी)	03/1996	03/2004	03/2016	144
सड़क परिवहन एवं राजमार्ग					
1	बिजनी से असम/पश्चिम बंगाल सीमा चरण.II, 30.00 किमी. से 0.00 किमी., एनएच-31 सी	12/2003	06/2005	12/2016	138
2	हरंगाजो से मैबंग, 164.08 किमी.-190.587 किमी. एनएच-54	12/2003	09/2007	12/2016	111
3	आगरा-बाईपास (एन एस -1 / यूपी-1), एनएच 2,3	12/2003	09/2007	06/2016	105
4	नलबाड़ी से बिजनी (एएस-7)	12/2003	04/2008	01/2017	105
5	सोनापुर से गुवाहाटी (एएस -3)	12/2003	03/2008	07/2016	100
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे एफ/ओ स्पेशल पर्पस ब्लीकल (एसपीवी)	10/2002	03/2006	07/2016	124
2	कोचीन पोर्ट ट्रस्ट में बल्लापाइम में आईसीटीटी से रेल कनेक्टिविटी	03/2007	04/2009	08/2016	88
इस्पात					
1	भिलाई इस्पात प्लांट का विस्तार	08/2010	03/2013	11/2016	44
2	45एमवीए साफ के साथ अन्य एसोसिएटेड सुविधाओं का संग्रहण	12/2011	10/2013	06/2016	32
3	गुलबर्गा में चिकित्सा कॉलेज और अस्पताल का निर्माण	05/2005	02/2014	03/2016	25
4	बागमती का कार्य इरीगेशन	10/2005	03/2015	03/2017	24
5	एसएमएस-1 कन्वर्टर्स रिवैम्पिंग	05/2012	07/2015	06/2017	23
दूरसंचार					
1	इंटेलिजेंट फाइबर ऑप्टिक सी के पैकेज एफ तथा जी भाग ख स्पेक्ट्रम (एनएफएस) ओएफसी लेयिंग प्रोजेक्ट के लिए नेटवर्क	09/2014	09/2014	03/2017	30
2	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	03/2017	20
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	06/2011	06/2016	60
2	नागपुर महाराष्ट्र में राष्ट्रीय फायर कॉलेज का उन्नयन	06/2010	03/2012	03/2017	60
3	हरिघंटा कल्याणी पश्चिम बंगाल में आईआईएसईआर कोलकाता के अकादमी सह स्थायीआवासीय परिसर का निर्माण	01/2009	06/2012	05/2016	47

1	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	1105.78	10/2011	04/2016
2	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1459.15	01/2012	05/2016
3	एन्नोर में नई विपणन टर्मिनल	11/2006	171.83	171.83	0.00	उ.न.	उ.न.
4	12 ऑफशोर आपूर्ति वेसेल वेजेल्स का निर्माण	06/2007	736.65	736.65	514.33	09/2011	10/2016
5	छः पाइपलाइन रिप्लेसमेंट परियोजना	03/2009	181.02	173.28	78.73	01/2017	01/2017
विद्युत							
1	सुबनसिरी लोअर एच.ई.पी 8x 250मेवा (एनएचपीसी)	09/2003	6285.33	18063.89	8357.64	09/2010	उ.न.
2	उत्तर में फाइबर ऑप्टिक संचार की स्थापना	03/2012	198.63	198.63	104.63	09/2014	06/2016
3	यूआरटीडीएसएम चरण-I	01/2014	374.63	374.63	17.20	04/2016	11/2016
4	पकल दुल हाइड्रो इलेक्ट्रिक परियोजना (1000 मेवा.)	10/2014	8112.12	8112.12	121.97	04/2020	03/2022
5	फाइबर ऑप्टिक विस्तार परियोजना के तहत एनआर में संचार प्रणाली	03/2015	197.40	197.40	0.00	03/2018	03/2018
रेलवे							
1	हावड़ा-अमटा-चंपादंगा एनएल (एसईआर)	04/1974	393.46	154.46		03/2007	उ.न.
2	नांगल बांध-तलवाड़ा (एनएल), एन.आर.	03/1981	450.00	2100.00	391.95	07/2012	उ.न.
3	एकलाखी-बलूरघाट सहित जी से नई बीजी रेलवे लाइन	04/1983	36.80	1336.57	255.55	उ.न.	03/2019
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	गुना-इटावा के माध्यम से शिवपुरी-ग्वालियर -भिंड एनएल, (एनसीआर)	04/1986	158.77	608.02	602.10	03/1994	03/2015
सड़क परिवहन एवं राजमार्ग							
1	"मधुगिरी-माल्वागल (400.330 किमी. से 483.151) - एलओटी-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	अनिशाबाद-औरंगाबाद-हरिनगंज (0.000 किमी.	01/1991	282.41	282.41	0.00	08/2016	08/2016

	से 62.000 किमी.)- एलओटी						
3	अनिशाबाद-औरंगाबाद- हरिनगंज (62.000 किमी. से 154.625 किमी.)-	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	बख्तियारपुर-मोकामा	01/1991	1167.45	1167.45	0.00	उ.न.	उ.न.
5	बंकुरा-पारुलिया (0.000 किमी. से 84.000 किमी.)	01/1991	322.00	322.00	0.00	03/2018	03/2018
पोत परिवहन एवं पत्तन							
1	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	525.49	03/2006	07/2016
2	सेतुसमुंद्रम शिप चैनल प्रोजेक्ट	06/2005	2427.40	2427.40	841.02	10/2008	उ.न.
3	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	415.80	12/2010	01/2016
4	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल कनक्टिविटी	03/2007	245.67	409.83	366.20	04/2009	08/2016
5	कामराजार पोर्ट लिमिटेड मे कोयला बर्थ-4 के निर्माण	09/2015	210.00	210.00	0.00	01/2018	01/2018
इस्पात							
1	गुलबर्गा में मेडिकल कॉलेज एवं अस्पताल	05/2005	768.88	1070.97	1070.97	02/2014	03/2016
2	बागमती का इरिगेशन कार्य	10/2005	956.00	956.00	0.00	03/2015	03/2017
3	ग्रामीण सड़क का प्रबंध एवं निर्माण	03/2007	149.73	175.94	177.06	12/2015	03/2017
4	ग्रामीण सड़क का प्रबंध एवं निर्माण	12/2007	202.61	227.00	197.59	12/2016	12/2016
5	गिरीडीह में रोड एवं पुल का निर्माण, कोडरमा	12/2007	200.00	200.00	131.15	03/2018	03/2018
दूरसंचार							
1	नेटवर्क के लिए स्पेक्ट्रम	03/2012	13334.00	13334.00	196.20	07/2015	03/2017
शहरी विकास							
1	सेवरेज परियोजना	08/2007	246.90	246.90	0.00	उ.न.	उ.न.

2	संसदीय सौध संसद भवन परिसर में भवन के विस्तार हेतु निर्माण कार्य	05/2009	261.85	261.85	183.26	05/2013	06/2016
3	एनआईटी कालीकट केरल के लिए मेगा होस्टल II का निर्माण	01/2010	165.23	165.23	0.00	10/2012	उ.न.

एन.ए. : उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानों वाली शुरूआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-03-2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	संशोधित लागत (रु. करोड़)	संचयी व्यय (रु. करोड़)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	21304.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी 500 एमडब्ल्यूई)	09/2003	3492.00	0.00	5187.55
नागर विमानन					
1	पाक्यांग (सिक्किम) में नए हवाई अड्डा का निर्माण	01/2009	309.46	0.00	424.30
कोयला					
1	कुल्दा ओसीपी (महानदी कोल फील्ड लिमिटेड)	01/2005	302.96	0.00	303.14
2	अनंता ओसी एक्सपेंशन चरण -III (15.0 एमटीवाई)	08/2008	207.28	0.00	207.71
3	रामगुंडम ओसी -II विस्तार	12/2009	418.97	0.00	475.38
4	अद्वियाला शाफ्ट परियोजना	12/2009	212.34	0.00	872.21
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	8920.00	9356.28
पेट्रोलियम					

1	इम्फाल, मणिपुर में पोल डिपोट का निर्माण	08/2010	103.02	0.00	114.42
2	कोरबा में टॉप मार्केटिंग	01/2011	141.86	0.00	174.38
विद्युत					
1	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	0.00	5548.25
2	सुबनसिरी लोअर एचईपी (8X250 मेवा) (एनएचपीसी)	09/2003	6285.33	0.00	8357.64
3	तीस्ता लो डैम एचईपी, चरण-IV (4X40 मेवा.) (एनएचपीसी)	09/2005	1061.38	0.00	2011.96
4	बीआरबीसीएल-नबीनगर टीपीपी- जेवी (4X250 मेवा.)	01/2007	5353.00	0.00	5472.83
5	किशनगंगा एचईपी (3X110 मेवा.)	01/2009	3642.04	0.00	4490.39
रेलवे					
1	गजोल-इटाहार (एनएल) सहित इकलाखी-बेलूरघाट से नई बीजी रेलवे लाइन, एनईएफआर	04/1983	36.80	36.38	255.55
2	विरमगम-भिल्डी (डब्ल्यू आर(, जीसी	04/1990	155.66	0.00	201.26
3	पेड़ापल्ली-करिमनगर-निजामाबाद एनएल, (एससीआर)	12/1994	124.43	0.00	712.02
4	उधमपुर (बारामूला (एनएल-श्रीनगर-, एनआर	03/1995	2500.00	0.00	10722.72
5	कुट्टक-बैरंग (एलडी)	04/1995	127.13	0.00	193.37
सड़क परिवहन एवं राजमार्ग					
1	गुवाहाटी से नलबारी (एएस-5)	12/2003	198.16	0.00	242.40
2	नलबारी से बिजनी (एएस -6)	12/2003	225.00	0.00	311.13
3	नलबारी से बिजनी (एएस -7)	12/2003	208.00	230.00	295.20
4	फोरबेसगंज से सिमराही (एनएच-57)(एनएचएआई)	12/2003	332.94	0.00	497.20
5	आगरा-बाड़पास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	348.16	0.00	362.77
पोत परिवहन एवं पत्तन					
1	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	0.00	415.80
इस्पात					
1	गुलबर्गा में चिकित्सा कॉलेज और अस्पताल का निर्माण	05/2005	768.88	1060.00	1070.97
2	प्रधानमंत्री ग्राम सड़क योजना के तहत ग्रामीण सड़क का निर्माण तथा प्रबंधन	03/2007	149.73	173.00	177.06
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	0.00	12712.23

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-03-2016 की स्थिति के अनुसार)

क्र.सं.	सेक्टर/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	उ.न.	03/2015
2	विभिन्न हवाई अड्डों पर 56 एनओएस एयरफील्ड फायर टैंडर की सप्लाई	10/2012	03/2015	उ.न.	09/2015
कोयला					
1	जल्लाराम शाफ्ट परियोजना	09/2007	03/2013	उ.न.	उ.न.
स्वास्थ्य एवं परिवार कल्याण					
1	एलएचएमसी नई दिल्ली पुनः-विकास	02/2013	11/2013	उ.न.	11/2014
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2013	12/2015
पेट्रोलियम					
1	एन्नोर में नई मार्केटिंग टर्मिनल	11/2006	उ.न.	उ.न.	उ.न.
2	2000 एचपी की 2 एनओएस ड्रिलिंग रिग की खरीद	04/2010	06/2012	उ.न.	01/2016
3	एक ईटीपी और तीन ईटीपी सह वाटर इंजेक्शन संयंत्रों का निर्माण (डब्ल्यूआईपी)	06/2010	01/2014	उ.न.	उ.न.
4	एन्नोर-त्रिची-मदुरै एलपीजी पाइपलाइन	05/2013	उ.न.	उ.न.	उ.न.
5	पटना और मुजफ्फरपुर तक पारादीप-हल्दिया-दुर्गापुर एलपीजी पाइपलाइन और आईटीएस विस्तार का उन्नयन	01/2015	उ.न.	उ.न.	उ.न.
विद्युत					
1	सुबनसिरी लोअर एचईपी (8X250 मेवा.)	09/2003	09/2010	उ.न.	उ.न.

	(एनएचपीसी)				
2	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	07/2013	01/2016	01/2016
3	आन्ध्रप्रदेश भाग-क1 के बीमागिरि क्षेत्र में आईएसजीएस परियोजनाओं से संबंधित सामान्य प्रणाली	03/2012	06/2014	उ.न.	उ.न.
रेलवे					
1	हावड़ा-अमटा-चंपादंगा एनएल (एसईआर)	04/1974	03/2007	03/2007	उ.न.
2	ननगलडम-तालवारा (एनएल) एनआर	03/1981	07/2012	उ.न.	उ.न.
3	गुना-इटावा वाया शिवपुरी-ग्वालियर-भिंड एनएल, एनसीआर	04/1986	03/1994	उ.न.	03/2015
4	नामखाना-चंद्रनगर, काकद्वीप-बुदाखली और चंद्र नाग के लिए लक्ष्मीकांतपुर-नामखाना के बाद एमएम	04/1987	उ.न.	उ.न.	उ.न.
5	बिरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	उ.न.	03/2010	उ.न.
सड़क परिवहन एवं राजमार्ग					
1	एनएच 66 के टिंडीवनम अनुभाग के लिए पांडिचेरी	01/1991	01/2008	उ.न.	उ.न.
2	पुनर्वास और 2 लाइन्स -2 पेव्ड शोल्डर विन्यास और मजबूत बनाने ओ के साथ लेन करने के लिए उन्नयन	01/1991	04/2014	उ.न.	उ.न.
3	पेव्ड शोल्डर के साथ 2 लेन का उन्नयन तथा पुनर्विकास, बिरपुर-बिहपुर के विन्यास तथा सुदृढीकरण,	01/1991	उ.न.	उ.न.	उ.न.
4	ईपीसी आधार पर एनएच 52 की नगांव बाईपास की सीमा से रांगगारा तक 4 लेनिंग (182.00 किमी से 208.00 किमी.)	01/1991	उ.न.	उ.न.	उ.न.
5	भोजपुर से बक्सर का चार लेनिंग	01/1991	उ.न.	उ.न.	उ.न.
पोत परिवहन एवं पत्तन					
1	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	उ.न.	उ.न.
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	12/2010	उ.न.	01/2016
इस्पात					
1	7.0 एमटीपीए कुमारस्वामी लौह अयस्क खदान परियोजना (एनएमडीसी)	02/2011	05/2013	01/2015	08/2015
2	1.2 एमटीपीए पेलेट संयंत्र परियोजना, डोनिमलई (एनएमडीसी)	04/2011	04/2013	09/2014	06/2015
3	राजीव गांधी के अंतर्गत इनडोर खेल हॉल	07/2014	01/1999	उ.न.	उ.न.

	के लिए तेलंगाना में 123 ब्लॉकों तथा आंध्र प्रदेश में 167 ब्लॉकों का निर्माण				
शहरी विकास					
1	मूसी के दक्षिण पर पुरानी शहरी क्षेत्र में सीवरेज प्रणाली को मजबूत बनाना तथा पुनर्वास (2 जोन में)	08/2007	उ.न.	उ.न.	उ.न.
2	एनआईटी कालीकट केरल के लिए मेगा छात्रावास द्वितीय का निर्माण	01/2010	10/2012	उ.न.	उ.न.
3	प्लॉट नं. सी- 41-43 जी ब्लॉक बांद्रा इंकम टैक्स विभाग का लिए कार्यालय भवन	02/2011	11/2014	उ.न.	उ.न.
4	बिहटा में पटना के अंतर्गत बिहार राज्य में राज्य राजमार्गों का विकास	02/2012	09/2014	07/2015	07/2015
5	प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	उ.न.	उ.न.

एनए: उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार कार्य शुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

i) **सड़क परिवहन एवं राजमार्ग क्षेत्र में,** 414 परियोजनाओं में से, 126 परियोजनाएं विलंबित हैं । माह के दौरान 27 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 27 परियोजनाओं में से 4 मेगा परियोजनाएं हैं । एक परियोजना 'कोटा बाइपास, आरजे-4, एनएच-76, एनएचएआई', के संबंध में वन संबंधी अनुमति तथा रेलवे से अनुमति में विलंब होने के कारण 1 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । एक परियोजना 'किशनगढ़-अजमेर-बिवार, एनएचएआई' के संबंध में निर्माण के चरण में धीमी प्रगति होने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । दो परियोजनाएँ 'गंगा पुल से रामदेवी क्रॉसिंग चरण-II एनएच-25, 75 किमी-80.06 किमी, एनएचएआई तथा 'दिल्ली /हरियाना सीमा से रोहत, एनएचएआई' के संबंध में ठेकेदार द्वारा धीमी प्रगति तथा परियोजना कार्मिक प्रबंधन में निरंतर व्यतियान के कारण प्रत्येक में 3 माह तथा 4 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । दो परियोजनाएँ 'पानीपत -जलंधर 6 लाइन (96 किमी से 387.1 किमी, एनएचएआई ' तथा 'पनवेल-इंदापूर ,एनएचएआई' के संबंध में क्रमशः ठेकेदार के कम निष्पादन तथा ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना के कारण क्रमशः 6 माह तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । एक परियोजना 'पिंपलगांव-नासिक-गोंडे, एनएच-3 (एनएचडीपी-चरण-III), एनएचएआई' के संबंध में वृक्षों को काटने पर न्यायालय संबंधी विधियों तथा लोक संघर्ष के कारण 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । पांच परियोजनाएं 'फोरबेसगंज से सिमराही (एनएच-57) एनएचएआई', 'मोकामा-मुंगेर की दो लेनिंग करना, एनएचएआई', 'जयपुर-रिंगस,

एनएचएआई 'एनएच-232 के रायबरेली-बांदा सेक्शन के पेव्ड शोल्डर की दो लेनिंग, एनएचएआई' और 'गोमती चौराहा-उदयपुर का चार लेनिंग, डीओआरटीएच' प्रत्येक में 1 माह के अतिरिक्त विलंब हुआ है; एक परियोजना 'हरिद्वार देहरादून अनुमोदित लंबाई 69 किमी., एनएचएआई' के संबंध में 2 माह का विलंब हुआ है, आठ परियोजनाएं "नलवारी से बिजनी (एएस-6), एनएचएआई', 'आगरा वाइपास (एनएस-5.1/यूपी-1) एनएच-2,3, एनएचएआई', मुरादाबाद-बरेली, एनएचएआई', 'रोहतक-बबाल, एनएचएआई', 'खागड़िया-पूर्णिया पीएस के साथ दो लेनिंग, एनएचएआई', 'पटना-बख्तियारपुर के किमी. 181.3 से 231.95 किमी., एनएचएआई', 'मुजफ्फरपुर-सोनवर्षा के दो लेनिंग, एनएचएआई' और 'बीवरपाली पिंडवारा, एनएचएआई' में प्रत्येक में 3 माह के अतिरिक्त विलंब हुआ है; दो परियोजनाओं 'गुडगांव-कोटपुतली-जयपुर (छ: लेन:), डीओआरटीएच' और 'लुधियाना-तलवंडी अनुभाग में चार लेनिंग, एनएचएआई' में प्रत्येक में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'देवली-कोटा, एनएचएआई' और 'मोतिहारी-रक्सौल पीएस के साथ दो लेनिंग, एनएचएआई' के संबंध में क्रमशः 8 माह और 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है और दो परियोजनाएं 'एनएच-52 के विश्वनाथचरियाली से गोहपुर 208 किमी. से 264.10 किमी. तक की चार लेनिंग, एनएचआईडीसीएल' और 'अंबाला-कैथल-पैकेज 1 की चार लेनिंग, एनएचएआई' के संबंध में क्रमशः 10 माह और 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

ii) **विद्युत क्षेत्र में**, 111 परियोजनाओं में से, 64 परियोजनाएं विलंबित हैं । माह के दौरान 11 परियोजनाओं के संबंध में 1-9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 11 परियोजनाओं में से 7 परियोजनाएं मेगा परियोजनाएं हैं । एक परियोजना 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण स्कीम-XIX, पीजीसीआईएल' में भूमि अधिग्रहण में विलंब के कारण 1 माह के अतिरिक्त विलंब हुआ है; तीन परियोजनाएं ' उत्तरी क्षेत्र ट्रांसमिशन सुदृढीकरण स्कीम, पीजीसीआईएल', 'मौडा चरण-II के साथ जुड़े ट्रांसमिशन प्रणाली', 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण स्कीम-XXI, पीजीसीआईएल' 'झारखंड तथा पश्चिम बंगाल भाग-क2 में चरण-I जेनरेशन परियोजनाओं के लिए ट्रांसमिशन प्रणाली' में किसान आंदोलन और जेनरेशन परियोजनाओं में विलंब के कारण प्रत्येक में 2 माह का अतिरिक्त विलंब हुआ है; दो परियोजनाओं 'कोस्टल एनर्जनप्राइवेट लिमिटेड और इंद-बराथ पावर (मद्रास) लिमिटेड के साथ जुड़े सामान्य प्रणाली, पीजीसीआईएल' और 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण स्कीम-XXVIII, पीजीसीआईएल' में कठोर आरओडब्ल्यू समस्या और शटडाउन की अनुपलब्धता के कारण प्रत्येक में 3 माह का अतिरिक्त विलंब हुआ है; एक परियोजना 'पूर्वी क्षेत्र सुदृढीकरण स्कीम-V, पीजीसीआईएल' में भूमि अधिग्रहण में विलंब के कारण 3 माह का अतिरिक्त विलंब हुआ है; दो परियोजनाएं 'तपोवन-विष्णुगढ़ एचईपी (4X130 मेवा.) एनटीपीसी' और 'दक्षिणी क्षेत्र-XIV का प्रणाली सुदृढीकरण, पीजीसीआईएल' में क्रमशः कार्यकारी एजेंसी द्वारा सिविल कार्यों में विलंब और आरओडब्ल्यू समस्याओं के कारण क्रमशः 6 माह और 9 माह का अतिरिक्त विलंब हुआ है ।

(iii) **पेट्रोलियम क्षेत्र में**, 68 परियोजनाओं में से 38 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 1-13 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 7 परियोजनाओं में से 3 मेगा परियोजनाएं हैं; दो परियोजनाएं 'मैंगलूर में सामरिक कच्चा तेल भंडारण परियोजना, आईएसपीआरएल' तथा 'पारादीप हलदिया दुर्गापूर एलपीजी पाइपलाइन, आईओसीएल' में आरओडब्ल्यू

समस्याओं और वन अनुमति के कारण क्रमशः 1 माह तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'रिंग सागर सम्राट से मोबाइल ऑफशोर उत्पादन यूनिट (एमओपीएस) का रूपांतरण, ओएनजीसी' और 'पाइपलाइन प्रतिस्थापन परियोजना, अहमदाबाद, ओएनजीसी' में क्रमशः इस्पात प्राप्ति में विलंब और धीमी गति से निर्माण में विलंब के कारण क्रमशः 8 माह तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; एक परियोजना 'मधुवन में निर्जलीकरण सुविधाएं और प्रवाह उपचार संयंत्र के साथ माध्यमिक टैंक फार्म, ओआईएल' में कोर्ट केस के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है और दो परियोजनाएं 'बी-127 क्षेत्रों का एकीकृत विकास, ओएनजीसी' और 'एमएच दक्षिण क्षेत्र के पश्चिमी घेरे का विकास, ओएनजीसी' के संबंध में प्रत्येक में ठेकेदारों के कम निष्पादन के कारण प्रत्येक में 13 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(iv) **कोयला क्षेत्र में**, 88 परियोजनाओं में से 42 परियोजनाएं विलंबित हैं । माह के दौरान 7 परियोजनाओं के संबंध में 1-60 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । दो परियोजनाएं "विंड पावर परियोजना, काजहुप नीरकुलम, तमिलनाडु, एनएलसी" और 'मुराड्डीह यूजी टर्न-की परियोजना, बीसीसीएल' में क्रमशः सिविल कार्यों में विलंब और पर्यावरण संबंधी अनुमति में विलंब का कारण क्रमशः 1 माह तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड), एमसीएल' और 'पूर्णडीह ओसीपी (3.0 एमटीवाई) सीसीएल' कोयला निकासी समस्या और भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 12 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'कल्याणीखानी ओपनकास्ट परियोजना, एससीसीएल' और 'झांझरा संयुक्त पीआर (3.50 एमटीवाई), ईसीएल' भूमि अधिग्रहण में विलंब के कारण और परियोजना में डिबोटेलिंग के कारण क्रमशः 24 माह तथा 60 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है और एक परियोजना 'आरकेपी ओसीपी, चरण-I, एससीसीएल' में 12 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

v) **शहरी विकास क्षेत्र में**, 31 परियोजनाओं में से, 13 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'पातालगंगा रसायनी जिल्ला रायगढ़ में एनआईएसएम आवास के निर्माण ,सीपीडब्लूडी 'के संबंध में 1 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । 12 परियोजनाएँ 'आईआईएम के लिए सी/ओ स्थिर आवास के चरण 1 , सीपीडब्लूडी' तथा धनपाद आईएसएम में (1000 डबल बेडेड रूम) 2000 बाल छात्रवास, सीपीडब्लूडी' के संबंध में 4 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) **स्वास्थ्य एवं परिवार कल्याण क्षेत्र में**, 9 परियोजनाओं में से, 4 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'सफदरजंग हॉस्पिटल विकास और अन्य- सुपर स्पेशलिटी ब्लॉक, एचएससीसी' में निधि की कमी होने के कारण 3 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(vii) **पोत परिवहन तथा पतन क्षेत्र में**, 8 परियोजनाओं में से, 2 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना 'एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी) पोर्ट ट्रस्ट' में फिशिंग स्टोलों के स्थानांतरण के कारण 4 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है।

12. रेल मंत्रालय ने 1 जनवरी, 2015 से इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी जारी परियोजनाओं पर मासिक स्थिति रिपोर्टें प्रस्तुत करने की परंपरा को **समाप्त** कर दिया है। रेल मंत्रालय ने अपनी 20 परियोजनाओं के संबंध में नवीनतम जानकारी प्रदान की है, केवल इन्हीं परियोजनाओं को सां. और कार्य. कार्या. मंत्रालय स्तर पर निगरानी के लिए पहचान किया गया है। अतः उपलब्ध सूचना/आंकड़े का (जनवरी 2015 की स्थिति के अनुसार) रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में उपयोग किया गया है।

13. दिनांक 31.03.2016 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

14. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for March 2016 contains information on the status of the 1076 Central Sector Infrastructure Projects costing ₹150 crore and above. During March 2016, 2 projects (1 project each in Steel and Petroleum sector) have reported completion.

2. During the reference month, out of 1076 projects, 343 projects are delayed with respect to their original schedules and 57 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 57 projects, 14 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	414	126	27	4
2	RAILWAYS	298	31	0	0
3	POWER	111	64	11	7
4	COAL	88	42	7	0
5	PETROLEUM	68	38	7	3
6	STEEL	33	15	0	0
7	URBAN DEVELOPMENT	31	13	3	0
8	HEALTH AND FAMILY WELFARE	9	4	1	0
9	SHIPPING AND PORTS	8	2	1	0
10	CIVIL AVIATION	4	1	0	0
11	ATOMIC ENERGY	4	4	0	0
12	MINES	3	0	0	0
13	TELECOMMUNICATIONS	2	2	0	0
14	FERTILISERS	1	0	0	0
15	PETROCHEMICALS	1	0	0	0
16	HEAVY INDUSTRIES	1	1	0	0
Total		1076	343	57	14

3. Total original cost of implementation of the 1076 projects was ₹12,38,517.07 crore and their anticipated completion cost is likely to be ₹13,93,627.86 crore, which reflects overall cost overruns of ₹1,55,110.79 crore (12.52% of original cost). The expenditure incurred on these projects till March 2016 is ₹5,75,677.42 crore, which is 41.31% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-03-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	16.86
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
5	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.02
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	82.49
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
3	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR	08/2010	103.02	171.04	66.03
4	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
5	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	12/2009	309.81	462.79	49.38
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	187.40
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
4	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.57	139.32
5	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	133.06
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
2	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
3	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	3500.00	1313.23
4	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
5	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
2	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75

4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
5	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	156.63	276.00	76.21
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	66.82
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	5.66
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	39.29
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	17.79
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	17.50
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53
2	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	202.00	18.06

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 31-03-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	70.65
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
5	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.10
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEAVY INDUSTRY					

1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	2109.30
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	4504.39
	PETROLEUM				
1	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
3	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	495.00
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	394.93
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	11778.56
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	5484.82
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.76	4479.17
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	3683.06
	RAILWAYS				
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	20000.00	17500.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
4	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	3500.00	3252.34
	ROAD TRANSPORT AND HIGHWAYS				
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
3	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
5	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	121.51
	SHIPPING AND PORTS				
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	164.16
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	13.83
	STEEL				
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	302.09
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	31.22

4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	26.21
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00
2	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	202.00	30.90

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1076 projects, 6 projects are ahead of schedule, 258 are on schedule, 343 are delayed, 241 projects reported cost overrun and 83 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 304 if delay is calculated on the basis of latest schedule of completion. Further, 36 projects have been sanctioned without original commissioning date and for 433 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 343 delayed projects, 65 projects have overall delay in the range of 1 to 12 months, 62 projects have delay in the range of 13 to 24 months, 146 projects have delay in the range of 25 to 60 months and 70 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 31-03-2016)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	05/2016	89
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	12/2019	36
4	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11/2018	35
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
COAL					
1	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
2	MAGADH OC 20 MTY (CCL)	08/2008	07/2012	03/2021	104
3	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
4	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
5	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
HEALTH AND FAMILY WELFARE					
1	AIIMS-RAEBARELI-HOUSING	10/2013	11/2013	06/2016	31
2	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	03/2016	15
3	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	12/2015	06/2016	6
4	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	01/2016	04/2016	3
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	12/2017	75

	PETROLEUM				
1	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	06/2009	12/2012	02/2019	74
2	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
3	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	10/2016	61
4	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	04/2016	54
	POWER				
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2016	97
4	BARH STPP(3X660MW) NTPC	02/2005	01/2011	05/2018	88
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	09/2009	09/2016	84
	RAILWAYS				
1	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2017	181
3	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
5	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2016	144
	ROAD TRANSPORT AND HIGHWAYS				
1	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2016	138
2	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	09/2007	12/2016	111
3	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	06/2016	105
4	NALBARI T BIJNI (AS-7)	12/2003	04/2008	01/2017	105
5	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	07/2016	100
	SHIPPING AND PORTS				
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	07/2016	124
2	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	08/2016	88
	STEEL				
1	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	11/2016	44
2	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	06/2016	32
3	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	03/2016	25
4	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2017	24
5	SMS-1 CONVERTERS REVAMPING	05/2012	07/2015	06/2017	23
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	09/2014	09/2014	03/2017	30
2	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2017	20
	URBAN DEVELOPMENT				
1	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	06/2016	60
2	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	03/2017	60
3	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	05/2016	47
4	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	06/2016	37

5	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	12/2014	03/2017	27
---	---	---------	---------	---------	----

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during March 2016, out of 1076 projects, 241 projects reported cost overruns and 343 projects reported time overruns. In comparison to April 2015, number of **projects** reporting **cost overruns** has gone **down** from **30.47%** to **22.40%** whereas **projects** reporting **time overruns** have **decreased** from **42.61%** to **31.88%**.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-03-2016)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIR	01/2009	309.46	309.46	424.30	01/2011	09/2017
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	318.00	305.60	05/2012	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	30.74	03/2015	09/2015
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRP	10/2013	314.61	314.61	24.09	09/2018	09/2018
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	67.25	12/2019	12/2019
2	HADLA LIGNITE MINE	03/2015	522.45	522.45	2.56	09/2019	09/2019

	PROJECT(1.90 MTPA)						
3	KOC III	10/2015	426.79	426.79	0.00	03/2018	03/2018
4	MADANNAGAR OCP	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
FERTILISERS							
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	56.41	11/2016	11/2016
HEALTH AND FAMILY WELFARE							
1	LGBRIMH	07/2012	175.57	175.57	113.50	12/2014	03/2016
2	LHMC -HOSPITAL	02/2013	414.11	414.11	210.91	11/2013	11/2014
3	SAFDARJUNG SSB	09/2013	444.70	444.70	285.20	12/2015	06/2016
4	RAEBARELI-HOUSING	10/2013	159.50	159.50	120.80	11/2013	06/2016
5	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	196.70	165.97	01/2016	04/2016
MINES							
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1856.00	2.02	09/2017	09/2017
2	WPPMH	12/2015	355.13	355.13	107.67	11/2016	11/2016
3	WPPRJ	12/2015	344.50	344.50	126.21	11/2016	11/2016
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	1105.78	10/2011	04/2016
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1459.15	01/2012	05/2016
3	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	171.83	0.00	N.A.	N.A.
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	514.33	09/2011	10/2016
5	SIX PIPELINE REPLACEMENT PROJECT	03/2009	181.02	173.28	78.73	01/2017	01/2017
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	8357.64	09/2010	N.A.
2	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER	03/2012	198.63	198.63	104.63	09/2014	06/2016
3	URTDSM PHASE-I	01/2014	374.63	374.63	17.20	04/2016	11/2016
4	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	121.97	04/2020	03/2022
5	COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJE	03/2015	197.40	197.40	0.00	03/2018	03/2018
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	154.46		03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	391.95	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING G	04/1983	36.80	1336.57	255.55	N.A.	03/2019
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	1428.00	466.36	06/2005	12/2019

5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	602.10	03/1994	03/2015
ROAD TRANSPORT AND HIGHWAYS							
1	"MADHUGIRI-MULBAGAL (KM 400.330 TO KM 483.151) - LOT-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	ANISABAD-AURANGABAD-HARIHARGANJ (KM 0.000 TO KM 62.000)-LOT	01/1991	282.41	282.41	0.00	08/2016	08/2016
3	ANISABAD-AURANGABAD-HARIHARGANJ (KM 62.000 TO KM 154.625) -	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	BAKHTIYARPUR - MOKAMA	01/1991	1167.45	1167.45	0.00	N.A.	N.A.
5	BANKUARA- PURULIA (KM 0.000 TO KM 84.000)	01/1991	322.00	322.00	0.00	03/2018	03/2018
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI	10/2002	150.00	600.00	525.49	03/2006	07/2016
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	841.02	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF	01/2007	366.39	669.46	415.80	12/2010	01/2016
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	409.83	366.20	04/2009	08/2016
5	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED	09/2015	210.00	210.00	0.00	01/2018	01/2018
STEEL							
1	MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1070.97	02/2014	03/2016
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	0.00	03/2015	03/2017
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER	03/2007	149.73	175.94	177.06	12/2015	03/2017
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER	12/2007	202.61	227.00	197.59	12/2016	12/2016
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERM	12/2007	200.00	200.00	131.15	03/2018	03/2018
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	13334.00	196.20	07/2015	03/2017
URBAN DEVELOPMENT							
1	SEWEWRAGE PROJECT	08/2007	246.90	246.90	0.00	N.A.	N.A.
2	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEX	05/2009	261.85	261.85	183.26	05/2013	06/2016
3	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KER	01/2010	165.23	165.23	0.00	10/2012	N.A.

4	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHA	06/2010	205.00	191.97	0.00	03/2012	03/2017
5	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-4	02/2011	241.33	241.33	87.13	11/2014	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-03-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	21304.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5187.55
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	424.30
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	302.96	0.00	303.14
2	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	207.71
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	0.00	475.38
4	ADRIYALA SHAFT PROJECT	12/2009	212.34	0.00	872.21
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	8920.00	9356.28
PETROLEUM					
1	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR	08/2010	103.02	0.00	114.42
2	MARKETING TOP AT KORBA	01/2011	141.86	0.00	174.38
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5548.25
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	8357.64
3	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	2011.96
4	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	5472.83
5	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	4490.39
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	36.38	255.55
2	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	0.00	201.26
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	0.00	712.02
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	0.00	10722.72
5	CUTTACK - BARANG (LD)	04/1995	127.13	0.00	193.37
ROAD TRANSPORT AND HIGHWAYS					
1	GUWAHATI TO NALBARI (AS-5)	12/2003	198.16	0.00	242.40

2	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	311.13
3	NALBARI T BIJNI (AS-7)	12/2003	208.00	230.00	295.20
4	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	12/2003	332.94	0.00	497.20
5	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	348.16	0.00	362.77
SHIPPING AND PORTS					
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	415.80
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	1070.97
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	177.06
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	0.00	12712.23

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31-03-2016)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	N.A.	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015
COAL					
1	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2013	12/2015
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.
2	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	04/2010	06/2012	N.A.	01/2016
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.A.	N.A.	N.A.
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	N.A.	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	01/2016	01/2016
3	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.A.	N.A.

	RAILWAYS				
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	03/1994	N.A.	03/2015
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.A.	03/2010	N.A.
	ROAD TRANSPORT AND HIGHWAYS				
1	PONDICHERRY TO TINDIVANAM SECTION OF NH-66	01/1991	01/2008	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
4	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	N.A.	N.A.	N.A.
5	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	N.A.	N.A.	N.A.
	SHIPPING AND PORTS				
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	N.A.	01/2016
	STEEL				
1	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	01/2015	08/2015
2	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	04/2011	04/2013	09/2014	06/2015
3	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA	07/2014	01/1999	N.A.	N.A.
	URBAN DEVELOPMENT				
1	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
2	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
3	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	11/2014	N.A.	N.A.
4	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	09/2014	07/2015	07/2015
5	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Road Transport & Highways Sector**, out of 414 projects, 126 projects are delayed. During the month, 27 projects have reported additional delay in the range of 1-24 months. Out of 27 projects, 4 projects are mega projects. One project 'Kota Bypass, RJ-4, NH-76, NHAI' has reported additional delay of 1 month due to forest clearance and delay in approval from Railways; one project 'Kishangarh-Ajmer-Beawer, NHAI' has reported additional delay of 1 month due to slow progress in construction phase; two projects 'Ganga Bridge to Ramdevi Crossing PH.II NH-25, KM.75-80.06, NHAI' and 'Delhi/Haryana Border to Rohtak, NHAI' have additional delay of 3 months and 4 months respectively due to slow progress by contractor and frequent changes in the project management personnel; two projects 'Panipat-Jalandhar 6 Lane (Km 96 to 387.1 Km), NHAI' and 'Panvel-Indapur, NHAI' have additional delay of 6 months and 9 months respectively due to poor performance of contractor and inadequate mobilization of resources by contractor respectively; one project 'Pimpalgaon-Nasik-Gonde, NH-3 (NHDP-Phase-III), NHAI' has additional delay of 11 months due to court orders on cutting of trees and public agitation; five projects 'Forbesganj to Simrahi (NH-57), NHAI', '2 Lanning of Mokama-Munger, NHAI', 'Jaipur-Reengus NHAI', '2-Laning with Paved Shoulders of Raebareli - Banda Section of NH-232, NHAI' and '4 Laning of Gomti Chauraha- Udaipur, DORTH' have additional delay of 1 month each; one project 'Haridwar Dehradun Approved Length 69 KM, NHAI' has additional delay of 2 months; eight projects 'Nalbari to Bijni (AS-6), NHAI', 'Agra-Bypass (NS-1/UP-1), NH-2,3,NHAI', 'Muradabad-Bareilly, NHAI', 'Rohtak-Bawal, NHAI', '2-Laning with PS Khagaria-Purnea, NHAI', 'Patna-Baktzarpur KM.181.3 to KM.231.95 NHAI', '2 Lanning of Muzaffarpur-Sonbarsa, NHAI' and 'Beawar Pali Pindwara, NHAI' have additional delay of 3 months each; two project 'Gurgaon-Kotputli-Jaipur (Six Lane), DORTH' and 'Four Lanning of Ludhiyana- Talwandi Section, NHAI' have reported additional delay of 5 months each; two projects 'Deoli-Kota, NHAI' and '2-Lanning With PS Motihari-Raxaul, NHAI' have reported additional delay of 8 months and 9 months respectively and two projects 'Four Laning From Biswanath Chariali To Gohpur From KM 208 to KM 264.10 of NH-52, NHIDCL' and '4 Laning of Ambala - Kaithal - Package -1, NHAI' have reported additional delay of 10 months and 24 months respectively (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- ii) In the **Power Sector**, out of 111 projects, 64 projects are delayed. During the month, 11 projects have reported additional delay in the range of 1-9 months. Out of 11 projects, 7 are mega projects. One project 'Northern Region System Strengthening Scheme-XIX PGCIL' has additional delay of 1 month due to delay in land acquisition; three projects

‘Northern Region Transmission Strengthening Scheme PGCIL’, ‘Transmission System Associated With Krishnapatnam UMPP-Part B PGCIL’ and ‘Transmission System Associated With Mauda Stage-II PGCIL’ have additional delay of 1 month each due to severe RoW problem; two projects ‘Northern Region System Strengthening Scheme-XXI, PGCIL’ and ‘Transmission System for Phase-I Generation Projects in Jharkhand and West Bengal-Part-A2 PGCIL’ have additional delay of 2 months each due to farmer agitation and delay in generation project; two projects ‘Common System Associated With Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited, PGCIL’ and ‘Northern Region System Strengthening Scheme-XXVIII, PGCIL’ have additional delay of 3 months each due to severe RoW problem and non-availability of shut down; one project ‘Eastern Region Strengthening Scheme-V, PGCIL’ has additional delay of 3 months due to delay in land acquisition; two projects ‘Tapovan-Vishnugad HEP (4X130MW) NTPC’ and ‘System Strengthening of Southern Region-XIV PGCIL’ have additional delay of 6 months and 9 months respectively due to delay in civil work by executing agency and RoW problem respectively.

- iii) In the **Petroleum Sector**, out of 68 projects, 38 projects are delayed. During the month, 7 projects have reported additional delays in the range of 1-13 months. Out of 7 projects, 3 projects are mega projects. Two projects ‘Strategic Crude Oil Storage Project at Mangalore, ISPRL’ and ‘Paradip Haldia Durgapur LPG Pipeline IOCL’ have reported additional delay of 1 month and 3 months respectively due to RoU issue and forest clearance; two projects ‘Conversion of Rig Sagar Samrat to Mobile Offshore Production Unit (MOPS), ONGC’ and ‘Pipeline Replacement Project, Ahmedabad, ONGC’ have reported additional delay of 8 months and 9 months respectively due to delay in steel procurement and slow manufacturing respectively; one project ‘Secondary Tank Farm With Dehydration Facility and Effluent Treatment Plant at Madhuban, OIL’ has reported additional delay of 12 months due to court cases and two projects ‘Integrated Development of B-127 Fields ONGC’ and ‘Development of Western Periphery of MH South Field ONGC’ have reported additional delay of 13 months each due to non-performance of the contractors.
- iv) In the **Coal Sector**, out of 88 projects, 42 projects are delayed. During the month, 7 projects have reported additional delay in the range of 1-60 months. Two projects ‘Wind Power Project, Kazhup Neerkulam, Tamil nadu, NLC’ and ‘Muraidih UG Turn-Key Project, BCCL’ have reported additional delay of 1 month and 3 months respectively due to delay in civil works and delay in environmental clearances respectively; two projects

‘Kulda OCP (Mahanadi Coalfields Ltd), MCL’ and ‘Purnadih OCP (3.0 MTY) CCL’ have reported additional delay of 12 months each due to coal evacuation problem and delay in land acquisition; two projects ‘Kalyanikhani Opencast Project SCCL’ and ‘Jhanjra Combined PR(3.50 MTY), ECL’ have reported additional delay of 24 months and 60 months respectively due to delay in land acquisition and due to dovetailing in the project and one project ‘RKP OCP Phase-I, SCCL’ has reported additional delay of 12 months (however, no specific reason has been reported by the project implementing agency for the delay in this project).

- v) In the **Urban Development Sector**, out of 31 projects, 13 projects are delayed. During the month, 1 project ‘Construction of NISM Campus at Patalganga Rasayani District Raigadh, CPWD’ has additional delay of 1 month and 2 projects ‘Stage I of C/O Permanent Campus For IIM, CPWD’ and ‘2000 Boys Hostel (1000 Dounle Bedded Room) at ISM Dhanbad, CPWD’ have additional delay of 4 months each (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- vi) In the **Health and Family Welfare Sector**, out of 9 projects, 4 projects are delayed. During the month, 1 project ‘Safdarjung Hospital Re-development and Others -Super Speciality Block, HSCC have reported additional delay of 3 months due to fund constraint.
- vii) In the **Shipping and Ports Sector**, out of 8 projects, 2 projects are delayed. During the month, 1project ‘Ennore Manali Express Way, F/O Special Purpose Vehicle (SPV) Port Trust’ has reported additional delay of 4 months due to relocation of fishing stalls.


12. Ministry of Railways have **discontinued** the practice of furnishing monthly status reports on all its on-going projects to this Ministry w.e.f 1st January 2015. The Ministry of Railways have provided latest information of their 20 projects only which have been identified by them to be monitored at MoSPI level. Therefore, the available information/data (**as on January 2015**) has been used in respect of remaining projects of Railways sector

13. The status as on 31.03.2016 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

14. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	414	27
2	RAILWAYS	298	0
3	POWER	111	11
4	COAL	88	7
5	PETROLEUM	68	7
6	STEEL	33	0
7	URBAN DEVELOPMENT	31	3
8	HEALTH AND FAMILY WELFARE	9	1
9	SHIPPING AND PORTS	8	1
10	ATOMIC ENERGY	4	0
11	CIVIL AVIATION	4	0
12	MINES	3	0
13	TELECOMMUNICATIONS	2	0
14	FERTILISERS	1	0
15	PETROCHEMICALS	1	0
16	HEAVY INDUSTRY	1	0
	Total	1076	57

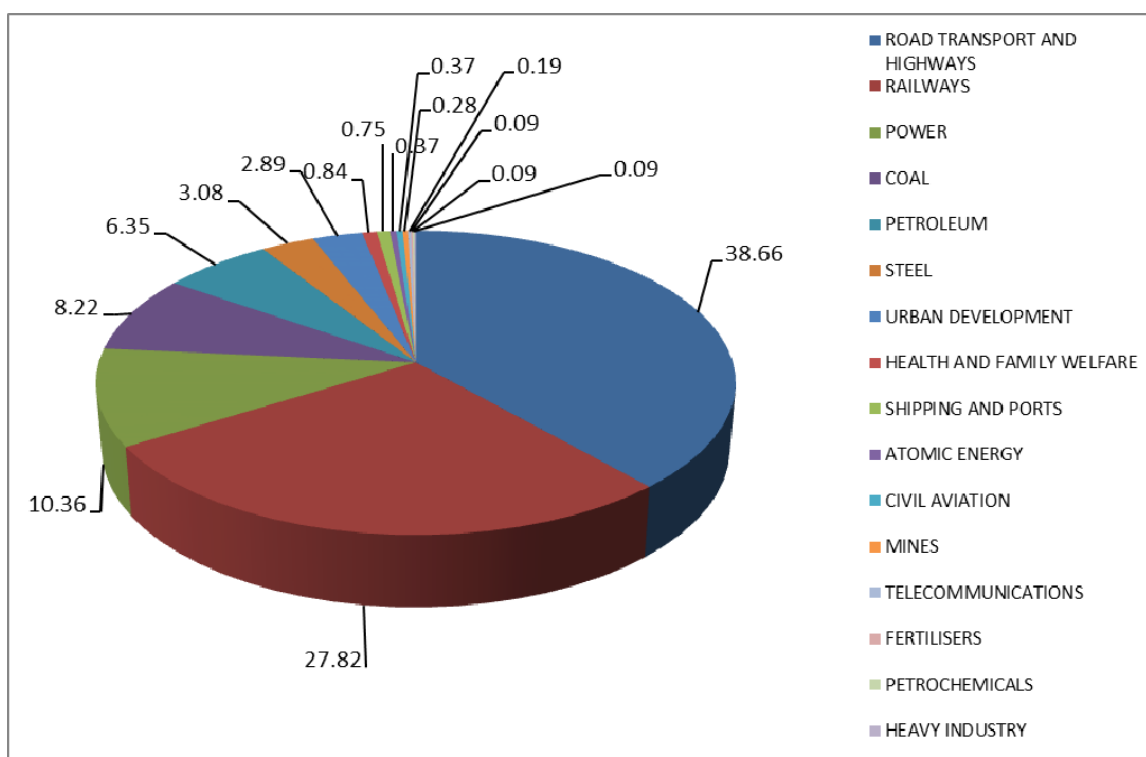

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May,2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
	June,2015			
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30
	July,2015			
	<u>STEEL</u>			
15	AUGMENTATION OF IRON ORE STORAGE IN RMHP (RASTRIYA ISPAT NIGAM LIMITED) - [N12000053]	480.00	09/2009	388.52
	<u>PETROLEUM</u>			
16	SURAT PARADIP PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000163]	10,281.00	04/2015	1.49
	<u>POWER</u>			
17	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000130]	1,263.26	11/2014	1,131.58
	August,2015			
	<u>CIVIL AVIATION</u>			
18	GAGAN PROJECT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000065]	626.00	06/2013	483.53
	<u>COAL</u>			
19	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) (NEYVELI LIGNITE CORPORATION) - [060100087]	2,030.78	06/2009	3,215.91
20	TUTICORIN THERMAL POWER PROJECT- 2X500 MW (NEYVELI LIGNITE CORPORATION) - [N06000047]	4,904.54	03/2012	6,426.43
	<u>PETROLEUM</u>			
21	DEVELOPMENT OF G1 AND GS-15 (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100231]	429.82	04/2006	3,439.38
22	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000098]	288.04	08/2012	229.16
23	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000123]	331.20	08/2013	190.04
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000156]	672.00	10/2011	1,082.12

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
25	BARH STPP STAGE -II (NATIONAL THERMAL POWER CORPORATION) - [N18000047]	7,341.04	10/2013	8,962.00
26	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000076]	4,672.99	11/2012	3,769.57
27	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000096]	2,569.25	03/2014	2,876.57
28	VINDHYACHAL STPP STAGE-V (NATIONAL THERMAL POWER CORPORATION) - [N18000134]	3,180.40	08/2015	2,042.00
	September,2015			
	<u>STEEL</u>			
29	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000018]	607.17	12/2011	394.89
30	EXPANSION OF BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000055]	6,325.00	12/2011	5,256.65
	<u>PETROLEUM</u>			
31	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000132]	5,608.40	05/2015	4,457.47
	<u>POWER</u>			
32	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000124]	213.78	03/2014	204.54
33	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000154]	1,315.90	10/2016	632.97
34	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000156]	296.87	12/2014	318.66
	October,2015			
	<u>CIVIL AVIATION</u>			
35	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000070]	452.00	03/2015	449.41
	<u>STEEL</u>			
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) (RASTRIYA ISPAT NIGAM LIMITED) - [120100067]	8,692.00	10/2009	11,483.12
37	CAPTIVE POWER PLANT - 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000087]	677.00	09/2013	537.19

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>PETROLEUM</u>			
38	102 MW WIND POWER PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000119]	1,106.00	06/2012	437.69
	<u>POWER</u>			
39	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [180100246]	588.25	12/2007	1,020.81
40	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000093]	2,743.19	12/2013	2,827.00
	<u>URBAN DEVELOPMENT</u>			
41	FARIDABAD EXTENSION (DELHI METRO RAIL CORPORATION LTD) - [N28000057]	2,494.00	09/2014	1,311.53
	November,2015			
	<u>POWER</u>			
42	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N16000144]	1,508.74	03/2015	1,211.48
	December,2015			
	<u>CIVIL AVIATION</u>			
43	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000072]	344.28	03/2014	80.60
	<u>COAL</u>			
44	CHURCHA ROUG(1.35MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000046]	462.35	03/2014	497.01
	<u>PETROLEUM</u>			
45	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000142]	1,419.00	12/2014	1,291.63
46	REWARI KANPUR PIPELINE PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000145]	1,210.64	11/2015	1,249.03
47	MARKETING TERMINAL AT PARADEEP (INDIAN OIL CORPORATION LIMITED) - [N16000168]	199.75	07/2013	211.72
48	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000182]	429.06	10/2014	439.02
	<u>POWER</u>			
49	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000160]	243.53	08/2016	185.63

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>SHIPPING AND PORTS</u>			
50	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN(SHIPPING CRP. OF INDIA) - [N25000064]	994.82	11/2013	427.54
	<u>TELECOMMUNICATIONS</u>			
51	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS (BHARAT SANCHAR NIGAM LIMITED) - [N26000096]	384.00	10/2010	74.74
	January,2016			
	<u>COAL</u>			
52	BLOCK-B OCP NCL (3.5 MTY) (NORTHERN COAL FIELDS LIMITED) - [N06000009]	746.04	03/2015	550.32
	<u>STEEL</u>			
53	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000079]	237.09	12/2014	221.88
54	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000080]	313.05	06/2015	319.91
55	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000082]	160.48	09/2014	143.89
	<u>POWER</u>			
56	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000087]	2,074.86	03/2013	1,975.94
	<u>URBAN DEVELOPMENT</u>			
57	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000078]	2,727.89	03/2010	2,709.00
	February,2016			
	<u>COAL</u>			
58	DIPKA EXPANSION OCP (SECL) (20-25) MTY (SOUTH-EASTERN COAL FIELDS LIMITED) - [060100094]	1,943.66	03/2014	2,121.76
	<u>PETROLEUM</u>			
59	DEVELOPMENT OF WO-16 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000105]	2,523.00	01/2014	1,792.85
	March,2016			

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>STEEL</u>			
60	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000078]	332.65	08/2014	237.86
	<u>PETROLEUM</u>			
61	PARADIP REFINERY PROJECT (INDIAN OIL CORPORATION LIMITED) - [N16000058]	29,777.00	11/2012	31,427.90

Month wise List of Deleted Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2016			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000103]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000120]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000121]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000122]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000181]	2,913.10	05/2016	13.86
	June,2016			
7	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
8	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N26000065]	1,077.00	03/2009	.00
	August,2016			
	<u>SHIPPING AND PORTS</u>			
9	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21
10	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	October,2016			
	<u>PETROLEUM</u>			
11	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>SHIPPING AND PORTS</u>			
12	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21

Month wise List of Deleted Projects Costing Rs.150 crore and above during 2015-2016

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	December,2016			
	<u>PETROLEUM</u>			
14	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	667.40
15	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
16	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000270]	297.78	02/2015	37.72
17	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000271]	297.78	02/2015	37.72
18	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T(PUBLIC WORKS DEPT OF STATE) - [N24000285]	297.78	02/2015	37.72
19	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG(PUBLIC WORKS DEPT OF STATE) - [N24000400]	282.41	08/2016	.00
	<u>SHIPPING AND PORTS</u>			
20	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL (MUMBAI PORT TRUST) - [N25000016]	1,228.00	12/2010	1,038.00


Summary of projects in the Flash Report for the month of March, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1071
Number of Projects completed/dropped/frozen in Current Month	2
Projects reported Anti. Cost less then Rs.150 crore in Current Month	2
Number of Projects Added in Current Month	9
Number of Projects in Current Month	1076


Brief Analysis

Project Status with respect to Original Schedule: Out of 1076 projects, 6 projects are ahead of schedule, 258 projects are on schedule 343 projects are delayed. 433 projects do not have fixed dates of commissioning. 36 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

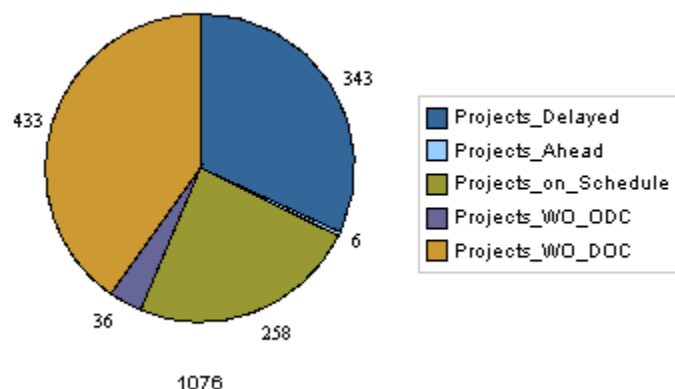

Investment Scenario

Total original cost of implementation of 1076 projects when sanctioned, was of the order of Rs. 1238517.07 crore but this was subsequently revised to Rs. 1393627.86 crore implying a cost overrun of 12.5%. The expenditure incurred on these projects till March, 2016 is Rs. 575677.42 crore, which is 41.3% of the revised cost of the projects.

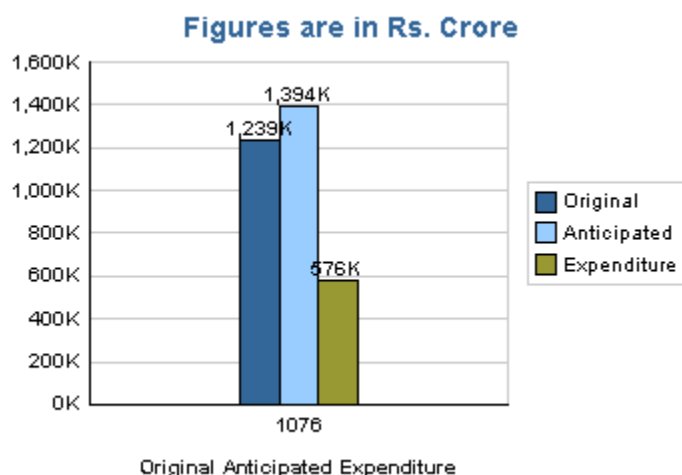

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	1071
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects reported Anticipated Cost below Rs 150 crore	2
No of Projects added in Current Month	9
No of Projects in Current Month	1076

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	343	6	258	36	433	1076	31.88
Latest Approved (Date)	304	8	295	36	433	1076	28.25

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	942	10,71,410.96	11,29,158.59	4,17,124.77	36.90	57,747.63	5.40
Project with Revision in Cost	134	2,26,949.54	2,64,469.27	1,58,552.65	60.00	37,519.73	16.50
Total	1,076	12,98,360.50	13,93,627.86	5,75,677.42	41.31	95267.36	7.34
Original Cost of All Projects							
Original Cost	1076	12,38,517.07	13,93,627.86	5,75,677.42	41.31	1,55,110.79	12.52

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	343	528,819.65	644,703.02	407,654.58	63.20	115,883.37	21.90
Latest Approved (RCE)	304	456,102.09	525,573.65	343,309.47	65.30	69,471.56	15.20

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	57	44,246.92	48,380.50	44,094.21	91.14	4133.58	9.34

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Cost overrun^ (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	88	60,724.30	61,837.03	1.83	5	1,800.69	3,170.48	76.07
4	FERTILISERS	1	197.79	209.44	5.89	1	197.79	209.44	5.89
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0.00
6	STEEL	33	53,712.21	54,241.65	0.99	6	1,964.58	2,494.02	26.95
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	68	108,058.21	111,974.00	3.62	15	29,610.77	35,479.55	19.82
9	POWER	111	304,580.02	354,153.57	16.28	26	66,934.70	116,571.86	74.16
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS*	298	254,176.67	327,636.22	28.90	159	82,135.89	212,266.74	158.43
13	ROAD TRANSPORT AND HIGHWAYS	414	249,122.45	251,469.02	0.94	18	5,171.67	7,634.21	47.62
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	4	1,006.56	1,937.62	92.50
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	134,465.83	139,697.70	3.89	2	6,566.10	11,811.00	79.88
Total		1076	1,238,517.07	1,393,627.86	12.52	241	219,447.96	433,750.32	97.66

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to original schedule(State Wise)

MoSPI
OEWS
(All Cost Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	47	21,226.93	23,061.97	8.64	5	1,263.14	3,108.40	146.09
2	ARUNACHAL PRADESH	15	12,006.22	28,372.49	136.31	5	9,616.85	25,983.12	170.18
3	ASSAM	50	28,781.83	44,485.17	54.56	14	15,918.17	31,722.22	99.28
4	BIHAR	66	58,528.87	72,279.46	23.49	16	13,908.83	28,445.47	104.51
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	0.00
6	GUJARAT	31	30,605.81	31,660.45	3.45	6	3,425.92	4,607.88	34.50
7	HARYANA	20	14,065.88	16,036.50	14.01	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	8,088.55	14,487.83	79.12	2	4,966.47	11,365.75	128.85
9	JAMMU AND KASHMIR	9	25,620.25	45,229.68	76.54	2	6,142.04	25,751.47	319.27
10	KARNATAKA	42	72,113.99	87,378.98	21.17	19	14,794.54	30,065.56	103.22
11	KERALA	16	25,825.82	30,300.97	17.33	8	17,335.36	21,810.51	25.82
12	MADHYA PRADESH	51	53,152.52	55,716.01	4.82	5	2,404.35	5,184.88	115.65
13	MAHARASHTRA	76	122,792.90	131,552.82	7.13	12	17,419.89	27,446.77	57.56
14	MANIPUR	3	1,047.27	6,958.48	564.44	2	830.58	6,741.79	711.70
15	MEGHALAYA	6	6,970.03	8,194.91	17.57	1	4,083.02	5,307.90	30.00
16	MIZORAM	6	2,188.16	5,402.06	146.88	2	988.06	4,201.96	325.27
17	NAGALAND	3	6,420.00	8,757.12	36.40	2	5,124.00	7,461.12	45.61
18	ODISHA	47	42,720.12	47,180.91	10.44	12	3,867.42	8,349.55	115.89
19	PUNJAB	23	11,796.33	11,800.33	0.03	1	573.96	605.00	5.41
20	RAJASTHAN	61	41,310.71	41,853.65	1.31	7	2,884.16	3,512.63	21.79
21	SIKKIM	5	2,149.08	4,999.32	132.63	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	59	69,760.85	89,410.09	28.17	21	23,753.56	43,402.80	82.72
23	TRIPURA	9	3,776.07	7,489.01	98.33	7	2,909.18	6,622.12	127.63
24	UTTAR PRADESH	60	52,378.07	56,264.19	7.42	8	2,576.25	6,510.63	152.72
25	WEST BENGAL	47	50,532.01	63,071.99	24.82	12	8,224.18	23,254.63	182.76
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	16	49,997.48	49,997.48	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	39	86,092.87	87,391.15	1.51	5	5,001.85	6,300.43	25.96
29	JHARKHAND	45	43,305.84	45,868.59	5.92	6	3,485.18	6,089.67	74.73
30	UTTARAKHAND	6	9,352.40	11,651.71	24.59	3	4,855.31	7,155.13	47.37
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
32	TELANGANA	33	13,759.66	16,706.05	21.41	9	2,836.21	5,870.81	106.99
33	MULTI STATE	170	261,824.38	239,759.93	-8.43	45	37,286.44	69,077.94	85.26
Total		1076	1,238,517.07	1,393,627.86	12.52	241	219,447.96	433,750.32	97.66

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	35 - 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	88	60,724.30	61,837.03	1.83	42	23,986.78	25,308.31	4 - 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	-
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	-
6	STEEL	33	53,712.21	54,241.65	0.99	15	39,095.46	39,600.51	3 - 44
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	68	108,058.21	111,974.00	3.62	38	47,994.98	49,998.86	1 - 74
9	POWER	111	304,580.02	354,153.57	16.28	64	171,621.73	208,830.16	1 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	4	976.47	976.47	3 - 31
12	RAILWAYS*	298	254,176.67	327,636.22	28.90	31	36,714.20	90,432.32	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	414	249,122.45	251,469.02	0.94	126	88,006.21	89,832.14	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	2	395.67	1,009.83	88 - 124
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	2	15,445.17	15,345.17	20 - 30
16	URBAN DEVELOPMENT	31	134,465.83	139,697.70	3.89	13	62,113.52	67,314.49	4 - 60
Total		1076	1,238,517.07	1,393,627.86	12.52	343	528,819.65	644,703.02	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	47	21,226.93	23,061.97	8.64	18	9,281.00	9,426.40	5 - 50
2	ARUNACHAL PRADESH	15	12,006.22	28,372.49	136.31	2	3,070.89	7,442.23	35 - 79
3	ASSAM	50	28,781.83	44,485.17	54.56	25	14,944.65	25,602.84	15 - 138
4	BIHAR	66	58,528.87	72,279.46	23.49	17	24,988.43	32,567.42	8 - 91
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	-
6	GUJARAT	31	30,605.81	31,660.45	3.45	9	17,606.95	17,545.17	5 - 45
7	HARYANA	20	14,065.88	16,036.50	14.01	5	3,130.20	4,310.20	14 - 73
8	HIMACHAL PRADESH	5	8,088.55	14,487.83	79.12	2	4,190.42	8,669.59	16 - 111
9	JAMMU AND KASHMIR	9	25,620.25	45,229.68	76.54	7	21,314.62	40,924.05	10 - 181
10	KARNATAKA	42	72,113.99	87,378.98	21.17	10	24,904.13	31,087.43	2 - 60
11	KERALA	16	25,825.82	30,300.97	17.33	4	2,462.73	3,434.08	4 - 88
12	MADHYA PRADESH	51	53,152.52	55,716.01	4.82	8	4,208.96	4,698.93	11 - 87
13	MAHARASHTRA	76	122,792.90	131,552.82	7.13	23	41,808.94	46,578.31	1 - 144
14	MANIPUR	3	1,047.27	6,958.48	564.44	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	6	6,970.03	8,194.91	17.57	1	536.00	536.00	29 - 29
16	MIZORAM	6	2,188.16	5,402.06	146.88	2	988.06	4,201.96	47 - 123
17	NAGALAND	3	6,420.00	8,757.12	36.40	1	850.00	2,973.42	60 - 60
18	ODISHA	47	42,720.12	47,180.91	10.44	16	7,355.96	7,780.42	5 - 91
19	PUNJAB	23	11,796.33	11,800.33	0.03	1	523.85	523.85	12 - 12
20	RAJASTHAN	61	41,310.71	41,853.65	1.31	13	20,641.20	20,682.39	1 - 90
21	SIKKIM	5	2,149.08	4,999.32	132.63	2	1,648.94	4,499.46	51 - 80
22	TAMIL NADU	59	69,760.85	89,410.09	28.17	21	52,668.72	65,002.75	4 - 124
23	TRIPURA	9	3,776.07	7,489.01	98.33	4	2,033.56	4,500.90	7 - 108
24	UTTAR PRADESH	60	52,378.07	56,264.19	7.42	19	19,506.39	21,717.77	7 - 105
25	WEST BENGAL	47	50,532.01	63,071.99	24.82	19	34,268.44	42,670.23	3 - 177
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
27	DELHI	16	49,997.48	49,997.48	0.00	5	39,893.26	39,893.26	3 - 37
28	CHHATISGARH	39	86,092.87	87,391.15	1.51	15	54,951.07	55,842.48	7 - 93
29	JHARKHAND	45	43,305.84	45,868.59	5.92	19	9,581.96	11,780.19	3 - 104
30	UTTARAKHAND	6	9,352.40	11,651.71	24.59	4	7,605.57	9,794.74	35 - 78
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	33	13,759.66	16,706.05	21.41	13	4,422.52	5,748.91	21 - 132
33	MULTI STATE	170	261,824.38	239,759.93	-8.43	56	92,618.59	101,610.81	1 - 261
Total		1076	1,238,517.07	1,393,627.86	12.52	343	528,819.65	644,703.02	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	3	36,950.00	46,241.00	35 - 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	88	60,724.30	61,837.03	1.83	38	15,131.83	16,226.19	4 - 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	-
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	-
6	STEEL	33	53,712.21	54,241.65	0.99	14	23,570.46	24,075.51	3 - 44
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	68	108,058.21	111,974.00	3.62	22	18,266.42	20,096.64	1 - 74
9	POWER	111	304,580.02	354,153.57	16.28	55	142,043.65	162,315.99	1 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	4	976.47	976.47	3 - 31
12	RAILWAYS*	298	254,176.67	327,636.22	28.90	29	30,564.20	79,472.86	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	414	249,122.45	251,469.02	0.94	121	86,961.48	88,695.46	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	2	395.67	1,009.83	88 - 124
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	2	15,445.17	15,345.17	20 - 30
16	URBAN DEVELOPMENT	31	134,465.83	139,697.70	3.89	12	61,780.80	66,981.77	8 - 60
Total		1076	1,238,517.07	1,393,627.86	12.52	304	434,113.61	525,573.65	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning
 ^ - Cost Overrun = Anticipated Cost minus Original Cost

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun [^] (%)
1	ATOMIC ENERGY	4	44,541.00	51,918.00	16.56	2	20,762.00	28,139.00	35.53
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	88	60,694.71	61,837.03	1.88	4	1,541.29	2,683.91	74.13
4	FERTILISERS	1	209.44	209.44	0.00	0	0.00	0.00	0.00
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0.00
6	STEEL	33	54,082.71	54,241.65	0.29	3	1,576.00	1,735.31	10.11
7	PETROCHEMICALS	1	8,920.00	9,965.00	11.72	1	8,920.00	9,965.00	11.72
8	PETROLEUM	68	109,117.51	111,974.00	2.62	6	17,365.01	20,438.81	17.70
9	POWER	111	333,729.44	354,153.57	6.12	7	28,130.05	48,554.18	72.61
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS*	298	273,408.29	327,636.22	19.83	151	85,571.20	196,447.26	129.57
13	ROAD TRANSPORT AND HIGHWAYS	414	251,055.27	251,469.02	0.16	13	3,887.63	5,884.15	51.36
14	SHIPPING AND PORTS	8	4,708.80	5,048.81	7.22	3	997.61	1,337.62	34.08
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	134,434.10	139,697.70	3.92	2	6,537.37	11,800.97	80.52
Total		1076	1,298,360.50	1,393,627.86	7.34	194	177,223.76	331,057.61	86.80

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R \$ (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	1	13,171.00	22,462.00	89- 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	88	60,724.30	61,837.03	1.83	1	259.40	486.57	60- 60
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0- 0
6	STEEL	33	53,712.21	54,241.65	0.99	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44- 44
8	PETROLEUM	68	108,058.21	111,974.00	3.62	6	4,814.29	6,307.49	4- 43
9	POWER	111	304,580.02	354,153.57	16.28	19	40,550.53	61,962.36	18- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS*	298	254,176.67	327,636.22	28.90	5	5,984.97	12,493.69	48- 177
13	ROAD TRANSPORT AND HIGHWAYS	414	249,122.45	251,469.02	0.94	2	425.61	517.56	77- 105
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	2	395.67	1,009.83	88- 124
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	134,465.83	139,697.70	3.89	1	171.10	202.00	10- 10
Total		1076	1238517.07	1393627.86	12.52	38	71233.18	115406.5	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R \$ (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	88	60,724.30	61,837.03	1.83	5	1,800.69	3,170.48	24- 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0- 0
6	STEEL	33	53,712.21	54,241.65	0.99	5	1,761.97	2,267.02	3- 25
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	68	108,058.21	111,974.00	3.62	10	7,763.20	10,878.04	4- 54
9	POWER	111	304,580.02	354,153.57	16.28	24	60,228.36	97,500.40	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS*	298	254,176.67	327,636.22	28.90	26	21,862.31	77,189.14	3- 261
13	ROAD TRANSPORT AND HIGHWAYS	414	249,122.45	251,469.02	0.94	8	2,586.46	4,438.02	61- 93
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	2	395.67	1,009.83	88- 124
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	134,465.83	139,697.70	3.89	0	0.00	0.00	0- 0
Total		1076	1238517.07	1393627.86	12.52	83	114779.66	228419.23	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information. The Ministry of Railways has resumed data updation of 20 projects which have been identified to be monitored at MoSPI level.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	PARADIP REFINERY PROJECT	02/2009	29,777.00	11/2012	34,555.00	02/2016	31,427.90
	<u>STEEL</u>						
2	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	07/2012	332.65	08/2014	332.65	03/2016	237.86

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR	8/2010	103.02	7/2016	171.04	7/2016
2	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	247.52	2/2019	247.52	2/2019
3	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	6/2012	150.00	7/2014	150.00	1/2017
4	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY	2/2016	367.11	4/2017	367.11	4/2017
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
5	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2014	377.64	3/2014	377.64	9/2016
6	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	1/2014	292.98	11/2014	292.98	11/2014
7	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	278.39	8/2014	278.39	8/2014
	<u>URBAN DEVELOPMENT</u>					
8	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN	8/2014	350.02	3/2015	350.02	3/2015
9	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	216.69	3/2015	216.69	3/2015

Milestones (Cumulative due & achieved)

Total	3864
Achieved up to month	1794

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	03/2016	04/2016	1
2	MURADIH UG TURN-KEY PROJECT BCCL	339.88	339.88	04/2014	03/2016	06/2016	3
3	KULDA OCP (MAHANADI COALFIELDS LTD) MCL	302.96	302.96	03/2010	03/2016	03/2017	12
4	RKP OCP PHASE-I SCCL	209.78	209.78	03/2015	03/2016	03/2017	12
5	PURNADIH OCP (3.0 MTY) CCL	210.98	210.98	03/2013	03/2016	03/2017	12
6	KALYANIKHANI OPENCAST PROJECT SCCL	417.33	417.33	07/2016	03/2017	03/2019	24
7	JHANJRA COMBINED PR(3.50 MTY) ECL	602.86	602.86	03/2022	03/2017	03/2022	60
	<u>PETROLEUM</u>						
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE ISPRL	732.00	1,227.00	10/2011	03/2016	04/2016	1
9	PARADIP HALDIA DURGAPUR LPG PIPELINE IOCL	913.00	913.00	08/2015	12/2016	03/2017	3
10	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	1,256.72	05/2013	04/2016	12/2016	8
11	PIPELINE REPLACEMENT PROJECT, AHMEDABAD ONGC	202.25	160.16	07/2016	07/2016	04/2017	9
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN OIL	352.56	450.55	03/2017	03/2017	03/2018	12
13	INTEGRATED DEVELOPMENT OF B-127 FIELDS ONGC	2,059.63	2,665.65	03/2015	05/2016	06/2017	13
14	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD ONGC	600.17	600.17	12/2014	05/2016	06/2017	13
	<u>POWER</u>						
15	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX PGCIL	410.29	410.29	02/2012	03/2016	04/2016	1
16	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	03/2016	04/2016	1

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
17	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B PGCIL	1,927.16	1,940.58	10/2014	03/2016	04/2016	1
18	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II PGCIL	1,575.30	1,575.30	05/2016	05/2016	06/2016	1
19	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI PGCIL	1,677.57	1,677.57	04/2013	03/2016	05/2016	2
20	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 PGCIL	2,422.66	2,422.66	08/2014	03/2016	05/2016	2
21	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L PGCIL	1,940.13	1,940.13	09/2014	06/2016	09/2016	3
22	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	05/2015	03/2016	06/2016	3
23	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,364.52	04/2016	06/2016	09/2016	3
24	TAPOVAN-VISHNUGAD HEP (4X130MW) NTPC	2,978.48	3,846.30	03/2013	12/2018	06/2019	6
25	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	346.79	08/2014	06/2016	03/2017	9
	<u>HEALTH AND FAMILY WELFARE</u>						
26	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK HSCC	444.70	444.70	12/2015	03/2016	06/2016	3
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
27	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	332.94	332.94	09/2008	03/2016	04/2016	1
28	KOTA BYPASS,RJ-4, NH-76 (NHAI)	275.00	250.39	10/2008	03/2016	04/2016	1
29	KISHANGARH-AJMER-BEAWER NHAI	795.00	795.00	05/2012	03/2016	04/2016	1
30	2 LANNING OF MOKAMA-MUNGER NHAI	351.54	351.54	05/2013	03/2016	04/2016	1
31	JAIPUR-REENGUS NHAI	267.81	267.81	02/2013	03/2016	04/2016	1
32	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 NHAI	351.34	351.34	01/2016	09/2016	10/2016	1
33	4 LANING OF GOMTI CHAURAHA - UDAIPUR DORTH	914.50	914.50	10/2015	02/2016	03/2016	1

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
34	HARIDWAR DEHRADUN APPROVED LENGTH 69 NHAI	478.51	478.00	10/2013	07/2016	09/2016	2
35	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHAI	155.00	201.66	09/2008	03/2016	06/2016	3
36	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	04/2016	07/2016	3
37	AGRA-BYPASS(NS-1/UP-1), NH-2,3 NHAI	348.16	348.16	09/2007	03/2016	06/2016	3
38	MURADABAD-BAREILLY NHAI	1,267.00	1,267.00	06/2013	03/2016	06/2016	3
39	ROHTAK-BAWAL NHAI	650.00	650.00	11/2013	03/2016	06/2016	3
40	2-LANNING WITH PS KHAGARIA-PURNEA NHAI	664.00	664.00	02/2014	03/2016	06/2016	3
41	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 NHAI	574.00	574.00	03/2014	03/2016	06/2016	3
42	2 LANNING OF MUZAFFARPUR - SONBARSA NHAI	511.54	511.54	11/2013	03/2016	06/2016	3
43	BEAWAR PALI PINDWARA NHAI	2,388.51	2,388.00	06/2014	03/2016	06/2016	3
44	DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	02/2016	06/2016	4
45	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) DORTH	1,673.70	1,673.70	10/2011	01/2016	06/2016	5
46	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION NHAI	479.00	479.00	N.A.	07/2016	12/2016	5
47	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) NHAI	1,108.00	2,288.00	11/2011	06/2016	12/2016	6
48	DEOLI-KOTA NHAI	593.00	593.00	07/2013	04/2016	12/2016	8
49	2-LANNING WITH PS MOTIHARI-RAXAUL NHAI	375.09	375.09	04/2014	03/2016	12/2016	9
50	PANVEL-INDAPUR NHAI	942.69	942.69	06/2014	03/2016	12/2016	9
51	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 NHIDCL	829.00	829.00	01/2019	03/2018	01/2019	10
52	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) NHAI	940.00	940.00	07/2012	04/2016	03/2017	11
53	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 NHAI	602.95	602.95	06/2016	06/2016	06/2018	24
	<u>SHIPPING AND PORTS</u>						

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
54	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) PORT TRUST	150.00	600.00	03/2006	03/2016	07/2016	4
	<u>URBAN DEVELOPMENT</u>						
55	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA CPWD	315.00	315.00	06/2015	10/2016	11/2016	1
56	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD	332.72	332.72	09/2016	09/2016	01/2017	4
57	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD CPWD	171.86	171.86	03/2016	05/2017	09/2017	4

Graphical Presentation of All Projects w.r.t. Original Schedule

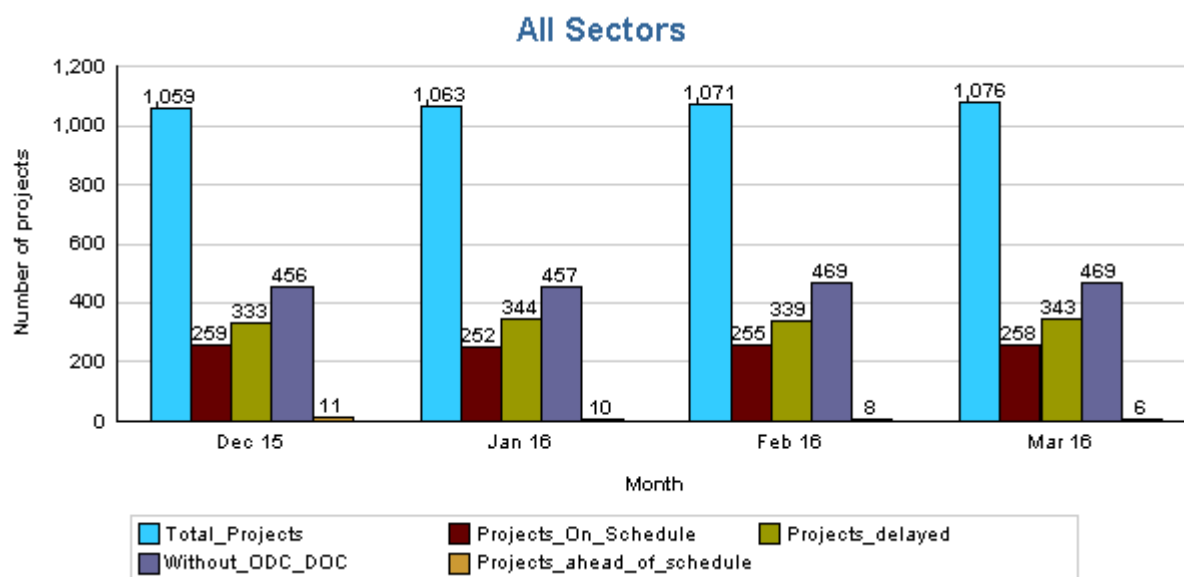

Break-up of 343 Delayed projects in March 2016

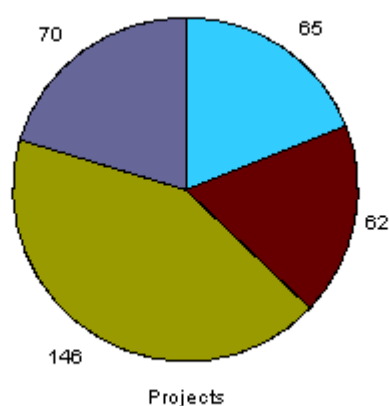


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

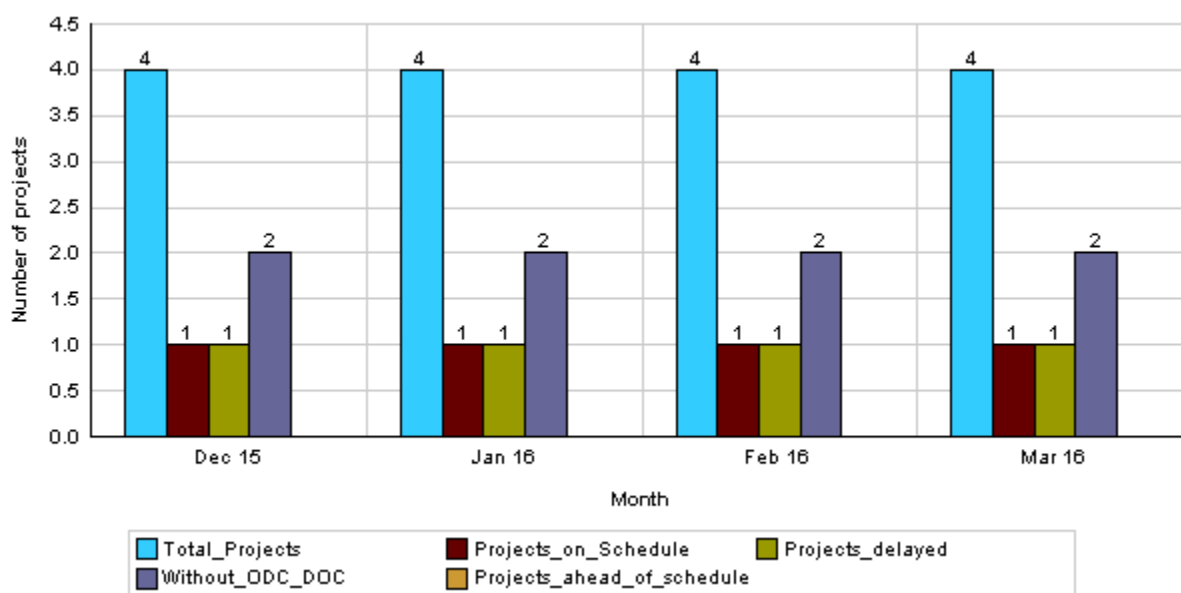


Break-up of 1 Delayed projects in March 2016



Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1	1	0	0	0

Graphical Presentation of ATOMIC ENERGY Sector

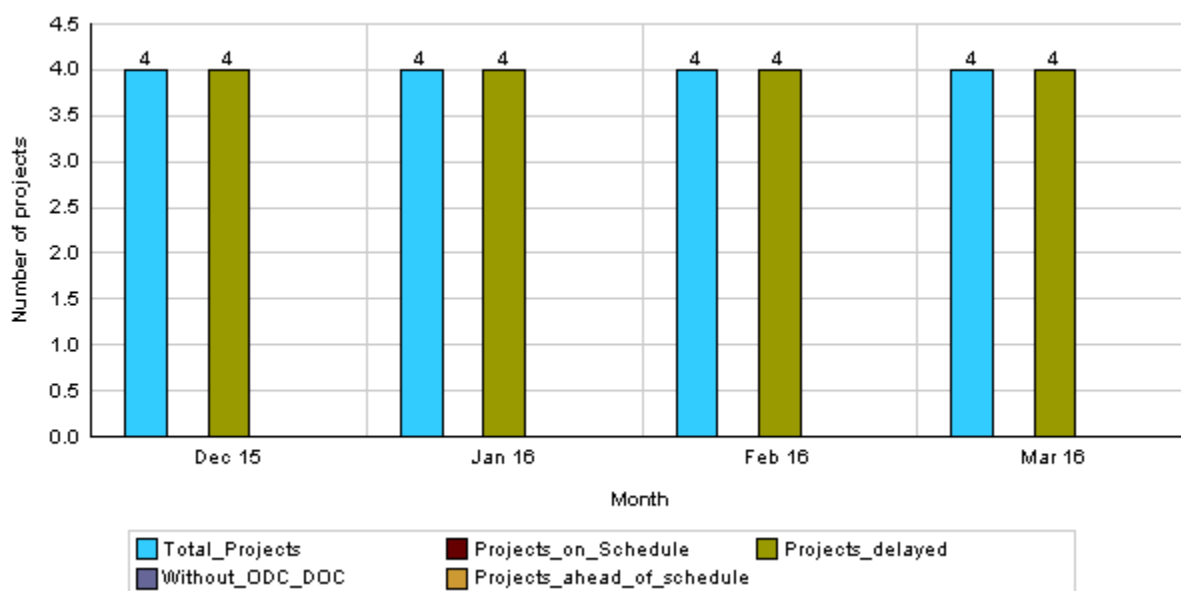


Break-up of 4 Delayed projects in March 2016




Delay in Months

Category	Count
1-12	2
13-24	2
25-60	2
MORE THAN 60	2

Graphical Presentation of COAL Sector

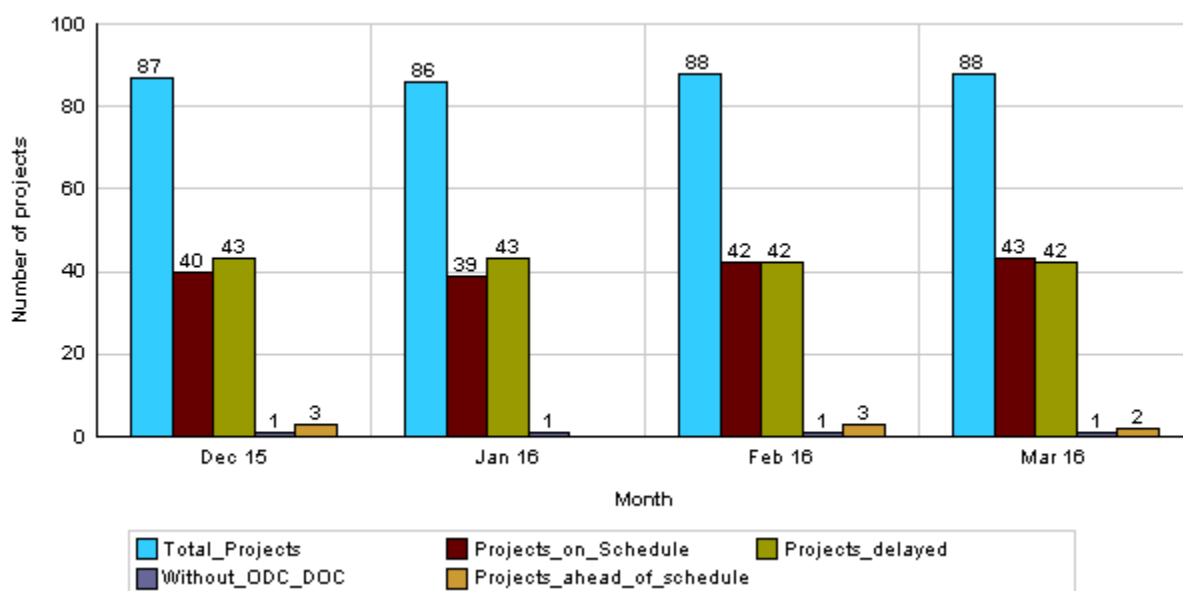


Break-up of 42 Delayed projects in March 2016

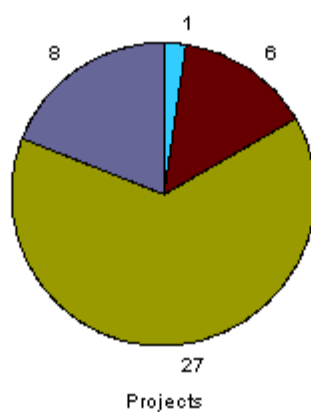


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of STEEL Sector

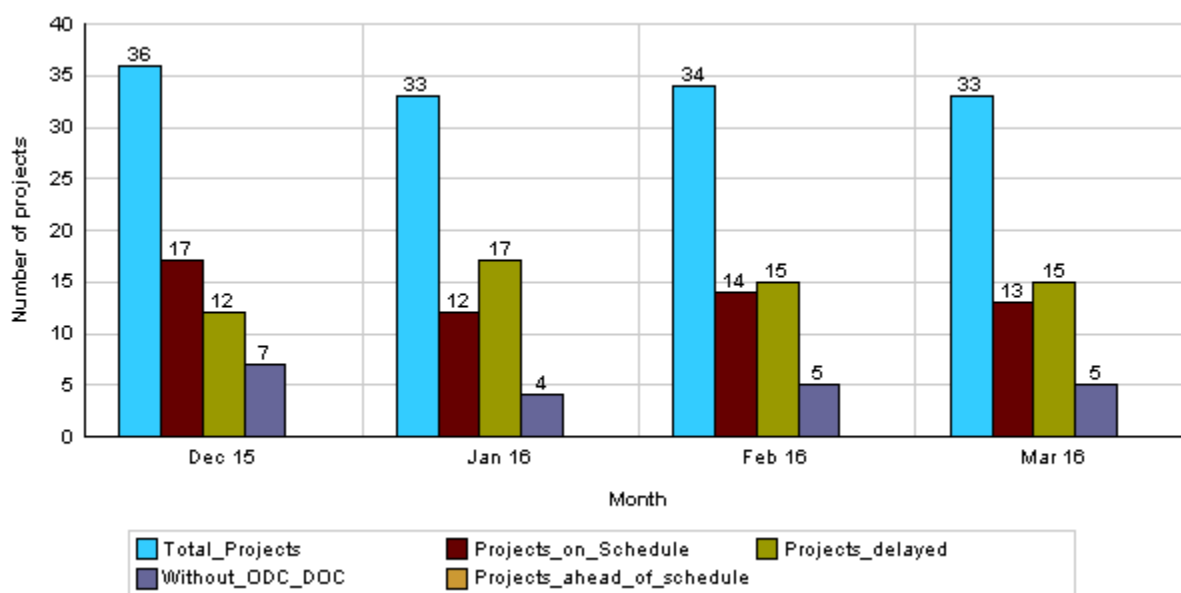


Break-up of 15 Delayed projects in March 2016

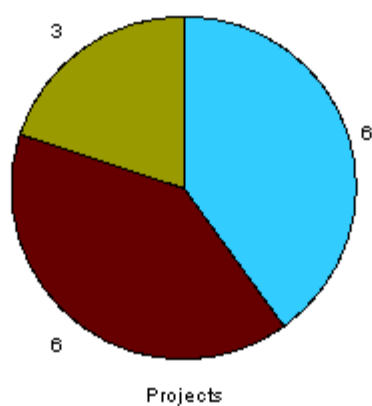


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of PETROLEUM Sector

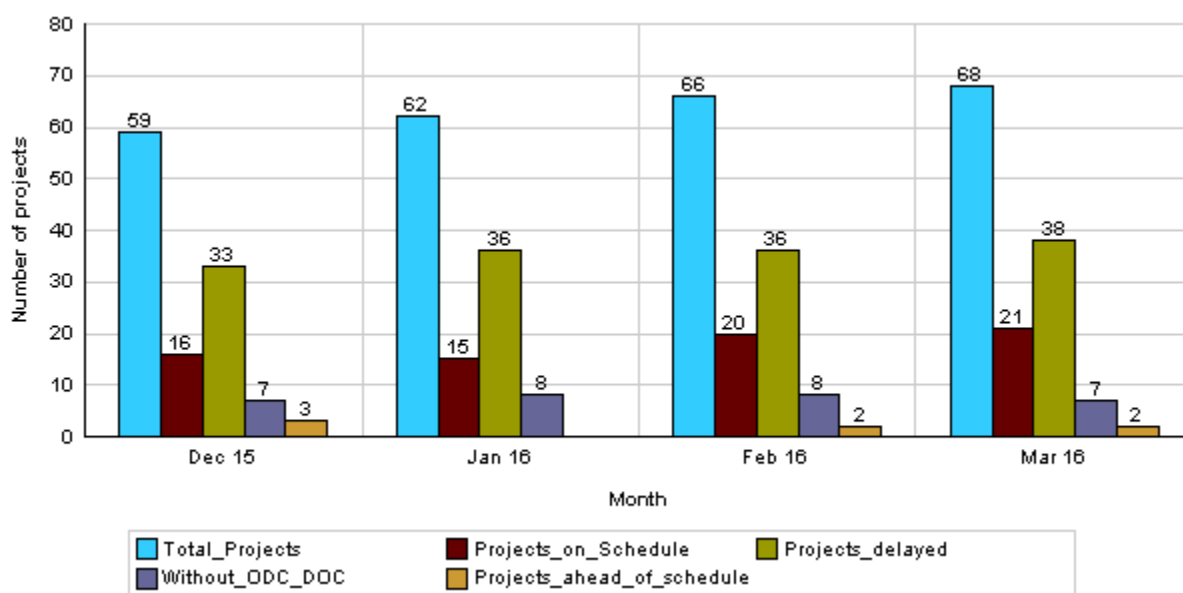


Break-up of 38 Delayed projects in March 2016

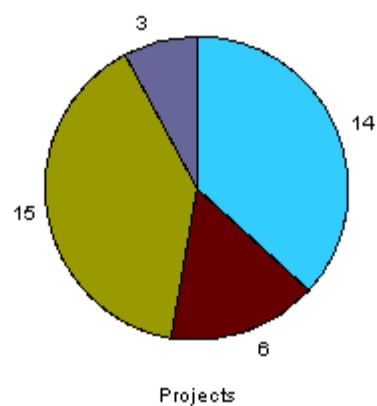


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of POWER Sector

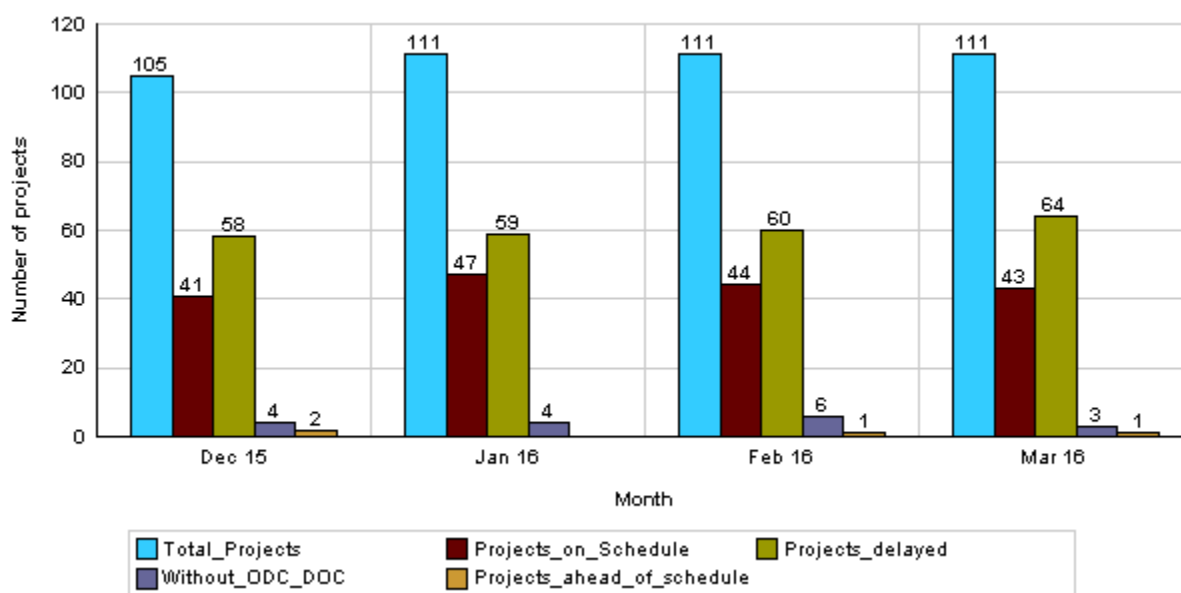


Break-up of 64 Delayed projects in March 2016

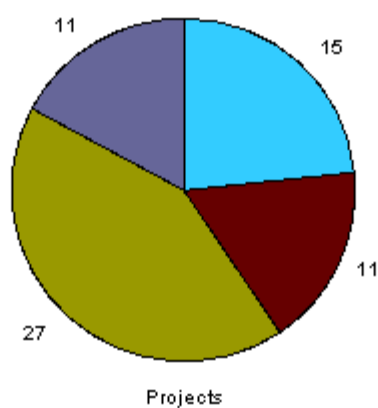


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	15	11	27	11

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

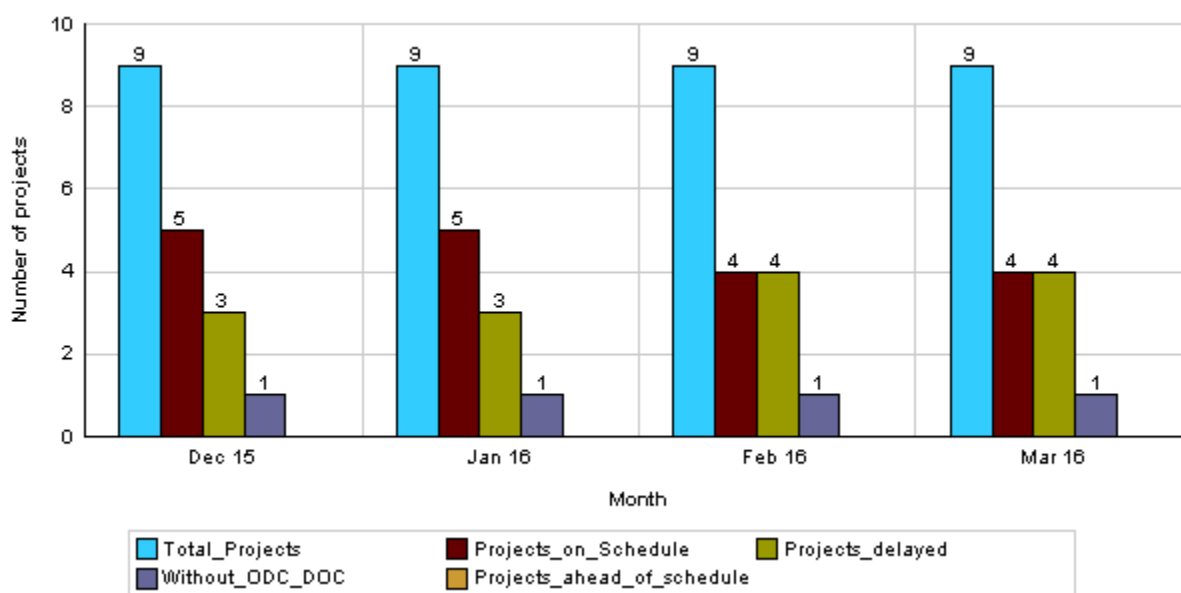


Break-up of 4 Delayed projects in March 2016

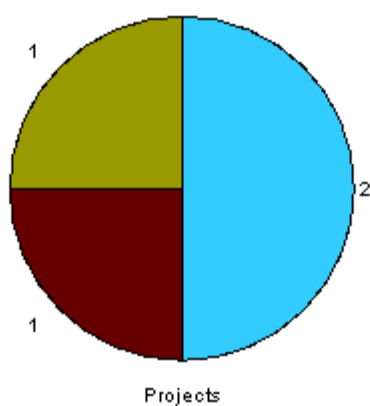


Delay in Months

Delay in Months	Count
1-12	2
13-24	1
25-60	1
MORE THAN 60	0

Graphical Presentation of RAILWAYS Sector

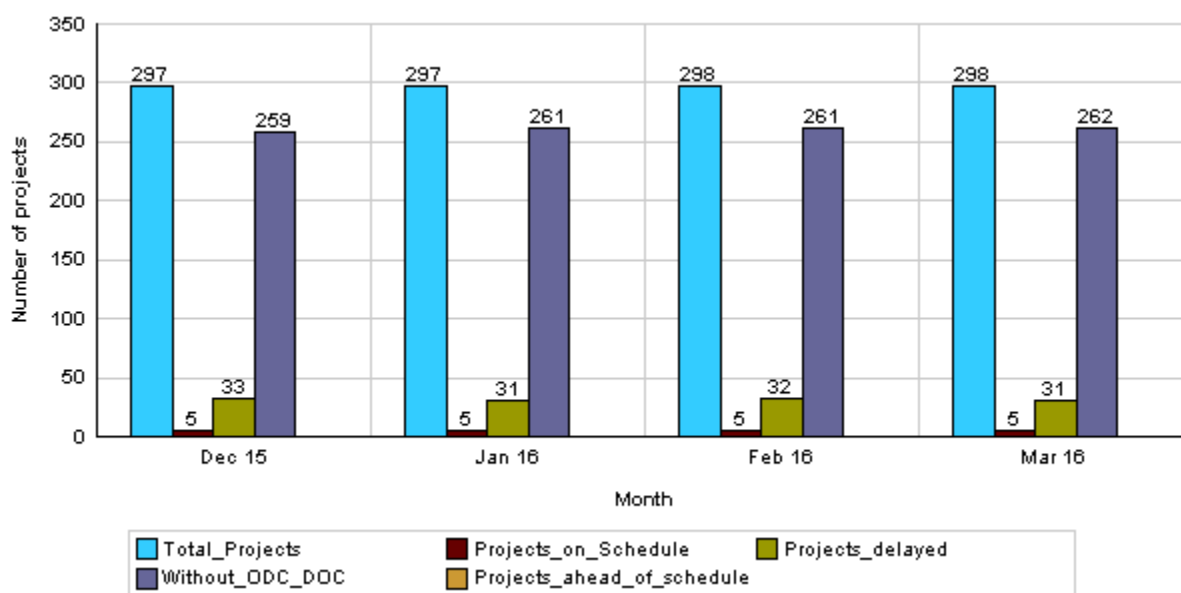


Break-up of 31 Delayed projects in March 2016

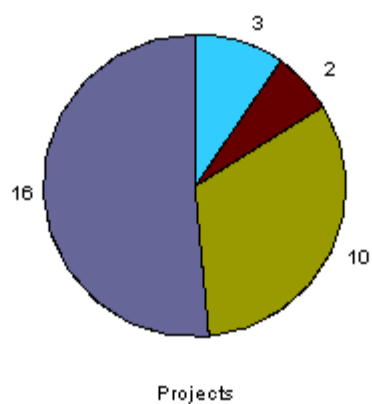


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	3	2	10	16

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

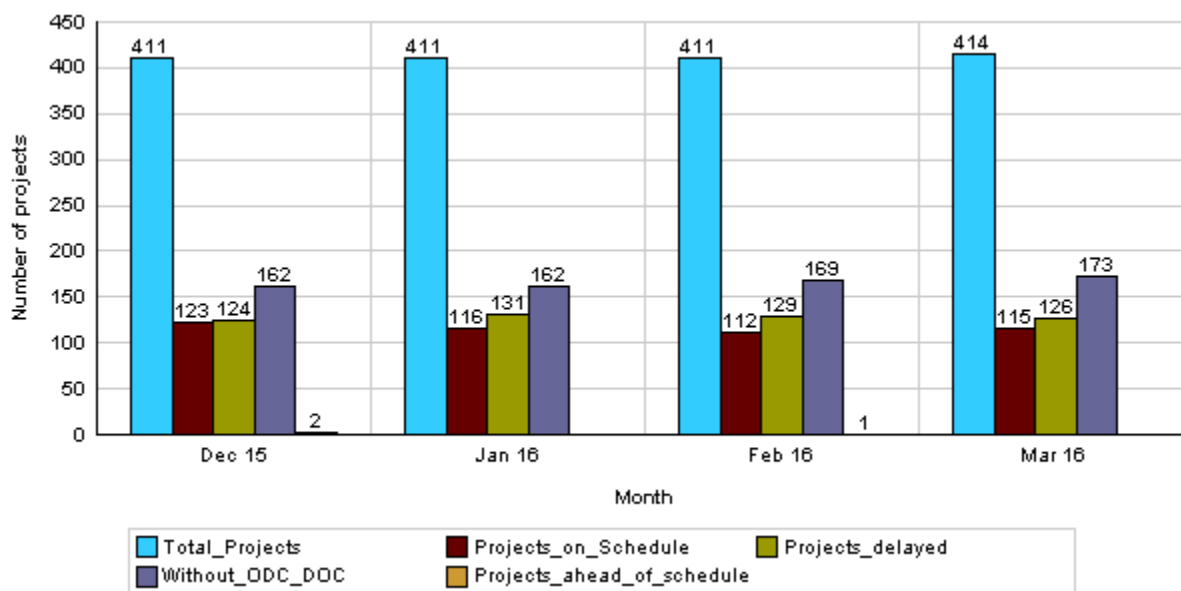


Break-up of 126 Delayed projects in March 2016

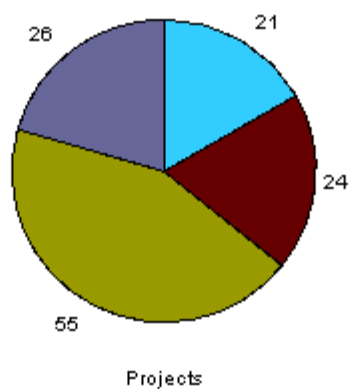


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of SHIPPING AND PORTS Sector

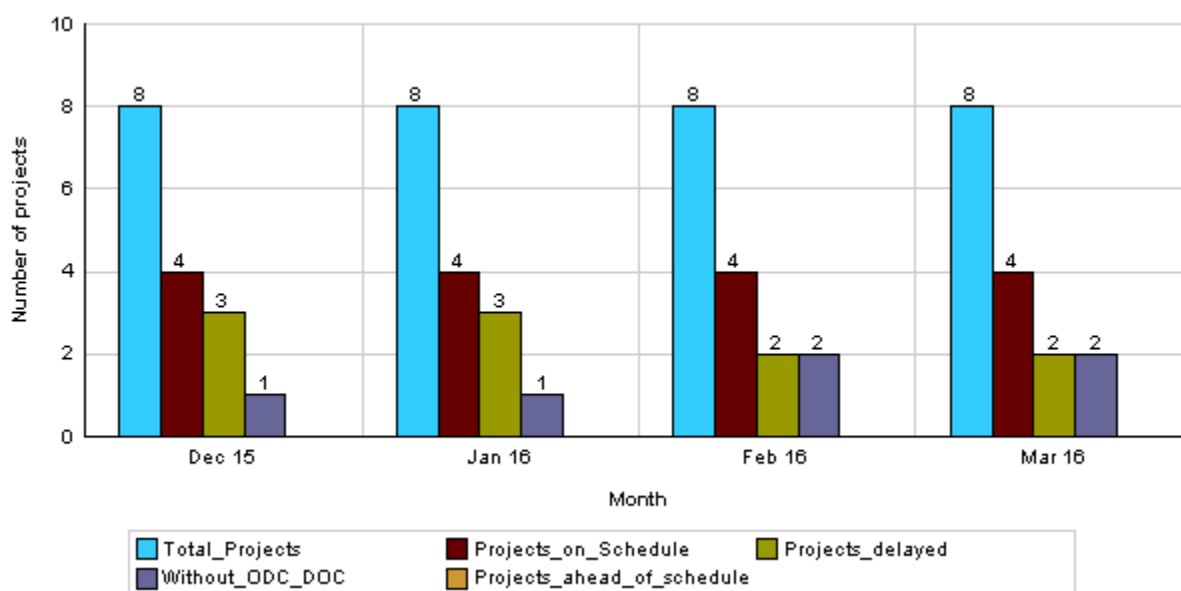


Break-up of 2 Delayed projects in March 2016

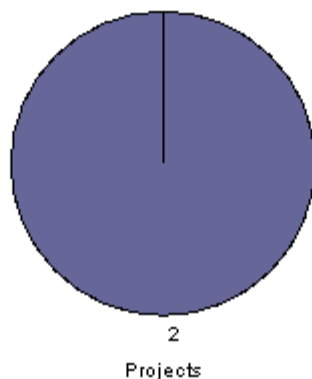


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of TELECOMMUNICATIONS Sector

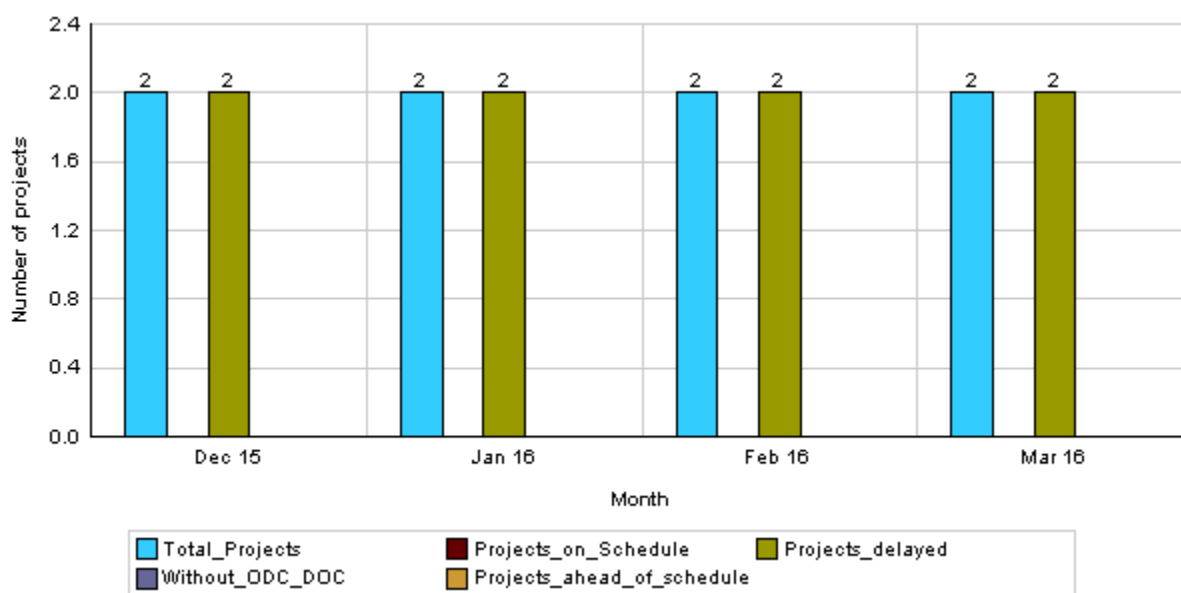


Break-up of 2 Delayed projects in March 2016

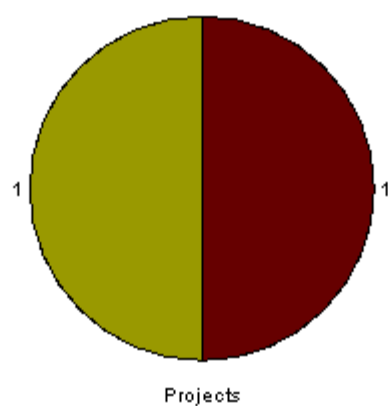


Delay in Months

Delay in Months	Count
1-12	1
13-24	1
25-60	0
MORE THAN 60	0

Graphical Presentation of URBAN DEVELOPMENT Sector

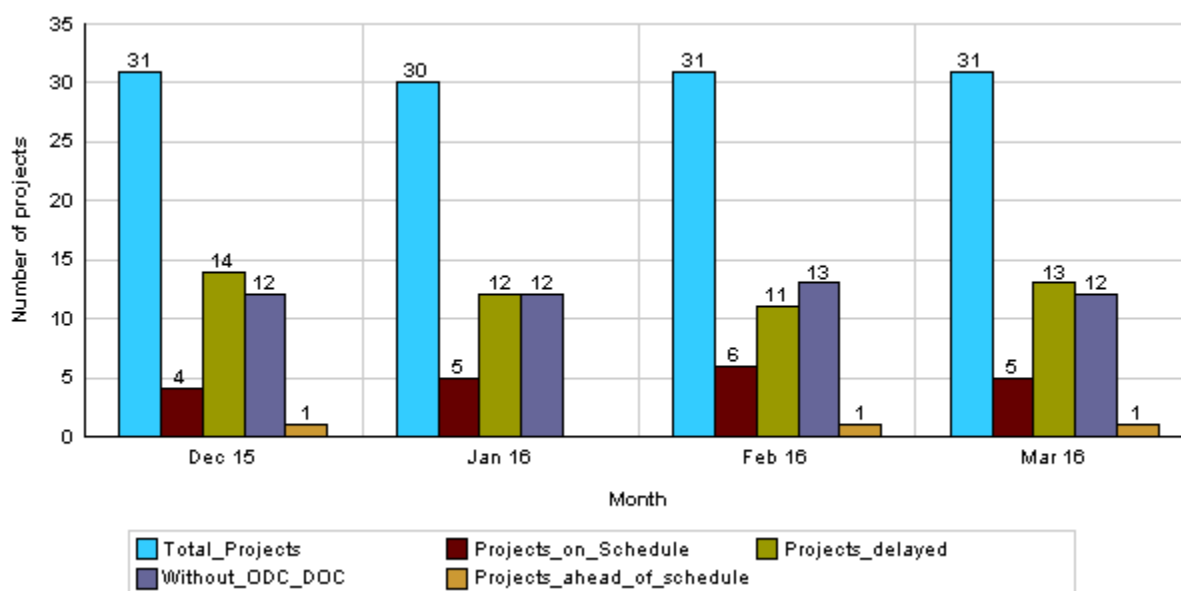

Break-up of 13 Delayed projects in March 2016

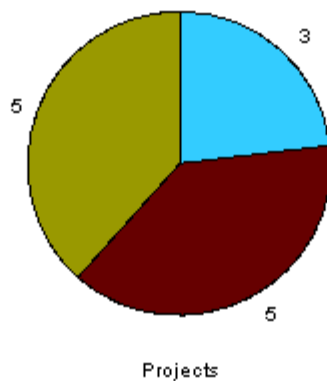

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	44,541.00	51,918.00	40,349.55
CIVIL AVIATION	4	1,177.28	1,177.28	1,186.17	784.73
COAL	88	60,724.30	60,694.71	61,837.03	14,400.83
FERTILISERS	1	197.79	209.44	209.44	56.41
MINES	3	2,555.63	2,555.63	2,555.63	235.90
STEEL	33	53,712.21	54,082.71	54,241.65	30,793.35
PETROCHEMICALS	1	5,460.61	8,920.00	9,965.00	9,356.28
PETROLEUM	68	108,058.21	109,117.51	111,974.00	40,449.61
POWER	111	304,580.02	333,729.44	354,153.57	192,162.73
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	2,563.15	1,018.40
RAILWAYS	298	254,176.67	273,408.29	327,636.22	93,023.07
ROAD TRANSPORT AND HIGHWAYS	414	249,122.45	251,055.27	251,469.02	96,094.78
SHIPPING AND PORTS	8	4,117.75	4,708.80	5,048.81	2,353.06
TELECOMMUNICATIONS	2	15,445.17	15,445.17	15,345.17	1,556.20
URBAN DEVELOPMENT	31	134,465.83	134,434.10	139,697.70	53,042.52
Grand total	1076	1,238,517.07	1,298,360.50	1,393,627.86	575,677.42

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU , .	12/2001	13,171.00 17,270.00	22,462.00	21,304.00	12/2008 10/2013	05/2016	89(O) 31(R)	55/102
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU , .	09/2003	3,492.00 -	5,677.00	5,187.55	09/2010 09/2016	09/2016	72(O) 0(R)	12/88
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT , .	10/2009	11,459.00 -	11,459.00	8,066.00	12/2015 11/2016	11/2018	35(O) 24(R)	42/70
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN , .	10/2009	12,320.00 -	12,320.00	5,792.00	12/2016 03/2017	12/2019	36(O) 33(R)	29/69
	Total		40,442.00 -	51,918.00	40,349.55				138/329
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA , .	05/2010	335.61 -	318.00	305.60	05/2012 -	03/2015	-	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM , .	01/2009	309.46 -	309.46	424.30	01/2011 06/2016	09/2017	80(O) 15(R)	0/0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE , .	10/2012	217.60 -	244.10	30.74	03/2015 -	09/2015	-	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS , .	10/2013	314.61 -	314.61	24.09	09/2018 -	09/2018	0(O) -	0/0
	Total		1,177.28 -	1,186.17	784.73				0/0
	<u>COAL</u>								
9	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA , .	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA , .	01/2005	302.96 -	302.96	303.14	03/2010 -	03/2017	84(O) -	8/10
11	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH , .	06/2010	2,675.67 -	2,675.67	2,023.54	03/2014 -	03/2016	24(O) -	11/16
12	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND , .	12/2007	341.63 -	341.63	128.02	03/2011 -	03/2017	72(O) -	2/5
13	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH , .	06/2011	789.88 741.62	741.62	511.06	03/2013 -	03/2016	36(O) -	2/5
14	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH , .	08/2013	7,612.33 7,612.33	7,612.33	813.94	03/2023 03/2023	03/2023	0(O) 0(R)	2/17
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH , .	12/2009	1,352.04 1,143.54	1,143.54	847.83	03/2016 -	03/2016	0(O) -	4/6
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , .	08/2008	706.40 -	706.40	79.49	07/2012 03/2017	03/2021	104(O) 48(R)	2/3

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA , .	12/2009	212.34 -	1,228.39	872.21	03/2013 -	03/2016	36(O) -	21/22
18	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , .	10/2006	249.03 -	249.03	119.06	03/2012 -	03/2018	72(O) -	30/42
19	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL , .	11/2015	602.86 -	602.86	188.76	03/2022 -	03/2022	0(O) -	2/2
20	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , .	10/2007	259.40 486.57	486.57	157.69	03/2012 03/2018	03/2017	60(O) -12(R)	1/1
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , .	12/2007	490.10 -	490.10	206.38	03/2017 -	03/2017	0(O) -	11/11
22	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , .	12/2007	457.77 -	457.77	229.69	03/2013 -	03/2017	48(O) -	8/9
23	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA , .	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	2/13
24	TALABIRA OCP - [N06000043]MCL,ODISHA , .	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , .	12/2007	172.08 -	172.08	152.18	03/2010 -	03/2017	84(O) -	2/4
26	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH , .	11/2014	1,624.59 1,624.59	1,624.59	5.43	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
27	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , .	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51(O) -	11/44
28	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH , .	08/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023	0(O) -	1/9
29	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , .	09/2014	441.82 -	441.82	149.65	03/2020 -	03/2020	0(O) -	5/13
30	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , .	08/2008	207.28 -	207.28	207.71	03/2012 -	03/2017	60(O) -	4/5
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , .	11/2008	479.53 -	479.63	185.35	03/2013 -	03/2017	48(O) -	4/8
32	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH , .	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60(O) -	1/6
33	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH , .	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
34	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , .	12/2009	418.97 -	489.62	475.38	03/2012 -	03/2023	132(O) -	0/2
35	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , .	03/2010	209.78 -	209.78	86.48	03/2015 -	03/2017	24(O) -	8/31
36	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , .	03/2010	181.19 -	181.19	83.51	03/2012 -	03/2016	48(O) -	5/6
37	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH , .	12/2009	321.50 -	321.50	211.06	03/2014 -	03/2018	48(O) -	4/7
38	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH , .	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016	0(O) -	3/7
39	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND , .	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2016	60(O) -	1/3
40	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND , .	12/2007	179.87 -	179.87	95.17	03/2012 -	03/2017	60(O) -	3/3
41	PURNADIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND , .	07/2008	210.98 -	210.98	151.89	03/2013 -	03/2017	48(O) -	4/4

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND , .	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48(O) -	2/4
43	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND , .	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2016	0(O) -	2/4
44	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND , .	06/2009	162.46 -	162.46	71.83	03/2014 -	03/2017	36(O) -	3/4
45	KISTARAM OCP - [N06000089]SCCL,TELANGANA , .	11/2010	242.29 -	242.29	8.03	03/2015 -	03/2018	36(O) -	0/5
46	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH , .	06/2011	1,131.28 1,131.28	1,131.28	236.49	03/2018 -	03/2018	0(O) -	6/9
47	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , .	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36(O) -	4/29
48	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , .	07/2011	447.06 -	447.06	77.44	03/2015 -	03/2018	36(O) -	4/13
49	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH , .	04/2012	258.56 -	258.56	102.72	03/2016 -	03/2018	24(O) -	3/6
50	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , .	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21(O) -	18/51
51	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , .	07/2012	417.33 -	417.33	27.85	07/2016 -	03/2019	32(O) -	6/28
52	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , .	11/2012	430.45 -	486.27	93.51	03/2016 -	03/2018	24(O) -	7/39
53	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND , .	02/2012	858.11 -	858.11	110.10	03/2020 -	03/2020	0(O) -	3/3
54	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH , .	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	0(O) -	1/7
55	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , .	02/2014	555.52 -	555.52	3.52	03/2021 -	03/2017	-48(O) -	0/2
56	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH , .	05/2014	164.49 -	164.49	76.43	03/2020 -	03/2020	0(O) -	3/6
57	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , .	05/2014	479.15 -	479.15	10.89	03/2019 -	03/2019	0(O) -	1/9
58	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , .	05/2014	3,756.36 -	3,756.36	620.96	03/2026 -	03/2026	0(O) -	3/15
59	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , .	05/2014	337.66 -	337.66	0.74	03/2019 -	03/2019	0(O) -	2/6
60	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , .	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
61	GARJANBAHAL OCP - [N06000117]MCL,ODISHA , .	11/2014	1,375.38 -	1,375.38	179.12	03/2021 -	03/2021	0(O) -	1/9
62	DINESH OCP - [N06000118]WCL,MAHARASHTRA , .	11/2014	611.16 -	611.16	232.58	03/2020 -	03/2020	0(O) -	3/9
63	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , .	09/2014	266.23 -	266.23	106.05	03/2021 -	03/2021	0(O) -	4/12
64	GOKUL - [N06000120]WCL,MAHARASHTRA , .	11/2014	267.67 -	267.67	175.50	03/2018 -	03/2018	0(O) -	2/8
65	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA , .	02/2015	187.94 -	187.94	39.64	03/2023 -	03/2023	0(O) -	5/10
66	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , .	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	AMERA OC RCE - [N06000123]SECL,CHHATISGARH , .	02/2015	335.97 -	335.97	34.09	03/2018 -	03/2018	0(O) -	1/4
68	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , .	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021	0(O) -	0/7
69	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , .	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021	0(O) -	0/6
70	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , .	05/2015	295.56 -	295.56	78.27	03/2019 -	03/2019	0(O) -	6/14
71	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA , .	05/2015	397.09 -	397.09	0.05	03/2019 -	03/2019	0(O) -	5/18
72	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , .	06/2015	205.49 -	205.49	1.37	03/2020 -	03/2020	0(O) -	4/13
73	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , .	06/2015	483.69 -	483.69	48.67	03/2021 -	03/2021	0(O) -	3/9
74	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , .	08/2015	727.28 -	727.28	72.15	03/2025 -	03/2025	0(O) -	3/13
75	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , .	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	3/11
76	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , .	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	0/6
77	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH , .	07/2015	316.10 -	316.10	16.87	03/2020 -	03/2020	0(O) -	0/5
78	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH , .	02/2015	916.24 -	916.24	-	03/2023 -	03/2023	0(O) -	0/8
79	MALACHUA OPENCAS PROJECT - [N06000139]SECL,MADHYA PRADESH , .	10/2015	488.33 -	488.33	-	03/2023 -	03/2023	0(O) -	0/8
80	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH , .	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/0
81	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , .	11/2015	277.65 -	277.65	-	03/2021 -	03/2021	0(O) -	2/9
82	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , .	11/2015	498.42 -	498.42	-	03/2020 -	03/2018	-24(O) -	1/9
83	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , .	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022	0(O) -	0/24
84	KOYAGUDEM OPENCAS PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2018	0(O) -	0/0
85	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , .	06/2011	5,907.11 -	5,907.11	1,813.37	12/2015 04/2018	04/2018	28(O) 0(R)	13/35
86	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , .	08/2011	1,230.27 -	1,230.27	49.03	04/2015 04/2019	04/2019	48(O) 0(R)	1/6
87	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , .	08/2011	988.35 -	988.35	45.27	04/2017 -	04/2017	0(O) -	0/3
88	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU , .	04/2012	364.75 -	364.75	197.05	10/2014 -	04/2016	18(O) -	8/10
89	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , .	02/2011	339.88 -	339.88	12.08	04/2014 -	06/2016	26(O) -	4/7
90	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL , .	08/2012	1,055.05 -	1,055.05	225.81	03/2018 -	07/2018	4(O) -	5/15
91	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU , .	04/2013	1,458.17 -	1,458.17	30.39	06/2015 08/2019	08/2019	50(O) 0(R)	1/7

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND , .	09/2009	153.82 -	153.82	81.37	03/2014 -	09/2016	30(O) -	6/9
93	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	2.56	09/2019 -	09/2019	0(O) -	0/0
94	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND , .	08/2010	289.45 -	289.45	122.07	05/2014 -	10/2016	29(O) -	0/8
95	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND , .	10/2012	269.82 -	269.82	77.34	04/2014 -	11/2016	31(O) -	0/10
96	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	67.25	12/2019 -	12/2019	0(O) -	0/0
	Total		60,724.30 -	61,837.03	14,400.83				322/999
	<u>FERTILISERS</u>								
97	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA , .	10/2014	197.79 209.44	209.44	56.41	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	209.44	56.41				0/0
	<u>MINES</u>								
98	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH , .	09/2011	1,856.00 -	1,856.00	2.02	09/2017 -	09/2017	0(O) -	0/0
99	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO,MAHARASHTRA , Private	12/2015	355.13 355.13	355.13	107.67	11/2016 11/2016	11/2016	0(O) 0(R)	0/0
100	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 344.50	344.50	126.21	11/2016 11/2016	11/2016	0(O) 0(R)	0/0
	Total		2,555.63 -	2,555.63	235.90				0/0
	<u>STEEL</u>								
101	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH , .	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
102	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND , .	03/2015	255.19 -	255.19	27.42	03/2018 -	03/2018	0(O) -	0/0
103	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA , .	03/2007	149.73 173.00	175.94	177.06	12/2015 -	03/2017	15(O) -	0/0
104	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA , .	05/2005	768.88 1,060.00	1,070.97	1,070.97	02/2014 -	03/2016	25(O) -	0/0
105	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , .	07/2011	324.87 325.00	325.00	263.57	12/2015 -	03/2016	3(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
106	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN , .	05/2015	189.00 -	189.00	-	03/2017 -	03/2017	0(O) -	0/0
107	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR , .	10/2005	956.00 -	956.00	-	03/2015 -	03/2017	24(O) -	0/0
108	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , .	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
109	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	-	03/2016 -	03/2016	0(O) -	0/0
110	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA , .	04/2015	3,127.30 -	3,127.30	309.85	04/2018 -	04/2018	0(O) -	0/0
111	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , .	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
112	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA , .	04/2011	572.00 -	572.00	490.09	04/2013 09/2014	06/2015	-	18/19
113	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA , .	12/2011	187.33 -	187.33	175.60	10/2013 -	06/2016	32(O) -	2/5
114	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH , .	05/2012	404.16 -	404.16	289.28	07/2015 -	06/2017	23(O) -	0/1
115	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , .	12/2009	343.00 -	488.40	45.93	10/2016 -	06/2017	8(O) -	0/0
116	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , .	12/2007	253.92 254.00	253.92	193.97	06/2016 -	06/2016	0(O) -	0/0
117	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA , .	10/2011	175.49 207.00	206.71	125.65	12/2016 -	07/2017	7(O) -	0/0
118	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA , .	02/2011	898.55 -	898.55	419.60	05/2013 01/2015	08/2015	-	19/20
119	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH , .	07/2011	877.73 -	877.73	486.38	07/2015 -	08/2016	13(O) -	2/2
120	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA , .	06/2014	708.91 -	708.91	363.11	04/2016 -	09/2016	5(O) -	2/2
121	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH , .	12/2009	280.00 -	280.00	29.55	09/2016 -	09/2016	0(O) -	1/1
122	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA , .	04/2014	151.33 -	151.33	4.84	09/2017 -	09/2017	0(O) -	0/0
123	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , .	03/2015	1,034.01 -	1,034.01	53.68	10/2017 -	10/2017	0(O) -	0/0
124	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , .	08/2010	17,265.00 -	17,265.00	15,905.05	03/2013 -	11/2016	44(O) -	32/35
125	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , .	10/2013	245.67 -	245.67	115.64	05/2016 -	12/2016	7(O) -	1/3

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
126	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , .	04/2014	188.93 -	188.93	61.26	04/2015 -	12/2016	20(O) -	2/3
127	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH , .	01/2010	15,525.00 -	15,525.00	9,162.07	05/2015 12/2016	12/2016	19(O) 0(R)	34/81
128	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH , .	07/2011	974.76 -	974.76	261.96	07/2016 -	12/2016	5(O) -	1/1
129	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND , .	05/2015	1,154.18 -	1,154.18	78.00	12/2017 -	12/2017	0(O) -	0/0
130	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA , .	12/2007	202.61 227.00	227.00	197.59	12/2016 -	12/2016	0(O) -	0/0
131	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT , .	01/2013	175.00 -	175.00	-	- -	12/2017	- -	0/0
132	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , .	02/2014	787.29 -	787.29	251.53	12/2016 -	12/2016	0(O) -	0/0
133	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , .	02/2014	4,749.00 -	4,749.00	13.64	09/2017 -	-	-	0/0
	Total		53,712.21 -	54,241.65	30,793.35				114/173
	<u>PETROCHEMICALS</u>								
134	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM , .	04/2006	5,460.61 8,920.00	9,965.00	9,356.28	04/2012 12/2013	12/2015	-	23/26
	Total		5,460.61 -	9,965.00	9,356.28				23/26
	<u>PETROLEUM</u>								
135	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU , .	05/2013	711.00 -	711.00	7.98	- -	-	-	0/0
136	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE , .	04/2010	270.00 -	251.66	172.53	06/2012 -	01/2016	-	0/0
137	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU , .	11/2006	171.83 -	171.83	-	- -	-	-	0/0
138	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , .	01/2015	1,823.00 -	1,823.00	2.18	- -	-	-	0/0
139	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE , .	01/2015	2,321.00 -	2,321.00	2.56	- -	-	-	0/0
140	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE , .	02/2015	890.00 -	890.00	3.61	- -	-	-	0/0
141	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	38.82	01/2018 -	01/2018	0(O) -	0/61
142	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	173.28	78.73	01/2017 -	01/2017	0(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
143	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM , .	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30(O) -	0/0
144	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE , .	06/2009	2,915.00 -	2,915.00	1,381.47	12/2012 -	02/2019	74(O) -	7/14
145	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA , .	10/2015	607.06 714.25	714.25	99.05	10/2017 02/2018	02/2018	4(O) 0(R)	21/48
146	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	130.87	02/2020 -	02/2020	0(O) -	0/0
147	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH , .	01/2016	247.52 -	247.52	-	02/2019 -	02/2019	0(O) -	1/3
148	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM , .	03/2009	2,465.15 2,378.89	2,378.89	1,803.00	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
149	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE , .	12/2009	463.32 -	463.32	327.10	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
150	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA , .	03/2012	2,592.17 2,592.17	2,592.17	1,235.07	05/2014 03/2017	03/2017	34(O) 0(R)	0/21
151	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE , .	02/2011	913.00 -	913.00	523.10	08/2015 -	03/2017	19(O) -	0/0
152	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU , .	12/2012	279.00 -	279.00	190.86	12/2014 -	03/2016	15(O) -	58/58
153	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE , .	12/2009	309.81 462.79	462.79	275.04	10/2014 03/2017	03/2017	29(O) 0(R)	28/40
154	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE , .	07/2011	352.56 -	450.55	12.10	03/2017 03/2017	03/2018	12(O) 12(R)	0/0
155	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA , .	11/2014	6,068.80 -	6,068.80	1,057.64	04/2019 -	03/2019	-1(O) -	0/0
156	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI , .	08/2014	6,086.08 -	6,086.08	749.95	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
157	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA , .	03/2014	238.50 -	238.50	18.62	03/2017 -	03/2017	0(O) -	0/0
158	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA , .	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
159	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT , Central Sector Projects	11/2015	500.00 -	500.00	-	03/2017 -	03/2017	0(O) -	0/0
160	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA , .	01/2006	732.00 1,227.00	1,227.00	1,105.78	10/2011 -	04/2016	54(O) -	0/0
161	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT , .	09/2011	202.25 -	160.16	77.90	07/2016 -	04/2017	9(O) -	5/12
162	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU , .	05/2015	257.87 -	257.87	35.76	11/2016 -	04/2017	5(O) -	11/22
163	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,190.69	-	04/2018 -	04/2018	0(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
164	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects	02/2016	367.11 -	367.11	-	04/2017 -	04/2017	0(O) -	0/0
165	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE , .	01/2012	352.49 -	352.49	141.15	03/2014 05/2016	05/2016	26(O) 0(R)	0/3
166	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA , .	03/2012	14,225.00 -	16,504.00	11,119.68	05/2016 -	05/2016	0(O) -	0/30
167	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA , .	03/2013	1,138.50 686.58	686.58	595.62	04/2015 05/2016	05/2016	13(O) 0(R)	0/0
168	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KERALA , .	01/2006	993.00 1,693.00	1,693.00	1,459.15	01/2012 -	05/2016	52(O) -	0/0
169	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE , .	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
170	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA , .	06/2014	5,706.47 5,813.25	5,813.25	3,089.78	05/2017 05/2017	05/2017	0(O) 0(R)	6/16
171	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA , .	02/2015	2,899.93 2,098.43	2,098.43	757.83	05/2017 -	05/2017	0(O) -	0/0
172	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE , .	08/2009	1,793.00 -	1,793.00	1,387.48	09/2012 -	06/2016	45(O) -	6/7
173	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA , .	12/2009	1,584.00 -	1,584.00	1,355.41	08/2015 -	06/2016	10(O) -	3/12
174	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT , .	03/2009	317.64 -	240.95	127.28	09/2012 06/2016	06/2016	45(O) 0(R)	0/5
175	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA , .	12/2011	2,059.63 2,665.65	2,665.65	1,334.59	03/2015 06/2017	06/2017	27(O) 0(R)	0/17
176	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE , .	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	06/2017	30(O) 25(R)	0/8
177	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE , .	08/2011	586.00 -	586.00	440.18	08/2015 -	06/2016	10(O) -	3/12
178	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH , .	07/2014	419.04 -	419.04	339.10	01/2017 -	06/2016	-7(O) -	13/16
179	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT , .	12/2011	160.00 -	160.00	76.60	02/2016 02/2016	07/2016	5(O) 5(R)	0/0
180	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]IOCL,MANIPUR , Central Sector Projects	08/2010	103.02 -	171.04	114.42	07/2016 -	07/2016	0(O) -	5/10
181	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM , .	09/2012	871.35 -	1,200.00	565.63	03/2015 -	08/2016	17(O) -	0/5
182	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA , .	03/2014	3,150.00 -	3,150.00	193.74	09/2017 -	09/2017	0(O) -	0/0
183	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH , .	01/2011	141.86 -	232.00	174.38	09/2016 -	09/2016	0(O) -	0/12
184	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	195.63	-	09/2018 -	09/2018	0(O) -	0/0
185	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE , .	06/2007	736.65 -	736.65	514.33	09/2011 10/2016	10/2016	61(O) 0(R)	0/0
186	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR , .	04/2013	480.00 -	422.00	238.14	02/2016 -	10/2016	8(O) -	5/6
187	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN , .	11/2011	310.00 370.00	370.00	17.84	03/2013 10/2016	10/2016	43(O) 0(R)	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
188	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA , .	02/2012	666.00 838.08	838.08	606.85	11/2015 11/2016	11/2016	12(O) 0(R)	26/29
189	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU , .	03/2013	3,110.36 -	3,110.36	1,666.63	11/2015 11/2016	11/2016	12(O) 0(R)	47/52
190	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT , .	05/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
191	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE , .	07/2009	3,957.00 3,561.00	3,561.00	112.83	01/2013 12/2018	12/2018	71(O) 0(R)	12/38
192	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA , .	03/2011	861.79 1,256.72	1,256.72	1,017.24	05/2013 04/2016	12/2016	43(O) 8(R)	1/5
193	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE , .	05/2013	4,124.35 4,124.35	4,124.35	633.74	04/2016 12/2017	12/2017	20(O) 0(R)	0/6
194	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL , .	03/2014	3,076.00 -	3,076.00	284.19	09/2017 03/2018	12/2017	3(O) -3(R)	0/1
195	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE , .	03/2014	2,476.82 -	2,476.82	673.48	12/2018 -	12/2018	0(O) -	3/8
196	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , .	04/2011	191.96 -	191.96	112.86	05/2015 -	12/2016	19(O) -	0/12
197	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM , .	03/2009	228.64 -	214.19	142.35	12/2016 -	12/2016	0(O) -	0/0
198	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE , .	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5(O) -	1/39
199	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE , .	10/2011	725.00 -	725.00	185.40	11/2016 -	12/2016	1(O) -	0/14
200	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA , .	05/2015	2,443.00 -	2,443.00	148.72	12/2017 -	12/2017	0(O) -	0/0
201	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	975.16	12/2017 -	12/2017	0(O) -	0/0
202	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM , .	06/2010	202.94 -	202.94	2.95	01/2014 -	-	-	0/2
	Total		108,058.21 -	111,974.00	40,449.61				280/684
	<u>POWER</u>								
203	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH , .	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
204	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , .	07/2009	421.01 1,007.57	1,007.57	985.52	07/2013 01/2016	01/2016	-	25/26
205	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , .	01/2013	12,964.60 -	12,964.60	6,002.76	01/2018 -	01/2018	0(O) -	23/31
206	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , .	08/2014	288.49 -	288.49	76.80	02/2017 -	02/2017	0(O) -	1/12

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
207	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , .	02/2014	14,366.58 -	14,366.58	2,632.00	02/2019 -	02/2019	0(O) -	11/13
208	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , .	05/2011	195.42 -	195.42	62.56	02/2014 -	02/2018	48(O) -	1/1
209	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM , .	01/2008	4,375.35 6,749.18	6,749.18	5,944.00	09/2011 -	03/2017	66(O) -	21/37
210	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL , .	04/2010	4,404.57 -	4,404.57	2,556.75	01/2015 -	03/2017	26(O) -	8/16
211	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , .	02/2010	232.34 -	232.34	219.29	06/2012 -	03/2017	57(O) -	1/4
212	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE , .	03/2011	1,585.12 -	1,585.12	1,623.96	11/2013 -	03/2016	28(O) -	11/12
213	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE , .	07/2010	1,272.80 1,731.10	1,731.10	1,268.73	11/2012 03/2016	03/2017	52(O) 12(R)	8/13
214	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT , .	12/2011	552.44 609.44	609.44	600.90	02/2014 03/2016	03/2016	25(O) 0(R)	10/10
215	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE , .	12/2011	297.33 346.79	346.79	312.57	08/2014 06/2015	03/2017	31(O) 21(R)	8/10
216	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA , .	01/2012	15,166.19 -	15,166.19	10,699.00	01/2017 -	03/2017	2(O) -	31/40
217	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE , .	06/2014	5,151.37 -	5,151.37	719.20	03/2018 -	03/2018	0(O) -	8/12
218	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH , .	08/2014	188.75 -	188.75	85.90	02/2017 -	03/2016	-11(O) -	2/2
219	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR , .	10/2014	8,112.12 -	8,112.12	121.97	04/2020 -	03/2022	23(O) -	0/0
220	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH , .	09/2014	9,188.98 -	9,188.98	1,226.00	03/2019 -	03/2019	0(O) -	15/16
221	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE , .	01/2015	268.80 -	268.80	26.40	03/2018 -	03/2018	0(O) -	0/3
222	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , .	03/2015	197.40 -	197.40	-	03/2018 -	03/2018	0(O) -	0/0
223	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH , .	03/2015	550.06 -	550.06	23.80	03/2018 -	03/2018	0(O) -	0/3
224	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR , .	03/2010	3,984.03 -	3,984.03	3,290.44	01/2013 -	03/2016	38(O) -	1/1
225	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL , .	04/2007	4,122.00 8,781.30	9,606.82	8,357.23	02/2011 -	03/2016	61(O) -	26/26
226	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , .	02/2015	302.49 302.00	302.49	271.07	02/2016 -	03/2016	1(O) -	0/1

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
227	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH , .	01/2016	305.04 -	305.04	-	03/2017 -	03/2017	0(O) -	0/0
228	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE , .	02/2009	410.29 -	410.29	373.67	02/2012 -	04/2016	50(O) -	7/10
229	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE , .	03/2010	965.58 -	965.58	776.84	11/2012 -	04/2016	41(O) -	7/10
230	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE , .	02/2012	1,927.16 1,940.58	1,940.58	1,604.27	10/2014 03/2016	04/2016	18(O) 1(R)	5/7
231	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE , .	06/2014	400.47 -	400.47	57.90	04/2017 -	04/2017	0(O) -	0/3
232	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , .	12/2014	6,517.36 -	6,517.36	430.30	04/2018 -	04/2018	0(O) -	3/12
233	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , .	04/2015	3,705.61 -	3,705.61	352.70	04/2018 -	04/2018	0(O) -	4/9
234	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , .	04/2015	1,479.30 -	1,479.30	113.20	04/2017 -	04/2017	0(O) -	2/8
235	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , .	02/2005	8,692.97 15,095.67	15,095.67	11,675.00	01/2011 05/2018	05/2018	88(O) 0(R)	27/48
236	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE , .	08/2010	1,677.57 -	1,677.57	1,471.42	04/2013 -	05/2016	37(O) -	9/11
237	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE , .	05/2010	250.03 390.51	390.51	246.70	01/2013 03/2016	05/2016	40(O) 2(R)	13/15
238	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE , .	12/2011	2,422.66 -	2,422.66	2,448.76	08/2014 -	05/2016	21(O) -	11/14
239	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA , .	02/2014	167.40 -	167.40	90.50	12/2015 -	05/2016	5(O) -	6/8
240	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE , .	01/2015	3,662.02 -	3,662.02	451.20	05/2018 -	05/2018	0(O) -	0/5
241	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , .	03/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017	0(O) -	0/9
242	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH-PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH , .	05/2015	312.94 -	312.94	36.50	05/2016 -	05/2016	0(O) -	0/0
243	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU , .	01/2016	162.11 -	162.11	-	05/2018 -	05/2018	0(O) -	0/0
244	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND , .	11/2006	2,978.48 3,846.30	3,846.30	2,788.00	03/2013 -	06/2019	75(O) -	3/15
245	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE , .	02/2009	509.66 -	509.66	558.96	11/2011 -	06/2016	55(O) -	8/11

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
246	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE , .	12/2009	1,216.83 -	1,216.83	1,073.59	08/2012 -	06/2016	46(O) -	3/5
247	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE , .	07/2010	752.64 689.03	689.03	561.02	07/2013 11/2015	06/2016	35(O) 7(R)	7/9
248	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH , .	05/2011	1,961.87 2,310.58	2,310.58	1,801.75	05/2014 06/2016	06/2016	25(O) 0(R)	8/12
249	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND , .	10/2011	558.26 -	558.26	554.11	11/2013 -	06/2016	31(O) -	8/12
250	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH , .	01/2012	1,422.85 -	1,422.85	1,474.62	01/2015 -	06/2016	17(O) -	9/11
251	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE , .	03/2012	198.63 -	198.63	104.63	09/2014 -	06/2016	21(O) -	0/0
252	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH , .	03/2012	9,569.76 -	9,569.76	5,922.99	06/2015 -	06/2016	12(O) -	21/30
253	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE , .	11/2011	723.63 -	723.63	606.22	11/2014 -	06/2016	19(O) -	7/10
254	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE , .	02/2012	3,201.44 -	3,201.44	3,186.31	10/2014 -	06/2016	20(O) -	9/17
255	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE , .	09/2012	524.40 -	524.40	348.02	05/2015 -	06/2016	13(O) -	10/12
256	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH , .	12/2012	11,846.00 -	11,846.00	6,152.00	06/2017 -	06/2017	0(O) -	23/40
257	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE , .	09/2013	680.69 -	680.69	484.19	03/2016 -	06/2016	3(O) -	10/12
258	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE , .	09/2013	1,575.30 -	1,575.30	864.80	05/2016 -	06/2016	1(O) -	8/13
259	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE , .	02/2014	539.82 -	539.82	133.60	06/2016 -	06/2016	0(O) -	8/11
260	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE , .	02/2014	908.08 -	908.08	249.80	06/2016 -	06/2016	0(O) -	9/18
261	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE , .	03/2014	155.57 -	155.57	8.90	03/2016 -	06/2016	3(O) -	2/6
262	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE , .	02/2014	196.58 -	196.58	28.80	02/2016 -	06/2016	4(O) -	7/17
263	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND , .	08/2006	2,313.00 4,138.41	4,237.67	3,453.39	12/2011 03/2016	06/2016	54(O) 3(R)	13/14
264	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA , .	01/2016	187.04 -	187.04	-	06/2018 -	06/2018	0(O) -	0/0
265	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH , .	12/2004	2,496.90 6,179.96	6,179.96	4,574.78	12/2009 07/2016	07/2016	79(O) 0(R)	16/30
266	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH , .	12/2008	573.99 1,262.27	1,262.27	1,160.87	08/2013 07/2016	07/2016	35(O) 0(R)	29/38

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
267	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE , .	05/2014	303.07 -	303.07	25.10	07/2016 -	07/2016	0(O) -	3/9
268	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE , .	01/2015	203.28 -	203.28	18.38	07/2017 -	07/2017	0(O) -	0/5
269	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI , .	05/2015	780.33 -	780.33	0.90	07/2017 -	07/2017	0(O) -	0/0
270	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE , .	07/2015	2,247.37 -	2,247.37	16.50	07/2018 -	07/2018	0(O) -	0/0
271	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT , .	01/2016	244.19 -	244.19	-	07/2018 -	07/2018	0(O) -	0/0
272	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE , .	01/2016	1,455.47 -	1,455.47	-	07/2018 -	07/2018	0(O) -	0/0
273	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH , .	01/2016	207.88 -	207.88	-	07/2018 -	07/2018	0(O) -	0/0
274	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA , .	03/2012	9,395.18 -	9,395.18	6,254.00	11/2016 -	08/2017	9(O) -	27/31
275	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND , .	07/2012	1,527.00 -	1,527.00	143.00	08/2017 -	08/2017	0(O) -	0/9
276	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE , .	03/2013	514.20 -	514.20	369.70	06/2015 -	08/2016	14(O) -	7/10
277	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE , .	06/2012	1,909.24 -	1,909.24	1,088.53	06/2015 -	08/2016	14(O) -	3/5
278	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , .	05/2014	829.98 -	829.98	138.90	08/2016 -	08/2016	0(O) -	1/4
279	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , .	02/2014	12,532.44 -	12,532.44	3,068.00	08/2018 -	08/2018	0(O) -	18/18
280	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL , .	09/2005	1,061.38 -	2,193.08	2,011.96	09/2009 -	09/2016	84(O) -	3/6
281	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , .	07/2006	1,657.00 - 2,978.86	2,978.86	1,706.73	02/2016 09/2019	09/2019	43(O) 0(R)	12/21
282	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU , .	09/2011	1,940.13 -	1,940.13	1,991.86	09/2014 -	09/2016	24(O) -	8/13
283	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , .	03/2013	11,638.55 -	11,638.55	5,427.00	09/2017 -	09/2017	0(O) -	20/41
284	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE , .	10/2013	1,364.52 -	1,364.52	556.04	04/2016 -	09/2016	5(O) -	8/12
285	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL , .	09/2014	1,381.84 -	1,381.84	174.00	09/2019 -	09/2019	0(O) -	4/5
286	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE , .	03/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017	0(O) -	0/0
287	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR , .	01/2007	5,353.00 -	5,353.00	5,472.83	05/2014 -	09/2017	40(O) -	1/4

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
288	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , .	04/2012	9,750.89 -	9,750.89	5,079.75	12/2016 -	09/2017	9(O) -	25/32
289	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH , .	03/2015	9,870.51 -	9,870.51	1,536.00	09/2019 -	09/2019	0(O) -	10/10
290	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM , .	07/1998	368.72 1,381.71	1,381.71	1,005.51	07/2006 10/2016	10/2016	123(O) 0(R)	5/13
291	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT , .	02/2014	378.71 -	378.71	125.80	10/2016 -	10/2016	0(O) -	8/11
292	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE , .	01/2015	871.62 -	871.62	38.50	10/2017 -	10/2017	0(O) -	0/5
293	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL,GUJARAT , .	10/2015	315.00 -	315.00	13.50	10/2016 -	10/2016	0(O) -	0/0
294	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR , .	01/2009	3,642.04 -	5,751.47	4,490.39	01/2016 -	11/2016	10(O) -	7/9
295	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE , .	01/2014	374.63 -	374.63	17.20	04/2016 -	11/2016	7(O) -	0/0
296	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE , .	05/2014	522.29 -	522.29	120.80	11/2016 -	11/2016	0(O) -	2/12
297	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE , .	11/2014	972.42 -	972.42	74.00	11/2017 -	11/2017	0(O) -	0/3
298	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN , .	07/2015	307.18 -	307.18	12.70	11/2017 -	11/2017	0(O) -	0/0
299	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH , .	09/2002	3,919.59 -	8,398.76	5,548.25	09/2009 -	12/2018	111(O) -	2/3
300	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU , .	05/2005	1,779.29 2,187.32	2,187.32	1,907.75	11/2008 01/2016	12/2016	97(O) 11(R)	20/22
301	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , .	12/2007	477.69 738.48	738.48	602.69	09/2010 01/2016	12/2016	75(O) 11(R)	4/8
302	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND , .	08/2008	2,491.58 -	2,491.58	824.04	06/2013 -	12/2019	78(O) -	7/8
303	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE , .	10/2008	4,824.12 -	4,824.12	4,277.58	10/2012 -	12/2016	50(O) -	7/11
304	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE , .	02/2009	11,130.19 13,762.80	13,762.80	11,612.50	08/2013 12/2017	12/2017	52(O) 0(R)	17/26
305	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE , .	02/2010	2,144.00 2,932.88	2,932.88	2,315.20	12/2012 12/2016	12/2016	48(O) 0(R)	11/23
306	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , .	10/2011	487.49 639.46	639.46	448.72	06/2014 03/2016	12/2016	30(O) 9(R)	10/12
307	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH , .	11/2011	2,127.51 -	2,127.51	2,350.13	07/2014 -	12/2016	29(O) -	6/8
308	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH , .	12/2011	1,746.65 2,228.71	2,228.71	1,501.63	08/2014 12/2015	12/2016	28(O) 12(R)	7/11

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
309	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , .	03/2012	7,921.47 -	7,921.47	5,285.00	09/2016 -	12/2016	3(O) -	33/37
310	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , .	03/2013	2,514.88 -	2,514.88	1,080.15	12/2015 -	12/2016	12(O) -	15/18
311	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , .	07/2013	3,363.12 -	3,363.12	1,261.00	12/2016 -	12/2016	0(O) -	19/20
312	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR , .	05/2015	436.68 -	436.68	439.94	12/2016 -	12/2016	0(O) -	0/1
313	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH , .	09/2003	6,285.33 -	18,063.89	8,357.64	09/2010 -	-	-	0/0
	Total		304,580.02 -	354,153.57	192,162.73				864/1317
	<u>HEAVY INDUSTRY</u>								
314	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE , .	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
315	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM , .	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	15(O) -	0/0
316	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA , .	09/2014	505.58 -	505.58	14.38	03/2018 -	03/2018	0(O) -	0/0
317	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI , .	11/2013	196.70 -	196.70	165.97	01/2016 -	04/2016	3(O) -	0/0
318	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI , .	12/2013	204.44 -	204.44	36.17	05/2017 -	05/2017	0(O) -	0/0
319	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI , .	08/2014	293.65 -	293.65	67.84	05/2017 -	05/2017	0(O) -	0/0
320	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL , .	12/2014	168.90 -	168.90	3.63	05/2017 -	05/2017	0(O) -	0/0
321	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI , .	09/2013	444.70 -	444.70	285.20	12/2015 -	06/2016	6(O) -	0/0
322	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH , .	10/2013	159.50 -	159.50	120.80	11/2013 -	06/2016	31(O) -	0/0
323	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI , .	02/2013	414.11 -	414.11	210.91	11/2013 -	11/2014	-	0/0
	Total		2,563.15 -	2,563.15	1,018.40				0/0
	<u>RAILWAYS</u>								
324	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND , .	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005 -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
325	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE , ,	09/1998	247.66 3,500.00	3,500.00	1,007.95	05/2008 -	-	-	0/0
326	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL , ,	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
327	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA , ,	04/1996	301.64 -	1,185.64	577.84	- 09/2009	-	-	0/0
328	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND , ,	04/2002	459.91 -	418.17	260.67	- -	-	-	0/0
329	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR , ,	04/2002	921.00 -	2,363.00	1,691.12	03/2009 -	-	-	0/0
330	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR , ,	04/2001	624.47 -	2,921.00	2,521.72	10/2007 -	-	-	0/0
331	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA , ,	04/1998	183.23 -	1,202.70	185.46	02/2015 -	-	-	0/0
332	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT , ,	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
333	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR , ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
334	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR , ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
335	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR, MULTI STATE , ,	04/2008	822.39 -	1,280.83	1,031.83	- -	-	-	0/0
336	BAGALKOT-KUDACHI NL - [N22000258]SWR, KARNATAKA , ,	04/2010	377.93 -	986.30	100.76	- -	-	-	0/0
337	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE , ,	04/2012	1,054.35 2,200.00	2,200.00	51.67	- -	-	-	0/0
338	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR, KARNATAKA , ,	04/2010	2,127.00 -	2,127.00	325.00	- -	-	-	0/0
339	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA , ,	03/2011	679.27 -	1,111.99	60.31	- -	-	-	0/0
340	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR, UTTAR PRADESH , ,	04/1997	836.26 -	1,072.51	-	- -	-	-	0/0
341	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	- -	-	-	0/0
342	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL , ,	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
343	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE , ,	04/2006	96.16 -	260.16	240.21	- -	01/2015	-	0/0
344	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR) - [220100106]SCR, TELANGANA , ,	12/1994	124.43 -	925.30	712.02	- -	02/2014	-	0/0
345	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE , ,	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
346	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE , ,	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
347	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE , ,	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
348	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE , ,	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
349	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL , .	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	- -	0/0
350	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA , .	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144(O) -	0/0
351	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH , .	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	- -	0/0
352	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , .	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	- -	0/0
353	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE , .	04/1997	218.24 236.41	645.00	309.19	- -	03/2015	- -	0/0
354	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR , .	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
355	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA , .	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	- -	0/0
356	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE , .	04/1999	744.71 -	744.71	576.86	- -	03/2016	- -	1/1
357	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE , .	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
358	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR , .	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
359	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND , .	04/1996	768.87 -	768.87	682.31	- 03/2010	03/2010	- -	0/0
360	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH , .	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	- -	0/0
361	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH , .	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	- -	0/0
362	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU , .	09/2006	343.17 -	914.98	846.18	- -	03/2016	- -	0/0
363	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM , .	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	- -	0/0
364	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR , .	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	- -	0/0
365	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH , .	04/2006	325.00 2,434.00	2,434.00	419.45	03/2010 -	03/2017	84(O) -	0/0
366	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA , .	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
367	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH , .	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
368	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA , .	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
369	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM , .	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
370	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR , .	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
371	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM , .	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
372	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN , .	04/2008	829.74 -	829.74	96.76	03/2015 -	03/2015	- -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
373	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND , .	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
374	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM , .	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
375	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM , .	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84(O) -	0/0
376	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND , .	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
377	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE , .	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	- -	0/0
378	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL , .	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	- -	0/0
379	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA , .	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108(O) -	0/0
380	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , .	04/2012	252.00 -	886.65	-	- -	03/2018	- -	0/0
381	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND , .	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	- -	0/0
382	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL , .	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
383	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL , .	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0
384	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU , .	04/2007	247.00 -	951.24	619.87	- -	03/2015	- -	0/0
385	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA , .	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
386	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE , .	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	- -	0/0
387	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE , .	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	- -	0/0
388	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE , .	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	- -	0/0
389	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE , .	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	- -	0/0
390	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM , .	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	- -	0/0
391	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM , .	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	- -	0/0
392	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRT,MAHARASHTRA , .	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11(O) -	0/0
393	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE , .	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	- -	0/0
394	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE , .	04/2011	299.60 -	299.60	-	03/2017 -	03/2017	0(O) -	0/0
395	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE , .	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	- -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
396	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE , .	04/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	0(O) -	0/0
397	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , .	04/2007	98.74 -	203.00	227.84	- -	03/2015	-	0/0
398	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , PPP (BOT)	03/2012	1,503.71 -	1,503.71	175.26	- -	03/2020	- -	0/0
399	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH , .	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	- -	0/0
400	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA , .	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86(O) 86(R)	0/0
401	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM , .	09/1997	1,500.00 -	4,996.19	4,102.70	04/2008 12/2011	06/2017	110(O) 66(R)	0/0
402	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH , .	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	-	0/0
403	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU , .	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
404	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , .	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87(O) -	0/0
405	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL , .	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(O) -	0/0
406	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL , .	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27(O) -	0/0
407	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA , .	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
408	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA , .	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
409	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , .	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	-	0/0
410	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL , .	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	-	0/0
411	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA , .	04/2010	203.40 -	203.40	153.29	- -	09/2015	-	0/0
412	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , .	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	-	0/0
413	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA , .	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
414	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA , .	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91(O) 91(R)	0/0
415	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL , .	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
416	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , .	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181(O) -	0/0
417	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , .	02/1997	386.30 -	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
418	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND , .	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
419	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL , .	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
420	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , .	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
421	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , .	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93(O) -	0/0
422	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL , .	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
423	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL , .	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57(O) -	0/0
424	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL , .	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33(O) -	0/0
425	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , .	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	- -	0/0
426	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA , .	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
427	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , .	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	- -	0/0
428	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA , .	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21(O) -	0/0
429	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA , .	03/2012	155.81 -	155.81	18.25	- -	12/2016	- -	0/0
430	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , .	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
431	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE , .	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
432	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH , .	04/1995	304.00 -	304.00		12/2012 -	-	-	0/0
433	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , .	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
434	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA , .	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
435	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA , .	02/1997	295.00 -	1,289.92	1,092.98	- -	-	-	0/0
436	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN , .	02/1997	410.08 -	410.08	297.58	- -	-	-	0/0
437	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE , .	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
438	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU , .	02/1997	155.55 -	800.00	800.70	- -	-	-	0/0
439	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA , .	04/1997	227.00 997.58	2,135.00	117.24	- -	-	-	0/0
440	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL , .	04/1974	393.46 154.30	154.46		03/2007 03/2007	-	-	0/0
441	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR , .	04/1997	501.69 501.69	1,043.56	819.19	03/2012 -	-	-	0/0
442	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , .	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
443	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , .	04/1997	162.87 -	541.00	158.58	- -	-	-	0/0
444	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE , .	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
445	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU , .	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
446	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , .	03/1998	280.00 -	1,122.00	889.95	- -	-	-	0/6
447	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH , .	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
448	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL , .	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
449	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , .	04/1998	92.63 -	270.00	376.18	02/2011 02/2011	-	-	0/0
450	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE , .	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
451	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA , .	04/1996	138.00 -	1,382.78	2.81	- -	-	-	0/0
452	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA , .	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
453	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR , .	04/2003	528.65 -	324.66	227.03	- -	-	-	0/0
454	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR , .	04/2002	322.95 -	341.41	325.36	03/2012 -	-	-	0/0
455	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR , .	04/2001	406.92 -	339.00	204.83	- -	-	-	0/0
456	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR , .	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0
457	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE , .	04/2005	230.03 -	230.03	172.58	- -	-	-	0/0
458	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA , .	04/2005	810.78 -	810.80	160.80	- -	-	-	0/0
459	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH , .	04/2003	136.62 -	360.00	357.91	12/2007 03/2010	-	-	0/0
460	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR , .	04/1996	332.92 332.92	477.88	498.37	03/2012 -	-	-	0/0
461	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA , .	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
462	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND , .	03/1997	261.70 -	360.00	253.92	02/2006 -	-	-	0/0
463	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH , .	07/2006	743.00 -	732.81	770.18	03/2008 06/2008	-	-	0/0
464	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU , .	09/2007	404.19 -	1,383.45	457.88	- -	-	-	0/0
465	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE , .	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
466	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU , .	09/2006	125.00 -	490.00	67.57	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
467	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU , .	09/2006	456.00 -	1,080.00	194.61	- -	-	-	0/0
468	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL , .	04/2007	1,106.62 -	1,106.62	244.99	12/2010 -	-	-	0/0
469	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL , .	04/2010	2,298.42 -	1,655.68	38.46	03/2014 -	-	-	0/0
470	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN , PPP (BOT)	04/2008	653.19 -	653.55	258.78	03/2014 -	-	-	0/0
471	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN , .	04/2008	516.23 732.06	516.23	597.72	03/2014 -	-	-	0/0
472	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND , .	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
473	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL , .	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
474	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL , .	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
475	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH , .	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
476	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT , .	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
477	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT , .	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
478	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT , .	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
479	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT , .	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
480	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH , .	03/2013	307.00 -	307.00	-	- -	-	-	0/0
481	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE , .	03/2007	243.78 -	243.78	30.05	- -	-	-	0/0
482	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH , .	03/2008	195.64 -	195.64	94.11	- -	-	-	0/0
483	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH , .	03/2012	199.75 -	199.75	76.08	- -	-	-	0/0
484	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE , .	03/2013	295.00 -	494.92	4.22	- -	-	-	0/0
485	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH , .	03/2013	643.00 -	643.00	-	- -	-	-	0/0
486	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN , .	04/2012	246.08 -	246.08	4.20	- -	-	-	0/0
487	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE , .	04/2007	1,347.26 -	1,347.26	164.55	- -	-	-	0/0
488	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE , .	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
489	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT , .	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
490	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT , .	04/2012	376.59 -	376.59	4.58	- -	-	-	0/0
491	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT , .	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
492	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , .	04/1994	320.66 913.48	913.48	457.67	- -	-	-	0/0
493	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , .	04/2011	446.00 -	685.17	206.59	- -	-	-	0/0
494	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , .	04/2010	279.40 -	279.40	249.02	- -	-	-	0/0
495	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE , .	04/2011	2,082.75 -	3,500.00	54.23	- -	-	-	0/0
496	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , .	04/2013	236.93 -	262.00	0.41	- -	-	-	0/0
497	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN , .	04/2013	822.00 -	822.00	-	- -	-	-	0/0
498	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , .	04/2013	323.00 -	323.00	-	- -	-	-	0/0
499	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN , .	04/2013	456.00 -	855.16	557.82	- -	-	-	0/0
500	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , .	04/2010	739.65 -	872.22	794.11	- -	-	-	0/0
501	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN , .	04/2011	239.73 -	179.32	75.76	- -	-	-	0/0
502	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , .	04/2011	213.39 -	218.39	23.63	- -	-	-	0/0
503	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , .	04/2012	288.97 -	288.97	1.09	- -	-	-	0/0
504	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , .	04/2013	242.09 -	242.09	0.39	- -	-	-	0/0
505	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL , .	04/2010	267.37 -	434.00	35.90	- -	-	-	0/0
506	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL , .	04/2011	289.64 -	760.00	0.09	- -	-	-	0/0
507	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , .	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
508	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR , .	04/2008	620.57 -	620.57	-	- -	-	-	0/0
509	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR , .	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
510	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE , .	04/2008	415.67 -	415.67	14.00	- -	-	-	0/0
511	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR , .	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
512	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR , .	04/1999	175.69 -	325.00	259.31	- -	-	-	0/0
513	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR , .	04/2006	285.07 -	378.56	111.87	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
514	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR , .	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
515	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR , .	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0
516	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR , .	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
517	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR , .	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
518	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR , .	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
519	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , .	04/2004	372.14 -	355.81	294.07	- -	-	-	0/0
520	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR , .	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
521	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR , .	04/2013	213.01 -	367.17	17.19	- -	-	-	0/0
522	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU , .	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
523	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE , .	04/2008	523.52 -	1,200.00	2.07	- -	-	-	0/0
524	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , .	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
525	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU , .	04/1999	198.68 -	556.64	268.56	- -	-	-	0/0
526	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU , .	04/1998	271.24 -	520.00	462.69	- -	-	-	0/0
527	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE , .	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0
528	KUMBALAM-TURAVUR - [N22000191]SR,KERALA , .	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
529	ERODE-PALANI - [N22000199]SR,TAMIL NADU , .	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
530	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , .	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
531	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , .	04/2006	191.72 -	222.95	112.40	- -	-	-	0/0
532	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , .	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
533	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL , .	04/2009	573.78 -	573.78	166.89	- -	-	-	0/0
534	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE , .	04/2011	601.43 -	800.00	0.69	- -	-	-	0/0
535	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , .	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
536	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , .	04/2007	450.00 -	450.00	7.91	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
537	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , .	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
538	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , .	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
539	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , .	04/2011	288.35 -	288.35	9.60	- -	-	-	0/0
540	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , .	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
541	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE , .	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
542	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , .	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
543	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , .	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
544	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , .	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
545	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , .	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
546	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , .	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
547	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , .	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
548	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , .	04/2008	499.30 -	2,501.05	84.11	- -	-	-	0/0
549	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , .	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0
550	BARIARPUUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , .	04/2007	450.55 -	450.55	13.53	- -	-	-	0/0
551	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , .	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
552	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , .	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
553	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , .	04/2011	193.44 -	193.44	53.01	- -	-	-	0/0
554	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , .	04/2011	175.80 -	175.80	1.46	- -	-	-	0/0
555	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , .	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
556	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKUPUR NL - [N22000241]ER,MULTI STATE , .	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
557	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE , .	04/2003	337.96 -	337.96	61.36	- -	-	-	0/0
558	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , .	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
559	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]JR,MAHARASHTRA , .	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
560	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , .	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
561	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , .	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
562	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]JR,MAHARASHTRA , .	04/2012	297.85 -	297.85	7.17	- -	-	-	0/0
563	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , .	04/2011	913.00 -	1,801.01	1.47	- -	-	-	0/0
564	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , .	04/2007	179.65 -	1,350.91	380.62	- -	-	-	0/0
565	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , .	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
566	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE , .	04/2013	723.00 -	723.00	-	- -	-	-	0/0
567	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE , .	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
568	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , .	04/2012	923.23 -	923.23	1.01	- -	-	-	0/0
569	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH , .	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
570	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , .	04/2012	377.44 -	377.44	7.50	- -	-	-	0/0
571	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB , .	04/2009	396.04 -	369.00	188.93	- -	-	-	0/0
572	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , .	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
573	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH , .	04/2013	654.00 -	654.00	-	- -	-	-	0/0
574	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , .	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
575	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , .	04/2012	287.00 -	576.18	3.40	- -	-	-	0/0
576	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH , .	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
577	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , .	04/2007	336.91 -	336.91	144.25	- -	-	-	0/0
578	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , .	04/2013	558.00 -	692.43	-	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
579	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , .	04/2013	296.00 -	466.65	-	-	-	-	0/0
580	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , .	04/2011	562.74 -	832.47	0.94	-	-	-	0/0
581	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE , .	04/2007	970.34 -	1,743.00	359.06	-	-	-	0/0
582	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , .	04/2011	341.05 -	348.85	0.34	-	-	-	0/0
583	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI , .	04/2012	295.68 -	295.68	0.86	-	-	-	0/0
584	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , .	04/2013	829.00 -	829.00	-	-	-	-	0/0
585	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA , .	04/2011	390.60 -	390.60	4.69	-	-	-	0/0
586	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , .	04/2011	1,313.48 -	1,313.48	5.13	-	-	-	0/0
587	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , .	04/2010	337.49 -	337.50	0.21	-	-	-	0/0
588	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE , .	04/2008	2,050.00 -	2,050.00	194.45	-	-	-	0/0
589	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND , .	04/2012	219.83 -	329.97	2.38	-	-	-	0/0
590	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE , .	04/2010	338.54 -	338.54	129.14	-	-	-	0/0
591	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE , .	04/2008	162.96 -	162.96	143.62	-	-	-	0/0
592	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA , .	04/2013	400.00 -	400.00	-	-	-	-	0/0
593	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE , .	04/2013	876.00 -	876.00	-	-	-	-	0/0
594	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH , .	04/2012	380.00 -	380.00	1.38	-	-	-	0/0
595	QADIAN-BEAS - [N22000295]NR,PUNJAB , .	04/2011	205.22 -	205.22	1.54	-	-	-	0/0
596	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE , .	04/2007	328.14 -	328.14	0.31	-	-	-	0/0
597	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , .	04/2011	146.75 -	167.50	0.32	-	-	-	0/0
598	GADAG-WADI NL - [N22000299]SWR,KARNATAKA , .	04/2013	1,117.00 -	1,922.00	1.89	-	-	-	0/0
599	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , .	04/2013	327.25 -	367.77	-	-	-	-	0/0
600	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE , .	04/2012	250.93 -	250.93	0.14	-	-	-	0/0
601	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL , .	04/2012	255.64 -	255.64	-	-	-	-	0/0
602	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU , .	04/1999	460.94 -	1,030.00	-	01/1999 -	-	-	0/0
603	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , .	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
604	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , .	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
605	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , .	04/2012	285.57 -	279.54	1.38	01/1999 -	-	-	0/0
606	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL , .	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
607	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA , .	03/2013	858.67 -	837.33	1.15	-	-	-	0/0
608	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA , .	03/2006	201.00 -	230.00	218.67	-	-	-	0/0
609	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA , .	03/2011	165.16 -	234.71	137.01	03/2015 -	-	-	0/0
610	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH , .	04/2014	182.92 -	197.73	-	-	-	-	0/0
611	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU , .	04/2011	190.10 -	190.10	33.19	-	-	-	0/0
612	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA , .	03/2015	1,900.00 -	1,900.00	-	-	-	-	0/0
613	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE , .	05/2015	600.00 -	600.00	-	-	-	-	0/0
614	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE , .	03/2015	1,830.00 -	1,830.00	-	-	-	-	0/0
615	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE , .	05/2015	860.43 -	860.43	-	-	-	-	0/0
616	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR , .	05/2015	380.00 -	380.00	-	-	-	-	0/0
617	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN , .	05/2015	873.71 -	873.71	-	-	-	-	0/0
618	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA , .	05/2015	400.00 -	400.00	-	-	-	-	0/0
619	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA , .	03/2015	960.00 -	960.00	-	-	-	-	0/0
620	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE , .	03/2015	1,618.00 -	1,618.00	-	-	-	-	0/0
621	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE , .	05/2015	720.00 -	720.00	-	-	-	-	0/0
	Total		254,176.67 -	327,636.22					1/7
	ROAD TRANSPORT AND HIGHWAYS								
622	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM , .	12/2003	157.47 -	157.47	-	09/2007 -	-	-	0/0
623	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR , .	12/2003	300.00 -	300.00	-	10/2008 -	-	-	0/0
624	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH , .	12/2003	251.03 -	251.03	-	10/2008 -	-	-	0/0
625	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL , .	12/2003	225.00 -	225.00	-	07/2008 -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
626	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
627	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
628	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
629	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA , .	03/2005	557.00 -	557.00	932.30	02/2010 -	-	-	0/0
630	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	-	-	2/2
631	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH , .	05/2009	572.30 -	572.30	761.40	10/2011 -	-	-	0/0
632	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN , PPP (BOT)	06/2010	792.06 -	792.06	1,983.00	12/2012 -	-	-	0/0
633	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , .	09/2010	946.00 -	946.00	-	- -	-	-	3/3
634	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU , PPP (BOT)	09/2010	1,655.00 -	1,655.00	641.78	09/2013 -	-	-	0/0
635	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
636	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND , .	08/2010	625.07 -	625.07	-	01/2013 -	-	-	0/0
637	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA , .	02/2010	390.56 -	390.56	-	02/2012 -	-	-	0/0
638	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA , .	04/2011	807.00 -	807.00	-	10/2014 -	-	-	0/0
639	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA , .	12/2010	453.00 -	453.00	487.90	- -	-	-	1/1
640	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA , .	12/2010	480.00 -	480.00	438.00	- -	-	-	2/2
641	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA , .	11/2010	680.00 -	680.00	-	- -	-	-	2/2
642	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT , PPP (BOT)	03/2011	785.50 -	785.50	919.56	08/2013 -	-	-	0/3
643	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA , .	02/2011	226.00 -	226.00	-	02/2014 -	-	-	0/0
644	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR , .	12/2011	325.51 -	325.00	160.20	05/2014 -	-	-	0/0
645	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND , .	02/2012	398.00 -	398.00	-	02/2014 -	-	-	0/0
646	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH , .	10/2011	209.00 -	209.00	-	01/2013 -	-	-	0/0
647	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA , PPP (BOT)	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26(O)	0/0
648	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA , .	11/2011	909.00 -	909.00	844.10	05/2014 -	-	-	0/0
649	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH , .	07/1999	635.90 -	635.90	-	07/2012 -	-	-	0/0
650	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA , .	04/2011	682.00 -	682.00	34.81	10/2013 -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
651	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE , PPP (BOT)	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7(O) -	0/0
652	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH , .	10/2012	250.50 -	250.50	-	10/2014 -	-	-	0/0
653	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH , .	01/2013	373.47 -	373.47	358.30	07/2014 -	-	-	0/0
654	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH , .	09/2013	606.00 -	606.00	-	-	-	-	0/0
655	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA , .	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
656	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN , .	01/2014	177.32 -	177.32	86.65	01/2016 -	-	-	0/0
657	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016	0(O) -	1/4
658	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	03/2016	0(O) -	0/2
659	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	50.85	03/2016 -	03/2016	0(O) -	1/4
660	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LW E S - [N24000249]PWD,TELANGANA , .	03/2011	218.31 -	339.82	282.02	12/2015 -	-	-	0/3
661	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , EPC	03/2015	298.33 -	298.33	-	-	-	-	0/4
662	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	-	-	-	-	0/4
663	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	-	-	-	-	0/4
664	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	71.38	02/2015 -	-	-	0/4
665	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH , .	01/2014	361.30 -	361.30	-	07/2014 -	-	-	0/1
666	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	-	-	-	0/1
667	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	-	-	-	0/4

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
668	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	-	-	-	0/0
669	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600(JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	-	-	-	0/0
670	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	50.94	-	-	-	0/0
671	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	-	-	-	-	0/0
672	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	20.70	03/2015 -	-	-	0/0
673	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	5.26	03/2015 -	-	-	0/0
674	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	10.14	03/2015 -	-	-	0/0
675	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	111.73	12/2012 -	-	-	0/0
676	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	96.04	-	-	-	0/0
677	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
678	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	15.50	-	-	-	0/0
679	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	29.39	-	-	-	0/0
680	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	256.48	-	-	-	0/0
681	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	198.10	-	-	-	0/0
682	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	-	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
683	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	27.00	01/2015 -	-	-	0/0
684	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	15.17	01/2015 -	-	-	0/0
685	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
686	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	171.16	04/2014 -	-	-	0/0
687	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	131.09	03/2015 -	-	-	0/0
688	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM , ITEM RATE	08/2010	186.96 -	186.96	132.80	- -	-	-	0/0
689	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	219.50	03/2011 -	-	-	0/0
690	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	140.75	02/2012 -	-	-	0/0
691	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	122.00	10/2010 -	-	-	0/0
692	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	4.39	03/2011 -	-	-	0/0
693	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	12.66	05/2012 -	-	-	0/0
694	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM , .	04/2013	151.59 -	151.59	7.19	08/2013 -	-	-	0/0
695	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
696	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	49.42	02/2013 -	-	-	0/0
697	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
698	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	20.80	08/2015 -	-	-	0/0
699	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	161.70	2.55	07/2015 -	-	-	0/0
700	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	2.55	08/2015 -	-	-	0/0
701	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
702	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	31.64	03/2016 -	03/2016	0(0) -	0/0
703	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	-	- -	-	-	0/0
704	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	45.64	- -	-	-	0/0
705	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	25.87	- -	-	-	0/0
706	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	89.68	- -	-	-	0/0
707	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	-	-	0/0
708	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	-	02/2016 -	-	-	0/0
709	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
710	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	-	- -	-	-	0/0
711	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	51.28	- -	-	-	0/0
712	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	12.08	- -	-	-	0/0
713	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
714	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.55	- -	-	-	0/0
715	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	2,090.00	02/2011 -	-	-	0/0
716	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	388.43	- -	-	-	0/0
717	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	7.97	02/2011 -	-	-	0/0
718	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	-	- -	-	-	0/0
719	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	72.79	- -	-	-	0/0
720	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	-	-	0/0
721	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	157.22	10/2010 -	-	-	0/0
722	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	135.01	09/2010 -	-	-	0/0
723	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	-	-	0/0
724	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	- -	-	-	0/0
725	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , .	07/2015	1,282.94 -	1,282.94	-	- -	-	-	0/0
726	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	-	- -	-	-	0/0
727	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA , .	09/2015	414.51 -	414.00	-	- -	-	-	0/0
728	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH , .	06/2015	583.79 -	583.79	-	- -	-	-	0/0
729	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA , .	10/2015	531.13 -	531.13	-	- -	-	-	0/0
730	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH,WEST BENGAL , .	10/2015	361.15 -	361.15	-	- -	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
731	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	-	-	-	0/0
732	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA , .	10/2015	593.26 -	593.26	-	-	-	-	0/0
733	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA , .	12/2015	649.50 -	649.50	-	-	-	-	0/0
734	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	-	-	-	0/0
735	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	-	02/2015 -	-	-	0/0
736	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	-	-	-	0/0
737	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA , .	08/2015	505.00 -	505.00	-	-	-	-	0/0
738	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	-	-	-	-	0/0
739	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,012.90 -	1,012.90	-	-	-	-	0/0
740	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA , .	06/2015	845.24 -	845.24	-	-	-	-	0/0
741	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2016 -	-	-	0/0
742	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU , .	01/1991	285.00 -	285.00	-	01/2008 -	-	-	0/0
743	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	-	-	0/0
744	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH , .	03/2015	795.76 -	795.76	-	-	-	-	0/0
745	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH , .	03/2015	794.30 -	794.30	-	-	-	-	0/0
746	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	-	-	0/0
747	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA , .	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
748	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR , .	08/2015	556.07 -	556.07	-	-	-	-	0/0
749	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB , .	09/2015	273.06 -	273.06	-	-	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
750	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR , .	12/2015	1,041.10 -	1,041.10	-	-	-	-	0/0
751	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH , .	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7(O) -	0/0
752	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR , .	08/2015	814.04 -	814.04	-	-	-	-	0/0
753	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA , .	12/2015	752.28 -	752.28	-	-	-	-	0/0
754	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA , .	12/2015	1,423.96 -	1,423.96	-	-	-	-	0/0
755	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , .	03/2015	928.83 -	928.83	-	-	-	-	0/0
756	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH , .	12/2015	596.67 -	596.67	-	-	-	-	0/0
757	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2019 -	-	-	0/0
758	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR , .	08/2015	322.09 -	322.09	-	-	-	-	0/0
759	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH , .	12/2015	509.13 -	509.13	-	-	-	-	0/0
760	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH , .	03/2015	810.22 -	810.22	-	-	-	-	0/0
761	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	-	-	-	0/0
762	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR , .	01/1991	642.41 -	642.41	-	-	-	-	0/0
763	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR , .	01/1991	1,167.45 -	1,167.45	-	-	-	-	0/0
764	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH , .	12/2015	726.67 -	726.67	-	-	-	-	0/0
765	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7(O) -	0/0
766	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
767	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	-	-	-	0/0
768	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	-	-	-	-	0/0
769	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	-	-	-	0/0
770	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA , .	12/2015	479.20 -	479.20	-	-	-	-	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
771	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR , .	08/2015	399.54 -	399.54	-	-	-	-	0/0
772	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR , .	01/1991	478.35 -	478.35	-	-	-	-	0/0
773	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN , .	08/2015	275.90 -	275.90	-	-	-	-	0/0
774	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR , .	08/2015	516.13 -	516.13	18.48	-	-	-	0/0
775	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	14.70	-	-	-	0/0
776	ROHTAK - BAWAL(APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA , .	02/2010	650.00 -	650.00	-	-	-	-	0/0
777	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	13.13	-	-	-	0/0
778	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	626.93	07/2008 -	-	-	0/0
779	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
780	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	-	-	-	0/0
781	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	-	-	-	0/0
782	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM , .	12/2003	208.00 230.00	208.00	295.20	04/2008 01/2017	01/2017	105(O) 0(R)	0/0
783	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU , PPP (BOT)	06/2011	535.00 -	535.00	913.00	12/2013 -	01/2016	-	0/0
784	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT , PPP (BOT)	09/2010	805.39 -	805.39	-	03/2013 -	01/2016	-	0/0
785	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	0(O) -	0/0
786	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	-	01/2019 -	01/2019	0(O) -	0/4
787	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	-	01/2019 -	01/2019	0(O) -	0/0
788	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB , .	01/2014	523.85 -	523.85	77.49	01/2016 -	01/2017	12(O) -	0/0
789	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU , .	07/2014	401.11 -	401.11	200.96	01/2017 -	01/2017	0(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
790	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
791	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	0(O) -	0/0
792	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	1,060.85	- -	01/2018	- -	0/0
793	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,055.00	-	11/2015 -	01/2016	-	0/0
794	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	1,200.90	01/2018 -	01/2018	0(O) -	0/0
795	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM , .	12/2003	264.72 -	264.72	-	06/2008 -	02/2016	-	0/0
796	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 2,782.54	1,509.10	-	09/2012 -	02/2016	-	2/3
797	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31(O) -	0/0
798	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN , PPP (ANNUITY)	03/2012	333.51 -	333.51	226.96	09/2014 -	02/2016	-	0/0
799	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	12.80	02/2017 -	02/2017	0(O) -	0/1
800	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH , .	02/2015	241.61 -	241.61	44.89	02/2017 -	02/2017	0(O) -	0/1
801	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017	0(O) -	0/0
802	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24(O) -	0/1
803	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN , .	08/2015	538.08 -	538.08	38.08	02/2018 -	02/2018	0(O) -	0/0
804	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA , .	08/2015	723.54 -	723.54	235.85	02/2018 -	02/2018	0(O) -	0/0
805	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN , .	08/2015	482.27 -	482.27	40.75	02/2018 -	02/2018	0(O) -	0/0
806	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	106.61	02/2018 -	02/2018	0(O) -	0/0
807	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
808	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM , .	12/2003	280.00 -	361.00	-	02/2009 -	03/2016	85(O) -	0/0
809	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM , .	12/2003	199.81 -	385.13	-	04/2009 -	03/2016	83(O) -	0/0
810	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM , .	12/2003	167.64 -	167.64	-	11/2008 -	03/2016	88(O) -	0/0
811	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM , .	12/2003	155.04 -	280.13	-	11/2008 -	03/2016	88(O) -	0/0
812	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	04/2009 -	03/2016	83(O) -	0/0
813	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM , .	12/2003	195.00 -	195.00	-	06/2008 -	03/2016	93(O) -	0/0
814	BIJNI TO ASSAM WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM , .	12/2003	237.80 -	237.80	-	06/2008 -	03/2016	93(O) -	0/0
815	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM , .	12/2003	196.00 -	331.23	-	07/2009 -	03/2016	80(O) -	0/0
816	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA , PPP (BOT)	03/2005	940.00 -	940.00	1,415.36	07/2012 -	03/2017	56(O) -	3/3
817	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	-	04/2013 -	03/2016	35(O) -	0/0
818	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	-	08/2012 -	03/2017	55(O) -	0/0
819	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2016	19(O) -	0/0
820	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	282.68	08/2013 -	03/2017	43(O) -	0/0
821	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31(O) -	0/0
822	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21(O) -	0/0
823	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA , PPP (BOT)	04/2012	484.19 -	484.19	458.86	10/2014 -	03/2016	17(O) -	0/0
824	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU , PPP (BOT)	06/2013	1,287.95 -	1,287.95	715.50	11/2015 -	03/2017	16(O) -	0/0
825	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN , .	03/2014	240.10 -	240.10	151.72	03/2016 -	03/2016	0(O) -	0/0
826	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	116.28	03/2016 -	03/2016	0(O) -	3/4
827	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.55	03/2016 -	03/2016	0(O) -	3/4
828	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018	0(O) -	0/4
829	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR , .	11/2005	240.00 -	240.00	295.38	11/2008 -	03/2016	88(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
830	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN , .	09/2015	567.51 -	567.51	42.79	03/2018 -	03/2018	0(O) -	0/0
831	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	0(O) -	0/0
832	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017	0(O) -	0/0
833	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0
834	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL , EPC	01/1991	322.00 -	322.00	-	03/2018 -	03/2018	0(O) -	0/0
835	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	140.88	03/2017 -	03/2017	0(O) -	0/0
836	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	0(O) -	0/0
837	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH , .	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(O) -	0/0
838	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH , .	09/2015	664.53 -	664.53	-	03/2018 -	03/2018	0(O) -	0/0
839	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH , .	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(O) -	0/0
840	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE , .	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
841	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH , .	09/2015	785.78 -	785.78	-	03/2018 -	03/2018	0(O) -	0/0
842	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH,RAJASTHAN , EPC	03/2012	914.50 -	914.50	1,108.96	10/2015 -	03/2016	5(O) -	0/0
843	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	-	03/2018 -	03/2018	0(O) -	0/0
844	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH , .	09/2015	934.46 -	934.46	57.43	03/2018 -	03/2018	0(O) -	0/0
845	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH , .	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016	0(O) -	0/0
846	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
847	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR , .	12/2003	332.94 -	332.94	497.20	09/2008 -	04/2016	91(O) -	0/0
848	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN , .	12/2003	275.00 -	250.39	274.11	10/2008 -	04/2016	90(O) -	0/0
849	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM , .	12/2003	198.16 -	198.16	242.40	04/2008 04/2016	04/2016	96(O) 0(R)	0/0
850	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE , .	12/2003	232.45 -	232.45	-	09/2010 -	04/2016	67(O) -	0/0
851	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN , PPP (BOT)	11/2009	795.00 -	795.00	1,607.78	05/2012 -	04/2016	47(O) -	0/0
852	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	04/2016	35(O) -	0/0
853	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,948.67	08/2013 -	04/2016	32(O) -	0/0
854	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	574.74	03/2014 -	04/2017	37(O) -	0/0
855	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN , .	08/2010	267.81 -	267.81	699.60	02/2013 -	04/2016	38(O) -	0/0
856	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	1,607.34	04/2015 -	04/2016	12(O) -	0/0
857	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN , PPP (BOT)	10/2013	677.79 -	677.79	849.40	04/2016 -	04/2016	0(O) -	0/0
858	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP, GOA , EPC	03/2015	297.00 -	297.00	36.02	- -	04/2018	- -	0/1
859	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL, TRIPURA , EPC	05/2014	497.89 -	497.89	49.78	04/2017 -	04/2017	0(O) -	0/3
860	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI, RAJASTHAN , .	10/2014	206.12 -	206.12	112.00	04/2017 -	04/2017	0(O) -	0/0
861	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN , .	10/2014	264.72 -	264.72	98.18	04/2017 -	04/2017	0(O) -	0/0
862	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI, HARYANA , .	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
863	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12(O) -	0/0
864	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	55.00	04/2018 -	04/2018	0(O) -	0/0
865	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN , .	12/2003	275.00 -	281.31	168.31	02/2010 -	05/2017	87(O) -	0/0
866	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
867	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL , PPP (BOT)	02/2011	580.43 -	580.43	226.67	08/2013 -	05/2017	45(O) -	0/0
868	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,310.32	09/2014 -	05/2016	20(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
869	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	498.11	06/2015 -	05/2017	23(O) -	0/0
870	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN , .	01/2014	158.04 -	158.04	117.97	12/2015 -	05/2016	5(O) -	0/0
871	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24(O) -	1/4
872	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.75	05/2018 -	05/2018	0(O) -	0/4
873	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	-	05/2018 -	05/2018	0(O) -	0/4
874	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN , .	11/2014	279.14 -	279.14	62.77	05/2017 -	05/2017	0(O) -	0/0
875	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH , .	05/2015	261.09 -	261.09	31.17	05/2017 -	05/2017	0(O) -	0/0
876	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	0(O) -	0/0
877	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017	0(O) -	0/0
878	SHAHDLI TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	-	05/2017 -	05/2017	0(O) -	0/0
879	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	-	05/2016 -	05/2016	0(O) -	0/0
880	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , .	01/1991	229.41 -	229.41	-	05/2018 -	05/2018	0(O) -	0/0
881	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13(O) -	0/0
882	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	28.86	05/2018 -	05/2018	0(O) -	0/4
883	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , .	02/2015	327.32 -	327.32	-	05/2017 -	05/2017	0(O) -	0/0
884	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH , .	12/2003	155.00 -	201.66	244.34	09/2008 -	06/2016	93(O) -	0/0
885	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH , .	12/2003	348.16 -	348.16	362.77	09/2007 -	06/2016	105(O) -	0/0
886	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	469.41	05/2010 -	06/2016	73(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
887	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU , PPP (BOT)	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56(O) -	0/0
888	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	863.58	03/2013 -	06/2016	39(O) -	0/0
889	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,187.71	06/2013 -	06/2016	36(O) -	0/0
890	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11(O) -	0/0
891	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2016	35(O) -	0/0
892	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT , PPP (BOT)	12/2010	1,008.50 -	1,008.50	1,275.83	06/2013 -	06/2016	36(O) -	0/3
893	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	06/2016	31(O) -	0/0
894	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU , .	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36(O) -	0/0
895	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	-	07/2013 -	06/2016	35(O) -	0/0
896	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	-	01/2014 -	06/2016	29(O) -	0/0
897	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,620.63	05/2014 -	06/2016	25(O) -	0/0
898	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	654.59	02/2014 -	06/2016	28(O) -	0/0
899	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	898.99	03/2014 -	06/2016	27(O) -	0/0
900	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	545.27	11/2013 -	06/2016	31(O) -	0/0
901	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2016	24(O) -	0/0
902	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN , PPP (BOT)	12/2011	2,388.51 -	2,388.00	2,490.61	06/2014 -	06/2016	24(O) -	0/0
903	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,071.52	03/2013 -	06/2016	39(O) -	0/0
904	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	06/2016	9(O) -	0/0
905	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,467.07	12/2015 -	06/2016	6(O) -	0/3
906	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21(O) -	0/3
907	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN , .	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5(O) -	0/0
908	REHABILITATION AND UPGRADEATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	-	- -	06/2017	- -	0/4

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
909	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24(O) -	0/2
910	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	-	06/2018 -	06/2018	0(O) -	0/4
911	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	-	06/2018 -	06/2018	0(O) -	0/4
912	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/0
913	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
914	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI,TAMIL NADU , .	12/2014	451.58 -	451.58	28.00	06/2017 -	06/2017	0(O) -	0/0
915	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI,UTTAR PRADESH , PPP (ANNUITY)	06/2014	569.38 -	569.38	737.51	06/2016 -	06/2016	0(O) -	0/0
916	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
917	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA , .	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
918	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]DORTH,HARYANA , PPP (BOT)	03/2013	959.25 -	959.25	1,194.67	06/2016 -	06/2016	0(O) -	0/0
919	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH , .	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24(O) -	0/0
920	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL , .	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018	0(O) -	0/0
921	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR , .	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
922	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	2,816.74	10/2011 -	06/2016	56(O) -	0/0
923	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	-	06/2018 -	06/2018	0(O) -	0/0
924	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH , .	01/2016	815.28 -	815.28	-	06/2018 -	06/2018	0(O) -	0/0
925	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH , .	01/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018	0(O) -	0/0
926	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH , .	12/2015	667.00 -	667.00	-	06/2018 -	06/2018	0(O) -	0/0
927	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM , .	12/2003	245.00 -	245.00	-	03/2008 07/2016	07/2016	100(O) 0(R)	0/0
928	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM , .	12/2003	225.00 -	225.00	311.13	06/2008 06/2016	07/2016	97(O) 1(R)	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
929	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,674.79	08/2013 -	07/2017	47(O) -	0/0
930	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD, MAHARASHTRA , EPC	08/2014	187.79 -	187.79	-	07/2016 -	07/2016	0(O) -	0/12
931	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24(O) -	0/1
932	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP, MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	-	07/2017 -	07/2017	0(O) -	0/0
933	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN , .	07/2015	455.60 -	455.60	54.50	07/2017 -	07/2017	0(O) -	0/0
934	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA , .	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
935	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	957.02	07/2017 -	07/2017	0(O) -	0/0
936	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH , .	06/2016	667.00 -	667.00	-	07/2018 -	07/2018	0(O) -	0/0
937	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI, MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
938	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM , .	12/2003	175.96 -	175.96	-	04/2008 08/2016	08/2016	100(O) 0(R)	0/0
939	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM , .	12/2003	160.00 -	160.00	-	05/2008 07/2016	08/2016	99(O) 1(R)	0/0
940	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	1,708.35	05/2013 -	08/2016	39(O) -	0/0
941	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	1,876.89	08/2013 -	08/2016	36(O) -	0/0
942	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,328.50	02/2014 -	08/2016	30(O) -	2/2
943	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD, ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23(O) -	0/4
944	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT , .	03/2014	503.16 -	503.16	-	08/2016 -	08/2016	0(O) -	0/0
945	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH, BIHAR , ITEM RATE	01/1991	282.41 -	282.41	-	08/2016 -	08/2016	0(O) -	0/0
946	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD, MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11(O) -	0/0
947	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	234.21	08/2016 -	08/2016	0(O) -	0/0
948	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI, MADHYA PRADESH , PPP (BOT)	02/2012	912.00 -	912.00	-	08/2016 -	08/2016	0(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
949	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	785.00	08/2016 -	08/2016	0(O) -	0/0
950	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	01/1991	1,388.00 -	1,388.00	20.60	- -	08/2018	- -	0/0
951	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA , .	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	08/2016	50(O) -	0/0
952	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	-	08/2017 -	08/2017	0(O) -	0/0
953	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR , .	10/2013	278.39 -	278.39	22.18	08/2014 -	08/2014	-	0/0
954	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM , .	12/2003	217.61 309.56	309.56	-	04/2010 09/2016	09/2016	77(O) 0(R)	0/0
955	KUNDUPUR-SURATHKAL AND MANGLORE - [N24000146]NHAI,KARNATAKA , PPP (BOT)	09/2010	671.00 -	671.00	818.53	- -	09/2017	- -	2/3
956	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	-	05/2013 -	09/2016	40(O) -	0/0
957	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	320.46	01/2014 -	09/2016	32(O) -	0/0
958	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND , .	11/2011	478.51 -	478.00	277.41	10/2013 -	09/2016	35(O) -	0/0
959	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
960	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017	0(O) -	0/0
961	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA , .	05/2015	709.00 -	709.00	19.24	09/2017 -	09/2017	0(O) -	0/0
962	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND , .	09/2015	341.61 -	341.61	114.87	09/2017 -	09/2017	0(O) -	0/0
963	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN , .	09/2014	425.19 -	425.19	217.87	09/2016 -	09/2016	0(O) -	0/0
964	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH , .	09/2015	368.73 -	368.73	70.23	09/2016 -	09/2017	12(O) -	0/0
965	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13(O) -	0/0
966	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI,HARYANA , .	12/2012	438.75 -	438.75	-	09/2016 -	09/2016	0(O) -	0/0
967	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR , .	10/2014	377.64 -	377.64	105.83	03/2014 -	09/2016	30(O) -	0/0
968	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
969	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	-	- -	10/2017	- -	0/4
970	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
971	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	19.72	10/2018 -	10/2018	0(O) -	0/4
972	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016	0(O) -	0/0
973	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH , .	04/2014	351.34 -	351.34	160.49	01/2016 -	10/2016	9(O) -	0/0
974	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH , .	04/2014	495.78 -	495.78	239.48	01/2016 -	10/2016	9(O) -	0/0
975	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN , .	01/1991	269.26 -	269.26	-	10/2016 -	10/2016	0(O) -	0/0
976	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	0(O) -	0/0
977	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	-	10/2017 -	10/2017	0(O) -	0/0
978	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	-	10/2016 -	10/2016	0(O) -	0/0
979	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	0(O) -	0/0
980	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	0(O) -	0/0
981	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN , .	10/2015	597.00 -	597.00	-	10/2017 -	10/2017	0(O) -	0/0
982	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,288.44	11/2016 -	11/2016	0(O) -	0/0
983	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA , EPC	06/2014	260.39 -	260.39	-	11/2016 -	11/2016	0(O) -	0/4
984	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	-	11/2016 -	11/2016	0(O) -	0/4

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
985	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017	0(O) -	0/0
986	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24(O) -	0/4
987	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	39.53	11/2014 -	11/2016	24(O) -	0/4
988	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	-	11/2018 -	11/2018	0(O) -	0/4
989	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	-	11/2018 -	11/2018	0(O) -	0/4
990	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24(O) -	0/0
991	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24(O) -	0/0
992	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU , .	05/2015	1,387.11 -	1,387.11	114.38	11/2017 -	11/2017	0(O) -	0/0
993	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU , .	11/2014	563.92 -	563.92	103.08	11/2016 -	11/2016	0(O) -	0/0
994	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017	0(O) -	0/0
995	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA , .	01/2014	292.98 -	292.98	95.60	11/2014 -	11/2014	-	0/0
996	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM , .	12/2003	230.00 -	230.00	-	06/2005 -	12/2016	138(O) -	0/0
997	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM , .	12/2003	212.00 -	212.00	-	09/2007 -	12/2016	111(O) -	0/0
998	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,708.29	11/2011 -	12/2016	61(O) -	0/0
999	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,036.26	07/2013 -	12/2016	41(O) -	0/0
1000	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA , .	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49(O) -	0/0
1001	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39(O) -	0/0
1002	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	1,788.25	03/2013 -	12/2016	45(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1003	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	880.29	02/2013 -	12/2016	46(O) -	0/0
1004	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,326.02	12/2013 -	12/2016	36(O) -	0/0
1005	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	303.94	05/2013 -	12/2017	55(O) -	0/0
1006	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	622.74	10/2013 -	12/2017	50(O) -	0/0
1007	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR , .	10/2011	375.09 -	375.09	494.33	04/2014 -	12/2016	32(O) -	0/0
1008	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	604.61	07/2013 -	12/2016	41(O) -	0/0
1009	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA , PPP (BOT)	07/2011	586.00 -	586.00	-	01/2014 -	12/2016	35(O) -	0/0
1010	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	533.13	09/2013 -	12/2016	39(O) -	0/0
1011	2-LANING WITH PAVED SHOULDER OF MUZZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR , PPP (BOT)	07/2012	356.40 -	356.40	348.00	07/2014 -	12/2017	41(O) -	0/0
1012	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	343.75	04/2014 -	12/2016	32(O) -	0/0
1013	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA , .	12/2011	942.69 -	942.69	229.16	06/2014 -	12/2016	30(O) -	0/0
1014	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1015	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA , PPP (BOT)	10/2013	283.25 -	283.25	177.61	10/2015 -	12/2016	14(O) -	0/0
1016	REHABILITATION AND UPGRADE OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 156.09	156.09	61.17	12/2016 -	12/2016	0(O) -	0/4
1017	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH , .	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12(O) -	0/2
1018	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH , .	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12(O) -	0/0
1019	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU , .	06/2015	563.92 -	563.92	11.37	12/2017 -	12/2017	0(O) -	0/0
1020	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH , .	06/2014	301.04 -	301.04	39.38	01/2016 -	12/2016	11(O) -	0/0
1021	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA , .	06/2015	996.37 -	996.37	-	12/2017 -	12/2017	0(O) -	0/0
1022	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	-	12/2017 -	12/2017	0(O) -	0/0
1023	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	225.02	-	12/2018 -	12/2018	0(O) -	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1024	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
1025	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	297.35	11/2016 -	12/2016	1(O) -	0/0
1026	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , .	09/2014	479.00 -	479.00	349.60	- -	12/2016	- -	0/0
1027	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , .	12/2015	239.23 -	239.23	-	12/2017 -	12/2017	0(O) -	0/0
1028	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , .	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
1029	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB , .	10/2015	447.29 -	447.29	-	12/2017 -	12/2017	0(O) -	0/0
1030	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
1031	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	8.89	- -	-	-	0/0
1032	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	-	- -	-	-	0/0
1033	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	-	- -	-	-	0/0
1034	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA , .	11/2015	867.66 -	867.66	154.48	- -	05/2018	-	0/0
1035	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , .	08/2015	854.80 -	854.80	-	- -	-	-	0/0
	Total		249,122.45 -	251,469.02	96,094.78				28/176
	<u>SHIPPING AND PORTS</u>								
1036	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	841.02	10/2008 -	-	-	0/0
1037	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	415.80	12/2010 -	01/2016	-	0/0
1038	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , .	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
1039	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU , .	12/2014	274.85 -	274.85	104.26	04/2017 -	04/2017	0(O) -	0/1
1040	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	198.94	88.01	06/2017 -	06/2017	0(O) -	0/2

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1041	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 600.00	600.00	525.49	03/2006 01/2016	07/2016	124(O) 6(R)	0/0
1042	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA , .	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88(O) 77(R)	0/0
1043	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	12.28	12/2017 -	12/2017	0(O) -	0/1
	Total		4,117.75 -	5,048.81	2,353.06				0/4
	<u>TELECOMMUNICATIONS</u>								
1044	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , .	03/2012	13,334.00 -	13,334.00	196.20	07/2015 -	03/2017	20(O) -	0/0
1045	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30(O) -	0/70
	Total		15,445.17 -	15,345.17	1,556.20				0/70
	<u>URBAN DEVELOPMENT</u>								
1046	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA , .	05/2006	6,395.00 -	11,609.00	12,712.23	06/2011 -	06/2016	60(O) -	3/3
1047	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA , .	02/2011	241.33 -	241.33	87.13	11/2014 -	-	-	0/0
1048	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI , .	07/2012	884.30 -	884.30	234.42	08/2014 -	-	-	0/0
1049	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI , Central Sector Projects	06/2015	197.33 -	197.33	-	- -	-	-	0/0
1050	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB , .	02/2014	388.00 -	388.00	115.19	01/2015 -	-	-	3/12
1051	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU , .	12/2015	209.00 -	209.00	-	- -	-	-	0/0
1052	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU , .	04/2014	332.72 -	332.72	105.95	09/2016 01/2017	01/2017	4(O) 0(R)	0/0
1053	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA , .	02/2014	26,405.14 -	26,405.14	30.04	02/2019 -	02/2019	0(O) -	0/0
1054	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH , .	12/2012	188.87 -	188.87	93.68	12/2014 12/2016	03/2017	27(O) 3(R)	0/1
1055	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH , .	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16(O) -	0/0
1056	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA , .	06/2010	205.00 142.37	191.97	-	03/2012 08/2016	03/2017	60(O) 7(R)	0/0

Sector Wise Details

(March 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1057	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH , .	06/2014	157.84 -	157.84	30.67	03/2017 -	03/2017	0(O) -	0/0
1058	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA , .	08/2014	8,680.00 -	8,680.00	105.22	03/2018 -	03/2018	0(O) -	0/0
1059	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN , Central Sector Projects	08/2014	350.02 -	350.02	-	03/2015 -	03/2015	-	0/0
1060	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	-	03/2015 -	03/2015	-	0/0
1061	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL , .	02/2014	156.57 -	156.57	41.86	09/2015 07/2016	04/2017	19(O) 9(R)	1/7
1062	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI , .	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	1/3
1063	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL , .	01/2009	225.81 -	225.81	143.72	06/2012 03/2016	05/2016	47(O) 2(R)	15/16
1064	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI , .	05/2009	261.85 -	261.85	183.26	05/2013 10/2015	06/2016	37(O) 8(R)	0/0
1065	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA , .	07/2012	5,181.79 -	5,181.79	2,757.97	07/2017 -	06/2017	-1(O) -	0/0
1066	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR , .	02/2012	171.10 202.00	202.00	192.24	09/2014 07/2015	07/2015	-	0/0
1067	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI , .	10/2013	1,219.21 -	1,219.21	10.53	07/2017 -	07/2017	0(O) -	0/0
1068	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU , .	02/2009	14,600.00 14,600.00	14,600.00	12,472.32	12/2015 -	08/2016	8(O) -	1/24
1069	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND , .	09/2012	171.86 -	171.86	16.16	03/2016 -	09/2017	18(O) -	0/6
1070	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARAstra - [N28000074]CPWD,MAHARASHTRA , .	12/2012	315.00 315.00	315.00	188.33	06/2015 08/2016	11/2016	17(O) 3(R)	0/0
1071	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI , .	06/2012	4,264.00 -	4,264.00	1,317.71	11/2019 -	11/2019	0(O) -	0/7
1072	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI , .	09/2011	38,585.00 -	38,585.00	22,146.20	03/2016 -	12/2016	9(O) -	0/0
1073	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA , .	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	-	0/0

Sector Wise Details									
(March 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1074	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA , .	11/2012	238.43 -	238.43	-	02/2015 -	-	-	0/0
1075	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA , .	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
1076	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH , .	08/2007	246.90 -	246.90	-	- -	-	-	0/0
	Total		134,465.83 -	139,697.70	53,042.52				24/79
	Grand Total		1,238,517.07	1,393,627.86					1794/3864


Summary of projects in the Flash Report for the month of March, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1071
Number of Projects completed/dropped/frozen in Current Month	2
Projects reported Anti. Cost less then Rs.150 crore in Current Month	2
Number of Projects Added in Current Month	9
Number of Projects in Current Month	1076


Brief Analysis

Project Status with respect to Original Schedule: Out of 1076 projects, 6 projects are ahead of schedule, 258 projects are on schedule 343 projects are delayed. 433 projects do not have fixed dates of commissioning. 36 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

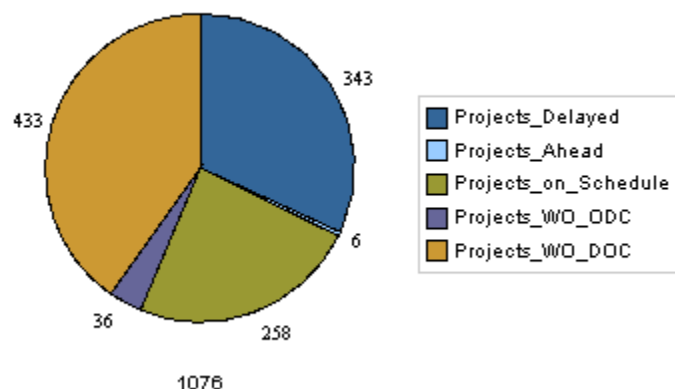

Investment Scenario

Total original cost of implementation of 1076 projects when sanctioned, was of the order of Rs. 1238517.07 crore but this was subsequently revised to Rs. 1393627.86 crore implying a cost overrun of 12.5%. The expenditure incurred on these projects till March, 2016 is Rs. 575677.42 crore, which is 41.3% of the revised cost of the projects.

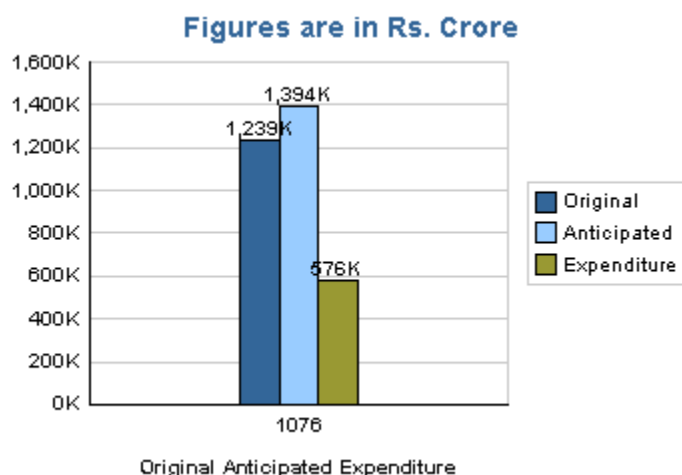

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:


Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

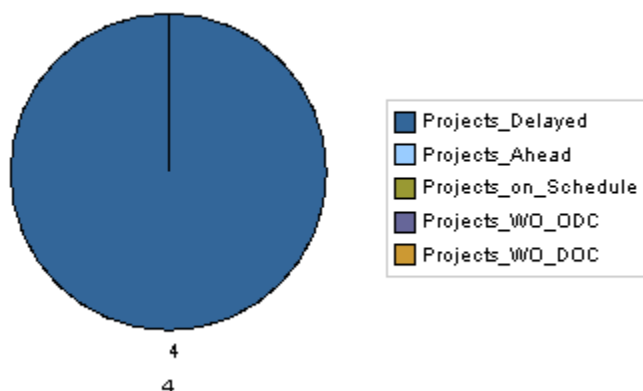**Investment Scenario**

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till March, 2016 is Rs. 40349.55 crore, which is 77.7% of the revised cost of the projects.

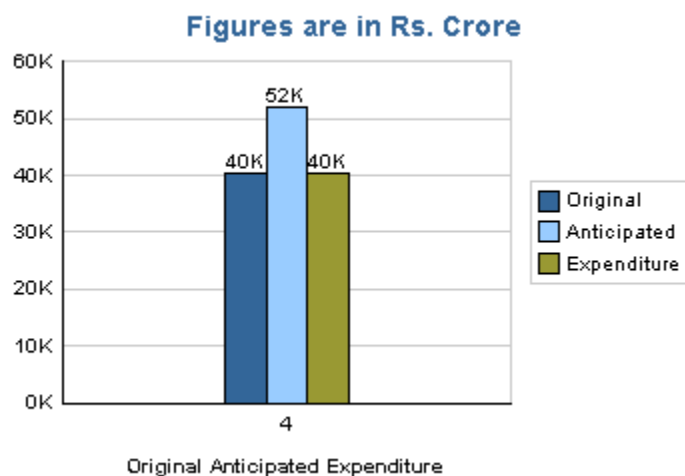

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 1 project is delayed. 2 projects do not have fixed dates of commissioning.

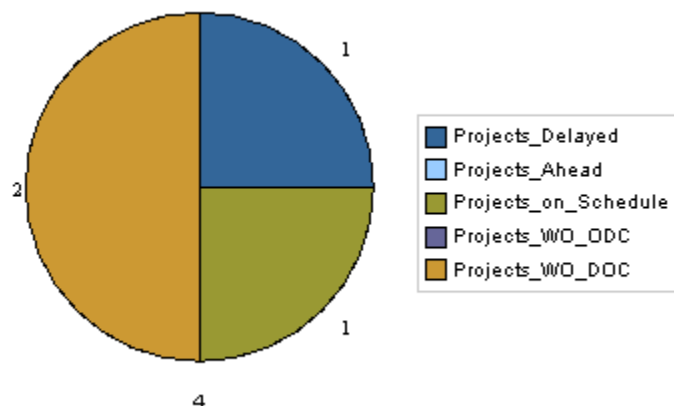

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1177.28 crore but this was subsequently anticipated to Rs. 1186.17 crore implying a cost overrun of .8%. The expenditure incurred on these projects till March, 2016 is Rs. 784.73 crore, which is 66.2% of the revised cost of the projects.

Figures are in Rs. Crore

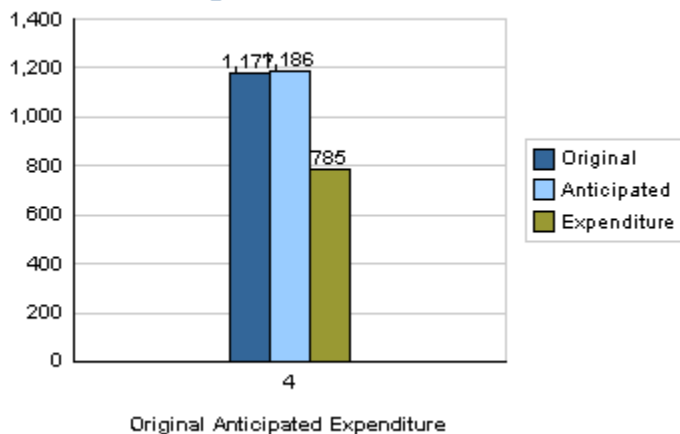

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	88
Number of Projects On Schedule	43
Number of Projects Delayed	42
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 88 projects, 2 projects are ahead of schedule, 43 projects are on schedule 42 projects are delayed. 1 project does not have fixed dates of commissioning.

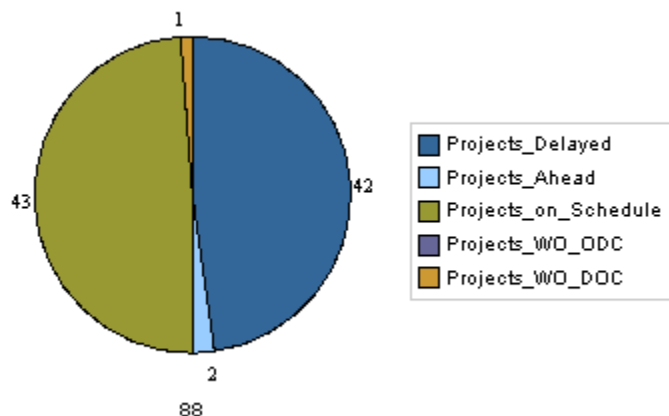

Investment Scenario

Total original cost of implementation of 88 projects when sanctioned, was of the order of Rs. 60724.3 crore but this was subsequently anticipated to Rs. 61837.03 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till March, 2016 is Rs. 14400.83 crore, which is 23.3% of the revised cost of the projects.

Figures are in Rs. Crore

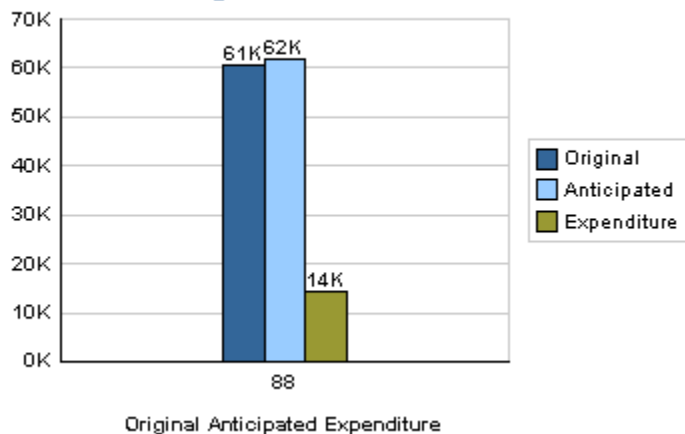

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	33
Number of Projects On Schedule	13
Number of Projects Delayed	15

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 33 projects, 13 projects are on schedule 15 projects are delayed. 4 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

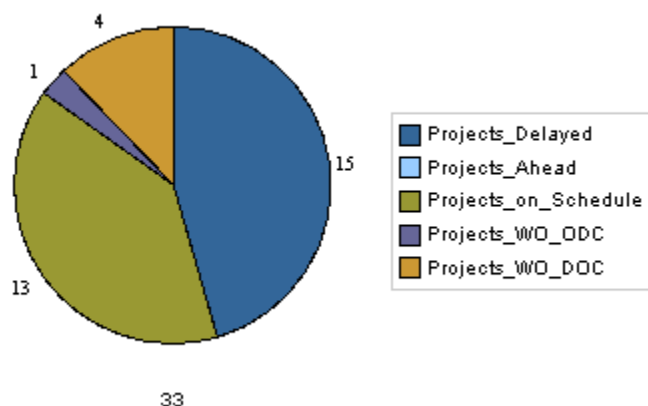

Investment Scenario

Total original cost of implementation of 33 projects when sanctioned, was of the order of Rs. 53712.21 crore but this was subsequently anticipated to Rs. 54241.65 crore implying a cost overrun of 1%. The expenditure incurred on these projects till March, 2016 is Rs. 30793.35 crore, which is 56.8% of the revised cost of the projects.

Figures are in Rs. Crore

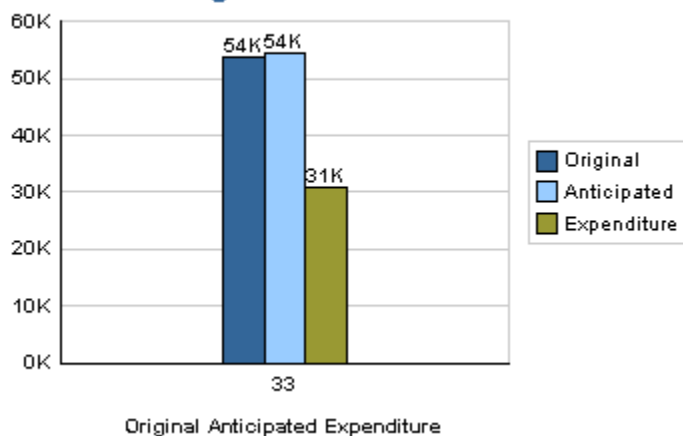

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	68
Number of Projects On Schedule	21
Number of Projects Delayed	38
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	7

Brief Analysis


Project Status with respect to Original Schedule: Out of 68 projects, 2 projects are ahead of schedule, 21 projects are on schedule 38 projects are delayed. 7 projects do not have fixed dates of commissioning.

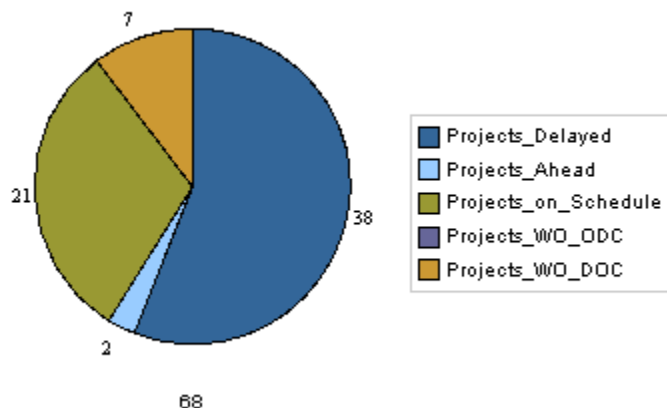

Investment Scenario

Total original cost of implementation of 68 projects when sanctioned, was of the order of Rs. 108058.21 crore but this was subsequently anticipated to Rs. 111974 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till March, 2016 is Rs. 40449.61 crore, which is 36.1% of the revised cost of the projects.

Figures are in Rs. Crore

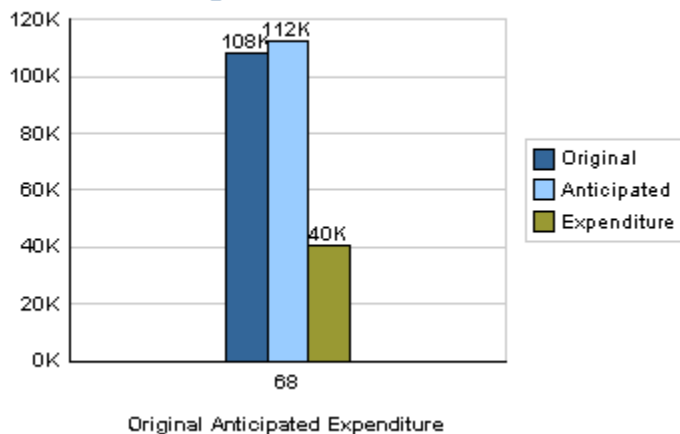

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	111
Number of Projects On Schedule	43
Number of Projects Delayed	64
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 111 projects, 1 project is ahead of schedule, 43 projects are on schedule 64 projects are delayed. 3 projects do not have fixed dates of commissioning.

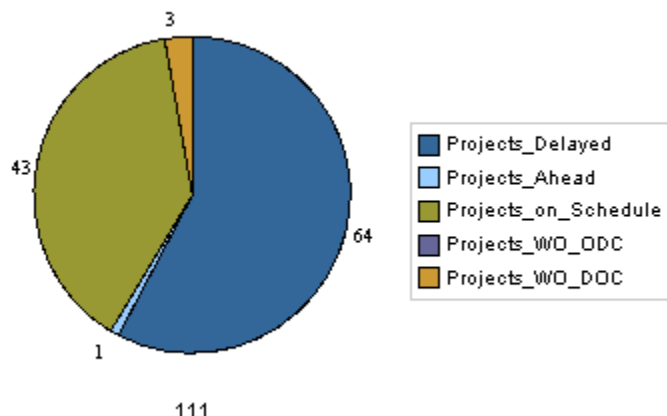

Investment Scenario

Total original cost of implementation of 111 projects when sanctioned, was of the order of Rs. 304580.02 crore but this was subsequently anticipated to Rs. 354153.57 crore implying a cost overrun of 16.3%. The expenditure incurred on these projects till March, 2016 is Rs. 192162.73 crore, which is 54.3% of the revised cost of the projects.

Figures are in Rs. Crore

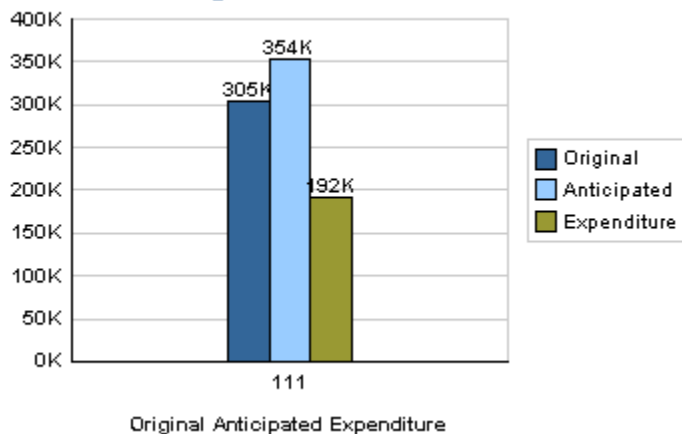

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	9
Number of Projects On Schedule	4
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 4 projects are on schedule 4 projects are delayed. 1 project does not have fixed dates of commissioning.

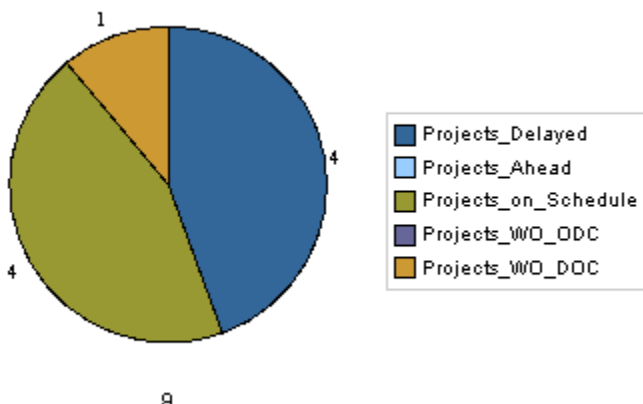

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 2563.15 crore but this was subsequently anticipated to Rs. 2563.15 crore. The expenditure incurred on these projects till March, 2016 is Rs. 1018.4 crore, which is 39.7% of the revised cost of the projects.

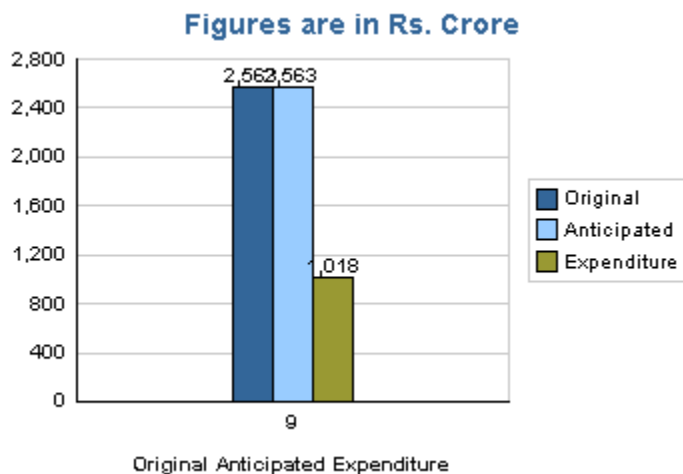

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	298
Number of Projects On Schedule	5
Number of Projects Delayed	31

Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	235

Brief Analysis


Project Status with respect to Original Schedule: Out of 298 projects, 5 projects are on schedule 31 projects are delayed. 235 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

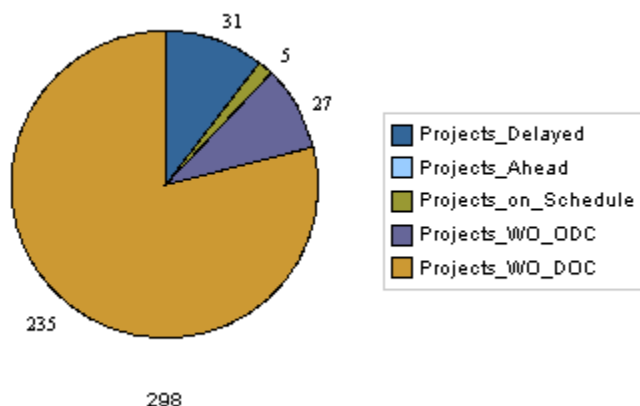

Investment Scenario

Total original cost of implementation of 298 projects when sanctioned, was of the order of Rs. 254176.67 crore but this was subsequently anticipated to Rs. 327636.22 crore implying a cost overrun of 28.9%. The expenditure incurred on these projects till March, 2016 is Rs. 93023.07 crore, which is 28.4% of the revised cost of the projects.

Figures are in Rs. Crore

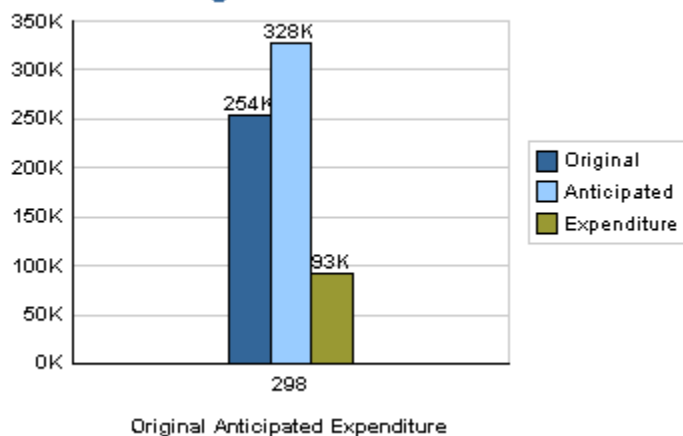

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	414
Number of Projects On Schedule	115
Number of Projects Delayed	126

Number of Projects Without Original Date of Commissioning	8
Number of Projects Without Date Of Commissioning	165

Brief Analysis


Project Status with respect to Original Schedule: Out of 414 projects, 115 projects are on schedule 126 projects are delayed. 165 projects do not have fixed dates of commissioning. 8 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

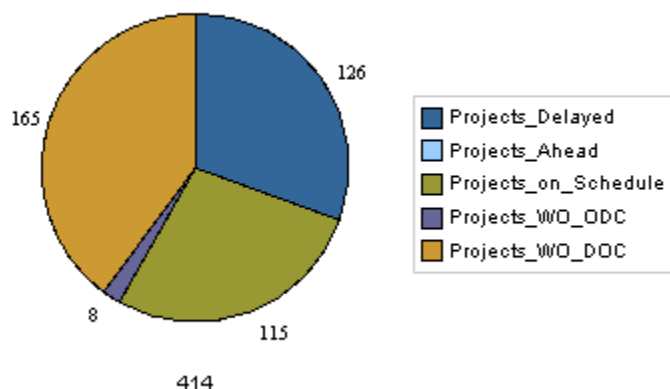

Investment Scenario

Total original cost of implementation of 414 projects when sanctioned, was of the order of Rs. 249122.45 crore but this was subsequently anticipated to Rs. 251469.02 crore implying a cost overrun of .9%. The expenditure incurred on these projects till March, 2016 is Rs. 96094.78 crore, which is 38.2% of the revised cost of the projects.

Figures are in Rs. Crore

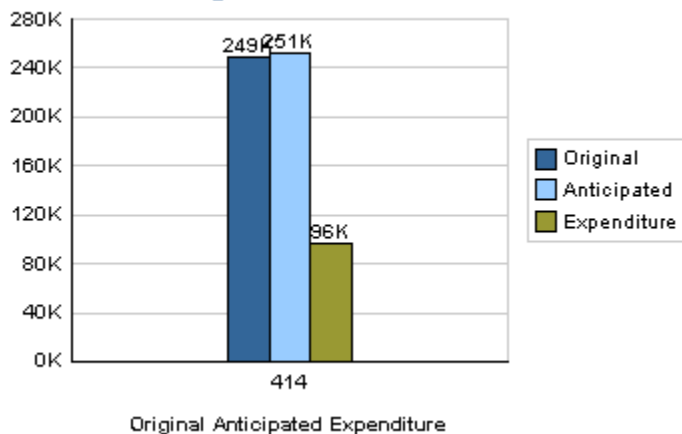

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

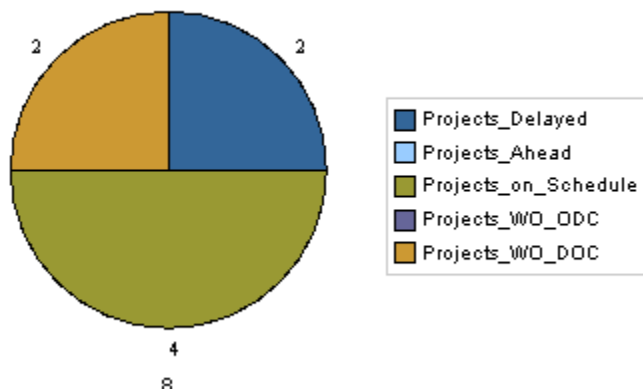

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5048.81 crore implying a cost overrun of 22.6%. The expenditure incurred on these projects till March, 2016 is Rs. 2353.06 crore, which is 46.6% of the revised cost of the projects.

Figures are in Rs. Crore

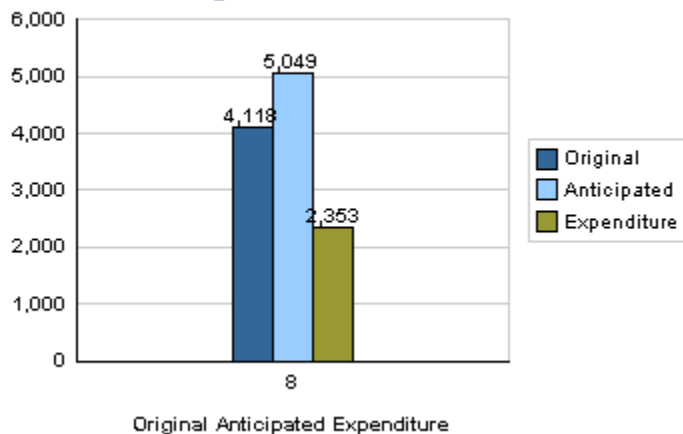

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.

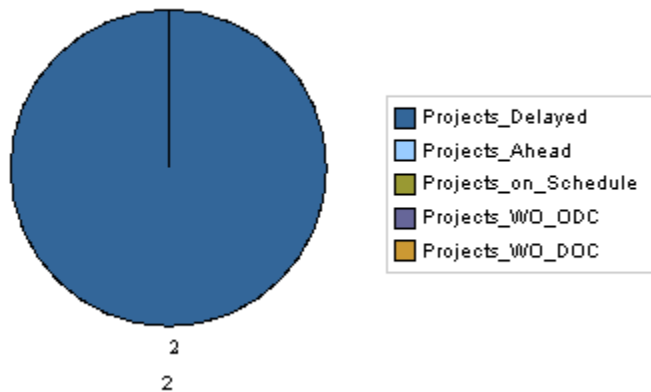

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 15445.17 crore but this was subsequently anticipated to Rs. 15345.17 cr. The expenditure incurred on these projects till March, 2016 is Rs. 1556.2 crore, which is 10.1% of the revised cost of the projects.

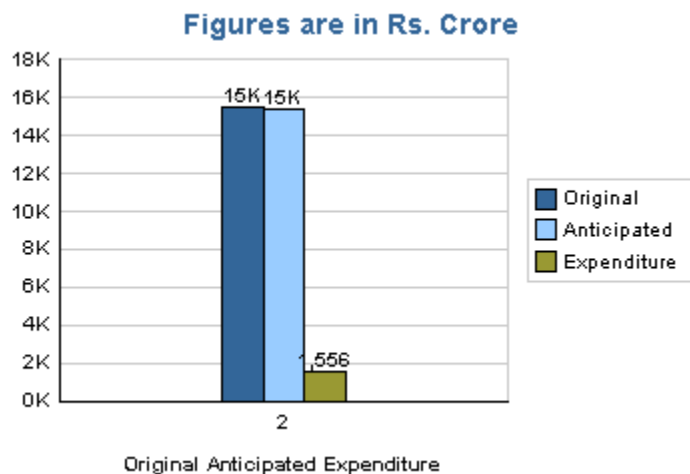

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	31
Number of Projects On Schedule	5
Number of Projects Delayed	13
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	12

Brief Analysis


Project Status with respect to Original Schedule: Out of 31 projects, 1 project is ahead of schedule, 5 projects are on schedule 13 projects are delayed. 12 projects do not have fixed dates of commissioning.

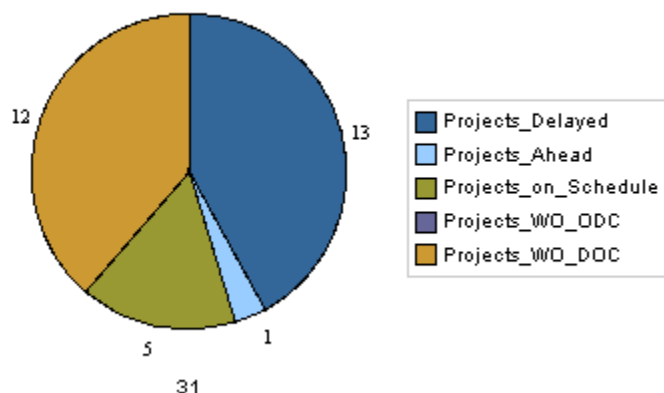

Investment Scenario

Total original cost of implementation of 31 projects when sanctioned, was of the order of Rs. 134465.83 crore but this was subsequently anticipated to Rs. 139697.7 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till March, 2016 is Rs. 53042.52 crore, which is 38% of the revised cost of the projects.

Figures are in Rs. Crore

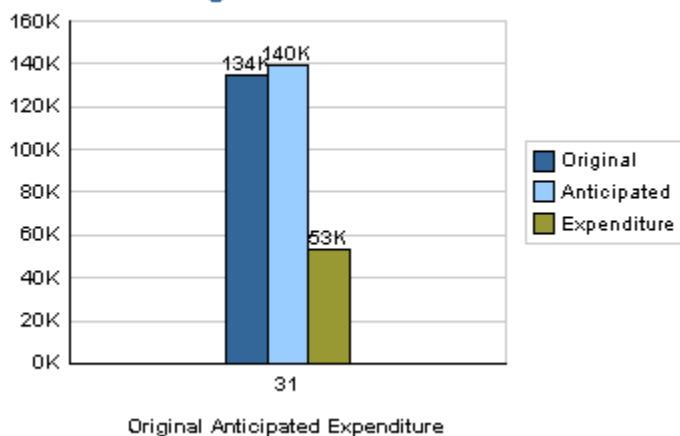

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE
(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	24.09
2	ANDHRA PRADESH	47	21,226.93	23,061.97	9,927.87
3	ARUNACHAL PRADESH	15	12,006.22	28,372.49	14,434.68
4	ASSAM	50	28,781.83	44,485.17	28,599.15
5	BIHAR	66	58,528.87	72,279.46	41,405.47
6	CHHATISGARH	39	86,092.87	87,391.15	48,733.78
7	D & N HAVELI	1	6,086.08	6,086.08	749.95
8	DELHI	16	49,997.48	49,997.48	24,714.67
9	GOA	8	3,925.48	3,907.87	341.62
10	GUJARAT	31	30,605.81	31,660.45	18,042.11
11	HARYANA	20	14,065.88	16,036.5	8,491.1
12	HIMACHAL PRADESH	5	8,088.55	14,487.83	6,992.61
13	JAMMU AND KASHMIR	9	25,620.25	45,229.68	15,335.08
14	JHARKHAND	45	43,305.84	45,868.59	14,298.29
15	KARNATAKA	42	72,113.99	87,378.98	33,901.65
16	KERALA	16	25,825.82	30,300.97	17,038.54
17	MADHYA PRADESH	51	53,152.52	55,716.01	10,056.01
18	MAHARASHTRA	76	1,22,792.9	1,31,552.82	42,644.23
19	MANIPUR	3	1,047.27	6,958.48	2,902.41
20	MEGHALAYA	6	6,970.03	8,194.91	2,102.63
21	MIZORAM	6	2,188.16	5,402.06	1,836.34
22	MULTI STATE	170	2,61,824.38	2,39,759.93	71,237.03
23	NAGALAND	3	6,420	8,757.12	10.44
24	ODISHA	47	42,720.12	47,180.91	9,724.48
25	PUNJAB	23	11,796.33	11,800.33	2,172.58
26	RAJASTHAN	61	41,310.71	41,853.65	24,100.8
27	SIKKIM	5	2,149.08	4,999.32	569.47
28	TAMIL NADU	59	69,760.85	89,410.09	60,341.04
29	TELANGANA	33	13,759.66	16,706.05	3,572.52
30	TRIPURA	9	3,776.07	7,489.01	3,424.98
31	UTTAR PRADESH	60	52,378.07	56,264.19	21,010.88
32	UTTARAKHAND	6	9,352.4	11,651.71	5,741.56
33	WEST BENGAL	47	50,532.01	63,071.99	31,199.36
TOTAL		1,076	12,38,517.07	13,93,627.86	5,75,677.42

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	21,304
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	5,187.55
3	KULDA OCP (MAHANADI COALFIELDS LTD)	COAL	01/2005	302.96	-	303.14
4	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,548.25
5	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	8,357.64
6	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	2,011.96
7	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	201.26
8	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	-	712.02
9	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	-	10,722.72
10	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
11	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
12	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	1,092.98
13	GONDIA-JABALPUR(GC), (SECR)	RAILWAYS	02/1997	386.3	-	590.26
14	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	-	800.7

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	NANDYAL - YERRAGUNTALA(NL), SCR	RAILWAYS	03/1996	155.74	164.36	755.5
16	KANPUR KASGANJ MATHURA(GC) NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4
17	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	-	4,102.7
18	MUNEERABAD-MAHABOBNAGAR(NL), SCR	RAILWAYS	04/1997	218.24	236.41	309.19
19	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	-	230.67
20	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	501.69	501.69	819.19
21	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
22	KATI HAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	743.74
23	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	798.87
24	JALANDHAR-PATHANKOT-JAMMU-TAWI(LD), NR	RAILWAYS	03/2002	625.3	408.76	835.14
25	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	-	596.66
26	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	889.95
27	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,732.43
28	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	376.18
30	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	639.77
31	HARIDASPUR-PARADEEP(NL)	RAILWAYS	04/1996	301.64	-	577.84
32	RAJATGARH-BARANG(LD), ECR	RAILWAYS	04/1999	166.16	-	349.36
33	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
34	KOSI BRIDGE (NL), ECR	RAILWAYS	04/2002	322.95	-	325.36
35	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	RAILWAYS	04/2002	921	-	1,691.12
36	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,521.72
37	ETAHWAH-MAINPURI (NL), NCR	RAILWAYS	04/1997	120	245.39	249.33
38	SUKINDA ROAD - ANGUL (NL)(ECOR)	RAILWAYS	04/1998	183.23	-	185.46
39	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
40	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	322.75
41	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	357.91
42	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	244.34

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	497.2
44	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	424.3
45	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	-	872.21
46	ANANTA OC EXPANSION PH-III (15.0 MTY)	COAL	08/2008	207.28	-	207.71
47	RAMAGUNDAM OC-II EXTENSION	COAL	12/2009	418.97	-	475.38
48	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	STEEL	03/2007	149.73	173	177.06
49	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	STEEL	05/2005	768.88	1060	1,070.97
50	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	8920	9,356.28
51	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	-	174.38
52	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR	PETROLEUM	08/2010	103.02	-	114.42
53	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	4,490.39
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	POWER	02/2009	509.66	-	558.96
55	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	POWER	03/2011	1,585.12	-	1,623.96
56	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	POWER	09/2011	1,940.13	-	1,991.86

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,350.13
58	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2	POWER	12/2011	2,422.66	-	2,448.76
59	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	POWER	01/2012	1,422.85	-	1,474.62
60	BRBCL-NABINAGAR TPP- JV (4X250 MW)	POWER	01/2007	5,353	-	5,472.83
61	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	POWER	05/2015	436.68	-	439.94
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
63	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RAILWAYS	07/2006	743	-	770.18
64	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RAILWAYS	09/2006	324.9	-	351.79
65	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	896.75
66	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
67	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
68	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
69	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
70	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
72	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
73	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
74	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,769.59
75	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
76	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.11
77	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	259.31
78	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
79	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
80	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
81	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	1,047.1
82	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
83	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
84	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
86	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62
87	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
88	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
89	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	311.13
90	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	295.2
91	AGRA-BYPASS(NS-1/UP-1), NH-2,3	ROAD TRANSPORT AND HIGHWAYS	12/2003	348.16	-	362.77
92	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
93	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,415.36
94	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,607.78
95	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	365.08
96	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	761.4
97	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,708.29
98	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,055.94
100	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	863.58
101	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	ROAD TRANSPORT AND HIGHWAYS	11/2010	1,585	-	1,708.35
102	KUNDUPUR-SURATHKAL AND MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	818.53
103	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	1,036.26
104	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	487.9
105	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,187.71
106	PUNE-SATARA(NH-4)	ROAD TRANSPORT AND HIGHWAYS	10/2010	1,724.55	-	1,788.25
107	PATNA-MUZZAFFARPUR	ROAD TRANSPORT AND HIGHWAYS	08/2010	671.3	-	880.29
108	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,275.83
109	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	919.56
110	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	832.39
111	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	1,948.67
112	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	ROAD TRANSPORT AND HIGHWAYS	06/2011	535	-	913

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,326.02
114	TIRUPATI - TIRUTHANI - CHENNAI	ROAD TRANSPORT AND HIGHWAYS	04/2011	571	-	622.74
115	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,620.63
116	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	898.99
117	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	494.33
118	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	604.61
119	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	545.27
120	PUNE-SHOLAPUR, PKG-II	ROAD TRANSPORT AND HIGHWAYS	09/2011	835	-	1,684
121	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
122	BEAWAR PALI PINDWARA	ROAD TRANSPORT AND HIGHWAYS	12/2011	2,388.51	-	2,490.61
123	MUZAFFARNAGAR-HARIDWAR	ROAD TRANSPORT AND HIGHWAYS	09/2011	754	-	1,071.52
124	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,876.89
125	4-LANING OF BRAHAMPURE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,674.79
126	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	2,310.32

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	ROAD TRANSPORT AND HIGHWAYS	07/2012	291.36	-	320.46
128	ETAWAH CHAKERI	ROAD TRANSPORT AND HIGHWAYS	03/2013	1,573	-	1,850
129	AHMEDABAD TO VADODARA SECTION	ROAD TRANSPORT AND HIGHWAYS	01/2013	2,125.24	-	4,467.07
130	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA	ROAD TRANSPORT AND HIGHWAYS	10/2013	677.79	-	849.4
131	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	ROAD TRANSPORT AND HIGHWAYS	03/2011	218.31	-	282.02
132	KOTWA TO DEWAPUR (LMNHP-10)	ROAD TRANSPORT AND HIGHWAYS	11/2005	240	-	295.38
133	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,494.48	-	2,090
134	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR	ROAD TRANSPORT AND HIGHWAYS	06/2014	569.38	-	737.51
135	4 LANING OF GOMTI CHAURAHA - UDAIPUR	ROAD TRANSPORT AND HIGHWAYS	03/2012	914.5	-	1,108.96
136	4-LANING OF ROHTAK - HISSAR SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2013	959.25	-	1,194.67
137	NAGPUR - KONDHALI	ROAD TRANSPORT AND HIGHWAYS	09/2005	168	-	279.92
138	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	02/2008	1,673.7	-	2,816.74
139	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,170.52	-	2,041.03
140	TRICHY - KARUR	ROAD TRANSPORT AND HIGHWAYS	03/2007	516	-	626.93

Annexure - II**LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST**

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
141	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	SHIPPING AND PORTS	01/2007	366.39	-	415.8
142	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6,395	-	12,712.23

Details of Projects Ahead of Schedule w.r.t. Original Schedule

							(March 2016)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142	11/2015	498.42 -	498.42	-	03/2020 -	03/2018
2	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		1,053.94 -	1,053.94	3.52		
	<u>POWER</u>						
3	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170	8/2014	188.75 -	188.75	85.90	02/2017 -	03/2016
	Total		188.75 -	188.75	85.90		
	<u>PETROLEUM</u>						
4	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190	7/2014	419.04 -	419.04	339.10	01/2017 -	06/2016
	Total		419.04 -	419.04	339.10		
	<u>URBAN DEVELOPMENT</u>						
5	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79	5,181.79	2,757.97	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,757.97		
	<u>PETROLEUM</u>						
6	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	6,068.80	1,057.64	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	1,057.64		
	Grand Total		12,912.32	12,912.32	4,244.13		

Details of On Schedule Projects w.r.t. Original Schedule

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	314.61	24.09	09/2018 -	09/2018
	Total		314.61 -	314.61	24.09		
	<u>COAL</u>						
2	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2016
4	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	179.12	03/2021 -	03/2021
6	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.09	03/2018 -	03/2018
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	206.38	03/2017 -	03/2017
8	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	72.15	03/2025 -	03/2025
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	620.96	03/2026 -	03/2026
10	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	16.87	03/2020 -	03/2020
11	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.27	04/2017 -	04/2017
12	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	106.05	03/2021 -	03/2021
13	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
14	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020
15	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	188.76	03/2022 -	03/2022
16	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	149.65	03/2020 -	03/2020
17	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	813.94	03/2023 03/2023	03/2023
18	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021
19	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	232.58	03/2020 -	03/2020
20	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
22	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
23	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	847.83	03/2016 -	03/2016
24	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
25	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	78.27	03/2019 -	03/2019
26	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
27	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	110.10	03/2020 -	03/2020
28	GOKUL - [N06000120]	11/2014	267.67 -	267.67	175.50	03/2018 -	03/2018
29	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
30	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.89	03/2019 -	03/2019
31	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.05	03/2019 -	03/2019
32	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
33	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	48.67	03/2021 -	03/2021
34	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	236.49	03/2018 -	03/2018
35	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	67.25	12/2019 -	12/2019
36	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
37	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
38	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
39	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
40	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.74	03/2019 -	03/2019
41	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
42	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
43	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	39.64	03/2023 -	03/2023
44	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021
	Total		35,215.80 -	35,007.00	4,866.84		

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
45	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	56.41	11/2016 -	11/2016
	Total		197.79 -	209.44	56.41		
	<u>HEALTH AND FAMILY WELFARE</u>						
46	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	9/2014	505.58 -	505.58	14.38	03/2018 -	03/2018
47	AIIMS - OPD(NEW) - [N21000009	8/2014	293.65 -	293.65	67.84	05/2017 -	05/2017
48	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	168.90	3.63	05/2017 -	05/2017
49	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	204.44	36.17	05/2017 -	05/2017
	Total		1,172.57 -	1,172.57	122.02		
	<u>MINES</u>						
50	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007	9/2011	1,856.00 -	1,856.00	2.02	09/2017 -	09/2017
51	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008	12/2015	355.13 -	355.13	107.67	11/2016 11/2016	11/2016
52	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009	12/2015	344.50 -	344.50	126.21	11/2016 11/2016	11/2016
	Total		2,555.63 -	2,555.63	235.90		
	<u>PETROLEUM</u>						
53	PIPELINE REPLACEMENT PROJECT -4 - [N16000203	2/2015	2,899.93 -	2,098.43	757.83	05/2017 -	05/2017
54	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205	5/2015	2,443.00 -	2,443.00	148.72	12/2017 -	12/2017
55	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218	2/2016	367.11 -	367.11	-	04/2017 -	04/2017
56	DIESEL HYDROTREATOR - [N16000207	7/2015	1,031.37 -	1,031.37	38.82	01/2018 -	01/2018
57	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,190.69	-	04/2018 -	04/2018
58	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212	1/2015	4,619.94 -	4,619.94	975.16	12/2017 -	12/2017
59	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
60	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211	11/2014	195.63 -	195.63	-	09/2018 -	09/2018
61	SIX PIPELINE REPLACEMENT PROJECT - [N16000214	3/2009	181.02 -	173.28	78.73	01/2017 -	01/2017

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	130.87	02/2020 -	02/2020
63	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]	8/2010	103.02 -	171.04	114.42	07/2016 -	07/2016
64	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
65	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	193.74	09/2017 -	09/2017
66	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	174.38	09/2016 -	09/2016
67	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	11,119.68	05/2016 -	05/2016
68	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	142.35	12/2016 -	12/2016
69	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	673.48	12/2018 -	12/2018
70	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	3,089.78	05/2017 05/2017	05/2017
71	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	18.62	03/2017 -	03/2017
72	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
73	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	-	02/2019 -	02/2019
	Total		47,185.62 -	49,115.87	17,656.58		
	POWER						
74	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	143.00	08/2017 -	08/2017
75	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,261.00	12/2016 -	12/2016
76	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
77	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	719.20	03/2018 -	03/2018
78	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	12.70	11/2017 -	11/2017
79	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	36.50	05/2016 -	05/2016
80	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	249.80	06/2016 -	06/2016
81	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	23.80	03/2018 -	03/2018
82	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	125.80	10/2016 -	10/2016

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
83	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	25.10	07/2016 -	07/2016
84	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	-	05/2018 -	05/2018
85	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	16.50	07/2018 -	07/2018
86	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	6,152.00	06/2017 -	06/2017
87	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	439.94	12/2016 -	12/2016
88	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	138.90	08/2016 -	08/2016
89	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	74.00	11/2017 -	11/2017
90	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	76.80	02/2017 -	02/2017
91	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	1,536.00	09/2019 -	09/2019
92	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
93	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
94	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	6,002.76	01/2018 -	01/2018
95	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	3,068.00	08/2018 -	08/2018
96	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
97	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
98	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	120.80	11/2016 -	11/2016
99	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	451.20	05/2018 -	05/2018
100	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	13.50	10/2016 -	10/2016
101	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	1,226.00	03/2019 -	03/2019
102	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	-	07/2018 -	07/2018
103	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	26.40	03/2018 -	03/2018
104	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	5,427.00	09/2017 -	09/2017
105	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	174.00	09/2019 -	09/2019
106	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04 -	187.04	-	06/2018 -	06/2018

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	133.60	06/2016 -	06/2016
108	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	38.50	10/2017 -	10/2017
109	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	57.90	04/2017 -	04/2017
110	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,632.00	02/2019 -	02/2019
111	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
112	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	430.30	04/2018 -	04/2018
113	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	352.70	04/2018 -	04/2018
114	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	113.20	04/2017 -	04/2017
115	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	-	03/2017 -	03/2017
116	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	-	07/2018 -	07/2018
	Total		125,856.76 -	125,856.76	31,319.98		
	<u>RAILWAYS</u>						
117	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
118	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
119	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
120	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
121	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
	Total		2,670.53 -	6,808.36	172.17		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
122	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
123	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	112.00	04/2017 -	04/2017
124	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
125	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018
126	PADI - DAHOD - [N24000353]	11/2014	279.14 -	279.14	62.77	05/2017 -	05/2017

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
127	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
128	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	114.38	11/2017 -	11/2017
129	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342]	5/2015	709.00 -	709.00	19.24	09/2017 -	09/2017
130	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
131	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	40.75	02/2018 -	02/2018
132	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
133	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]	10/2014	264.72 -	264.72	98.18	04/2017 -	04/2017
134	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	54.50	07/2017 -	07/2017
135	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	44.89	02/2017 -	02/2017
136	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	38.08	02/2018 -	02/2018
137	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
138	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]	12/2014	451.58 -	451.58	28.00	06/2017 -	06/2017
139	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
140	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	151.72	03/2016 -	03/2016
141	VADODARA-SURAT SECTION - [N24000361]	3/2014	503.16 -	503.16	-	08/2016 -	08/2016
142	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	31.17	05/2017 -	05/2017
143	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
144	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19 -	425.19	217.87	09/2016 -	09/2016
145	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]	11/2014	563.92 -	563.92	103.08	11/2016 -	11/2016
146	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]	6/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016
147	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
148	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]	6/2015	563.92 -	563.92	11.37	12/2017 -	12/2017

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
149	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
150	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26 -	269.26	-	10/2016 -	10/2016
151	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	-	05/2017 -	05/2017
152	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
153	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
154	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	-	05/2018 -	05/2018
155	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461	12/2012	438.75 -	438.75	-	09/2016 -	09/2016
156	FOUR LANING OF CHADIGARH - KHARAR - [N24000503	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
157	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016
158	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
159	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
160	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428	6/2014	569.38 -	569.38	737.51	06/2016 -	06/2016
161	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	849.40	04/2016 -	04/2016
162	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	1,200.90	01/2018 -	01/2018
163	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	957.02	07/2017 -	07/2017
164	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
165	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	785.00	08/2016 -	08/2016
166	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	-	03/2017 -	03/2017
167	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
168	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
169	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
170	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399	10/2013	317.76 -	317.76	140.88	03/2017 -	03/2017

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
171	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
172	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.75	05/2018 -	05/2018
173	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	-	06/2018 -	06/2018
174	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
175	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
176	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
177	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
178	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]	1/2014	397.04 -	397.04	-	10/2016 -	10/2016
179	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
180	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
181	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	-	06/2018 -	06/2018
182	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]	1/2014	282.41 -	282.41	31.64	03/2016 -	03/2016
183	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017
184	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	-	03/2018 -	03/2018
185	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
186	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
187	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	-	01/2019 -	01/2019
188	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
189	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
190	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
191	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
192	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
193	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	1/1991	282.41 -	282.41	-	08/2016 -	08/2016
194	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017
195	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAU LI - [N24000406	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
196	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
197	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	106.61	02/2018 -	02/2018
198	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
199	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
200	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241	12/2013	177.18 -	177.18	116.28	03/2016 -	03/2016
201	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017
202	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
203	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
204	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
205	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242	12/2013	158.65 -	158.65	103.55	03/2016 -	03/2016
206	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	-	10/2016 -	10/2016
207	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	156.09	61.17	12/2016 -	12/2016
208	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	-	08/2017 -	08/2017

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
209	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245	1/2014	270.00 -	270.00	50.85	03/2016 -	03/2016
210	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
211	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
212	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
214	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
215	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
216	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
217	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	12.80	02/2017 -	02/2017
218	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	225.02	-	12/2018 -	12/2018
219	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
220	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	-	05/2018 -	05/2018
221	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
222	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
223	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
224	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456	3/2013	959.25 -	959.25	1,194.67	06/2016 -	06/2016
225	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	234.21	08/2016 -	08/2016
226	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,288.44	11/2016 -	11/2016
227	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	55.00	04/2018 -	04/2018
228	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
229	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
230	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	114.87	09/2017 -	09/2017
231	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
232	FOUR LANING OF PARWANOO - SOLAN - [N24000479]	9/2015	934.46 -	934.46	57.43	03/2018 -	03/2018
233	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
234	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]	8/2015	723.54 -	723.54	235.85	02/2018 -	02/2018
235	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
236	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]	7/2014	401.11 -	401.11	200.96	01/2017 -	01/2017
	Total		62,060.38 -	62,199.76	10,315.35		
	<u>SHIPPING AND PORTS</u>						
237	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]	12/2014	274.85 -	274.85	104.26	04/2017 -	04/2017
238	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	12.28	12/2017 -	12/2017
239	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	198.94	88.01	06/2017 -	06/2017
240	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
	Total		928.29 -	942.12	204.55		
	<u>STEEL</u>						
241	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
242	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	309.85	04/2018 -	04/2018
243	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
244	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	53.68	10/2017 -	10/2017
245	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	27.42	03/2018 -	03/2018
246	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]	4/2014	151.33 -	151.33	4.84	09/2017 -	09/2017
247	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
248	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]	8/2012	185.37 -	185.37	-	03/2016 -	03/2016

(March 2016)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
249	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 253.92	253.92	193.97	06/2016 -	06/2016
250	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	197.59	12/2016 -	12/2016
251	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]	2/2014	787.29 -	787.29	251.53	12/2016 -	12/2016
252	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	29.55	09/2016 -	09/2016
253	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	78.00	12/2017 -	12/2017
	Total		7,990.20 -	8,014.59	1,366.49		
	<u>URBAN DEVELOPMENT</u>						
254	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	30.04	02/2019 -	02/2019
255	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	1,317.71	11/2019 -	11/2019
256	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	30.67	03/2017 -	03/2017
257	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	10.53	07/2017 -	07/2017
258	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	105.22	03/2018 -	03/2018
	Total		40,726.19 -	40,726.19	1,494.17		
	Grand Total		326,874.37	332,922.90	67,834.55		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,800.69 -	3,170.48			
	<u>FERTILISERS</u>						
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	11/2016	5.89
	Total		197.79 -	209.44			
	<u>HEAVY INDUSTRY</u>						
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
11	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49

(March 2016)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		5,460.61	9,965.00			
			-				
	<u>PETROLEUM</u>						
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56	450.55	03/2017	03/2018	27.79
			-		-		
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00	1,693.00	01/2012	05/2016	70.49
			-		-		
14	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06	714.25	10/2017	02/2018	17.66
			-		-		
15	MARKETING TOP AT KORBA - [N16000186	01/2011	141.86	232.00	09/2016	09/2016	63.54
			-		-		
16	MH NORTH REDEVELOPMENT PHASE III - [N16000188	06/2014	5,706.47	5,813.25	05/2017	05/2017	1.87
			-		-		
17	GAMJI REDEVELOPMENT PROJECT - [N16000202	05/2015	1,671.22	1,881.22	11/2019	11/2019	12.57
			-		-		
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79	1,256.72	05/2013	12/2016	45.83
			-		-		
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63	2,665.65	03/2015	06/2017	29.42
			-		-		
20	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	03/2012	14,225.00	16,504.00	05/2016	05/2016	16.02
			-		-		
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	02/2012	666.00	838.08	11/2015	11/2016	25.84
			-		-		
22	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81	462.79	10/2014	03/2017	49.38
			-		-		
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00	1,227.00	10/2011	04/2016	67.62
			-		-		
24	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35	1,200.00	03/2015	08/2016	37.72
			-		-		
25	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00	370.00	03/2013	10/2016	19.35
			-		-		
26	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215	08/2010	103.02	171.04	07/2016	07/2016	66.03
			-		-		
	Total		29,610.77	35,479.55			
			-				
	<u>POWER</u>						
27	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59	8,398.76	09/2009	12/2018	114.28
			-		-		
28	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33	18,063.89	09/2010	-	187.40
			-		-		
29	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38	2,193.08	09/2009	09/2016	106.63
			-		-		
30	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69	738.48	09/2010	12/2016	54.59
			-		-		
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19	13,762.80	08/2013	12/2017	23.65
			-		-		

(March 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
32	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	12/2016	36.79
33	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	05/2011	1,961.87 -	2,310.58	05/2014 -	06/2016	17.77
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14
35	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
36	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]	05/2010	250.03 -	390.51	01/2013 -	05/2016	56.19
37	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	03/2017	36.01
38	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	06/2016	83.21
39	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06
40	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	07/2016	147.51
41	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
42	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2016	31.17
43	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91
44	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
45	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	03/2017	16.63
46	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2016	27.60
47	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92
48	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2016	22.93
49	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
50	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
51	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	01/2016	139.32
52	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	02/2012	1,927.16 -	1,940.58	10/2014 -	04/2016	0.70
	Total		66,934.70 -	116,571.86			
	<u>RAILWAYS</u>						
53	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96

(March 2016)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
54	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
55	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
56	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
57	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
58	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
59	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
60	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
61	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
62	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
63	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
64	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
65	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
66	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	-	156.57
67	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
68	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
69	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
70	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
71	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
72	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
73	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
74	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
75	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
76	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	360.00	02/2006 -	-	37.56
77	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24

(March 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
78	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
79	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
80	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
81	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
82	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
83	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
84	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
85	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
86	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
87	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
88	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
89	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
90	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
91	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
92	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
93	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
94	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
95	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
96	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
97	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
98	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
99	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
100	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
101	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
102	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09

(March 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
103	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65 -	- -	-	57.65
104	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47 -	- -	-	47.93
105	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00 -	- -	-	79.63
106	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85 -	- -	-	2.29
107	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50 -	- -	-	0.00
108	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97 -	- -	-	50.10
109	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50 -	- -	-	14.14
110	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00 -	- -	-	72.07
111	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77 -	- -	-	12.38
112	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00 -	01/1999 -	-	123.46
113	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00 -	01/1999 -	-	71.50
114	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00 -	01/1999 -	-	53.96
115	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00 -	- -	-	447.91
116	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98 -	03/2004 -	03/2016	259.68
117	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19 -	04/2008 12/2011	06/2017	233.08
118	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	3,500.00 -	05/2008 -	-	1,313.23
119	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56 -	03/2012 -	-	108.01
120	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72 -	12/2009 -	06/2015	300.67
121	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00 -	- -	-	232.17
122	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	2,531.34 -	12/2008 -	03/2018	245.34
123	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25 -	- -	-	324.33
124	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75 -	03/2011 -	03/2019	803.12
125	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41 -	03/2012 -	-	5.72
126	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00 -	10/2007 -	-	367.76
127	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00 -	03/2011 -	-	185.29
128	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24 -	- -	03/2017	148.12

(March 2016)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
129	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
130	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
131	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
132	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
133	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
134	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
135	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
136	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
137	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
138	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
139	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
140	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	2,434.00	03/2010 -	03/2017	648.92
141	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
142	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
143	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
144	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
145	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
146	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
147	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
148	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
149	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
150	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) [N22000345]	04/1997	836.26 -	1,072.51	- -	-	28.25
151	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
152	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01

(March 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
153	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
154	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
155	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
156	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
157	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
158	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
159	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	-	42.11
160	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
161	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
162	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
163	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
164	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
165	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
166	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	- -	-	184.87
167	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63
168	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	3,500.00	- -	-	68.05
169	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
170	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	262.00	- -	-	10.58
171	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152	04/2013	456.00 -	855.16	- -	-	87.54
172	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153	04/2010	739.65 -	872.22	- -	-	17.92
173	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	218.39	- -	-	2.34
174	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR- BANSI PAHARPUR - [N22000158	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
175	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	434.00	- -	-	62.32
176	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	553.63 -	1,009.00	- -	12/2019	82.25

(March 2016)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
177	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
178	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
179	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
180	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
181	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
182	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
183	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
184	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
185	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
186	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
187	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
188	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
189	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
190	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
191	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
192	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
193	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
194	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
195	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
196	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
197	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
198	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
199	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
200	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
201	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12

(March 2016)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
202	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
203	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
204	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
205	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
206	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
207	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
208	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
209	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
210	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
211	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
	Total		82,135.89 -	212,266.74			
	ROAD TRANSPORT AND HIGHWAYS						
212	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	03/2016	28.93
213	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75
214	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68
215	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99
216	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50
217	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH- 52) FROM - [N24000292]	11/2014	573.96 605.00	605.00	- -	-	5.41
218	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
219	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
220	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	161.70	07/2015 -	-	2.88
221	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25
222	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2016	30.10
223	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29

(March 2016)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
224	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
225	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
226	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
227	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
228	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
229	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		5,171.67 -	7,634.21			
	<u>SHIPPING AND PORTS</u>						
230	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	07/2016	300.00
231	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
232	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
233	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,006.56 -	1,937.62			
	<u>STEEL</u>						
234	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	12/2016	12.04
235	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79
236	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29
237	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102	07/2011	324.87 324.87	325.00	12/2015 -	03/2016	0.04
238	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
239	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50

(March 2016)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		1,964.58 -	2,494.02			
	<u>URBAN DEVELOPMENT</u>						
240	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
241	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA [N28000063	02/2012	171.10 -	202.00	09/2014 -	07/2015	18.06
	Total		6,566.10 -	11,811.00			
	Grand Total		219,447.96	433,750.32			

Details of Delayed Projects w.r.t. Original and Revised Schedule

(March 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,304.00	12/2008 10/2013	05/2016	89	70.54	
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,187.55	09/2010 09/2016	09/2016	72	62.57	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	8,066.00	12/2015 11/2016	1p1/2018	35	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,792.00	12/2016 03/2017	12/2019	36	0	
	Total		40,442.00 -	51,918.00	40,349.55					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	424.30	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		309.46 -	309.46	424.30					
	<u>COAL</u>									
6	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	2,023.54	03/2014 -	03/2016	24	0	
7	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	511.06	03/2013 -	03/2016	36	-6.11	
8	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 -	1,228.39	872.21	03/2013 -	03/2016	36	478.5	
9	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	83.51	03/2012 -	03/2016	48	0	
10	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2016	60	0	
11	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
12	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	197.05	10/2014 -	04/2016	18	0	
13	MURADH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	06/2016	26	0	
14	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	81.37	03/2014 -	09/2016	30	0	Delay/ non issuance of 'Patta' for land/plots allotted to PAFs shifted and being shifted in the area acquired under CBA Act.
15	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	122.07	05/2014 -	10/2016	29	0	
16	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	77.34	04/2014 -	11/2016	31	0	
17	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	303.14	03/2010 -	03/2017	84	0	
18	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL, JHARKHAND	12/2007	341.63 -	341.63	128.02	03/2011 -	03/2017	72	0	
19	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 486.57	486.57	157.69	03/2012 03/2018	03/2017	60	87.58	
20	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	229.69	03/2013 -	03/2017	48	0	
21	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	152.18	03/2010 -	03/2017	84	0	
22	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51	0	
23	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	207.71	03/2012 -	03/2017	60	0	
24	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	185.35	03/2013 -	03/2017	48	.02	
25	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	86.48	03/2015 -	03/2017	24	0	
26	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	95.17	03/2012 -	03/2017	60	0	
27	PURNADH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	151.89	03/2013 -	03/2017	48	0	
28	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	71.83	03/2014 -	03/2017	36	0	
29	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
30	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	119.06	03/2012 -	03/2018	72	0	
31	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.06	03/2014 -	03/2018	48	0	
32	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	8.03	03/2015 -	03/2018	36	0	
33	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	0	
34	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	77.44	03/2015 -	03/2018	36	0	
35	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	102.72	03/2016 -	03/2018	24	0	
36	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	486.27	93.51	03/2016 -	03/2018	24	12.97	
37	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,813.37	12/2015 04/2018	04/2018	28	0	
38	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	225.81	03/2018 -	07/2018	4	0	
39	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	27.85	07/2016 -	03/2019	32	0	Aquisition of non forest land and R&R
40	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	49.03	04/2015 04/2019	04/2019	48	0	
41	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	1,458.17	30.39	06/2015 08/2019	08/2019	50	0	
42	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	
43	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	
44	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	
45	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	79.49	07/2012 03/2017	03/2021	104	0	
46	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	
47	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	475.38	03/2012 -	03/2023	132	16.86	
	Total		23,986.78 -	25,308.31	9,527.62					

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	STEEL									
48	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	1,070.97	1,070.97	02/2014 -	03/2016	25	39.29	
49	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	325.00	263.57	12/2015 -	03/2016	3	.04	
50	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	175.60	10/2013 -	06/2016	32	0	
51	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	486.38	07/2015 -	08/2016	13	0	
52	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	363.11	04/2016 -	09/2016	5	0	
53	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,905.05	03/2013 -	11/2016	44	0	
54	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	115.64	05/2016 -	12/2016	7	0	
55	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	61.26	04/2015 -	12/2016	20	0	
56	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	9,162.07	05/2015 12/2016	12/2016	19	0	
57	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	261.96	07/2016 -	12/2016	5	0	
58	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	177.06	12/2015 -	03/2017	15	17.5	
59	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	-	03/2015 -	03/2017	24	0	
60	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	289.28	07/2015 -	06/2017	23	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
61	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	45.93	10/2016 -	06/2017	8	42.39	
62	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCCL,TRIPURA	10/2011	175.49 207.00	206.71	125.65	12/2016 -	07/2017	7	17.79	
	Total		39,095.46 -	39,600.51	28,503.53					
	<u>PETROLEUM</u>									
63	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	327.10	06/2011 03/2012	03/2016	57	0	
64	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	190.86	12/2014 -	03/2016	15	0	Nil
65	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,105.78	10/2011 -	04/2016	54	67.62	issues faced with local elements in the RoU.
66	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	141.15	03/2014 05/2016	05/2016	26	0	
67	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	595.62	04/2015 05/2016	05/2016	13	-39.69	
68	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,459.15	01/2012 -	05/2016	52	70.49	Progress is slow due to heavy rains during the period, RoU issue
69	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,387.48	09/2012 -	06/2016	45	0	
70	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,355.41	08/2015 -	06/2016	10	0	
71	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	127.28	09/2012 06/2016	06/2016	45	-24.14	
72	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	440.18	08/2015 -	06/2016	10	0	
73	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	76.60	02/2016 02/2016	07/2016	5	0	
74	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	565.63	03/2015 -	08/2016	17	37.72	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
75	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	514.33	09/2011 10/2016	10/2016	61	0	
76	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	422.00	238.14	02/2016 -	10/2016	8	-12.08	
77	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 370.00	370.00	17.84	03/2013 10/2016	10/2016	43	19.35	
78	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	606.85	11/2015 11/2016	11/2016	12	25.84	
79	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	1,666.63	11/2015 11/2016	11/2016	12	0	Nil
80	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,017.24	05/2013 04/2016	12/2016	43	45.83	
81	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	112.86	05/2015 -	12/2016	19	0	
82	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	185.40	11/2016 -	12/2016	1	0	
83	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30	0	
84	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,803.00	03/2013 03/2016	03/2017	48	-3.5	
85	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	1,235.07	05/2014 03/2017	03/2017	34	0	
86	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	523.10	08/2015 -	03/2017	19	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
87	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	275.04	10/2014 03/2017	03/2017	29	49.38	1. Delay in Working permission for from PWD works stopped by local villagers at Pimple Jagtap, Khed Taluk, Pune District Requested assistance from State Govt. / PWD authorities to provide the suitable documents confirming the ownership 2. ROU: Taluk, due to agitation by land owners demanding higher compensation over and above PMP act / LARR Act. Several rounds of discussions were held in the presence of local Tehsildar /MLA to resolve the issue. Works have been since commenced. Minor issues are being sorted out at Site level.
88	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	77.90	07/2016 -	04/2017	9	-20.81	
89	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	35.76	11/2016 -	04/2017	5	0	
90	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25	0	
91	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,334.59	03/2015 06/2017	06/2017	27	29.42	
92	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	06/2017	30	0	
93	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,124.35	4,124.35	633.74	04/2016 12/2017	12/2017	20	0	

(March 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
94	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	284.19	09/2017 03/2018	12/2017	3	0	
95	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	99.05	10/2017 02/2018	02/2018	4	17.66	
96	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	12.10	03/2017 03/2017	03/2018	12	27.79	
97	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	112.83	01/2013 12/2018	12/2018	71	-10.01	
98	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	0	
99	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,381.47	12/2012 -	02/2019	74	0	Problem faced & action taken in Kerala Severe resistance by local groups in Kerala state hampered the laying . Hon'ble Supreme Court has given Judgment dated 02.02.2016 in favour of GAIL on the SLP of Govt of Tamil Nadu against GAIL. However, Govt of Tamil Nadu have filed review petition on 08.02.2016 in Supreme Court against the above judgment which is also dismissed on 01.03.16 by Hon'ble Supreme court.
100	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	749.95	05/2019 03/2020	03/2020	10	0	
	Total		47,994.98 -	49,998.86	21,204.48					
	<u>POWER</u>									
101	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,623.96	11/2013 -	03/2016	28	0	Implementation affected due to delay in land acquisition & forest clearance.

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
102	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 609.44	609.44	600.90	02/2014 03/2016	03/2016	25	10.32	
103	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR	03/2010	3,984.03 -	3,984.03	3,290.44	01/2013 -	03/2016	38	0	
104	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	9,606.82	8,357.23	02/2011 -	03/2016	61	133.06	Balance land acquisition and to maintain Law & order.
105	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC, RAJASTHAN	02/2015	302.49 302.00	302.49	271.07	02/2016 -	03/2016	1	0	
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	373.67	02/2012 -	04/2016	50	0	Severe ROW problem resolved. Ckt-I of LILO line completed. Completion matching with Sub station.
107	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	965.58	776.84	11/2012 -	04/2016	41	0	4/5 lines & 4/5 sub station completed. Balance LILO at Saharanpur & Saharanpur S/Stn. is severely affected due to severe ROW problem in Western UP (farmers agitation). Keeping in view severe ROW problem, State Admn. has advised to review the scheme. LILO line proposed for deletion as advised by state Govt. (matter referred to CEA for deletion of line & revised of proj. scope). The balance s/stn. is planned to be commissioned alongwith Roorkee -Saharanpur line (Covered under NRSS-XXI).

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
108	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 1,940.58	1,940.58	1,604.27	10/2014 03/2016	04/2016	18	.7	02/05 line & 02/03 sub station completed ahead of schedule. Further 02 lines & 01 S/S. completed in Feb'15. Severe ROW problem are being faced in balance LILO line. ROW problem being resolved progressively.
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,471.42	04/2013 -	05/2016	37	0	04/05 lines & 01/01 S/s completed. Implementation of balance line affected
110	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 390.51	390.51	246.70	01/2013 03/2016	05/2016	40	56.19	
111	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,448.76	08/2014 -	05/2016	21	0	02/03 line & 01/01 sub station completed. Gen. Project delayed (ant. in 2016-17 & beyond). Implementation affected due to delay in land acquisition of Varansai S/S (land acquired in Jun'14). ROW (Nexalite) problem faced in Gaya-Varanasi line.
112	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	90.50	12/2015 -	05/2016	5	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	558.96	11/2011 -	06/2016	55	0	Severe ROW problem in Western U.P. (near Bagpat etc.) initially due to farmers agitations & high compensation demand. ROW problem continues. ROW being addressed with support from State Admn. & Ministry of power
114	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,073.59	08/2012 -	06/2016	46	0	04/05 lines & 02/02 sub station completed. Balance one lines (Sikar-Jaipur) delayed due to contractual/ legal issues arising out of change of ownership & poor performance of the executing contractor. Contract revived by assigning the balance works to the JV Partner and being executed with support by POWERGRID. ROW problem being faced.
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	561.02	07/2013 11/2015	06/2016	35	-8.45	Project completed except Kishenpur – New Wanpoo line. Implementation of balance line affected due to delay final forest clearance. Forest clearance received in Oct'15 NBWL clearance & State Govt. clearance. Limited working period due to snow-bound area affecting implementation. Critical

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
116	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 2,310.58	2,310.58	1,801.75	05/2014 06/2016	06/2016	25	17.77	Project completed except balance ICT's at Champa S/stn. Land acquisition for Champa S/S was delayed. (acquired in Apr'13). Balance work of Champa S/stn. shall be completed matching with HVDC link to Kurakshetra (ant. by Jun'16).
117	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	554.11	11/2013 -	06/2016	31	0	Generation Project delayed (ant. in 2016-17 & beyond). Completion affected due to delay in land acquisition of Chandwa s/s. (land acquired in Apr'13). Also project involves huge forest (Stage-I received in Dec'14 & permission to work received in May'15). Repeated stoppage of work by extremists affecting progress.
118	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	1,474.62	01/2015 -	06/2016	17	0	Completion delayed due to delay in forest clearance. (Huge forest involvement 295 Ha.). Permission to work obtained in Jul'15. Stage-II forest clearance obtained in Dec'15.

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
119	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	104.63	09/2014 -	06/2016	21	0	During the installation of OPGW, RoW problems are being encountered across the TL, which hampered the progress. Mostly OPGW is being laid on charged transmission line and many times PTW(Permit to Work) is not being issued in time due to Power System constraints which affects the work progress.
120	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	5,922.99	06/2015 -	06/2016	12	0	Implementation affected due to delay in land acquisition of Champa Sub station (land acquired in Apr'13). Implementation affected due to ROW problem in western UP (Shamli area). Completion matching with HVDC Station.
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	606.22	11/2014 -	06/2016	19	0	Severe ROW problem in Uttarakhand in Dehradun-Abdullapur line. Implementation affected of Dulhasti-Kishenpur line due to limited working period (snow bound) & difficult working condition.

(March 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
122	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	3,186.31	10/2014 -	06/2016	20	0	Gen. Proj. delayed (ant. in 2016-17 & beyond). Implementation affected due to delay in land acquisition of Kanpur S/stn.(land acquired in Jun'13). Final forest clearance awaited. Permission to work obtained in Jan'16. Completion matching with Sub station.
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	348.02	05/2015 -	06/2016	13	0	Completion delayed due to non-availability of shut down. Completion matching with LILO of Varansai-Sarnath at Sarnath. (Covered under ATS Jharkhara & West Bengal Part-B project).
124	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	484.19	03/2016 -	06/2016	3	0	02 out of 03 lines completed. Completion delayed due to severe ROW problem at Bhiwani end. Bay at Jaipur (RRV PNL) earlier planned for execution through RRV PNL being awarded by Powergrid (under process).
125	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	864.80	05/2016 -	06/2016	1	0	Completion likely to be delay due to severe ROW problem & forest clearance awaited. Permission to work obtained in Jan'16 for Betul – Khandwa line & Khandwa-Indore obtained in Mar'16. Final forest clearance awaited.

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
126	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	8.90	03/2016 -	06/2016	3	0	
127	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	28.80	02/2016 -	06/2016	4	0	
128	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,453.39	12/2011 03/2016	06/2016	54	83.21	
129	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	4,574.78	12/2009 07/2016	07/2016	79	147.51	
130	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,262.27	1,262.27	1,160.87	08/2013 07/2016	07/2016	35	119.91	
131	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	369.70	06/2015 -	08/2016	14	0	Commissioning linked to Angul – Srikakulam line & readiness of Srikakulam – Vemagiri line being executed under TBCB rout (sch Aug'16) Progress being expedited.
132	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,088.53	06/2015 -	08/2016	14	0	Stage – I forest clearance & working permission received. 01 pkg. re-awarded in Jun'15. Commissioning of line linked to readiness of Srikakulam – Vemagiri line being implemented under TBCB route (sch. Aug'16) being expedited.
133	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	2,193.08	2,011.96	09/2009 -	09/2016	84	106.63	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
134	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,991.86	09/2014 -	09/2016	24	0	01 line completed but charging awaited. Completion of balance line delayed due to severe ROW problem faced in Karnataka & contractual issues involved in Salam - Tuticorin line. Issues resolved. Work under progress.
135	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	556.04	04/2016 -	09/2016	5	0	Completion delayed due to delay in sub station land acquisition (land acquired in Feb'14). ROW issues being faced in Jharkhand. Progress being expedited.
136	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	1,005.51	07/2006 10/2016	10/2016	123	274.73	
137	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,751.47	4,490.39	01/2016 -	11/2016	10	57.92	
138	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	17.20	04/2016 -	11/2016	7	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
139	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,907.75	11/2008 01/2016	12/2016	97	22.93	06/07 lines & 02/02 S/s completed ahead of Gen. Proj. Balance 01 line (Edaman-Muvattupuza line) getting delayed due to severe ROW problem in Kerala. Work to start after assessment of compensation & payment by State Govt./KSEB. (G.O. with enhanced compensation issued in Jan 15 again revised on 30.07.15). Compensation to be paid based on land value, to be finalised by concerned DC which is under process.
140	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	602.69	09/2010 01/2016	12/2016	75	54.59	S/s completed but could not be charged because of delay in associated line. 220KV down stream system (under MSETCL scope) delayed Critical. Severe ROW problem in balance 02 lines. LILO line is being completed using underground cable, however, ROW problem for laying of cable continue. Critical. Vapi-Navi Mumbai line now decided to be terminated at Kudus S/S of MSETCL. Stg.-I forest clearance received in Aug 15. Further, its commissioning is linked to readiness of Kudus S/s. which is critical.

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
141	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12	4,824.12	4,277.58	10/2012	12/2016	50	0	Navsari-Boisar line affected due to severe ROW problem & forest clearance (Stg.-I obtained in Mar 16). Permission to work awaited. 1200kV Wardha - Aurangabad affected due to delay in implementation arising out of complexities involved (1200KV tower) & ROW problem also encountered, subsequent contractual issues. 01 pkg. terminated & re-awarded in Dec'14/ Feb'15. Remaining 01 pkg. also terminated in Aug 15. However, contract was revived in Feb 16.
142	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,315.20	12/2012 12/2016	12/2016	48	36.79	11/17 line & 03/07 S/s completed. Implementing of balance lines affected due to stiff resistance/ local disturbances & geographical constraints in NER. 03 nos. lines under re-tendering due to poor performance by contractor. 03 lines in Arunachal Pradesh affected due to issue arising out of compensation to forest clearance & land ownership disputes. Issue getting resolved with support of state/Distt. Admn.

(March 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
143	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	448.72	06/2014 03/2016	12/2016	30	31.17	Project completed except 400KV Madugiri-Yelhanka line. Severe ROW problem being faced in Karnataka. Matter taken up at State level but no break through yet. Down stream system being executed by State not available.
144	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,350.13	07/2014 -	12/2016	29	0	01/02 line & 01/01 S/stn. completed. Balance Aurangabad-Boisor line affected due to delay in forest clearance (Stage-I received in Aug'15). Permission to work received in Oct'15 & severe ROW in routing of line through grape garden. Critical
145	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,501.63	08/2014 12/2015	12/2016	28	27.6	01/03 lines completed. Implementation affected due to delay in forest clearance and NOC for wildlife (awaited for Aurangabad – Padghe) & anticipated delay in completion Kudus (Padghe) S/stn. being executed by MSETCL. Critical
146	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	5,285.00	09/2016 -	12/2016	3	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
147	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,080.15	12/2015 -	12/2016	12	0	Implementation affected due to severe ROW problems in Odisha & Huge forest involvement in Chattisgarh. Involvement of additional forest area reported by State Govt., under process. Stage-I forest clearance awaited. Critical. Processing of forest case very slow.
148	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,944.00	09/2011 -	03/2017	66	54.25	
149	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,556.75	01/2015 -	03/2017	26	0	Gen. Proj.(Punatsangchu HEP in Bhutan) getting delayed. Proj.getting completed ahead of Gen. Proj. now ant. in 2017-18. Work slowed down to the extent feasible to match Gen. Wild life clearance (NBWL) for Punatsangchu - Alipurduar line received in Nov 15 & forwarded to state for further processing for forest clearance, awaited. LILO of HVAC line affected due to ROW problem.

(March 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
150	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34	232.34	219.29	06/2012	03/2017	57	0	S/S almost ready since Jun 12. Line completed except 5 kms near Yelahanka (Bengaluru), which was held up due to Severe ROW/Court case problem. Works commenced after court decision in favour of Powergrid. However, work again stopped due to agitation. State Govt. help required for resolution of compensation issue. Completion very critical as matter taken up at all level but no break through achieved till now.
151	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,268.73	11/2012 03/2016	03/2017	52	36.01	06/08 line & 05/07 sub station completed. Completion affected due to delay in land acquisition of Daltonganj (land acquired in May'15) & Change of location of Ultra S/stn. to Pandiabil due to local resistance. ROW problem being faced in LILO line. Further Daltonganj S/S pkg. re-tendered. Down stream network also not envisaged by JSEB.
152	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	312.57	08/2014 06/2015	03/2017	31	16.63	Completion delayed due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Issue still
153	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19	15,166.19	10,699.00	01/2017	03/2017	2	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
154	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	6,254.00	11/2016 -	08/2017	9	0	
155	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,472.83	05/2014 -	09/2017	40	0	
156	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,079.75	12/2016 -	09/2017	9	0	
157	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	11,612.50	08/2013 12/2017	12/2017	52	23.65	05/08 line completed Implementation affected due to agitation against Big Dam proj. affecting the construction works in Assam and adverse law & order situation in NER. Lower Subhanshri-B Chariyali line in almost standstill since Dec 11 due to agitation. Gen. Proj. are also getting delayed. Kameng HEP is anticipated in FY 2016-17. Project expected completed progressively by Dec 17 matching with Gen. Proj.
158	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	62.56	02/2014 -	02/2018	48	0	
159	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,675.00	01/2011 05/2018	05/2018	88	73.65	
160	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.76	5,548.25	09/2009 -	12/2018	111	114.28	
161	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,788.00	03/2013 -	06/2019	75	29.14	

[illegible]

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
166	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	15	0	i) Delay in issuance of labour licence from labour Deptt. ii) Frequent bandhs and heavy rain iii) Obstruction of work by locals. iv) Difficulty in procurement of sand and aggregates due to ban of forest produce.
167	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	196.70	165.97	01/2016 -	04/2016	3	0	Fund Constraints.
168	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	285.20	12/2015 -	06/2016	6	0	Fund Constraints.
169	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	120.80	11/2013 -	06/2016	31	0	Local disturbances.
	Total		976.47 -	976.47	685.47					
	<u>RAILWAYS</u>									
170	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	259.68	
171	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defroze and Ghaziabad-Meerut section also included as a material modification.
172	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
173	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84	228.1	
174	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	
175	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108	38.8	
176	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, ODISHA	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86	95.9	Contractual issues
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
178	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91	138.61	Contractual issues
179	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	
180	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 2,434.00	2,434.00	419.45	03/2010 -	03/2017	84	648.92	
181	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	
182	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	233.08	
183	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87	38.24	
184	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181	700	
185	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93	18.66	Contractual issue, land aquisition, non finalisation of alignment of flyover at Bilaspur
186	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21	29.06	land aquisition & hurdle clearances like drains etc. by GHMC authorities.

(March 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
187	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
188	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
189	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
190	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	
191	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	
192	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33	-28.09	Non-handing over of land of Joka Depot
193	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
194	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
195	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,544.40	590.26	03/1998 -	12/2019	261	299.79	
196	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
197	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Karthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
198	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
199	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
200	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57	-20	land aquisition problem
	Total		36,714.20 -	90,432.32	38,147.23					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
201	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26	0	
202	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7	0	
203	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7	0	
204	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7	0	
205	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	03/2016	85	28.93	
206	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	03/2016	83	92.75	
207	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	03/2016	88	0	
208	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2016	88	80.68	
209	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	03/2016	83	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
210	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	-	06/2008 -	03/2016	93	0	
211	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	-	06/2008 -	03/2016	93	0	
212	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	03/2016	80	68.99	
213	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	-	04/2013 -	03/2016	35	0	
214	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2016	19	0	
215	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31	0	
216	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21	0	
217	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	458.86	10/2014 -	03/2016	17	0	
218	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	240.00	295.38	11/2008 -	03/2016	88	0	
219	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH,RAJASTHAN	03/2012	914.50 -	914.50	1,108.96	10/2015 -	03/2016	5	0	
220	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	497.20	09/2008 -	04/2016	91	0	
221	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	274.11	10/2008 -	04/2016	90	-8.95	
222	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 04/2016	04/2016	96	0	
223	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	-	09/2010 -	04/2016	67	0	
224	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,607.78	05/2012 -	04/2016	47	0	
225	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	04/2016	35	0	
226	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.67	08/2013 -	04/2016	32	0	
227	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	04/2016	38	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
228	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	1,607.34	04/2015 -	04/2016	12	0	
229	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12	0	
230	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	0	
231	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,310.32	09/2014 -	05/2016	20	0	
232	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	117.97	12/2015 -	05/2016	5	0	
233	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13	0	
234	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	244.34	09/2008 -	06/2016	93	30.1	
235	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	348.16	362.77	09/2007 -	06/2016	105	0	
236	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	469.41	05/2010 -	06/2016	73	0	
237	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56	0	
238	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	863.58	03/2013 -	06/2016	39	0	
239	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,187.71	06/2013 -	06/2016	36	0	
240	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	0	
241	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2016	35	0	
242	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,275.83	06/2013 -	06/2016	36	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
243	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	06/2016	31	0	
244	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36	0	
245	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	-	07/2013 -	06/2016	35	0	
246	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	06/2016	29	0	
247	SIX LANNING OF NELLORE- CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,620.63	05/2014 -	06/2016	25	0	
248	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	06/2016	28	0	
249	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	06/2016	27	0	
250	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	545.27	11/2013 -	06/2016	31	0	
251	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2016	24	0	
252	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	2,388.00	2,490.61	06/2014 -	06/2016	24	-02	
253	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,071.52	03/2013 -	06/2016	39	0	
254	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	06/2016	9	0	
255	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,467.07	12/2015 -	06/2016	6	0	
256	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21	0	
257	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
258	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24	0	
259	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,816.74	10/2011 -	06/2016	56	0	
260	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	-	03/2008 07/2016	07/2016	100	0	
261	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	311.13	06/2008 06/2016	07/2016	97	0	
262	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	0	
263	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	-	04/2008 08/2016	08/2016	100	0	
264	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 07/2016	08/2016	99	0	
265	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	1,708.35	05/2013 -	08/2016	39	0	
266	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	1,876.89	08/2013 -	08/2016	36	0	
267	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,328.50	02/2014 -	08/2016	30	0	
268	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11	0	
269	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	08/2016	50	0	
270	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	-	04/2010 09/2016	09/2016	77	42.25	
271	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	-	05/2013 -	09/2016	40	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
272	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	09/2016	32	0	
273	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	277.41	10/2013 -	09/2016	35	-11	
274	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	0	
275	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	377.64	105.83	03/2014 -	09/2016	30	0	
276	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25	0	
277	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	160.49	01/2016 -	10/2016	9	0	
278	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	239.48	01/2016 -	10/2016	9	0	
279	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	0	
280	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	39.53	11/2014 -	11/2016	24	0	
281	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	12/2016	138	0	
282	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	12/2016	111	0	
283	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,708.29	11/2011 -	12/2016	61	106.5	
284	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,036.26	07/2013 -	12/2016	41	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
285	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49	0	
286	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39	0	
287	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,788.25	03/2013 -	12/2016	45	0	
288	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	880.29	02/2013 -	12/2016	46	0	
289	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,326.02	12/2013 -	12/2016	36	0	
290	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	494.33	04/2014 -	12/2016	32	0	
291	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.61	07/2013 -	12/2016	41	0	
292	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	-	01/2014 -	12/2016	35	0	
293	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	533.13	09/2013 -	12/2016	39	0	
294	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	343.75	04/2014 -	12/2016	32	0	
295	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	229.16	06/2014 -	12/2016	30	0	
296	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	177.61	10/2015 -	12/2016	14	0	
297	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12	0	
298	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
299	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	301.04	39.38	01/2016 -	12/2016	11	0	
300	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	297.35	11/2016 -	12/2016	1	0	
301	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	295.20	04/2008 01/2017	01/2017	105	0	
302	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	77.49	01/2016 -	01/2017	12	0	
303	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	0	
304	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	0	
305	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	03/2017	56	0	
306	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	03/2017	55	0	
307	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	282.68	08/2013 -	03/2017	43	0	
308	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	715.50	11/2015 -	03/2017	16	0	
309	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	574.74	03/2014 -	04/2017	37	0	
310	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	168.31	02/2010 -	05/2017	87	2.29	
311	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL	02/2011	580.43 -	580.43	226.67	08/2013 -	05/2017	45	0	
312	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	1,479.00	498.11	06/2015 -	05/2017	23	0	
313	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
314	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,674.79	08/2013 -	07/2017	47	0	
315	REHABILITATION AND UPGRADE OF NH-42 FROM KM 4 TO 350 TO KM 75 TO 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	0	
316	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	368.73	70.23	09/2016 -	09/2017	12	0	
317	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	
318	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24	0	
319	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24	0	
320	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	303.94	05/2013 -	12/2017	55	0	
321	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	622.74	10/2013 -	12/2017	50	0	
322	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	348.00	07/2014 -	12/2017	41	0	
323	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	
324	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA) - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
325	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
326	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	0	
	Total		88,006.21 -	89,832.14	66,833.39					
	<u>SHIPPING AND PORTS</u>									
327	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 600.00	600.00	525.49	03/2006 01/2016	07/2016	124	300	Relocating of fishing stalls for a length about 300m in fishing harbour.
328	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88	66.82	
	Total		395.67 -	1,009.83	891.69					
	<u>TELECOMMUNICATIONS</u>									
329	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	196.20	07/2015 -	03/2017	20	0	
330	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30	-4.74	
	Total		15,445.17 -	15,345.17	1,556.20					
	<u>URBAN DEVELOPMENT</u>									
331	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	12,712.23	06/2011 -	06/2016	60	81.53	
332	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16	0	
333	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	

(March 2016)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
334	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	143.72	06/2012 03/2016	05/2016	47	0	
335	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	183.26	05/2013 10/2015	06/2016	37	0	
336	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	12,472.32	12/2015 -	08/2016	8	0	
337	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	315.00	188.33	06/2015 08/2016	11/2016	17	0	
338	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	22,146.20	03/2016 -	12/2016	9	0	Rehabilitation and Resettlement, Land Acquisition problem.
339	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	105.95	09/2016 01/2017	01/2017	4	0	
340	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	93.68	12/2014 12/2016	03/2017	27	0	
341	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	191.97	-	03/2012 08/2016	03/2017	60	-6.36	
342	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	41.86	09/2015 07/2016	04/2017	19	0	
343	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	16.16	03/2016 -	09/2017	18	0	
	Total		62,113.52 -	67,314.49	48,161.40					
	Grand Total		528,819.65	644,703.02	407,654.58					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54	89
	Total		16,663.00 -	28,139.00				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58	60
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
6	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97	24
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
	Total		1,800.69 -	3,170.48				
	<u>HEAVY INDUSTRY</u>							
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROLEUM</u>							
9	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38	29
10	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	10/2016	19.35	43
11	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2018	27.79	12
12	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	02/2018	17.66	4
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	04/2016	67.62	54
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2016	45.83	43
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72	17
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	05/2016	70.49	52
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	06/2017	29.42	27
	Total		7,763.20 -	10,878.04				
	<u>POWER</u>							
19	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]	05/2010	250.03 -	390.51	01/2013 -	05/2016	56.19	40
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	03/2017	16.63	31
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
22	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2016	54.59	75
23	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2016	31.17	30
24	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32	25
25	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91	35
26	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63	84
27	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	03/2017	36.01	52
28	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77	43
29	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2016	27.60	28
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2016	22.93	97
31	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	02/2012	1,927.16 -	1,940.58	10/2014 -	04/2016	0.70	18
32	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	05/2011	1,961.87 -	2,310.58	05/2014 -	06/2016	17.77	25

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
33	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	12/2016	36.79	48
34	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	06/2016	83.21	54
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	07/2016	147.51	79
36	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14	75
37	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92	10
38	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28	111
39	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06	61
40	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
41	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
42	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		60,228.36 -	97,500.40				
	<u>RAILWAYS</u>							
43	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
44	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61	91
45	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
46	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90	86
47	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
48	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
49	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
50	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
51	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66	93
52	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	2,434.00	03/2010 -	03/2017	648.92	84

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
53	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
54	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
55	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
56	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
57	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06	21
58	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24	87
59	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
60	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
61	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
62	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
63	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
64	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
65	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
67	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
68	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		21,862.31 -	77,189.14				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
69	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221	12/2003	155.00 -	201.66	09/2008 -	06/2016	30.10	93
70	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68	88
71	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99	80
72	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75	83

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25	77
74	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29	87
75	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	03/2016	28.93	85
76	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50	61
	Total		2,586.46 -	4,438.02				
	<u>SHIPPING AND PORTS</u>							
77	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	03/2006 -	07/2016	300.00	124
78	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82	88
	Total		395.67 -	1,009.83				
	<u>STEEL</u>							
79	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50	15
80	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79	7
81	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102	07/2011	324.87 324.87	325.00	12/2015 -	03/2016	0.04	3
82	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39	8
83	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29	25
	Total		1,761.97 -	2,267.02				
	Grand Total		114,779.66	228,419.23				

Annexure - VIII

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015
	Total		553.21 -		
	<u>COAL</u>				
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		467.78 -		
	<u>STEEL</u>				
4	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	04/2013 09/2014	06/2015
5	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	05/2013 01/2015	08/2015
6	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
7	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		6,451.55 -		
	<u>PETROCHEMICALS</u>				
8	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	04/2012 12/2013	12/2015
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
9	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 -	01/2016
10	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
11	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
12	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
13	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
14	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
15	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	01/2014 -	-
	Total		6,389.77 -		
	<u>POWER</u>				
16	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.57	07/2013 01/2016	01/2016
17	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
18	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	Total		6,912.78 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
19	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014
	Total		414.11 -		
	<u>RAILWAYS</u>				
20	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
21	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
22	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
23	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
24	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
25	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
26	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
27	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
28	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
29	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014
30	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
31	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015
32	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
33	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
34	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015
35	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
36	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
37	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015
38	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
39	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015
40	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015
41	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESJI- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015
42	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015
43	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015
44	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
45	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015
46	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
47	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-
48	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
49	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
50	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
51	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 -	-
52	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	10/2007 -	-
53	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
54	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
55	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
56	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
57	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
58	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
59	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 2,200.00	- -	-
60	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
61	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
62	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR,UTTAR PRADESH	04/1997	836.26 -	- -	-
63	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
64	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
65	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
66	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
67	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
68	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
69	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
70	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
71	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
72	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
73	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
74	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
75	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
76	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
77	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
78	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
79	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
80	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
81	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
82	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
83	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
84	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
85	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
86	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
87	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
88	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
89	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
90	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
91	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
92	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
93	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
94	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
95	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
96	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
97	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N220000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
98	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
99	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
100	TIDIVANAM-NAGARI (NL) - [N220000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
101	BARDHAMAN-KATWA (GC) - [N220000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
102	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N220000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
103	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N220000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
104	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N220000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
105	TINPAHAR - SAHIBGANJ (ER) - [N220000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
107	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
108	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
109	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	-
110	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	-
111	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	-
112	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-
113	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
114	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-
115	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-
116	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	-
117	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-
118	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
119	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-
120	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-
121	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	- -	-
122	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	- -	-
123	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	- -	-
124	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-
125	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 913.48	- -	-
126	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	-
127	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	- -	-
128	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
129	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-
130	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
131	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
132	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
133	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
134	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
135	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
136	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
137	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
138	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
139	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
140	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
141	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
142	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
143	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
144	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
145	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
146	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
147	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
148	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
149	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-
150	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
151	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
152	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-
153	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-
154	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
155	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-
156	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
158	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
159	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
160	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
161	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
162	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
163	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
164	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
165	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
166	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
167	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
168	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
169	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
170	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
171	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
172	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
173	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
174	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
175	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
176	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
177	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
178	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
179	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
180	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
181	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
182	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
183	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
184	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
185	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
186	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
187	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
188	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
189	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
190	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
191	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
192	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
193	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
194	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
195	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
196	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
197	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
198	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
199	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
200	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
201	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
202	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
203	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
204	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
205	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
206	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
207	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
208	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
209	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
210	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
211	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
212	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
213	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
214	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
215	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
216	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
217	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
218	MUDKhed-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
219	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
220	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
221	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
222	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
223	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
224	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
225	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
226	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
227	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
228	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
229	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
230	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
231	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
232	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
233	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
234	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
235	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
236	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
237	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
238	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
239	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
240	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
241	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
242	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-
243	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
244	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
245	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
246	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
247	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
248	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
249	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
250	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
251	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
252	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
253	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
254	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		195,201.06		
			-		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
255	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39	08/2014	08/2014
			-	-	
256	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98	11/2014	11/2014
			-	-	
257	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00	12/2013	01/2016
			-	-	
258	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39	03/2013	01/2016
			-	-	
259	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH,MADHYA PRADESH	05/2013	1,055.00	11/2015	01/2016
			-	-	
260	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72	06/2008	02/2016
			-	-	
261	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10	09/2012	02/2016
			2,782.54	-	
262	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51	09/2014	02/2016
			-	-	
263	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47	09/2007	-
			-	-	
264	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00	10/2008	-
			-	-	
265	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03	10/2008	-
			-	-	
266	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00	07/2008	-
			-	-	
267	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00	06/2008	-
			-	-	
268	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00	06/2008	-
			-	-	
269	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00	12/2009	-
			-	-	
270	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00	02/2010	-
			-	-	
271	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75	08/2011	-
			-	-	
272	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30	10/2011	-
			-	-	
273	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06	12/2012	-
			-	-	
274	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00	-	-
			-	-	
275	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00	09/2013	-
			-	-	
276	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00	11/2013	-
			-	-	
277	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07	01/2013	-
			-	-	

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
278	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	-
279	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-
280	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
281	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
282	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	-
283	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
284	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-
285	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.51 -	05/2014 -	-
286	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	-
287	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
288	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-
289	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
290	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-
291	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
292	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-
293	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
294	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
295	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	-
296	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
297	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
298	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
299	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
300	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
301	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
302	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
303	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
304	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
305	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
306	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
307	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-
308	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
309	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
310	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
311	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
312	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
313	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
314	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
315	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
316	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
317	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
318	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
319	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
320	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
321	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
322	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
323	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
324	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-
325	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
326	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
327	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
328	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
329	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
330	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
331	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
332	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
333	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
334	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
335	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
336	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
337	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-

Date of Commissioning (Month/Year)					
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
338	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
339	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
340	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
341	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
342	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
343	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
344	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
345	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
346	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
347	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
348	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
349	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
350	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-
351	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
352	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
353	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
354	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
355	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
356	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
357	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
358	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
359	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-
360	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
361	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
362	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	-
363	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH	06/2015	583.79 -	- -	-
364	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	- -	-
365	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH,WEST BENGAL	10/2015	361.15 -	- -	-
366	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-
367	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-
368	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-
369	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
370	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
371	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-
372	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	-
373	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	-
374	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	- -	-
375	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-
376	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2016 -	-
377	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU	01/1991	285.00 -	01/2008 -	-
378	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
379	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
380	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
381	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
382	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
383	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
384	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	-
385	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-
386	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR	08/2015	814.04 -	- -	-
387	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
388	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	- -	-
389	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
390	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-
391	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2019 -	-
392	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	- -	-
393	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-
394	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
395	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-
396	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
397	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-
398	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-
399	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
400	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
401	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
402	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
403	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	-
404	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-
405	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
406	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
407	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	- -	-
408	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
409	ROHTAK - BAWAL (APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA	02/2010	650.00 -	- -	-
410	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
411	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
412	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
413	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
414	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
415	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
416	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
417	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
418	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
419	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
	Total		93,345.13 -		
	<u>SHIPPING AND PORTS</u>				
420	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	01/2016
421	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		2,793.79		
			-		
	<u>URBAN DEVELOPMENT</u>				
422	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02	03/2015	03/2015
			-	-	
423	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69	03/2015	03/2015
			-	-	
424	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD, BIHAR	02/2012	171.10	09/2014	07/2015
			202.00	07/2015	
425	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00	01/2015	12/2015
			-	-	
426	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33	11/2014	-
			-	-	
427	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30	08/2014	-
			-	-	
428	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD, DELHI	06/2015	197.33	-	-
			-	-	
429	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB	02/2014	388.00	01/2015	-
			-	-	
430	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD, TAMIL NADU	12/2015	209.00	-	-
			-	-	
431	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43	02/2015	-
			-	-	
432	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23	10/2012	-
			-	-	
433	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI (IN ZONE 2 IN - [N28000082]JnNURM, ANDHRA PRADESH	08/2007	246.90	-	-
			-	-	
	Total		26,444.33		
			-		
	Grand Total		344,434.12		

Annexure - IX

Details of Projects Without Original Date of Commissioning

(March 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	175.00	-	- -	12/2017	-	0/0
	Total		175.00 -	175.00	.00				0/0
	<u>RAILWAYS</u>								
2	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	0/1
3	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2016	-	0/0
4	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
5	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
6	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
7	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
8	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
9	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
10	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
12	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
13	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
14	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
15	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
16	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0

(March 2016)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
18	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
19	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
21	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
22	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
23	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
24	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
25	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
26	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
27	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
28	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	175.26	- -	03/2020	-	0/0
	Total		19,590.88 -	30,884.76	5,992.51				0/1
	ROAD TRANSPORT AND HIGHWAYS								
29	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	349.60	- -	12/2016	-	0/0
30	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	446.77	-	- -	06/2017	-	0/4
31	KUNDUPUR-SURATHKAL AND MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	818.53	- -	09/2017	-	2/3
32	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	-	- -	10/2017	-	0/4
33	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	1,393.00	1,060.85	- -	01/2018	-	0/0

(March 2016)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
34	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	36.02	- -	04/2018	-	0/1
35	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	1,388.00	20.60	- -	08/2018	-	0/0
36	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	154.48	- -	05/2018	-	0/0
	Total		5,710.73 -	5,710.73	2,440.08				2/12
	Grand Total		25,476.61	36,770.49	8,432.59				2/13

Annexure - X

Details of Projects Without Milestones w.r.t. Original Schedule

			(March 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	09/2017	0/0
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	09/2018	0/0
	Total		1,177.28 -			0/0
	<u>COAL</u>					
5	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	03/2018 -	03/2018	0/0
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
8	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	03/2024 -	03/2024	0/0
	Total		3,338.19 -			0/0
	<u>FERTILISERS</u>					
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
10	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 355.13	11/2016 11/2016	11/2016	0/0
11	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 344.50	11/2016 11/2016	11/2016	0/0
12	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	09/2017	0/0
	Total		2,555.63 -			0/0
	<u>STEEL</u>					

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
13	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	02/2014 -	03/2016	0/0
14	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	12/2015 -	03/2016	0/0
15	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016	0/0
16	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 254.00	06/2016 -	06/2016	0/0
17	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2016	0/0
18	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2016	0/0
19	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	03/2017	0/0
20	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	03/2017	0/0
21	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2017	0/0
22	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	06/2017	0/0
23	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 207.00	12/2016 -	07/2017	0/0
24	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	09/2017	0/0
25	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
26	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
27	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
28	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
29	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
30	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0
31	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
32	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
33	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	Total		15,584.17 -			0/0
	<u>PETROLEUM</u>					
34	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 -	01/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	04/2016	0/0
36	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 05/2016	05/2016	0/0
37	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	05/2016	0/0
38	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	07/2016	0/0
39	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 10/2016	10/2016	0/0
40	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 370.00	03/2013 10/2016	10/2016	0/0
41	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
42	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	01/2017 -	01/2017	0/0
43	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM	06/2012	150.00 -	07/2014 -	01/2017	0/0
44	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	03/2017	0/0
45	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	03/2017 -	03/2017	0/0
46	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT	11/2015	500.00 -	03/2017 -	03/2017	0/0
47	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	04/2017 -	04/2017	0/0
48	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 2,098.43	05/2017 -	05/2017	0/0
49	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
50	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA	05/2015	2,443.00 -	12/2017 -	12/2017	0/0
51	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	12/2017 -	12/2017	0/0
52	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 03/2017	03/2018	0/0
53	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 -	04/2018	0/0
54	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 -	09/2018	0/0
55	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
56	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 -	03/2019	0/0
57	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 -	11/2019 -	11/2019	0/0
58	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
59	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 03/2020	03/2020	0/0
60	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
61	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
62	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
63	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
64	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-	0/0
	Total		47,080.98 -			0/0
	<u>POWER</u>					
65	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	05/2016 -	05/2016	0/0
66	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
67	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL,GUJARAT	10/2015	315.00 -	10/2016 -	10/2016	0/0
68	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	11/2016	0/0
69	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 -	03/2017	0/0
70	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
71	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2017	0/0
72	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
73	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
74	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	05/2018	0/0
75	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA	01/2016	187.04 -	06/2018 -	06/2018	0/0
76	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
77	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT	01/2016	244.19 -	07/2018 -	07/2018	0/0
78	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
79	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
80	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	03/2022	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
81	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		22,763.90 -			0/0
	<u>HEAVY INDUSTRY</u>					
82	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
83	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014	0/0
84	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016	0/0
85	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	04/2016	0/0
86	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	06/2016	0/0
87	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 -	06/2016	0/0
88	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	05/2017	0/0
89	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	05/2017	0/0
90	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	05/2017	0/0
91	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	03/2018	0/0
	Total		2,563.15 -			0/0
	<u>RAILWAYS</u>					
92	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
93	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
94	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
95	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
96	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
97	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
98	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
99	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
100	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
101	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
102	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
103	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
104	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015	0/0
105	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
106	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
107	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
108	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
109	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
110	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
111	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
112	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
113	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0
114	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
115	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
116	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
117	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
118	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	03/2004 -	03/2016	0/0
119	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
120	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
121	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
122	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
123	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
124	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016	0/0
125	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	04/2016	0/0
126	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
127	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	10/2016	0/0
128	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
129	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	12/2016	0/0
130	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
131	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
132	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
133	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
134	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 2,434.00	03/2010 -	03/2017	0/0
135	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
136	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
137	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
138	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
139	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2017	0/0
140	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
141	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2017	0/0
142	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	12/2017	0/0
143	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
144	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
145	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
146	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
147	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
148	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
149	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
150	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
151	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	- -	03/2018	0/0
152	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
153	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
154	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0
155	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
156	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR, MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
157	AMBARİ FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
158	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
159	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
160	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
161	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
162	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
163	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
164	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
165	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
166	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
167	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
168	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
169	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
170	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
171	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
172	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
173	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
174	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
175	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
176	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
177	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
178	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
180	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
181	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-	0/0
182	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
183	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
184	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-	0/0
185	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	03/2009 -	-	0/0
186	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 -	-	0/0
187	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
188	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-	0/0
189	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
190	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0
191	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR, MULTI STATE	04/2008	822.39 -	- -	-	0/0
192	BAGALKOT-KUDACHI NL - [N22000258]SWR, KARNATAKA	04/2010	377.93 -	- -	-	0/0
193	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,054.35 2,200.00	- -	-	0/0
194	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR, KARNATAKA	04/2010	2,127.00 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
195	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
196	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR,UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
197	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
198	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
199	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
200	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
201	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
202	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
203	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
204	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
205	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
206	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
207	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
208	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
209	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
210	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
211	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
212	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
213	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
214	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
215	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
216	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
217	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
218	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
219	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
220	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
221	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
222	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
223	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
224	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
225	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
226	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
227	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
228	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
229	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
230	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
231	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
232	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
233	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
234	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
235	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
236	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
237	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
238	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
239	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
240	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
241	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
242	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
243	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
244	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
245	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
246	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
247	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
248	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
249	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
250	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
251	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
252	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
253	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
254	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
255	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
256	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
257	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
258	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
259	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
260	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
261	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
262	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
263	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
264	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
265	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
266	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
267	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
268	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
269	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
270	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
271	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
272	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
273	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-	0/0
274	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0
275	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-	0/0
276	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-	0/0
277	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-	0/0
278	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-	0/0
279	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-	0/0
280	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-	0/0
281	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-	0/0
282	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-	0/0
283	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-	0/0
284	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-	0/0
285	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-	0/0
286	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-	0/0
287	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-	0/0
288	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-	0/0
289	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-	0/0
290	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
291	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
292	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
293	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
294	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
295	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
296	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
297	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
298	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
299	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
300	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
301	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
302	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
303	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
304	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
305	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
306	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
307	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
308	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
309	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
310	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
311	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
312	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
313	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
314	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
316	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
317	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
318	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
319	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
320	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
321	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
322	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
323	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
324	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
325	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
326	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
327	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
328	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
329	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
330	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
331	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
332	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
333	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
334	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
335	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
336	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
337	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
338	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
339	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
340	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
341	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
342	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
343	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
344	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
345	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
346	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
347	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
348	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
349	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
350	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
351	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
352	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
353	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
354	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
355	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
356	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
357	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
358	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
359	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
360	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
361	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
362	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
363	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
364	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
365	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
366	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
367	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-	0/0
368	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
369	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
370	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
371	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
372	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
373	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0
374	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
375	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-	0/0
376	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
377	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
378	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0
379	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
380	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-	0/0
381	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-	0/0
382	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
383	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
384	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
385	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-	0/0
386	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
387	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-	0/0
	Total		253,151.96 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
388	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	03/2016	0/0
389	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
390	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
391	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
392	WIDENING WITH PS AND STRONG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	03/2016	0/0
393	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0
394	REHABILITATION AND AUGMENTATION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
395	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	01/2016	0/0
396	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	01/2016	0/0
397	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	01/2016	0/0
398	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	02/2016	0/0
399	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	02/2016	0/0
400	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	03/2016	0/0
401	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	03/2016	0/0
402	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	03/2016	0/0
403	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	03/2016	0/0
404	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	03/2016	0/0
405	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	03/2016	0/0
406	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	03/2016	0/0
407	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	03/2016	0/0
408	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	03/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
409	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	03/2016	0/0
410	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	03/2016	0/0
411	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2016	0/0
412	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	03/2016	0/0
413	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	03/2016	0/0
414	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	11/2008 -	03/2016	0/0
415	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH,RAJASTHAN	03/2012	914.50 -	10/2015 -	03/2016	0/0
416	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2016	0/0
417	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	04/2016	0/0
418	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	04/2016	0/0
419	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 04/2016	04/2016	0/0
420	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	04/2016	0/0
421	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	04/2016	0/0
422	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	04/2016	0/0
423	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	04/2016	0/0
424	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	04/2016	0/0
425	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2016	0/0
426	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	04/2016 -	04/2016	0/0
427	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2016	0/0
428	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	05/2016	0/0
429	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2016	0/0
430	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	05/2016	0/0
431	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	05/2016	0/0
432	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
433	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	06/2016	0/0
434	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	06/2016	0/0
435	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	06/2016	0/0
436	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	06/2016	0/0
437	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2016	0/0
438	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	06/2016	0/0
439	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
440	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	06/2016	0/0
441	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	06/2016	0/0
442	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	06/2016	0/0
443	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2016	0/0
444	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2016	0/0
445	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2016	0/0
446	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	06/2016	0/0
447	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	06/2016	0/0
448	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	06/2016	0/0
449	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	06/2016	0/0
450	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	06/2014 -	06/2016	0/0
451	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	06/2016	0/0
452	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	06/2016	0/0
453	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	06/2016	0/0
454	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI,UTTAR PRADESH	06/2014	569.38 -	06/2016 -	06/2016	0/0
455	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]DORTH,HARYANA	03/2013	959.25 -	06/2016 -	06/2016	0/0
456	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	06/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
457	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 07/2016	07/2016	0/0
458	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 06/2016	07/2016	0/0
459	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 08/2016	08/2016	0/0
460	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 07/2016	08/2016	0/0
461	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	08/2016	0/0
462	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	08/2016	0/0
463	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	08/2016	0/0
464	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
465	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
466	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	08/2016	0/0
467	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH	02/2012	912.00 -	08/2016 -	08/2016	0/0
468	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2016	0/0
469	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	08/2016	0/0
470	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2016	09/2016	0/0
471	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	09/2016	0/0
472	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2016	0/0
473	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	09/2016	0/0
474	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
475	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2016	0/0
476	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
477	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI,HARYANA	12/2012	438.75 -	09/2016 -	09/2016	0/0
478	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	09/2016	0/0
479	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2016	0/0
480	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
481	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	10/2016	0/0
482	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	10/2016	0/0
483	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
484	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
485	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
486	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
487	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
488	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
489	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	11/2016	0/0
490	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	12/2016	0/0
491	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	12/2016	0/0
492	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	12/2016	0/0
493	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	12/2016	0/0
494	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2016	0/0
495	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
496	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2016	0/0
497	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2016	0/0
498	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2016	0/0
499	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	12/2016	0/0
500	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2016	0/0
501	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
502	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2016	0/0
503	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	12/2016	0/0
504	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	12/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
505	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	12/2016	0/0
506	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
507	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016	0/0
508	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	12/2016	0/0
509	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	12/2016	0/0
510	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	01/2017	0/0
511	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
512	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	01/2017	0/0
513	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	01/2017	0/0
514	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
515	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	02/2017	0/0
516	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
517	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2017	0/0
518	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	03/2017	0/0
519	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	03/2017	0/0
520	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
521	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
522	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
523	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
524	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2017	0/0
525	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN	10/2014	206.12 -	04/2017 -	04/2017	0/0
526	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017	0/0
527	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	05/2017	0/0
528	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL	02/2011	580.43 -	08/2013 -	05/2017	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
529	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	05/2017	0/0
530	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	05/2017	0/0
531	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	05/2017	0/0
532	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
533	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
534	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
535	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
536	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI,TAMIL NADU	12/2014	451.58 -	06/2017 -	06/2017	0/0
537	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	07/2017	0/0
538	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
539	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
540	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	07/2017	0/0
541	UMARIYA TO SHAHNOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
542	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
543	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
544	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
545	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
546	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
547	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATTA - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	10/2017	0/0
548	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2017	0/0
549	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
550	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
551	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
552	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
553	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
554	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
555	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
556	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	12/2017	0/0
557	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
558	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2017	0/0
559	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
560	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
561	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
562	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	12/2017	0/0
563	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
564	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
565	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
566	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
567	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
568	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
569	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
570	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
571	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
572	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
573	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
574	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
575	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
576	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
577	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
578	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
579	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
580	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
581	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
582	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
583	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
584	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	05/2018	0/0
585	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	06/2018	0/0
586	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
587	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
588	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
589	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
590	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
591	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
592	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
593	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
594	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
595	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
596	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	07/2018	0/0
597	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
598	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	- -	08/2018	0/0
599	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	12/2018	0/0
600	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
601	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
602	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	01/2019	0/0
603	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
604	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 -	-	0/0
605	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
606	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
607	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
608	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
609	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
610	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
611	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
612	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
613	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-	0/0
614	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
615	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
616	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
617	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	-	0/0
618	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-	0/0
619	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-	0/0
620	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.51 -	05/2014 -	-	0/0
621	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	-	0/0
622	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0
623	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-	0/0
624	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
625	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-	0/0
626	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-	0/0
627	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-	0/0
628	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
629	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
630	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	-	0/0
631	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
632	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
633	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
634	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
635	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
636	REHABILITATION AND UPGADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
637	REHABILITATION AND UPGADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
638	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
639	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
640	REHABILITATION AND UPGADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
641	REHABILITATION AND UPGADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
642	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
643	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
644	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
645	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
646	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
647	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
648	REHABILITATION AND UPGADATION TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
649	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
650	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
651	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-	0/0
652	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
653	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
654	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
655	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
656	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
657	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
658	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
659	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
660	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
661	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
662	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
663	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
664	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
665	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
666	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
667	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
668	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
669	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
670	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
671	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
672	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
673	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
674	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
675	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
676	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
677	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
678	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
679	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
680	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
681	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
682	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
683	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0
684	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
685	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
686	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-	0/0
687	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
688	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
689	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	-	0/0
690	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH	06/2015	583.79 -	- -	-	0/0
691	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	- -	-	0/0
692	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH,WEST BENGAL	10/2015	361.15 -	- -	-	0/0
693	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-	0/0
694	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-	0/0
695	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-	0/0
696	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
697	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
698	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-	0/0
699	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	-	0/0
700	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	-	0/0
701	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	- -	-	0/0
702	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-	0/0
703	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2016 -	-	0/0
704	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU	01/1991	285.00 -	01/2008 -	-	0/0
705	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
706	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
707	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
708	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
709	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
710	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
711	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	-	0/0
712	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-	0/0
713	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR	08/2015	814.04 -	- -	-	0/0
714	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
715	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	- -	-	0/0
716	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
717	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-	0/0
718	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2019 -	-	0/0
719	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	- -	-	0/0
720	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
721	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
722	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-	0/0
723	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
724	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-	0/0
725	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-	0/0
726	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
727	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
728	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
729	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
730	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	-	0/0
731	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-	0/0
732	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
733	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0
734	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	- -	-	0/0
735	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
736	ROHTAK - BAWAL(APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA	02/2010	650.00 -	- -	-	0/0
737	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
738	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
739	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
740	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
741	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
742	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
743	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
744	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
745	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
746	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	- -	05/2018	0/0
747	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-	0/0
	Total		223,521.39 -			0/0
	<u>SHIPPING AND PORTS</u>					
748	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	01/2016	0/0
749	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 600.00	03/2006 01/2016	07/2016	0/0
750	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	04/2009 03/2010	08/2016	0/0
751	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
752	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		3,399.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
753	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	03/2017	0/0
	Total		13,334.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
754	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 -	03/2015 -	03/2015	0/0
755	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	03/2015 -	03/2015	0/0
756	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 202.00	09/2014 07/2015	07/2015	0/0
757	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
758	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	03/2016	0/0
759	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 10/2015	06/2016	0/0
760	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	06/2015 08/2016	11/2016	0/0
761	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
762	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 01/2017	01/2017	0/0
763	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	03/2012 08/2016	03/2017	0/0
764	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
765	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	06/2017	0/0
766	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
767	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
768	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
769	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	-	0/0
770	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-	0/0
771	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	- -	-	0/0
772	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-	0/0
773	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	-	0/0
774	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
775	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		107,670.71 -			0/0
	Grand Total		698,056.61			0/0

Annexure - XI

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(March 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	157.69	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	157.69		
	<u>PETROLEUM</u>						
2	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	284.19	09/2017 03/2018	12/2017
	Total		3,076.00 -	3,076.00	284.19		
	<u>COAL</u>						
3	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	-	03/2020 -	03/2018
4	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		1,053.94 -	1,053.94	3.52		
	<u>POWER</u>						
5	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	85.90	02/2017 -	03/2016
	Total		188.75 -	188.75	85.90		
	<u>PETROLEUM</u>						
6	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	339.10	01/2017 -	06/2016
	Total		419.04 -	419.04	339.10		
	<u>URBAN DEVELOPMENT</u>						
7	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	2,757.97	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,757.97		
	<u>PETROLEUM</u>						

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
8	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	6,068.80	1,057.64	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	1,057.64		
	Grand Total		16,247.72	16,474.89	4,686.01		

Annexure - XII

List of Projects on schedule w.r.t. Latest Schedule

(March 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	5,677.00	5,187.55	09/2010 09/2016	09/2016
	Total		3,492.00 -	5,677.00	5,187.55		
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	314.61	24.09	09/2018 -	09/2018
	Total		314.61 -	314.61	24.09		
	<u>COAL</u>						
3	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
4	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2016
5	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	206.38	03/2017 -	03/2017
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	236.49	03/2018 -	03/2018
8	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021
9	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	813.94	03/2023 03/2023	03/2023
10	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	188.76	03/2022 -	03/2022
11	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	16.87	03/2020 -	03/2020
12	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.27	04/2017 -	04/2017
13	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	106.05	03/2021 -	03/2021
14	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	49.03	04/2015 04/2019	04/2019
15	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
16	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
17	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	149.65	03/2020 -	03/2020
18	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	620.96	03/2026 -	03/2026
19	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	72.15	03/2025 -	03/2025
20	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
21	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	78.27	03/2019 -	03/2019
22	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
23	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
24	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.74	03/2019 -	03/2019
25	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
26	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
27	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	39.64	03/2023 -	03/2023
28	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
29	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	67.25	12/2019 -	12/2019
30	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
31	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
32	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	232.58	03/2020 -	03/2020
33	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	1,458.17	30.39	06/2015 08/2019	08/2019
34	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	1,813.37	12/2015 04/2018	04/2018
35	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016
36	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
37	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
38	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	847.83	03/2016 -	03/2016
39	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	110.10	03/2020 -	03/2020
40	GOKUL - [N06000120]	11/2014	267.67 -	267.67	175.50	03/2018 -	03/2018

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
41	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
42	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.89	03/2019 -	03/2019
43	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.05	03/2019 -	03/2019
44	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
45	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	48.67	03/2021 -	03/2021
46	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021
47	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	179.12	03/2021 -	03/2021
48	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.09	03/2018 -	03/2018
	Total		43,811.35 -	43,602.55	6,759.63		
	<u>FERTILISERS</u>						
49	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	56.41	11/2016 -	11/2016
	Total		197.79 -	209.44	56.41		
	<u>HEALTH AND FAMILY WELFARE</u>						
50	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	14.38	03/2018 -	03/2018
51	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR [N21000010]	12/2014	168.90 -	168.90	3.63	05/2017 -	05/2017
52	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	293.65	67.84	05/2017 -	05/2017
53	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	204.44	36.17	05/2017 -	05/2017
	Total		1,172.57 -	1,172.57	122.02		
	<u>MINES</u>						
54	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	2.02	09/2017 -	09/2017
55	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	126.21	11/2016 11/2016	11/2016
56	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR [N10000008]	12/2015	355.13 -	355.13	107.67	11/2016 11/2016	11/2016

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		2,555.63 -	2,555.63	235.90		
	<u>PETROLEUM</u>						
57	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	595.62	04/2015 05/2016	05/2016
58	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]	2/2016	367.11 -	367.11	-	04/2017 -	04/2017
59	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	38.82	01/2018 -	01/2018
60	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,190.69	-	04/2018 -	04/2018
61	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]	1/2015	4,619.94 -	4,619.94	975.16	12/2017 -	12/2017
62	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
63	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	195.63	-	09/2018 -	09/2018
64	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	173.28	78.73	01/2017 -	01/2017
65	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	130.87	02/2020 -	02/2020
66	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215]	8/2010	103.02 -	171.04	114.42	07/2016 -	07/2016
67	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
68	IOR OF B-173A FIELD - [N16000140]	1/2012	352.49 -	352.49	141.15	03/2014 05/2016	05/2016
69	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	1,235.07	05/2014 03/2017	03/2017
70	RESID UPGRADATION PROJECT - [N16000184]	3/2013	3,110.36 -	3,110.36	1,666.63	11/2015 11/2016	11/2016
71	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	193.74	09/2017 -	09/2017
72	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	7/2009	3,957.00 -	3,561.00	112.83	01/2013 12/2018	12/2018
73	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	606.85	11/2015 11/2016	11/2016
74	CONSTRUCTION OF 6 ETPS - [N16000117]	3/2009	317.64 -	240.95	127.28	09/2012 06/2016	06/2016
75	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	633.74	04/2016 12/2017	12/2017
76	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	99.05	10/2017 02/2018	02/2018
77	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	174.38	09/2016 -	09/2016

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
78	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
79	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	11,119.68	05/2016 -	05/2016
80	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,334.59	03/2015 06/2017	06/2017
81	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	142.35	12/2016 -	12/2016
82	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	673.48	12/2018 -	12/2018
83	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	3,089.78	05/2017 05/2017	05/2017
84	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	18.62	03/2017 -	03/2017
85	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	6/2007	736.65 -	736.65	514.33	09/2011 10/2016	10/2016
86	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	148.72	12/2017 -	12/2017
87	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	17.84	03/2013 10/2016	10/2016
88	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
89	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	275.04	10/2014 03/2017	03/2017
90	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	-	02/2019 -	02/2019
91	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	757.83	05/2017 -	05/2017
92	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	749.95	05/2019 03/2020	03/2020
	Total		73,838.18 -	75,942.09	25,766.55		
	<u>POWER</u>						
93	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	2/2010	2,144.00 -	2,932.88	2,315.20	12/2012 12/2016	12/2016
94	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	143.00	08/2017 -	08/2017
95	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,261.00	12/2016 -	12/2016
96	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	719.20	03/2018 -	03/2018
97	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	12.70	11/2017 -	11/2017

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
98	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	36.50	05/2016 -	05/2016
99	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	352.70	04/2018 -	04/2018
100	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	11,675.00	01/2011 05/2018	05/2018
101	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	-	05/2018 -	05/2018
102	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	16.50	07/2018 -	07/2018
103	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	6,152.00	06/2017 -	06/2017
104	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	600.90	02/2014 03/2016	03/2016
105	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	439.94	12/2016 -	12/2016
106	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	1,160.87	08/2013 07/2016	07/2016
107	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	138.90	08/2016 -	08/2016
108	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	430.30	04/2018 -	04/2018
109	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	113.20	04/2017 -	04/2017
110	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	4,574.78	12/2009 07/2016	07/2016
111	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	-	03/2017 -	03/2017
112	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	1,226.00	03/2019 -	03/2019
113	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	-	07/2018 -	07/2018
114	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	26.40	03/2018 -	03/2018
115	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	5,427.00	09/2017 -	09/2017
116	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	174.00	09/2019 -	09/2019
117	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	2,978.86	1,706.73	02/2016 09/2019	09/2019

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04 -	187.04	-	06/2018 -	06/2018
119	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	133.60	06/2016 -	06/2016
120	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	38.50	10/2017 -	10/2017
121	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,381.71	1,005.51	07/2006 10/2016	10/2016
122	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	57.90	04/2017 -	04/2017
123	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	11,612.50	08/2013 12/2017	12/2017
124	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	2,310.58	1,801.75	05/2014 06/2016	06/2016
125	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	74.00	11/2017 -	11/2017
126	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	1,536.00	09/2019 -	09/2019
127	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,632.00	02/2019 -	02/2019
128	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
129	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
130	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
131	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	6,002.76	01/2018 -	01/2018
132	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	3,068.00	08/2018 -	08/2018
133	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
134	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
135	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	76.80	02/2017 -	02/2017
136	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	120.80	11/2016 -	11/2016
137	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	451.20	05/2018 -	05/2018

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204	10/2015	315.00 -	315.00	13.50	10/2016 -	10/2016
139	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII [N18000159	2/2014	908.08 -	908.08	249.80	06/2016 -	06/2016
140	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186	3/2015	550.06 -	550.06	23.80	03/2018 -	03/2018
141	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166	2/2014	378.71 -	378.71	125.80	10/2016 -	10/2016
142	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163	5/2014	303.07 -	303.07	25.10	07/2016 -	07/2016
143	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208	1/2016	1,455.47 -	1,455.47	-	07/2018 -	07/2018
144	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
	Total		155,434.84 -	172,370.93	67,773.22		
	<u>RAILWAYS</u>						
145	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR- BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
146	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
147	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019
148	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
149	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
150	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
151	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
	Total		8,820.53 -	17,767.82	2,626.23		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
152	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
153	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
154	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349	5/2015	1,387.11 -	1,387.11	114.38	11/2017 -	11/2017
155	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342	5/2015	709.00 -	709.00	19.24	09/2017 -	09/2017
156	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
157	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	40.75	02/2018 -	02/2018
158	SONAPUR TO GUWAHTI (AS-3) - [N24000044	12/2003	245.00 -	245.00	-	03/2008 07/2016	07/2016
159	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
160	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338	10/2014	206.12 -	206.12	112.00	04/2017 -	04/2017
161	GUWAHATI TO NALBARI (AS-5) - [N24000046	12/2003	198.16 -	198.16	242.40	04/2008 04/2016	04/2016
162	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72 -	264.72	98.18	04/2017 -	04/2017
163	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60 -	455.60	54.50	07/2017 -	07/2017
164	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263	2/2015	241.61 -	241.61	44.89	02/2017 -	02/2017
165	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	-	04/2010 09/2016	09/2016
166	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	200.96	01/2017 -	01/2017
167	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	957.02	07/2017 -	07/2017
168	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
169	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	785.00	08/2016 -	08/2016
170	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
171	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
172	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456	3/2013	959.25 -	959.25	1,194.67	06/2016 -	06/2016
173	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	234.21	08/2016 -	08/2016

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
174	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,288.44	11/2016 -	11/2016
175	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	55.00	04/2018 -	04/2018
176	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.75	05/2018 -	05/2018
177	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	-	06/2018 -	06/2018
178	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
179	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
180	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
181	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
182	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	12.80	02/2017 -	02/2017
183	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	225.02	-	12/2018 -	12/2018
184	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
185	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	282.41	-	08/2016 -	08/2016
186	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017
187	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
188	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
189	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	106.61	02/2018 -	02/2018
190	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	-	03/2018 -	03/2018

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
191	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
192	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
193	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	-	01/2019 -	01/2019
194	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
195	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
196	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
197	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
198	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
199	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
200	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
201	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241	12/2013	177.18 -	177.18	116.28	03/2016 -	03/2016
202	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017
203	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
204	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
205	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
206	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242	12/2013	158.65 -	158.65	103.55	03/2016 -	03/2016
207	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
208	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
209	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
210	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377	1/2014	397.04 -	397.04	-	10/2016 -	10/2016
211	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
212	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
213	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	-	06/2018 -	06/2018
214	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	282.41	31.64	03/2016 -	03/2016
215	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017
216	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	-	10/2016 -	10/2016
217	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	156.09	61.17	12/2016 -	12/2016
218	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	-	08/2017 -	08/2017
219	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245	1/2014	270.00 -	270.00	50.85	03/2016 -	03/2016
220	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
221	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
222	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
223	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
224	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	-	03/2017 -	03/2017

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
225	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
226	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
227	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
228	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399	10/2013	317.76 -	317.76	140.88	03/2017 -	03/2017
229	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
230	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	-	05/2018 -	05/2018
231	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
232	YAN TO NIRMAL SEREHAABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016
233	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
234	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
235	2-LANING WITH PAVED SHOULDER OF RAEARELI TO JAUNPUR - [N24000428	6/2014	569.38 -	569.38	737.51	06/2016 -	06/2016
236	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	849.40	04/2016 -	04/2016
237	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	1,200.90	01/2018 -	01/2018
238	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
239	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
240	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350	6/2015	563.92 -	563.92	11.37	12/2017 -	12/2017
241	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	-	05/2017 -	05/2017
242	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	-	03/2018 -	03/2018

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
243	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	38.08	02/2018 -	02/2018
244	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
245	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	-	05/2018 -	05/2018
247	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461	12/2012	438.75 -	438.75	-	09/2016 -	09/2016
248	FOUR LANING OF CHADIGARH - KHARAR - [N24000503	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
249	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
250	GUWHATI TO NALBARI (AS-4) - [N24000038	12/2003	175.96 -	175.96	-	04/2008 08/2016	08/2016
251	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240	3/2014	240.10 -	240.10	151.72	03/2016 -	03/2016
252	VADODARA-SURAT SECTION - [N24000361	3/2014	503.16 -	503.16	-	08/2016 -	08/2016
253	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
254	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26 -	269.26	-	10/2016 -	10/2016
256	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340	12/2014	451.58 -	451.58	28.00	06/2017 -	06/2017
257	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344	9/2014	425.19 -	425.19	217.87	09/2016 -	09/2016
258	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368	11/2014	563.92 -	563.92	103.08	11/2016 -	11/2016
259	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496	6/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016
260	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
261	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018
262	PADI - DAHOD - [N24000353	11/2014	279.14 -	279.14	62.77	05/2017 -	05/2017
263	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
264	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	114.87	09/2017 -	09/2017
265	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	31.17	05/2017 -	05/2017
266	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	295.20	04/2008 01/2017	01/2017
267	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
268	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	57.43	03/2018 -	03/2018
269	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
270	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	235.85	02/2018 -	02/2018
271	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
	Total		63,105.11 -	63,336.44	10,852.95		
	<u>SHIPPING AND PORTS</u>						
272	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]	12/2014	274.85 -	274.85	104.26	04/2017 -	04/2017
273	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	198.94	88.01	06/2017 -	06/2017
274	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	12.28	12/2017 -	12/2017
275	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
	Total		928.29 -	942.12	204.55		
	<u>STEEL</u>						
276	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
277	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	53.68	10/2017 -	10/2017
278	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]	8/2012	185.37 -	185.37	-	03/2016 -	03/2016
279	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 253.92	253.92	193.97	06/2016 -	06/2016

(March 2016)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
280	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	197.59	12/2016 -	12/2016
281	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
282	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]	4/2014	151.33 -	151.33	4.84	09/2017 -	09/2017
283	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]	2/2014	787.29 -	787.29	251.53	12/2016 -	12/2016
284	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	27.42	03/2018 -	03/2018
285	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	29.55	09/2016 -	09/2016
286	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	78.00	12/2017 -	12/2017
287	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	309.85	04/2018 -	04/2018
288	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
289	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	9,162.07	05/2015 12/2016	12/2016
	Total		23,515.20 -	23,539.59	10,528.56		
	<u>URBAN DEVELOPMENT</u>						
290	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	30.04	02/2019 -	02/2019
291	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	105.22	03/2018 -	03/2018
292	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	1,317.71	11/2019 -	11/2019
293	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	30.67	03/2017 -	03/2017
294	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	10.53	07/2017 -	07/2017
295	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	105.95	09/2016 01/2017	01/2017
	Total		41,058.91 -	41,058.91	1,600.12		
	Grand Total		418,245.01	448,489.70	131,737.78		

Annexure - XIII

List of ongoing projects having cost overrun w.r.t. to revised schedule

(March 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	RAMAGUNDAM OC-II EXTENSION - [N06000078	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
5	ADRIYALA SHAFT PROJECT - [N06000016	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
7	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,541.29 -	2,683.91			
	<u>HEAVY INDUSTRY</u>						
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
9	ASSAM GAS CRACKER PROJECT - [N16000106	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00			
	<u>PETROLEUM</u>						

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	450.55	03/2017 -	03/2018	27.79
11	MARKETING TOP AT KORBA - [N16000186	01/2011	141.86 -	232.00	09/2016 -	09/2016	63.54
12	GAMJI REDEVELOPMENT PROJECT - [N16000202	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
13	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72
15	CONSTRUCTION OF POL DEPOT AT IMPHAL, MANIPUR - [N16000215	08/2010	103.02 -	171.04	07/2016 -	07/2016	66.03
	Total		17,365.01 -	20,438.81			
	<u>POWER</u>						
16	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	18,063.89	09/2010 -	-	187.40
18	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63
19	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203	02/2015	302.49 302.00	302.49	02/2016 -	03/2016	0.00
20	BOKARO THERMAL POWER STATION-A - [N18000199	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	06/2016	83.21
21	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06
22	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92
	Total		21,645.83 -	48,554.18			
	<u>RAILWAYS</u>						
23	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
24	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
25	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
26	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
27	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
28	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
29	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
30	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
31	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
32	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
33	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
34	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
35	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	-	156.57
36	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
37	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
38	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
39	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
40	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
41	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
42	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
43	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
44	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	360.00	02/2006 -	-	37.56
45	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
46	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
48	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
49	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
50	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
51	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
52	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
53	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
54	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
55	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
56	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
57	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
58	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
59	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
60	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
61	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
62	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
63	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
64	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
65	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
66	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
67	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
68	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
69	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
70	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
71	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
72	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
73	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
74	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
75	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
76	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
77	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
78	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
79	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
80	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
81	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
82	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
83	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
84	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
85	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
86	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
87	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
88	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
89	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
90	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
91	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	-	367.76
92	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
93	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
94	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
95	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
96	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
97	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
98	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
99	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
100	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
101	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
102	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
103	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
104	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
105	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
106	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
107	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
108	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
109	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
110	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
111	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	154.46	03/2007 03/2007	-	-60.74
112	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
113	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
114	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
115	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) [N22000345]	04/1997	836.26 -	1,072.51	- -	-	28.25
116	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
117	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
118	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]	09/1995	100.00 -	980.00	- -	-	880.00
120	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
121	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
122	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
123	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
124	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	-	42.11
125	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
126	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
127	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
128	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
129	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
130	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
131	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
132	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
133	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
134	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
135	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
136	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
137	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
138	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
139	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
140	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
141	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
142	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
143	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
144	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
145	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
146	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
147	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
148	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
149	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
150	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
151	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
152	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
153	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
154	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
155	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
156	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
157	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
158	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
159	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
160	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
161	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
162	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
163	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
164	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
165	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
166	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
167	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
168	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
169	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
170	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
171	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
172	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
173	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
	Total		78,387.05 -	196,447.26			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
174	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	03/2016	28.93
175	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75
176	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68
177	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99
178	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50
179	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2016	30.10
180	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
181	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
182	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66
183	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24

(March 2016)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
184	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
185	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	0.00
186	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		3,710.66 -	5,884.15			
	<u>SHIPPING AND PORTS</u>						
187	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
188	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
189	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		856.56 -	1,337.62			
	<u>STEEL</u>						
190	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29
191	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
192	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50
	Total		1,261.61 -	1,735.31			
	<u>URBAN DEVELOPMENT</u>						
193	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
194	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073	06/2010	205.00 -	191.97	03/2012 -	03/2017	-6.36
	Total		6,600.00 -	11,800.97			
	Grand Total		155,427.22	331,057.61			

List of Delayed Projects w.r.t. Latest Schedule

(March 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,304.00	12/2008 10/2013	05/2016	89	31
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	8,066.00	12/2015 11/2016	11/2018	35	24
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,792.00	12/2016 03/2017	12/2019	36	33
	Total		36,950.00 -	46,241.00	35,162.00				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	424.30	01/2011 06/2016	09/2017	80	15
	Total		309.46 -	309.46	424.30				
	<u>COAL</u>								
5	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	2,023.54	03/2014 -	03/2016	24	-
6	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 741.62	741.62	511.06	03/2013 -	03/2016	36	-
7	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 -	1,228.39	872.21	03/2013 -	03/2016	36	-
8	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	83.51	03/2012 -	03/2016	48	-
9	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2016	60	-
10	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	-
11	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	197.05	10/2014 -	04/2016	18	-
12	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	06/2016	26	-
13	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	81.37	03/2014 -	09/2016	30	-
14	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	122.07	05/2014 -	10/2016	29	-
15	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	77.34	04/2014 -	11/2016	31	-
16	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	303.14	03/2010 -	03/2017	84	-
17	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	128.02	03/2011 -	03/2017	72	-
18	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	229.69	03/2013 -	03/2017	48	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	152.18	03/2010 -	03/2017	84	-
20	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51	-
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	207.71	03/2012 -	03/2017	60	-
22	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	185.35	03/2013 -	03/2017	48	-
23	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	86.48	03/2015 -	03/2017	24	-
24	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	95.17	03/2012 -	03/2017	60	-
25	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	151.89	03/2013 -	03/2017	48	-
26	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	71.83	03/2014 -	03/2017	36	-
27	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	-
28	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	119.06	03/2012 -	03/2018	72	-
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	211.06	03/2014 -	03/2018	48	-
30	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	8.03	03/2015 -	03/2018	36	-
31	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	-
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	77.44	03/2015 -	03/2018	36	-
33	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	102.72	03/2016 -	03/2018	24	-
34	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	486.27	93.51	03/2016 -	03/2018	24	-
35	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	225.81	03/2018 -	07/2018	4	-
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	27.85	07/2016 -	03/2019	32	-
37	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	-
38	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	-
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	-
40	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	79.49	07/2012 03/2017	03/2021	104	48
41	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-
42	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	475.38	03/2012 -	03/2023	132	-
	Total		15,131.83 -	16,226.19	7,477.14				
	STEEL								

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
43	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	1,070.97	1,070.97	02/2014 -	03/2016	25	-
44	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	325.00	263.57	12/2015 -	03/2016	3	-
45	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	175.60	10/2013 -	06/2016	32	-
46	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	486.38	07/2015 -	08/2016	13	-
47	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	363.11	04/2016 -	09/2016	5	-
48	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,905.05	03/2013 -	11/2016	44	-
49	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	115.64	05/2016 -	12/2016	7	-
50	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	61.26	04/2015 -	12/2016	20	-
51	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	261.96	07/2016 -	12/2016	5	-
52	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	177.06	12/2015 -	03/2017	15	-
53	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	-	03/2015 -	03/2017	24	-
54	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	289.28	07/2015 -	06/2017	23	-
55	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	45.93	10/2016 -	06/2017	8	-
56	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 207.00	206.71	125.65	12/2016 -	07/2017	7	-
	Total		23,570.46 -	24,075.51	19,341.46				
	<u>PETROLEUM</u>								
57	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	327.10	06/2011 03/2012	03/2016	57	48
58	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	190.86	12/2014 -	03/2016	15	-
59	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPR,L,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,105.78	10/2011 -	04/2016	54	-
60	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,L,KERALA	01/2006	993.00 1,693.00	1,693.00	1,459.15	01/2012 -	05/2016	52	-
61	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,387.48	09/2012 -	06/2016	45	-
62	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,355.41	08/2015 -	06/2016	10	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
63	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	440.18	08/2015 -	06/2016	10	-
64	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	76.60	02/2016 02/2016	07/2016	5	5
65	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	565.63	03/2015 -	08/2016	17	-
66	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	422.00	238.14	02/2016 -	10/2016	8	-
67	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,017.24	05/2013 04/2016	12/2016	43	8
68	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	112.86	05/2015 -	12/2016	19	-
69	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	185.40	11/2016 -	12/2016	1	-
70	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30	-
71	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,803.00	03/2013 03/2016	03/2017	48	12
72	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	523.10	08/2015 -	03/2017	19	-
73	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	77.90	07/2016 -	04/2017	9	-
74	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	35.76	11/2016 -	04/2017	5	-
75	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	06/2017	30	25
76	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	12.10	03/2017 03/2017	03/2018	12	12
77	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	-
78	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,381.47	12/2012 -	02/2019	74	-
	Total		18,266.42 -	20,096.64	12,810.32				
	POWER								
79	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,623.96	11/2013 -	03/2016	28	-
80	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,290.44	01/2013 -	03/2016	38	-
81	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.30	9,606.82	8,357.23	02/2011 -	03/2016	61	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
82	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	302.49	271.07	02/2016 -	03/2016	1	-
83	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	373.67	02/2012 -	04/2016	50	-
84	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	776.84	11/2012 -	04/2016	41	-
85	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 1,940.58	1,940.58	1,604.27	10/2014 03/2016	04/2016	18	1
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,471.42	04/2013 -	05/2016	37	-
87	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 390.51	390.51	246.70	01/2013 03/2016	05/2016	40	2
88	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,448.76	08/2014 -	05/2016	21	-
89	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	90.50	12/2015 -	05/2016	5	-
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	558.96	11/2011 -	06/2016	55	-
91	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,073.59	08/2012 -	06/2016	46	-
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	561.02	07/2013 11/2015	06/2016	35	7
93	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	554.11	11/2013 -	06/2016	31	-
94	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,474.62	01/2015 -	06/2016	17	-
95	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	104.63	09/2014 -	06/2016	21	-
96	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	5,922.99	06/2015 -	06/2016	12	-
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	606.22	11/2014 -	06/2016	19	-
98	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	3,186.31	10/2014 -	06/2016	20	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	348.02	05/2015 -	06/2016	13	-
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	484.19	03/2016 -	06/2016	3	-
101	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	864.80	05/2016 -	06/2016	1	-
102	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	8.90	03/2016 -	06/2016	3	-
103	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	28.80	02/2016 -	06/2016	4	-
104	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,453.39	12/2011 03/2016	06/2016	54	3
105	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART - C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	369.70	06/2015 -	08/2016	14	-
106	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,088.53	06/2015 -	08/2016	14	-
107	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	2,193.08	2,011.96	09/2009 -	09/2016	84	-
108	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,991.86	09/2014 -	09/2016	24	-
109	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	556.04	04/2016 -	09/2016	5	-
110	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,751.47	4,490.39	01/2016 -	11/2016	10	-
111	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	17.20	04/2016 -	11/2016	7	-
112	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,907.75	11/2008 01/2016	12/2016	97	11
113	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	602.69	09/2010 01/2016	12/2016	75	11
114	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,277.58	10/2012 -	12/2016	50	-
115	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	448.72	06/2014 03/2016	12/2016	30	9
116	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,350.13	07/2014 -	12/2016	29	-
117	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,501.63	08/2014 12/2015	12/2016	28	12

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
118	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	5,285.00	09/2016 -	12/2016	3	-
119	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,080.15	12/2015 -	12/2016	12	-
120	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,944.00	09/2011 -	03/2017	66	-
121	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,556.75	01/2015 -	03/2017	26	-
122	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	219.29	06/2012 -	03/2017	57	-
123	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,268.73	11/2012 03/2016	03/2017	52	12
124	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	312.57	08/2014 06/2015	03/2017	31	21
125	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	10,699.00	01/2017 -	03/2017	2	-
126	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	6,254.00	11/2016 -	08/2017	9	-
127	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,472.83	05/2014 -	09/2017	40	-
128	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,079.75	12/2016 -	09/2017	9	-
129	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	62.56	02/2014 -	02/2018	48	-
130	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.76	5,548.25	09/2009 -	12/2018	111	-
131	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,788.00	03/2013 -	06/2019	75	-
132	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	824.04	06/2013 -	12/2019	78	-
133	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	121.97	04/2020 -	03/2022	23	-
	Total		142,043.65 -	162,315.99	114,916.48				
	<u>HEAVY INDUSTRY</u>								
134	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	.00				
	<u>HEALTH AND FAMILY WELFARE</u>								
135	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	15	-
136	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	196.70	165.97	01/2016 -	04/2016	3	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
137	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	285.20	12/2015 -	06/2016	6	-
138	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	120.80	11/2013 -	06/2016	31	-
	Total		976.47 -	976.47	685.47				
	<u>RAILWAYS</u>								
139	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	-
140	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
141	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
142	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84	-
143	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
144	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108	-
145	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86	86
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	-
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91	91
148	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
149	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 2,434.00	2,434.00	419.45	03/2010 -	03/2017	84	-
150	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	-
151	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	66
152	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87	-
153	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181	-
154	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93	-
155	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21	-
156	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
157	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
158	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
160	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	-
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33	-
162	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
163	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,544.40	590.26	03/1998 -	12/2019	261	-
164	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
165	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
166	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
167	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57	-
	Total		30,564.20 -	79,472.86	35,693.17				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
168	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26	-
169	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7	-
170	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7	-
171	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7	-
172	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	03/2016	85	-
173	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	03/2016	83	-
174	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	03/2016	88	-
175	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2016	88	-
176	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	03/2016	83	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
177	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	-	06/2008 -	03/2016	93	-
178	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	-	06/2008 -	03/2016	93	-
179	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	03/2016	80	-
180	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	-	04/2013 -	03/2016	35	-
181	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2016	19	-
182	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31	-
183	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21	-
184	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	458.86	10/2014 -	03/2016	17	-
185	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	240.00	295.38	11/2008 -	03/2016	88	-
186	4 LANING OF GOMTI CHAURAH - UDAIPUR - [N24000455]DORTH,RAJASTHAN	03/2012	914.50 -	914.50	1,108.96	10/2015 -	03/2016	5	-
187	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	497.20	09/2008 -	04/2016	91	-
188	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	274.11	10/2008 -	04/2016	90	-
189	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	-	09/2010 -	04/2016	67	-
190	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,607.78	05/2012 -	04/2016	47	-
191	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	04/2016	35	-
192	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.67	08/2013 -	04/2016	32	-
193	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	04/2016	38	-
194	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	1,607.34	04/2015 -	04/2016	12	-
195	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12	-
196	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
197	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,310.32	09/2014 -	05/2016	20	-
198	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	117.97	12/2015 -	05/2016	5	-
199	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13	-
200	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	244.34	09/2008 -	06/2016	93	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
201	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	348.16	362.77	09/2007 -	06/2016	105	-
202	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	469.41	05/2010 -	06/2016	73	-
203	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	365.08	10/2011 -	06/2016	56	-
204	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	863.58	03/2013 -	06/2016	39	-
205	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,187.71	06/2013 -	06/2016	36	-
206	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
207	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2016	35	-
208	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,275.83	06/2013 -	06/2016	36	-
209	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	06/2016	31	-
210	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36	-
211	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	-	07/2013 -	06/2016	35	-
212	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	06/2016	29	-
213	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,620.63	05/2014 -	06/2016	25	-
214	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	06/2016	28	-
215	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	06/2016	27	-
216	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	545.27	11/2013 -	06/2016	31	-
217	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2016	24	-
218	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	2,388.00	2,490.61	06/2014 -	06/2016	24	-
219	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,071.52	03/2013 -	06/2016	39	-
220	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	06/2016	9	-
221	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,467.07	12/2015 -	06/2016	6	-
222	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21	-
223	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
224	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24	-
225	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,816.74	10/2011 -	06/2016	56	-
226	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	311.13	06/2008 06/2016	07/2016	97	1
227	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	-
228	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 07/2016	08/2016	99	1
229	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	1,708.35	05/2013 -	08/2016	39	-
230	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	1,876.89	08/2013 -	08/2016	36	-
231	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,328.50	02/2014 -	08/2016	30	-
232	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11	-
233	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	08/2016	50	-
234	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	-	05/2013 -	09/2016	40	-
235	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	09/2016	32	-
236	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	277.41	10/2013 -	09/2016	35	-
237	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	-
238	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	377.64	105.83	03/2014 -	09/2016	30	-
239	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25	-
240	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	160.49	01/2016 -	10/2016	9	-
241	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	239.48	01/2016 -	10/2016	9	-
242	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
243	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	39.53	11/2014 -	11/2016	24	-
244	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	12/2016	138	-
245	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	12/2016	111	-
246	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,708.29	11/2011 -	12/2016	61	-
247	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,036.26	07/2013 -	12/2016	41	-
248	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49	-
249	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39	-
250	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,788.25	03/2013 -	12/2016	45	-
251	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	880.29	02/2013 -	12/2016	46	-
252	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,326.02	12/2013 -	12/2016	36	-
253	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	494.33	04/2014 -	12/2016	32	-
254	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.61	07/2013 -	12/2016	41	-
255	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	-	01/2014 -	12/2016	35	-
256	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	533.13	09/2013 -	12/2016	39	-
257	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	343.75	04/2014 -	12/2016	32	-
258	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	229.16	06/2014 -	12/2016	30	-
259	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	177.61	10/2015 -	12/2016	14	-
260	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12	-
261	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	-
262	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	301.04	39.38	01/2016 -	12/2016	11	-
263	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	297.35	11/2016 -	12/2016	1	-
264	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	77.49	01/2016 -	01/2017	12	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
265	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	-
266	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	-
267	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	03/2017	56	-
268	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	-	08/2012 -	03/2017	55	-
269	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	282.68	08/2013 -	03/2017	43	-
270	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	1,287.95	715.50	11/2015 -	03/2017	16	-
271	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	574.74	03/2014 -	04/2017	37	-
272	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	168.31	02/2010 -	05/2017	87	-
273	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43 -	580.43	226.67	08/2013 -	05/2017	45	-
274	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	498.11	06/2015 -	05/2017	23	-
275	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
276	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,674.79	08/2013 -	07/2017	47	-
277	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	-
278	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	368.73	70.23	09/2016 -	09/2017	12	-
279	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
280	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24	-
281	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24	-
282	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	303.94	05/2013 -	12/2017	55	-
283	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	622.74	10/2013 -	12/2017	50	-
284	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	348.00	07/2014 -	12/2017	41	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
285	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
286	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31	-
287	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
288	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	-
	Total		86,961.48 -	88,695.46	66,295.79				
	<u>SHIPPING AND PORTS</u>								
289	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 600.00	600.00	525.49	03/2006 01/2016	07/2016	124	6
290	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88	77
	Total		395.67 -	1,009.83	891.69				
	<u>TELECOMMUNICATIONS</u>								
291	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	196.20	07/2015 -	03/2017	20	-
292	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30	-
	Total		15,445.17 -	15,345.17	1,556.20				
	<u>URBAN DEVELOPMENT</u>								
293	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 -	11,609.00	12,712.23	06/2011 -	06/2016	60	-
294	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16	-
295	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
296	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	143.72	06/2012 03/2016	05/2016	47	2
297	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	183.26	05/2013 10/2015	06/2016	37	8
298	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	12,472.32	12/2015 -	08/2016	8	-

(March 2016)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
299	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	315.00	188.33	06/2015 08/2016	11/2016	17	3
300	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	22,146.20	03/2016 -	12/2016	9	-
301	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	93.68	12/2014 12/2016	03/2017	27	3
302	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	191.97	-	03/2012 08/2016	03/2017	60	7
303	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	41.86	09/2015 07/2016	04/2017	19	9
304	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	16.16	03/2016 -	09/2017	18	-
	Total		61,780.80 -	66,981.77	48,055.45				
	Grand Total		434,113.61	525,573.65	343,309.47				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2019	12320	36
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2018	11459	35
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	05/2016	13171	89
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2019	417.33	32
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
9	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
10	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2018	162.76	36
11	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
12	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	06/2016	339.88	26
13	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
14	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
15	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
16	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
17	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
18	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
19	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2017	209.78	24
20	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
22	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	08/2019	1458.17	50
23	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	04/2016	364.75	18
24	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	36
25	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
26	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
27	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
28	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
29	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
30	JAGANNATHPOR OCP (3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
31	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
32	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
33	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
37	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
38	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
39	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
40	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
41	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
42	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	09/2016	153.82	30
43	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
45	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
46	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	LGBRIMH-TEZPUR, ASSAM	HSCC	07/2012	12/2014	03/2016	175.57	15
48	AIIMS-RAEBARELI-HOUSING	HSCC	10/2013	11/2013	06/2016	159.5	31
49	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	HSCC	09/2013	12/2015	06/2016	444.7	6

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	01/2017	150	30
52	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	HPCL	11/2011	03/2013	10/2016	310	43
53	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	17
54	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	29
55	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	03/2017	913	19
56	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
57	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
58	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	04/2017	202.25	9
59	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	05/2016	1138.5	13
60	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	10/2016	736.65	61
61	SECONDARY TANK FARM WITH DEHYDRATION	OIL	07/2011	03/2017	03/2018	352.56	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN						
62	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993	52
63	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
64	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
65	REPLACEMENT OF COKE CHAMBERS	IOCL	04/2013	02/2016	10/2016	480	8
66	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2016	191.96	19
67	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
68	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	06/2016	317.64	45
69	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
70	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2016	861.79	43
71	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	06/2016	1793	45
72	DE-BOTTLENECKING OF SMPL	IOCL	12/2009	08/2015	06/2016	1584	10
73	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
74	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	GAIL	06/2009	12/2012	02/2019	2915	74
75	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	11/2016	3110.36	12
76	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	06/2017	2059.63	27
77	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	03/2017	2592.17	34
78	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	06/2017	600.17	30
79	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
80	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	IOCL	08/2011	08/2015	06/2016	586	10
81	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	03/2016	279	15
82	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	04/2016	732	54

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
83	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
84	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
85	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	05/2016	2422.66	21
86	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	03/2017	297.33	31
87	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2016	1746.65	28
88	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
89	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	97
90	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
91	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	06/2016	1422.85	17
92	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
93	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	04/2016	1927.16	18
94	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
95	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	05/2016	250.03	40
96	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	03/2017	1272.8	52
97	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	03/2017	232.34	57
98	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48
99	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
100	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
101	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
102	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	06/2016	2313	54
103	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	03/2016	4122	61
104	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
105	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
106	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2016	477.69	75
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	PGCIL	02/2009	02/2012	04/2016	410.29	50
108	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2016	4824.12	50
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	05/2016	1677.57	37
110	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	04/2016	965.58	41
111	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	03/2016	1585.12	28
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	06/2016	509.66	55
113	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2017	4404.57	26
114	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
115	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	06/2016	1216.83	46
116	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	12/2016	2144	48
117	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	11/2016	374.63	7
118	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	75
119	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
120	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	03/2022	8112.12	23
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	06/2016	752.64	35
122	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	07/2016	2496.9	79
123	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	06/2016	558.26	31
124	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	09/2016	1940.13	24
125	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43
126	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2016	487.49	30
127	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	12/2016	2127.51	29
128	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	35

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
129	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	03/2016	552.44	25
130	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	25
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2016	723.63	19
132	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	06/2016	524.4	13
134	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2016	9569.76	12
135	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2016	3201.44	20
136	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
137	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	12/2016	2514.88	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
138	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
139	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
140	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
141	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	91
142	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87
143	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
144	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
145	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
146	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
147	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
148	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
149	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2017	2500	181
150	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
151	RAJATGARH-BARANG(LD),ECOR	RVNL	04/1999	02/2009	04/2016	166.16	86
152	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
153	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
154	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
155	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
156	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2016	495.44	144
157	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
158	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2018	733	111
159	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
160	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
162	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
163	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	12/2017	632.68	21
164	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
165	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
166	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
167	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	MORTH	10/2014	03/2014	09/2016	377.64	30
168	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	08/2016	1170.52	50
169	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	03/2016	1232	7
170	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
171	BEAWAR PALI PINDWARA	NHAI	12/2011	06/2014	06/2016	2388.51	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
172	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
173	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	06/2016	754	39
174	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2016	1078.84	36
175	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	07/2017	998.79	47
176	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
177	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
178	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	05/2016	1396.18	20
179	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2016	291.36	32
180	REHABILITATION AND UPGRADE OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	PWD	02/2014	07/2014	07/2016	258.99	24
181	REHABILITATION UPGRADE OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24
182	REHABILITATION AND UPGRADE OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	PWD	01/2014	11/2014	11/2016	195.45	24
183	REHABILITATION AND UPGRADE OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	PWD	02/2014	11/2014	11/2016	170.21	24
184	REHABILITATION AND UPGRADE OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
185	REHABILITATION AND UPGRADE OF NH-42 FROM KM 4 to 350 TO KM 75 TO 600 TO TWO LANE WITH PAVE SOLDOU	PWD	03/2015	09/2015	08/2017	309.01	23
186	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
187	REHABILITATION AND UPGRADE OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	PWD	02/2014	06/2014	06/2016	417.61	24
188	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
189	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
190	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70	PWD	02/2015	04/2015	05/2016	224.83	13
191	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	03/2016	164.54	7
192	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
193	SATANA-BELA SECTION OF NH-75(4L) IN MP	PWD	01/2012	08/2015	09/2016	320.48	13
194	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	08/2016	871.15	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
195	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	04/2016	381.86	12
196	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
197	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	03/2016	2498.76	19
198	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
199	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2016	2159	11
200	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	06/2016	1813.76	35
201	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2016	671.3	46
202	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	04/2016	351.54	35
203	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
204	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	03/2017	485	43
205	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2016	536	29
206	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	06/2016	664	28
207	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2016	575	41
208	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	06/2016	511.54	31
209	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	06/2016	1100.7	24
210	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
211	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	12/2016	624	32
212	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	05/2017	1479	23
213	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	06/2016	486	73
214	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	04/2016	795	47
215	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	12/2016	1108	61
216	DEOLI-KOTA	NHAI	01/2011	07/2013	12/2016	593	41
217	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	06/2016	828	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
218	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	03/2017	1287.95	16
219	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2016	1348.2	30
220	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2017	617	55
221	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
222	MURADABAD-BAREILY	NHAI	04/2010	06/2013	06/2016	1267	36
223	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2016	1724.55	45
224	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	09/2016	325	40
225	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	06/2016	852	39
226	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	08/2016	1585	39
227	4-LANING OF ROHATAK JIND(LENGTH 45 KM)	NHAI	10/2013	10/2015	12/2016	283.25	14
228	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	03/2016	1175	35
229	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	07/2012	03/2017	940	56
230	CHENNAI-TADA(SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
231	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	06/2016	1008.5	36
232	ROHTAK-BAWAL	NHAI	05/2011	11/2013	06/2016	650	31
233	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	04/2016	1141	32
234	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2016	1250	36
235	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	06/2016	953.88	35
236	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50
237	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
238	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2016	1535	25
239	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	06/2016	574	27
240	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	03/2016	835	26

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
241	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
242	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	03/2016	500.29	31
243	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	10/2016	1410	25
244	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
245	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	12/2017	356.4	41
246	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	03/2016	1232	7
247	ETAWAH CHAKERI	NHAI	03/2013	09/2015	06/2016	1573	9
248	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	06/2016	2125.24	6
249	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	04/2016	1928.22	12
250	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	DORTH	02/2008	10/2011	06/2016	1673.7	56
251	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	88
252	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	03/2016	200	83
253	AGRA-BYPASS(NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	06/2016	348.16	105
254	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	08/2016	160	99
255	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	08/2016	175.96	100
256	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	NHAI	12/2003	09/2008	04/2016	332.94	91
257	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	12/2016	212	111
258	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196	80
259	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	04/2016	232.45	67
260	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2016	230	138
261	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	03/2016	280	85
262	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	83
263	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	03/2016	167.64	88

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
264	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	06/2016	600	36
265	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	12/2003	06/2008	03/2016	237.8	93
266	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	12/2016	375.09	32
267	JAIPUR-REENGUS	NHAI	08/2010	02/2013	04/2016	267.81	38
268	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	09/2016	478.51	35
269	PANVEL-INDAPUR	NHAI	12/2011	06/2014	12/2016	942.69	30
270	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
271	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	10/2016	495.78	9
272	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	07/2016	245	100
273	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	09/2016	217.61	77
274	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	01/2017	208	105
275	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	07/2016	225	97
276	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	NHAI	12/2003	06/2008	03/2016	195	93
277	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	06/2016	155	93
278	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	04/2016	275	90
279	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
280	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	PWD	07/2015	12/2015	12/2016	333.21	12
281	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	12/2016	333.21	12
282	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	04/2016	198.16	96
283	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	NHAI	02/2011	11/2012	12/2016	193.45	49
284	2-LANING WITH PS SITARGANJ BAREILY SECTION	NHAI	06/2014	01/2016	12/2016	301.04	11
285	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	NHAI	09/2015	09/2016	09/2017	368.73	12
286	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	10/2016	351.34	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
287	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	01/2017	523.85	12
288	KOTWA TO DEWAPUR (LMNHP-10)	NHAI	11/2005	11/2008	03/2016	240	88

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
289	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	88
290	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	07/2016	150	124

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
291	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	06/2016	187.33	32
292	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	08/2016	877.73	13
293	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
294	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	12/2016	245.67	7
295	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCIL	10/2011	12/2016	07/2017	175.49	7
296	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCIL	05/2005	02/2014	03/2016	768.88	25
297	IRRIGATION WORK OF BAGMATI	HSCIL	10/2005	03/2015	03/2017	956	24
298	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	11/2016	17265	44
299	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	SAIL	04/2014	04/2015	12/2016	188.93	20
300	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	06/2017	404.16	23
301	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCIL	03/2007	12/2015	03/2017	149.73	15
302	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343	8

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
303	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2017	13334	20
304	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF	ITI	09/2014	09/2014	03/2017	2111.17	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	INTELLIGENT FIBER OPTIC C						

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
305	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
306	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2017	171.86	18
307	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	04/2017	156.57	19
308	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	03/2017	188.87	27
309	BANGALORE METRO RAIL PROJECT	MRTPT	05/2006	06/2011	06/2016	6395	60
310	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	05/2016	225.81	47
311	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	03/2016	270.83	16
312	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	06/2016	261.85	37
313	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
314	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	CPWD	12/2012	06/2015	11/2016	315	17
315	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	03/2017	205	60
316	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
8	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
9	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
14	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
17	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.76	4479.17
19	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	18063.89	11778.56
20	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
21	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
22	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	2193.08	1131.7
23	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
24	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1262.27	688.28
25	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
26	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
27	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
28	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9606.82	5484.82
29	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
30	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
31	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	250.03	390.51	140.48
32	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
33	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.57	586.56
34	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
35	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
37	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5751.47	2109.43
38	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	1961.87	2310.58	348.71
40	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
42	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
43	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
44	KARUR-SALEM(NL), SR	SR	02/1997	N.A.	155.55	800	644.45
45	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
46	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	844	601.58
47	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
48	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
49	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
50	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	270	177.37
51	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
52	JIND-SONEPAT (NL), NR	NR	01/2004	03/2012	238.56	740	501.44
53	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
54	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	921	2363	1442
55	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
56	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
57	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
58	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
59	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
60	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
62	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
63	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
64	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
65	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
66	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
67	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
68	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
69	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
70	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
71	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
72	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
73	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
74	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
75	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
76	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
77	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
78	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
79	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
80	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
81	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
82	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
83	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
85	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
86	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
87	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
88	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
89	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
90	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
91	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
92	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
93	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
94	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
95	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
96	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
97	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
98	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
99	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
100	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
101	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
102	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
103	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
104	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
105	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
106	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
108	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
109	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
110	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
111	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
112	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
113	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
114	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
115	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
116	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
117	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
118	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
119	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
120	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
121	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
122	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
123	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	WCR	04/1997	N.A.	836.26	1072.51	236.25
124	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	227	2135	1908
125	RANCHI-LOHARDAGA(GC), SER	SER	04/1997	06/2004	194.07	335	140.93
126	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
127	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
128	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
129	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	1566	1016

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87
131	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
132	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
133	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
134	MUNEERABAD-MAHABOONNAGAR (NL), SCR	SCR	04/1997	N.A.	218.24	645	426.76
135	NANDYAL-YERRAGUNTALA (NL), SCR	SCR	03/1996	02/2009	155.74	883	727.26
136	RAJATGARH-BARANG (LD), ECR	RVNL	04/1999	02/2009	166.16	325.5	159.34
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	2434	2109
138	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	847.75	222.45
139	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	20000	17500
140	NANGALDAM-TALWARA (NL), NR	NR	03/1981	07/2012	450	2100	1650
141	KANPUR KASGANJ MATHURA (GC) NER	NER	03/1997	N.A.	677.97	1651.54	973.57
142	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
143	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
144	KHURDA ROAD-BOLANGIR (NL) ECR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
145	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
146	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
147	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
148	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
149	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	3500	3252.34
150	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
151	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
152	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
154	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
155	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
156	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
157	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
158	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
159	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
160	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
161	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
162	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
163	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
164	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	12/2007	136.62	360	223.38
165	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	318.33	184.92
166	VIRAMGAM-BHILDI(WR), GC	WR	04/1990	N.A.	155.66	548.01	392.35
167	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
168	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
169	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
170	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
171	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
172	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
173	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
174	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
175	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
176	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
177	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
178	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
179	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
180	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
181	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
182	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1070.97	302.09
183	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
184	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	05/2016	1,3171.00	2,2462.00	9291	89
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	1228.39	1016.05	36
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	1200.00	328.65	17
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	04/2016	732.00	1227.00	495	54
8	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	462.79	152.98	29
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993.00	1693.00	700	52
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
11	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2016	861.79	1256.72	394.93	43
12	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	06/2017	2059.63	2665.65	606.02	27

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
14	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2016	1746.65	2228.71	482.06	28
15	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2016	487.49	639.46	151.97	30
16	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	3846.30	867.82	75
17	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
18	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	05/2016	250.03	390.51	140.48	40
19	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	03/2017	1272.80	1731.10	458.3	52
20	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	06/2016	2313.00	4237.67	1924.67	54
21	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	03/2016	4122.00	9606.82	5484.82	61
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	07/2016	2496.90	6179.96	3683.06	79
23	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
24	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.76	4479.17	111
25	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	2193.08	1131.7	84
26	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2016	477.69	738.48	260.79	75
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
28	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	12/2016	2144.00	2932.88	788.88	48
29	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	2310.58	348.71	25
30	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	1262.27	688.28	35

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5751.47	2109.43	10
32	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88
33	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	2187.32	408.03	97

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
34	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	MRTP	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
35	RAJATGARH-BARANG(LD), ECOR	RVNL	04/1999	02/2009	04/2016	166.16	325.50	159.34	86
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2017	2500.00	2,0000.00	17500	181
37	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
38	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	318.33	184.92	91
40	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
41	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
42	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
43	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
44	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
45	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
46	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
48	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
49	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
50	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
51	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
52	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
53	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	2434.00	2109	84
54	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
55	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
56	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
57	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196.00	331.23	135.23	80
58	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	385.13	185.32	83
59	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	12/2016	1108.00	2288.00	1180	61
60	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	280.13	125.09	88

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
61	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT	RVNL	03/2007	04/2009	08/2016	245.67	409.83	164.16	88

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	TRUST								
62	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	07/2016	150.00	600.00	450	124

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
63	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343.00	488.40	145.4	8
64	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	03/2016	768.88	1070.97	302.09	25

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
65	BANGALORE METRO RAIL PROJECT	MRTP	05/2006	06/2011	06/2016	6395.00	1,1609.00	5214	60

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure-XVIII

Details of 20 Railways Projects [as identified by Ministry of Railways vide letter
no. 2011/w-1 /Genl / MoSPI dated 28/10/2015] to be monitored at MoSPI level

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>RAILWAYS</u>					
1	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 - 5,500.00	03/2009 -	03/2016	0/0
2	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 - 1,242.25	03/2007 -	03/2016	0/0
3	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 2,434.00 2,434.00	03/2010 -	03/2017	0/0
4	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 - 4,996.19	04/2008 12/2011	06/2017	0/0
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 - 20,000.00	11/2002 -	12/2017	0/0
6	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36 1,651.54	- - -	03/2018	0/0
7	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 - 1,143.60	- - -	03/2018	0/0
8	GONDIA-JABALPUR(GC), (SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 - 1,544.40	03/1998 -	12/2019	0/0
9	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 - 2,957.21	07/2005 -	-	0/0
10	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 3,500.00 3,500.00	05/2008 -	-	0/0
11	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 - 1,185.64	- 09/2009	-	0/0
12	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 - 2,363.00	03/2009 -	-	0/0
13	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 - 2,921.00	10/2007 -	-	0/0
14	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 - 1,202.70	02/2015 -	-	0/0

			(March 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 - 1,266.89	- -	-	0/0
16	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 - 1,280.83	- -	-	0/0
17	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 2,200.00 2,200.00	- -	-	0/0
18	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 - 2,127.00	- -	-	0/0
19	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 - 1,111.99	- -	-	0/0
20	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR,UTTAR PRADESH	04/1997	836.26 - 1,072.51	- -	-	0/0
	Total		20,808.52 -			0/0
	Grand Total		20,808.52			0/0

Details of Ongoing Projects Under -Public Private Partnership Mode

(March 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
1	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT PPP (ANNUITY) - [N10000009]	12/2015	344.50 -	344.50	11/2016 -	11/2016	0.00	0
	Total		344.50 -	344.50				
	<u>RAILWAYS</u>							
2	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) PPP (BOT) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06	0
3	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM) - PPP (BOT) - [N22000313]	03/2012	1,503.71 -	1,503.71	- -	03/2020	0.00	0
	Total		2,156.90 -	2,157.26				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
4	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - PPP (BOT) - [N24000231]	10/2013	283.25 -	283.25	10/2015 -	12/2016	0.00	14
5	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	09/2016	0.00	32
6	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	09/2016	0.00	40
7	REENGUS SIKAR - PPP (ANNUITY) - [N24000227]	03/2012	333.51 -	333.51	09/2014 -	02/2016	0.00	17
8	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	04/2016	0.00	35
9	CHENNAI-TADA(SIX LANE) - PPP (BOT) - [N24000129]	04/2009	353.37 -	353.37	10/2011 -	06/2016	0.00	56
10	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - PPP (BOT) - [N24000211]	07/2012	356.40 -	356.40	07/2014 -	12/2017	0.00	41
11	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - PPP (BOT) - [N24000153]	03/2011	359.00 -	359.00	09/2013 -	12/2016	0.00	39
12	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2017	0.00	55
13	NAGPUR-WAINGANGA BRIDGE - PPP (BOT) - [N24000210]	04/2012	484.19 -	484.19	10/2014 -	03/2016	0.00	17

(March 2016)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
14	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177	09/2011	485.00 -	485.00	08/2013 -	03/2017	0.00	43
15	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122	04/2007	486.00 -	486.00	05/2010 -	06/2016	0.00	73
16	BHUBANESWAR TO PURI - PPP (BOT) - [N24000195	03/2011	500.29 -	500.29	08/2013 -	03/2016	0.00	31
17	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188	05/2011	511.54 -	511.54	11/2013 -	06/2016	0.00	31
18	TRICHY - KARUR - PPP (BOT) - [N24000528	03/2007	516.00 -	516.00	07/2008 -	-	0.00	0
19	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426	11/2012	530.07 -	530.07	08/2016 -	08/2016	0.00	0
20	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - PPP (BOT) - [N24000171	06/2011	535.00 -	535.00	12/2013 -	01/2016	0.00	25
21	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180	01/2011	536.00 -	536.00	01/2014 -	06/2016	0.00	29
22	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140	11/2009	567.00 -	567.00	11/2013 -	-	0.00	0
23	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - PPP (ANNUITY) - [N24000428	06/2014	569.38 -	569.38	06/2016 -	06/2016	0.00	0
24	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178	04/2011	571.00 -	571.00	10/2013 -	12/2017	0.00	50
25	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185	09/2011	574.00 -	574.00	03/2014 -	06/2016	0.00	27
26	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187	01/2011	575.00 -	575.00	07/2013 -	12/2016	0.00	41
27	4-LANING OF RAIGANJ-DALKOLA - PPP (BOT) - [N24000204	02/2011	580.43 -	580.43	08/2013 -	05/2017	0.00	45
28	NIROLI-ROXY-RAJAMUNDA - PPP (BOT) - [N24000194	07/2011	586.00 -	586.00	01/2014 -	12/2016	0.00	35
29	DEOLI-KOTA - PPP (BOT) - [N24000148	01/2011	593.00 -	593.00	07/2013 -	12/2016	0.00	41
30	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089	12/2003	604.00 -	604.00	12/2009 -	-	0.00	0
31	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149	02/2010	617.00 -	617.00	08/2012 -	03/2017	0.00	55
32	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213	04/2012	624.00 -	624.00	04/2014 -	12/2016	0.00	32
33	ROHTAK-BAWAL - PPP (BOT) - [N24000169	05/2011	650.00 -	650.00	11/2013 -	06/2016	0.00	31
34	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184	05/2011	664.00 -	664.00	02/2014 -	06/2016	0.00	28
35	KUNDUPUR-SURATHKAL AND MANGLORE - PPP (BOT) - [N24000146	09/2010	671.00 -	671.00	-	09/2017	0.00	0

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
36	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	12/2016	0.00	46
37	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - PPP (BOT) - [N24000236]	10/2013	677.79 -	677.79	04/2016 -	04/2016	0.00	0
38	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	02/2017	0.00	31
39	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	06/2016	0.00	39
40	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - PPP (BOT) - [N24000168]	03/2011	785.50 -	785.50	08/2013 -	-	0.00	0
41	JAIPUR-TONK-DEOLI - PPP (BOT) - [N24000135]	06/2010	792.06 -	792.06	12/2012 -	-	0.00	0
42	KISHANGARH-AJMER-BEAWER - PPP (BOT) - [N24000128]	11/2009	795.00 -	795.00	05/2012 -	04/2016	0.00	47
43	SAMAIKHALI - GANDHIDHAM - PPP (BOT) - [N24000179]	09/2010	805.39 -	805.39	03/2013 -	01/2016	0.00	34
44	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	04/2018	0.00	0
45	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - PPP (BOT) - [N24000225]	03/2012	828.00 -	828.00	09/2014 -	06/2016	0.00	21
46	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - PPP (BOT) - [N24000464]	03/2015	830.36 -	830.36	01/2016 -	-	0.00	0
47	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH- 3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - PPP (BOT) - [N24000497]	03/2015	830.36 -	830.36	01/2019 -	-	0.00	0
48	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36 -	830.36	07/2018 -	07/2018	0.00	0
49	PUNE-SHOLAPUR,PKG-II - PPP (BOT) - [N24000193]	09/2011	835.00 -	835.00	01/2014 -	-	0.00	26
50	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM - PPP (BOT) - [N24000144]	09/2010	852.00 -	852.00	03/2013 -	06/2016	0.00	39
51	BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229]	08/2012	867.00 -	867.00	02/2015 -	12/2017	0.00	34
52	4 LANING OF OBEDULLAGANJ-BETUL SECTION - PPP (BOT) - [N24000457]	02/2012	912.00 -	912.00	08/2016 -	08/2016	0.00	0
53	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	12/2016	0.00	1
54	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE- III) - PPP (BOT) - [N24000123]	03/2005	940.00 -	940.00	07/2012 -	03/2017	0.00	56
55	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	06/2016	0.00	35
56	4-LANING OF ROHTAK - HISSAR SECTION - PPP (BOT) - [N24000456]	03/2013	959.25 -	959.25	06/2016 -	06/2016	0.00	0

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
57	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453	01/2015	972.50 -	972.50	07/2017 -	07/2017	0.00	0
58	4-LANING OF BRAHAMPORE-FARAKA - PPP (BOT) - [N24000203	02/2011	998.79 -	998.79	08/2013 -	07/2017	0.00	47
59	4 LANNING OF AHMEDABAD TO GODHARA - PPP (BOT) - [N24000167	12/2010	1,008.50 -	1,008.50	06/2013 -	06/2016	0.00	36
60	4 LANING OF GUNA TO BIAORA - PPP (BOT) - [N24000458	06/2015	1,012.90 -	1,012.90	-	-	0.00	0
61	BAREILY-SITAPUR (NH-24) - PPP (BOT) - [N24000200	03/2011	1,046.00 -	1,046.00	09/2013 -	12/2016	0.00	39
62	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2016	0.00	21
63	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494	05/2013	1,055.00 -	1,055.00	11/2015 -	01/2016	0.00	2
64	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202	02/2011	1,078.84 -	1,078.84	08/2013 -	08/2016	0.00	36
65	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189	06/2011	1,100.70 -	1,100.70	06/2014 -	06/2016	0.00	24
66	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50	61
67	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170	02/2011	1,141.00 -	1,141.00	08/2013 -	04/2016	0.00	32
68	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136	10/2010	1,175.00 -	1,175.00	04/2013 -	03/2016	0.00	35
69	FOUR LANING OF ORISSA CHATTISHGARH BORDER - PPP (BOT) - [N24000218	02/2013	1,232.00 -	1,232.00	08/2015 -	-	0.00	7
70	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2016	0.00	36
71	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233	04/2014	1,266.60 -	1,266.60	09/2016 -	09/2016	0.00	0
72	MURADABAD-BAREILY - PPP (BOT) - [N24000154	04/2010	1,267.00 -	1,267.00	06/2013 -	06/2016	0.00	36
73	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - PPP (BOT) - [N24000228	06/2013	1,287.95 -	1,287.95	11/2015 -	03/2017	0.00	16
74	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230	05/2013	1,348.20 -	1,348.20	02/2014 -	08/2016	0.00	30
75	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490	01/1991	1,388.00 -	1,388.00	-	08/2018	0.00	0
76	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487	07/2015	1,393.00 -	1,393.00	-	01/2018	0.00	0
77	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206	04/2012	1,396.18 -	1,396.18	09/2014 -	05/2016	0.00	20
78	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197	03/2012	1,410.00 -	1,410.00	09/2014 -	10/2016	0.00	25
79	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215	12/2012	1,479.00 -	1,479.00	06/2015 -	05/2017	0.00	23

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
80	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125	03/2010	1,509.10 -	1,509.10	09/2012 -	02/2016	0.00	41
81	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183	11/2011	1,535.00 -	1,535.00	05/2014 -	06/2016	0.00	25
82	ETAWAH CHAKERI - PPP (BOT) - [N24000219	03/2013	1,573.00 -	1,573.00	09/2015 -	06/2016	0.00	9
83	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505	06/2015	1,583.79 -	1,583.79	- -	-	0.00	0
84	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145	11/2010	1,585.00 -	1,585.00	05/2013 -	08/2016	0.00	39
85	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - PPP (BOT) - [N24000139	09/2010	1,655.00 -	1,655.00	09/2013 -	-	0.00	0
86	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462	05/2014	1,655.01 -	1,655.01	08/2016 -	08/2016	0.00	0
87	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452	07/2015	1,657.20 -	1,657.20	- -	-	0.00	0
88	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515	04/2014	1,665.00 -	1,665.00	- -	-	0.00	0
89	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477	02/2008	1,673.70 -	1,673.70	10/2011 -	06/2016	0.00	56
90	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131	02/2009	1,693.75 -	1,693.75	08/2011 -	-	0.00	0
91	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156	10/2010	1,724.55 -	1,724.55	03/2013 -	12/2016	0.00	45
92	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163	07/2010	1,813.76 -	1,813.76	07/2013 -	06/2016	0.00	35
93	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508	07/2015	1,871.34 -	1,871.34	01/2018 -	01/2018	0.00	0
94	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232	11/2013	1,916.79 -	1,916.79	11/2016 -	11/2016	0.00	0
95	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224	10/2012	1,928.22 -	1,928.22	04/2015 -	04/2016	0.00	12
96	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161	07/2010	1,987.00 -	1,987.00	07/2015 -	06/2016	0.00	11
97	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222	01/2013	2,125.24 -	2,125.24	12/2015 -	06/2016	0.00	6
98	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449	07/2015	2,128.72 -	2,128.72	- -	-	0.00	0
99	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162	05/2011	2,159.00 -	2,159.00	06/2015 -	05/2016	0.00	11
100	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425	07/2015	2,288.18 -	2,288.18	- -	-	0.00	0
101	BEAWAR PALI PINDWARA - PPP (BOT) - [N24000199	12/2011	2,388.51 -	2,388.00	06/2014 -	06/2016	-0.02	24

(March 2016)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
102	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155	02/2011	2,498.76 -	2,498.76	08/2014 -	03/2016	0.00	19
103	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182	09/2011	2,848.00 -	2,848.00	03/2014 -	04/2017	0.00	37
	Total		106,350.46 -	107,529.95				
	<u>SHIPPING AND PORTS</u>							
104	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065	10/2013	198.94 -	198.94	06/2017 -	06/2017	0.00	0
105	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66	0
106	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72	61
	Total		809.83 -	1,126.73				
	Grand Total		109,661.69	111,158.44				
