

**425th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
March, 2021**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division**

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for March 2021 contains information on the status of the 1737 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, 1737 projects, 3 projects are added. 557 projects are delayed with respect to their original schedules and 99 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these projects, 35 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report	Additional delayed Mega Projects
1	ROAD TRANSPORT AND HIGHWAYS	908	135	25	3
2	RAILWAYS	312	155	6	5
3	PETROLEUM	139	76	18	7
4	COAL	101	50	5	0
5	POWER	78	45	25	16
6	WATER RESOURCES	49	20	2	0
7	URBAN DEVELOPMENT	33	10	3	2
8	HEALTH AND FAMILY WELFARE	29	13	4	0
9	EDUCATION	26	14	0	0
10	CIVIL AVIATION	19	11	1	0
11	STEEL	9	5	1	1
12	MINES	5	2	1	0
13	HOME AFFAIRS	5	2	0	0
14	ATOMIC ENERGY	4	4	0	0
15	FERTILISERS	4	4	4	0
16	RURAL DEVELOPMENT	4	3	3	0
17	TELECOMMUNICATIONS	3	3	0	0
18	FINANCE	2	1	0	0
19	DPIIT	2	2	1	1
20	HEAVY INDUSTRY	1	0	0	0
21	SHIPPING AND PORTS	1	0	0	0
22	DEFENCE PRODUCTION	1	1	0	0
23	COMMERCE	1	0	0	0
24	CULTURE DEVELOPMENT	1	1	0	0
Total		1737	557	99	35

3. Total original cost of implementation of the 1737 projects was ₹22,33,409.53 crore and their anticipated completion cost is likely to be ₹26,69,649.35 crore, which reflects overall cost overruns of ₹4,36,239.82 crore (19.53 % of original cost). The expenditure incurred on these projects till March 2021 is ₹13,06,617.54 crore, which is 48.94% of the anticipated cost of the projects. The information can be viewed graphically as:

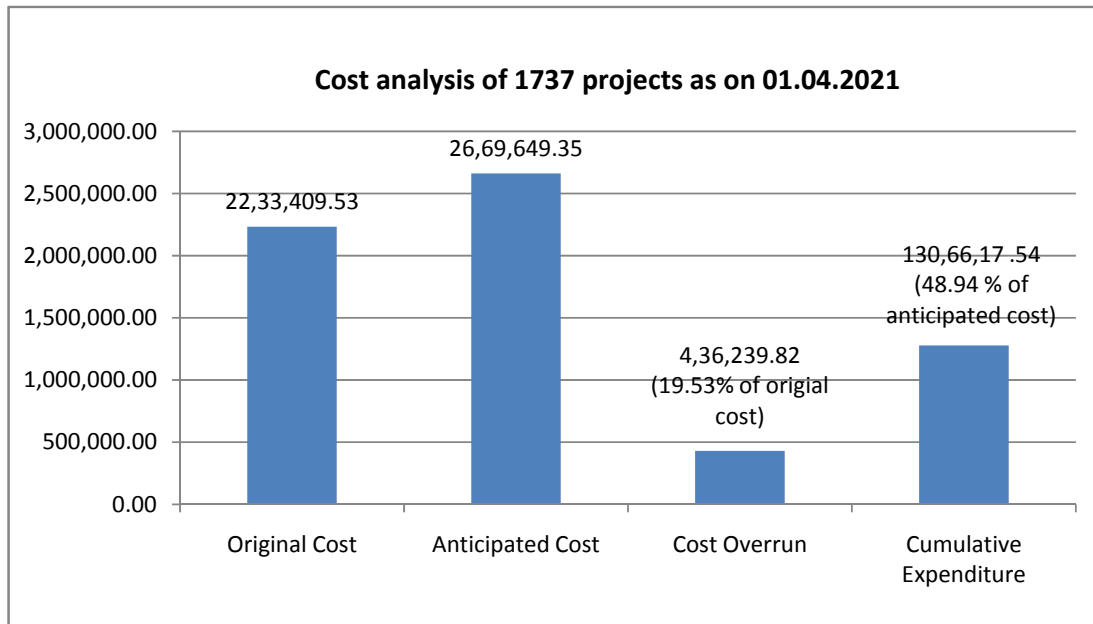


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.

5. Out of the 1737 projects, 13 projects are ahead of schedule, 229 are on schedule, 557 are delayed, 462 projects reported cost overrun and 136 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 412 if delay is calculated on the basis of latest schedule of completion. Further, for 938 projects neither the year of commissioning nor the tentative gestation period has been reported.


Status of projects (as on 01.04.2021)

(All the figures corresponds to number of project)

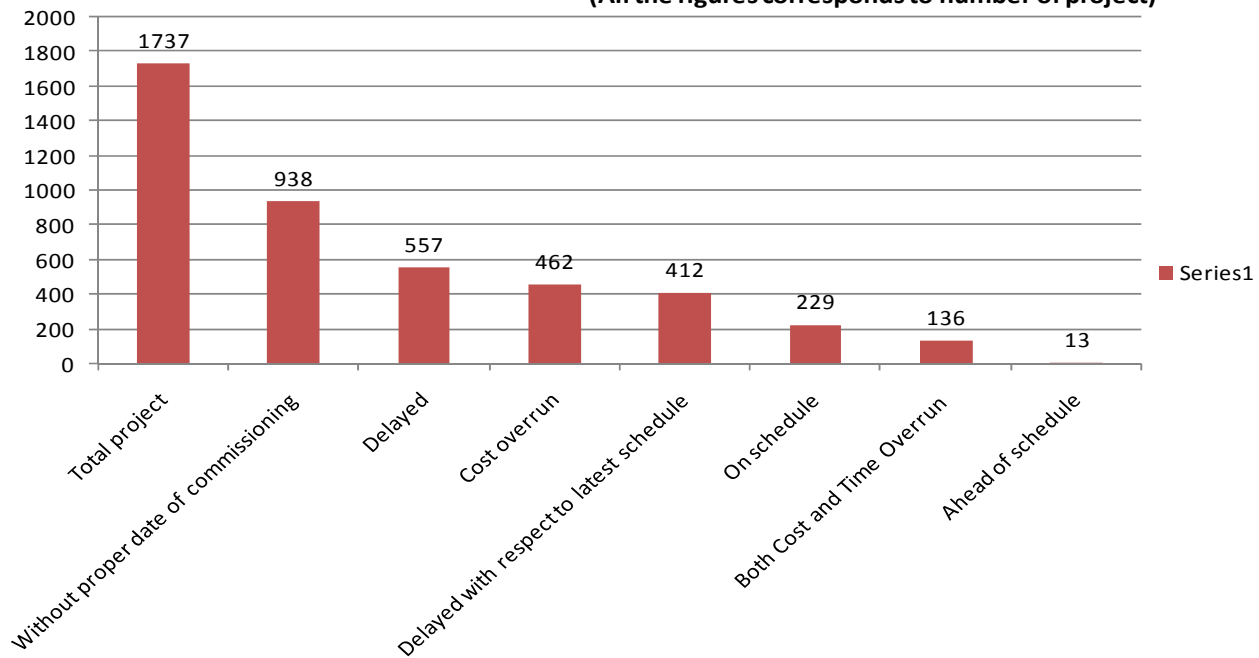


6. Out of 557 delayed projects, 114 (18.99%) projects have overall delay in the range of 1 to 12 months, 131 (23.48%) projects have delay in the range of 13 to 24 months, 190 (33.51%) projects have delay in the range of 25 to 60 months and 122 (20.61%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

Break-up of 557 Delayed projects in March 2021

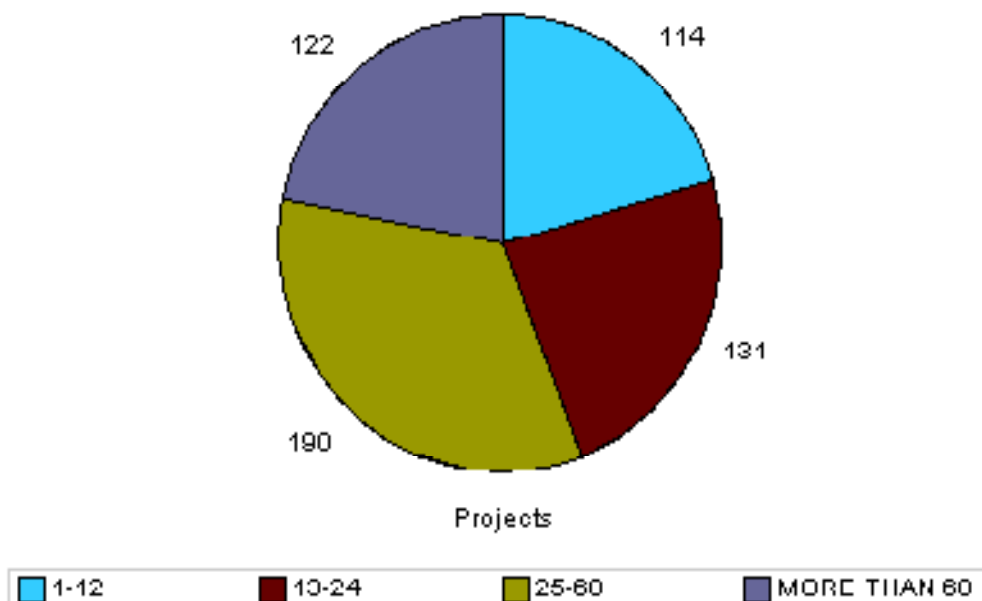

7. The status of online reporting of projects can be viewed month wise as:

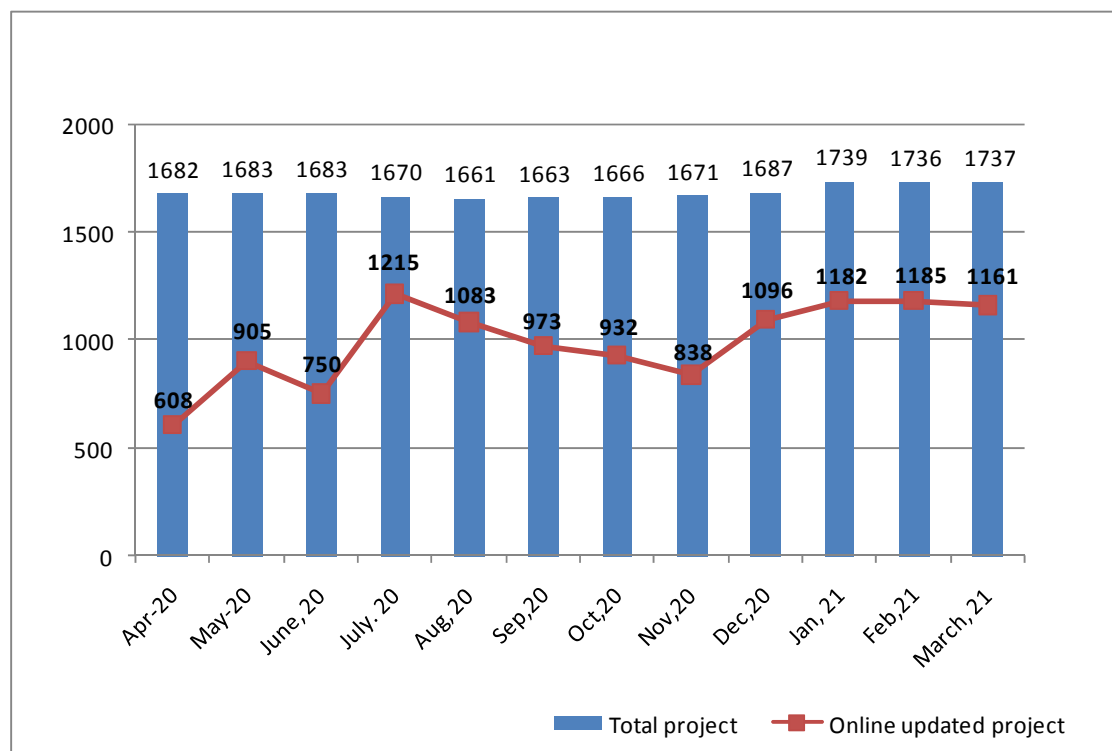

The average time overrun in these 557 delayed projects is 44.69 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-04-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	5.78
COAL					
7	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
8	BHANEAGAON OC	02/2015	187.94	409.68	117.98
9	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
10	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35

11	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	325.18	63.67
	DPIIT				
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
	HEALTH AND FAMILY WELFARE				
14	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
15	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	190.34	21.58
16	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	20.55
17	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
18	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
	HOME AFFAIRS				
19	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
20	NSG AT KOLKATA	10/2014	162.88	238.00	46.12
	HUMAN RESOURCE DEVELOPMENT				
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
22	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	350.69	19.28
23	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	10.22
24	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	1.85
25	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
	PETROLEUM				
26	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
27	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1846.46	114.26
28	LPG TERMINAL AT KOCHI	10/2015	607.06	1236.00	103.60
29	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
30	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
	POWER				
31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
33	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52
34	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
35	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	97.38
	RAILWAYS				
36	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
37	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	2172.16	1699.64
38	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
39	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
40	RAMGANJMUNDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
	ROAD TRANSPORT AND HIGHWAYS				
41	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
42	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
43	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
44	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95
45	4 LANING FROM PHAGWARA TO RUPNAGAR 6	08/2016	1169.61	2280.00	94.94

	RURAL DEVELOPMENT				
46	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	3.96
47	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	2.23
	STEEL				
48	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	41.32
	TELECOMMUNICATIONS				
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
	URBAN DEVELOPMENT				
50	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
51	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	44.39
52	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
53	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
54	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	18.69
	WATER RESOURCES				
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
56	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	22.24
57	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	17.91
58	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	370.40	430.49	16.22
59	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	05/2018	198.43	224.69	13.23

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-04-2021)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
	ATOMIC ENERGY				
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
	CIVIL AVIATION				
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	441.33	24.10
	COAL				
7	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
9	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
10	BHANEAGAON OC	02/2015	187.94	409.68	221.74

11	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
	DPIIT				
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
	HEALTH AND FAMILY WELFARE				
14	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00
15	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
16	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	85.12
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
18	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	45.56
	HOME AFFAIRS				
19	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
20	NSG AT KOLKATA	10/2014	162.88	238.00	75.12
	HUMAN RESOURCE DEVELOPMENT				
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
22	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	350.69	56.69
23	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	19.00
24	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	10.16
25	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
	PETROLEUM				
26	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
27	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00
28	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
29	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
30	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
	POWER				
31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
32	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
33	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
35	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	5213.00
	RAILWAYS				
36	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
37	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
38	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
39	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
40	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12264.15	7809.98
	ROAD TRANSPORT AND HIGHWAYS				
41	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
42	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51

43	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2587.50	1199.16
44	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
45	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
RURAL DEVELOPMENT					
46	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	5.93
47	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	4.51
STEEL					
48	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	6415.00
TELECOMMUNICATIONS					
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
URBAN DEVELOPMENT					
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	10270.00
51	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
52	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	4289.98
53	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
54	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
WATER RESOURCES					
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
56	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	370.40	430.49	60.09
57	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	50.14
58	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	47.50
59	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	05/2018	198.43	224.69	26.26

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-04-2021)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	03/2023	75
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	02/2022	74
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2021	33
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	01/2016	03/2020	12/2021	21
7	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	06/2021	16

8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	05/2021	13
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	03/2021	03/2022	12
	COAL				
10	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	03/2010	03/2029	228
11	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	03/2013	03/2028	180
12	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	03/2017	03/2031	168
13	MAGADH EXPANSION OC(51 MTY)	08/2008	07/2012	03/2025	152
14	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2022	132
	DEFENCE PRODUCTION				
15	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	04/2014	09/2017	03/2021	42
16	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	02/2020	06/2021	16
	DPIIT				
17	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	12/2021	24
18	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	07/2021	22
	FERTILISERS				
19	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	04/2021	17
20	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	04/2021	17
21	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	04/2021	17
22	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	05/2021	13
	FINANCE				
23	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	04/2021	18
	HEALTH AND FAMILY WELFARE				
24	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	05/2021	90
25	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	03/2021	46
26	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	12/2021	43
27	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	03/2021	37
28	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	03/2019	06/2021	27
	HOME AFFAIRS				
29	NSG AT KOLKATA	10/2014	04/2018	12/2021	44
30	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	12/2021	26
	HUMAN RESOURCE DEVELOPMENT				
31	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	06/2021	63
32	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	10/2021	52
33	PERMANENT CAMPUS FOR IIM BODH GAYA	09/2018	09/2020	11/2022	26
34	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	04/2019	04/2021	24

35	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	01/2018	05/2020	02/2022	21
	MINES				
36	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	04/2021	03/2023	23
37	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	12/2022	20
	PETROLEUM				
38	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
39	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	03/2021	94
40	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
41	LPG TERMINAL AT KOCHI	10/2015	10/2017	03/2022	53
42	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	03/2017	03/2021	48
	POWER				
43	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
44	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	07/2022	154
45	BARH STPP(3X660MW) NTPC	02/2005	10/2011	07/2023	141
46	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2023	126
47	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	03/2013	12/2022	117
	RAILWAYS				
48	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
49	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
50	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
51	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2022	241
52	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
	ROAD TRANSPORT AND HIGHWAYS				
53	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	06/2021	128
54	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	10/2010	06/2021	128
55	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
56	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	03/2022	103
57	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	05/2010	05/2013	08/2021	99
	RURAL DEVELOPMENT				
58	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	10/2021	70
59	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016	12/2021	60
60	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	10/2021	58
	STEEL				
61	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2021	74
62	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	12/2021	50
63	FORGED WHEEL PLANT	04/2014	09/2018	04/2021	31
64	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	06/2019	05/2021	23
65	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	09/2020	05/2021	8
	TELECOMMUNICATIONS				

66	NETWORK FOR SPECTRUM	03/2012	07/2015	06/2021	71
67	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	03/2018	06/2021	39
68	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	11/2021	5
URBAN DEVELOPMENT					
69	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	03/2023	98
70	DELHI MRTS PHASE-III	09/2011	03/2016	09/2021	66
71	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2019	06/2024	64
72	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	08/2022	44
73	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	07/2021	12/2024	41
WATER RESOURCES					
74	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
75	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	04/2022	25
76	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	12/2021	24
77	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	05/2021	17
78	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	02/2017	11/2019	03/2021	16

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-04-2021)**

SN	PROJECTS	DATE OF APPR OVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	438.28	438.28	335.58	06/2019	N.A.
2	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB I AIRPORT KOLKATA	01/2016	458.00	458.00	135.60	03/2020	12/2021
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	303.80	303.80	115.88	04/2020	05/2021
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	323.90	03/2021	03/2022
5	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	01/2018	1405.00	1405.00	199.55	08/2022	08/2022
COAL							

6	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	86.85	09/2020	N.A.
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
8	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	140.80	09/2020	N.A.
9	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
10	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	18.35	04/2018	06/2022
COMMERCE							
11	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	60.00	10/2020	N.A.
DPIIT							
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	8715.07	09/2019	07/2021
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	2432.15	12/2019	12/2021
HEALTH AND FAMILY WELFARE							
14	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
15	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	488.22	11/2013	05/2021
16	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	469.13	06/2020	07/2021
17	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	548.39	04/2020	07/2021
18	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
HEAVY INDUSTRY							
19	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	900.00	815.00	09/2019	N.A.
HOME AFFAIRS							
20	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ RAF	06/2019	277.35	277.35	5.30	07/2022	07/2022
21	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	166.98	166.98	0.00	10/2023	10/2023
22	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96	01/2020	166.98	166.98	0.29	05/2022	05/2022
HUMAN RESOURCE DEVELOPMENT							
23	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	N.A.
24	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	171.72	171.72	53.94	03/2020	06/2021
25	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676.00	676.00	0.00	04/2023	04/2023
26	STUDY IN INDIA	03/2018	150.00	150.00	0.00	04/2018	N.A.
27	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	418.00	418.00	110.00	03/2019	N.A.
PETROLEUM							
28	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	18.80	02/2017	08/2022
29	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
30	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1112.00	1507.24	725.00	06/2019	02/2022
31	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-	05/2016	261.00	261.00 13	157.94	01/2021	04/2021

	AHMEDNAGAR-SOLAPUR PIPELI						
32	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	212.00	212.00	146.57	01/2021	04/2021
POWER							
33	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13537.76	09/2010	08/2023
35	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3380.97	10/2017	N.A.
36	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	241.68	04/2016	06/2021
37	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1706.23	04/2020	07/2025
RAILWAYS							
38	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
39	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2200.00	714.78	07/2012	03/2024
40	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.06	03/2019	N.A.
41	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	149.30	03/2006	03/2025
42	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	541.83	07/2014	N.A.
ROAD TRANSPORT AND HIGHWAYS							
43	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	446.62	N.A.	N.A.
44	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	238.01	N.A.	N.A.
45	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
46	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	318.64	08/2016	N.A.
47	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	358.22	377.64	343.70	10/2016	N.A.
SHIPPING AND PORTS							
48	JAL MARG VIKAS PROJECT	01/2018	5369.18	4633.81	1814.28	03/2023	03/2023
STEEL							
49	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	31.60	12/2023	12/2023
50	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	377.18	377.18	16.12	05/2023	05/2023
TELECOMMUNICATIONS							
51	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	16594.00	07/2015	06/2021
52	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	248.20	248.20 14	133.09	03/2018	06/2021

53	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	431.16	0.00	06/2021	11/2021
URBAN DEVELOPMENT							
54	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOB LA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	N.A.
55	DELHI MRTS PHASE-III	09/2011	38585.00	38585.00	39838.90	03/2016	09/2021
56	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	884.30	884.30	812.00	12/2015	N.A.
57	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6059.17	07/2017	09/2020
58	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	17039.36	01/2015	03/2023
WATER RESOURCES							
59	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	222.79	12/2019	01/2021
60	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	201.30	12/2019	05/2021
61	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	225.77	271.22	03/2020	03/2021
62	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	214.52	04/2020	03/2021
63	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	286.36	01/2021	N.A.

N.A.: Not Available.

Table-E

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates
(as on 01-04-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	5922.21
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	16488.00
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12320.00	0.00	13158.00
COAL					
4	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	0.00	288.72
5	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	0.00	246.55
HEALTH AND FAMILY WELFARE					
6	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	488.22
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	233.39
8	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
PETROLEUM					

11	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	352.56	0.00	455.00
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	0.00	4977.00
13	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	0.00	2888.48
14	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	0.00	1933.53
POWER					
15	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	8154.50
16	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	487.49	0.00	590.30
17	MUNPL-MEJA TPP - JV (2X660 MW)	04/2012	9750.89	0.00	11130.00
18	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	11846.00	0.00	13766.78
19	KHARGONE STPP STAGE I (1320 MW)	03/2015	9870.51	0.00	10019.31
RAILWAYS					
20	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	714.78
21	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	541.83
22	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FROM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	1207.34
23	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	0.00	23132.28
24	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	697.29
ROAD TRANSPORT AND HIGHWAYS					
25	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	0.00	318.64
26	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	612.58
27	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	325.28
28	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	0.00	251.39
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	0.00	655.17
TELECOMMUNICATIONS					
30	NETWORK FOR SPECTRUM	03/2012	13334.00	0.00	16594.00
URBAN DEVELOPMENT					
31	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16365.87
32	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39838.90
33	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	0.00	4683.08
WATER RESOURCES					
34	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	0.00	271.22
35	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	0.00	286.36

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-04-2021)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
SN	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	N.A.	N.A.
	COAL				
1	RANIGANJ MASTER PLAN	08/2009	08/2019	N.A.	N.A.
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	12/2015	N.A.	02/2021
3	PATHERDIH NLW WASHERY	10/2012	04/2014	N.A.	04/2020
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	12/2019	N.A.	N.A.
	COMMERCE				
6	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	N.A.
	HEALTH AND FAMILY WELFARE				

7	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
8	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
11	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	05/2019
	HEAVY INDUSTRY				
12	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	N.A.	N.A.
	HUMAN RESOURCE DEVELOPMENT				
13	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
14	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	N.A.	N.A.
15	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	N.A.	N.A.
16	STUDY IN INDIA	03/2018	04/2018	N.A.	N.A.
17	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	03/2019	N.A.	N.A.
	MINES				
18	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	N.A.	02/2021
19	UTKAL D AND E COAL BLOCK	05/2016	01/2020	N.A.	N.A.
	PETROLEUM				
20	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
21	MUMBAI REFINERY EXPANSION PROJECT	09/2015	03/2020	N.A.	N.A.
22	BS-VI PROJECTS	09/2017	12/2019	N.A.	01/2021
	POWER				
23	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
24	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
25	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	02/2021	02/2021
26	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	06/2014	N.A.	N.A.
27	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
	RAILWAYS				
28	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
29	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	03/2019	N.A.	N.A.
30	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
31	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	02/2009	N.A.	N.A.
32	HARIDASPUR-PARADEEP(NL)	04/1996	12/2017	N.A.	N.A.
	ROAD TRANSPORT AND HIGHWAYS				
33	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
34	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
35	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
	STEEL				
38	COKE OVEN BATTERY-5	12/2011	12/2017	12/2020	12/2020
	URBAN DEVELOPMENT				

39	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	N.A.	N.A.
40	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
41	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	11/2019	N.A.	N.A.
42	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	12/2015	N.A.	N.A.
43	KOCHI METRO RAIL PROJECT	07/2012	07/2017	09/2020	09/2020
WATER RESOURCES					
44	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	12/2019	N.A.	01/2021
45	SAIDPUR SEWER NETWORK PATNA	04/2015	01/2021	N.A.	N.A.
46	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	03/2017	08/2019	N.A.	N.A.
47	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	05/2017	05/2020	N.A.	N.A.
48	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	09/2020	N.A.	N.A.

N.A.: Not Available.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	908	25
2	RAILWAYS	312	6
3	PETROLEUM	139	18
4	COAL	101	5
5	POWER	78	25
6	WATER RESOURCES	49	2
7	URBAN DEVELOPMENT	33	3
8	HEALTH AND FAMILY WELFARE	29	4
9	HUMAN RESOURCE DEVELOPMENT	26	0
10	CIVIL AVIATION	19	1
11	STEEL	9	1
12	MINES	5	1
13	HOME AFFAIRS	5	0
14	ATOMIC ENERGY	4	0
15	FERTILISERS	4	4
16	RURAL DEVELOPMENT	4	3
17	TELECOMMUNICATIONS	3	0
18	FINANCE	2	0
19	DPIIT	2	1
20	HEAVY INDUSTRY	1	0
21	SHIPPING AND PORTS	1	0
22	DEFENCE PRODUCTION	1	0
23	COMMERCE	1	0
24	CULTURE DEVELOPMENT	1	0
	Total	1737	99

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2020			
	<u>STEEL</u>			
1	INSTALLATION OF NEW HOT STRIP MILL AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000094]	3,127.30	04/2018	3,201.42
	<u>PETROLEUM</u>			
2	INTEGRATED DEVELOPMENT OF B-127 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000131]	2,059.63	03/2015	2,011.80
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000197]	6,068.80	04/2019	4,956.05
4	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000212]	4,619.94	12/2017	4,663.66
5	INDMAX PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000243]	2,582.00	11/2019	1,718.52
6	MOTIHARI AMLEKHGANJ PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000254]	324.00	06/2020	129.09
7	DEVELOPMENT OF B-147 FIELD Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000292]	546.15	11/2019	537.69
8	BS-VI PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000310]	3,380.00	09/2019	2,381.00
9	BS-VI PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000320]	1,222.00	09/2019	764.17
10	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000322]	2,934.40	09/2019	1,957.94
11	BS-VI PROJECT AT PANIPAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000325]	3,529.00	07/2019	2,095.75
12	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR (GAS AUTHORITY OF INDIA LIMITED) - [N16000330]	221.45	10/2022	63.59
13	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000366]	154.84	11/2019	128.71
	June,2020			
	<u>COAL</u>			
14	RKP OCP PHASE-I (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000079]	209.78	03/2015	104.19
15	RG OC -III EXTENSION (PHASE -II) PROJECT (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000100]	365.01	06/2015	365.01
	July,2020			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
16	KULDA OCP (MAHANADI COALFIELDS LTD) (MAHANADI COAL FIELDS LIMITED) - [060100092]	302.96	03/2010	281.80
	<u>PETROLEUM</u>			
17	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000204]	2,818.88	03/2019	2,907.03
18	BS-VI PROJECT AT MATHURA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000306]	666.64	09/2019	493.90
19	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000335]	766.37	12/2019	606.49
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
20	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000347]	723.54	02/2018	1,163.64
21	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000492]	867.66	05/2018	1,289.81
22	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000604]	320.30	01/2019	237.81
23	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000667]	648.32	03/2020	511.34
24	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) Central Sector Projects(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000700]	648.33	06/2017	229.94
25	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000951]	382.81	01/2015	338.18
26	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000952]	179.32	11/2017	129.04
27	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000953]	155.77	09/2016	111.65
28	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000954]	378.07	01/2014	188.65
29	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000955]	511.21	10/2013	813.54
30	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000956]	501.00	09/2013	659.98
31	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000960]	621.43	10/2016	429.97
32	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000961]	163.54	07/2017	108.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>TELECOMMUNICATIONS</u>			
33	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000105]	418.26	06/2017	367.04
34	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000113]	231.80	10/2018	119.92
	<u>URBAN DEVELOPMENT</u>			
35	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000101]	768.88	02/2014	1,125.98
36	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000102]	324.87	12/2015	270.24
37	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000062]	156.57	08/2016	159.35
38	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000108]	206.58	03/2019	185.84
	August,2020			
	<u>COAL</u>			
39	MANUGURU OC-II EXTENSION PHASE-II (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000080]	181.19	03/2012	170.60
	<u>PETROLEUM</u>			
40	RESID UPGRADEATION PROJECT (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000184]	3,110.36	11/2015	2,915.00
41	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000255]	224.00	04/2019	164.61
42	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000256]	135.00	03/2019	156.65
43	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000260]	554.00	02/2020	375.80
44	50MW WIND ENERGY POWER PROJECT (OIL INDIA LIMITED) - [N16000298]	500.00	06/2017	368.24
45	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP (INDIAN OIL CORPORATION LIMITED) - [N16000354]	204.00	09/2019	162.53
46	UPGRADEATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE (OIL INDIA LIMITED) - [N18000148]	871.35	03/2015	565.63
	<u>URBAN DEVELOPMENT</u>			
47	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000109]	253.92	06/2016	1,113.24

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
48	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000110]	200.00	03/2018	131.15
49	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000111]	787.29	12/2016	285.30
50	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000112]	170.00	04/2018	88.91
51	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG Central Sector Projects(HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000114]	185.37	03/2016	178.30
52	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000093]	154.00	11/2015	280.32
	September,2020			
	<u>HUMAN RESOURCE DEVELOPMENT</u>			
53	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000088]	388.00	05/2017	452.80
	October,2020			
	<u>COAL</u>			
54	PENGANGA OCP(REVISED) (WESTERN COAL FIELDS LIMITED) - [N06000066]	441.82	03/2020	259.82
55	GAURI DEEP OC (WESTERN COAL FIELDS LIMITED) - [N06000181]	164.96	03/2019	96.37
	December,2020			
56	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000114]	337.66	03/2019	258.65
	<u>PETROLEUM</u>			
57	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000277]	429.00	01/2019	373.62
58	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000284]	208.35	07/2020	170.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
59	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000505]	1,583.79	01/2019	1,648.90
60	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000669]	165.50	03/2020	117.09

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
61	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000670]	239.68	03/2020	219.75
	January,2021			
	<u>COAL</u>			
62	KULDA EXPN OC. (5.00 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000115]	289.03	03/2018	115.24
	<u>PETROLEUM</u>			
63	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000169]	993.00	01/2012	1,693.00
64	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000238]	1,879.00	06/2020	1,694.25
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
65	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000324]	194.11	05/2018	196.23
66	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000325]	179.82	01/2019	199.53
67	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000411]	218.31	02/2018	292.55
68	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000614]	183.65	11/2016	187.33
69	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000770]	158.65	06/2018	110.62
70	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000920]	223.67	02/2017	112.81
71	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000921]	208.34	02/2016	112.87
72	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000947]	259.52	-	184.51
73	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000977]	189.91	-	160.05

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	February,2021			
	<u>STEEL</u>			
74	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000096]	1,154.18	12/2017	1,027.04
75	CENTRAL DISPATCH YARD (RASTRIYA ISPAT NIGAM LIMITED) - [N12000119]	320.66	08/2018	280.96
	March,2021			
	<u>PETROLEUM</u>			
76	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000348]	951.64	10/2019	708.43
	<u>URBAN DEVELOPMENT</u>			
77	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 (JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION) - [N28000082]	246.90	-	177.77

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	August,2021			
	<u>COAL</u>			
1	KALYANIKHANI 6 INCLINE PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000147]	477.65	03/2020	2.11
2	RAMPURAM SHAFT BLOCK (SINGARENI COLLIERS COMPANY LIMITED) - [N06000174]	431.92	-	0.00
3	SRAVANAPALLI OPENCAST PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000175]	412.70	-	0.76
	<u>HUMAN RESOURCE DEVELOPMENT</u>			
4	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000092]	216.69	03/2015	52.00
	September,2021			
	<u>COAL</u>			
5	KOYAGUDEM OPENCAST PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000146]	426.79	03/2018	0.72
	January,2021			
6	SHANTIKHANI LONGWALL PROJ-SCCL (SINGARENI COLLIERS COMPANY LIMITED) - [N06000017]	249.03	03/2012	326.69
7	KAKATIYA LONGWALL (SINGARENI COLLIERS COMPANY LIMITED) - [N06000048]	453.63	12/2012	121.91
8	BAROUD OC EXPANSION (RCE)- 3MTY (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000099]	258.56	03/2016	182.04
9	KAPURIA UG(PSLW) (BHARAT COKING COAL LIMITED) - [N06000108]	988.35	04/2017	45.26
10	BIJARI OC RCE (1.50 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000111]	164.49	03/2020	82.60
11	MALACHUA OPENCAST PROJECT (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000139]	488.33	03/2023	30.47
12	SAONER I UG TO OC PHASE I (WESTERN COAL FIELDS LIMITED) - [N06000177]	162.10	03/2022	36.94
	<u>PETROLEUM</u>			
13	HALDIA BARAUNI PRODUCT PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000251]	1,021.00	12/2020	4.45
14	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000309]	1,342.00	08/2020	6.30
15	2G ETHANOL BIO REFINERY AT BARGARH (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000341]	750.00	12/2020	34.73

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	February,2021			
16	HALDIA LPG IMPORT FACILITY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000223]	694.00	10/2018	971.84
17	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000269]	342.00	03/2021	0.00
18	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM (INDIAN OIL CORPORATION LIMITED) - [N16000270]	247.00	03/2021	0.00
19	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN (OIL INDIA LIMITED) - [N16000299]	350.00	01/2019	2.06
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
20	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000429]	225.02	12/2018	26.00
21	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000682]	168.32	04/2017	43.28
22	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000684]	216.71	04/2017	26.84
23	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000974]	199.02	-	14.21
24	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000975]	184.88	-	6.85
	<u>TELECOMMUNICATIONS</u>			
25	CONVERGENT BILLING AND CRM-MTNL(DELHI) (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000011]	249.00	02/2007	0.00
26	CONVERGENT BILLING AND CRM(MUMBAI) (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000016]	247.00	02/2007	0.00
27	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (DEPARTMENT OF TELECOMMUNICATION) - [N26000065]	1,077.00	03/2009	0.00
28	DELHI CONVERGENT BILLING AND CRM PE-5834 (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000099]	229.41	03/2012	0.00
29	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY (INDIAN TELEPHONE INDUSTRY) - [N26000102]	2,111.17	09/2014	253.90
	<u>WATER RESOURCES</u>			
30	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR(Uttar Pradesh Jal Nigam) - [N30000012]	857.26	08/2021	0.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
31	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA (Uttar Pradesh Jal Nigam) - [N30000023]	317.19	08/2021	0.00

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1736
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	3
No of Projects in Current Month	1737

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	557 (32.07%)	13 (.75%)	229 (13.18%)	115 (6.62%)	823 (47.38%)	1737
Latest Approved (Date)	412 (23.72%)	24 (1.38%)	373 (21.47%)	105 (6.04%)	823 (47.38%)	1737

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1473	18,09,420.69	20,30,877.11	9,41,945.22	46.40	2,21,456.42	12.20
Project with Revision in Cost	264	6,35,788.05	6,38,772.24	3,64,672.32	57.10	2,984.19	.50
Total	1,737	24,45,208.74	26,69,649.35	13,06,617.54	48.94	2,24,440.61	9.18
Original Cost of All Projects							
Original Cost	1,737	22,33,409.53	26,69,649.35	13,06,617.54	48.94	4,36,239.82	19.53

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	557	9,41,540.20	12,18,511.14	7,02,411.67	57.60	2,76,970.94	29.42
Latest Approved (RCE)	412	7,23,399.28	8,68,167.56	4,86,843.46	56.10	1,44,768.28	20.01

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	99	2,01,967.27	2,44,342.24	1,86,396.08	76.30	42,374.97	21.00
Total	99	2,01,967.27	2,44,342.24	1,86,396.08	76.28	42,374.97	20.98

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	3	1,905.50	2,153.66	13.02
3	COAL	101	1,45,653.01	1,44,210.92	-0.99	14	28,896.09	34,612.18	19.78
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0.00
7	STEEL	9	25,452.51	31,567.51	24.03	1	15,525.00	21,940.00	41.32
8	PETROLEUM	139	2,96,976.45	3,04,102.14	2.40	27	62,139.58	81,062.32	30.45
9	POWER	78	2,95,137.42	3,67,699.63	24.59	32	1,75,198.45	2,49,834.01	42.60
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	12	5,589.39	6,287.30	12.49
12	RAILWAYS	312	4,62,095.03	7,00,073.54	51.50	211	2,29,432.02	4,78,444.49	108.53
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,60,519.84	3.62	133	94,385.49	1,20,598.50	27.77
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	33	2,82,500.28	3,05,097.88	8.00	7	84,474.19	1,07,150.99	26.84
17	WATER RESOURCES	49	26,781.06	72,049.94	169.03	7	12,126.97	57,719.96	375.96
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	5	2,009.81	2,240.41	11.47
21	HOME AFFAIRS	5	1,993.40	2,849.31	42.94	2	1,382.09	2,238.00	61.93

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	2.96
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		1737	22,33,409.53	26,69,649.35	19.53	462	7,71,374.01	12,48,797.90	61.89

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	38.68	16	47,279.32	1,04,034.99	120.04
2	ARUNACHAL PRADESH	42	24,624.65	44,366.68	80.17	10	12,055.29	31,797.32	163.76
3	ASSAM	47	42,046.33	45,657.63	8.59	19	9,301.62	14,229.97	52.98
4	BIHAR	108	1,22,099.62	1,58,462.50	29.78	35	42,074.64	79,557.34	89.09
5	GOA	11	5,629.77	5,640.26	0.19	2	529.17	539.66	1.98
6	GUJARAT	59	1,06,069.60	1,17,304.95	10.59	17	33,456.55	45,670.99	36.51
7	HARYANA	43	30,316.35	32,837.14	8.32	7	3,872.20	6,803.47	75.70
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	3	8,237.58	18,122.01	119.99
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	4	6,582.27	32,776.33	397.95
10	KARNATAKA	60	71,320.53	80,933.03	13.48	15	43,150.08	53,060.00	22.97
11	KERALA	22	37,466.85	42,584.93	13.66	12	18,147.21	23,289.33	28.34
12	MADHYA PRADESH	84	91,161.40	1,04,808.86	14.97	20	35,307.11	49,952.02	41.48
13	MAHARASHTRA	242	2,17,334.38	2,40,364.76	10.60	32	61,705.33	90,012.20	45.87
14	MANIPUR	12	8,137.49	15,887.67	95.24	1	4,454.17	12,264.15	175.34
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	2	1,390.78	4,709.28	238.61
16	MIZORAM	18	9,030.03	12,978.73	43.73	5	3,593.57	7,542.27	109.88
17	NAGALAND	38	18,265.97	22,463.91	22.98	2	2,699.59	7,298.00	170.34
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	17	27,755.43	36,328.65	30.89
19	PUNJAB	29	15,325.05	18,249.98	19.09	8	5,301.19	8,645.53	63.09
20	RAJASTHAN	60	53,090.50	61,137.54	15.16	14	19,890.78	27,938.05	40.46
21	SIKKIM	14	5,074.99	12,481.74	145.95	3	1,909.76	9,316.51	387.84
22	TAMIL NADU	71	1,19,185.26	1,38,366.76	16.09	23	39,340.59	60,194.77	53.01
23	TRIPURA	13	3,479.87	3,662.68	5.25	3	921.97	1,104.78	19.83
24	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	4.19	33	56,372.60	66,070.83	17.20
25	WEST BENGAL	75	65,583.67	84,487.51	28.82	29	29,934.59	49,180.29	64.29
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	2	655.03	679.33	3.71
27	CHANDIGARH	2	349.15	570.00	63.25	2	349.15	570.00	63.25
28	DELHI	36	90,723.12	92,153.92	1.58	9	11,777.30	13,941.30	18.37
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	12	39,499.71	50,796.46	28.60
31	JHARKHAND	42	70,673.40	68,776.10	-2.68	12	23,623.12	29,539.75	25.05
32	UTTARAKHAND	32	34,539.29	46,325.58	34.12	10	25,404.50	37,217.29	46.50
33	TELANGANA	47	36,326.25	39,359.69	8.35	10	15,929.81	19,457.47	22.15
34	MULTI STATE	128	3,66,425.54	4,80,969.26	31.26	73	1,38,872.00	2,56,157.56	84.46

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
Total		1737	22,33,409.53	26,69,649.35	19.53	462	7,71,374.01	12,48,797.90	61.89

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	11	8,526.85	8,640.95	5 - 33
3	COAL	101	1,45,653.01	1,44,210.92	-0.99	50	69,601.31	63,379.05	8 - 228
4	FINANCE	2	557.77	557.73	-0.01	1	209.00	208.96	18 - 18
5	FERTILISERS	4	1,101.28	1,101.28	0.00	4	1,101.28	1,101.28	13 - 17
6	MINES	5	7,078.62	7,075.17	-0.05	2	6,023.00	6,023.00	20 - 23
7	STEEL	9	25,452.51	31,567.51	24.03	5	18,768.09	25,183.09	8 - 74
8	PETROLEUM	139	2,96,976.45	3,04,102.14	2.40	76	1,29,073.92	1,36,017.85	2 - 110
9	POWER	78	2,95,137.42	3,67,699.63	24.59	45	1,96,783.14	2,53,859.03	4 - 155
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	13	4,940.96	4,754.30	11 - 90
12	RAILWAYS	312	4,62,095.03	7,00,073.54	51.50	155	2,00,935.84	3,21,844.05	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,60,519.84	3.62	135	77,324.48	80,483.35	1 - 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	3	14,013.36	25,343.36	5 - 71
16	URBAN DEVELOPMENT	33	2,82,500.28	3,05,097.88	8.00	10	1,05,425.47	1,21,920.25	4 - 98
17	WATER RESOURCES	49	26,781.06	72,049.94	169.03	20	15,804.03	60,964.10	4 - 72
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	1	246.31	246.31	16 - 16
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	14	6,229.82	6,276.31	3 - 63
21	HOME AFFAIRS	5	1,993.40	2,849.31	42.94	2	1,382.09	2,238.00	26 - 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	3	527.83	538.27	58 - 70
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	1	151.33	151.33	42 - 42
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		1737	22,33,409.53	26,69,649.35	19.53	557	9,41,540.20	12,18,511.14	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	38.68	27	84,418.70	1,30,874.97	1 - 180
2	ARUNACHAL PRADESH	42	24,624.65	44,366.68	80.17	3	7,822.52	21,529.62	47 - 155
3	ASSAM	47	42,046.33	45,657.63	8.59	14	9,013.04	11,982.60	2 - 63
4	BIHAR	108	1,22,099.62	1,58,462.50	29.78	25	38,335.22	64,094.90	4 - 141
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	59	1,06,069.60	1,17,304.95	10.59	12	29,299.67	39,621.46	3 - 132
7	HARYANA	43	30,316.35	32,837.14	8.32	15	10,754.03	11,359.18	5 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	3	6,665.52	12,643.52	11 - 154
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	2	10,612.12	36,061.12	63 - 241
10	KARNATAKA	60	71,320.53	80,933.03	13.48	17	40,828.50	45,934.34	2 - 264
11	KERALA	22	37,466.85	42,584.93	13.66	9	12,856.97	14,623.43	4 - 53
12	MADHYA PRADESH	84	91,161.40	1,04,808.86	14.97	41	31,692.83	38,402.56	8 - 73
13	MAHARASHTRA	242	2,17,334.38	2,40,364.76	10.60	43	61,363.35	79,403.22	3 - 216
14	MANIPUR	12	8,137.49	15,887.67	95.24	2	4,971.74	12,721.92	36 - 153
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	2	515.32	515.32	42 - 43
16	MIZORAM	18	9,030.03	12,978.73	43.73	11	6,946.25	10,391.41	43 - 128
17	NAGALAND	38	18,265.97	22,463.91	22.98	14	6,473.72	10,762.04	38 - 117
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	36	71,613.20	74,946.36	3 - 228
19	PUNJAB	29	15,325.05	18,249.98	19.09	12	5,108.01	5,003.71	3 - 108
20	RAJASTHAN	60	53,090.50	61,137.54	15.16	14	19,626.99	25,103.00	4 - 75
21	SIKKIM	14	5,074.99	12,481.74	145.95	0	0.00	0.00	-
22	TAMIL NADU	71	1,19,185.26	1,38,366.76	16.09	27	70,255.53	79,757.87	3 - 198
23	TRIPURA	13	3,479.87	3,662.68	5.25	5	1,269.36	1,452.17	11 - 70
24	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	4.19	41	65,659.77	66,375.60	2 - 68
25	WEST BENGAL	75	65,583.67	84,487.51	28.82	32	30,504.70	38,647.74	4 - 324
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	1	417.23	441.33	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	36	90,723.12	92,153.92	1.58	17	51,136.48	52,373.75	4 - 90
29	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	23	32,502.66	42,200.64	15 - 96
31	JHARKHAND	42	70,673.40	68,776.10	-2.68	19	53,677.79	47,078.45	12 - 152
32	UTTARAKHAND	32	34,539.29	46,325.58	34.12	6	22,461.02	33,218.80	3 - 126
33	TELANGANA	47	36,326.25	39,359.69	8.35	15	17,686.46	18,566.60	9 - 168
34	MULTI STATE	128	3,66,425.54	4,80,969.26	31.26	68	1,36,856.50	1,92,228.51	5 - 276
Total		1737	22,33,409.53	26,69,649.35	19.53	557	9,41,540.20	12,18,511.14	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	9	7,679.14	7,793.24	5 - 33
3	COAL	101	1,47,413.00	1,44,210.92	-2.17	44	38,079.53	38,428.09	0 - 168
4	FINANCE	2	557.77	557.73	-0.01	1	209.00	208.96	18 - 18
5	FERTILISERS	4	1,101.28	1,101.28	0.00	4	1,101.28	1,101.28	13 - 17
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	-
7	STEEL	9	31,867.51	31,567.51	-0.94	1	263.36	263.36	8 - 8
8	PETROLEUM	139	3,10,698.53	3,04,102.14	-2.12	35	37,687.24	41,484.23	2 - 94
9	POWER	78	3,60,540.42	3,67,699.63	1.99	19	1,15,702.52	1,16,009.29	5 - 126
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	13	4,940.96	4,754.30	11 - 90
12	RAILWAYS	312	5,30,826.75	7,00,073.54	31.88	132	1,79,087.32	2,81,600.00	0 - 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,43,235.61	5,60,519.84	3.18	101	60,311.28	61,459.60	0 - 105
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	3	14,013.20	25,343.36	5 - 71
16	URBAN DEVELOPMENT	33	2,87,978.35	3,05,097.88	5.94	9	1,09,293.45	1,21,498.25	9 - 98
17	WATER RESOURCES	49	72,273.40	72,049.94	-0.31	15	59,907.71	59,673.08	4 - 72
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	1	246.31	246.31	16 - 16
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	14	6,242.64	6,276.31	3 - 63
21	HOME AFFAIRS	5	2,068.54	2,849.31	37.75	1	1,219.21	2,000.00	26 - 26
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	3	606.71	538.27	58 - 70
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	1	151.33	151.33	42 - 42
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		1737	24,45,208.74	26,69,649.35	9.18	412	7,23,399.28	8,68,167.56	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest cost						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	3	1,905.50	2,153.66	13.02
3	COAL	101	1,47,413.00	1,44,210.92	-2.17	10	22,289.42	25,496.41	14.39
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0.00
7	STEEL	9	31,867.51	31,567.51	-0.94	0	0.00	0.00	0.00
8	PETROLEUM	139	3,10,698.53	3,04,102.14	-2.12	8	17,320.45	22,353.20	29.06
9	POWER	78	3,60,540.42	3,67,699.63	1.99	12	68,118.64	77,351.20	13.55
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	12	5,589.39	6,287.30	12.49
12	RAILWAYS	312	5,30,826.75	7,00,073.54	31.88	194	1,94,414.36	3,76,579.30	93.70
13	ROAD TRANSPORT AND HIGHWAYS	908	5,43,235.61	5,60,519.84	3.18	155	1,06,378.03	1,30,764.64	22.92
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	2	13,765.00	25,095.16	82.31
16	URBAN DEVELOPMENT	33	2,87,978.35	3,05,097.88	5.94	4	52,773.00	69,971.73	32.59
17	WATER RESOURCES	49	72,273.40	72,049.94	-0.31	2	913.57	924.74	1.22
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	5	2,022.63	2,240.41	10.77
21	HOME AFFAIRS	5	2,068.54	2,849.31	37.75	1	1,219.21	2,000.00	64.04
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0.00
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		1737	24,45,208.74	26,69,649.35	9.18	413	5,33,517.29	8,00,707.05	50.08

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	74- 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	2	1,559.23	1,673.33	12- 33
3	COAL	101	1,47,413.00	1,44,210.92	-2.17	7	2,202.75	2,702.45	12- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0- 0
7	STEEL	9	31,867.51	31,567.51	-0.94	0	0.00	0.00	0- 0
8	PETROLEUM	139	3,10,698.53	3,04,102.14	-2.12	7	16,897.45	21,851.20	5- 48
9	POWER	78	3,60,540.42	3,67,699.63	1.99	2	5,991.58	7,854.35	10- 126
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	4	1,043.69	1,199.69	24- 90
12	RAILWAYS	312	5,30,826.75	7,00,073.54	31.88	88	1,22,364.64	2,34,837.27	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,43,235.61	5,60,519.84	3.18	12	11,720.70	14,189.36	14- 105
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	2	13,765.00	25,095.16	5- 71
16	URBAN DEVELOPMENT	33	2,87,978.35	3,05,097.88	5.94	2	33,909.00	46,193.00	44- 98
17	WATER RESOURCES	49	72,273.40	72,049.94	-0.31	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	4	1,538.31	1,614.15	6- 52
21	HOME AFFAIRS	5	2,068.54	2,849.31	37.75	1	1,219.21	2,000.00	26- 26
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0- 0
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		1737	24,45,208.74	26,69,649.35	9.18	136	2,59,019.65	4,18,699.26	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	19	13,786.34	14,034.50	1.80	2	1,559.23	1,673.33	12- 33
3	COAL	101	1,45,653.01	1,44,210.92	-0.99	11	20,139.31	21,075.23	8- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0- 0
7	STEEL	9	25,452.51	31,567.51	24.03	1	15,525.00	21,940.00	74- 74
8	PETROLEUM	139	2,96,976.45	3,04,102.14	2.40	22	52,580.91	70,049.13	5- 110
9	POWER	78	2,95,137.42	3,67,699.63	24.59	18	1,19,401.05	1,78,550.29	10- 155
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	4	1,043.69	1,199.69	24- 90
12	RAILWAYS	312	4,62,095.03	7,00,073.54	51.50	108	1,37,034.98	2,68,383.97	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,60,519.84	3.62	23	16,924.25	21,555.93	1- 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	1	13,334.00	24,664.00	71- 71
16	URBAN DEVELOPMENT	33	2,82,500.28	3,05,097.88	8.00	3	60,314.14	76,888.12	44- 98
17	WATER RESOURCES	49	26,781.06	72,049.94	169.03	3	10,719.87	56,204.05	4- 25
18	DEFENCE PRODUCTION	1	246.31	246.31	0.00	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	4	1,525.49	1,614.15	6- 52
21	HOME AFFAIRS	5	1,993.40	2,849.31	42.94	2	1,382.09	2,238.00	26- 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	58- 70
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		1737	22,33,409.53	26,69,649.35	19.53	209	4,96,459.44	8,05,887.97	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	06/2017	951.64	10/2019	951.64	N.A.	708.43
	<u>URBAN DEVELOPMENT</u>						
2	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	N.A.	246.90	N.A.	177.77

TABLE-14

List of projects added					Rs. 150	Crore and above		(March 2021)	
			Original		Anticipated				
Sl.No	Project	DOA	Cost	DOC	Cost	DOC			
	HOME AFFAIRS								
1	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ R AF EPC	6/2019	277.35	7/2022	277.35	7/2022			
	PETROLEUM								
2	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R	8/2020	697.00	3/2023	697.00	3/2023			
3	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	1,614.00	8/2023	1,614.00	8/2023			

TABLE-15

Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		5857	
Achieved up to month		3038	

TABLE-16

List of projects reporting additional delayed Rs. 150 Crore and above							(March 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA AAI	458.00	458.00	03/2020	06/2021	12/2021	6
	<u>COAL</u>						
2	MADHUBAND NLW WASHERY BCCL	289.45	289.45	05/2014	06/2021	07/2021	1
3	2.0 MTPA BHOJUDIH NLW WASHERY BCCL	304.13	341.22	03/2017	10/2021	03/2022	5
4	PATHERDIH 2.5 NLW COAL WASHERY BCCL	243.00	334.27	04/2018	12/2021	06/2022	6
5	CHHAL OC SEAM -III (6.00 MTY) SECL	610.63	610.63	03/2022	03/2022	03/2025	36
6	DURGAPUR OPENCAST PROJECT SECL	916.24	916.24	03/2023	03/2023	03/2026	36
	<u>FERTILISERS</u>						
7	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT NFL	215.92	215.92	11/2019	03/2021	04/2021	1
8	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL NFL	239.81	239.81	11/2019	03/2021	04/2021	1
9	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY RCF	426.72	426.72	04/2020	04/2021	05/2021	1
10	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA NFL	218.83	218.83	11/2019	02/2021	04/2021	2
	<u>MINES</u>						
11	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN NALCO Central Sector Projects	483.00	483.00	04/2021	04/2021	03/2023	23
	<u>STEEL</u>						
12	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	03/2021	04/2021	1
	<u>PETROLEUM</u>						

List of projects reporting additional delayed Rs. 150 Crore and above (March 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
13	MMPL PIPELINE REROUTING PROJECT BPCL	449.58	449.58	12/2019	03/2021	04/2021	1
14	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT GAIL	286.42	327.01	08/2020	05/2021	06/2021	1
15	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	03/2021	05/2021	2
16	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	04/2021	06/2021	2
17	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY BPCL	3,313.00	3,288.96	02/2020	03/2021	05/2021	2
18	RESITEMENT OF RAICHUR DEPOT TO GULBARGA BPCL	206.26	206.26	03/2021	03/2021	05/2021	2
19	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT BPCL	580.20	580.20	02/2021	03/2021	05/2021	2
20	PARADIP SOMNATHPUR HALDIA PIPELINE IOCL	1,297.50	1,297.50	10/2021	12/2021	03/2022	3
21	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END IOCL	1,378.00	1,378.00	12/2022	09/2022	12/2022	3
22	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS HPCL EPC	520.00	520.00	09/2026	09/2026	02/2027	5
23	CITY GAS DISTRIBUTION IN UP AND UK HPCL	3,450.20	3,450.20	03/2029	03/2029	08/2029	5
24	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY IOCL	199.36	199.36	10/2020	02/2022	08/2022	6
25	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY IOCL	371.00	371.00	09/2022	09/2022	03/2023	6
26	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT GAIL	217.92	217.92	04/2021	04/2021	10/2021	6
27	R and D CAMPUS II AT FARIDABAD IOCL	2,281.94	2,281.94	12/2022	12/2022	07/2023	7
28	COMPRESSED BIO GAS PLANT AT GORAKHPUR IOCL	164.69	164.69	07/2021	07/2021	03/2022	8
29	PARADIP HYDERABAD PIPELINE IOCL	2,321.00	3,338.00	12/2020	06/2021	03/2022	9
30	ADDITIONAL STORAGE TANKS AT PARADIP IOCL	462.30	462.30	09/2021	09/2021	06/2022	9
	<u>POWER</u>						

List of projects reporting additional delayed Rs. 150 Crore and above							(March 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
31	DARLIPALLI STPP STAGE-I (2X800 MW) NTPC	12,532.44	13,140.91	12/2018	04/2021	05/2021	1
32	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR PGCIL	808.63	808.63	01/2018	03/2021	04/2021	1
33	EASTERN REGION STRENGTHENING SCHEME-XV PGCIL	454.11	454.11	04/2018	03/2021	04/2021	1
34	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P PGCIL	14,733.37	14,733.37	11/2019	03/2021	04/2021	1
35	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	04/2021	05/2021	1
36	EASTERN REGION STRENGTHENING SCHEME- XVIII PGCIL Central Sector Projects	3,500.00	3,994.00	07/2020	04/2021	05/2021	1
37	EASTERN REGION STRENGTHENING SCHEME XX PGCIL	358.83	358.83	05/2020	03/2021	04/2021	1
38	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI CPWD	271.90	271.90	11/2019	05/2021	06/2021	1
39	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	10,566.00	07/2012	04/2021	06/2021	2
40	DURGAPUR PP-III (2X20 MW) - NSPCL NTPC	529.68	529.68	11/2018	05/2021	07/2021	2
41	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR PGCIL	5,070.13	5,070.13	04/2020	03/2021	06/2021	3
42	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN PGCIL Central Sector Projects	1,931.39	1,931.39	02/2020	03/2021	06/2021	3
43	PARBATI HEP (4X200 MW) (NHPC) II NHPC	3,919.59	9,897.59	09/2009	03/2022	07/2022	4
44	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,997.70	11/2020	03/2022	07/2022	4
45	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	1,885.13	12/2018	03/2021	07/2021	4
46	DEVIKOT SOLAR 90MW NTPC EPC	501.29	501.29	09/2021	09/2021	01/2022	4
47	DEVIKOT SOLAR 150MW NTPC EPC	798.24	798.24	09/2021	09/2021	01/2022	4
48	NOKHRA NTPC EPC	1,722.14	1,722.14	09/2021	09/2021	01/2022	4
49	SAMBHU KI BHURJ SOLAR 250 MW NTPC EPC	1,522.71	1,522.71	09/2021	09/2021	01/2022	4

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (March 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
50	SAMBHU KI BHURJ-II SOLAR 300MW NTPC EPC	1,782.00	1,782.00	09/2021	09/2021	01/2022	4
51	KAYAMKULAM SOLAR 70 MW NTPC EPC	403.62	403.62	06/2021	06/2021	10/2021	4
52	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	14,719.10	08/2013	03/2022	08/2022	5
53	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	07/2021	12/2021	5
54	BARH STPP(3X660MW) NTPC NTPC	8,692.97	21,312.11	10/2011	04/2022	07/2023	15
55	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P PGCIL	4,754.42	9,129.32	12/2018	12/2021	03/2024	27
	<u>HEALTH AND FAMILY WELFARE</u>						
56	SUPER SPECIALITY BLOCK PMSSY GOA HSCC Central Sector Projects	249.01	249.07	N.A.	12/2020	01/2021	1
57	LHMC NEW DELHI-RE-DEVELOPMENT HSCC	414.11	499.23	11/2013	03/2021	05/2021	2
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL HSCC Central Sector Projects	355.15	355.15	03/2019	03/2021	06/2021	3
59	GERIATRICS BLOCK- AIIMS DLEHI HSCC	156.56	190.34	N.A.	03/2021	06/2021	3
	<u>RAILWAYS</u>						
60	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM- CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,121.00	N.A.	02/2021	04/2021	2
61	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) WR	829.74	1,959.74	03/2020	12/2023	03/2024	3
62	ARSIKERE-TUMKUR SWR	578.00	783.00	03/2020	03/2021	06/2021	3
63	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I IRCON	3,055.00	3,055.15	09/2018	12/2021	03/2022	3
64	HUBLI- CHIKJAJUR SWR	1,156.94	1,656.00	03/2020	11/2021	03/2023	16
65	HOTGI-KUDGI-GADAG SWR	1,614.59	1,870.41	03/2019	03/2021	03/2024	36
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
66	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS NHAI	364.56	392.00	N.A.	02/2021	03/2021	1

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (March 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
67	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	07/2021	08/2021	1
68	2L+PS OF THIKRI ANJAD SECTION OF NH-347B MoRTH	249.05	249.05	07/2018	03/2021	04/2021	1
69	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 MoRTH	249.50	249.50	05/2019	02/2021	03/2021	1
70	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT MoRTH	218.90	218.90	03/2020	02/2021	03/2021	1
71	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO MoRTH	208.88	208.88	10/2019	02/2021	03/2021	1
72	NALBARI T BIJNI (AS-7) NHAI	208.00	230.00	04/2008	12/2020	02/2021	2
73	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 NHAI	314.43	314.43	N.A.	04/2021	06/2021	2
74	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA MoRTH	169.63	169.63	03/2018	04/2021	06/2021	2
75	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS MoRTH	296.50	296.50	09/2020	03/2021	05/2021	2
76	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN NHAI	649.50	649.50	03/2019	12/2021	03/2022	3
77	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 MoRTH EPC	628.45	628.45	01/2020	03/2021	06/2021	3
78	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH NHAI Central Sector Projects	641.17	641.17	07/2016	11/2020	02/2021	3
79	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULAM (KM 7.300) TO NATHAM (KM. 3 NHAI EPC	505.35	505.35	N.A.	05/2021	08/2021	3
80	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) NHAI EPC	628.71	628.71	N.A.	09/2021	12/2021	3
81	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS MoRTH	233.04	233.04	03/2018	03/2021	06/2021	3
82	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS MoRTH	254.17	254.17	02/2018	03/2021	06/2021	3

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (March 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
83	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS MoRTH	279.44	279.44	03/2018	03/2021	06/2021	3
84	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A MoRTH	188.80	188.80	05/2019	03/2021	06/2021	3
85	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 MoRTH	379.16	379.16	11/2017	03/2021	06/2021	3
86	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS MoRTH	162.56	162.56	03/2018	02/2021	06/2021	4
87	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS MoRTH	184.62	184.62	02/2018	02/2021	06/2021	4
88	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS NHAI	1,016.92	1,071.00	N.A.	07/2021	01/2022	6
89	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	12/2020	08/2021	8
90	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD MoRTH	264.50	264.50	03/2021	03/2021	11/2021	8
	<u>URBAN DEVELOPMENT</u>						
91	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI CPWD	197.33	197.33	04/2019	10/2021	12/2021	2
92	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR NBCC	2,694.00	2,694.00	N.A.	07/2022	12/2022	5
93	DELHI MRTS PHASE-III DMRC	38,585.00	38,585.00	03/2016	03/2021	09/2021	6
	<u>WATER RESOURCES</u>						
94	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA KMDA	198.43	224.69	02/2022	02/2022	06/2022	4
95	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH KMDA	160.00	154.73	02/2022	02/2022	10/2022	8
	<u>RURAL DEVELOPMENT</u>						
96	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V HSCL	149.73	155.66	12/2015	03/2021	10/2021	7

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (March 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
97	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI HSCL	202.61	207.12	12/2016	03/2021	10/2021	7
98	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII HSCL	175.49	175.49	12/2016	03/2021	12/2021	9
	<u>DPIIT</u>						
99	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE IICC	4,773.00	5,178.00	12/2019	10/2021	12/2021	2

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	59,216.21
CIVIL AVIATION	19	13,786.34	137,86.34	14,034.50	2,939.03
COAL	101	1,45,653.01	1,474,13.00	1,44,210.92	48,349.37
FINANCE	2	557.77	5,57.77	557.73	319.39
FERTILISERS	4	1,101.28	11,01.28	1,101.28	866.91
MINES	5	7,078.62	79,71.07	7,075.17	1,311.10
STEEL	9	25,452.51	318,67.51	31,567.51	23,080.97
PETROLEUM	139	2,96,976.45	3,106,98.53	3,04,102.14	1,12,387.28
POWER	78	2,95,137.42	3,605,40.42	3,67,699.63	2,55,492.70
HEAVY INDUSTRY	1	1,554.00	15,54.00	900.00	815.00
HEALTH AND FAMILY WELFARE	29	15,273.26	152,73.26	15,628.51	7,793.54
RAILWAYS	312	4,62,095.03	5,308,26.75	7,00,073.54	2,48,327.84
ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,432,35.61	5,60,519.84	3,54,098.27
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,814.28
TELECOMMUNICATIONS	3	14,013.36	140,13.20	25,343.36	16,727.09
URBAN DEVELOPMENT	33	2,82,500.28	2,879,78.35	3,05,097.88	1,35,973.44
WATER RESOURCES	49	26,781.06	722,73.40	72,049.94	21,633.37
DEFENCE PRODUCTION	1	246.31	2,46.31	246.31	123.83
COMMERCE	1	302.64	3,02.64	302.64	60.00
HUMAN RESOURCE DEVELOPMENT	26	11,077.40	110,90.22	11,265.83	2,437.07
HOME AFFAIRS	5	1,993.40	20,68.54	2,849.31	1,082.82
RURAL DEVELOPMENT	4	889.43	9,68.31	899.87	472.48
CULTURE DEVELOPMENT	1	151.33	1,51.33	151.33	148.33
DPIIT	2	17,352.09	173,52.09	18,990.30	11,147.22
Grand total	1737	22,33,409.53	24,45,208.74	26,69,649.35	13,06,617.54

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	38.68	10	41,926.16	97,304.43	1 - 180
2	ARUNACHAL PRADESH	42	24,624.65	44,366.68	80.17	1	6,285.33	19,992.43	155 - 155
3	ASSAM	47	42,046.33	45,657.63	8.59	8	6,161.24	9,356.06	2 - 48
4	BIHAR	108	1,22,099.62	1,58,462.50	29.78	10	30,865.91	56,867.93	15 - 141
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	59	1,06,069.60	1,17,304.95	10.59	9	27,063.50	37,513.07	3 - 132
7	HARYANA	43	30,316.35	32,837.14	8.32	3	828.42	1,520.46	7 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	1	3,919.59	9,897.59	154 - 154
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	1	2,500.00	27,949.00	241 - 241
10	KARNATAKA	60	71,320.53	80,933.03	13.48	5	29,365.86	34,769.12	15 - 96
11	KERALA	22	37,466.85	42,584.93	13.66	4	7,431.46	9,221.96	32 - 53
12	MADHYA PRADESH	84	91,161.40	1,04,808.86	14.97	12	10,415.44	17,739.52	12 - 73
13	MAHARASHTRA	242	2,17,334.38	2,40,364.76	10.60	15	39,712.26	62,189.46	9 - 216
14	MANIPUR	12	8,137.49	15,887.67	95.24	1	4,454.17	12,264.15	153 - 153
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	0	0.00	0.00	-
16	MIZORAM	18	9,030.03	12,978.73	43.73	3	2,782.20	6,227.36	108 - 128
17	NAGALAND	38	18,265.97	22,463.91	22.98	2	2,699.59	7,298.00	57 - 117
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	12	25,923.02	33,494.18	15 - 204
19	PUNJAB	29	15,325.05	18,249.98	19.09	3	1,201.49	1,284.88	18 - 37
20	RAJASTHAN	60	53,090.50	61,137.54	15.16	6	14,806.96	20,283.20	15 - 75
21	SIKKIM	14	5,074.99	12,481.74	145.95	0	0.00	0.00	-
22	TAMIL NADU	71	1,19,185.26	1,38,366.76	16.09	9	11,406.45	22,407.51	21 - 198
23	TRIPURA	13	3,479.87	3,662.68	5.25	3	921.97	1,104.78	24 - 70
24	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	4.19	8	30,509.13	32,601.95	7 - 68
25	WEST BENGAL	75	65,583.67	84,487.51	28.82	11	17,317.29	25,480.93	4 - 324
26	A & N ISLANDS	9	2,888.63	2,893.59	0.17	1	417.23	441.33	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	36	90,723.12	92,153.92	1.58	4	6,610.76	7,927.23	24 - 90
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	9	25,751.75	35,569.08	21 - 84
31	JHARKHAND	42	70,673.40	68,776.10	-2.68	3	14,867.78	16,082.37	30 - 50
32	UTTARAKHAND	32	34,539.29	46,325.58	34.12	3	21,686.06	32,443.84	3 - 126
33	TELANGANA	47	36,326.25	39,359.69	8.35	7	12,777.27	14,151.63	9 - 132
34	MULTI STATE	128	3,66,425.54	4,80,969.26	31.26	45	95,851.15	1,52,504.52	5 - 276
Total		1737	22,33,409.53	26,69,649.35	19.53	209	4,96,459.44	8,05,887.97	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	161	5
2	ROAD TRANSPORT AND HIGHWAYS	156	3
3	PETROLEUM	57	7
4	POWER	46	16
5	COAL	30	0
6	URBAN DEVELOPMENT	23	2
7	CIVIL AVIATION	5	0
8	STEEL	5	1
9	ATOMIC ENERGY	4	0
10	HEALTH AND FAMILY WELFARE	4	0
11	DPIIT	2	1
12	MINES	1	0
13	SHIPPING AND PORTS	1	0
14	TELECOMMUNICATIONS	1	0
15	WATER RESOURCES	1	0
16	HOME AFFAIRS	1	0
	Total	498	35

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2020			
	<u>STEEL</u>			
1	INSTALLATION OF NEW HOT STRIP MILL AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000094]	3,127.30	04/2018	3,201.42
	<u>PETROLEUM</u>			
2	INTEGRATED DEVELOPMENT OF B-127 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000131]	2,059.63	03/2015	2,011.80
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000197]	6,068.80	04/2019	4,956.05
4	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000212]	4,619.94	12/2017	4,663.66
5	INDMAX PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000243]	2,582.00	11/2019	1,718.52
6	BS-VI PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000310]	3,380.00	09/2019	2,381.00
7	BS-VI PROJECT AT BONGAIGAON REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000320]	1,222.00	09/2019	764.17
8	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000322]	2,934.40	09/2019	1,957.94
9	BS-VI PROJECT AT PANIPAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000325]	3,529.00	07/2019	2,095.75
	July,2020			
10	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000204]	2,818.88	03/2019	2,907.03
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000347]	723.54	02/2018	1,163.64
12	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000492]	867.66	05/2018	1,289.81
	<u>URBAN DEVELOPMENT</u>			
13	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000101]	768.88	02/2014	1,125.98
	August,2020			
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2020-2021

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
14	RESID UPGRADATION PROJECT (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000184]	3,110.36	11/2015	2,915.00
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA- BARAUNI CRUDE OIL TRUNK PIPELINE (OIL INDIA LIMITED) - [N18000148]	871.35	03/2015	565.63
	<u>URBAN DEVELOPMENT</u>			
16	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND (HINDUSTAN STEELWORK CONSTRUCTION LIMITED) - [N12000109]	253.92	06/2016	1,113.24
	December,2020			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000505]	1,583.79	01/2019	1,648.90
	January,2021			
	<u>PETROLEUM</u>			
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000169]	993.00	01/2012	1,693.00
19	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000238]	1,879.00	06/2020	1,694.25
	February,2021			
	<u>STEEL</u>			
20	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000096]	1,154.18	12/2017	1,027.04

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2020-2021				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	January,2021			
	<u>PETROLEUM</u>			
1	HALDIA BARAUNI PRODUCT PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000251]	1,021.00	12/2020	4.45
2	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000309]	1,342.00	08/2020	6.30
	February,2021			
3	HALDIA LPG IMPORT FACILITY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000223]	694.00	10/2018	971.84
	<u>TELECOMMUNICATIONS</u>			
4	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (DEPARTMENT OF TELECOMMUNICATION) - [N26000065]	1,077.00	03/2009	0.00
5	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY (INDIAN TELEPHONE INDUSTRY) - [N26000102]	2,111.17	09/2014	253.90

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	495
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects added in Current Month	1
No of Projects in Current Month	498

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	207 (41.57%)	8 (1.61%)	76 (15.26%)	38 (7.63%)	169 (33.94%)	498
Latest Approved (Date)	151 (30.32%)	11 (2.21%)	132 (26.51%)	35 (7.03%)	169 (33.94%)	498

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	419	13,70,481.57	15,84,035.46	7,21,652.16	45.60	2,13,553.89	15.60
Project with Revision in Cost	79	5,58,481.44	5,66,641.03	3,20,321.80	56.50	8,159.59	1.50
Total	498	19,28,963.01	21,50,676.49	10,41,973.96	48.45	2,21,713.48	11.49
Original Cost of All Projects							
Original Cost	498	17,21,591.41	21,50,676.49	10,41,973.96	48.45	4,29,085.08	24.92

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	207	7,83,221.88	10,67,737.57	6,22,925.16	58.30	2,84,515.69	36.33
Latest Approved (RCE)	151	6,10,003.82	7,58,552.17	4,30,985.24	56.80	1,48,548.35	24.35

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	35	1,79,298.86	2,21,227.83	1,74,567.73	78.90	41,928.97	23.40
Total	35	1,79,298.86	2,21,227.83	1,74,567.73	78.91	41,928.97	23.38

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 1000 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	30	1,08,556.34	1,13,115.57	4.20	3	25,805.84	30,365.07	17.67
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	5	24,006.86	30,121.86	25.47	1	15,525.00	21,940.00	41.32
6	PETROLEUM	57	2,64,239.96	2,71,066.38	2.58	16	58,110.61	76,233.97	31.19
7	POWER	46	2,81,387.51	3,53,015.51	25.46	24	1,71,424.92	2,45,126.27	42.99
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
9	RAILWAYS	161	3,94,274.15	6,24,000.70	58.27	121	1,98,375.92	4,29,387.46	116.45
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,314.59	6.63	44	59,229.74	76,309.55	28.84
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	23	2,78,636.14	3,01,082.00	8.06	6	84,359.93	1,06,884.99	26.70
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		498	17,21,591.41	21,50,676.49	24.92	226	6,86,229.30	11,32,480.48	65.03

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun[^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	10	45,532.51	1,02,125.54	124.29
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	3	10,761.23	29,956.67	178.38
3	ASSAM	6	27,224.48	29,692.21	9.06	4	4,630.48	7,098.21	53.29
4	BIHAR	27	87,426.57	1,21,814.59	39.33	15	33,512.04	67,900.06	102.61
5	GUJARAT	24	87,824.17	98,441.87	12.09	10	30,646.76	41,923.51	36.80
6	HARYANA	12	16,498.78	18,358.28	11.27	1	1,108.00	2,967.50	167.82
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	3	8,237.58	18,122.01	119.99
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	3	6,236.00	32,296.00	417.90
9	KARNATAKA	17	53,661.87	62,706.98	16.86	10	40,753.66	49,798.77	22.19
10	KERALA	11	32,478.92	37,206.00	14.55	8	16,604.02	21,355.14	28.61
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	11	31,854.48	45,006.24	41.29
12	MAHARASHTRA	49	1,39,827.20	1,66,044.35	18.75	20	57,187.57	84,111.65	47.08
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	175.34
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	130.69
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	197.05
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	11	26,251.24	34,290.60	30.62
18	PUNJAB	4	5,049.00	7,181.59	42.24	2	2,557.95	4,867.50	90.29
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	5	16,355.72	23,031.18	40.81
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	27	99,664.04	1,17,838.13	18.24	14	37,271.47	55,840.56	49.82
22	UTTAR PRADESH	48	1,40,935.26	1,47,900.58	4.94	14	48,992.89	56,899.34	16.14
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	14	25,352.53	43,152.57	70.21
24	DELHI	9	80,186.38	81,749.70	1.95	3	10,256.21	11,898.73	16.01
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	8	37,748.96	48,488.81	28.45
26	JHARKHAND	16	56,545.31	60,442.40	6.89	6	21,917.94	27,371.03	24.88
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	4	23,213.06	34,244.91	47.52
28	TELANGANA	6	19,991.02	22,099.10	10.55	3	12,977.58	15,453.54	19.08
29	MULTI STATE	62	3,38,662.43	4,48,460.13	32.42	39	1,24,849.32	2,36,900.79	89.75
Total		498	17,21,591.41	21,50,676.49	24.92	226	6,86,229.30	11,32,480.48	65.03

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	3	4,992.00	5,082.00	7 - 12
3	COAL	30	1,08,556.34	1,13,115.57	4.20	13	48,174.85	48,175.65	8 - 228
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	20 - 20
5	STEEL	5	24,006.86	30,121.86	25.47	3	18,241.86	24,656.86	31 - 74
6	PETROLEUM	57	2,64,239.96	2,71,066.38	2.58	25	1,09,652.67	1,16,304.73	5 - 110
7	POWER	46	2,81,387.51	3,53,015.51	25.46	29	1,90,089.57	2,47,107.90	4 - 155
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	-
9	RAILWAYS	161	3,94,274.15	6,24,000.70	58.27	100	1,65,657.03	2,88,502.53	2 - 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,314.59	6.63	18	27,848.42	30,472.81	1 - 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71 - 71
13	URBAN DEVELOPMENT	23	2,78,636.14	3,01,082.00	8.06	6	1,03,849.14	1,20,343.92	36 - 98
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26 - 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		498	17,21,591.41	21,50,676.49	24.92	207	7,83,221.88	10,67,737.57	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	9	77,591.98	1,23,929.47	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	2	7,538.43	21,245.53	60 - 155
3	ASSAM	6	27,224.48	29,692.21	9.06	4	4,630.48	7,098.21	2 - 48
4	BIHAR	27	87,426.57	1,21,814.59	39.33	9	32,035.52	57,490.05	15 - 141
5	GUJARAT	24	87,824.17	98,441.87	12.09	7	26,970.60	36,965.18	3 - 74
6	HARYANA	12	16,498.78	18,358.28	11.27	3	6,046.66	6,046.66	7 - 29
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	2	6,405.52	12,383.52	15 - 154
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	2	10,612.12	36,061.12	63 - 241
9	KARNATAKA	17	53,661.87	62,706.98	16.86	5	33,596.70	38,385.74	22 - 264
10	KERALA	11	32,478.92	37,206.00	14.55	5	10,744.46	12,510.92	15 - 53
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	13	19,338.26	25,650.22	12 - 73
12	MAHARASHTRA	49	1,39,827.20	1,66,044.35	18.75	15	44,494.24	66,503.66	9 - 216
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	108 - 108
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	117 - 117
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	23	60,801.54	68,182.07	5 - 228
18	PUNJAB	4	5,049.00	7,181.59	42.24	1	1,069.59	1,069.59	22 - 22
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	3	15,624.71	20,383.71	4 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	0	0.00	0.00	-
21	TAMIL NADU	27	99,664.04	1,17,838.13	18.24	13	62,212.91	71,866.08	3 - 145
22	UTTAR PRADESH	48	1,40,935.26	1,47,900.58	4.94	14	56,087.54	57,140.57	4 - 48
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	12	23,827.27	31,756.93	12 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	5	47,151.73	48,258.32	24 - 66
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	6	25,403.02	34,561.43	21 - 74
26	JHARKHAND	16	56,545.31	60,442.40	6.89	7	43,801.65	43,268.49	13 - 83
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	6	19,991.02	22,099.10	10.55	3	13,183.42	13,214.26	20 - 168
29	MULTI STATE	62	3,38,662.43	4,48,460.13	32.42	38	1,23,193.31	1,76,625.40	5 - 276
Total		498	17,21,591.41	21,50,676.49	24.92	207	7,83,221.88	10,67,737.57	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

Extent of time overrun in projects with respect to latest schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	3	4,992.00	5,082.00	7 - 12
3	COAL	30	1,10,630.02	1,13,115.57	2.25	9	24,640.15	24,640.15	0 - 168
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	-
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	-
6	PETROLEUM	57	2,77,392.84	2,71,066.38	-2.28	11	28,561.89	32,459.02	5 - 94
7	POWER	46	3,46,364.58	3,53,015.51	1.92	13	1,13,525.80	1,13,832.57	10 - 126
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	-
9	RAILWAYS	161	4,62,128.07	6,24,000.70	35.03	84	1,48,116.89	2,53,716.53	0 - 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,460.39	2,52,314.59	6.70	16	25,268.80	26,926.81	15 - 105
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71 - 71
13	URBAN DEVELOPMENT	23	2,83,962.47	3,01,082.00	6.03	6	1,08,139.12	1,20,343.92	36 - 98
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26 - 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		498	19,28,963.01	21,50,676.49	11.49	151	6,10,003.82	7,58,552.17	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	30	1,10,630.02	1,13,115.57	2.25	2	19,898.73	22,384.28	12.49
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0.00
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	0.00
6	PETROLEUM	57	2,77,392.84	2,71,066.38	-2.28	5	15,906.29	20,708.86	30.19
7	POWER	46	3,46,364.58	3,53,015.51	1.92	9	66,779.54	75,503.82	13.06
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
9	RAILWAYS	161	4,62,128.07	6,24,000.70	35.03	109	1,64,879.13	3,30,212.75	100.28
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,460.39	2,52,314.59	6.70	47	63,357.74	80,476.17	27.02
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	23	2,83,962.47	3,01,082.00	6.03	4	52,773.00	69,971.73	32.59
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		498	19,28,963.01	21,50,676.49	11.49	186	4,49,025.73	6,89,941.91	53.65

[^] - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	12- 12
3	COAL	30	1,10,630.02	1,13,115.57	2.25	0	0.00	0.00	0- 0
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0- 0
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	0- 0
6	PETROLEUM	57	2,77,392.84	2,71,066.38	-2.28	5	15,906.29	20,708.86	5- 38
7	POWER	46	3,46,364.58	3,53,015.51	1.92	2	5,991.58	7,854.35	10- 126
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	0- 0
9	RAILWAYS	161	4,62,128.07	6,24,000.70	35.03	61	1,09,934.84	2,16,630.45	2- 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,460.39	2,52,314.59	6.70	5	8,142.83	10,168.72	15- 105
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71- 71
13	URBAN DEVELOPMENT	23	2,83,962.47	3,01,082.00	6.03	2	33,909.00	46,193.00	44- 98
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26- 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		498	19,28,963.01	21,50,676.49	11.49	83	2,36,387.84	3,88,940.68	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	12- 12
3	COAL	30	1,08,556.34	1,13,115.57	4.20	1	17,237.00	17,237.80	8- 8
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	5	24,006.86	30,121.86	25.47	1	15,525.00	21,940.00	74- 74
6	PETROLEUM	57	2,64,239.96	2,71,066.38	2.58	13	49,427.63	66,296.13	5- 110
7	POWER	46	2,81,387.51	3,53,015.51	25.46	16	1,18,692.59	1,77,784.27	10- 155
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	0- 0
9	RAILWAYS	161	3,94,274.15	6,24,000.70	58.27	74	1,21,438.63	2,45,569.12	2- 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,314.59	6.63	6	9,675.45	12,667.72	1- 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	71- 71
13	URBAN DEVELOPMENT	23	2,78,636.14	3,01,082.00	8.06	3	60,314.14	76,888.12	44- 98
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26- 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		498	17,21,591.41	21,50,676.49	24.92	123	4,62,779.78	7,61,317.33	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure

TABLE-32

List of projects added					Rs. 1000 Crore and above		(March 2021)	
			Original		Anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC		
	PETROLEUM							
1	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	1,614.00	8/2023	1,614.00	8/2023		

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2836	
Achieved up to month	1852	

TABLE-34

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above							(March 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>STEEL</u>						
1	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	03/2021	04/2021	1
	<u>PETROLEUM</u>						
2	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	03/2021	05/2021	2
3	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY BPCL	3,313.00	3,288.96	02/2020	03/2021	05/2021	2
4	PARADIP SOMNATHPUR HALDIA PIPELINE IOCL	1,297.50	1,297.50	10/2021	12/2021	03/2022	3
5	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END IOCL	1,378.00	1,378.00	12/2022	09/2022	12/2022	3
6	CITY GAS DISTRIBUTION IN UP AND UK HPCL	3,450.20	3,450.20	03/2029	03/2029	08/2029	5
7	R and D CAMPUS II AT FARIDABAD IOCL	2,281.94	2,281.94	12/2022	12/2022	07/2023	7
8	PARADIP HYDERABAD PIPELINE IOCL	2,321.00	3,338.00	12/2020	06/2021	03/2022	9
	<u>POWER</u>						
9	DARLIPALLI STPP STAGE-I (2X800 MW) NTPC	12,532.44	13,140.91	12/2018	04/2021	05/2021	1
10	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P PGCIL	14,733.37	14,733.37	11/2019	03/2021	04/2021	1
11	EASTERN REGION STRENGTHENING SCHEME- XVIII PGCIL Central Sector Projects	3,500.00	3,994.00	07/2020	04/2021	05/2021	1
12	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	10,566.00	07/2012	04/2021	06/2021	2
13	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR PGCIL	5,070.13	5,070.13	04/2020	03/2021	06/2021	3
14	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN PGCIL Central Sector Projects	1,931.39	1,931.39	02/2020	03/2021	06/2021	3
15	PARBATI HEP (4X200 MW) (NHPC) II NHPC	3,919.59	9,897.59	09/2009	03/2022	07/2022	4

List of projects reporting additional delayed Rs. 1000 Crore and above							(March 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,997.70	11/2020	03/2022	07/2022	4
17	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	1,885.13	12/2018	03/2021	07/2021	4
18	NOKHRA NTPC EPC	1,722.14	1,722.14	09/2021	09/2021	01/2022	4
19	SAMBHU KI BHURJ SOLAR 250 MW NTPC EPC	1,522.71	1,522.71	09/2021	09/2021	01/2022	4
20	SAMBHU KI BHURJ-II SOLAR 300MW NTPC EPC	1,782.00	1,782.00	09/2021	09/2021	01/2022	4
21	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	14,719.10	08/2013	03/2022	08/2022	5
22	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	07/2021	12/2021	5
23	BARH STPP(3X660MW) NTPC NTPC	8,692.97	21,312.11	10/2011	04/2022	07/2023	15
24	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P PGCIL	4,754.42	9,129.32	12/2018	12/2021	03/2024	27
<u>RAILWAYS</u>							
25	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,121.00	N.A.	02/2021	04/2021	2
26	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) WR	829.74	1,959.74	03/2020	12/2023	03/2024	3
27	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I IRCON	3,055.00	3,055.15	09/2018	12/2021	03/2022	3
28	HUBLI- CHIKJAJUR SWR	1,156.94	1,656.00	03/2020	11/2021	03/2023	16
29	HOTGI-KUDGI-GADAG SWR	1,614.59	1,870.41	03/2019	03/2021	03/2024	36
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
30	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	07/2021	08/2021	1
31	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS NHAI	1,016.92	1,071.00	N.A.	07/2021	01/2022	6
32	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	12/2020	08/2021	8

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above (March 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>URBAN DEVELOPMENT</u>						
33	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR NBCC	2,694.00	2,694.00	N.A.	07/2022	12/2022	5
34	DELHI MRTS PHASE-III DMRC	38,585.00	38,585.00	03/2016	03/2021	09/2021	6
	<u>DPIIT</u>						
35	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE IICC	4,773.00	5,178.00	12/2019	10/2021	12/2021	2

TABLE-35

Sector wise analysis of projects Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	59,216.21
CIVIL AVIATION	5	7,613.90	76,13.90	7,703.90	1,318.37
COAL	30	1,08,556.34	1,106,30.02	1,13,115.57	38,525.04
MINES	1	5,540.00	64,35.90	5,540.00	721.87
STEEL	5	24,006.86	304,21.86	30,121.86	22,634.63
PETROLEUM	57	2,64,239.96	2,773,92.84	2,71,066.38	97,672.44
POWER	46	2,81,387.51	3,463,64.58	3,53,015.51	2,47,332.40
HEALTH AND FAMILY WELFARE	4	6,160.00	61,60.00	6,531.00	882.53
RAILWAYS	161	3,94,274.15	4,621,28.07	6,24,000.70	2,12,831.79
ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,364,60.39	2,52,314.59	1,79,385.38
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,814.28
TELECOMMUNICATIONS	1	13,334.00	133,34.00	24,664.00	16,594.00
URBAN DEVELOPMENT	23	2,78,636.14	2,839,62.47	3,01,082.00	1,33,966.75
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	17,025.01
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	906.04
DPIIT	2	17,352.09	173,52.09	18,990.30	11,147.22
Grand total	498	17,21,591.41	19,28,963.01	21,50,676.49	10,41,973.96


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	7	41,080.27	96,339.76	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	1	6,285.33	19,992.43	155 - 155
3	ASSAM	6	27,224.48	29,692.21	9.06	4	4,630.48	7,098.21	2 - 48
4	BIHAR	27	87,426.57	1,21,814.59	39.33	7	29,343.85	54,798.38	15 - 141
5	GUJARAT	24	87,824.17	98,441.87	12.09	6	25,968.21	35,962.79	3 - 74
6	HARYANA	12	16,498.78	18,358.28	11.27	0	0.00	0.00	-
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	1	3,919.59	9,897.59	154 - 154
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	1	2,500.00	27,949.00	241 - 241
9	KARNATAKA	17	53,661.87	62,706.98	16.86	2	27,562.08	32,351.12	36 - 64
10	KERALA	11	32,478.92	37,206.00	14.55	4	7,431.46	9,221.96	32 - 53
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	7	8,906.63	15,736.63	12 - 73
12	MAHARASHTRA	49	1,39,827.20	1,66,044.35	18.75	11	38,100.29	60,109.71	9 - 216
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	108 - 108
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	117 - 117
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	10	25,065.60	32,446.13	15 - 204
18	PUNJAB	4	5,049.00	7,181.59	42.24	0	0.00	0.00	-
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	0	0.00	0.00	-
21	TAMIL NADU	27	99,664.04	1,17,838.13	18.24	6	10,455.67	20,503.84	27 - 145
22	UTTAR PRADESH	48	1,40,935.26	1,47,900.58	4.94	5	29,479.84	31,304.82	8 - 39
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	6	16,254.80	24,199.79	63 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	2	5,992.21	7,178.00	24 - 26
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	5	24,001.00	33,261.43	21 - 74
26	JHARKHAND	16	56,545.31	60,442.40	6.89	1	14,366.58	15,389.42	40 - 40
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	6	19,991.02	22,099.10	10.55	1	10,598.98	10,997.70	20 - 20
29	MULTI STATE	62	3,38,662.43	4,48,460.13	32.42	29	87,656.69	1,42,359.18	5 - 276
Total		498	17,21,591.41	21,50,676.49	24.92	123	4,62,779.78	7,61,317.33	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

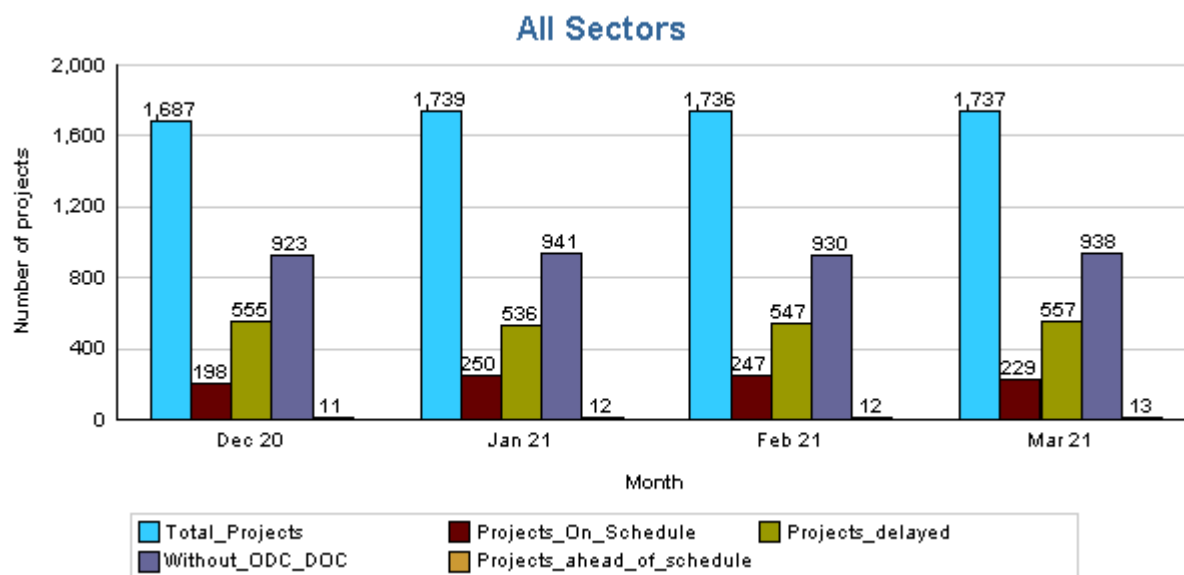

Break-up of 557 Delayed projects in March 2021

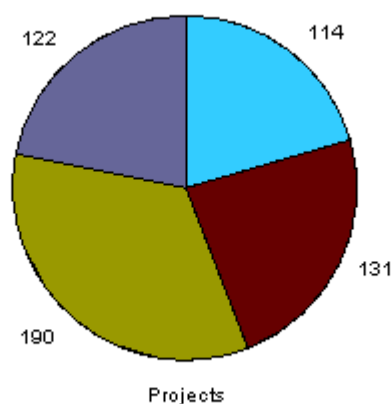


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of RURAL DEVELOPMENT Sector

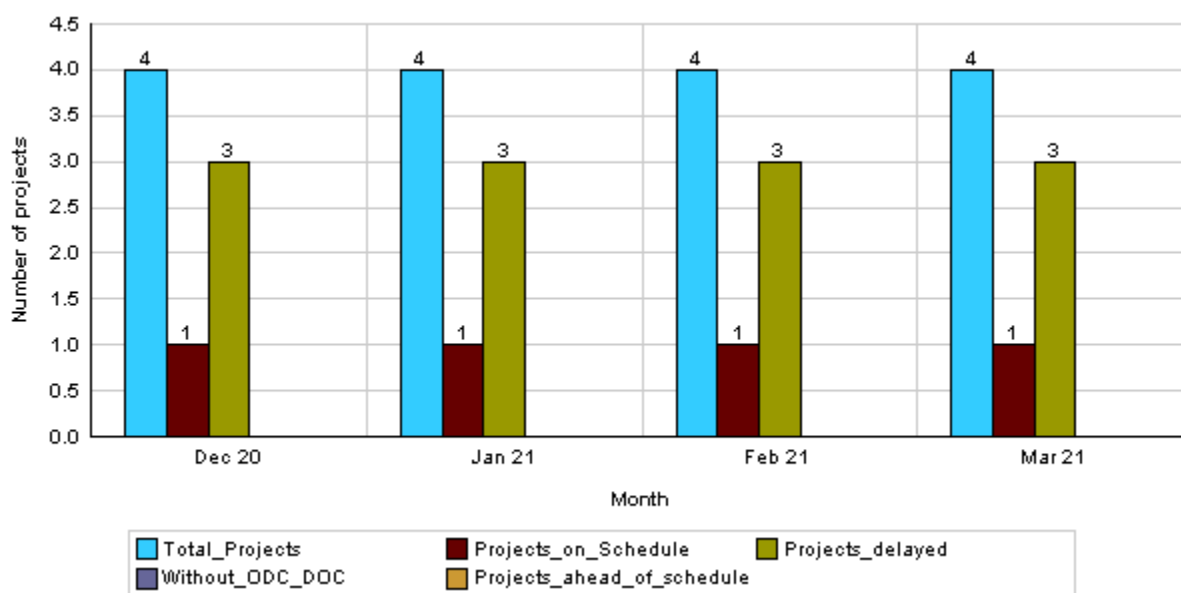

Break-up of 3 Delayed projects in March 2021

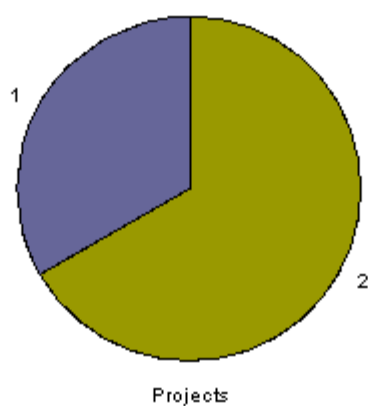


Delay in Months

Legend:

- 1-12 (Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of HOME AFFAIRS Sector

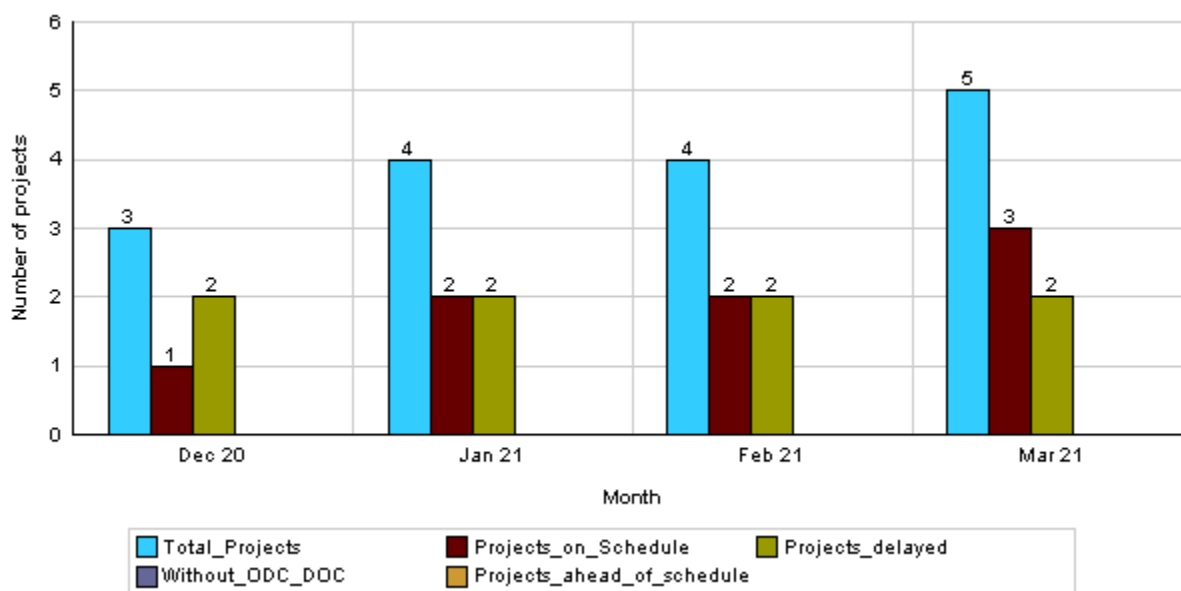


Break-up of 2 Delayed projects in March 2021




Delay in Months

1-12	13-24	25-60	MORE THAN 60
1	1	0	0

Graphical Presentation of HUMAN RESOURCE DEVELOPMENT Sector

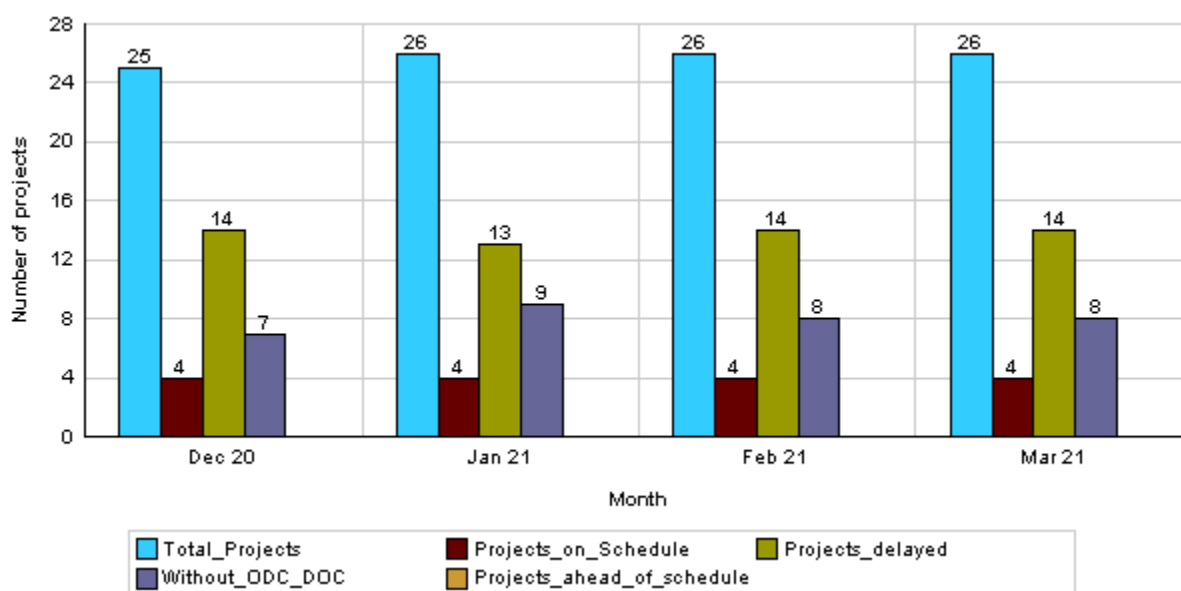


Break-up of 14 Delayed projects in March 2021

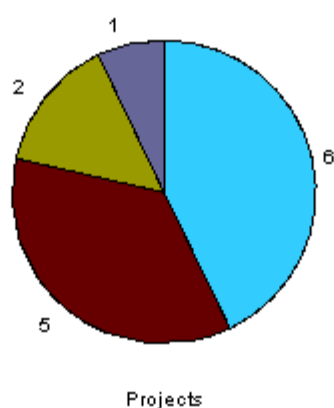


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of WATER RESOURCES Sector

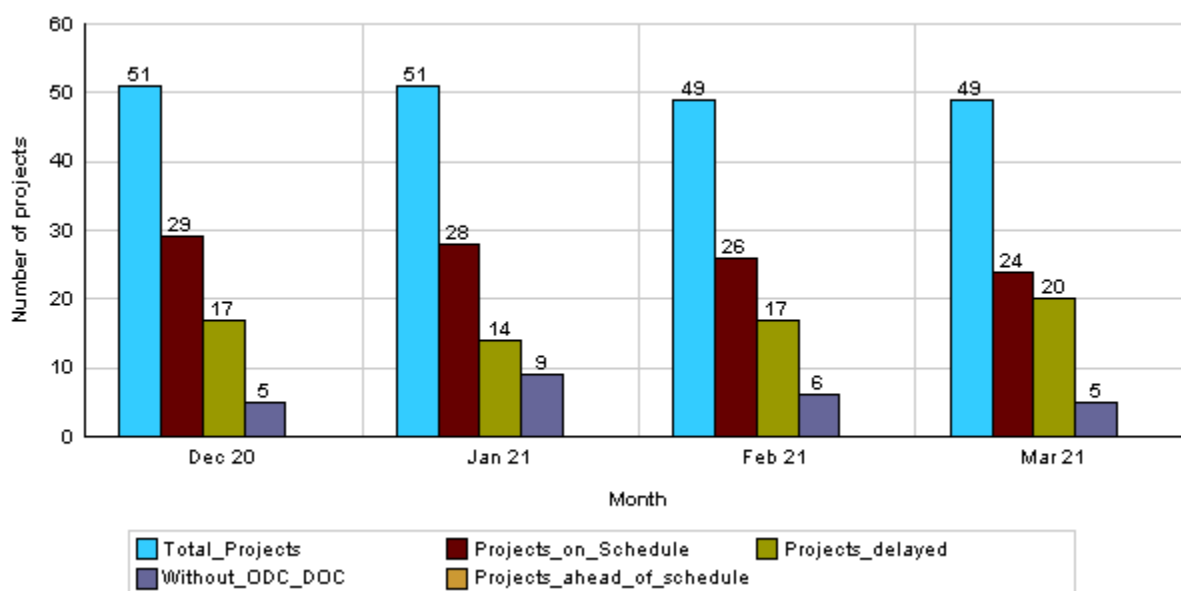


Break-up of 20 Delayed projects in March 2021

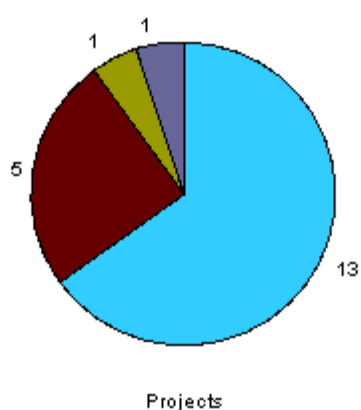


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

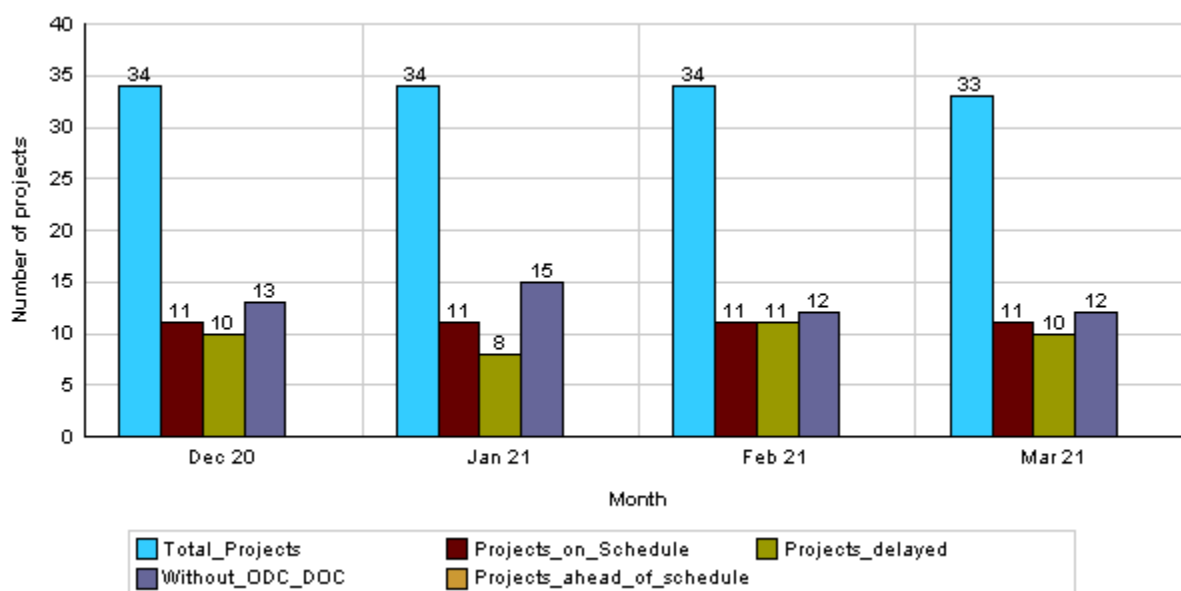


Break-up of 10 Delayed projects in March 2021

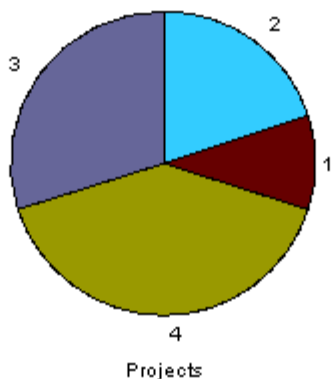


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of TELECOMMUNICATIONS Sector

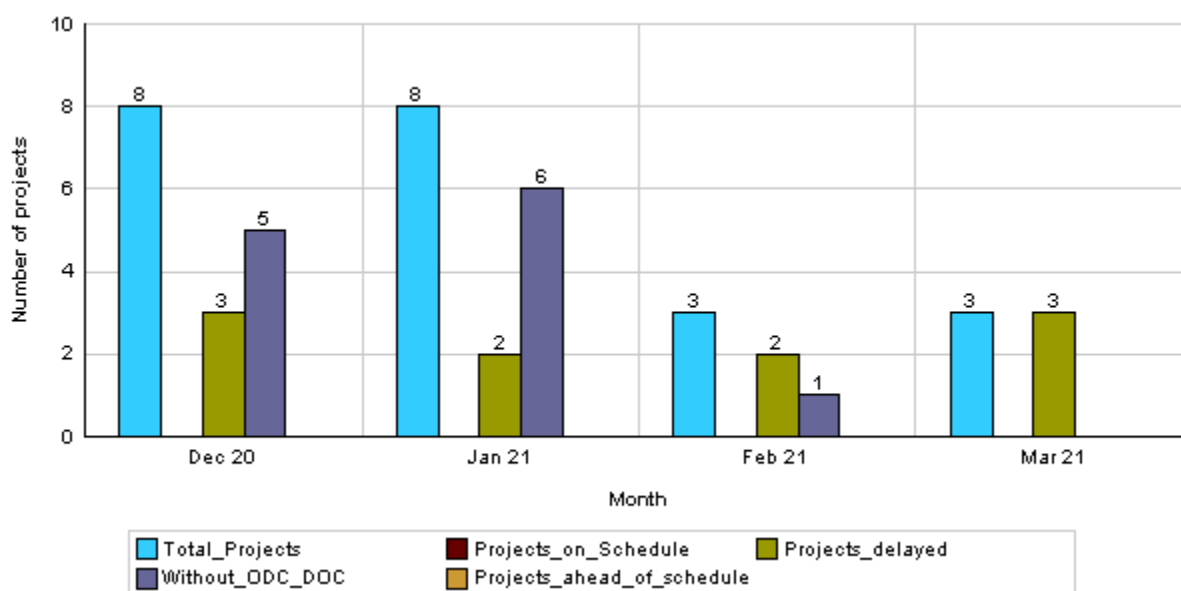

Break-up of 3 Delayed projects in March 2021

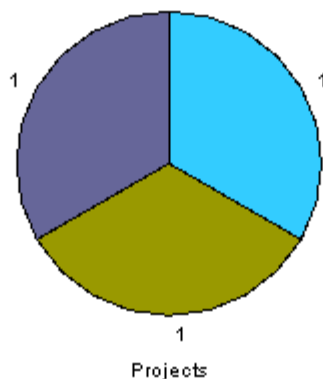


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

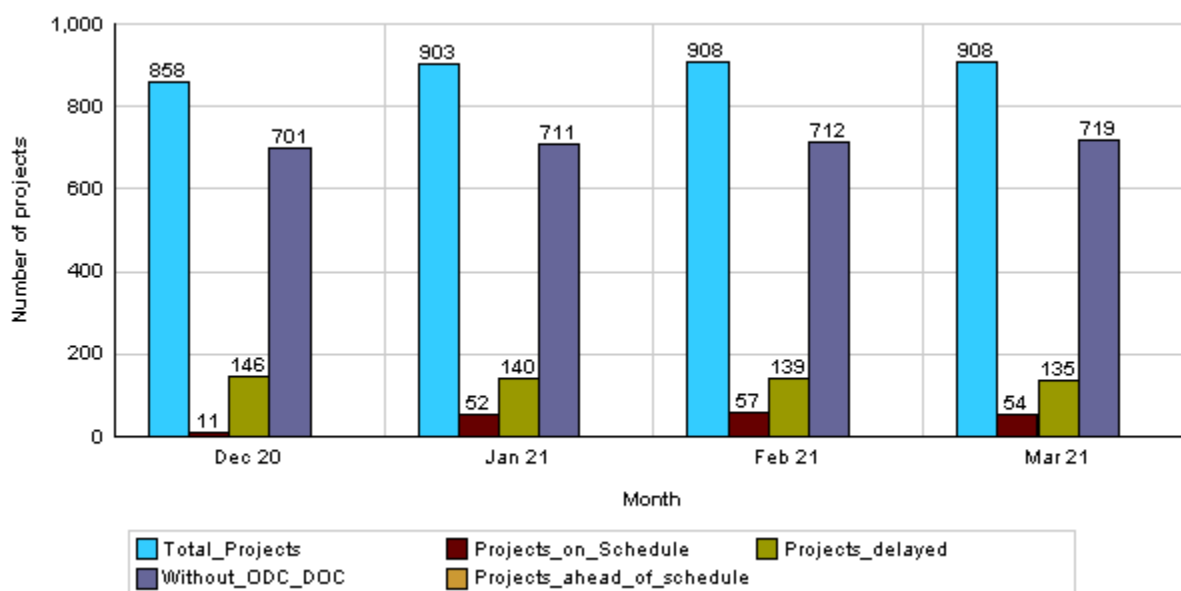


Break-up of 135 Delayed projects in March 2021

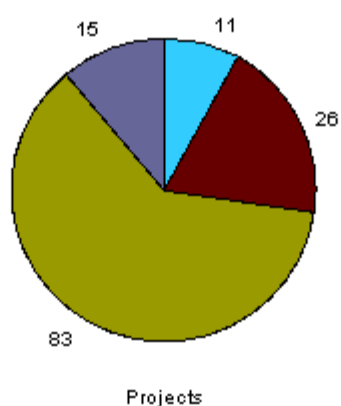


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

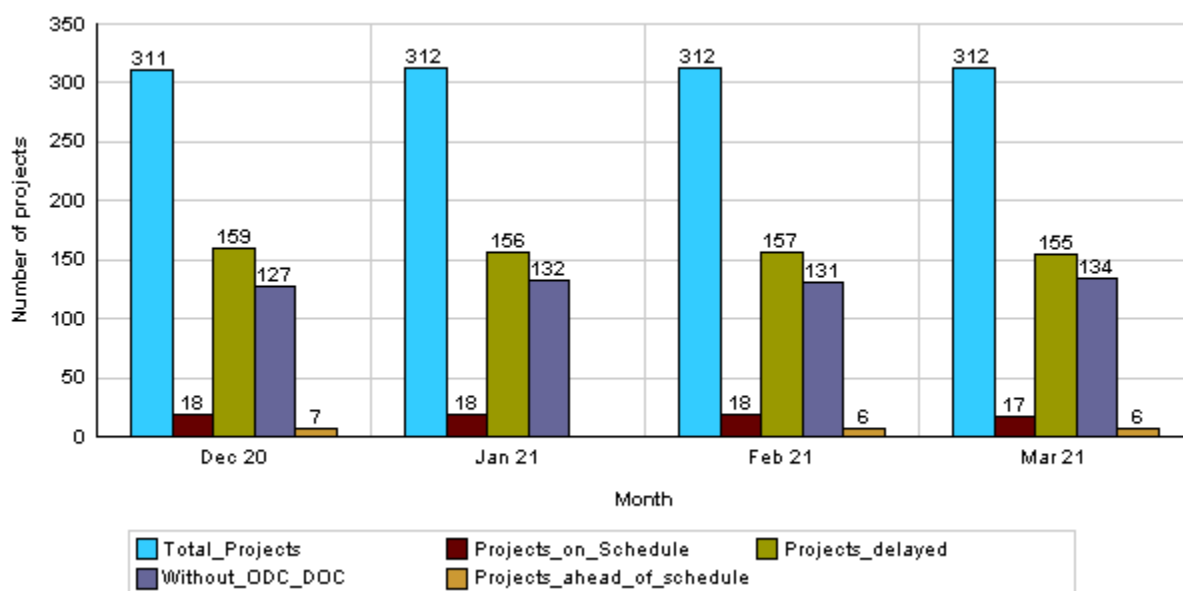


Break-up of 155 Delayed projects in March 2021

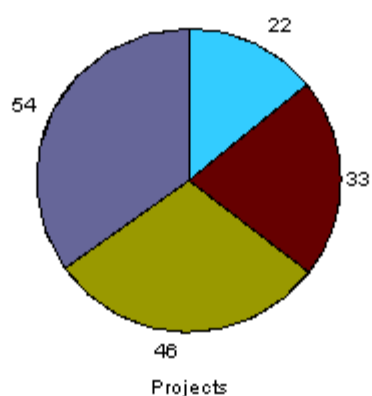


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

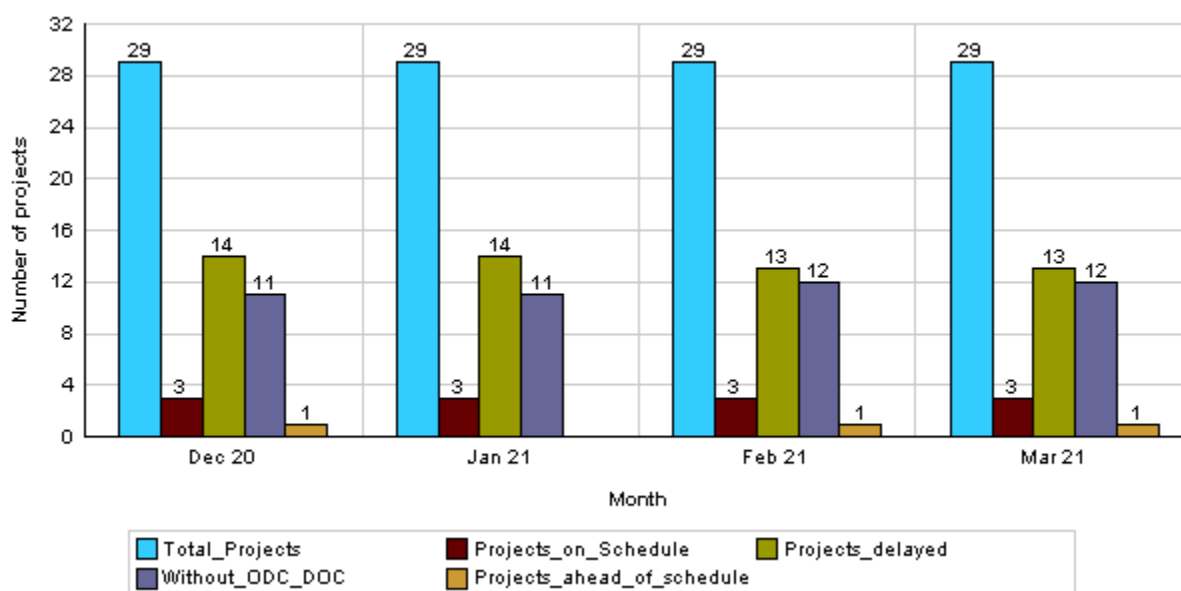


Break-up of 13 Delayed projects in March 2021

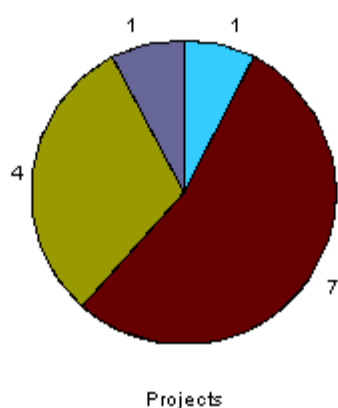


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

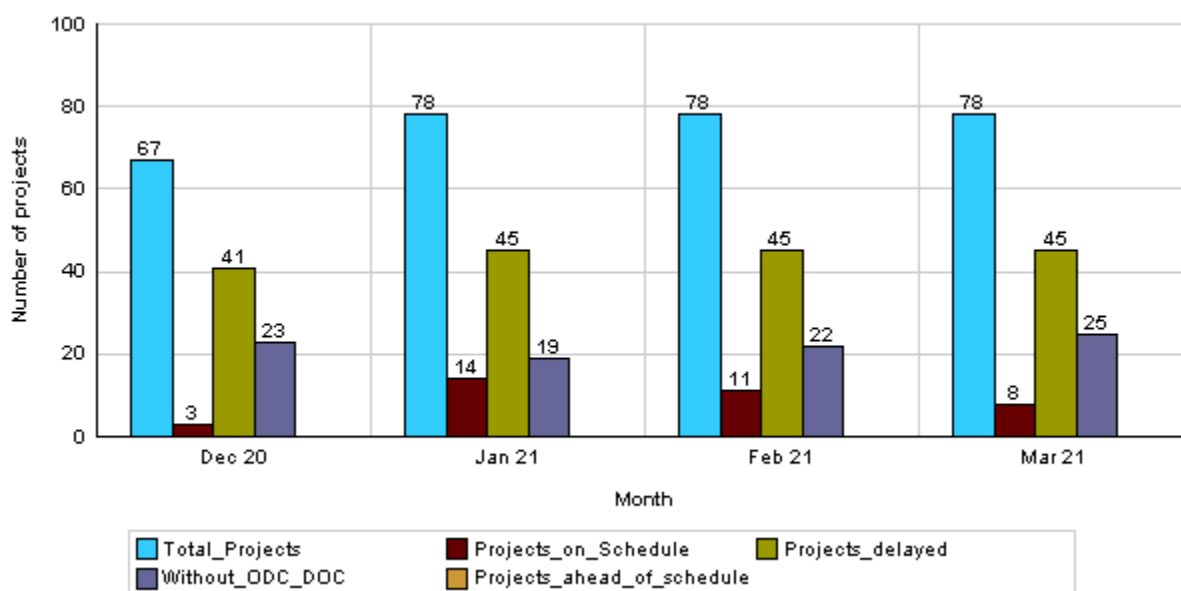


Break-up of 45 Delayed projects in March 2021

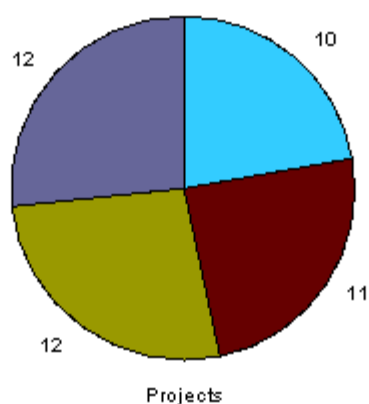


Delay in Months

1-12
 13-24
 25-60
 MORE THAN 60

Graphical Presentation of PETROLEUM Sector

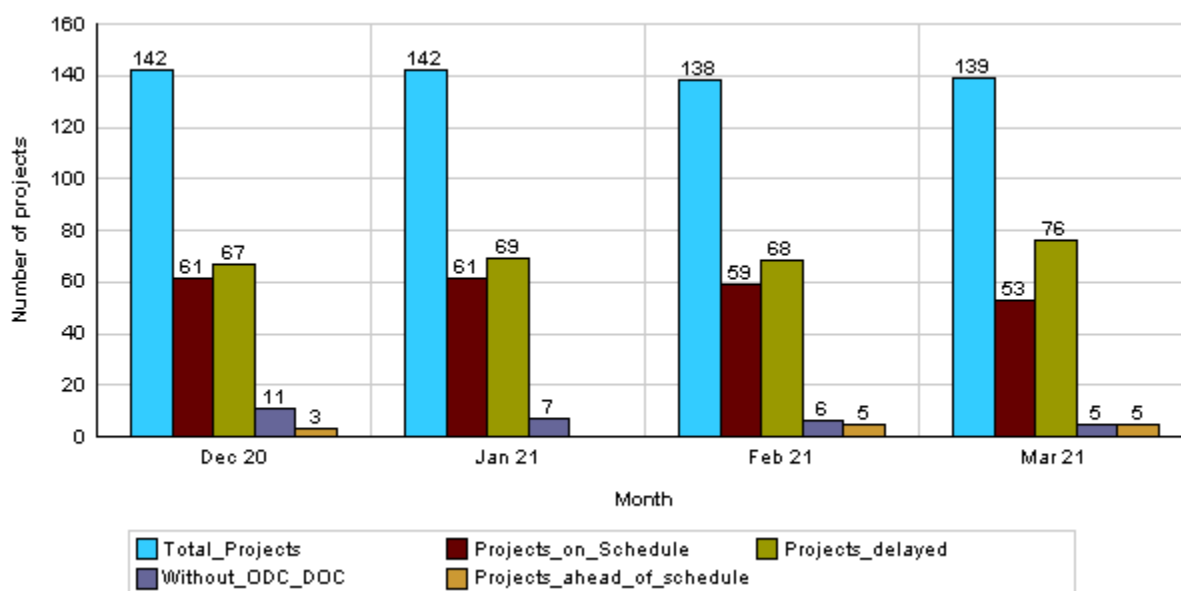


Break-up of 76 Delayed projects in March 2021

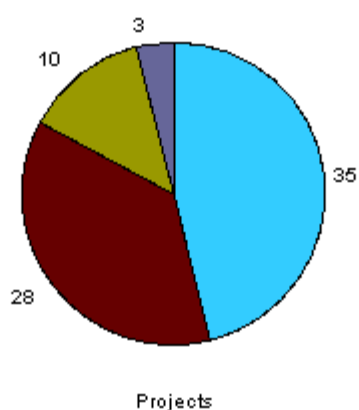


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of STEEL Sector

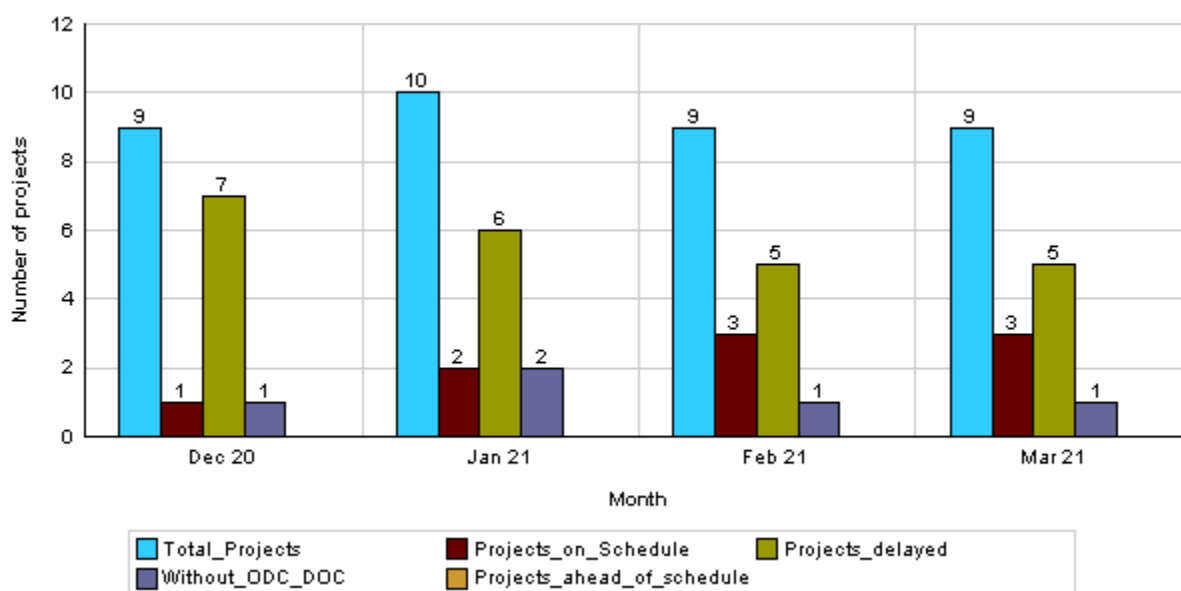


Break-up of 5 Delayed projects in March 2021

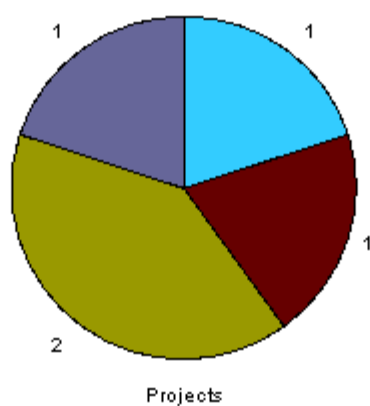


Delay in Months: 1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of MINES Sector

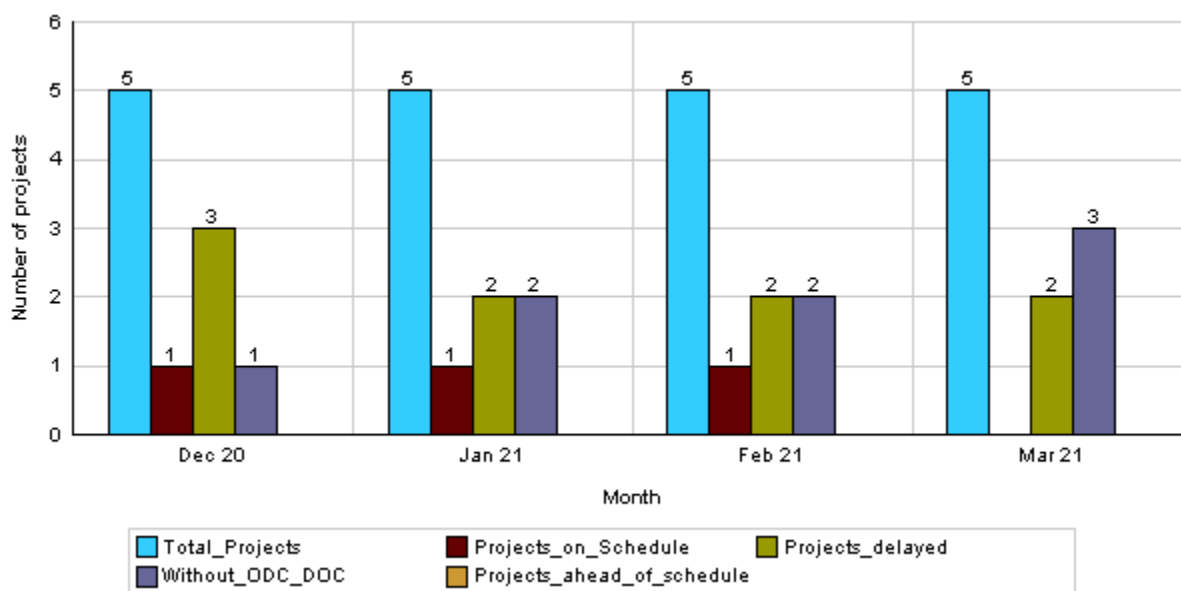


Break-up of 2 Delayed projects in March 2021

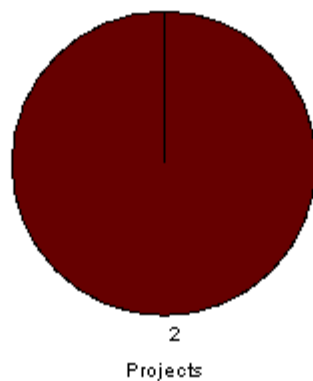


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	0	2	0	0

Graphical Presentation of FERTILISERS Sector

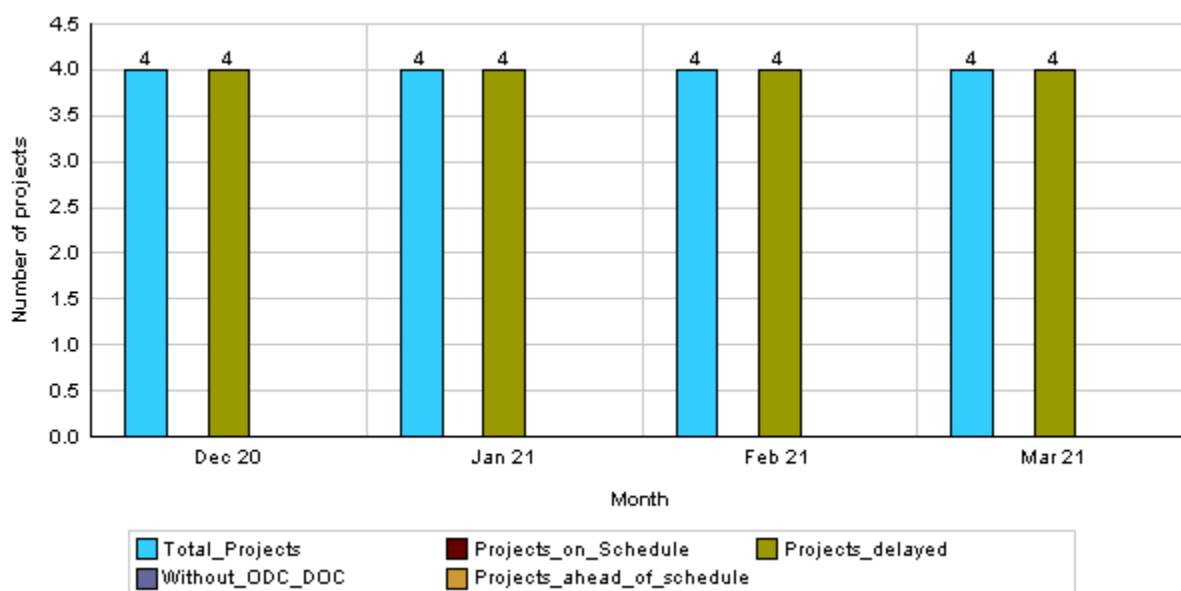


Break-up of 4 Delayed projects in March 2021

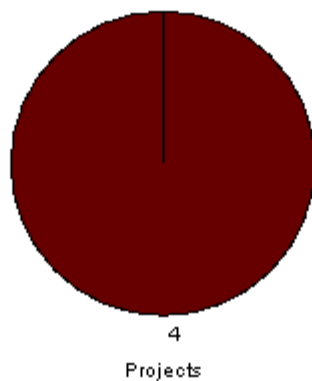


Delay in Months

1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of COAL Sector

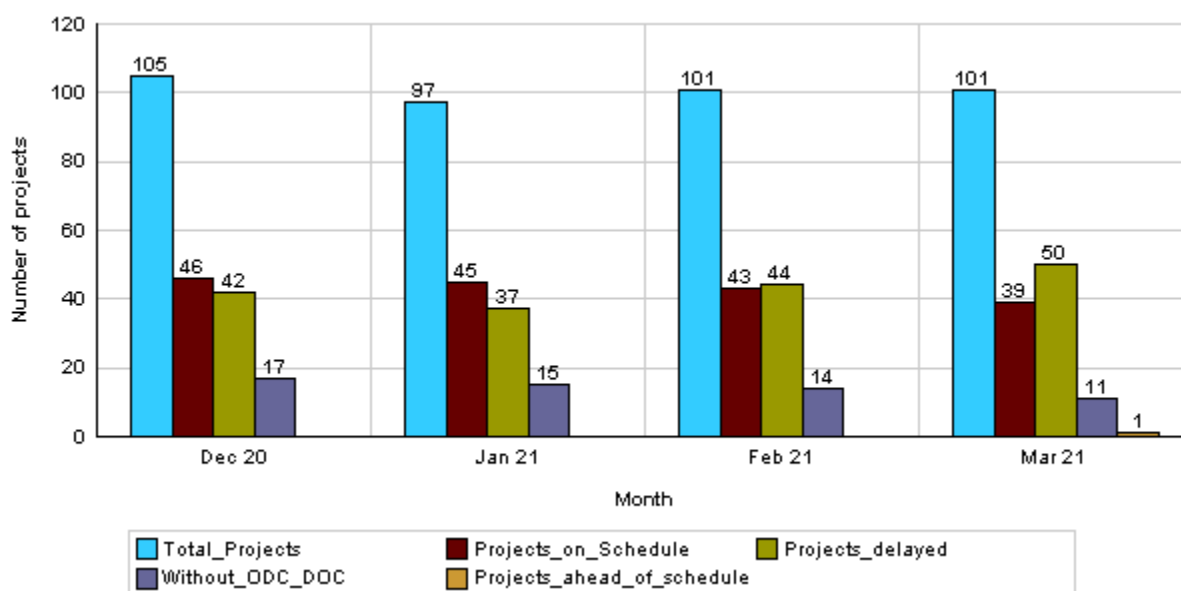


Break-up of 50 Delayed projects in March 2021

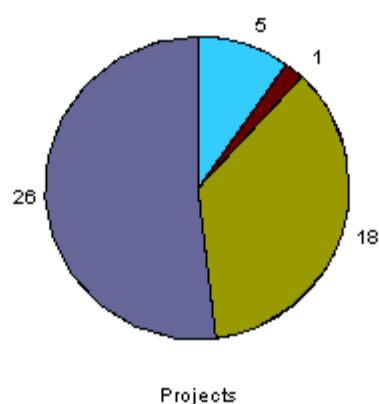


Delay in Months

1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

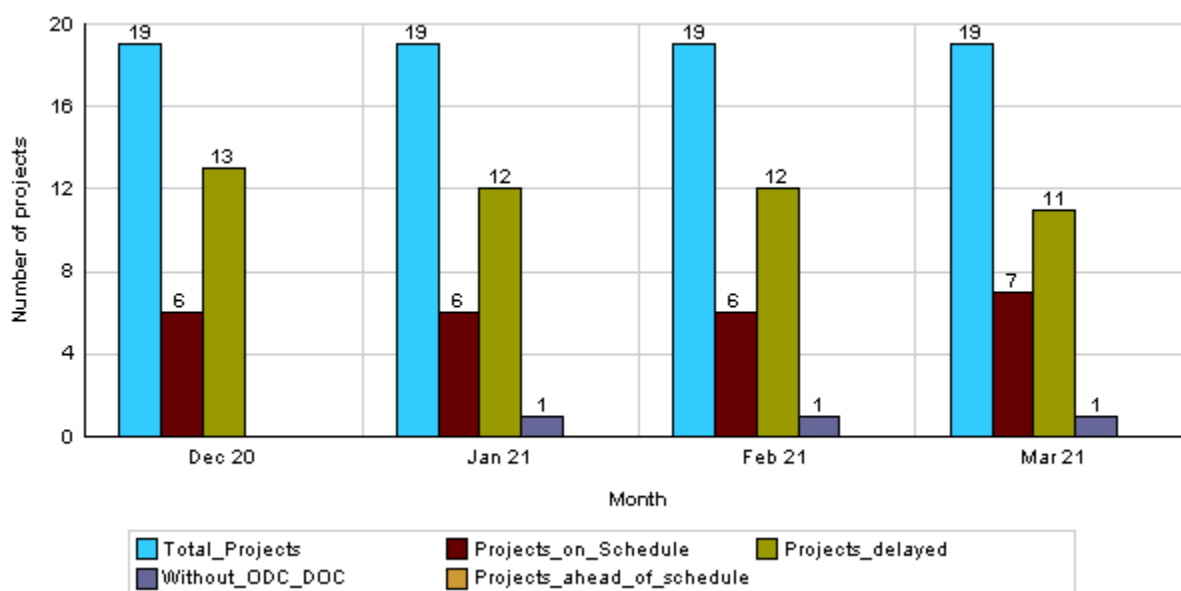


Break-up of 11 Delayed projects in March 2021

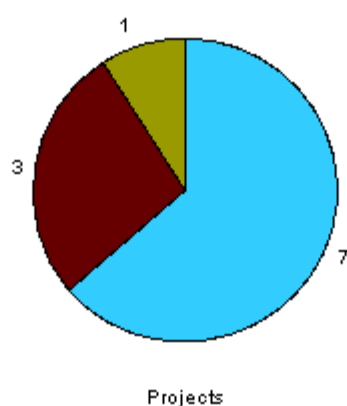


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

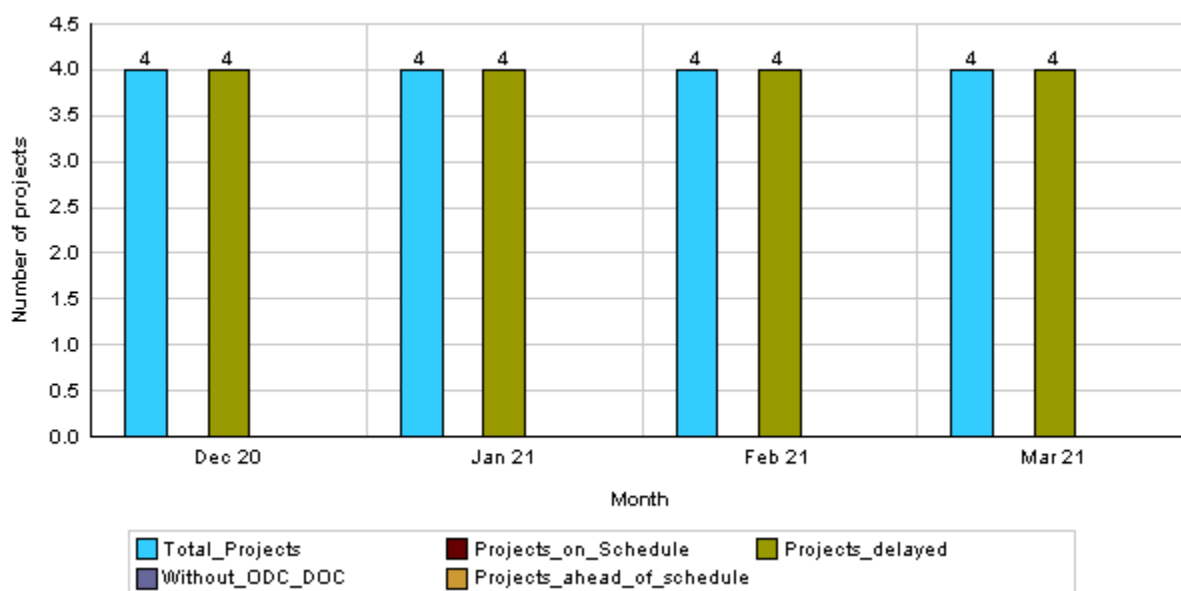

Break-up of 4 Delayed projects in March 2021

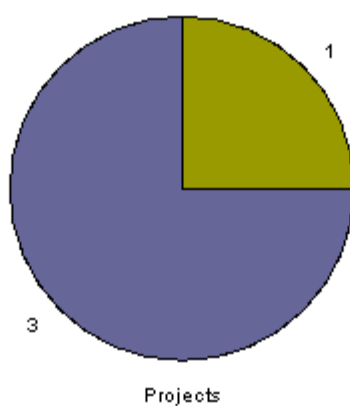

Delay in Months

1-12 13-24 25-60 MORE THAN 60

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	74(O) -	58/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	17,079.00	13,158.00	12/2016 -	03/2023	75(O) -	44/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,840.00	5,922.21	09/2010 09/2016	10/2022	145(O) 0	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	23,648.00	11/2020 -	11/2023	36(O) -	28/76
	Total		67,120.00 -	80,348.00	59,216.21				213/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	33(O) -	0/6
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10 -	177.10	.00	02/2020 -	06/2021	16(O) -	0/4
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80 -	611.80	8.46	03/2023 -	03/2023	0(O) -	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	12(O) -	0/0
9	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022	0(O) -	0/0
10	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAI AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13(O) -	0/0
11	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00 -	1,405.00	199.55	08/2022 -	08/2022	0(O) -	0/0
12	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	346.27 -	480.33	51.11	09/2021 -	09/2021	0(O) -	0/4
13	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24 -	412.24	.00	06/2021 -	06/2021	0(O) -	0/1
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39 -	475.39	88.11	04/2021 -	04/2021	0(O) -	0/1
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7(O) -	0/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5(O) -	0/13
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	.00	03/2022 -	03/2023	12(O) -	0/1
18	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	.00	05/2022 -	05/2022	0(O) -	0/0
19	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	438.28 -	438.28	335.58	06/2019 -	-	-	0/0
20	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12(O) -	0/0
21	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10(O) -	0/1
22	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	135.60	03/2020 12/2021	12/2021	21(O) 6	0/0
23	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	389.71 -	389.71	140.62	11/2021 10/2022	10/2022	11(O) 0	0/2
	Total		13,786.34 -	14,034.50	2,939.03				0/45
	<u>COAL</u>								
24	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	4,268.97	03/2023 03/2016	03/2023	0(O) 0	15/21
25	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,630.04	03/2023 -	03/2023	0(O) -	13/22
26	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	8.28	03/2023 -	03/2023	0(O) -	1/12
27	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	201.48	03/2015 03/2020	03/2022	84(O) 0	9/11
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	6.50	03/2014 -	03/2022	96(O) -	3/9
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	209.24	03/2014 -	03/2021	84(O) -	5/6
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	145.83	03/2022 -	03/2025	36(O) -	4/11
31	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60(O) -	1/7
32	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	130.17	03/2020 -	03/2023	36(O) -	3/6
33	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	9.71	03/2023 -	03/2026	36(O) -	2/12
34	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	2/6
35	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.95	03/2026 -	03/2026	0(O) -	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	28.26	03/2026 -	03/2026	0(O) -	2/4
37	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	3/5
38	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH ,	08/2020	2,309.80 -	2,309.80	276.19	03/2029 -	03/2029	0(O) -	0/0
39	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH ,	05/2020	278.64 -	278.64	182.99	03/2024 -	03/2024	0(O) -	0/0
40	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH ,	12/2020	2,310.12 -	2,310.12	.00	03/2029 -	03/2029	0(O) -	0/0
41	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH ,	12/2020	5,241.40 -	5,241.40	1,931.04	03/2029 -	03/2029	0(O) -	0/0
42	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND ,	08/2008	6,964.33 6,964.33	706.40	706.20	07/2012 03/2025	03/2025	152(O) 0	7/7
43	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	107.27	03/2011 -	03/2022	132(O) -	7/7
44	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	426.30	03/2016 -	03/2022	72(O) -	7/7
45	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	98.21	03/2014 -	03/2022	96(O) -	7/7
46	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	23.47	04/2014 -	04/2023	108(O) -	4/7
47	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	461.54	04/2015 -	03/2022	83(O) -	2/6
48	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND ,	02/2012	4,983.58 4,983.58	4,983.58	245.85	03/2020 03/2024	03/2024	48(O) 0	8/8
49	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2021	0(O) -	0/2
50	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	281.27	05/2014 -	07/2021	86(O) -	0/8
51	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	208.76	04/2014 -	04/2020	-	0/10
52	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	163.16	03/2022 -	03/2022	0(O) -	4/22
53	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	98.11	03/2024 -	03/2024	0(O) -	0/17
54	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	277.47	03/2023 -	03/2023	0(O) -	2/2
55	TETARIAKHAR EXPANSION OCP - [N06000186]CCL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023	0(O) -	1/1
56	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	34.62	08/2022 -	09/2023	13(O) -	5/11
57	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 334.27	334.27	18.35	04/2018 -	06/2022	50(O) -	0/0
58	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	3/10
59	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	100.63	03/2021 04/2024	03/2021	0(O) -	4/10
60	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	64.12	03/2021 -	03/2024	36(O) -	5/9
61	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	1.09	03/2022 -	03/2022	0(O) -	1/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	121.28	03/2021 -	03/2022	12(O) -	4/6
63	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	281.25 -	281.25	20.99	03/2022 -	03/2026	48(O) -	0/0
64	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	622.66	03/2021 -	03/2022	12(O) -	3/9
65	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	152.16	03/2022 -	03/2023	12(O) -	3/9
66	SEMARIA OPENCASST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
67	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
68	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.87	03/2026 -	03/2026	0(O) -	0/7
69	BLOCK-B EXPANSION OPENCASST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	1/7
70	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/8
71	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA ,	11/2014	1,184.33 -	1,184.33	368.56	03/2020 -	03/2027	84(O) -	5/8
72	BHANEAGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	409.68	85.82	03/2023 -	03/2023	0(O) -	7/11
73	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	160.23	03/2019 -	03/2025	72(O) -	10/13
74	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	135.36	03/2020 -	03/2020	-	7/10
75	AMALGAMATED PAUNI-II OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	251.34	03/2021 -	03/2021	0(O) -	3/6
76	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	281.92	03/2025 -	03/2025	0(O) -	7/13
77	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	12(O) -	3/10
78	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA ,	11/2015	313.34 -	313.34	141.08	03/2021 -	03/2024	36(O) -	5/6
79	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA ,	11/2015	851.60 -	826.80	194.28	03/2020 -	03/2026	72(O) -	2/6
80	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	325.18	246.55	03/2019 -	03/2022	36(O) -	4/9
81	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	142.28	03/2019 -	03/2026	84(O) -	5/8
82	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	330.34	03/2020 -	03/2020	-	0/0
83	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	211.41	03/2021 -	03/2021	0(O) -	0/4
84	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	99.77	03/2021 -	03/2021	0(O) -	0/3
85	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	226.81	03/2022 -	03/2021	-12(O) -	0/3
86	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	36(O) -	2/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	274.95	03/2021 -	03/2021	0(O) -	3/6
88	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
89	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168(O) -	11/12
90	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028	180(O) 0	8/10
91	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL,ODISHA ,	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029	228(O) 0	3/5
92	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	168.13	03/2012 -	03/2021	108(O) -	5/7
93	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108(O) -	6/9
94	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60(O) -	3/9
95	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026	0(O) -	7/15
96	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36(O) -	8/10
97	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027	0(O) -	3/12
98	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029	0(O) -	0/9
99	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	854.37	07/2020 -	04/2020	-	18/22
100	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
101	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
102	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	86.85	09/2020 -	-	-	0/0
103	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	140.80	09/2020 -	-	-	0/0
104	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,980.79	7,980.79	7,404.29	12/2015 -	02/2021	-	35/35
105	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	484.65	06/2015 03/2025	03/2025	117(O) 0	5/7
106	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132(O) -	1/2
107	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84(O) -	3/5
108	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	288.72	03/2015 -	03/2022	84(O) -	12/29
109	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	49.77	03/2015 -	03/2022	84(O) -	10/13
110	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	131.63	07/2016 -	03/2022	68(O) -	26/28
111	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	193.00	03/2016 -	03/2021	60(O) -	38/39

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	108.64	03/2019 -	03/2022	36(O) -	17/18
113	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	169.95	03/2019 -	03/2022	36(O) -	6/11
114	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	-	03/2022	-	2/6
115	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	11,452.38	11/2021 07/2022	07/2022	8(O) 0	11/48
116	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	1,210.12 -	1,210.12	24.49	03/2022 03/2029	03/2029	84(O) 0	9/13
117	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	658.63	03/2018 -	03/2021	36(O) -	12/16
118	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	606.30	08/2019 -	-	-	1/19
119	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	1.39	03/2026 -	03/2026	0(O) -	4/22
120	NAKRAKONDA KUMARDI B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	10.11	03/2029 -	03/2029	0(O) -	1/22
121	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.61	03/2027 -	03/2027	0(O) -	1/27
122	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.03	03/2027 -	03/2027	0(O) -	0/22
123	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	.00	03/2025 -	03/2025	0(O) -	0/0
124	2.0 MTPA BHOJUDH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 341.22	341.22	38.59	03/2017 -	03/2022	60(O) -	0/0
	Total		1,45,653.01 -	1,44,210.92	48,349.37				473/989
	<u>FINANCE</u>								
125	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	208.96	205.40	10/2019 -	04/2021	18(O) -	1/6
126	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	113.99	11/2021 -	11/2021	0(O) -	2/8
	Total		557.77 -	557.73	319.39				3/14
	<u>FERTILISERS</u>								
127	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	167.49	11/2019 -	04/2021	17(O) -	0/2
128	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	325.19	04/2020 03/2021	05/2021	13(O) 1	12/14
129	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	187.51	11/2019 -	04/2021	17(O) -	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	186.72	11/2019 -	04/2021	17(O) -	1/2
	Total		1,101.28 -	1,101.28	866.91				14/20
	<u>MINES</u>								
131	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	5,540.00	721.87	04/2021 12/2022	12/2022	20(O) 0	4/4
132	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	359.06	01/2020 -	-	-	2/3
133	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	94.25	11/2020 -	02/2021	-	3/3
134	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.92	04/2021 03/2023	03/2023	23(O) 23	2/2
135	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 06/2021	12/2020	-	1/1
	Total		7,078.62 -	7,075.17	1,311.10				12/13
	<u>STEEL</u>								
136	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,558.00	1,804.98	12/2017 12/2020	12/2020	-	5/6
137	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 21,940.00	21,940.00	18,486.77	05/2015 07/2021	07/2021	74(O) 0	70/86
138	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH ,	11/2020	542.24 -	542.24	31.60	12/2023 -	12/2023	0(O) -	0/0
139	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH , Central Sector Projects	11/2015	2,907.00 -	2,907.00	254.56	06/2023 -	06/2023	0(O) -	0/8
140	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	536.50	10/2017 12/2021	12/2021	50(O) 0	0/2
141	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	185.40	06/2019 05/2021	05/2021	23(O) 0	1/1
142	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	16.12	05/2023 -	05/2023	0(O) -	0/0
143	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,551.82	09/2018 04/2021	04/2021	31(O) 1	5/5
144	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	213.22	09/2020 -	05/2021	8(O) -	1/4
	Total		25,452.51 -	31,567.51	23,080.97				82/112
	<u>PETROLEUM</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
145	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	14,820.60	07/2020 07/2022	07/2022	24(O) 0	93/111
146	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	25,090.00	11,190.15	06/2020 06/2022	06/2022	24(O) 0	15/20
147	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	247.72	04/2021 03/2021	03/2021	-1(O) 0	0/0
148	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	254.90	04/2021 -	07/2021	3(O) -	0/0
149	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	92.80	04/2022 -	02/2023	10(O) -	0/0
150	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	95.40	10/2021 -	10/2021	0(O) -	0/0
151	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	151.16	02/2021 -	05/2021	3(O) -	0/16
152	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	92.33	07/2020 -	07/2021	12(O) -	1/5
153	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	8.95	07/2022 -	07/2022	0(O) -	0/0
154	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH , EPC	10/2020	332.61 -	332.61	.00	11/2022 -	11/2022	0(O) -	0/0
155	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH , EPC	10/2020	303.40 -	303.40	199.11	03/2021 -	03/2021	0(O) -	0/0
156	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH , EPC	10/2020	210.94 -	210.94	117.00	08/2021 -	08/2021	0(O) -	0/0
157	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	502.00	421.03	08/2019 06/2021	06/2021	22(O) 0	6/13
158	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 303.75	303.75	197.20	05/2020 05/2021	05/2021	12(O) 0	4/5
159	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 638.60	652.10	136.05	02/2020 -	04/2021	14(O) -	1/14
160	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	487.25	02/2020 06/2021	06/2021	16(O) 0	5/5
161	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	222.21	144.80	08/2020 -	04/2021	8(O) -	0/0
162	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY - [N16000379]NRL,ASSAM ,	01/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024	0(O) -	0/0
163	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024	0(O) -	0/0
164	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	134.82	03/2021 09/2021	09/2021	6(O) 0	18/26
165	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	34.40	10/2020 08/2022	08/2022	22(O) 6	2/2
166	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	142.34	10/2022 -	10/2022	0(O) -	10/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
167	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]OCL,BIHAR ,	07/2018	189.00 -	189.00	144.29	01/2021 06/2021	06/2021	5(O) 0	6/8
168	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]OCL,BIHAR ,	04/2018	522.00 -	522.00	318.04	03/2021 12/2021	12/2021	9(O) 0	0/0
169	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]OCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	865.95	04/2023 -	04/2023	0(O) -	1/2
170	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]OCL,BIHAR ,	06/2020	403.00 -	403.00	1.77	08/2022 -	08/2022	0(O) -	0/0
171	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	197.30	04/2018 -	06/2021	38(O) -	19/20
172	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	970.30	827.75	03/2026 -	03/2026	0(O) -	7/10
173	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]OCL,GUJARAT ,	10/2017	906.00 -	906.00	272.27	02/2020 10/2021	10/2021	20(O) 0	7/8
174	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]OCL,GUJARAT ,	03/2018	588.20 730.20	730.20	77.30	- 05/2023	05/2023	- 0	11/17
175	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 247.90	247.90	40.10	02/2021 -	12/2021	10(O) -	5/8
176	LAB REVAMP AT GUJARAT REFINERY - [N16000377]OCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	101.64	12/2021 -	12/2021	0(O) -	8/11
177	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]OCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	143.52	05/2023 -	05/2023	0(O) -	3/11
178	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]OCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	24.66	12/2022 -	12/2022	0(O) -	0/0
179	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT ,	02/2020	444.87 -	444.87	87.19	08/2022 -	08/2022	0(O) -	0/0
180	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]OCL,GUJARAT , Central Sector Projects	09/2020	18,936.00 -	18,936.00	685.07	09/2024 -	09/2024	0(O) -	0/0
181	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]OCL,GUJARAT ,	10/2020	1,614.00 -	1,614.00	.00	08/2023 -	08/2023	0(O) -	0/0
182	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 300.00	300.00	269.18	11/2020 06/2021	06/2021	7(O) 0	44/46
183	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]OCL,HARYANA ,	04/2018	206.63 -	206.63	89.71	02/2020 08/2021	08/2021	18(O) 0	5/7
184	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]OCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	710.21	08/2020 04/2022	04/2022	20(O) 0	6/7
185	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]OCL,HARYANA ,	01/2019	909.00 -	909.00	301.41	01/2021 03/2022	03/2022	14(O) 0	2/6
186	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]OCL,HARYANA ,	10/2018	598.00 -	598.00	286.33	02/2020 02/2022	02/2022	24(O) 0	4/5
187	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.01	327.01	181.70	08/2020 05/2021	06/2021	10(O) 1	13/16
188	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]OCL,HARYANA ,	12/2018	278.60 -	278.60	44.73	06/2021 07/2022	07/2022	13(O) 0	1/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 -	2,281.94	431.31	12/2022 07/2023	07/2023	7(O) 7	0/0
190	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	179.69	10/2021 -	10/2021	0(O) -	0/0
191	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	13.16	07/2021 03/2022	03/2022	8(O) 8	0/0
192	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	91.57	09/2026 02/2027	02/2027	5(O) 5	0/0
193	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	667.03	03/2023 03/2022	03/2022	-12(O) 0	6/10
194	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	75.31	06/2020 09/2021	09/2021	15(O) 0	4/12
195	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	109.54	10/2022 -	10/2022	0(O) -	19/19
196	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	106.83	06/2022 -	06/2022	0(O) -	0/0
197	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	92.04	10/2022 -	10/2022	0(O) -	9/9
198	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,607.38	12/2019 04/2021	10/2021	22(O) 0	9/10
199	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 637.00	637.00	466.87	03/2020 11/2020	06/2021	15(O) 0	2/3
200	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	129.96	03/2021 -	05/2021	2(O) -	0/15
201	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	875.03	06/2022 -	06/2022	0(O) -	12/18
202	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	147.24	12/2022 -	12/2022	0(O) -	12/19
203	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	222.20	11/2021 -	11/2021	0(O) -	11/19
204	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 -	200.00	2.09	06/2023 -	06/2023	0(O) -	1/6
205	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 1,236.00	1,236.00	393.38	10/2017 03/2022	03/2022	53(O) 0	42/52
206	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 -	5,245.96	4,977.00	08/2018 11/2019	05/2021	33(O) 2	0/20
207	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 -	3,288.96	2,925.17	02/2020 03/2021	05/2021	15(O) 2	0/20
208	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	725.00	06/2019 -	02/2022	32(O) -	0/0
209	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	377.64	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
210	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL, MADHYA PRADESH ,	08/2017	236.00 293.00	293.00	155.76	06/2020 09/2021	09/2021	15(O) 0	0/0
211	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA ,	03/2011	861.79 1,846.46	1,846.46	1,550.87	05/2013 12/2020	03/2021	94(O) 0	5/8
212	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,775.79	04/2018 05/2021	05/2021	37(O) 0	13/15
213	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL, MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,525.53	02/2022 -	02/2022	0(O) -	5/5
214	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL, MAHARASHTRA ,	04/2013	449.58 -	449.58	396.13	12/2019 03/2021	04/2021	16(O) 1	0/17
215	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA ,	05/2016	212.00 -	212.00	146.57	01/2021 -	04/2021	3(O) -	0/0
216	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA ,	05/2016	348.00 -	348.00	156.30	01/2021 -	10/2021	9(O) -	0/0
217	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL, MAHARASHTRA ,	05/2016	261.00 -	261.00	157.94	01/2021 -	04/2021	3(O) -	0/0
218	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL, MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	4,486.77	03/2020 -	-	-	122/135
219	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC, MAHARASHTRA ,	02/2017	4,006.83 4,475.92	3,596.00	3,507.79	05/2021 05/2021	05/2021	0(O) 0	14/15
220	PUNE POL STORAGE DEPOT - [N16000313]BPCL, MAHARASHTRA ,	08/2016	282.64 -	282.64	246.11	08/2020 -	03/2021	7(O) -	0/15
221	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL, MAHARASHTRA ,	06/2017	249.26 -	249.26	130.48	06/2020 12/2021	09/2021	15(O) 0	3/12
222	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC, MAHARASHTRA ,	02/2019	2,292.46 -	2,203.71	1,595.82	05/2021 -	05/2021	0(O) -	4/6
223	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC, MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	1,005.13	03/2022 05/2023	05/2023	14(O) 0	4/6
224	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC, MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	2,521.33	05/2021 -	05/2021	0(O) -	4/6
225	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC, MAHARASHTRA ,	06/2019	2,494.68 -	2,354.72	1,302.43	03/2022 -	03/2022	0(O) -	4/6
226	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC, MAHARASHTRA ,	05/2019	763.92 -	733.86	637.29	12/2020 05/2021	05/2021	5(O) 0	4/5
227	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA ,	07/2020	640.00 -	640.00	321.21	12/2021 -	12/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
228	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA ,	08/2020	697.00 -	697.00	77.84	03/2023 -	03/2023	0(O) -	0/0
229	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021	48(O) 0	2/15
230	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	3,027.90	1,933.53	03/2021 -	08/2021	5(O) -	5/5
231	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	3,338.00	2,888.48	12/2020 -	03/2022	15(O) -	5/5
232	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	540.76	07/2018 05/2021	05/2021	34(O) 0	27/36
233	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	187.00	10/2020 -	03/2021	5(O) -	6/12
234	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	457.91	12/2019 -	04/2021	16(O) -	6/22
235	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,612.80	12/2020 -	05/2021	5(O) -	21/24
236	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	2,109.70	12/2020 12/2021	06/2021	6(O) 0	20/24
237	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 3,048.00	3,048.00	1,840.50	12/2020 12/2021	12/2021	12(O) 0	19/24
238	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,607.20	12/2012 02/2022	02/2022	110(O) 0	26/42
239	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	3,072.00	2,201.31	06/2021 -	08/2022	14(O) -	18/26
240	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 3,060.00	3,060.00	2,200.60	12/2021 -	12/2021	0(O) -	16/20
241	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	189.70	11/2022 -	11/2022	0(O) -	8/20
242	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	245.60	07/2022 -	07/2022	0(O) -	8/14
243	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	71.90	11/2022 -	11/2022	0(O) -	7/12
244	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	1,022.40	05/2023 -	05/2023	0(O) -	7/29
245	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,263.80	12/2020 12/2021	12/2021	12(O) 0	19/24
246	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	49.54	12/2019 03/2022	03/2022	27(O) 0	18/26
247	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	114.73	07/2022 -	07/2022	0(O) -	10/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
248	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	206.17	12/2021 -	06/2021	-6(O) -	3/3
249	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	77.27	07/2022 -	07/2022	0(O) -	9/9
250	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	2,754.90	10/2021 -	10/2021	0(O) -	7/10
251	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	689.83	10/2021 -	03/2022	5(O) -	1/1
252	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	22.97	09/2021 06/2022	06/2022	9(O) 9	1/5
253	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	1,652.79	08/2021 -	08/2021	0(O) -	7/11
254	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	4.44	09/2022 03/2023	03/2023	6(O) 6	1/8
255	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	08/2019	1,607.00 -	1,607.00	212.84	08/2022 -	08/2022	0(O) -	0/21
256	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	11.85	07/2022 -	07/2022	0(O) -	0/0
257	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	92.44	01/2024 -	01/2024	0(O) -	0/0
258	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL,PUNJAB ,	05/2020	1,421.46 -	1,244.50	68.76	02/2023 -	02/2023	0(O) -	5/22
259	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	81.43	- 05/2022	05/2022	- 0	17/26
260	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
261	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 1,472.00	1,472.00	18.80	02/2017 08/2022	08/2022	66(O) 0	0/0
262	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	624.35	446.72	03/2019 05/2021	05/2021	26(O) 0	4/5
263	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	6,025.00	3,636.76	12/2018 -	02/2022	38(O) -	5/5
264	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	135.89	11/2021 -	11/2021	0(O) -	5/5
265	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,528.75	12/2019 -	01/2021	-	0/0
266	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13(O) -	0/0
267	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	205.98	10/2020 -	08/2021	10(O) -	0/0
268	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL,TAMIL NADU ,	10/2020	921.00 -	921.00	3.05	09/2023 -	09/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
269	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU , EPC	10/2020	1,398.00 -	1,398.00	80.68	12/2023 -	12/2023	0(O) -	0/0
270	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	76.47	04/2022 -	08/2023	16(O) -	0/0
271	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 345.15	345.15	200.10	04/2022 -	04/2022	0(O) -	43/43
272	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	146.91	08/2021 -	11/2021	3(O) -	0/0
273	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	63.74	08/2020 11/2021	11/2021	15(O) 0	1/1
274	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	430.93	08/2022 -	08/2022	0(O) -	3/3
275	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	772.75	12/2021 -	12/2021	0(O) -	0/21
276	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	153.20	03/2029 08/2029	08/2029	5(O) 5	0/0
277	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 -	217.92	86.30	04/2021 -	10/2021	6(O) -	12/14
278	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	93.23	02/2020 06/2021	06/2021	16(O) 0	19/26
279	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	831.40	12/2020 12/2021	12/2021	12(O) 0	13/24
280	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	94.21	04/2020 10/2021	10/2021	18(O) 0	18/26
281	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	1,951.62	09/2022 -	03/2022	-6(O) -	3/3
282	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	14.63	03/2031 08/2029	08/2029	-19(O) -19	0/0
283	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	58.06	01/2023 -	01/2023	0(O) -	0/0
	Total		2,96,976.45 -	3,04,102.14	1,12,387.28				1031/1577
	POWER								
284	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	13,537.76	09/2010 08/2023	08/2023	155(O) 0	0/0
285	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	8,154.50	12/2009 02/2021	02/2021	-	30/30
286	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	18,530.80	10/2011 07/2023	07/2023	141(O) 15	32/48

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
287	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 10,566.00	10,566.00	8,839.26	07/2012 06/2020	06/2021	107(O) 2	13/25
288	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	15,761.92	05/2018 -	12/2021	43(O) -	43/45
289	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	1,998.39	01/2024 -	01/2024	0(O) -	16/27
290	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	-	41/41
291	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	2,369.23	11/2019 -	-	-	0/0
292	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	532.79	05/2017 09/2021	06/2021	49(O) 0	4/9
293	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	240.96	11/2019 -	06/2021	19(O) -	0/0
294	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	122.47	09/2018 11/2020	09/2020	-	0/0
295	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	123.36	06/2019 11/2020	09/2020	-	0/0
296	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT , EPC	08/2020	261.80 -	261.80	.00	10/2021 -	10/2021	0(O) -	0/0
297	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	8,866.70	09/2009 07/2022	07/2022	154(O) 4	3/5
298	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	417.95	01/2026 -	01/2026	0(O) -	0/0
299	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,706.23	04/2020 -	07/2025	63(O) -	0/0
300	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,389.42	11,672.15	06/2019 10/2022	10/2022	40(O) 0	29/30
301	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,380.97	10/2017 -	-	-	0/0
302	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	17,112.00	4,295.79	03/2023 -	09/2024	18(O) -	3/7
303	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 675.73	675.73	463.08	02/2019 02/2021	02/2021	-	0/0
304	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA , EPC	09/2019	403.62 -	403.62	46.03	06/2021 10/2021	10/2021	4(O) 4	0/0
305	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 15,105.22	15,105.22	13,657.43	01/2018 10/2020	02/2021	-	43/43
306	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	-	41/41
307	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	495.34	09/2020 08/2022	08/2022	23(O) 0	10/16
308	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
309	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
310	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,634.56	10/2012 11/2020	03/2021	101(O) 0	8/11
311	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,886.91	08/2013 08/2022	08/2022	108(O) 5	23/26
312	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	590.30	06/2014 -	-	-	10/12
313	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,326.81	04/2016 09/2020	07/2020	-	12/12
314	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	241.68	04/2016 12/2017	06/2021	62(O) 0	0/0
315	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	477.69	11/2016 09/2021	05/2021	54(O) 0	10/12
316	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	3,269.93	03/2018 -	-	-	9/12
317	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 902.49	902.49	648.77	10/2017 05/2021	01/2021	-	5/5
318	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	200.16	07/2017 -	-	-	3/5
319	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	89.76	03/2018 -	06/2021	39(O) -	0/0
320	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	652.14	01/2018 04/2021	04/2021	39(O) 1	0/0
321	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	-	-	0/0
322	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	11,505.07	11/2019 04/2021	04/2021	17(O) 1	0/0
323	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	196.10	11/2019 -	-	-	0/0
324	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 516.12	516.12	417.12	01/2019 09/2020	04/2020	-	0/0
325	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	425.04	04/2019 -	-	-	0/0
326	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	201.10	02/2019 06/2021	06/2021	28(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
327	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	148.70	06/2019 08/2021	05/2021	23(O) 1	0/0
328	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	229.18	12/2019 06/2021	06/2021	18(O) 0	0/0
329	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	4,060.04	04/2020 06/2021	06/2021	14(O) 3	0/0
330	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 9,129.32	9,129.32	2,056.36	12/2018 -	03/2024	63(O) -	0/0
331	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 6,700.00	6,700.00	2,605.89	12/2018 -	12/2021	36(O) -	0/0
332	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,508.04	04/2019 -	-	-	0/0
333	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,994.00	2,868.53	07/2020 12/2020	05/2021	10(O) 1	0/0
334	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,677.06	02/2020 06/2021	06/2021	16(O) 3	0/0
335	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	140.97	09/2019 09/2020	05/2020	-	0/0
336	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	246.14	05/2020 05/2021	04/2021	11(O) 1	0/0
337	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 13,140.91	13,140.91	11,701.78	12/2018 02/2021	05/2021	29(O) 1	40/42
338	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	1,763.69	12/2018 -	07/2021	31(O) -	0/0
339	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN , EPC	01/2020	1,522.71 -	1,522.71	203.13	09/2021 01/2022	01/2022	4(O) 4	0/0
340	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN , EPC	03/2020	1,782.00 -	1,782.00	69.21	09/2021 01/2022	01/2022	4(O) 4	0/0
341	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN , EPC	12/2019	702.28 -	702.28	.00	03/2021 -	03/2021	0(O) -	0/0
342	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN , EPC	03/2020	1,749.31 -	1,749.31	.00	09/2021 -	09/2021	0(O) -	0/0
343	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 219.66	219.66	157.13	07/2019 04/2021	04/2021	21(O) 0	0/0
344	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU , EPC	03/2020	1,316.22 -	1,316.22	.00	09/2021 -	09/2021	0(O) -	0/0
345	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 10,997.70	10,997.70	8,310.67	11/2020 07/2022	07/2022	20(O) 4	27/29
346	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA , EPC	06/2019	401.90 -	401.90	.00	04/2021 -	04/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
347	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,842.02	8,146.60	07/2019 03/2021	03/2021	20(O) 0	42/42
348	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	11,130.00	02/2017 06/2020	01/2021	-	40/40
349	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	1,728.08	09/2023 -	08/2024	11(O) -	1/11
350	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	463.48	09/2020 01/2021	01/2021	-	0/0
351	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	226.00	11/2020 -	04/2021	5(O) -	0/0
352	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH , EPC	03/2020	501.29 -	501.29	49.76	09/2021 01/2022	01/2022	4(O) 4	0/0
353	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH , EPC	01/2020	798.24 -	798.24	31.64	09/2021 01/2022	01/2022	4(O) 4	0/0
354	NOKHRA - [N18000282]NTPC,UTTAR PRADESH , EPC	03/2020	1,722.14 -	1,722.14	103.85	09/2021 01/2022	01/2022	4(O) 4	0/0
355	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,891.26	03/2013 12/2021	12/2022	117(O) 0	8/15
356	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	3,860.35	2,207.95	06/2013 -	12/2023	126(O) -	11/17
357	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	-	0/15
358	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	947.89	569.80	12/2021 -	12/2021	0(O) -	11/32
359	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.54	660.06	09/2019 12/2024	12/2024	63(O) 0	6/10
360	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	343.25	04/2018 03/2021	04/2021	36(O) 1	0/0
361	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 -	529.68	418.49	11/2018 -	07/2021	32(O) -	0/0
	Total		2,95,137.42 -	3,67,699.63	2,55,492.70				615/756
	<u>HEAVY INDUSTRY</u>								
362	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	900.00	815.00	09/2019 -	-	-	0/0
	Total		1,554.00 -	900.00	815.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
363	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	24(O) -	0/0
364	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	382.25	- -	06/2021	- -	0/0
365	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
366	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	331.55	05/2021 -	07/2022	14(O) -	0/0
367	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	499.23	488.22	11/2013 -	05/2021	90(O) -	0/0
368	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	233.39	05/2017 -	03/2021	46(O) -	2/2
369	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	5/5
370	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	190.34	143.04	-	06/2021	-	0/0
371	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	231.05	-	01/2021	-	0/0
372	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	2/2
373	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	682.54	09/2021 -	09/2021	0(O) -	2/4
374	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0
375	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	199.99	09/2023 -	09/2023	0(O) -	0/0
376	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
377	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	.00	09/2025 -	05/2024	-16(O) -	0/0
378	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	43.43	03/2020 -	12/2021	21(O) -	2/7
379	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	256.37	03/2019 -	01/2021	-	0/0
380	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	470.24	-	06/2021	-	0/0
381	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	237.89	05/2018 -	12/2021	43(O) -	0/0
382	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19(O) -	0/33
383	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	37(O) -	1/1
384	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	469.13	06/2020 -	07/2021	13(O) -	0/0
385	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	136.48	03/2020 -	05/2021	14(O) -	1/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
386	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	244.88	- -	03/2021	- -	0/0
387	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	548.39	04/2020 -	07/2021	15(O) -	0/0
388	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC, WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3
389	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
390	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	295.16	03/2019 -	06/2021	27(O) -	0/0
391	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL ,	04/2018	651.99 -	651.99	490.55	- -	06/2021	- -	0/0
	Total		15,273.26 -	15,628.51	7,793.54				18/62
	<u>RAILWAYS</u>								
392	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR, ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
393	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	180(O) -	0/0
394	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
395	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	- -	-	-	1/1
396	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH ,	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	36(O) -	0/1
397	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH ,	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24(O) -	0/0
398	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
399	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	24(O) -	0/0
400	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023	0(O) -	0/0
401	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	665.93	03/2022 03/2024	03/2024	24(O) 0	0/0
402	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH ,	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	36(O) -	0/0
403	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019 -	-	-	0/0
404	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR, ASSAM ,	09/2006	385.20 -	1,043.00	798.53	03/2019 -	03/2023	48(O) -	0/0
405	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM ,	04/2011	314.00 486.96	800.00	799.87	03/2019 -	03/2021	24(O) -	0/0
406	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM ,	04/2015	2,232.32 -	2,950.00	1,496.25	03/2022 -	03/2023	12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
407	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	1,873.21	1,162.39	03/2021 -	05/2021	2(O) -	0/0
408	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	128(O) -	0/0
409	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	614.45	340.21	-	12/2023	-	0/0
410	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.78	1,551.38	-	03/2023	-	0/0
411	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	427.28	03/2020 -	-	-	0/0
412	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
413	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	751.55	683.91	03/2012 -	07/2021	112(O) -	0/0
414	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,132.03	2,145.00	970.88	03/2019 -	03/2024	60(O) -	0/0
415	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	-	-	-	0/0
416	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	-	-	-	0/0
417	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.31	-	-	-	0/0
418	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	-	-	-	0/0
419	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	2.04	-	03/2024	-	0/0
420	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 -	735.20	380.48	-	03/2021	-	0/0
421	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	386.36	-	03/2023	-	0/0
422	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
423	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.74	-	-	-	0/0
424	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	-	-	-	0/0
425	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	-	03/2024	-	0/0
426	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	52.72	-	03/2023	-	0/0
427	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	-	-	-	0/0
428	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	-	-	-	0/0
429	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,470.50	1,085.63	-	03/2023	-	0/0
430	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	36(O) -	0/0
431	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	480.00	485.99	-	-	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
432	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	519.33	278.52	- -	03/2025	- -	0/0
433	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	925.70	03/2020 -	03/2023	36(O) -	0/1
434	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	510.65	03/2020 -	03/2023	36(O) -	1/1
435	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	546.71	541.83	07/2014 -	-	-	0/0
436	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	398.20	03/2021 -	03/2024	36(O) -	0/0
437	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	15(O) -	0/0
438	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	726.31	540.19	- -	-	-	0/0
439	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	1,483.14	1,207.34	- -	03/2022	- -	0/0
440	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 -	1,160.83	902.85	03/2020 -	03/2023	36(O) -	1/1
441	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,294.72	03/2020 -	12/2021	21(O) -	0/0
442	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
443	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,226.51	1,131.91	12/2019 -	-	-	0/0
444	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33(O) -	0/1
445	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21(O) -	0/1
446	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42(O) -	0/1
447	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15(O) -	1/2
448	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	359.00	111.51	- -	03/2024	- -	0/0
449	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	127.91	- -	09/2023	- -	0/0
450	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,959.74	1,959.74	1,799.00	03/2020 03/2024	03/2024	48(O) 3	0/0
451	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 411.62	411.62	126.05	03/2012 03/2023	03/2023	132(O) 0	0/0
452	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	-	0/0
453	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021	0(O) -	0/0
454	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
455	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	186.59	- 03/2024	03/2024	- 0	0/0
456	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48(O) 0	0/0
457	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	3(O) -	0/0
458	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,389.05	1,389.05	1,125.73	03/2021 12/2021	12/2021	9(O) 0	0/0
459	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	653.86	03/2021 12/2022	12/2022	21(O) 0	0/0
460	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
461	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
462	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
463	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
464	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 890.76	890.76	745.11	03/2019 10/2021	10/2021	31(O) 0	0/0
465	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 1,017.91	1,017.91	719.56	03/2020 02/2021	02/2021	-	0/0
466	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	114(O) -	0/0
467	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	316.04	03/2019 -	03/2021	24(O) -	0/0
468	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	6,753.42	926.84	12/2026 -	12/2025	-12(O) -	0/0
469	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	27,949.00	23,132.28	11/2002 -	12/2022	241(O) -	0/0
470	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 -	3,550.00	3,528.48	- -	03/2022	- -	0/0
471	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	1,625.87	767.07	- -	03/2023	- -	0/0
472	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	302.95	12/2018 12/2018	06/2021	30(O) 0	0/0
473	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	195.84	12/2016 -	08/2020	-	0/0
474	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	748.34	03/2021 03/2021	12/2023	33(O) 0	0/0
475	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	340.60	03/2021 -	03/2022	12(O) -	0/0
476	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
477	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
478	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,967.00	71.56	- -	12/2023	- -	0/0
479	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	312.23	03/2016 -	12/2023	93(O) -	1/1
480	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	558.00	.00	- -	12/2023	- -	0/0
481	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
482	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	- -	12/2023	- -	0/0
483	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022	-3(O) -	0/1
484	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	12/2023	- -	0/0
485	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	304.83	12/2018 -	06/2025	78(O) -	0/0
486	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	327.25	.00	- -	12/2023	- -	0/0
487	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	35.29	03/2016 -	12/2023	93(O) -	0/0
488	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023	36(O) 16	1/5
489	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021	15(O) 3	1/2
490	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	998.00	463.45	03/2017 03/2025	03/2025	96(O) 0	0/0
491	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	262.68	- -	-	-	0/0
492	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	369.55	8.50	- -	-	-	0/0
493	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	275.21	6.73	- -	-	-	0/0
494	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	198.81	- -	-	-	0/0
495	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,246.00	.81	- -	-	-	0/0
496	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
497	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,229.79	03/2021 03/2029	03/2023	24(O) 0	4/15
498	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,413.76	1,416.77	- -	-	-	0/0
499	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 5,912.40	5,912.40	2,161.74	03/2022 03/2024	03/2024	24(O) 0	0/0
500	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,762.94	1,153.73	03/2020 -	03/2023	36(O) -	1/1
501	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	12(O) -	0/0
502	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12(O) -	0/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
503	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	296.52	03/2022 -	03/2023	12(O) -	1/1
504	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	172.08	03/2019 -	-	-	0/0
505	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34(O) -	0/1
506	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24(O) -	0/0
507	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	254.73	06/2020 03/2023	03/2023	33(O) 0	0/0
508	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216(O) -	0/0
509	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24(O) -	0/0
510	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84(O) -	0/0
511	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
512	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023	0(O) -	0/0
513	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24(O) -	0/0
514	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 -	315.00	312.62	03/2019 -	03/2020	-	0/0
515	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24(O) -	0/0
516	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
517	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
518	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	-	-	0/0
519	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12(O) -	0/0
520	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12(O) -	0/0
521	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,204.21	03/2024 -	03/2023	-12(O) -	0/0
522	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023	0(O) -	0/0
523	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24(O) -	0/0
524	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12(O) -	0/0
525	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	21(O) -	0/0
526	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
527	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	9(O) -	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
528	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	269.73	03/2019 12/2020	12/2020	-	0/0
529	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
530	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
531	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36(O) -	0/1
532	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	12,264.15	10,842.65	03/2011 -	12/2023	153(O) -	0/0
533	NEW BG LINE FROM BYRNHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	4,083.02	263.68	03/2021 -	03/2021	0(O) -	0/0
534	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 5,021.45	5,521.45	3,838.64	03/2014 -	03/2023	108(O) -	0/0
535	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12(O) -	0/1
536	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140(O) -	0/0
537	MUNEERABAD-MAHABOBNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	276(O) -	0/0
538	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202(O) -	0/9
539	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	4,541.38	3,683.54	12/2008 -	04/2021	148(O) -	0/0
540	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.94	02/2013 -	03/2024	133(O) -	0/0
541	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
542	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	112.02	12/2021 -	12/2021	0(O) -	0/0
543	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	37(O) -	0/0
544	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	907.54	03/2022 03/2023	03/2023	12(O) 0	0/0
545	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	866.42	03/2022 03/2023	03/2023	12(O) -24	0/0
546	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	186.12	- -	-	-	0/1
547	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33(O) -	0/3
548	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
549	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
550	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.55	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
551	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 2,042.51	2,042.51	83.64	03/2019 -	03/2024	60(O) -	0/0
552	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	1,205.00	2.28	- 03/2024	03/2024	- 0	0/0
553	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	439.49	- -	12/2021	- -	0/0
554	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	73.97	03/2020 -	-	-	0/0
555	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	287.09	- -	12/2021	- -	0/0
556	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	1,040.00	155.65	03/2020 -	-	-	0/0
557	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
558	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	105(O) -	0/0
559	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228(O) -	0/0
560	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
561	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	11.43	- -	03/2025	- -	0/0
562	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	373.47	03/2022 -	03/2025	36(O) -	0/0
563	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	502.48	427.64	- -	03/2021	- -	0/0
564	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	565.00	539.40	- -	05/2019	-	0/0
565	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	643.11	03/2016 -	03/2025	108(O) -	0/0
566	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	103.64	03/2017 -	03/2025	96(O) -	0/0
567	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.43	- -	03/2025	- -	0/0
568	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	186.14	03/2016 -	03/2025	108(O) -	0/0
569	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	439.30	385.60	03/2017 -	03/2025	96(O) -	0/0
570	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
571	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.11	- -	03/2025	- -	0/0
572	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
573	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	663.13	520.48	03/2020 -	03/2021	12(O) -	0/0
574	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	495.10	284.21	- -	03/2022	- -	0/0
575	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
576	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
577	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
578	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
579	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	164.05	02/2012 -	03/2025	157(O) -	0/0
580	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	106.75	03/2014 -	03/2025	132(O) -	0/0
581	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
582	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	12(O) -	0/0
583	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 791.39	791.39	572.99	- -	03/2023	- -	0/0
584	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	296.10	.01	- -	12/2023	- -	0/0
585	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,432.50	1,127.71	- -	03/2025	- -	2/2
586	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 -	927.94	534.34	03/2020 03/2022	06/2021	15(O) 0	1/1
587	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	156(O) -	1/1
588	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	360.96	- -	03/2024	- -	0/0
589	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	701.81	207.09	03/2020 -	04/2022	25(O) -	0/0
590	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	15(O) -	0/0
591	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 03/2024	03/2024	60(O) 36	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
592	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	929.86	819.61	03/2019 -	05/2021	26(O) -	0/38
593	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
594	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,416.78	03/2021 -	03/2024	36(O) -	0/0
595	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
596	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	12,039.69	12/2023 -	12/2023	0(O) -	0/0
597	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	-	0/0
598	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 1,540.13	1,540.13	242.09	03/2023 03/2025	03/2025	24(O) 0	0/0
599	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	63(O) -	0/0
600	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	6,911.00	1,148.65	03/2015 -	12/2024	117(O) -	0/0
601	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
602	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,493.80	03/2009 03/2026	03/2026	204(O) 0	0/0
603	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	-	0/0
604	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88(O) -	0/0
605	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	-	1/1
606	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	864.71	06/2021 03/2025	03/2025	45(O) 0	0/0
607	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
608	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	34(O) -	0/0
609	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	223.65	10/2020 03/2024	03/2024	41(O) 0	0/0
610	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 238.03	238.03	221.37	03/2020 03/2021	03/2022	24(O) 0	0/0
611	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	635.77	03/2022 03/2023	03/2023	12(O) 0	0/0
612	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	432.17	03/2022 03/2026	03/2026	48(O) 0	0/0
613	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	64(O) -	0/0
614	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	610.79	12/2018 03/2024	03/2024	63(O) 0	0/0
615	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	901.11	03/2020 03/2020	12/2021	21(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
616	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	24(O) -	0/0
617	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	21(O) -	0/0
618	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39(O) -	0/0
619	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48(O) -	0/0
620	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
621	MANSA-BHATINDA (PHASE-I) INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB ,	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108(O) -	0/0
622	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	860.41	699.06	02/2019 -	11/2021	33(O) -	0/0
623	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	395.00	340.45	12/2019 -	02/2021	-	0/0
624	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	350.45	253.81	10/2018 -	-	-	0/0
625	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.00	.00	- -	-	-	0/1
626	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
627	MAVLI JUNCTION-BARI SADRI MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	480.00	313.18	03/2020 -	06/2021	15(O) -	0/0
628	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	375.00	345.38	11/2019 -	03/2021	16(O) -	0/0
629	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	525.00	463.25	02/2019 -	02/2020	-	0/0
630	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.60	- -	-	-	0/0
631	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	464.53	03/2018 -	-	-	0/0
632	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	184.11	08/2022 -	06/2022	-2(O) -	0/0
633	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	-	-	0/0
634	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	60(O) -	0/0
635	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102(O) -	1/4
636	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	73(O) -	0/0
637	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	227.40	63.90	- -	-	-	0/0
638	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	582.83	239.11	- -	12/2025	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
639	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	527.37	3.34	02/2019 -	-	-	0/0
640	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	- -	-	-	0/0
641	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	559.95	319.22	- -	03/2024	-	0/0
642	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
643	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	600.30	355.13	- 10/2021	09/2021	- 0	0/0
644	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	1,121.00	906.57	- 02/2021	04/2021	- 2	0/0
645	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	332.00	265.41	04/2014 03/2021	12/2020	-	0/0
646	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198(O) -	0/0
647	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	238.00	153.70	03/2018 -	-	-	0/0
648	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
649	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3(O) -	0/0
650	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27(O) -	0/0
651	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	502.93	03/2010 -	03/2024	168(O) -	1/1
652	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	69(O) -	0/0
653	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
654	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	549.50	03/2021 -	03/2021	0(O) -	3/3
655	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	850.00	705.50	12/2024 -	12/2024	0(O) -	0/0
656	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9(O) -	0/0
657	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24(O) -	2/3
658	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
659	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
660	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
661	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
662	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
663	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
664	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	929.79	03/2022 -	03/2022	0(O) -	0/0
665	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	-	4/6
666	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33(O) -	0/0
667	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	39(O) -	0/0
668	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	887.48	03/2023 -	12/2024	21(O) -	0/0
669	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24(O) -	0/0
670	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,165.22	03/2020 -	03/2024	48(O) -	0/0
671	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	235.00	03/2019 -	03/2022	36(O) -	0/0
672	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	68(O) -	0/0
673	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
674	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
675	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
676	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	476.60	04/2017 -	03/2021	47(O) -	0/0
677	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
678	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	63.70	- -	12/2023	-	0/0
679	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	238.15	01/2022 -	03/2022	2(O) -	0/0
680	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	80.76	12/2019 -	04/2021	16(O) -	0/0
681	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023	0(O) -	0/0
682	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021	0(O) -	0/6
683	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023	0(O) -	0/0
684	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
685	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	204.53	- -	-	-	0/0
686	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	3(O) -	0/0
687	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	275.06	03/2019 -	-	-	0/0
688	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
689	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
690	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	906.05	03/2019 12/2009	03/2025	72(O) 0	0/0
691	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	983.60	12/2010 -	03/2025	171(O) -	7/7
692	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
693	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0
694	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	108(O) -	0/0
695	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	108(O) -	0/0
696	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
697	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- -	03/2025	- -	0/0
698	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	38.20	- -	-	-	0/0
699	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
700	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	241.02	- -	03/2022	- -	0/0
701	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	602.27 -	2,144.78	824.96	12/2021 -	04/2021	-8(O) -	0/0
702	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
703	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL ,	02/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		4,62,095.03 -	7,00,073.54	2,48,327.84				37/139
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
704	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD,ANDHRA PRADESH ,	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6(O) -	3/7
705	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH ,	02/2019	655.34 -	655.34	49.89	06/2020 -	-	-	0/110
706	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH ,	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4(O) -	0/0
707	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52(O) -	2/6
708	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR ,	09/2018	375.00 375.00	375.00	48.46	09/2020 -	11/2022	26(O) -	0/0
709	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD,CHHATTISGARH ,	03/2020	808.62 -	808.62	57.42	07/2022 -	07/2022	0(O) -	0/0
710	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD,GOA ,	05/2019	303.90 -	303.90	16.50	03/2020 -	-	-	0/8
711	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	226.16	11/2014 -	-	-	2/8
712	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	35.88	06/2022 -	06/2022	0(O) -	0/0
713	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR ,	03/2019	329.00 -	329.00	.00	07/2022 -	07/2022	0(O) -	0/0
714	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR ,	01/2018	676.00 -	676.00	.00	04/2023 -	04/2023	0(O) -	0/0
715	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63(O) -	1/6
716	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6(O) -	0/0
717	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	-	-	1/8
718	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15(O) -	0/0
719	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11(O) -	4/14

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
720	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	-	-	0/0
721	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE ,	03/2018	150.00 -	150.00	.00	04/2018 -	-	-	0/0
722	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE ,	08/2018	418.00 -	418.00	110.00	03/2019 -	-	-	0/0
723	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	790.79	149.00	03/2022 -	06/2022	3(O) -	0/5
724	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	350.69	274.98	04/2019 -	04/2021	24(O) -	7/8
725	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	387.83	194.72	05/2020 -	02/2022	21(O) -	2/5
726	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD,PUNJAB ,	10/2019	348.24 -	348.24	15.55	05/2022 -	08/2022	3(O) -	0/7
727	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	20(O) -	3/6
728	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15(O) -	0/0
729	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL , EPC	03/2020	193.83 -	193.83	.45	06/2020 -	-	-	0/0
	Total		11,077.40 -	11,265.83	2,437.07				25/198
	HOME AFFAIRS								
730	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	26(O) -	1/7
731	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]CPWD,DELHI , EPC	06/2019	277.35 -	277.35	5.30	07/2022 -	07/2022	0(O) -	0/0
732	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD,HARYANA , EPC	01/2020	166.98 167.00	166.98	.00	10/2023 -	10/2023	0(O) -	0/0
733	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS 96 - [N45000001]CPWD,HARYANA ,	01/2020	166.98 -	166.98	.29	05/2022 -	05/2022	0(O) -	0/0
734	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 238.00	238.00	171.19	04/2018 12/2021	12/2021	44(O) 0	5/6
	Total		1,993.40 -	2,849.31	1,082.82				6/13

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RURAL DEVELOPMENT</u>								
735	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI ,	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021	0(O) -	0/2
736	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	70(O) -	0/1
737	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	58(O) -	2/5
738	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	175.49	124.87	12/2016 -	12/2021	60(O) -	0/4
	Total		889.43 -	899.87	472.48				2/12
	<u>CULTURE DEVELOPMENT</u>								
739	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	148.33	09/2017 -	03/2021	42(O) -	12/15
	Total		151.33 -	151.33	148.33				12/15
	<u>DPIIT</u>								
740	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI ,	11/2017	4,773.00 -	5,178.00	2,432.15	12/2019 -	12/2021	24(O) -	0/0
741	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE ,	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 01/2014	07/2021	22(O) 0	0/0
	Total		17,352.09 -	18,990.30	11,147.22				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
742	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	26.44	10/2018 -	-	-	0/4
743	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	47.28	12/2017 -	-	-	0/4
744	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	172.78	04/2017 -	-	-	3/4
745	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	39.86	10/2018 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
746	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	24.96	10/2018 -	-	-	1/4
747	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	-	-	0/0
748	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	-	-	0/0
749	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	164.81	07/2019 -	-	-	0/4
750	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
751	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,275.58	05/2014 -	-	-	0/0
752	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
753	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
754	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	225.81	10/2015 03/2021	03/2021	65(O) 0	3/4
755	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
756	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
757	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	1,634.05	11/2018 -	-	-	0/0
758	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
759	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	951.13	03/2020 -	-	-	0/0
760	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	234.49	- -	-	-	0/0
761	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
762	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
763	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
764	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	2,499.00	1,582.36	03/2021 10/2021	04/2021	1(0) 0	2/4
765	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,401.00	- -	09/2021	-	0/0
766	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	567.75	- -	02/2021	-	0/0
767	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	86.83	- -	06/2021	-	0/0
768	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	351.02	- -	-	-	0/0
769	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	355.89	315.57	12/2015 -	-	-	3/3
770	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	214.00	02/2017 06/2021	06/2021	52(0) 0	3/4
771	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	315.42	01/2018 -	-	-	4/4
772	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	214.00	05/2017 07/2021	07/2021	50(0) 0	2/4
773	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	214.00	08/2017 05/2021	08/2019	-	2/4
774	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	293.60	11/2017 04/2021	04/2021	41(0) 0	3/4
775	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	105.72	08/2018 03/2021	03/2021	31(0) 0	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
776	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	136.22	08/2018 -	-	-	2/3
777	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	177.78	08/2018 06/2021	02/2021	-	3/4
778	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	294.12	373.98	07/2018 -	-	-	4/4
779	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	427.08	11/2018 04/2021	01/2021	-	3/4
780	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	476.77	05/2016 08/2021	04/2021	59(O) 0	3/4
781	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	279.86	08/2018 05/2021	05/2021	33(O) 0	3/4
782	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	323.06	01/2017 12/2020	12/2020	-	3/4
783	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	199.35	05/2016 -	-	-	3/4
784	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021	59(O) 0	2/4
785	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	304.42	09/2016 -	-	-	3/4
786	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	264.97	08/2017 -	-	-	3/4
787	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021	44(O) 0	0/4
788	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	288.92	01/2018 -	-	-	1/4
789	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
790	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH , EPC	09/2018	597.67 -	597.67	.00	01/2020 -	-	-	0/0
791	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH , EPC	09/2018	617.41 -	617.41	.00	02/2019 -	-	-	0/0
792	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2019	1,226.88 -	1,226.88	.00	02/2021 -	-	-	0/0
793	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	1,601.10 -	1,601.10	.00	02/2021 -	-	-	0/0
794	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	.00	02/2012 -	-	-	0/0
795	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
796	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	389.45	349.94	05/2012 06/2018	-	-	0/0
797	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	91.25	10/2018 -	09/2018	-	2/4
798	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	400.56	06/2018 -	-	-	2/3
799	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	178.10	- -	-	-	3/4
800	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	184.62	10/2016 -	-	-	3/4
801	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	172.89	- -	-	-	2/4
802	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
803	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60(O) -	1/4
804	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	149.44	04/2017 03/2018	03/2021	47(O) 0	1/4
805	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	252.79	100.63	04/2017 -	-	-	2/4
806	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	263.31	116.97	04/2017 -	-	-	2/4
807	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	252.05	111.22	04/2017 -	-	-	2/4
808	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	51.78	04/2017 -	02/2021	-	1/4
809	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	22.06	04/2017 -	02/2021	-	1/4
810	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	252.05	111.21	04/2017 -	-	-	2/4
811	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
812	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	115.89	- -	-	-	0/0
813	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	376.69	- -	-	-	0/0
814	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	260.57	- -	-	-	0/0
815	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	91.23	- -	-	-	0/0
816	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	81.01	- -	04/2022	- -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
817	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	65.25	- -	04/2022	- -	0/4
818	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	144.19	- 01/2016	01/2019	-	0/4
819	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	134.38	- -	-	-	3/4
820	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
821	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,217.25	- 03/2020	-	-	0/0
822	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	163.66	- -	09/2020	-	0/0
823	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	301.06 -	301.06	.00	04/2022 -	04/2022	0(O) -	0/4
824	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH , EPC	09/2020	353.90 -	353.90	4.21	05/2022 -	05/2022	0(O) -	0/4
825	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	403.68 -	403.68	25.52	02/2020 -	-	-	0/0
826	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	342.55 -	342.55	107.43	02/2020 -	-	-	0/0
827	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	421.48 -	421.48	.00	11/2020 -	-	-	0/0
828	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	543.05 -	543.05	66.14	11/2020 -	-	-	0/0
829	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	486.70 -	486.70	30.34	10/2020 -	-	-	0/0
830	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	560.39 -	560.39	33.61	02/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
831	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	347.78 -	347.78	35.38	09/2020 -	-	-	0/0
832	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	394.27 -	394.27	.00	10/2020 -	-	-	0/0
833	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	450.65 -	450.65	.00	11/2020 -	-	-	0/0
834	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	520.00	612.58	02/2009 -	-	-	0/0
835	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	340.14	325.28	04/2009 -	-	-	0/0
836	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	435.78	427.96	11/2008 -	-	-	0/0
837	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	255.23	251.39	11/2008 -	-	-	0/0
838	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	240.36	03/2008 -	08/2020	-	0/0
839	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	390.72	06/2008 -	09/2019	-	0/0
840	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021	-	0/0
841	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019	-	0/0
842	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	655.17	655.17	07/2009 -	-	-	0/0
843	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	-	0/0
844	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	291.45	05/2018 -	12/2020	-	2/4
845	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	407.30	100.07	06/2018 -	12/2021	42(O) -	0/4
846	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	398.06	145.21	06/2018 -	12/2021	42(O) -	0/4
847	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	350.14	01/2019 -	-	-	2/4
848	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	125.80	11/2018 -	-	-	4/4
849	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	480.74	11/2018 -	-	-	3/4
850	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 390.73	390.73	267.46	05/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
851	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	386.98	02/2011 -	-	-	0/0
852	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	111.16	06/2018 -	-	-	3/4
853	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	303.49	168.19	- -	-	-	2/4
854	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	75.42	12/2018 -	-	-	1/4
855	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	201.60	01/2016 -	04/2021	63(O) -	1/4
856	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	223.50	116.92	01/2016 -	-	-	0/4
857	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	407.11	01/2016 -	-	-	2/3
858	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	887.68	259.50	- -	-	-	1/4
859	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/2018	160.00 -	160.00	70.46	09/2021 -	09/2021	0(O) -	0/0
860	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	-	-	0/0
861	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	273.40	132.79	- -	-	-	0/0
862	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM ,	03/2020	166.94 -	166.94	.00	12/2020 -	-	-	0/0
863	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL,ASSAM , EPC	03/2020	220.20 -	220.20	.00	12/2022 -	12/2022	0(O) -	0/4
864	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM , EPC	08/2020	208.84 -	208.84	.00	04/2022 -	04/2022	0(O) -	0/4
865	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM , EPC	08/2020	278.46 -	278.46	.00	03/2022 -	03/2022	0(O) -	0/4
866	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]NHIDCL,ASSAM , EPC	03/2020	216.49 -	216.49	15.29	03/2022 -	03/2022	0(O) -	0/4
867	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,360.63	02/2013 -	-	-	3/4
868	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
869	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
870	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	555.63	07/2013 -	-	-	2/3
871	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 585.00	591.00	575.99	11/2013 12/2020	01/2021	-	0/0
872	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 -	675.00	253.10	- -	-	-	0/0
873	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	318.64	08/2016 -	-	-	0/0
874	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	343.70	10/2016 -	-	-	0/0
875	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
876	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	343.52	04/2019 -	-	-	0/0
877	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
878	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	-	0/0
879	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	400.60	- -	-	-	1/4
880	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,182.94	186.70	- -	-	-	0/0
881	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	297.27	271.39	04/2019 -	-	-	3/4
882	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR ,	01/1991	478.35 -	478.35	446.62	- -	-	-	0/0
883	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	1,038.56	1,160.00	- -	-	-	3/4
884	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	649.27	712.15	04/2018 -	-	-	4/4
885	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
886	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	238.01	- -	-	-	0/0
887	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
888	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 -	560.70	664.50	07/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
889	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
890	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	95.10	05/2016 -	-	-	0/0
891	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
892	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	289.14	05/2016 -	-	-	0/0
893	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 -	925.87	699.76	10/2016 -	-	-	0/0
894	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
895	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR ,	08/2015	288.24 -	288.24	303.16	11/2015 -	-	-	0/0
896	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	89.69	05/2017 -	-	-	0/0
897	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,504.21	12/2016 -	-	-	0/0
898	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	31.82	03/2020 -	-	-	0/0
899	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14(O) -	0/0
900	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54(O) -	0/0
901	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
902	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	44.46	- -	-	-	0/0
903	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
904	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	38.11	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
905	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	9.02	- -	-	-	0/0
906	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR ,	11/2016	230.34 -	230.34	210.12	10/2019 -	-	-	0/0
907	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	39.82	- -	-	-	0/0
908	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR ,	05/2014	199.98 -	199.98	174.35	08/2016 -	12/2020	-	0/0
909	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	14.94	- -	-	-	0/0
910	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR , EPC	10/2013	649.90 -	649.90	.00	12/2020 -	-	-	0/0
911	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR , EPC	10/2013	446.97 -	446.97	.00	11/2020 -	-	-	0/0
912	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR , EPC	10/2013	464.09 -	464.09	.00	11/2020 -	-	-	0/0
913	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH ,	03/2010	179.89 271.00	271.00	270.91	03/2013 05/2019	-	-	0/0
914	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH ,	12/2010	169.26 299.00	299.00	.00	01/2019 -	-	-	0/0
915	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	200.71	- -	03/2021	-	0/0
916	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.13	12/2015 05/2020	05/2020	-	0/0
917	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	439.27	05/2018 -	-	-	0/0
918	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
919	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	299.11	- -	03/2021	-	0/0
920	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 572.66	572.66	270.56	08/2016 06/2021	06/2021	58(O) 0	0/0
921	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	269.15	06/2017 06/2021	06/2021	48(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
922	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 543.73	544.00	400.38	09/2016 06/2021	06/2021	57(O) 0	0/0
923	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH ,	03/2016	491.52 512.77	491.52	474.52	09/2016 10/2020	10/2020	-	0/0
924	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 731.50	731.50	416.16	10/2016 06/2021	06/2021	56(O) 0	0/0
925	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 435.61	435.61	94.34	07/2016 06/2021	06/2021	59(O) 0	0/0
926	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	273.27	01/2018 03/2021	03/2021	38(O) 0	0/0
927	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	240.11	03/2015 06/2021	06/2021	75(O) 0	0/0
928	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	78.69	05/2019 06/2021	06/2021	25(O) 3	0/0
929	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	272.43	11/2017 06/2021	06/2021	43(O) 3	0/0
930	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	-	-	0/0
931	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
932	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	310.72	- -	-	-	0/4
933	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	91.39	- -	-	-	2/4
934	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	219.47	- -	-	-	3/4
935	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	478.46	- -	-	-	0/0
936	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	336.25	- -	-	-	0/0
937	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	205.20	- -	-	-	0/0
938	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	278.30	05/2020 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
939	KARASWADA TO BAMBOLIM - [N24001005]MORTH,GOA ,	03/2017	852.67 -	852.67	138.14	12/2019 -	-	-	1/4
940	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.89	09/2012 -	-	-	2/3
941	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	-	-	0/0
942	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-	-	3/3
943	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0
944	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	715.10	-	-	-	2/2
945	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	203.40	-	-	-	1/1
946	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	503.45	-	-	-	2/2
947	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	450.54	-	-	-	2/2
948	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	134.77	-	-	-	0/0
949	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	392.00	353.42	-	03/2021	-	0/0
950	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	248.88	-	-	-	0/0
951	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	303.96	-	-	-	0/3
952	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	-	-	-	0/0
953	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	-	3/3
954	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
955	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,449.00	394.36	-	01/2021	-	0/0
956	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,043.00	1,327.65	-	06/2021	-	0/0
957	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	584.17	-	07/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
958	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	37.17	- -	-	-	0/0
959	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	447.81	11/2018 -	-	-	2/4
960	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	288.07	11/2018 -	-	-	3/4
961	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	131.34	05/2019 -	-	-	2/4
962	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	235.26	03/2018 -	-	-	1/4
963	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	128.31	06/2021 -	06/2021	0(O) -	2/4
964	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
965	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-	-	0/0
966	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	507.70	496.22	06/2016 -	-	-	0/0
967	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	537.16	516.32	07/2018 -	-	-	0/0
968	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29(O) -	0/0
969	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	270.65	05/2019 -	-	-	0/0
970	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	813.45	577.21	05/2019 -	-	-	0/0
971	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	597.77	03/2020 05/2021	05/2021	14(O) 0	0/0
972	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	444.49	- 06/2021	12/2020	-	0/0
973	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	169.48	- -	-	-	0/0
974	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	197.30	- -	-	-	0/0
975	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	931.21	268.17	- -	07/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
976	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	213.17	- -	07/2021	- -	0/0
977	REHABILITATION AND UPGRADE TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	117.51	- -	-	-	0/0
978	REHABILITATION AND UPGRADE OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	129.29	- -	-	-	0/0
979	REDESIGNING REHABILITATION AND UPGRADE TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	306.06	- -	-	-	0/0
980	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	178.64	03/2019 -	02/2021	-	0/0
981	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 -	-	-	0/0
982	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	526.09	- 02/2020	-	-	0/0
983	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	501.73	- -	-	-	0/0
984	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	690.88	- -	-	-	0/0
985	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	604.45	- -	-	-	0/0
986	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	659.79	- 01/2020	-	-	0/0
987	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	438.38	- 06/2020	-	-	0/0
988	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	468.24	- 02/2020	-	-	0/0
989	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	567.52	- -	-	-	0/0
990	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-	-	0/0
991	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	697.33	03/2018 -	-	-	0/0
992	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	667.10	02/2019 -	-	-	0/0
993	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	271.06	- -	-	-	0/0
994	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	663.25	- -	-	-	0/0
995	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,160.74	- -	08/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
996	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15(O) -	0/0
997	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	127.42	- -	05/2021	- -	0/0
998	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,107.29	07/2015 -	09/2020	-	0/0
999	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,709.65	06/2015 -	-	-	0/0
1000	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,651.77	07/2013 -	-	-	0/0
1001	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,922.79	06/2014 -	10/2020	-	0/0
1002	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	816.46	06/2019 -	12/2020	-	0/0
1003	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,615.66	12/2018 -	-	-	0/0
1004	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	840.31	- -	01/2021	-	2/3
1005	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	151.80	08/2018 -	-	-	2/4
1006	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	78.40	11/2018 -	-	-	1/4
1007	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	37.58	07/2019 -	-	-	0/0
1008	CONSTRUCTION OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]NHIDCL,JAMMU AND KASHMIR ,	12/2019	2,680.42 -	2,680.42	29.22	12/2023 -	12/2023	0(O) -	0/4
1009	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]NHIDCL,JAMMU AND KASHMIR , EPC	08/2020	6,808.69 -	6,808.69	63.83	09/2026 -	09/2026	0(O) -	0/6
1010	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	228.39 -	228.39	.00	04/2022 -	04/2022	0(O) -	0/4
1011	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	210.79 -	210.79	.00	04/2022 -	04/2022	0(O) -	0/4
1012	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1013	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	1,115.95	975.08	03/2019 -	10/2019	-	0/0
1014	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 486.00	486.00	432.16	- -	-	-	0/0
1015	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	336.60	312.79	08/2018 -	-	-	0/0
1016	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	72.53	- -	-	-	0/0
1017	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	366.61	- -	-	-	0/0
1018	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- -	03/2021	-	0/0
1019	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND ,	03/2018	212.99 -	212.99	155.56	06/2020 -	01/2021	-	0/0
1020	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021	0(O) -	0/4
1021	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	-	-	3/3
1022	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
1023	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
1024	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
1025	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	-	0/0
1026	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,287.50	08/2018 -	-	-	0/0
1027	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	125.51	03/2019 03/2022	03/2022	36(O) 0	0/0
1028	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	-	0/0
1029	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	981.12	04/2020 -	12/2020	-	0/0
1030	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	870.00	336.58	03/2019 01/2021	12/2021	33(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1031	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-	-	0/0
1032	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	-	0/0
1033	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,150.56	03/2020 -	-	-	0/0
1034	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	273.86	- -	-	-	0/0
1035	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	- -	0/0
1036	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,244.98	- -	-	-	0/0
1037	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
1038	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
1039	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0
1040	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
1041	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
1042	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0
1043	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
1044	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
1045	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	325.86	326.88	10/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1046	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
1047	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
1048	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
1049	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
1050	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
1051	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	-	-	0/0
1052	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
1053	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	-	-	0/0
1054	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
1055	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	-	-	0/0
1056	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	-	0/0
1057	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	889.83	- 01/2020	01/2020	-	0/0
1058	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	522.80	06/2018 10/2020	03/2021	33(O) 0	0/0
1059	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	44(O) -	0/0
1060	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1061	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1062	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1063	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1064	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	- 0	0/0
1065	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47(O) -	0/0
1066	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1067	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73(O) -	0/0
1068	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71(O) -	0/0
1069	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 686.13	686.13	669.94	- -	05/2020	-	0/0
1070	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 679.94	691.38	669.35	- -	05/2020	-	0/0
1071	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	439.63	01/2020 01/2021	06/2021	17(O) 3	0/0
1072	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	756.69	02/2020 04/2021	04/2021	14(O) 0	0/0
1073	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	824.83	- -	06/2015	-	0/0
1074	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1075	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1076	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	771.23	- 06/2015	06/2015	-	0/0
1077	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADHYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	375.50	08/2017 06/2021	06/2021	46(O) 0	0/0
1078	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	195.73	01/2019 -	-	-	4/4
1079	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	473.85	10/2017 -	-	-	3/4
1080	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	221.79	09/2017 -	-	-	3/4
1081	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	648.40	09/2017 -	01/2021	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1082	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	224.81	- -	08/2021	- -	3/4
1083	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	738.74	- -	-	-	0/4
1084	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	350.68	- -	07/2018	-	0/0
1085	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	129.98	03/2018 -	06/2021	39(O) -	0/0
1086	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 -	173.41	141.65	08/2018 -	03/2021	31(O) -	0/0
1087	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	46.52	03/2018 -	06/2021	39(O) -	0/0
1088	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH ,	11/2017	235.91 -	235.91	176.23	02/2018 02/2021	02/2021	-	0/0
1089	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	117.94	02/2018 06/2021	06/2021	40(O) 4	0/0
1090	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH ,	03/2018	191.21 -	191.21	127.13	11/2019 -	01/2021	-	0/0
1091	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	123.20	03/2017 -	06/2021	51(O) -	0/0
1092	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	69.34	03/2018 -	09/2021	42(O) -	0/0
1093	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 -	226.88	170.96	08/2018 09/2021	03/2021	31(O) -	0/0
1094	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	158.22	03/2018 -	06/2021	39(O) -	0/0
1095	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	195.13	07/2018 03/2021	04/2021	33(O) 1	0/0
1096	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	06/2021	40(O) 3	0/0
1097	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	06/2021	39(O) 3	0/0
1098	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH ,	09/2016	287.34 -	287.34	194.85	01/2019 09/2020	11/2020	-	0/0
1099	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	197.04	09/2019 06/2021	06/2021	21(O) 0	0/0
1100	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	573.85	07/2018 05/2021	05/2021	34(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1101	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	877.79	687.99	06/2019 04/2021	04/2021	22(O) 0	0/0
1102	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH ,	09/2016	178.23 -	178.23	122.99	09/2018 -	-	-	0/0
1103	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	308.11	06/2019 -	-	-	0/4
1104	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	351.92	03/2018 06/2021	06/2021	39(O) 0	0/0
1105	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	85.70	03/2021 11/2021	11/2021	8(O) 8	0/0
1106	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	263.60	- -	12/2021	- -	1/3
1107	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	76.17	- -	11/2022	- -	0/4
1108	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	425.85	- -	02/2022	- -	1/4
1109	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	193.30	- -	-	-	0/4
1110	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	537.28	12/2019 -	12/2021	24(O) -	2/3
1111	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	333.22	03/2020 -	04/2022	25(O) -	1/3
1112	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	349.24	05/2020 -	05/2022	24(O) -	1/3
1113	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	330.36	03/2020 -	-	-	1/3
1114	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,559.00	03/2013 -	03/2021	96(O) -	0/0
1115	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1116	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	80.00	- -	-	-	0/4
1117	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1118	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	300.50	- -	-	-	3/4
1119	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1120	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1121	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	89.93	- -	-	-	0/0
1122	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1123	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	409.40	05/2018 11/2020	11/2020	-	0/1
1124	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	730.97	642.54	05/2018 06/2021	06/2021	37(O) 0	0/0
1125	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1126	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	690.17	594.57	05/2018 06/2021	06/2021	37(O) 0	0/1
1127	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	209.18	03/2019 12/2021	03/2022	36(O) 3	0/0
1128	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	373.68	05/2018 04/2019	06/2021	37(O) 0	0/1
1129	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0
1130	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	861.99	11/2016 -	-	-	0/0
1131	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	3,443.43	01/2018 -	-	-	0/0
1132	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1133	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	151.11	07/2018 -	-	-	0/0
1134	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	307.08	07/2019 06/2021	12/2021	29(O) 0	0/0
1135	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	318.30	07/2019 06/2021	12/2021	29(O) 0	0/0
1136	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	585.85	- -	-	-	0/0
1137	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	324.00	- -	-	-	0/0
1138	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	921.02	- -	07/2021	- -	3/4
1139	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	296.60	- 01/2022	07/2021	- 0	1/4
1140	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	105.20	03/2019 -	02/2021	-	0/0
1141	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	70.85	03/2019 -	03/2021	24(O) -	0/0
1142	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	315.00	309.40	- -	-	-	0/0
1143	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	251.87	05/2019 -	-	-	0/0
1144	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	855.25	02/2020 -	-	-	0/0
1145	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	63.76	03/2020 -	-	-	0/0
1146	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	-	-	0/0
1147	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	-	0/3
1148	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-	-	3/3
1149	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	11/2020	-	0/0
1150	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1151	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	-	-	0/3
1152	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	448.18	419.23	- -	10/2020	-	0/0
1153	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	440.92	- -	08/2021	- -	0/1
1154	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	591.21	- -	04/2021	- -	2/3
1155	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	150.06	- 08/2021	02/2022	- 0	0/0
1156	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	194.57	- 02/2021	08/2021	- 0	0/0
1157	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	75.68	- -	07/2021	- -	0/0
1158	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	666.56	- -	-	-	0/0
1159	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	160.89	07/2019 -	-	-	0/4
1160	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	49.38	06/2019 -	-	-	0/4
1161	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	197.90	06/2019 -	-	-	0/4
1162	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	173.79	05/2019 -	-	-	0/0
1163	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	311.65	05/2019 -	-	-	0/4
1164	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	230.03	05/2019 -	-	-	0/4
1165	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	353.00	06/2019 -	-	-	0/4
1166	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	215.41	06/2019 -	-	-	0/0
1167	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	258.29	06/2019 -	-	-	0/0
1168	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	228.07	06/2019 -	-	-	0/0
1169	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	321.02	06/2019 -	-	-	0/0
1170	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	152.57	06/2019 -	-	-	3/4
1171	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	273.42	06/2019 -	-	-	0/0
1172	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	253.23	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1173	AMD TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 397.00	396.91	280.56	06/2019 -	-	-	3/4
1174	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 364.00	363.82	26.75	09/2019 -	-	-	1/4
1175	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	224.81	06/2019 -	-	-	0/4
1176	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 -	457.52	352.94	07/2019 -	-	-	2/4
1177	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	268.87	07/2019 -	-	-	3/4
1178	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	49.47	05/2019 -	-	-	1/4
1179	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	58.79	12/2019 -	-	-	1/4
1180	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	104.11	12/2019 -	-	-	0/4
1181	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	218.78	08/2019 -	-	-	2/4
1182	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	264.93	08/2019 -	-	-	2/4
1183	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	162.30	08/2019 -	-	-	2/4
1184	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	227.76	05/2019 -	-	-	0/4
1185	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	293.39	07/2019 -	-	-	2/4
1186	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	252.78	07/2019 -	-	-	2/4
1187	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	270.13	12/2019 -	-	-	0/4
1188	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.10	07/2019 -	-	-	0/0
1189	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	252.45	07/2019 -	-	-	2/4
1190	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	9.66	05/2020 -	-	-	0/4
1191	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	98.05	- -	-	-	0/4
1192	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	250.79	11/2019 -	-	-	2/4
1193	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	125.44	07/2019 -	-	-	2/4
1194	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	219.78	12/2019 -	-	-	0/4
1195	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	112.39	05/2020 -	-	-	0/4
1196	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	317.91	06/2019 -	-	-	0/4
1197	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	198.65	11/2019 -	-	-	0/4
1198	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	128.94	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1199	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	202.34	11/2019 -	-	-	0/0
1200	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	148.53	07/2019 -	-	-	0/0
1201	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	181.55	12/2019 -	-	-	0/4
1202	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	86.72	12/2019 -	-	-	0/4
1203	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	146.39	12/2019 -	-	-	0/4
1204	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	155.57	12/2019 -	-	-	0/4
1205	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	154.48	06/2019 -	-	-	0/4
1206	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	116.30	11/2019 -	-	-	0/4
1207	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	208.63	07/2019 -	-	-	0/4
1208	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	278.82	07/2019 -	-	-	0/0
1209	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	108.68	06/2019 -	-	-	0/4
1210	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	255.47	12/2019 -	-	-	0/4
1211	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	97.86	12/2019 -	-	-	0/4
1212	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	125.23	12/2019 -	-	-	0/4
1213	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	97.66	12/2019 -	-	-	0/4
1214	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	142.66	12/2019 -	-	-	0/4
1215	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	99.17	02/2020 -	-	-	0/4
1216	DHANGRIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	131.55	02/2020 -	-	-	0/4
1217	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	139.93	12/2019 -	-	-	0/4
1218	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	345.00	12/2019 -	-	-	0/4
1219	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	218.03	12/2019 -	-	-	0/4
1220	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	149.54	12/2019 -	-	-	1/4
1221	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	456.93	09/2019 -	-	-	1/4
1222	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	132.40	12/2019 -	-	-	2/4
1223	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	66.25	08/2020 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1224	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	138.50	12/2019 -	-	-	0/4
1225	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	152.42	08/2020 -	-	-	0/0
1226	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	155.48	12/2019 -	-	-	0/0
1227	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	107.35	08/2020 -	-	-	0/4
1228	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	123.76	12/2019 -	-	-	0/0
1229	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	254.75	12/2019 -	-	-	2/4
1230	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	73.50	12/2019 -	-	-	0/0
1231	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	162.57	06/2020 -	-	-	1/4
1232	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	262.63	12/2019 -	-	-	0/0
1233	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	96.59	12/2019 -	-	-	1/4
1234	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	26.85	12/2019 -	-	-	0/0
1235	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	222.37	12/2019 -	-	-	2/4
1236	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	127.80	05/2020 -	-	-	0/4
1237	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	199.01	06/2019 -	-	-	0/4
1238	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	124.95	07/2019 -	-	-	0/4
1239	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	153.84	11/2019 -	-	-	0/4
1240	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	-	-	0/0
1241	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	223.97	12/2019 -	-	-	0/4
1242	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	261.97	07/2019 -	-	-	0/4
1243	REHABILITATION AND UPGRADEATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 634.30	536.65	539.22	12/2019 03/2021	03/2021	15(O) 0	0/0
1244	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	252.00	07/2019 -	-	-	0/4
1245	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	181.32	12/2019 -	-	-	0/0
1246	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	142.76	03/2019 -	-	-	0/0
1247	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	187.77	- -	-	-	0/0
1248	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	165.67	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1249	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	22.40	05/2020 -	-	-	0/4
1250	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	136.15	12/2019 -	-	-	1/4
1251	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	223.28	07/2019 -	-	-	0/4
1252	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	446.67	08/2019 -	-	-	0/4
1253	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	190.69	07/2019 -	-	-	0/4
1254	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4
1255	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	137.63	07/2019 -	-	-	0/4
1256	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	189.91	06/2019 -	-	-	2/4
1257	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	164.90	03/2019 -	-	-	0/4
1258	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	50.71	03/2018 -	-	-	0/4
1259	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	9.66	05/2020 -	-	-	0/4
1260	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	135.41	12/2019 -	-	-	0/4
1261	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	140.20	12/2019 -	-	-	0/4
1262	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	149.29	04/2020 -	-	-	1/4
1263	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	362.73	04/2019 -	-	-	0/4
1264	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	163.36	09/2019 -	-	-	2/4
1265	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	61.53	09/2018 -	04/2021	31(O) -	0/4
1266	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	973.05	12/2019 -	-	-	1/4
1267	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	995.57	11/2019 -	-	-	1/4
1268	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	309.38	06/2019 -	-	-	2/4
1269	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	53.94	07/2019 -	-	-	1/4
1270	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	87.43	06/2019 -	-	-	0/4
1271	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.60	07/2019 -	-	-	0/4
1272	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	136.85	02/2019 -	-	-	0/4
1273	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	213.10	11/2018 -	-	-	0/4
1274	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	128.89	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1275	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	177.79	06/2019 -	-	-	0/4
1276	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	289.08	06/2019 -	-	-	0/4
1277	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	94.22	06/2019 -	-	-	0/4
1278	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	185.74	06/2019 -	-	-	0/4
1279	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.69	06/2019 -	-	-	0/0
1280	BHOKAR TO SANSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	188.64	07/2019 -	-	-	0/4
1281	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	193.08	06/2021 -	06/2021	0(O) -	1/4
1282	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	709.06	12/2019 -	-	-	1/4
1283	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	627.00	11/2019 -	-	-	1/4
1284	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	837.21	02/2019 -	-	-	0/0
1285	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	637.41	03/2020 -	-	-	2/4
1286	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	1,303.81	03/2020 -	-	-	3/5
1287	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	41.48	06/2019 -	-	-	1/4
1288	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	238.22	12/2019 -	-	-	0/0
1289	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 -	313.58	113.34	04/2020 -	-	-	0/4
1290	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	161.37	10/2018 -	10/2021	36(O) -	3/4
1291	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR ,	10/2016	235.31 -	235.31	170.53	11/2020 -	11/2020	-	0/0
1292	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL,MANIPUR , EPC	03/2019	471.00 -	471.00	101.20	07/2022 -	07/2022	0(O) -	0/4
1293	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL,MANIPUR , EPC	03/2020	292.24 -	292.24	12.44	06/2022 -	06/2022	0(O) -	0/4
1294	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL,MANIPUR , EPC	06/2020	365.53 -	365.53	17.51	08/2022 -	08/2022	0(O) -	0/4
1295	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL,MANIPUR , EPC	03/2020	167.95 -	167.95	22.24	06/2022 -	06/2022	0(O) -	0/4
1296	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL,MANIPUR , EPC	07/2020	177.76 -	177.76	20.53	08/2022 -	08/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1297	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL,MANIPUR , EPC	08/2020	379.39 -	379.39	.00	04/2022 -	04/2022	0(O) -	0/4
1298	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL,MANIPUR , EPC	08/2020	268.98 -	268.98	.00	04/2022 -	04/2022	0(O) -	0/4
1299	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL,MANIPUR , EPC	08/2020	228.97 -	228.97	.00	04/2022 -	04/2022	0(O) -	0/4
1300	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 -	-	-	0/0
1301	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	119.35	- -	09/2021	- -	2/4
1302	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	109.41	05/2019 -	-	-	1/4
1303	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	-	0/0
1304	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021	128(O) 0	0/0
1305	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021	128(O) 0	0/0
1306	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	65.01	09/2019 -	04/2023	43(O) -	0/0
1307	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	18.08	09/2019 -	07/2023	46(O) -	0/0
1308	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	33.18	09/2019 -	06/2023	45(O) -	0/0
1309	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	47.39	09/2019 -	04/2023	43(O) -	0/0
1310	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	58.49	09/2019 -	04/2023	43(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1311	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	72.44	09/2019 -	06/2023	45(O) -	0/0
1312	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	50.49	09/2019 -	04/2024	55(O) -	0/0
1313	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	59.92	09/2019 -	09/2023	48(O) -	0/0
1314	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	292.10	09/2014 12/2020	-	-	0/0
1315	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM , EPC	09/2020	275.02 -	275.02	4.72	10/2022 -	10/2022	0(O) -	0/4
1316	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM , EPC	03/2020	206.88 -	206.88	.00	07/2022 -	07/2022	0(O) -	0/4
1317	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM , EPC	03/2020	216.49 -	216.49	.00	07/2022 -	07/2022	0(O) -	0/4
1318	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM , EPC	03/2020	292.24 -	292.24	.00	07/2022 -	07/2022	0(O) -	0/4
1319	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM , EPC	03/2020	281.78 -	281.78	.00	07/2022 -	07/2022	0(O) -	0/4
1320	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	364.59	334.71	12/2009 -	-	-	0/0
1321	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1322	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1323	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105(O) -	0/0
1324	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	-	-	0/0
1325	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71(O) -	3/4
1326	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,590.00	- -	05/2021	- -	0/0
1327	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	-	-	0/0
1328	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1329	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1330	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	298.08	08/2016 -	05/2021	57(O) -	2/4
1331	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	339.55	282.82	08/2016 -	05/2021	57(O) -	2/4
1332	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	340.00	238.26	08/2016 -	05/2021	57(O) -	2/4
1333	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	129.13	04/2017 -	-	-	1/4
1334	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	283.11	09/2018 -	09/2020	-	2/4
1335	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 336.49	336.49	79.44	09/2018 -	11/2022	50(O) -	0/0
1336	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	141.44	09/2018 -	07/2022	46(O) -	0/0
1337	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	102.00	09/2018 -	05/2022	44(O) -	0/4
1338	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	77.86	09/2018 -	09/2022	48(O) -	0/4
1339	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	88.48	09/2018 -	12/2021	39(O) -	0/4
1340	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	102.94	09/2018 -	12/2021	39(O) -	0/4
1341	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	95.97	09/2018 -	-	-	1/2
1342	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	127.87	09/2018 -	-	-	0/2
1343	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	192.60	127.60	09/2018 -	-	-	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1344	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	100.90	09/2018 -	11/2021	38(O) -	1/4
1345	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	60.55	09/2018 -	12/2021	39(O) -	1/4
1346	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	44.52	09/2018 -	10/2022	49(O) -	0/4
1347	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	42.55	09/2018 -	11/2022	50(O) -	0/4
1348	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	98.42	12/2020 -	12/2020	-	0/0
1349	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	123.44	12/2020 -	12/2020	-	0/0
1350	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 369.96	336.25	301.49	09/2019 09/2020	-	-	0/0
1351	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	87.30	11/2020 05/2021	11/2020	-	0/0
1352	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	50.27	12/2022 -	12/2022	0(O) -	0/0
1353	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND , EPC	09/2020	277.44 -	277.44	.00	10/2022 -	10/2022	0(O) -	0/4
1354	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257]NHIDCL,NAGALAND , EPC	08/2020	159.85 -	159.85	.00	10/2022 -	10/2022	0(O) -	0/4
1355	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND , EPC	08/2020	202.36 -	202.36	.00	04/2022 -	04/2022	0(O) -	0/4
1356	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND , EPC	09/2020	315.63 -	315.63	.00	04/2022 -	04/2022	0(O) -	0/4
1357	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND , EPC	09/2020	257.15 -	257.15	5.29	04/2022 -	04/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1358	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND , EPC	03/2020	320.97 -	320.97	13.88	06/2022 -	06/2022	0(O) -	0/4
1359	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND , EPC	03/2020	355.79 -	355.79	24.01	06/2022 -	06/2022	0(O) -	0/4
1360	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND , EPC	03/2020	361.53 -	361.53	7.61	06/2022 -	06/2022	0(O) -	0/4
1361	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND , EPC	03/2020	330.78 -	330.78	19.71	12/2021 -	12/2021	0(O) -	0/4
1362	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND , EPC	03/2020	278.95 -	278.95	56.77	06/2022 -	06/2022	0(O) -	0/4
1363	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND , EPC	04/2020	330.80 -	330.80	6.57	12/2021 -	12/2021	0(O) -	0/4
1364	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288]NHIDCL,NAGALAND , EPC	08/2020	232.29 -	232.29	.00	04/2022 -	04/2022	0(O) -	0/4
1365	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1366	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021	81(O) 0	0/0
1367	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1368	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1369	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1370	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	- -	0/0
1371	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	213.52	- -	03/2022	- -	0/1
1372	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	-	-	0/0
1373	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	-	-	0/0
1374	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	611.71	- -	01/2021	-	0/0
1375	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	555.68	08/2019 -	03/2021	19(O) -	0/0
1376	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1377	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	-	0/0
1378	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1379	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1380	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1381	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	-	0/0
1382	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1383	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15(O) -	0/0
1384	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47(O) -	0/0
1385	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	227.63	- -	06/2021	- -	0/0
1386	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	127.61	- -	06/2021	- -	0/0
1387	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	332.04	- -	03/2022	- -	0/0
1388	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	276.59	- -	06/2021	- -	0/0
1389	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	63.98	- -	-	-	0/1
1390	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0
1391	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1
1392	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	261.74	- -	06/2021	-	0/0
1393	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1394	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	102.70	- -	06/2021	- -	0/0
1395	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	25.40	- -	06/2021	- -	0/0
1396	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	189.70	- -	04/2021	- -	0/0
1397	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1398	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1399	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1400	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1401	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1402	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1403	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1404	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB , EPC	12/2015	766.36 -	766.36	685.36	- -	-	-	0/0
1405	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB , EPC	11/2015	847.02 -	847.02	795.30	- -	-	-	0/0
1406	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 -	904.82	754.06	- -	12/2020	-	0/0
1407	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	456.80	- -	07/2021	- -	0/0
1408	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	746.43	676.33	12/2017 -	-	-	0/0
1409	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- -	-	-	0/0
1410	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	-	0/0
1411	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	2,280.00	1,282.04	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1412	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	363.86	03/2020 -	09/2021	18(O) -	0/0
1413	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	193.26	- -	07/2021	- -	0/0
1414	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	- -	-	-	0/0
1415	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	- -	-	-	0/0
1416	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB ,	03/2018	322.48 -	322.48	271.72	07/2020 -	08/2021	13(O) -	0/0
1417	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB ,	03/2018	173.24 -	173.24	114.55	06/2020 -	-	-	0/0
1418	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	156.80	08/2020 -	-	-	0/0
1419	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	692.14	10/2019 -	08/2021	22(O) -	0/0
1420	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 -	170.57	54.53	11/2020 -	05/2021	6(O) -	0/0
1421	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	-	-	0/0
1422	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	246.29	08/2020 -	-	-	0/0
1423	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1424	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1425	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1426	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1427	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH, RAJASTHAN , EPC	02/2015	383.40 -	383.40	244.68	03/2015 -	-	-	0/0
1428	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH, RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.22	06/2018 -	-	-	0/4
1429	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 -	-	-	0/0
1430	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN ,	10/2015	597.00 -	597.00	587.64	10/2017 -	-	-	3/4
1431	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1432	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	1,688.16	04/2018 -	-	-	0/0
1433	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1434	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	-	-	0/4
1435	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1436	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	-	-	-	0/0
1437	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1438	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	191.80	06/2019 -	-	-	1/1
1439	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN ,	06/2016	649.00 -	649.00	567.49	06/2019 -	-	-	0/0
1440	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN ,	07/2016	688.70 -	688.70	880.00	-	-	-	0/0
1441	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1442	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,727.66	1,674.80	-	01/2021	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1443	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021	- -	0/0
1444	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	- -	0/0
1445	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15(O) -	0/0
1446	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	773.03	10/2017 -	11/2020	-	0/0
1447	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	330.46	- -	-	-	0/0
1448	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	673.70	- -	09/2020	-	0/0
1449	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	168.78	- -	-	-	0/0
1450	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	610.56	- -	-	-	0/0
1451	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	886.59	- -	-	-	0/0
1452	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	611.28	- -	-	-	0/0
1453	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	131.74	04/2018 -	03/2021	35(O) -	2/4
1454	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35(O) -	3/4
1455	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34(O) -	1/4
1456	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37(O) -	1/4
1457	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	139.26	- -	03/2021	- -	0/0
1458	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	90.45	08/2022 -	08/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1459	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24(O) -	0/0
1460	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	.00	11/2020 -	08/2022	21(O) -	0/0
1461	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM ,	04/2013	151.59 370.01	151.59	282.36	08/2013 12/2020	-	-	0/0
1462	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM , ITEM RATE	04/2013	166.27 359.92	166.27	243.59	08/2013 12/2020	-	-	0/0
1463	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM , ITEM RATE	01/2013	182.28 369.64	269.14	274.07	02/2013 12/2020	-	-	0/0
1464	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	261.20	10/2017 -	-	-	3/4
1465	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	66.63	11/2017 -	-	-	2/4
1466	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	85.64	- -	-	-	1/4
1467	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	24.70	11/2017 -	-	-	1/4
1468	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	11.03	06/2018 -	-	-	0/4
1469	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM , EPC	03/2019	402.94 -	402.94	.78	04/2022 -	04/2022	0(O) -	0/4
1470	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL,SIKKIM , EPC	08/2020	295.97 -	295.97	.00	04/2023 -	04/2023	0(O) -	0/4
1471	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM , EPC	03/2020	242.97 -	242.97	.00	06/2022 -	06/2022	0(O) -	0/4
1472	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001261]NHIDCL,SIKKIM , EPC	08/2020	311.00 -	311.00	.00	04/2023 -	04/2023	0(O) -	0/4
1473	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001262]NHIDCL,SIKKIM , EPC	07/2020	345.38 -	345.38	.00	04/2023 -	04/2023	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1474	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,337.11	12/2013 -	-	-	0/0
1475	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	1.65	06/2013 -	10/2020	-	0/0
1476	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	54.22	05/2013 -	08/2021	99(O) -	0/0
1477	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	8.56	04/2014 -	01/2022	93(O) -	0/0
1478	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	223.10	08/2015 -	-	-	0/0
1479	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	-	0/0
1480	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	140.64	08/2015 -	-	-	0/0
1481	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	-	-	0/0
1482	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	-	-	0/0
1483	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1484	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1485	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	421.01	08/2018 -	03/2021	31(O) -	0/0
1486	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	395.10	07/2018 -	02/2021	-	0/0
1487	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 932.23	848.45	222.06	03/2020 -	12/2021	21(O) -	0/0
1488	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	394.32	07/2016 -	02/2021	-	0/0
1489	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	462.14	08/2017 -	07/2022	59(O) -	0/0
1490	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	182.00	09/2017 -	-	-	0/0
1491	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	566.14	09/2017 -	07/2022	58(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1492	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	203.77	- -	03/2021	- -	0/0
1493	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	- -	0/0
1494	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	243.30	- -	08/2021	- -	0/0
1495	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	310.06	- -	12/2021	- -	0/0
1496	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	-	0/0
1497	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	- -	0/0
1498	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	-	-	0/0
1499	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU ,	03/2019	297.55 -	297.55	45.52	11/2019 -	-	-	0/0
1500	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU ,	01/2016	162.72 -	162.72	136.46	09/2016 -	-	-	0/0
1501	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]MoRTH,TAMIL NADU ,	05/2016	307.70 -	307.70	312.82	01/2017 -	-	-	0/0
1502	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 -	240.38	74.56	06/2019 -	-	-	0/0
1503	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU , EPC	07/2020	3,426.00 -	3,426.00	.00	12/2021 -	12/2021	0(O) -	0/0
1504	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0
1505	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1506	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1507	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,056.08	974.60	11/2018 07/2019	03/2021	28(O) 0	0/0
1508	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1509	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	380.41	- -	-	-	0/0
1510	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	548.02	- -	-	-	0/0
1511	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	196.45	- -	-	-	0/0
1512	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1513	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	115.53	02/2019 -	-	-	0/0
1514	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	116.36	03/2019 -	-	-	0/0
1515	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	164.33	05/2019 -	-	-	0/0
1516	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	107.70	10/2019 -	-	-	0/0
1517	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	222.84	12/2019 -	-	-	0/0
1518	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	293.94	05/2019 -	-	-	0/0
1519	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	176.70	05/2019 -	-	-	0/0
1520	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	98.36	05/2020 -	-	-	0/0
1521	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	207.56	12/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1522	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA ,	02/2018	206.13 -	206.13	171.39	06/2020 -	-	-	0/0
1523	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA ,	02/2018	294.13 -	294.13	116.46	11/2019 -	-	-	0/0
1524	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA ,	02/2018	220.28 -	220.28	122.17	11/2019 -	-	-	0/0
1525	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA ,	02/2018	426.52 -	426.52	388.63	04/2020 -	-	-	0/0
1526	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA ,	03/2018	322.81 -	322.81	120.13	09/2020 -	-	-	0/0
1527	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA ,	03/2018	626.76 -	626.76	170.47	07/2020 -	-	-	0/0
1528	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA ,	01/2017	605.08 -	605.08	398.45	10/2019 -	-	-	0/0
1529	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA ,	03/2018	192.67 -	192.67	146.55	07/2019 -	-	-	0/0
1530	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA ,	01/2019	193.19 -	193.19	101.77	- -	-	-	0/0
1531	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00	359.11	03/2018 -	-	-	3/4
1532	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH, TRIPURA ,	10/2016	171.90 -	171.90	110.19	08/2020 07/2021	07/2021	11(O) 0	0/0
1533	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL, TRIPURA , EPC	03/2020	247.76 -	247.76	2.60	01/2022 -	01/2022	0(O) -	0/4
1534	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL, TRIPURA , EPC	06/2020	347.36 -	347.36	.00	01/2022 -	01/2022	0(O) -	0/4
1535	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL, TRIPURA , EPC	06/2020	277.50 -	277.50	.00	01/2022 -	01/2022	0(O) -	0/4
1536	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265]NHIDCL, TRIPURA , EPC	03/2020	154.51 -	154.51	.00	07/2022 -	07/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1537	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL,TRIPURA , EPC	03/2020	178.43 -	178.43	.00	07/2022 -	07/2022	0(O) -	0/4
1538	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA , EPC	01/2017	197.67 -	197.67	5.75	12/2022 -	12/2022	0(O) -	0/0
1539	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1540	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 469.31	469.31	459.07	01/2014 12/2020	12/2020	-	0/0
1541	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-	-	0/0
1542	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1543	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1544	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 417.68	417.68	433.68	01/2016 12/2020	12/2020	-	0/0
1545	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	239.04	09/2016 -	-	-	0/0
1546	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 627.93	627.93	633.24	01/2016 01/2020	01/2020	-	0/0
1547	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	-	-	0/0
1548	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1549	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1550	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1551	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1552	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1553	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1554	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1555	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	128.54	08/2015 -	-	-	0/0
1556	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	987.94	867.27	- -	-	-	0/2
1557	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,057.60	596.79	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1558	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	977.26	04/2019 -	-	-	0/0
1559	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	-	-	-	0/0
1560	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	-	-	-	0/0
1561	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1562	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	641.51	04/2019 -	-	-	0/0
1563	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	-	-	-	0/0
1564	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	-	-	-	0/0
1565	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	-	-	-	0/0
1566	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1567	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	-	-	-	0/0
1568	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	-	-	-	0/0
1569	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	974.57	03/2020 -	-	-	2/4
1570	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,039.23	03/2020 -	-	-	3/4
1571	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	756.92	03/2020 -	-	-	0/0
1572	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1573	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	1,059.17	- -	-	-	0/0
1574	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	43.23	- -	-	-	0/0
1575	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1576	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1577	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	287.84	- -	-	-	0/0
1578	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	517.66	- -	-	-	0/0
1579	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	1,011.70	- -	-	-	0/0
1580	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	-	0/0
1581	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,344.09	- -	-	-	0/0
1582	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,118.92	- -	-	-	0/0
1583	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	529.35	- -	-	-	0/0
1584	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	655.03	- -	-	-	0/0
1585	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0
1586	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	105.65	- -	09/2021	-	0/0
1587	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH ,	03/2016	208.50 -	208.50	165.82	11/2019 -	02/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1588	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	120.69	03/2020 -	-	-	0/0
1589	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	160.61	09/2019 -	-	-	0/0
1590	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	14(O) -	0/0
1591	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	141.11	10/2018 -	-	-	0/0
1592	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	49(O) -	0/0
1593	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	141.33	08/2015 -	01/2021	-	0/0
1594	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	210.31	05/2019 -	03/2021	22(O) -	0/0
1595	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH ,	10/2016	239.63 -	239.63	212.53	02/2019 -	-	-	0/0
1596	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH ,	03/2016	599.34 -	599.34	492.15	01/2020 -	-	-	0/0
1597	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	1,363.84	01/2019 -	-	-	0/0
1598	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH ,	03/2016	388.83 -	388.83	304.70	12/2019 -	-	-	0/0
1599	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	129.83	03/2020 -	03/2021	12(O) -	0/0
1600	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	175.51	10/2019 -	03/2021	17(O) -	0/0
1601	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH ,	12/2016	209.10 -	209.10	201.46	10/2019 -	06/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1602	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	188.43	04/2020 -	04/2021	12(O) -	0/0
1603	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	124.43	02/2020 -	01/2021	-	0/0
1604	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	120.68	08/2020 -	03/2021	7(O) -	0/0
1605	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	172.63	09/2020 -	05/2021	8(O) -	0/0
1606	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	.00	- -	-	-	0/0
1607	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	- -	-	-	0/0
1608	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6(O) -	0/0
1609	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH , EPC	10/2020	724.60 -	724.60	.00	03/2023 -	03/2023	0(O) -	0/0
1610	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	-	-	0/0
1611	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	348.16	- -	-	-	0/0
1612	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	- -	-	-	0/0
1613	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 -	-	-	0/0
1614	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	64.03	05/2018 -	-	-	2/4
1615	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	139.26	06/2018 -	-	-	2/4
1616	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	157.79	05/2018 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1617	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	-	-	0/0
1618	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	-	-	0/0
1619	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	-	-	0/0
1620	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	-	-	0/0
1621	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	-	-	0/0
1622	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	-	-	0/0
1623	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	-	-	0/0
1624	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	-	-	0/0
1625	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	- -	-	-	0/0
1626	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	-	-	0/0
1627	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1628	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	215.91	07/2018 -	-	-	1/5
1629	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	-	-	0/0
1630	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,288.54	08/2013 -	05/2021	93(O) -	3/4
1631	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,868.67	08/2013 -	03/2022	103(O) -	3/4
1632	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1633	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1634	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	363.93	272.98	- -	-	-	0/0
1635	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	-	0/0
1636	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	2,360.65	4,472.01	- -	-	-	0/0
1637	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	130.72	11/2018 -	-	-	0/0
1638	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	604.65	08/2018 -	-	-	0/0
1639	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
1640	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]MoRTH, WEST BENGAL ,	08/2014	600.87 720.97	720.97	682.36	11/2017 -	05/2019	-	0/0
1641	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]MoRTH, WEST BENGAL ,	08/2014	823.20 937.76	937.76	807.99	11/2017 -	06/2019	-	0/0
1642	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	242.97	09/2019 11/2020	05/2021	20(O) 0	0/0
1643	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH, WEST BENGAL ,	03/2017	202.69 202.69	202.69	144.89	11/2019 -	-	-	0/0
1644	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15(O) -	0/0
1645	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	103.81	11/2020 04/2020	04/2021	5(O) 0	0/0
1646	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 254.30	254.30	99.36	10/2020 -	03/2021	5(O) -	0/0
1647	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 213.97	213.97	25.03	08/2019 -	11/2022	39(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1648	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28(O) -	0/0
1649	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL ,	04/2014	279.70 398.52	398.52	331.86	08/2017 01/2020	02/2020	-	0/0
	Total		5,40,947.36 -	5,60,519.84	3,54,098.27				340/1239
	<u>SHIPPING AND PORTS</u>								
1650	JAL MARG VIKAS PROJECT - [N25000072]IWAI, MULTI STATE ,	01/2018	5,369.18 4,633.81	4,633.81	1,814.28	03/2023 -	03/2023	0(O) -	0/0
	Total		5,369.18 -	4,633.81	1,814.28				0/0
	<u>TELECOMMUNICATIONS</u>								
1651	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE (NICF) AT GHIT - [N28000115]CPWD, DELHI ,	10/2016	248.20 -	248.20	133.09	03/2018 -	06/2021	39(O) -	0/0
1652	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE ,	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	71(O) -	0/0
1653	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL, MULTI STATE , Central Sector Projects	03/2020	431.16 431.00	431.16	.00	06/2021 -	11/2021	5(O) -	0/0
	Total		14,013.36 -	25,343.36	16,727.09				0/0
	<u>URBAN DEVELOPMENT</u>								
1654	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL, BIHAR ,	02/2019	13,365.77 -	13,365.77	231.97	06/2024 -	06/2024	0(O) -	0/0
1655	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE VI-5) SHOPS CO - [N28000149]CPWD, CHHATISGARH ,	05/2019	299.97 -	299.97	.29	09/2020 -	-	-	0/0
1656	DELHI MRTS PHASE-III - [N28000056]DMRC, DELHI ,	09/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021	66(O) -	0/0
1657	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI ,	07/2012	884.30 -	884.30	812.00	12/2015 -	-	-	0/0
1658	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI ,	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	-	3/7
1659	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD, DELHI ,	06/2015	197.33 -	197.33	106.16	04/2019 06/2021	12/2021	32(O) 2	1/2
1660	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI ,	07/2016	2,694.00 -	2,694.00	679.91	- -	12/2022	- -	0/9
1661	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD, DELHI ,	11/2017	238.56 -	238.56	157.67	05/2020 -	-	-	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1662	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	69.02	03/2021 07/2021	07/2021	4(O) 0	0/0
1663	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19(O) -	0/0
1664	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	126.16	11/2020 -	-	-	0/2
1665	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41(O) -	0/0
1666	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022	0(O) -	0/0
1667	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	1,248.28	03/2025 -	03/2025	0(O) -	0/0
1668	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	511.60	12/2020 -	09/2021	9(O) -	0/0
1669	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI ,	02/2020	532.00 -	532.00	150.00	11/2020 -	11/2020	-	0/0
1670	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	8,706.79	12/2018 -	08/2022	44(O) -	0/0
1671	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	61.94	03/2024 -	03/2024	0(O) -	0/0
1672	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	18.27	03/2024 -	03/2024	0(O) -	0/0
1673	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 30,695.12	30,695.12	17,021.86	02/2019 03/2021	06/2024	64(O) 0	120/249
1674	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 6,218.14	6,218.14	6,059.17	07/2017 09/2020	09/2020	-	0/0
1675	BHOPAL METRO RAIL - [N28000124]JPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	126.50	02/2023 -	02/2023	0(O) -	0/0
1676	INDORE METRO RAIL - [N28000125]JPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	117.53	02/2023 -	02/2023	0(O) -	0/0
1677	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	7,068.52	03/2018 -	-	-	0/0
1678	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 09/2022	03/2023	98(O) 0	0/0
1679	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRCL,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	5,696.05	11/2021 -	11/2021	0(O) -	0/0
1680	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	3,320.23	06/2025 -	06/2025	0(O) -	0/0
1681	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-	-	14/24
1682	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	3,088.12	03/2018 -	03/2021	36(O) -	5/21
1683	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1684	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	.00	03/2024 -	03/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1685	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	.00	03/2024 -	03/2024	0(O) -	0/0
1686	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0
	Total		2,82,500.28 -	3,05,097.88	1,35,973.44				144/316
	<u>WATER RESOURCES</u>								
1687	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	17,025.01	03/2020 11/2021	04/2022	25(O) 0	0/19
1688	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	721.37	712.37	03/2015 -	03/2021	72(O) -	5/7
1689	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	55.02	07/2021 -	07/2021	0(O) -	0/0
1690	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	254.13	.05	09/2020 -	-	-	0/0
1691	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	28.53	12/2020 06/2021	06/2021	6(O) 0	0/0
1692	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	.00	08/2021 -	12/2021	4(O) -	0/0
1693	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1694	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	225.77	271.22	03/2020 -	03/2021	12(O) -	0/0
1695	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR ,	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14(O) -	0/0
1696	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	286.36	01/2021 -	-	-	0/0
1697	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	90.77	04/2021 -	04/2021	0(O) -	0/0
1698	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR ,	05/2017	184.86 -	184.86	152.78	05/2021 -	05/2021	0(O) -	0/0
1699	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	53.08	11/2020 03/2021	03/2021	4(O) 0	0/0
1700	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	133.75	05/2021 -	05/2021	0(O) -	0/0
1701	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	40.09	06/2022 -	06/2022	0(O) -	0/0
1702	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	40.09	06/2022 -	06/2022	0(O) -	0/0
1703	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	665.78	160.36	12/2022 -	12/2022	0(O) -	0/0
1704	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	64.03	12/2021 -	12/2022	12(O) -	0/0
1705	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	129.67	02/2022 -	12/2022	10(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1706	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND MAT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	314.33	01/2021 -	06/2021	5(O) -	0/0
1707	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1708	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	173.71	12/2019 -	12/2021	24(O) -	0/0
1709	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	49.66	09/2021 -	09/2021	0(O) -	0/0
1710	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH ,	03/2018	904.00 -	904.00	136.55	09/2021 -	09/2021	0(O) -	0/0
1711	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 261.12	261.12	.00	03/2022 -	03/2022	0(O) -	0/0
1712	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH ,	10/2016	370.40 430.49	430.49	376.22	08/2020 03/2021	03/2021	7(O) 0	0/0
1713	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	54.21	09/2021 -	09/2021	0(O) -	0/0
1714	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH ,	02/2017	161.31 -	161.31	91.38	11/2019 -	03/2021	16(O) -	0/0
1715	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	0(O) -	0/0
1716	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	216.89	12/2020 -	05/2021	5(O) -	0/0
1717	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 330.05	330.05	222.79	12/2019 -	01/2021	-	0/0
1718	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	.00	12/2021 -	12/2021	0(O) -	0/0
1719	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	21.10	10/2021 -	10/2021	0(O) -	0/0
1720	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	690.71	.00	06/2022 -	06/2022	0(O) -	0/0
1721	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 213.91	213.91	.00	07/2021 -	06/2022	11(O) -	0/0
1722	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND ,	03/2017	273.37 -	273.37	75.58	08/2019 -	-	-	0/0
1723	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	78.59	11/2019 03/2021	03/2021	16(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(March 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1724	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(O) -	0/0
1725	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(O) -	0/0
1726	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(O) -	0/0
1727	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 224.69	224.69	.00	02/2022 -	06/2022	4(O) -	0/0
1728	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(O) -	0/0
1729	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(O) -	0/0
1730	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 154.73	154.73	.00	02/2022 -	10/2022	8(O) -	0/0
1731	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	.00	12/2021 -	12/2021	0(O) -	0/0
1732	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	201.30	12/2019 05/2021	05/2021	17(O) 0	0/0
1733	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	214.52	04/2020 -	03/2021	11(O) -	0/0
1734	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	.00	12/2021 -	12/2021	0(O) -	0/0
1735	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	.00	12/2021 -	12/2021	0(O) -	0/0
	Total		26,781.06 -	72,049.94	21,633.37				5/26
	<u>DEFENCE PRODUCTION</u>								
1736	RESIDENTIAL QUARTERS FOR HAL BANGLORE - [N28000103]CPWD, KARNATAKA ,	12/2016	246.31 -	246.31	123.83	02/2020 -	06/2021	16(O) -	6/10
	Total		246.31 -	246.31	123.83				6/10
	<u>COMMERCE</u>								
1737	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC, DELHI ,	06/2018	302.64 -	302.64	60.00	10/2020 -	-	-	0/0
	Total		302.64 -	302.64	60.00				0/0
	Grand Total		22,33,409.53	26,69,649.35	13,06,617.54				3038/5857


Summary of projects in the Flash Report for the month of March, 2021

Project Implementation - Current Status:

Number of Projects in Previous Month	1736
Number of Projects completed/dropped/frozen in Current Month	2
	0
Number of Projects Added in Current Month	3
Number of Projects in Current Month	1737

Brief Analysis

Project Status with respect to Original Schedule: Out of 1737 projects, 13 projects are ahead of schedule, 229 projects are on schedule 557 projects are delayed. 823 projects do not have fixed dates of commissioning. 115 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

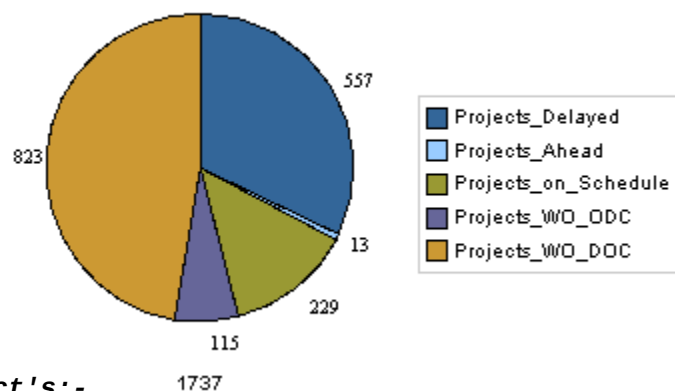


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1737 projects when sanctioned, was of the order of Rs. 2233409.53 crore but this was subsequently revised to Rs. 2669649.35 crore implying a cost overrun of 19.5%. The expenditure incurred on these projects till March, 2021 is Rs. 1306617.54 crore, which is 48.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

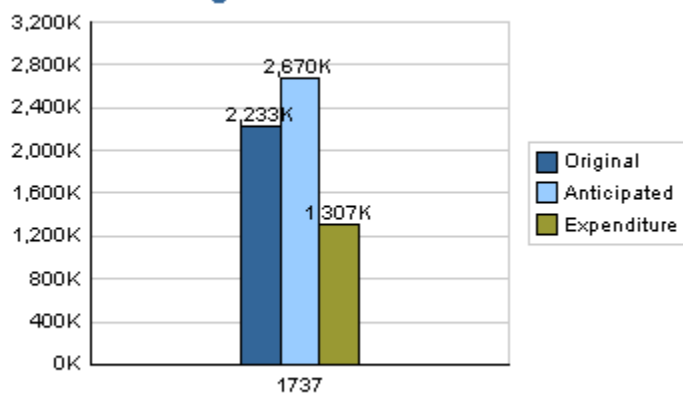

Sector wise current status of projects on the Flash Report


RURAL DEVELOPMENT

Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 3 projects are delayed.

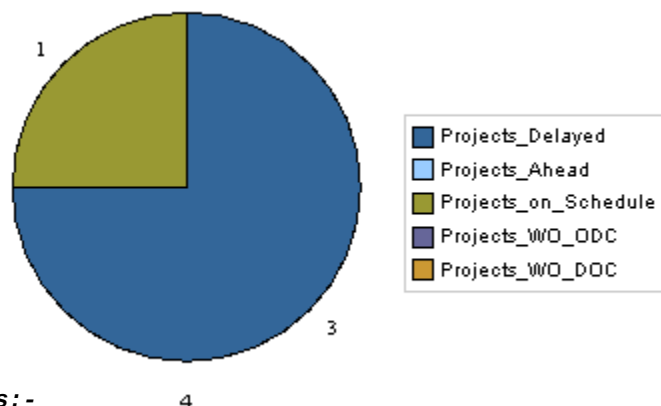

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 889.43 crore but this was subsequently anticipated to Rs. 899.87 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till March, 2021 is Rs. 472.48 crore, which is 52.5% of the anticipated cost of the projects.

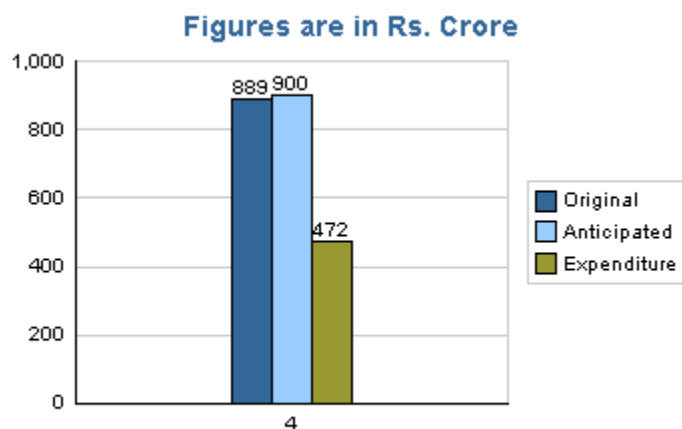

Sector wise current status of projects on the Flash Report


HOME AFFAIRS

Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule 2 projects are delayed.

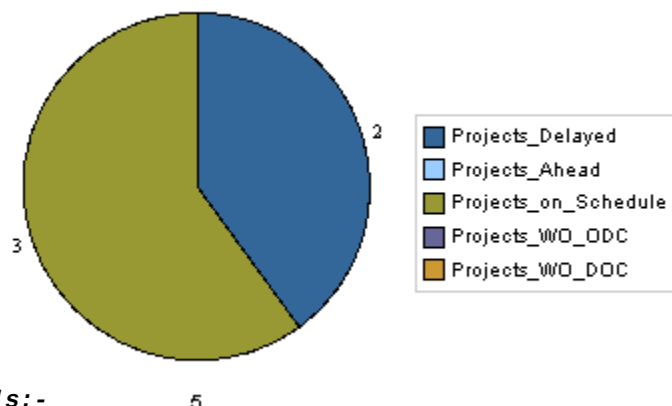


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1993.4 crore but this was subsequently anticipated to Rs. 2849.31 crore implying a cost overrun of 42.9%. The expenditure incurred on these projects till March, 2021 is Rs. 1082.82 crore, which is 38% of the anticipated cost of the projects.

Figures are in Rs. Crore

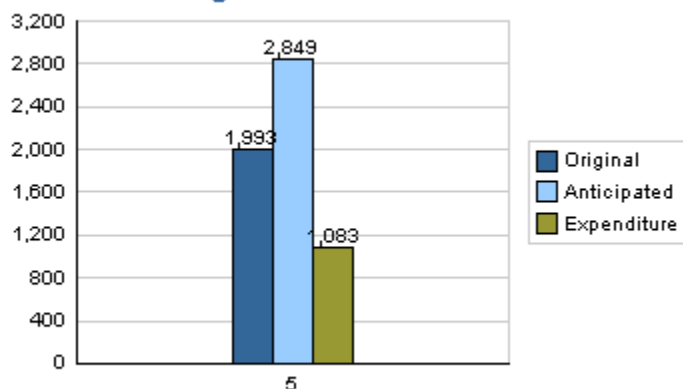

Sector wise current status of projects on the Flash Report

HUMAN RESOURCE DEVELOPMENT


Current Status:

Number of Projects	26
Number of Projects On Schedule	4
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	8
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 26 projects, 4 projects are on schedule 14 projects are delayed. 8 projects do not have fixed dates of commissioning.

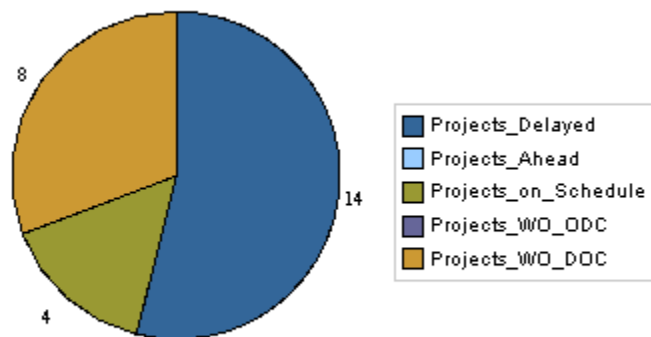


Total No Of Project's:-

26

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 11077.4 crore but this was subsequently anticipated to Rs. 11265.83 crore implying a cost overrun of 1.7%. The expenditure incurred on these projects till March, 2021 is Rs. 2437.07 crore, which is 21.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

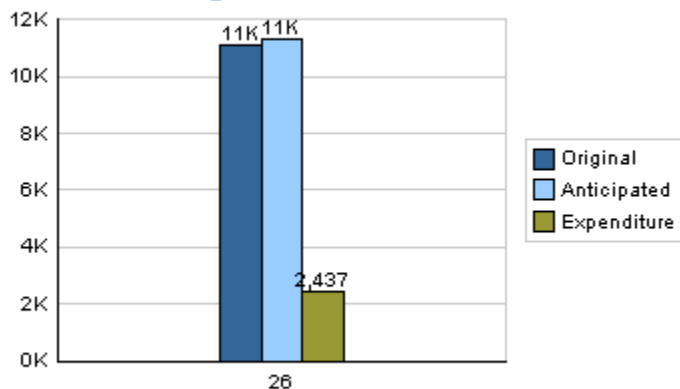

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	49
Number of Projects On Schedule	24
Number of Projects Delayed	20

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 49 projects, 24 projects are on schedule 20 projects are delayed. 5 projects do not have fixed dates of commissioning.

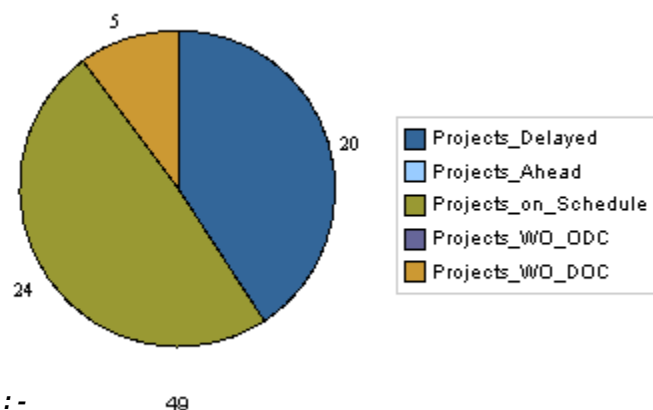


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 49 projects when sanctioned, was of the order of Rs. 26781.06 crore but this was subsequently anticipated to Rs. 72049.94 crore implying a cost overrun of 169%. The expenditure incurred on these projects till March, 2021 is Rs. 21633.37 crore, which is 30% of the anticipated cost of the projects.

Figures are in Rs. Crore

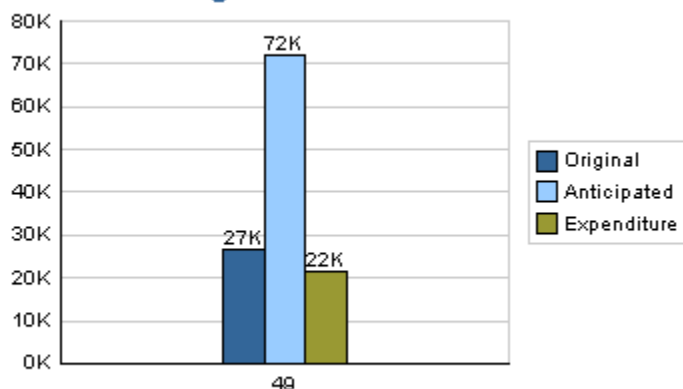

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	33
Number of Projects On Schedule	11
Number of Projects Delayed	10

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 33 projects, 11 projects are on schedule 10 projects are delayed. 11 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

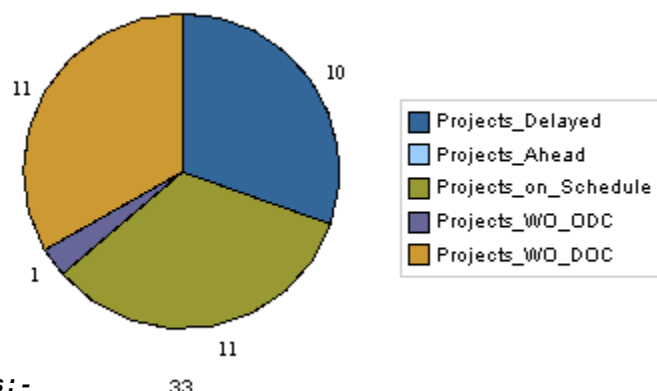


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 33 projects when sanctioned, was of the order of Rs. 282500.28 crore but this was subsequently anticipated to Rs. 305097.88 crore implying a cost overrun of 8%. The expenditure incurred on these projects till March, 2021 is Rs. 135973.44 crore, which is 44.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

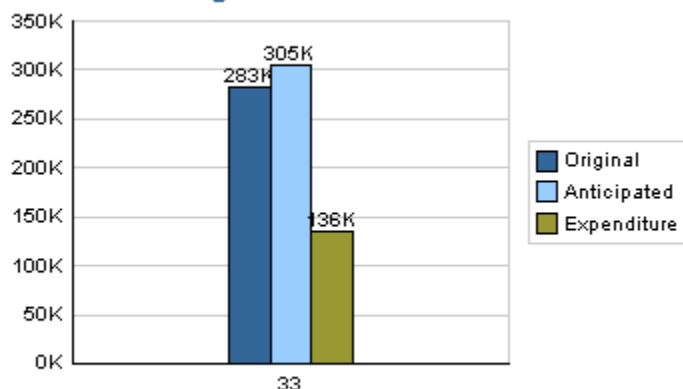

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are delayed.

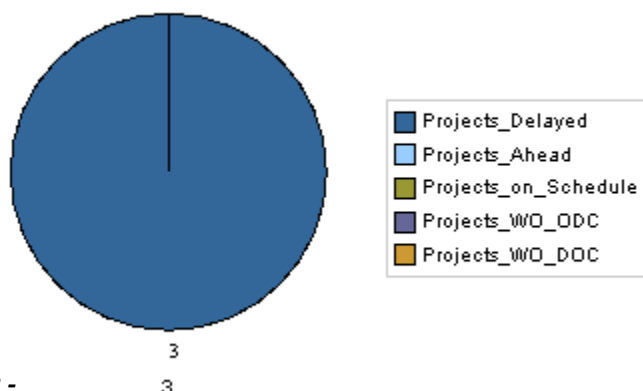


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14013.36 crore but this was subsequently anticipated to Rs. 25343.36 crore implying a cost overrun of 80.9%. The expenditure incurred on these projects till March, 2021 is Rs. 16727.09 crore, which is 66% of the anticipated cost of the projects.

Figures are in Rs. Crore

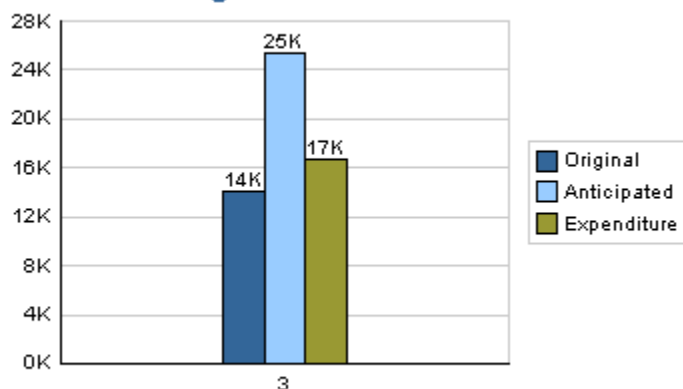

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	908
Number of Projects On Schedule	54
Number of Projects Delayed	135

Number of Projects Without Original Date of Commissioning	58
Number of Projects Without Date Of Commissioning	661

Brief Analysis

Project Status with respect to Original Schedule: Out of 908 projects, 54 projects are on schedule 135 projects are delayed. 661 projects do not have fixed dates of commissioning. 58 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

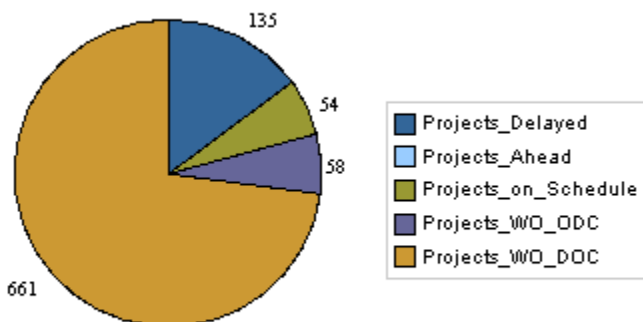


Total No Of Project's:-

908

Investment Scenario

Total original cost of implementation of 908 projects when sanctioned, was of the order of Rs. 540947.36 crore but this was subsequently anticipated to Rs. 560519.84 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till March, 2021 is Rs. 354098.27 crore, which is 63.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

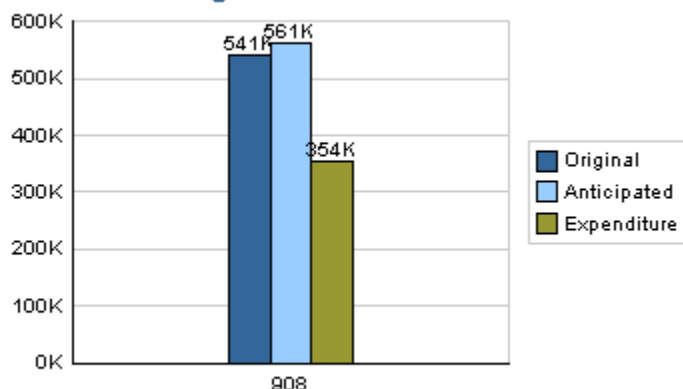

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	312
Number of Projects On Schedule	17
Number of Projects Delayed	155
Number of Projects Ahead	6
Number of Projects Without Original Date of Commissioning	48
Number of Projects Without Date Of Commissioning	86

Brief Analysis

Project Status with respect to Original Schedule: Out of 312 projects, 6 projects are ahead of schedule, 17 projects are on schedule 155 projects are delayed. 86 projects do not have fixed dates of commissioning. 48 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

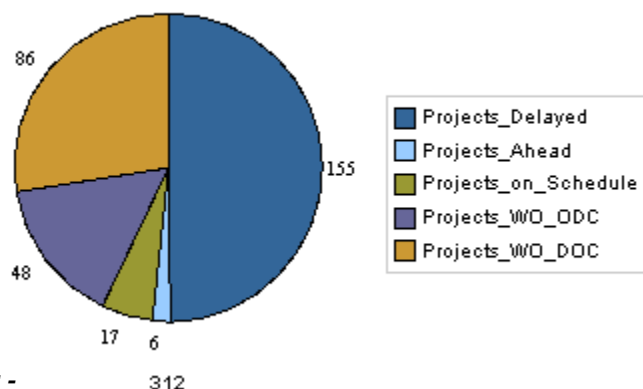

Investment Scenario

Total original cost of implementation of 312 projects when sanctioned, was of the order of Rs. 462095.03 crore but this was subsequently anticipated to Rs. 700073.54 crore implying a cost overrun of 51.5%. The expenditure incurred on these projects till March, 2021 is Rs. 248327.84 crore, which is 35.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

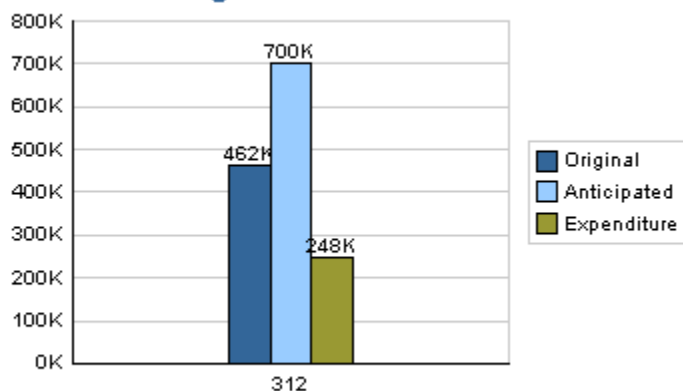

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	29
Number of Projects On Schedule	3
Number of Projects Delayed	13
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 1 project is ahead of schedule, 3 projects are on schedule 13 projects are delayed. 7 projects do not have fixed dates of commissioning. 5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

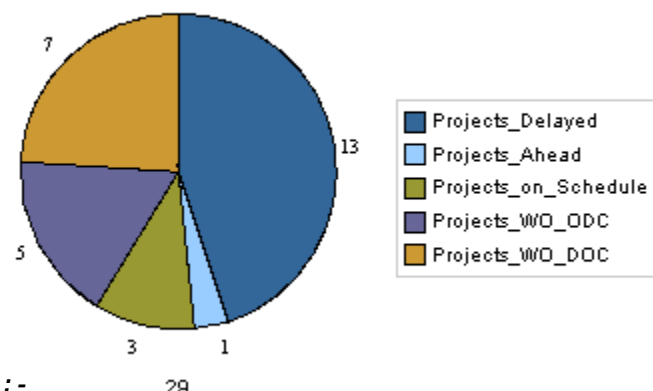


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 15273.26 crore but this was subsequently anticipated to Rs. 15628.51 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till March, 2021 is Rs. 7793.54 crore, which is 49.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

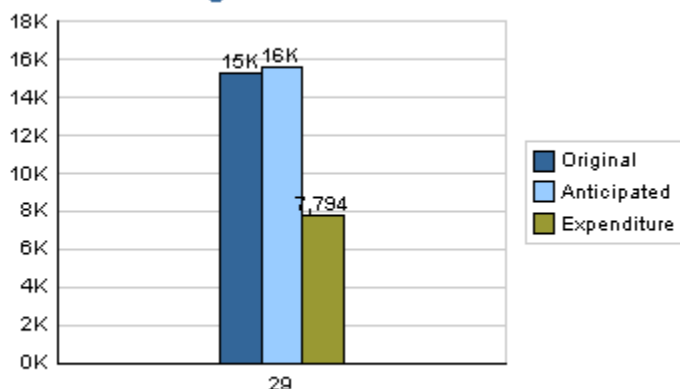

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	78
Number of Projects On Schedule	8
Number of Projects Delayed	45

Number of Projects Without Date Of Commissioning 25

Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 8 projects are on schedule 45 projects are delayed. 25 projects do not have fixed dates of commissioning.

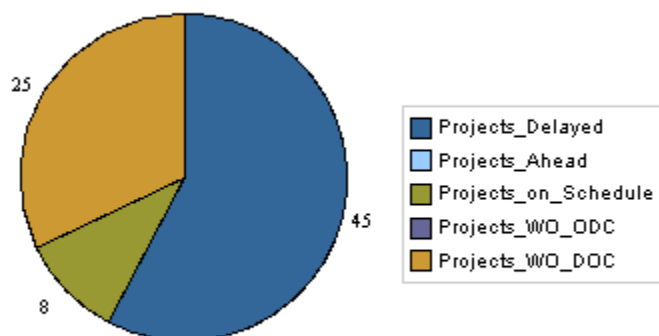


Total No Of Project's:-

78

Investment Scenario

Total original cost of implementation of 78 projects when sanctioned, was of the order of Rs. 295137.42 crore but this was subsequently anticipated to Rs. 367699.63 crore implying a cost overrun of 24.6%. The expenditure incurred on these projects till March, 2021 is Rs. 255492.7 crore, which is 69.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

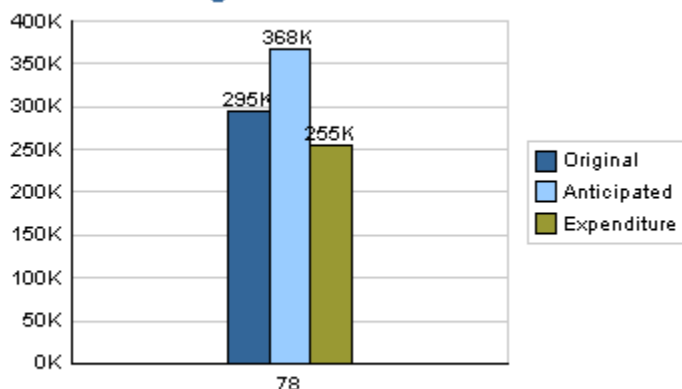

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	139
Number of Projects On Schedule	53
Number of Projects Delayed	76
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 139 projects, 5 projects are ahead of schedule, 53 projects are on schedule 76 projects are delayed. 3 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

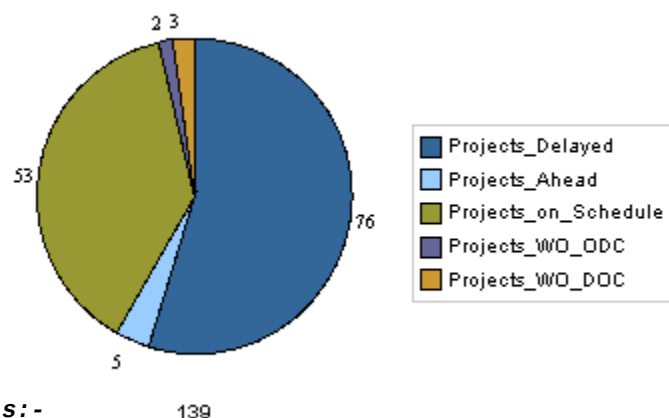


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 139 projects when sanctioned, was of the order of Rs. 296976.45 crore but this was subsequently anticipated to Rs. 304102.14 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till March, 2021 is Rs. 112387.28 crore, which is 37% of the anticipated cost of the projects.

Figures are in Rs. Crore

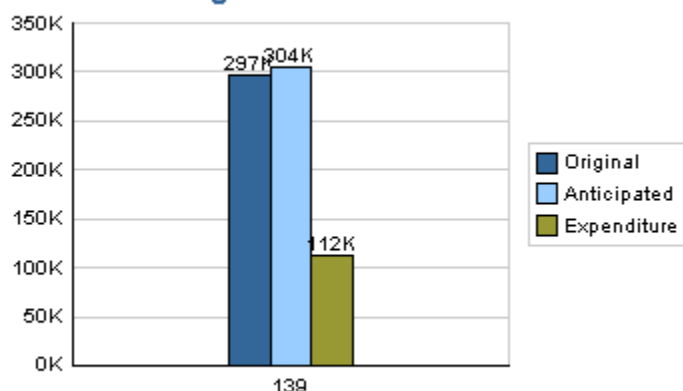

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	101
Number of Projects On Schedule	39
Number of Projects Delayed	50
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 101 projects, 1 project is ahead of schedule, 39 projects are on schedule 50 projects are delayed. 10 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.


Total No Of Project's:-

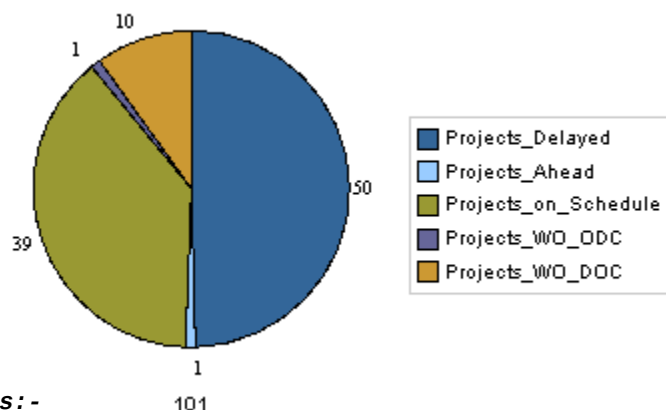

Investment Scenario

Total original cost of implementation of 101 projects when sanctioned, was of the order of Rs. 145653.01 crore but this was subsequently anticipated to Rs. 144210.92 cr The expenditure incurred on these projects till March, 2021 is Rs. 48349.37 crore, which is 33.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

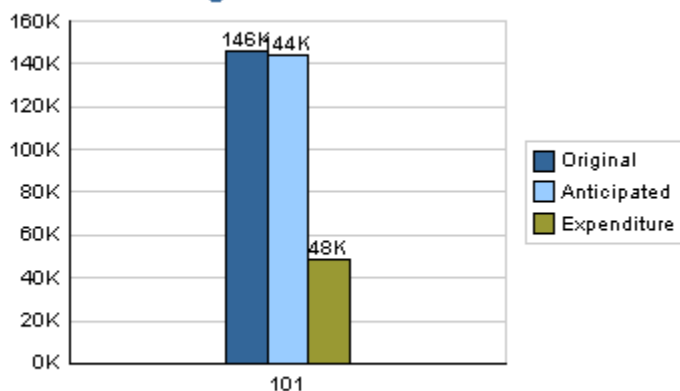

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	19
Number of Projects On Schedule	7
Number of Projects Delayed	11

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 7 projects are on schedule 11 projects are delayed. 1 project does not have fixed dates of commissioning.

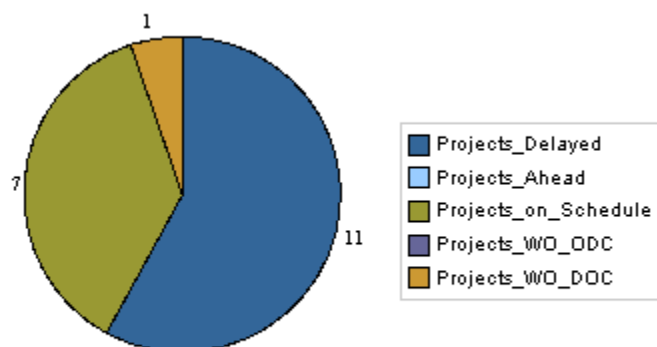


Total No Of Project's:-

19

Investment Scenario

Total original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 13786.34 crore but this was subsequently anticipated to Rs. 14034.5 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till March, 2021 is Rs. 2939.03 crore, which is 20.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

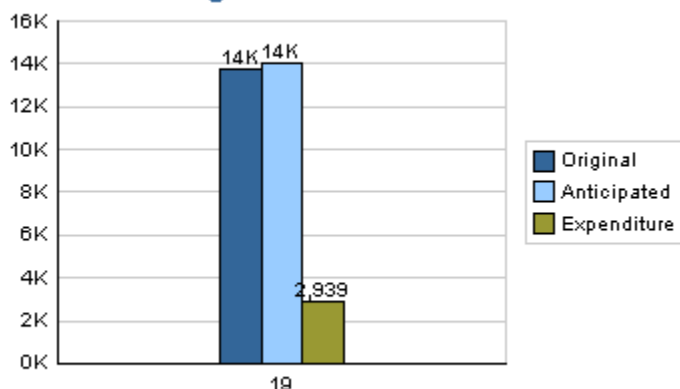

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

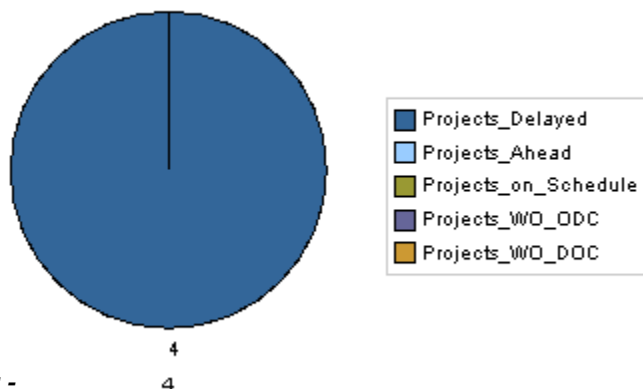

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till March, 2021 is Rs. 59216.21 crore, which is 73.7% of the anticipated cost of the projects.

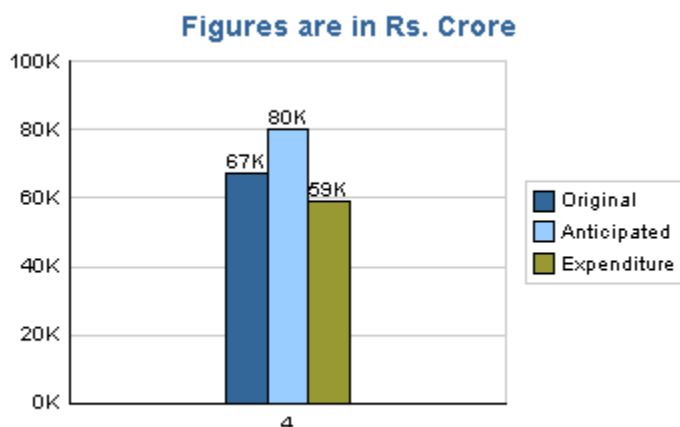

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

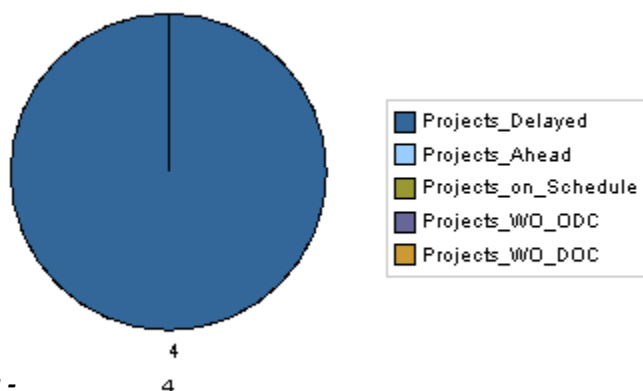

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till March, 2021 is Rs. 866.91 crore, which is 78.7% of the anticipated cost of the projects.

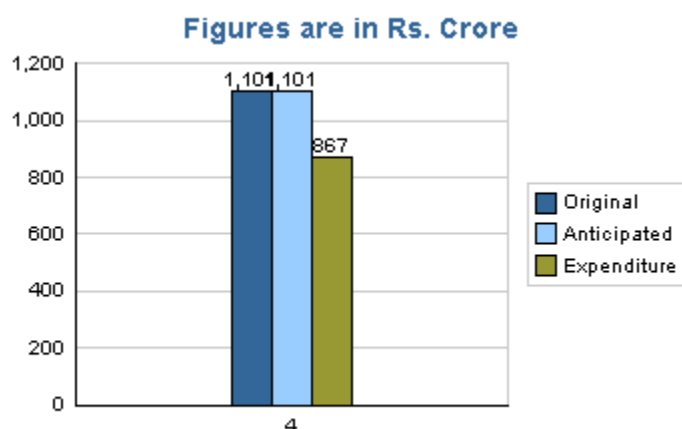

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	9
Number of Projects On Schedule	3
Number of Projects Delayed	5

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 3 projects are on schedule 5 projects are delayed. 1 project does not have fixed dates of commissioning.

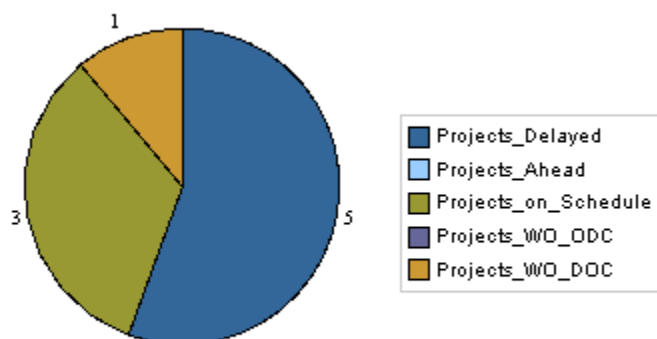


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 25452.51 crore but this was subsequently anticipated to Rs. 31567.51 crore implying a cost overrun of 24%. The expenditure incurred on these projects till March, 2021 is Rs. 23080.97 crore, which is 73.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

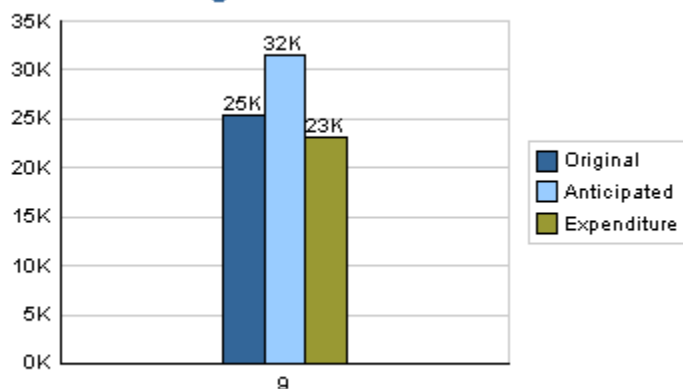

Sector wise current status of projects on the Flash Report

MINES

Current Status:


Number of Projects **5**

Number of Projects Delayed **2**

Number of Projects Without Date Of Commissioning **3**

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

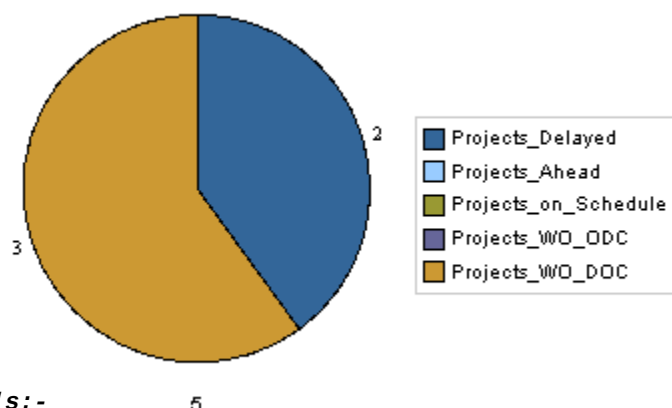


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore. The expenditure incurred on these projects till March, 2021 is Rs. 1311.1 crore, which is 18.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

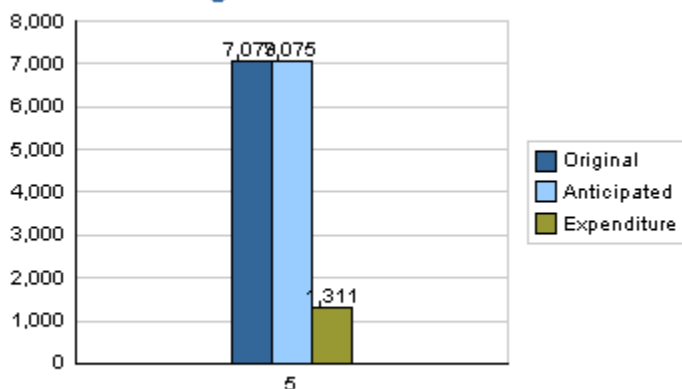

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (MARCH 2021)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	2,893.59	816.45
2	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	76,171.22
3	ARUNACHAL PRADESH	42	24,624.65	44,366.68	27,125.58
4	ASSAM	47	42,046.33	45,657.63	14,540.63
5	BIHAR	108	1,22,099.62	1,58,462.5	75,749.78
6	CHANDIGARH	2	349.15	570	270.91
7	CHHATISGARH	48	91,239.04	1,02,416.44	57,192.56
8	DELHI	36	90,723.12	92,153.92	55,840.07
9	GOA	11	5,629.77	5,640.26	2,596.12
10	GUJARAT	59	1,06,069.6	1,17,304.95	57,644.55
11	HARYANA	43	30,316.35	32,837.14	19,038.08
12	HIMACHAL PRADESH	15	20,365.24	30,249.67	17,556.91
13	JAMMU AND KASHMIR	22	40,412.13	66,473.44	42,114.37
14	JHARKHAND	42	70,673.4	68,776.1	33,415.31
15	KARNATAKA	60	71,320.53	80,933.03	42,532.68
16	KERALA	22	37,466.85	42,584.93	19,389.12
17	MADHYA PRADESH	84	91,161.4	1,04,808.86	55,412.82
18	MAHARASHTRA	242	2,17,334.38	2,40,364.76	1,32,687.93
19	MANIPUR	12	8,137.49	15,887.67	11,348.47
20	MEGHALAYA	7	3,245.09	6,563.59	1,591.55
21	MIZORAM	18	9,030.03	12,978.73	6,052.58
22	MULTI STATE	128	3,66,425.54	4,80,969.26	1,88,899.35
23	NAGALAND	38	18,265.97	22,463.91	4,366.93
24	ODISHA	89	1,29,891.78	1,34,147.04	56,365.94
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	29	15,325.05	18,249.98	11,046.17
27	RAJASTHAN	60	53,090.5	61,137.54	39,345.4
28	SIKKIM	14	5,074.99	12,481.74	1,869.18
29	TAMIL NADU	71	1,19,185.26	1,38,366.76	80,944.21
30	TELANGANA	47	36,326.25	39,359.69	19,661.19
31	TRIPURA	13	3,479.87	3,662.68	1,473.55
32	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	92,882.57
33	UTTARAKHAND	32	34,539.29	46,325.58	15,457.3
34	WEST BENGAL	75	65,583.67	84,487.51	45,201.65
TOTAL		1,737	22,33,409.53	26,69,649.35	13,06,617.54

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.63	03/2021 04/2024	03/2021
	<u>Western Coal Fields Limited</u>						
2	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	226.81	03/2022 -	03/2021
	Total		677.56 -	677.56	327.44		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
3	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	-	09/2025 -	05/2024
	Total		1,828.00 -	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
4	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	2,109.70	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
5	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	130.48	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00	315.00	206.17	12/2021 -	06/2021
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	1,951.62	09/2022 -	03/2022
	Total		6,709.26 -	6,693.26	4,397.97		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
8	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 546.36	546.36	477.69	11/2016 09/2021	05/2021
9	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	246.14	05/2020 05/2021	04/2021
10	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	148.70	06/2019 08/2021	05/2021
11	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	532.79	05/2017 09/2021	06/2021

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		2,511.17 -	2,535.24	1,405.32		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
12	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,204.21	03/2024 -	03/2023
	<u>North East Frontier Railway</u>						
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	2,144.78	824.96	12/2021 -	04/2021
	<u>North Western Railway</u>						
14	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	184.11	08/2022 -	06/2022
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	926.84	12/2026 -	12/2025
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.19	12/2025 -	03/2025
17	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022
	<u>South Central Railway</u>						
18	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	534.34	03/2020 03/2022	06/2021
	<u>Southern Railway</u>						
19	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	600.30	355.13	- 10/2021	09/2021
	<u>West Central Railway</u>						
20	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]	4/2001	424.60	2,909.99	1,229.79	03/2021 03/2029	03/2023
	Total		12,149.68 -	21,496.53	7,468.03		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
21	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	3/2018	217.22	226.88	170.96	08/2018 09/2021	03/2021
22	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09 -	995.09	476.77	05/2016 08/2021	04/2021
	<u>National Highways Authority Of India</u>						
23	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]	11/2016	1,064.88 -	1,021.00	296.60	- 01/2022	07/2021
24	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	2,499.00	1,582.36	03/2021 10/2021	04/2021
	Total		3,809.81 -	4,741.97	2,526.69		

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		27,685.48	37,972.56	16,125.45		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24 -	412.24	-	06/2021 -	06/2021
2	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	-	05/2022 -	05/2022
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	475.39 -	475.39	88.11	04/2021 -	04/2021
4	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]	1/2018	1,405.00 -	1,405.00	199.55	08/2022 -	08/2022
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	51.11	09/2021 -	09/2021
6	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	8.46	03/2023 -	03/2023
	Total		4,821.21 -	4,955.27	469.42		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
8	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.87	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
9	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	277.47	03/2023 -	03/2023
10	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
11	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	0.61	03/2027 -	03/2027
12	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	163.16	03/2022 -	03/2022
13	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	-	03/2025 -	03/2025
14	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	98.11	03/2024 -	03/2024
15	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.39	03/2026 -	03/2026
16	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	0.03	03/2027 -	03/2027
17	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	10.11	03/2029 -	03/2029

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Mahanadi Coal Fields Limited</u>						
18	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029
19	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027
20	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026
	<u>Northern Coal Fields Limited</u>						
21	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
22	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
23	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
24	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
	<u>South-Eastern Coal Fields Limited</u>						
25	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.63	03/2021 04/2024	03/2021
26	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
27	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	1.09	03/2022 -	03/2022
28	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,931.04	03/2029 -	03/2029
29	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	4,268.97	03/2023 03/2016	03/2023
30	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	8.28	03/2023 -	03/2023
31	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
32	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	28.26	03/2026 -	03/2026
33	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
34	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
35	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	276.19	03/2029 -	03/2029
36	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	182.99	03/2024 -	03/2024
37	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,630.04	03/2023 -	03/2023
38	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.95	03/2026 -	03/2026
	<u>Western Coal Fields Limited</u>						
39	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
40	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	0.87	03/2026 -	03/2026
41	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	211.41	03/2021 -	03/2021
42	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	274.95	03/2021 -	03/2021
43	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	99.77	03/2021 -	03/2021
44	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	85.82	03/2023 -	03/2023
45	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	251.34	03/2021 -	03/2021
46	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	281.92	03/2025 -	03/2025
	Total		58,306.28 -	58,528.02	14,773.10		
	<u>FINANCE</u>						
	<u>Central Public Works Department</u>						
47	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	113.99	11/2021 -	11/2021
	Total		348.77 -	348.77	113.99		
	<u>HEALTH AND FAMILY WELFARE</u>						
48	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	199.99	09/2023 -	09/2023
49	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
50	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	682.54	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	882.53		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
51	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	0.29	05/2022 -	05/2022
52	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]	6/2019	277.35 -	277.35	5.30	07/2022 -	07/2022
53	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
	Total		611.31 -	611.31	5.59		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
54	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	35.88	06/2022 -	06/2022
55	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
56	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
57	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
	Total		2,206.13 -	2,206.13	93.30		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
58	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	106.83	06/2022 -	06/2022
59	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	377.64	03/2023 -	03/2023
60	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	772.75	12/2021 -	12/2021
61	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) [N16000374]	8/2019	1,607.00 -	1,607.00	212.84	08/2022 -	08/2022
62	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	77.84	03/2023 -	03/2023
63	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	321.21	12/2021 -	12/2021
	<u>Gas Authority Of India Limited</u>						
64	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	109.54	10/2022 -	10/2022
65	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	77.27	07/2022 -	07/2022
66	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	114.73	07/2022 -	07/2022
67	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	200.10	04/2022 -	04/2022
68	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,022.40	05/2023 -	05/2023
69	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	142.34	10/2022 -	10/2022
70	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	245.60	07/2022 -	07/2022
71	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	92.04	10/2022 -	10/2022
72	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	71.90	11/2022 -	11/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
73	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,200.60	12/2021 -	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
74	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	222.20	11/2021 -	11/2021
75	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	875.03	06/2022 -	06/2022
76	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	189.70	11/2022 -	11/2022
77	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	117.00	08/2021 -	08/2021
78	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	-	11/2022 -	11/2022
79	220 KV GRID SUPPLY - [N16000407]	10/2020	303.40 -	303.40	199.11	03/2021 -	03/2021
80	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	147.24	12/2022 -	12/2022
81	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,244.50	68.76	02/2023 -	02/2023
	<u>Indian Oil Corporation Limited</u>						
82	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,754.90	10/2021 -	10/2021
83	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	430.93	08/2022 -	08/2022
84	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	179.69	10/2021 -	10/2021
85	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,525.53	02/2022 -	02/2022
86	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	143.52	05/2023 -	05/2023
87	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00 -	921.00	3.05	09/2023 -	09/2023
88	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	92.44	01/2024 -	01/2024
89	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	101.64	12/2021 -	12/2021
90	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00 -	18,936.00	685.07	09/2024 -	09/2024
91	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	135.89	11/2021 -	11/2021
92	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	11.85	07/2022 -	07/2022
93	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00 -	1,398.00	80.68	12/2023 -	12/2023
94	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	58.06	01/2023 -	01/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
95	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	-	08/2023 -	08/2023
96	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	24.66	12/2022 -	12/2022
97	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	8.95	07/2022 -	07/2022
98	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	1.77	08/2022 -	08/2022
99	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	1,652.79	08/2021 -	08/2021
100	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	865.95	04/2023 -	04/2023
101	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	95.40	10/2021 -	10/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
102	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	2.09	06/2023 -	06/2023
	<u>Numaligarh Refinery Limited</u>						
103	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY - [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024
104	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
105	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	827.75	03/2026 -	03/2026
106	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	3,596.00	3,507.79	05/2021 05/2021	05/2021
107	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,302.43	03/2022 -	03/2022
108	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	2,521.33	05/2021 -	05/2021
109	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	87.19	08/2022 -	08/2022
110	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	1,595.82	05/2021 -	05/2021
	Total		1,49,251.48 -	1,48,131.72	26,948.00		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
111	JETSAR SOLAR 160 MW - [N18000287]	12/2019	702.28 -	702.28	-	03/2021 -	03/2021
112	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	-	04/2021 -	04/2021
113	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	-	09/2021 -	09/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
114	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	261.80	-	10/2021 -	10/2021
115	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	-	09/2021 -	09/2021
	<u>Satluj Jal Vidyut Nigam Limited</u>						
116	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	1,998.39	01/2024 -	01/2024
117	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	417.95	01/2026 -	01/2026
118	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	569.80	12/2021 -	12/2021
	Total		17,329.49 -	17,629.05	2,986.14		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
119	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
120	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
121	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023
122	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023
	<u>North Central Railway</u>						
123	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021
124	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
125	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	4,083.02	263.68	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
126	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	112.02	12/2021 -	12/2021
127	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
128	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	929.79	03/2022 -	03/2022
	<u>National High Speed Rail Corporation Limited</u>						
129	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	12,039.69	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
130	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	549.50	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
131	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
132	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
133	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021
134	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021
135	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	705.50	12/2024 -	12/2024
	Total		1,44,397.85 -	1,52,478.71	22,486.63		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
136	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	193.08	06/2021 -	06/2021
137	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	197.67	5.75	12/2022 -	12/2022
138	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]	3/2018	351.00 -	351.00	128.31	06/2021 -	06/2021
139	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021
140	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]	3/2020	370.36 -	370.36	90.45	08/2022 -	08/2022
141	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51 -	237.51	50.27	12/2022 -	12/2022
142	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	70.46	09/2021 -	09/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
143	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR- SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	29.22	12/2023 -	12/2023
144	REHABILITATION & UPGRADE OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]	6/2020	277.50 -	277.50	-	01/2022 -	01/2022
145	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	-	04/2022 -	04/2022
146	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	63.83	09/2026 -	09/2026
147	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	20.53	08/2022 -	08/2022
148	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]	6/2020	347.36 -	347.36	-	01/2022 -	01/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
149	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284	3/2020	361.53 -	361.53	7.61	06/2022 -	06/2022
150	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251	3/2019	402.94 -	402.94	0.78	04/2022 -	04/2022
151	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	-	04/2023 -	04/2023
152	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274	8/2020	379.39 -	379.39	-	04/2022 -	04/2022
153	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287	4/2020	330.80 -	330.80	6.57	12/2021 -	12/2021
154	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257	8/2020	159.85 -	159.85	-	10/2022 -	10/2022
155	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
156	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244	8/2020	301.06 -	301.06	-	04/2022 -	04/2022
157	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247	3/2020	247.76 -	247.76	2.60	01/2022 -	01/2022
158	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001262	7/2020	345.38 -	345.38	-	04/2023 -	04/2023
159	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	22.24	06/2022 -	06/2022
160	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288	8/2020	232.29 -	232.29	-	04/2022 -	04/2022
161	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277	9/2020	275.02 -	275.02	4.72	10/2022 -	10/2022
162	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	-	04/2022 -	04/2022
163	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	-	03/2022 -	03/2022
164	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	-	10/2022 -	10/2022
165	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	-	12/2022 -	12/2022
166	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280	3/2020	320.97 -	320.97	13.88	06/2022 -	06/2022
167	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	56.77	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
168	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285	3/2020	330.78 -	330.78	19.71	12/2021 -	12/2021
169	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265	3/2020	154.51 -	154.51	-	07/2022 -	07/2022
170	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282	3/2020	355.79 -	355.79	24.01	06/2022 -	06/2022
171	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279	3/2020	216.49 -	216.49	-	07/2022 -	07/2022
172	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	15.29	03/2022 -	03/2022
173	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001261	8/2020	311.00 -	311.00	-	04/2023 -	04/2023
174	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260	9/2020	257.15 -	257.15	5.29	04/2022 -	04/2022
175	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	-	06/2022 -	06/2022
176	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAPOKPI TO SEKMAI SECTI - [N24001276	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
177	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	101.20	07/2022 -	07/2022
178	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283	3/2020	281.78 -	281.78	-	07/2022 -	07/2022
179	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270	3/2020	292.24 -	292.24	12.44	06/2022 -	06/2022
180	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245	9/2020	353.90 -	353.90	4.21	05/2022 -	05/2022
181	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	17.51	08/2022 -	08/2022
182	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278	3/2020	206.88 -	206.88	-	07/2022 -	07/2022
183	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	-	07/2022 -	07/2022
184	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264	7/2020	228.39 -	228.39	-	04/2022 -	04/2022
185	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248	8/2020	208.84 -	208.84	-	04/2022 -	04/2022
186	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281	3/2020	292.24 -	292.24	-	07/2022 -	07/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
187	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
	<u>National Highways Authority Of India</u>						
188	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
189	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
	Total		27,765.18 -	27,765.18	1,014.68		
	<u>RURAL DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
190	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021
	Total		361.60 -	361.60	12.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
191	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,814.28	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,814.28		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
192	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124	11/2015	2,907.00 -	2,907.00	254.56	06/2023 -	06/2023
	<u>Steel Authority Of India Limited (Sail)</u>						
193	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	31.60	12/2023 -	12/2023
194	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	16.12	05/2023 -	05/2023
	Total		3,826.42 -	3,826.42	302.28		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
195	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	18.27	03/2024 -	03/2024
196	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	61.94	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Central Public Works Department</u>						
197	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022
	<u>Delhi Metro Rail Corporation</u>						
198	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	1,248.28	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
199	KANPUR METRO RAIL PROJECT - [N28000144]	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
200	AGRA METRO RAIL PROJECT - [N28000145]	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
201	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	5,696.05	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
202	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	126.50	02/2023 -	02/2023
203	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	117.53	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
204	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	3,320.23	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
205	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,365.77	231.97	06/2024 -	06/2024
	Total		1,32,439.21 -	1,32,439.21	10,842.77		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
206	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	40.09	06/2022 -	06/2022
207	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	90.77	04/2021 -	04/2021
208	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	133.75	05/2021 -	05/2021
209	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
210	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	40.09	06/2022 -	06/2022
211	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	152.78	05/2021 -	05/2021
212	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	55.02	07/2021 -	07/2021
	<u>Delhi Jal Board</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
213	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	160.36	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
214	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
215	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
216	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
217	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
218	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
219	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
220	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
221	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
	<u>Uttar Pradesh Jal Nigam</u>						
222	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
223	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022
224	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
225	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
226	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23 -	967.23	54.21	09/2021 -	09/2021
227	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00 -	904.00	136.55	09/2021 -	09/2021
228	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	21.10	10/2021 -	10/2021
229	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	49.66	09/2021 -	09/2021
	Total		9,556.18 -	9,614.85	934.38		
	Grand Total		5,60,922.29	5,68,233.05	83,679.53		

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,922.21	09/2010 09/2016	10/2022
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,158.00	12/2016 -	03/2023
	Total		27,271.00 -	40,499.00	35,568.21		
	<u>COAL</u>						
	<u>Singareni Colliers Company Limited</u>						
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	288.72	03/2015 -	03/2022
	<u>Western Coal Fields Limited</u>						
5	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	325.18	246.55	03/2019 -	03/2022
	Total		361.44 -	674.46	535.27		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
6	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	499.23	488.22	11/2013 -	05/2021
7	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
8	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	164.17	02/2018 -	03/2021
9	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
10	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	233.39	05/2017 -	03/2021
11	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
	Total		1,739.63 -	2,028.35	1,942.01		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,977.00	08/2018 11/2019	05/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Indian Oil Corporation Limited</u>						
13	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	3,027.90	1,933.53	03/2021 -	08/2021
14	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 -	3,338.00	2,888.48	12/2020 -	03/2022
	<u>Oil India Limited</u>						
15	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	7/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021
	Total		9,084.85 -	12,102.10	10,254.01		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
16	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	4/2012	9,750.89 -	12,176.28	11,130.00	02/2017 06/2020	01/2021
17	KHARGONE STPP STAGE I (1320 MW) - [N18000205	3/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-
18	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-
	<u>North East Electric Power Corporation</u>						
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	7,927.34	8,154.50	12/2009 02/2021	02/2021
	<u>Power Grid Corporation Of India Limited</u>						
20	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	590.30	06/2014 -	-
	Total		34,451.79 -	44,631.76	43,660.89		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
21	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	315.00	312.62	03/2019 -	03/2020
22	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	2/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023
	<u>Container Corporation Of India</u>						
23	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	1/2013	387.70 -	487.13	434.63	03/2018 -	03/2021
	<u>East Central Railways</u>						
24	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	3/1999	1,033.07 -	3,550.00	3,528.48	- -	03/2022
25	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476	4/1991	329.39 -	1,483.14	1,207.34	- -	03/2022
26	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	4/1998	180.82 -	726.31	540.19	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
27	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	546.71	541.83	07/2014 -	-
28	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	480.00	485.99	- -	-
29	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	4/2004	372.14 -	1,470.50	1,085.63	- -	03/2023
30	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	4/2006	378.56 -	1,858.75	386.36	- -	03/2023
31	SAKRI-HASANPUR ROAD (NL) - [N22000171]	4/1999	325.00 -	735.20	380.48	- -	03/2021
32	KODERMA-TILAIYA (NL), ECR - [220100305]	4/2002	459.91 -	1,625.87	767.07	- -	03/2023
33	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	819.61	03/2019 -	05/2021
34	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	4/2003	528.65 -	2,066.78	1,551.38	- -	03/2023
35	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	4/1997	162.87 -	614.45	340.21	- -	12/2023
36	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022
37	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	4/1996	477.88 283.95	751.55	683.91	03/2012 -	07/2021
	<u>Eastern Railways</u>						
38	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	4/2000	607.09 -	1,425.44	637.94	02/2013 -	03/2024
39	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	4/2010	365.17 -	439.30	385.60	03/2017 -	03/2025
40	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	495.10	284.21	- -	03/2022
41	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	565.00	539.40	- -	05/2019
42	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	502.48	427.64	- -	03/2021
43	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	360.96	- -	03/2024
	<u>Metropolitan Rapid Transport Projects</u>						
44	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
45	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
46	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022
	<u>North Central Railway</u>						
47	ETAWAH-MAINPURI (NL),NCR - [220100318]	4/1997	120.00 -	346.00	345.51	12/2008 -	-
	<u>North East Frontier Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266]	4/2000	1,180.19 -	4,541.38	3,683.54	12/2008 -	04/2021
49	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	2/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-
50	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,043.00	798.53	03/2019 -	03/2023
51	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	373.87	287.09	- -	12/2021
52	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	800.00	799.87	03/2019 -	03/2021
53	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	2,144.78	824.96	12/2021 -	04/2021
54	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	1,873.21	1,162.39	03/2021 -	05/2021
55	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,871.00	1,082.01	- -	-
56	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288]	4/2003	4,454.17 -	12,264.15	10,842.65	03/2011 -	12/2023
<u>North Eastern Railway</u>							
57	HATHUA-BHATNI (N L) (NER) - [N220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
58	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	506.99	01/2019 -	02/2022
<u>North Western Railway</u>							
59	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	2/1997	410.08 -	860.41	699.06	02/2019 -	11/2021
60	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	375.00	345.38	11/2019 -	03/2021
61	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	350.45	253.81	10/2018 -	-
62	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	395.00	340.45	12/2019 -	02/2021
63	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	525.00	463.25	02/2019 -	02/2020
<u>Northern Railway</u>							
64	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	705.53	12/2011 -	06/2021
65	NANGALDAM-TALWARA(NL),NR - [N220100188]	3/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024
66	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [N220100133]	3/1995	2,500.00 -	27,949.00	23,132.28	11/2002 -	12/2022
67	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	859.00	852.73	03/2016 -	06/2021
<u>Rail Vikas Nigam Ltd.</u>							
68	HARIDASPUR-PARADEEP(NL) - [N220100285]	4/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
69	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	4/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-
71	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021
72	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022
73	BANASPAHI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022
74	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021
75	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021
76	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022
77	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	950.00	810.96	03/2016 -	12/2021
78	PALANPUR-SAMAKHAYALI (DL) - [N22000144	4/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022
79	DHASA-JETALSAR (GC) - [N22000141	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021
80	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021
81	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	3/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022
82	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022
	<u>South Central Railway</u>						
83	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
84	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	4/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023
	<u>South East Central Railway</u>						
85	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	4/2005	383.79 -	1,413.76	1,416.77	- -	-
86	GONDIA-JABALPUR(GC),(SECR) - [220100186	2/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021
87	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	4/2008	872.00 -	1,226.51	1,131.91	12/2019 -	-
88	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	4/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021
	<u>South Eastern Railway</u>						
89	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	377.00	195.84	12/2016 -	08/2020
	<u>South Western Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
90	HUBLI- CHIKAJAJUR - [N22000325]	3/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023
91	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021
92	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021
	<u>Southern Railway</u>						
93	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'- AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025
94	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025
95	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022
96	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	2/1996	268.87 -	950.00	928.36	03/2005 -	09/2021
97	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	332.00	265.41	04/2014 03/2021	12/2020
98	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027
99	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	600.30	355.13	- 10/2021	09/2021
100	KURUPPANTHARA-CHINGAVANAM - [N22000190]	4/2007	270.14 -	457.08	439.49	- -	12/2021
101	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	4/1999	198.68 -	559.95	319.22	- -	03/2024
	<u>West Central Railway</u>						
102	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,229.79	03/2021 03/2029	03/2023
103	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025
	<u>Western Railway</u>						
104	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	4/2006	117.36 196.95	202.35	809.40	03/2011 -	-
	Total		59,039.96 -	1,67,917.43	1,24,692.66		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
105	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020
106	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]	5/2016	307.70 -	307.70	312.82	01/2017 -	-
107	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	322.24	292.10	09/2014 12/2020	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	3/2018	325.86 -	325.86	326.88	10/2018 -	-
109	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021
110	KOLHA TO NASRATPUR - [N24001111	4/2016	281.78 282.00	281.78	362.73	04/2019 -	-
111	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080	3/2018	256.15 -	256.15	262.63	12/2019 -	-
112	KUNDRAI TO WAZAR - [N24001077	1/2018	225.25 225.00	225.25	254.75	12/2019 -	-
113	LATUR TO PANGAON - [N24001066	3/2018	336.47 336.00	336.47	345.00	12/2019 -	-
114	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	3/2018	297.12 294.00	294.12	373.98	07/2018 -	-
115	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581	8/2015	288.24 -	288.24	303.16	11/2015 -	-
116	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	210.29	11/2017 -	-
117	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
118	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	8/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021
119	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257	3/2015	298.33 -	298.33	310.72	- -	-
120	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021
121	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	464.05	03/2017 -	-
122	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	1/1991	282.41 -	322.01	318.64	08/2016 -	-
123	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021
124	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	3/2012	207.03 -	389.45	349.94	05/2012 06/2018	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
125	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	400.56	06/2018 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Highways Authority Of India</u>						
126	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	520.00	612.58	02/2009 -	-
127	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	3/2018	642.13 -	807.00	666.56	- -	-
128	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838	3/2018	874.25 -	874.25	886.59	- -	-
129	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810	3/2018	565.09 -	565.09	567.75	- -	02/2021
130	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	3/2018	1,532.62 -	2,499.00	1,582.36	03/2021 10/2021	04/2021
131	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	3/2018	925.40 -	1,197.00	1,011.70	- -	-
132	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	2/2018	2,177.80 -	2,450.00	2,244.98	- -	-
133	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	2/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021
134	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	419.23	- -	10/2020
135	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	1,150.56	03/2020 -	-
136	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	912.41	03/2020 -	-
137	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-
138	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-
139	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650	1/2017	244.90 -	244.90	251.87	05/2019 -	-
140	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	-
141	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634	10/2016	447.75 -	447.75	1,160.74	- -	08/2020
142	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	309.40	- -	-
143	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,590.00	- -	05/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
144	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	9/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021
145	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	9/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-
146	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	9/2016	1,239.82 -	1,727.66	1,674.80	- -	01/2021
147	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]	8/2016	248.97 -	248.97	270.65	05/2019 -	-
148	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	8/2016	1,169.61 -	2,280.00	1,282.04	- -	-
149	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-
150	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]	7/2016	688.70 -	688.70	880.00	- -	-
151	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]	3/2016	1,404.50 -	1,404.50	2,977.58	- -	-
152	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	667.10	02/2019 -	-
153	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]	1/2016	1,134.97 -	1,134.97	1,634.05	11/2018 -	-
154	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	977.26	04/2019 -	-
155	MEERUT-BULANDSHAHAH - [N24000539]	1/2016	683.24 -	987.94	867.27	- -	-
156	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	886.96	07/2008 -	-
157	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	8/2015	516.13 -	649.27	712.15	04/2018 -	-
158	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	8/2015	854.80 -	1,038.56	1,160.00	- -	-
159	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]	8/2015	275.90 -	275.90	289.13	- -	-
160	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	627.93	633.24	01/2016 01/2020	01/2020
161	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	417.68	433.68	01/2016 12/2020	12/2020
162	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021
163	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-
164	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-
165	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
166	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021
167	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,868.67	08/2013 -	03/2022
168	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,288.54	08/2013 -	05/2021
169	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,364.18	03/2013 -	-
170	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-
171	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,922.79	06/2014 -	10/2020
172	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
173	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.73	03/2014 -	-
174	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-
175	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-
176	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	390.72	06/2008 -	09/2019
177	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021
178	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019
179	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-
180	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,559.00	03/2013 -	03/2021
181	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
182	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]	2/2010	617.00 -	617.00	943.17	08/2012 -	-
183	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
184	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	6/2015	845.24 -	941.00	889.83	- 01/2020	01/2020
185	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 -	-
186	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
187	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	1,688.16	04/2018 -	-
188	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	594.57	05/2018 06/2021	06/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
189	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	730.97	642.54	05/2018 06/2021	06/2021
190	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020
191	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	3,275.58	05/2014 -	-
192	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517	12/2015	479.20 -	479.20	712.89	05/2018 -	-
193	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	2,360.65	4,472.01	- -	-
194	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
195	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	3,443.43	01/2018 -	-
196	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	676.33	12/2017 -	-
197	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
198	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
199	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-
200	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
201	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022
202	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.53	10/2013 -	-
203	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	976.79	07/2013 -	-
204	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,337.11	12/2013 -	-
205	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
206	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	1,360.63	02/2013 -	-
207	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163	7/2010	1,813.76 -	1,813.76	2,651.77	07/2013 -	-
208	NASHRI- CHANANI - [N24000162	5/2011	2,159.00 -	2,519.00	4,709.65	06/2015 -	-
209	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	3,107.29	07/2015 -	09/2020
210	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131	2/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-
211	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
212	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	1,509.10	3,684.89	09/2012 -	-
213	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
214	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	655.17	07/2009 -	-
215	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-
216	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019
217	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	325.28	04/2009 -	-
218	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	435.78	427.96	11/2008 -	-
219	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	255.23	251.39	11/2008 -	-
	Total		1,01,504.39 -	1,18,904.28	1,54,583.31		
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
220	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021
	Total		13,334.00 -	24,664.00	16,594.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Chennai Metro Rail Ltd</u>						
221	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-
	<u>Delhi Metro Rail Corporation</u>						
222	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021
	<u>National Building Construcion Corporation Ltd</u>						
223	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-
	Total		57,449.00 -	62,363.73	60,887.85		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
224	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	225.77	271.22	03/2020 -	03/2021
225	SAIDPUR SEWER NETWORK PATNA - [N30000039]	4/2015	268.63 -	268.63	286.36	01/2021 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		494.40 -	494.40	557.58		
	Grand Total		3,04,730.46	4,74,279.51	4,49,275.79		

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (March 2021)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044] BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,922.21	09/2010 09/2016	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010] NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	74	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027] NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,158.00	12/2016 -	03/2023	75	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028] NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	23,648.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	59,216.21					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076] AAI, DELHI	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13	0	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073] AAI, A & N ISLANDS	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	33	5.78	
7	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089] AAI, ANDHRA PRADESH	08/2017	177.10 -	177.10	-	02/2020 -	06/2021	16	0	
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085] AAI, UTTARAKHAND	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10	0	
9	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080] AAI, WEST BENGAL	01/2016	458.00 -	458.00	135.60	03/2020 12/2021	12/2021	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5	0	
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	12	7.88	
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7	0	
13	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12	0	
14	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	389.71	140.62	11/2021 10/2022	10/2022	11	0	NIL
15	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	-	03/2022 -	03/2023	12	0	
	Total		8,526.85 -	8,640.95	2,134.03					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
16	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	281.27	05/2014 -	07/2021	86	0	
17	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	461.54	04/2015 -	03/2022	83	0	
18	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	38.59	03/2017 -	03/2022	60	12.2	
19	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	18.35	04/2018 -	06/2022	50	37.56	
20	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	23.47	04/2014 -	04/2023	108	0	
	<u>Central Coal Fields Limited</u>									
21	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	107.27	03/2011 -	03/2022	132	0	
22	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	426.30	03/2016 -	03/2022	72	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
23	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	98.21	03/2014 -	03/2022	96	0	
24	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND	02/2012	4,983.58 4,983.58	4,983.58	245.85	03/2020 03/2024	03/2024	48	0	
25	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND	08/2008	6,964.33 6,964.33	706.40	706.20	07/2012 03/2025	03/2025	152	-89.86	
	<u>Eastern Coal Fields Limited</u>									
26	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	658.63	03/2018 -	03/2021	36	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2.Expediting the work of tree felling for hand over of 32.65 Ha forest land.
27	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL,WEST BENGAL	11/2015	1,210.12 -	1,210.12	24.49	03/2022 03/2029	03/2029	84	0	
	<u>Mahanadi Coal Fields Limited</u>									
28	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	168.13	03/2012 -	03/2021	108	0	
29	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108	0	
30	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60	0	
31	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36	0	
32	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL,ODISHA	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028	180	0	
33	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL,ODISHA	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029	228	0	
34	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168	0	
	<u>Neyveli Lignite Corporation</u>									
35	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	11,452.38	11/2021 07/2022	07/2022	8	0	
36	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	34.62	08/2022 -	09/2023	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
37	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	484.65	06/2015 03/2025	03/2025	117	-51.37	
	<u>Northern Coal Fields Limited</u>									
38	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	622.66	03/2021 -	03/2022	12	0	
39	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	152.16	03/2022 -	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
40	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	193.00	03/2016 -	03/2021	60	-3.5	
41	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84	-32.3	
42	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	288.72	03/2015 -	03/2022	84	114.6	
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	49.77	03/2015 -	03/2022	84	5.85	
44	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	131.63	07/2016 -	03/2022	68	-7.91	
45	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	108.64	03/2019 -	03/2022	36	11.42	
46	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	169.95	03/2019 -	03/2022	36	0	
47	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	16.86	
	<u>South-Eastern Coal Fields Limited</u>									
48	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	209.24	03/2014 -	03/2021	84	0	
49	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	201.48	03/2015 03/2020	03/2022	84	201.44	
50	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	6.50	03/2014 -	03/2022	96	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
51	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	121.28	03/2021 -	03/2022	12	0	
52	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	0	
53	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	130.17	03/2020 -	03/2023	36	0	
54	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	64.12	03/2021 -	03/2024	36	0	
55	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.63	145.83	03/2022 -	03/2025	36	0	
56	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	9.71	03/2023 -	03/2026	36	0	
	<u>Western Coal Fields Limited</u>									
57	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	325.18	246.55	03/2019 -	03/2022	36	63.67	
58	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	12	15.41	
59	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	141.08	03/2021 -	03/2024	36	0	
60	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	295.56	160.23	03/2019 -	03/2025	72	0	
61	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	36	0	
62	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 -	826.80	194.28	03/2020 -	03/2026	72	-2.91	
63	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	304.52	142.28	03/2019 -	03/2026	84	0	
64	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	281.25	20.99	03/2022 -	03/2026	48	0	
65	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA	11/2014	1,184.33 -	1,184.33	368.56	03/2020 -	03/2027	84	0	
	Total		69,601.31 -	63,379.05	23,243.46					
	<u>FINANCE</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Central Public Works Department</u>									
66	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	208.96	205.40	10/2019 -	04/2021	18	-02	
	Total		209.00 -	208.96	205.40					
	<u>FERTILISERS</u>									
	<u>National Fertiliser Limited</u>									
67	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	167.49	11/2019 -	04/2021	17	0	
68	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	218.83	187.51	11/2019 -	04/2021	17	0	
69	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	239.81	186.72	11/2019 -	04/2021	17	0	
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
70	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72 -	426.72	325.19	04/2020 03/2021	05/2021	13	0	
	Total		1,101.28 -	1,101.28	866.91					
	<u>MINES</u>									
	<u>National Aluminum Company Limited (Nalco)</u>									
71	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	5,540.00 6,435.90	5,540.00	721.87	04/2021 12/2022	12/2022	20	0	
72	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	483.00	.92	04/2021 03/2023	03/2023	23	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		6,023.00 -	6,023.00	722.79					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
73	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	18,486.77	05/2015 07/2021	07/2021	74	41.32	
	<u>Rastriya Ispat Nigam Limited</u>									
74	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,551.82	09/2018 04/2021	04/2021	31	0	No
	<u>Steel Authority Of India Limited (Sail)</u>									
75	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	185.40	06/2019 05/2021	05/2021	23	0	
76	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL	12/2018	263.36 -	263.36	213.22	09/2020 -	05/2021	8	0	
77	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	536.50	10/2017 12/2021	12/2021	50	0	
	Total		18,768.09 -	25,183.09	20,973.71					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
78	PUNE POL STORAGE DEPOT - [N16000313]BPCL, MAHARASHTRA	08/2016	282.64 -	282.64	246.11	08/2020 -	03/2021	7	0	
79	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL, MAHARASHTRA	04/2013	449.58 -	449.58	396.13	12/2019 03/2021	04/2021	16	0	
80	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA	11/2014	4,588.29 -	5,245.96	4,977.00	08/2018 11/2019	05/2021	33	14.33	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
81	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	3,288.96	2,925.17	02/2020 03/2021	05/2021	15	-73	
82	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	206.26	129.96	03/2021 -	05/2021	2	0	
83	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	151.16	02/2021 -	05/2021	3	0	
84	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	725.00	06/2019 -	02/2022	32	35.54	
85	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	18.80	02/2017 08/2022	08/2022	66	117.11	
	<u>Chennai Petroleum Corporation Limited</u>									
86	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13	-28.74	
	<u>Gas Authority Of India Limited</u>									
87	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,612.80	12/2020 -	05/2021	5	-30.59	
88	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	197.30	04/2018 -	06/2021	38	-38.98	
89	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00 -	2,433.00	2,109.70	12/2020 12/2021	06/2021	6	0	
90	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	181.70	08/2020 05/2021	06/2021	10	14.17	
91	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 -	217.92	86.30	04/2021 -	10/2021	6	0	
92	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 -	1,933.00	1,263.80	12/2020 12/2021	12/2021	12	0	
93	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00 3,048.00	3,048.00	1,840.50	12/2020 12/2021	12/2021	12	-11.32	
94	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	831.40	12/2020 12/2021	12/2021	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
95	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	40.10	02/2021 -	12/2021	10	9.91	
96	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,607.20	12/2012 02/2022	02/2022	110	102.71	
	<u>Hindustan Petroleum Corporation Limited</u>									
97	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA	11/2017	255.00 300.00	300.00	269.18	11/2020 06/2021	06/2021	7	17.65	
98	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	92.33	07/2020 -	07/2021	12	0	
99	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	130.48	06/2020 12/2021	09/2021	15	0	
100	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	75.31	06/2020 09/2021	09/2021	15	0	
101	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	14,820.60	07/2020 07/2022	07/2022	24	25.5	
102	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 -	3,072.00	2,201.31	06/2021 -	08/2022	14	14.76	
103	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	91.57	09/2026 02/2027	02/2027	5	0	
104	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	153.20	03/2029 08/2029	08/2029	5	0	
	<u>Indian Oil Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
105	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	146.57	01/2021 -	04/2021	3	0	
106	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	157.94	01/2021 -	04/2021	3	0	
107	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	540.76	07/2018 05/2021	05/2021	34	0	
108	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	502.00	421.03	08/2019 06/2021	06/2021	22	18.68	
109	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	93.23	02/2020 06/2021	06/2021	16	0	
110	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	144.29	01/2021 06/2021	06/2021	5	0	
111	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	487.25	02/2020 06/2021	06/2021	16	0	
112	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	254.90	04/2021 -	07/2021	3	0	
113	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	3,027.90	1,933.53	03/2021 -	08/2021	5	66.09	
114	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	205.98	10/2020 -	08/2021	10	0	
115	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 -	206.63	89.71	02/2020 08/2021	08/2021	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
116	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 293.00	293.00	155.76	06/2020 09/2021	09/2021	15	24.15	
117	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	134.82	03/2021 09/2021	09/2021	6	0	
118	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	156.30	01/2021 -	10/2021	9	0	
119	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	94.21	04/2020 10/2021	10/2021	18	0	
120	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	272.27	02/2020 10/2021	10/2021	20	0	
121	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	146.91	08/2021 -	11/2021	3	0	
122	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	63.74	08/2020 11/2021	11/2021	15	0	
123	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	318.04	03/2021 12/2021	12/2021	9	0	
124	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	6,025.00	3,636.76	12/2018 -	02/2022	38	33.98	
125	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	286.33	02/2020 02/2022	02/2022	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
126	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	393.38	10/2017 03/2022	03/2022	53	103.6	
127	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	3,338.00	2,888.48	12/2020 -	03/2022	15	43.82	
128	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	49.54	12/2019 03/2022	03/2022	27	0	
129	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	689.83	10/2021 -	03/2022	5	0	
130	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	301.41	01/2021 03/2022	03/2022	14	0	
131	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	13.16	07/2021 03/2022	03/2022	8	0	
132	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	710.21	08/2020 04/2022	04/2022	20	0	
133	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	462.30	22.97	09/2021 06/2022	06/2022	9	0	
134	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	44.73	06/2021 07/2022	07/2022	13	0	
135	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	34.40	10/2020 08/2022	08/2022	22	0	
136	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	92.80	04/2022 -	02/2023	10	0	
137	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 -	371.00	4.44	09/2022 03/2023	03/2023	6	0	
138	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	2,281.94	431.31	12/2022 07/2023	07/2023	7	0	
139	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	76.47	04/2022 -	08/2023	16	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
140	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	466.87	03/2020 11/2020	06/2021	15	9.64	
141	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,607.38	12/2019 04/2021	10/2021	22	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
142	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	1,846.46	1,550.87	05/2013 12/2020	03/2021	94	114.26	
143	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,775.79	04/2018 05/2021	05/2021	37	5.8	
144	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	624.35	446.72	03/2019 05/2021	05/2021	26	-4.07	
145	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	197.20	05/2020 05/2021	05/2021	12	21.57	
146	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	637.29	12/2020 05/2021	05/2021	5	-3.93	
147	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	25,090.00	11,190.15	06/2020 06/2022	06/2022	24	-26.23	
148	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	1,005.13	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									
149	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021	48	39.05	
150	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	187.00	10/2020 -	03/2021	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	457.91	12/2019 -	04/2021	16	0	
152	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 638.60	652.10	136.05	02/2020 -	04/2021	14	19.89	
153	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	222.21	144.80	08/2020 -	04/2021	8	-1.13	
	Total		1,29,073.92 -	1,36,017.85	76,166.74					
	<u>POWER</u>									
	<u>Central Public Works Department</u>									
154	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	240.96	11/2019 -	06/2021	19	0	
	<u>Chenab Valley Power Projects [P] Limited</u>									
155	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,706.23	04/2020 -	07/2025	63	0	
	<u>National Hydro-Electric Power Corporation</u>									
156	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	8,866.70	09/2009 07/2022	07/2022	154	152.52	
157	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	13,537.76	09/2010 08/2023	08/2023	155	218.08	
	<u>National Thermal Power Corporation</u>									
158	TANDA TPP STAGE-II (2X660 MW) - [N18000175]JNTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,842.02	8,146.60	07/2019 03/2021	03/2021	20	7.11	•Support of UP State Govt. is required in the following areas: Physical possession / Acquisition of balance 8.059 Acres Abadi Land for Main Plant area (6.285 acres) and for Ash Dyke area (1.774 acres).

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
159	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	349.00	226.00	11/2020 -	04/2021	5	0	
160	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 13,140.91	13,140.91	11,701.78	12/2018 02/2021	05/2021	29	4.86	Support of State Govt. of Odisha is required for following: •Balance RoW for 132 kV transmission line for Make Up Water pump house. Acquisition/possession of balance land for Railway siding.
161	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,839.26	07/2012 06/2020	06/2021	107	97.38	Support of State Govt. required for early resolution of acquisition / possession of 42.4355 Acres of critical land balance due to court cases, wrong payments in awarded land and ownership disputes in following areas: Main Plant 21.372 acres Make-Up water corridor: 0.190 acres Ash Dyke 14.8135 acres Township: 6.05 acres De-notification of 17.69 Acres GMM land for Raiyatikaran is critical as construction of Overflow Lagoon of Ash Dyke is held up. The proposal for de-notification is with Revenue Dept. GOB, since 05.02.2020. Report sent by Dist Authorities on 15.12.20.
162	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	1,763.69	12/2018 -	07/2021	31	0	
163	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	418.49	11/2018 -	07/2021	32	0	
164	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	403.62	46.03	06/2021 10/2021	10/2021	4	0	
165	NGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,761.92	05/2018 -	12/2021	43	33.47	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
166	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	501.29	49.76	09/2021 01/2022	01/2022	4	0	
167	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	798.24	31.64	09/2021 01/2022	01/2022	4	0	
168	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	1,722.14	103.85	09/2021 01/2022	01/2022	4	0	
169	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	1,522.71	203.13	09/2021 01/2022	01/2022	4	0	
170	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	1,782.00	69.21	09/2021 01/2022	01/2022	4	0	
171	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 10,997.70	10,997.70	8,310.67	11/2020 07/2022	07/2022	20	3.76	
172	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,389.42	11,672.15	06/2019 10/2022	10/2022	40	7.12	Support of State Govt of Jharkhand is required for following: 1.Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. 2.Acquisition of Land by CCL for external CHP. 3.Early completion of Road Widening and strengthening of SH-7 from Hazaribagh to Bijupara. It is being done on deposit basis by RCD. The road diversion in project area needs to be completed on priority. 4.Repair of damaged bridge over Garhi River is critical for transportation of material for project. 5.Forest clearance in ATS lines.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
173	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,891.26	03/2013 12/2021	12/2022	117	96.99	Award of Srinagar to Kashipur transmission line by PTCUL for power evacuation. Support of State Govt. of Uttarakhand is required for expeditious completion of Transmission line for Power evacuation system. During the meeting held on 16.10.2020 headed by Chairman CEA along PTCUL and NTPC, CEA and NTPC expressed its concern regarding delay in award of critical Srinagar to Kashipur line by PTCUL. It was decided that CEA would request PSPA-I Division, CEA to examine the proposal of PTCUL for construction of Khandulkhal- Koteswar 400kV line, instead of Srinagar (Khandulkhal) – Kashipur (Ranpura) 400 kV D/C line so that the line could be constructed before Jun'22. Also CEA had another meeting with NTPC, PTCUL, CTU and NRLDC on 09.11.20. regarding readiness of Power Evacuation System for TVHPP.
174	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	18,530.80	10/2011 07/2023	07/2023	141	145.16	•Support required for early completion of Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur rail route, which is critical to ease transportation of coal for Barh Project.
175	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,112.00	4,295.79	03/2023 -	09/2024	18	-8.34	Support requested for resolving inter-ministerial issues.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
176	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.54	660.06	09/2019 12/2024	12/2024	63	-0.2	•All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSERC. State Govt is not ready to finalize power evacuation line in absence of PPA. •Shifting of balance Homesteads from Project area. (13 Nos + 01 School)
	<u>Power Grid Corporation Of India Limited</u>									
177	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,634.56	10/2012 11/2020	03/2021	101	5.14	
178	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	808.63	652.14	01/2018 04/2021	04/2021	39	0	
179	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	343.25	04/2018 03/2021	04/2021	36	0	
180	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	14,733.37	11,505.07	11/2019 04/2021	04/2021	17	0	
181	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 219.66	219.66	157.13	07/2019 04/2021	04/2021	21	17.99	
182	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	358.83	246.14	05/2020 05/2021	04/2021	11	0	
183	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE	05/2014	522.29 546.36	546.36	477.69	11/2016 09/2021	05/2021	54	4.61	
184	EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	235.53	148.70	06/2019 08/2021	05/2021	23	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
185	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	2,868.53	07/2020 12/2020	05/2021	10	14.11	
186	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	241.68	04/2016 12/2017	06/2021	62	0	
187	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	89.76	03/2018 -	06/2021	39	0	
188	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	532.79	05/2017 09/2021	06/2021	49	0	
189	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	201.10	02/2019 06/2021	06/2021	28	0	
190	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	229.18	12/2019 06/2021	06/2021	18	0	
191	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	5,070.13	4,060.04	04/2020 06/2021	06/2021	14	0	
192	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,677.06	02/2020 06/2021	06/2021	16	0	
193	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	2,605.89	12/2018 -	12/2021	36	31.08	
194	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,886.91	08/2013 08/2022	08/2022	108	32.24	
195	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	9,129.32	2,056.36	12/2018 -	03/2024	63	92.02	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Thdc India Limited</u>									
196	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21	1,587.16	495.34	09/2020 08/2022	08/2022	23	-24.57	1. Te nancy/Private land (337.35 Ha): Title dispute of land of approx. 400 land holders pending in court of Collector, Singrauli due to which distribution of Compensation to beneficiaries is delayed. 2. Go vt. land for R&R (53.13 Ha): Declaration of the land as "Abadi Land" is pending at GoMP. 3. Govt. land of Coal Block (178.13 Ha): Collector, Singrauli informed that permission under section 247 shall be accorded after grant of Mining Lease which is pending with Director (Mining), GoMP.
197	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	3,860.35	2,207.95	06/2013	12/2023	126	54.94	Environment Clearance of Gadi Quarry is still pending In the meeting of SEIAA held in Nov19 it was informedthat Environmental Clearance for Gadi Quarry shall be given to the owner THDCIL in place of HCC In thiscontext THDCIL has written letter to District Magistrate Chamoli on 13.12.19 to consider the transfer of name ofapplicant from Ms HCC to THDC India Limited in the application of EC DM.
198	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42	11,089.42	1,728.08	09/2023	08/2024	11	0	• Co ntinuous help of District administration is required for expeditious land acquisition. • Co ntinuous help of District administration is required for expeditious shifting of Nagla residents to newly identified land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		1,96,783.14 -	2,53,859.03	1,70,119.09					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Central Public Works Department</u>									
199	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	136.48	03/2020 -	05/2021	14	0	
200	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	43.43	03/2020 -	12/2021	21	0	
201	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	0	
202	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	0	
	<u>HIL Infra Tech Services Limited</u>									
203	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	548.39	04/2020 -	07/2021	15	-8.91	
204	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	469.13	06/2020 -	07/2021	13	-20.7	
205	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	331.55	05/2021 -	07/2022	14	-14.54	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
206	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	250.00	233.39	05/2017 -	03/2021	46	22.29	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
207	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	37	16.33	
208	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	24	.13	
209	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	488.22	11/2013 -	05/2021	90	20.55	
210	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	295.16	03/2019 -	06/2021	27	0	
211	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	237.89	05/2018 -	12/2021	43	0	
	Total		4,940.96 -	4,754.30	3,248.11					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
212	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24	98.88	
213	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24	73.73	
214	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12	.89	
215	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24	0	
216	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12	0	
217	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24	0	
218	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
219	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	36	25.65	
220	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	346.32	316.04	03/2019 -	03/2021	24	0	
	<u>East Central Railways</u>									
221	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	678.54 678.54	929.86	819.61	03/2019 -	05/2021	26	37.04	
222	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	477.88 283.95	751.55	683.91	03/2012 -	07/2021	112	57.27	
223	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	235.00	03/2019 -	03/2022	36	0	
224	GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND	03/2015	348.23 -	348.23	340.60	03/2021 -	03/2022	12	0	
225	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]ECR, BIHAR	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	15	62.06	
226	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	128	229.5	
227	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	36	49.45	
228	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR, BIHAR	12/2015	1,200.20 1,200.20	1,200.20	925.70	03/2020 -	03/2023	36	0	
229	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR, BIHAR	12/2015	1,491.47 -	1,491.47	510.65	03/2020 -	03/2023	36	0	
230	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,165.22	03/2020 -	03/2024	48	0	
231	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR, BIHAR	04/2016	744.04 -	1,215.54	398.20	03/2021 -	03/2024	36	63.37	
	<u>East Coast Railway</u>									
232	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	34	38.43	
233	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 238.03	238.03	221.37	03/2020 03/2021	03/2022	24	52.77	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
234	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	1,160.00 -	1,160.83	902.85	03/2020 -	03/2023	36	.07	
235	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR, ODISHA	04/2015	1,547.38 1,547.38	1,547.38	635.77	03/2022 03/2023	03/2023	12	0	
236	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	843.04 843.04	843.04	223.65	10/2020 03/2024	03/2024	41	0	
237	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	665.93	03/2022 03/2024	03/2024	24	0	
238	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR, ODISHA	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	64	15.45	
239	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR, ODISHA	04/2015	1,172.92 1,172.92	1,172.92	610.79	12/2018 03/2024	03/2024	63	0	
240	TALCHER- BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 1,928.07	1,928.07	864.71	06/2021 03/2025	03/2025	45	137.8	
241	KHURDA ROAD- BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,493.80	03/2009 03/2026	03/2026	204	29.71	
242	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 2,361.74	2,361.74	432.17	03/2022 03/2026	03/2026	48	0	
	<u>Eastern Railways</u>									
243	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28	0	
244	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	542.18 -	663.13	520.48	03/2020 -	03/2021	12	22.31	State Govt. is requested to deposit. for their balance share of cost for the project. But still deposition is awaited.
245	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 -	1,425.44	637.94	02/2013 -	03/2024	133	134.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
246	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	906.05	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30 KM between Kamarpukur and Jairambati is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.
247	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	983.60	12/2010 -	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 238.75 Cr. for their balance share of cost towards project Katwa-Bardhaman G.C.
248	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
249	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	373.47	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
250	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	643.11	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to 41 nos. of un authorized crossings Amghata to Nabadwipghat work is dropped vide Bd's letter No. 2020/W- I/Compliance in Bd Mtg, dated 09.10.2020
251	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.64	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 km).- The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
252	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	186.14	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
253	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	385.60	03/2017 -	03/2025	96	20.3	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non-availability of land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
254	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahath (9.75 Km) New line-- Work could not be started due to non availability of land
255	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	164.05	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahath (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
256	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	106.75	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
257	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
258	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42	0	
259	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21	117.23	
260	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-81.5	
	<u>Metropolitan Rapid Transport Projects</u>									
261	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-82.67	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
262	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
263	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102	48.06	
264	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216	501.57	
	<u>North Central Railway</u>									
265	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	32.02	
	<u>North East Frontier Railway</u>									
266	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	800.00	799.87	03/2019 -	03/2021	24	154.78	
267	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,683.54	12/2008 -	04/2021	148	284.8	
268	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	1,873.21	1,162.39	03/2021 -	05/2021	2	115.07	
269	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	30.26	
270	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	1,043.00	798.53	03/2019 -	03/2023	48	170.77	
271	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	3,838.64	03/2014 -	03/2023	108	130.69	
272	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	2,950.00	1,496.25	03/2022 -	03/2023	12	32.15	
273	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	12,264.15	10,842.65	03/2011 -	12/2023	153	175.34	
274	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	2,145.00	970.88	03/2019 -	03/2024	60	302.54	
275	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	83.64	03/2019 -	03/2024	60	13.6	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
276	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NER,NAGALAND	04/2006	2,326.52 -	6,911.00	1,148.65	03/2015 -	12/2024	117	197.05	
	<u>North Eastern Railway</u>									
277	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	476.60	04/2017 -	03/2021	47	-31.45	
278	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	80.76	12/2019 -	04/2021	16	-12.65	
279	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	68	.16	
280	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	37	61.8	
281	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	238.15	01/2022 -	03/2022	2	-38.88	
282	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
283	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
284	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-32.79	
	<u>North Western Railway</u>									
285	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	375.00	345.38	11/2019 -	03/2021	16	75.73	
286	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	480.00	313.18	03/2020 -	06/2021	15	14.24	
287	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	699.06	02/2019 -	11/2021	33	109.82	
288	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	207.09	03/2020 -	04/2022	25	16.97	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Northern Railway</u>									
289	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	114	211.31	
290	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	63	37.44	
291	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	27,949.00	23,132.28	11/2002 -	12/2022	241	1017.96	
292	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	388.89	
293	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	1,540.13	242.09	03/2023 03/2025	03/2025	24	369.35	
294	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108	0	
	<u>Rail India Technical And Economic Service</u>									
295	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15	0	
	<u>Rail Vikas Nigam Ltd.</u>									
296	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	69	50.15	
297	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	21	281.93	
298	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	21	111.91	
299	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,294.72	03/2020 -	12/2021	21	-7.28	
300	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	12	23.55	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
301	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	3	20.68	
302	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24	124.58	
303	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	102.92	
304	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	39	51.02	
305	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	62.89	
306	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	54.24	
307	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	5.98	
308	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	887.48	03/2023 -	12/2024	21	0	
309	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	108	7.78	
310	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	108	59.22	
311	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	3	40.08	
312	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	18.95	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
313	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	24	42.47	
	<u>South Central Railway</u>									
314	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	704.31 -	927.94	534.34	03/2020 03/2022	06/2021	15	31.75	
315	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	275.34	
316	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	276	98.57	
317	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	180	102.85	
318	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	502.93	03/2010 -	03/2024	168	0	
319	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	12	5.16	
320	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	36	15.49	
321	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,416.78	03/2021 -	03/2024	36	0	
322	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	24	7.06	
323	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	156	42.44	
	<u>South East Central Railway</u>									
324	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12	291.76	
325	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34	116.46	
326	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	9	84.69	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
327	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33	8.23	
328	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24	.07	
329	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36	378.6	
	<u>South Eastern Railway</u>									
330	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	302.95	12/2018 12/2018	06/2021	30	38.92	
331	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	901.11	03/2020 03/2020	12/2021	21	35.38	
332	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	748.34	03/2021 03/2021	12/2023	33	0	
333	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	54.99	
334	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324	130.97	
	<u>South Western Railway</u>									
335	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	15	33.31	
336	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021	15	35.47	
337	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023	36	43.14	
338	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	312.23	03/2016 -	12/2023	93	0	
339	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	35.29	03/2016 -	12/2023	93	0	
340	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	
341	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
342	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 03/2024	03/2024	60	15.84	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
343	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	998.00	463.45	03/2017 03/2025	03/2025	96	54.78	
344	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	304.83	12/2018 -	06/2025	78	0	
	<u>Southern Railway</u>									
345	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	253.33	
346	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-23.24	
347	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	102.11	
348	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	60	465.83	
349	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	73	301.67	
350	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
351	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	105	1699.64	
	<u>West Central Railway</u>									
352	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,229.79	03/2021 03/2029	03/2023	24	585.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
353	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93	1,762.94	1,153.73	03/2020	03/2023	36	-06	Work is suffering badly on this Critical project due pending forest land clearance. The detail position is as under: ↳ Niwas Road to Deoragram: Forest land 46.067 Ha from Railway Km 1261 to 1301 under DFO Singrauli in isolated patches. Application has been uploaded on Sep'2018. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 2055 Nos. trees cutting have been submitted on 18.06.2020 and 21.07.2020. However, APCCF/Bhopal vide letter dated 31.07.2020 has sought clarifications from MOEF. MOEF vide letter dated 24.09.2020 has clarified that case need to be processed further in FCA. GM/WCR vide letter dated 09.10.2020 has requested Railway Board to intervene in this matter. A meeting was held in Collector Singrauli office on 12.12.20. This meeting was chaired by Hon'ble MP/ Sidhi Smt Riti Pathak. Collector Singrauli has been requested to expedite this proposal. ↳ Vijaysota to Beohari: Forest Land 66.69 Ha under DFO Shahdol from Rly Km 1162 to 1189 in isolated patches. Application has been uploaded in Feb'2019. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 17454 Nos trees cutting have been submitted on 18.08.2020

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
354	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	0	
355	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	296.52	03/2022 -	03/2023	12	114.32	
356	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	3230.57	
	<u>Western Railway</u>									
357	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 890.76	890.76	745.11	03/2019 10/2021	10/2021	31	61.51	
358	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	1,389.05	1,125.73	03/2021 12/2021	12/2021	9	33.93	
359	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	1,002.39	653.86	03/2021 12/2022	12/2022	21	0	
360	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 411.62	411.62	126.05	03/2012 03/2023	03/2023	132	29.34	
361	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	1,347.26	907.54	03/2022 03/2023	03/2023	12	0	
362	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	866.42	03/2022 03/2023	03/2023	12	0	
363	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48	329.77	
364	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	254.73	06/2020 03/2023	03/2023	33	-13.76	
365	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	5,912.40	2,161.74	03/2022 03/2024	03/2024	24	68.75	
366	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	1,959.74	1,799.00	03/2020 03/2024	03/2024	48	136.19	
	Total		2,00,935.84 -	3,21,844.05	1,58,881.73					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
367	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	173.41	141.65	08/2018 -	03/2021	31	4.33	
368	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	170.96	08/2018 09/2021	03/2021	31	4.45	
369	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	271.45	225.81	10/2015 03/2021	03/2021	65	0	
370	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71	0	
371	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	254.30	99.36	10/2020 -	03/2021	5	0	
372	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	105.72	08/2018 03/2021	03/2021	31	0	
373	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	187.82	131.74	04/2018 -	03/2021	35	0	
374	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
375	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 634.30	536.65	539.22	12/2019 03/2021	03/2021	15	0	
376	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	14	0	
377	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	210.31	05/2019 -	03/2021	22	0	
378	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	218.90	129.83	03/2020 -	03/2021	12	0	
379	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	175.51	10/2019 -	03/2021	17	0	
380	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	120.68	08/2020 -	03/2021	7	0	
381	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	273.27	01/2018 03/2021	03/2021	38	0	
382	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47	77.26	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
383	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	756.69	02/2020 04/2021	04/2021	14	0	
384	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	218.70	103.81	11/2020 04/2020	04/2021	5	0	
385	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	195.13	07/2018 03/2021	04/2021	33	0	
386	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	687.99	06/2019 04/2021	04/2021	22	0	
387	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	293.60	11/2017 04/2021	04/2021	41	0	
388	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	476.77	05/2016 08/2021	04/2021	59	0	
389	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34	0	
390	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	61.53	09/2018 -	04/2021	31	0	
391	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	49	46.51	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
392	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.43	04/2020 -	04/2021	12	-8.28	
393	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	242.97	09/2019 11/2020	05/2021	20	0	
394	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	573.85	07/2018 05/2021	05/2021	34	0	
395	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	170.57	54.53	11/2020 -	05/2021	6	0	
396	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	279.86	08/2018 05/2021	05/2021	33	0	
397	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021	44	0	
398	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	
399	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	172.63	09/2020 -	05/2021	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
400	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021	128	69.3	
401	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021	128	93.8	
402	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	439.63	01/2020 01/2021	06/2021	17	0	
403	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	375.50	08/2017 06/2021	06/2021	46	0	
404	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	129.98	03/2018 -	06/2021	39	0	
405	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	46.52	03/2018 -	06/2021	39	0	
406	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	117.94	02/2018 06/2021	06/2021	40	0	
407	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	123.20	03/2017 -	06/2021	51	0	
408	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	158.22	03/2018 -	06/2021	39	0	
409	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	06/2021	40	0	
410	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	06/2021	39	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
411	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	197.04	09/2019 06/2021	06/2021	21	0	
412	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 -	372.68	214.00	02/2017 06/2021	06/2021	52	0	
413	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37	0	
414	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	351.92	03/2018 06/2021	06/2021	39	9.23	
415	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	572.66	270.56	08/2016 06/2021	06/2021	58	15.19	
416	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	269.15	06/2017 06/2021	06/2021	48	0	
417	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	544.00	400.38	09/2016 06/2021	06/2021	57	14.24	
418	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	731.50	416.16	10/2016 06/2021	06/2021	56	17.04	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
419	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	435.61	94.34	07/2016 06/2021	06/2021	59	-3.83	
420	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	240.11	03/2015 06/2021	06/2021	75	0	
421	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	78.69	05/2019 06/2021	06/2021	25	0	
422	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	272.43	11/2017 06/2021	06/2021	43	0	
423	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6	0	
424	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	290.15	214.00	05/2017 07/2021	07/2021	50	0	
425	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021	59	0	
426	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	110.19	08/2020 07/2021	07/2021	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
427	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	322.48	271.72	07/2020 -	08/2021	13	0	
428	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	692.14	10/2019 -	08/2021	22	0	
429	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	69.34	03/2018 -	09/2021	42	0	
430	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	24.84	
431	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	85.70	03/2021 11/2021	11/2021	8	0	
432	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15	0	
433	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28	11.18	
434	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24	0	
435	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	-	11/2020 -	08/2022	21	-12	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
436	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	213.97	25.03	08/2019 -	11/2022	39	33.51	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
437	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	149.44	04/2017 03/2018	03/2021	47	0	
438	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	201.60	01/2016 -	04/2021	63	0	
439	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	387.00	298.08	08/2016 -	05/2021	57	3.73	
440	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	339.55	282.82	08/2016 -	05/2021	57	-14.37	
441	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	340.00	238.26	08/2016 -	05/2021	57	-20.84	
442	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	457.77	161.37	10/2018 -	10/2021	36	-11.55	
443	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL, NAGALAND	03/2018	215.12 -	215.12	100.90	09/2018 -	11/2021	38	0	
444	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	407.30	100.07	06/2018 -	12/2021	42	-6.88	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
445	FOUR LANE OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM)	06/2015	463.49 -	398.06	145.21	06/2018 -	12/2021	42	-14.12	
446	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	315.03	88.48	09/2018 -	12/2021	39	0	
447	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	240.64	102.94	09/2018 -	12/2021	39	0	
448	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	60.55	09/2018 -	12/2021	39	0	
449	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	0	
450	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	102.00	09/2018 -	05/2022	44	0	
451	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57 -	339.57	141.44	09/2018 -	07/2022	46	0	
452	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL, NAGALAND	03/2018	285.68 -	285.68	77.86	09/2018 -	09/2022	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
453	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	44.52	09/2018 -	10/2022	49	0	
454	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	336.49	79.44	09/2018 -	11/2022	50	-32.71	
455	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	42.55	09/2018 -	11/2022	50	0	
456	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	65.01	09/2019 -	04/2023	43	0	
457	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	47.39	09/2019 -	04/2023	43	0	
458	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	58.49	09/2019 -	04/2023	43	0	
459	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	33.18	09/2019 -	06/2023	45	0	
460	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	72.44	09/2019 -	06/2023	45	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
461	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	18.08	09/2019 -	07/2023	46	0	
462	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	59.92	09/2019 -	09/2023	48	0	
463	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	50.49	09/2019 -	04/2024	55	0	
	<u>National Highways Authority Of India</u>									
464	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,559.00	03/2013 -	03/2021	96	0	
465	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021	81	0	
466	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71	52.73	
467	FOUR LANNING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	974.60	11/2018 07/2019	03/2021	28	-25.83	
468	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	421.01	08/2018 -	03/2021	31	0	
469	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	522.80	06/2018 10/2020	03/2021	33	0	
470	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	555.68	08/2019 -	03/2021	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
471	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	70.85	03/2019 -	03/2021	24	0	
472	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	2,499.00	1,582.36	03/2021 10/2021	04/2021	1	63.05	
473	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,288.54	08/2013 -	05/2021	93	0	
474	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	552.90	597.77	03/2020 05/2021	05/2021	14	-13.58	
475	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-3.27	
476	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	44	9.67	Additional land acquisition
477	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	730.97	642.54	05/2018 06/2021	06/2021	37	37.63	
478	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	690.17	594.57	05/2018 06/2021	06/2021	37	16.34	
479	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	373.68	05/2018 04/2019	06/2021	37	-2	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
480	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15	10.24	
481	REHABILITATION AND UPGRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	0	
482	SIX-LANING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15	3.95	
483	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	166.90	54.22	05/2013 -	08/2021	99	-55.37	
484	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	0	
485	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 -	756.27	363.86	03/2020 -	09/2021	18	.23	
486	4-LANING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15	0	
487	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	546.00	307.08	07/2019 06/2021	12/2021	29	0	
488	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	591.66	318.30	07/2019 06/2021	12/2021	29	0	
489	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42 -	870.00	336.58	03/2019 01/2021	12/2021	33	-25.48	
490	FOUR LANING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI, TAMIL NADU	03/2017	848.45 932.23	848.45	222.06	03/2020 -	12/2021	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
491	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	537.28	12/2019 -	12/2021	24	0	
492	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	8.56	04/2014 -	01/2022	93	0	
493	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54	0	
494	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,868.67	08/2013 -	03/2022	103	0	
495	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	209.18	03/2019 12/2021	03/2022	36	0	
496	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	125.51	03/2019 03/2022	03/2022	36	0	
497	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	333.22	03/2020 -	04/2022	25	0	
498	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	349.24	05/2020 -	05/2022	24	0	
499	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	462.14	08/2017 -	07/2022	59	0	
500	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	566.14	09/2017 -	07/2022	58	0	
501	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105	18.66	Land Acquisition issue.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		77,324.48 -	80,483.35	48,522.06					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
502	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	431.16	-	06/2021 -	11/2021	5	0	
	<u>Central Public Works Department</u>									
503	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	133.09	03/2018 -	06/2021	39	0	
	<u>Department Of Telecommunication</u>									
504	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	71	84.97	
	Total		14,013.36 -	25,343.36	16,727.09					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
505	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	8,706.79	12/2018 -	08/2022	44	18.69	
	<u>Bangalore Metro Rail Corporation Limited</u>									
506	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	17,021.86	02/2019 03/2021	06/2024	64	16.25	
	<u>Central Public Works Department</u>									
507	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	69.02	03/2021 07/2021	07/2021	4	0	
508	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	106.16	04/2019 06/2021	12/2021	32	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
509	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19	0	
510	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41	-6.71	
	<u>Chennai Metro Rail Ltd</u>									
511	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	3,770.00	3,088.12	03/2018 -	03/2021	36	0	
	<u>Delhi Metro Rail Corporation</u>									
512	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021	66	0	
513	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	511.60	12/2020 -	09/2021	9	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
514	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 09/2022	03/2023	98	44.39	
	Total		1,05,425.47 -	1,21,920.25	86,491.23					
	<u>WATER RESOURCES</u>									
	<u>Brahmaputra Board</u>									
515	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPP,MAHARASHTRA	03/2017	233.57 -	233.57	173.71	12/2019 -	12/2021	24	0	
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
516	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	225.77	271.22	03/2020 -	03/2021	12	0	
517	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	191.62	53.08	11/2020 03/2021	03/2021	4	0	
518	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	236.15	28.53	12/2020 06/2021	06/2021	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
519	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14	0	
520	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	-	08/2021 -	12/2021	4	0	
	<u>Delhi Jal Board</u>									
521	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	515.07	314.33	01/2021 -	06/2021	5	0	
522	REHABILITATION AND UPGRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	64.03	12/2021 -	12/2022	12	0	
523	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	129.67	02/2022 -	12/2022	10	0	
	<u>Hindustan Steelwork Construction Limited</u>									
524	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	721.37	712.37	03/2015 -	03/2021	72	-24.54	
	<u>Kolkata Metropolitan Development Authority</u>									
525	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	272.32	214.52	04/2020 -	03/2021	11	0	
526	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	274.76	201.30	12/2019 05/2021	05/2021	17	0	
527	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022 -	06/2022	4	13.23	
528	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022 -	10/2022	8	-3.29	
	<u>Polavaram Project Authority</u>									
529	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	17,025.01	03/2020 11/2021	04/2022	25	447.22	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Uttar Pradesh Jal Nigam</u>									
530	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH	10/2016	370.40 430.49	430.49	376.22	08/2020 03/2021	03/2021	7	16.22	
531	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	161.31	91.38	11/2019 -	03/2021	16	0	
532	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	460.45	216.89	12/2020 -	05/2021	5	0	
533	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	06/2022	11	-28.25	
	<u>Uttarakhand Pey Jal Nigam</u>									
534	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARA KHAND	03/2017	158.00 -	158.00	78.59	11/2019 03/2021	03/2021	16	0	
	Total		15,804.03 -	60,964.10	20,114.21					
	<u>DEFENCE PRODUCTION</u>									
	<u>Central Public Works Department</u>									
535	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	123.83	02/2020 -	06/2021	16	0	
	Total		246.31 -	246.31	123.83					
	<u>HUMAN RESOURCE DEVELOPMENT</u>									
536	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	20	1.85	
537	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6	10.22	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
538	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	350.69	274.98	04/2019 -	04/2021	24	19.28	
539	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	0	
540	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15	0	
541	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	0	
542	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52	.57	
543	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	387.83	194.72	05/2020 -	02/2022	21	-9.81	
544	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	149.00	03/2022 -	06/2022	3	0	
545	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	0	
546	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD,PUNJAB	10/2019	348.24 -	348.24	15.55	05/2022 -	08/2022	3	0	
547	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	0	
548	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 375.00	375.00	48.46	09/2020 -	11/2022	26	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
549	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	0	
	Total		6,229.82 -	6,276.31	1,822.25					
	<u>HOME AFFAIRS</u>									
550	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	26	64.04	
551	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 238.00	238.00	171.19	04/2018 12/2021	12/2021	44	46.12	
	Total		1,382.09 -	2,238.00	1,077.23					
	<u>RURAL DEVELOPMENT</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
552	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	70	3.96	
553	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	58	2.23	
554	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	12/2021	60	0	
	Total		527.83 -	538.27	460.04					
	<u>CULTURE DEVELOPMENT</u>									
555	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	148.33	09/2017 -	03/2021	42	0	Non receipt of payment from Client

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		151.33 -	151.33	148.33					
	<u>DPIIT</u>									
	<u>Delhi Mumbai Industrial Corridor</u>									
556	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 01/2014	07/2021	22	9.8	
	<u>India International Convention And Expo Centre</u>									
557	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	5,178.00	2,432.15	12/2019 -	12/2021	24	8.49	
	Total		17,352.09 -	18,990.30	11,147.22					
	Grand Total		9,41,540.20	12,18,511.14	7,02,411.67					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,922.21	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00 -	17,079.00	13,158.00	12/2016 -	03/2023	38.63	75
	Total		27,271.00 -	40,499.00	35,568.21				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	5.78	33
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	7.88	12
	Total		1,559.23 -	1,673.33	615.65				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	18.35	04/2018 -	06/2022	37.56	50
7	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	38.59	03/2017 -	03/2022	12.20	60
	<u>Neyveli Lignite Corporation</u>								
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00 -	17,237.80	11,452.38	11/2021 -	07/2022	.00	8
	<u>Singareni Colliers Company Limited</u>								
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	288.72	03/2015 -	03/2022	114.60	84
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	108.64	03/2019 -	03/2022	11.42	36
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	49.77	03/2015 -	03/2022	5.85	84

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>								
13	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	201.48	03/2015 -	03/2022	201.44	84
	<u>Western Coal Fields Limited</u>								
14	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	.00	36
15	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 -	325.18	246.55	03/2019 -	03/2022	63.67	36
16	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	15.41	12
	Total		20,139.31 -	21,075.23	12,977.47				
	<u>DPIIT</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>								
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,432.15	12/2019 -	12/2021	8.49	24
	Total		17,352.09 -	18,990.30	11,147.22				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
19	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	16.33	37
20	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	233.39	05/2017 -	03/2021	22.29	46
21	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	.13	24
22	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	488.22	11/2013 -	05/2021	20.55	90
	Total		1,043.69 -	1,199.69	1,144.29				
	<u>HOME AFFAIRS</u>								
	<u>Central Public Works Department</u>								
23	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	171.19	04/2018 -	12/2021	46.12	44

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
24	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	64.04	26
	Total		1,382.09 -	2,238.00	1,077.23				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
25	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	10.22	6
26	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	274.98	04/2019 -	04/2021	19.28	24
27	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	.57	52
28	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	-	1.85	20
	Total		1,525.49 -	1,614.15	1,088.57				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
29	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	18.80	02/2017 -	08/2022	117.11	66
30	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	725.00	06/2019 -	02/2022	35.54	32
31	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,977.00	08/2018 -	05/2021	14.33	33
	<u>Gas Authority Of India Limited</u>								
32	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 -	247.90	40.10	02/2021 -	12/2021	9.91	10
33	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	181.70	08/2020 -	06/2021	14.17	10
34	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,607.20	12/2012 -	02/2022	102.71	110
	<u>Hindustan Petroleum Corporation Limited</u>								
35	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	269.18	11/2020 -	06/2021	17.65	7
36	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	2,201.31	06/2021 -	08/2022	14.76	14

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
37	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	14,820.60	07/2020 -	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								
38	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	293.00	155.76	06/2020 -	09/2021	24.15	15
39	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	421.03	08/2019 -	06/2021	18.68	22
40	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	393.38	10/2017 -	03/2022	103.60	53
41	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	1,933.53	03/2021 -	08/2021	66.09	5
42	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	2,888.48	12/2020 -	03/2022	43.82	15
43	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	3,636.76	12/2018 -	02/2022	33.98	38
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
44	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	466.87	03/2020 -	06/2021	9.64	15
	<u>Oil & Natural Gas Corporation Limited</u>								
45	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	197.20	05/2020 -	05/2021	21.57	12
46	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,846.46	1,550.87	05/2013 -	03/2021	114.26	94
47	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,775.79	04/2018 -	05/2021	5.80	37
48	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	1,005.13	03/2022 -	05/2023	23.16	14
	<u>Oil India Limited</u>								
49	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	455.00	03/2017 -	03/2021	39.05	48
50	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	136.05	02/2020 -	04/2021	19.89	14
	Total		52,580.91 -	70,049.13	42,856.74				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
51	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	8,866.70	09/2009 -	07/2022	152.52	154

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
52	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,992.43	13,537.76	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								
53	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,891.26	03/2013 -	12/2022	96.99	117
54	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	9,842.02	8,146.60	07/2019 -	03/2021	7.11	20
55	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,839.26	07/2012 -	06/2021	97.38	107
56	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,997.70	8,310.67	11/2020 -	07/2022	3.76	20
57	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,140.91	11,701.78	12/2018 -	05/2021	4.86	29
58	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	11,672.15	06/2019 -	10/2022	7.12	40
59	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	15,761.92	05/2018 -	12/2021	33.47	43
60	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	21,312.11	18,530.80	10/2011 -	07/2023	145.16	141
	<u>Power Grid Corporation Of India Limited</u>								
61	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	157.13	07/2019 -	04/2021	17.99	21
62	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	477.69	11/2016 -	05/2021	4.61	54
63	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	2,868.53	07/2020 -	05/2021	14.11	10
64	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,634.56	10/2012 -	03/2021	5.14	101
65	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	2,605.89	12/2018 -	12/2021	31.08	36
66	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,056.36	12/2018 -	03/2024	92.02	63
67	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,886.91	08/2013 -	08/2022	32.24	108
	<u>Thdc India Limited</u>								
68	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,207.95	06/2013 -	12/2023	54.94	126
	Total		1,19,401.05 -	1,78,550.29	138,153.92				
	<u>RAILWAYS</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Central Railways</u>								
69	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89	12
70	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	73.73	24
71	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	98.88	24
	<u>Container Corporation Of India</u>								
72	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	25.65	36
	<u>East Central Railways</u>								
73	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	683.91	03/2012 -	07/2021	57.27	112
74	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	49.45	36
75	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	819.61	03/2019 -	05/2021	37.04	26
76	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	229.50	128
77	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	62.06	15
78	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	398.20	03/2021 -	03/2024	63.37	36
	<u>East Coast Railway</u>								
79	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	221.37	03/2020 -	03/2022	52.77	24
80	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	15.45	64
81	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	902.85	03/2020 -	03/2023	.07	36
82	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	38.43	34
83	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	864.71	06/2021 -	03/2025	137.80	45
84	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,493.80	03/2009 -	03/2026	29.71	204
	<u>Eastern Railways</u>								
85	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108
86	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	385.60	03/2017 -	03/2025	20.30	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
87	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01	240
88	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	34.08	228
89	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	663.13	520.48	03/2020 -	03/2021	22.31	12
90	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	164.05	02/2012 -	03/2025	36.15	157
91	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	103.64	03/2017 -	03/2025	29.20	96
92	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	643.11	03/2016 -	03/2025	7.75	108
93	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	637.94	02/2013 -	03/2024	134.80	133
94	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	906.05	03/2019 12/2009	03/2025	36.22	72
95	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	373.47	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
96	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	.00	42
97	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	117.23	21
	<u>Metropolitan Rapid Transport Projects</u>								
98	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	48.06	102
99	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	501.57	216
100	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>								
101	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
102	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26	24
103	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	800.00	799.87	03/2019 -	03/2021	154.78	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
104	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,043.00	798.53	03/2019 -	03/2023	170.77	48
105	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,162.39	03/2021 -	05/2021	115.07	2
106	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING [N22000183]	04/2013	1,798.00 -	2,042.51	83.64	03/2019 -	03/2024	13.60	60
107	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	970.88	03/2019 -	03/2024	302.54	60
108	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,496.25	03/2022 -	03/2023	32.15	12
109	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,683.54	12/2008 -	04/2021	284.80	148
110	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	3,838.64	03/2014 -	03/2023	130.69	108
111	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,911.00	1,148.65	03/2015 -	12/2024	197.05	117
112	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	10,842.65	03/2011 -	12/2023	175.34	153
	<u>North Eastern Railway</u>								
113	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	.16	68
114	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	61.80	37
	<u>North Western Railway</u>								
115	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	345.38	11/2019 -	03/2021	75.73	16
116	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	480.00	313.18	03/2020 -	06/2021	14.24	15
117	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	207.09	03/2020 -	04/2022	16.97	25
118	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	699.06	02/2019 -	11/2021	109.82	33
	<u>Northern Railway</u>								
119	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	37.44	63
120	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	211.31	114
121	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.09	03/2023 -	03/2025	369.35	24
122	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	388.89	140

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
123	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	27,949.00	23,132.28	11/2002 -	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>								
124	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	50.15	69
125	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	5.98	33
126	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	51.02	39
127	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	62.89	39
128	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	54.24	24
129	BINA - KOTA DOUBLING WITH RE - [N22000414	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	23.55	12
130	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	20.68	3
131	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	111.91	21
132	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92	88
133	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	281.93	21
134	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95	141
135	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	42.47	24
136	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	124.58	24
137	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	7.78	108
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	59.22	108
139	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	40.08	3
	<u>South Central Railway</u>								
140	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	275.34	9
141	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	704.31 -	927.94	534.34	03/2020 -	06/2021	31.75	15

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
142	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95	1,952.68	567.51	03/2023	03/2024	5.16	12
143	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20	2,120.16	883.52	03/2009	03/2024	102.85	180
144	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70	2,643.25	1,231.85	03/2021	03/2024	15.49	36
145	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77	3,037.95	350.54	03/2014	03/2027	42.44	156
146	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [N220100205]	04/1997	1,723.00	3,421.35	1,895.77	03/2000	03/2023	98.57	276
147	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00	3,887.48	1,144.64	03/2022	03/2024	7.06	24
	<u>South East Central Railway</u>								
148	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	1,096.00	39.79	12/2021	12/2024	378.60	36
149	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93	1,268.32	941.56	02/2019	12/2021	116.46	34
150	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00	1,370.94	470.49	12/2021	12/2023	.07	24
151	GONDIA-JABALPUR(GC),(SECR) - [N220100186]	02/1997	511.86	2,005.25	1,777.22	04/2020	04/2021	291.76	12
152	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00	2,135.34	351.35	03/2021	12/2023	8.23	33
153	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51	3,524.81	982.38	03/2023	12/2023	84.69	9
	<u>South Eastern Railway</u>								
154	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20	358.68	302.95	12/2018	06/2021	38.92	30
155	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00	1,009.00	7.96	03/2015	03/2025	54.99	120
156	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83	1,312.96	901.11	03/2020	12/2021	35.38	21
157	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40	2,373.00	485.04	03/2003	03/2030	130.97	324
	<u>South Western Railway</u>								
158	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00	783.00	620.29	03/2020	06/2021	35.47	15
159	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78	998.00	463.45	03/2017	03/2025	54.78	96
160	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43	1,147.00	911.86	03/2020	06/2021	33.31	15
161	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94	1,656.00	1,160.49	03/2020	03/2023	43.14	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
162	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 -	03/2024	15.84	60
	<u>Southern Railway</u>								
163	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) [N22000441]	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	253.33	198
164	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11	27
165	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	465.83	60
166	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	1,699.64	105
167	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	301.67	73
	<u>West Central Railway</u>								
168	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	296.52	03/2022 -	03/2023	114.32	12
169	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,229.79	03/2021 -	03/2023	585.35	24
170	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
171	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	411.62	126.05	03/2012 -	03/2023	29.34	132
172	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION [N22000487]	02/1991	551.51 -	890.76	745.11	03/2019 -	10/2021	61.51	31
173	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77	48
174	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,389.05	1,125.73	03/2021 -	12/2021	33.93	9
175	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,959.74	1,799.00	03/2020 -	03/2024	136.19	48
176	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	5,912.40	2,161.74	03/2022 -	03/2024	68.75	24
	Total		1,37,034.98 -	2,68,383.97	138,166.85				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
177	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	173.41	141.65	08/2018 -	-	4.33	31

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
178	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	25.03	08/2019 -	11/2022	33.51	39
179	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	170.96	08/2018 -	-	4.45	31
180	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	12/2021	11.18	28
181	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	295.96	10/2010 -	06/2021	69.30	128
182	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	325.42	10/2010 -	06/2021	93.80	128
183	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	351.92	03/2018 -	06/2021	9.23	39
184	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	400.38	09/2016 -	06/2021	14.24	57
185	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	572.66	270.56	08/2016 -	06/2021	15.19	58
186	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	46.51	49
187	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	416.16	10/2016 -	06/2021	17.04	56
188	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	77.26	47
189	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84	73
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
190	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	298.08	08/2016 -	05/2021	3.73	57
	<u>National Highways Authority Of India</u>								
191	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	690.17	594.57	05/2018 -	06/2021	16.34	37
192	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	730.97	642.54	05/2018 -	06/2021	37.63	37
193	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	363.86	03/2020 -	09/2021	.23	18

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
194	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	3.95	15
195	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	9.67	44
196	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	10.24	15
197	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	2,499.00	1,582.36	03/2021 -	04/2021	63.05	1
198	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	52.73	71
199	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66	105
	Total		16,924.25 -	21,555.93	15,231.76				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
200	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	3.96	70
201	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	2.23	58
	Total		352.34 -	362.78	335.17				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
202	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	18,486.77	05/2015 -	07/2021	41.32	74
	Total		15,525.00 -	21,940.00	18,486.77				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
203	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	84.97	71
	Total		13,334.00 -	24,664.00	16,594.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
204	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	8,706.79	12/2018 -	08/2022	18.69	44
	<u>Bangalore Metro Rail Corporation Limited</u>								
205	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	02/2014	26,405.14 -	30,695.12	17,021.86	02/2019 -	06/2024	16.25	64
	<u>Mumbai Metro Rail Corporation Ltd</u>								
206	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	44.39	98
	Total		60,314.14 -	76,888.12	42,768.01				
	<u>WATER RESOURCES</u>								
	<u>Kolkata Metropolitan Development Authority</u>								
207	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23	4
	<u>Polavaram Project Authority</u>								
208	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	17,025.01	03/2020 -	04/2022	447.22	25
	<u>Uttar Pradesh Jal Nigam</u>								
209	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009	10/2016	370.40 -	430.49	376.22	08/2020 -	03/2021	16.22	7
	Total		10,719.87 -	56,204.05	17,401.23				
	Grand Total		4,96,459.44	8,05,887.97	493,613.09				

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,922.21	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,158.00	12/2016 -	03/2023	38.63
	Total		27,271.00 -	40,499.00	35,568.21			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	5.78
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	51.11	09/2021 -	09/2021	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	7.88
	Total		1,905.50 -	2,153.66	666.76			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
7	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	18.35	04/2018 -	06/2022	37.56
8	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	38.59	03/2017 -	03/2022	12.20
	<u>Eastern Coal Fields Limited</u>							
9	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	606.30	08/2019 -	-	93.35
	<u>Neyveli Lignite Corporation</u>							
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,404.29	12/2015 -	02/2021	35.10
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11,452.38	11/2021 -	07/2022	.00
	<u>Singareni Colliers Company Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86
13	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	108.64	03/2019 -	03/2022	11.42
14	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	49.77	03/2015 -	03/2022	5.85
15	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	288.72	03/2015 -	03/2022	114.60
	<u>South-Eastern Coal Fields Limited</u>							
16	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	201.48	03/2015 -	03/2022	201.44
	<u>Western Coal Fields Limited</u>							
17	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	85.82	03/2023 -	03/2023	117.98
18	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	15.41
19	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 -	325.18	246.55	03/2019 -	03/2022	63.67
20	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	.00
	Total		28,896.09 -	34,612.18	21,073.88			
	<u>DPIIT</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
21	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>							
22	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,432.15	12/2019 -	12/2021	8.49
	Total		17,352.09 -	18,990.30	11,147.22			
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
23	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>							
24	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	488.22	11/2013 -	05/2021	20.55
25	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	233.39	05/2017 -	03/2021	22.29
26	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
27	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
28	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71
29	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	16.33
30	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
31	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	.13
32	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	143.04	-	06/2021	21.58
33	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	231.05	-	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>							
34	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	682.54	09/2021 -	09/2021	8.88
	Total		5,589.39 -	6,287.30	3,482.07			
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
35	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	64.04
36	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	171.19	04/2018 -	12/2021	46.12
	Total		1,382.09 -	2,238.00	1,077.23			
	<u>HUMAN RESOURCE DEVELOPMENT</u>							
37	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	.57
38	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	274.98	04/2019 -	04/2021	19.28
39	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	-	1.85
40	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	10.22
	<u>Rail India Technical And Economic Service</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
41	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	-	09/2014 -	-	29.31
	Total		2,009.81 -	2,240.41	1,088.57			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
42	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	4,977.00	08/2018 -	05/2021	14.33
43	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	18.80	02/2017 -	08/2022	117.11
44	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	725.00	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							
45	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,607.20	12/2012 -	02/2022	102.71
46	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	04/2017	287.49 -	345.15	200.10	04/2022 -	04/2022	20.06
47	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 -	247.90	40.10	02/2021 -	12/2021	9.91
48	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	181.70	08/2020 -	06/2021	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
49	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	14,820.60	07/2020 -	07/2022	25.50
50	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	09/2015	4,199.00 -	5,060.00	4,486.77	03/2020 -	-	20.50
51	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	2,201.31	06/2021 -	08/2022	14.76
52	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312	11/2017	255.00 -	300.00	269.18	11/2020 -	06/2021	17.65
	<u>Indian Oil Corporation Limited</u>							
53	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	1,236.00	393.38	10/2017 -	03/2022	103.60
54	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00 -	3,027.90	1,933.53	03/2021 -	08/2021	66.09
55	PARADIP HYDERABAD PIPELINE - [N16000194	01/2015	2,321.00 -	3,338.00	2,888.48	12/2020 -	03/2022	43.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
56	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 -	502.00	421.03	08/2019 -	06/2021	18.68
57	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	3,636.76	12/2018 -	02/2022	33.98
58	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	08/2017	236.00 -	293.00	155.76	06/2020 -	09/2021	24.15
59	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT [N16000336	03/2018	588.20 -	730.20	77.30	- -	05/2023	24.14
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
60	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	637.00	466.87	03/2020 -	06/2021	9.64
	<u>Oil & Natural Gas Corporation Limited</u>							
61	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,846.46	1,550.87	05/2013 -	03/2021	114.26
62	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,375.90	2,775.79	04/2018 -	05/2021	5.80
63	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239	12/2015	823.27 -	1,137.79	667.03	03/2023 -	03/2022	38.20
64	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	07/2016	249.85 250.00	303.75	197.20	05/2020 -	05/2021	21.57
65	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	04/2019	3,228.80 -	3,976.67	1,005.13	03/2022 -	05/2023	23.16
66	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	05/2019	3,660.71 -	3,740.05	2,521.33	05/2021 -	05/2021	2.17
	<u>Oil India Limited</u>							
67	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	490.24	455.00	03/2017 -	03/2021	39.05
68	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	652.10	136.05	02/2020 -	04/2021	19.89
	Total		62,139.58 -	81,062.32	50,809.27			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
69	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	9,897.59	8,866.70	09/2009 -	07/2022	152.52
70	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	19,992.43	13,537.76	09/2010 -	08/2023	218.08

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>National Thermal Power Corporation</u>							
71	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	15,105.22	13,657.43	01/2018 -	02/2021	29.79
72	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,891.26	03/2013 -	12/2022	96.99
73	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	9,842.02	8,146.60	07/2019 -	03/2021	7.11
74	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,140.91	11,701.78	12/2018 -	05/2021	4.86
75	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	11,672.15	06/2019 -	10/2022	7.12
76	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,839.26	07/2012 -	06/2021	97.38
77	NGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	15,761.92	05/2018 -	12/2021	33.47
78	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	11,130.00	02/2017 -	01/2021	24.87
79	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	18,530.80	10/2011 -	07/2023	145.16
80	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	7.55
81	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	17.95
82	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	12.95
83	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,997.70	8,310.67	11/2020 -	07/2022	3.76
84	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,380.97	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>							
85	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	8,154.50	12/2009 06/2016	02/2021	217.49
	<u>Power Grid Corporation Of India Limited</u>							
86	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,634.56	10/2012 -	03/2021	5.14
87	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,886.91	08/2013 -	08/2022	32.24
88	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,326.81	04/2016 -	07/2020	38.61
89	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	477.69	11/2016 -	05/2021	4.61
90	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	01/2015	871.62 -	902.49	648.77	10/2017 -	01/2021	3.54
91	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	200.16	07/2017 -	-	27.92

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
92	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	-	31.17
93	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	516.12	417.12	01/2019 -	04/2020	26.36
94	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,056.36	12/2018 -	03/2024	92.02
95	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	2,605.89	12/2018 -	12/2021	31.08
96	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	2,868.53	07/2020 -	05/2021	14.11
97	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	157.13	07/2019 -	04/2021	17.99
98	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	05/2017	445.89 -	675.73	463.08	02/2019 -	02/2021	51.55
	<u>Satluj Jal Vidyut Nigam Limited</u>							
99	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	569.80	12/2021 -	12/2021	46.20
	<u>Thdc India Limited</u>							
100	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,207.95	06/2013 -	12/2023	54.94
	Total		1,75,198.45 -	2,49,834.01	202,628.16			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
101	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	73.73
102	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	315.00	312.62	03/2019 -	-	71.14
103	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	98.88
104	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
105	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	-	03/2024 -	-	25.04
106	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89
107	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
108	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	25.65
109	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	14.14	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
110	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346	10/2006	11,589.00 30,357.00	28,181.00	-	-	-	143.17
111	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
112	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	03/1999	1,033.07 -	3,550.00	3,528.48	-	03/2022	243.64
113	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	528.65 -	2,066.78	1,551.38	-	03/2023	290.95
114	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	751.55	683.91	03/2012 -	07/2021	57.27
115	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	229.50
116	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	614.45	340.21	-	12/2023	277.26
117	KOSI BRIDGE (NL), ECR - [220100304	04/2002	499.41 -	516.02	427.28	03/2020 -	-	3.33
118	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00 -	519.33	278.52	-	03/2025	36.67
119	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	819.61	03/2019 -	05/2021	37.04
120	KODERMA-TILAIYA (NL), ECR - [220100305	04/2002	459.91 -	1,625.87	767.07	-	03/2023	253.52
121	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 -	549.75	15.55	-	-	32.26
122	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	2.04	-	03/2024	818.15
123	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00 -	735.20	380.48	-	03/2021	126.22
124	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	386.36	-	03/2023	391.01
125	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	24.74	-	-	376.78
126	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14 -	1,470.50	1,085.63	-	03/2023	295.15
127	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	49.45
128	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01 -	480.00	485.99	-	-	125.34

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
129	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	541.83	07/2014 -	-	64.60
130	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	398.20	03/2021 -	03/2024	63.37
131	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	62.06
132	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	726.31	540.19	- -	-	301.68
133	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	1,207.34	- -	03/2022	350.27
<u>East Coast Railway</u>								
134	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	864.71	06/2021 -	03/2025	137.80
135	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,493.80	03/2009 -	03/2026	29.71
136	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	38.43
137	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	902.85	03/2020 -	03/2023	.07
138	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	221.37	03/2020 -	03/2022	52.77
139	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	15.45
<u>Eastern Railways</u>								
140	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	906.05	03/2019 12/2009	03/2025	36.22
141	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	637.94	02/2013 -	03/2024	134.80
142	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	385.60	03/2017 -	03/2025	20.30
143	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	1.76	- -	03/2025	44.46
144	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	520.48	03/2020 -	03/2021	22.31
145	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	495.10	284.21	- -	03/2022	181.63
146	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02
147	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01
148	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	52.09	- -	03/2025	.25

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
149	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	164.05	02/2012 -	03/2025	36.15
150	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	360.96	- -	03/2024	23.82
151	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	241.02	- -	03/2022	6.48
152	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	34.08
153	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	-	- -	03/2025	180.30
154	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	11.43	- -	03/2025	51.19
155	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	373.47	03/2022 -	03/2025	133.39
156	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	427.64	- -	03/2021	74.26
157	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	565.00	539.40	- -	05/2019	116.16
158	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	643.11	03/2016 -	03/2025	7.75
159	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	103.64	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>								
160	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	117.23
161	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	.00
<u>Metropolitan Rapid Transport Projects</u>								
162	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37
163	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	501.57
164	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	48.06
165	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91
<u>North Central Railway</u>								
166	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	345.51	12/2008 -	-	188.33
167	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
168	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	1.69
	North East Frontier Railway							
169	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	275.06	03/2019 -	-	106.51
170	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	3,838.64	03/2014 -	03/2023	130.69
171	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,683.54	12/2008 -	04/2021	284.80
172	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	10,842.65	03/2011 -	12/2023	175.34
173	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,043.00	798.53	03/2019 -	03/2023	170.77
174	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	970.88	03/2019 -	03/2024	302.54
175	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,911.00	1,148.65	03/2015 -	12/2024	197.05
176	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	6.74	- -	-	7.86
177	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	-	542.04
178	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,042.51	83.64	03/2019 -	03/2024	13.60
179	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	38.20	- -	-	71.62
180	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26
181	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	4,083.02	263.68	03/2021 -	03/2021	350.44
182	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	73.97	03/2020 -	-	94.45
183	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	287.09	- -	12/2021	54.80
184	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	1,040.00	155.65	03/2020 -	-	150.70
185	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJBHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	1,082.01	- -	-	128.39
186	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	800.00	799.87	03/2019 -	03/2021	154.78
187	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,496.25	03/2022 -	03/2023	32.15

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
188	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,162.39	03/2021 -	05/2021	115.07
189	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	2,144.78	824.96	12/2021 -	04/2021	256.12
190	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	1,087.60	04/2010 -	-	186.55
	<u>North Eastern Railway</u>							
191	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	0.15	- -	-	60.34
192	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	- -	-	8.10
193	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	- -	-	358.99
194	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	112.02	12/2021 -	12/2021	267.13
195	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	61.80
196	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	- -	-	.16
197	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	.16
198	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	-	01/2018 -	-	9.91
199	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	63.70	- -	12/2023	18.56
	<u>North Western Railway</u>							
200	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	699.06	02/2019 -	11/2021	109.82
201	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	207.09	03/2020 -	04/2022	16.97
202	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	4.60	- -	-	126.64
203	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	340.45	12/2019 -	02/2021	60.52
204	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	186.12	- -	-	104.65
205	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	253.81	10/2018 -	-	47.91
206	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	-	- -	-	33.70
207	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	- -	-	33.81

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
208	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	480.00	313.18	03/2020 -	06/2021	14.24
209	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	345.38	11/2019 -	03/2021	75.73
210	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	463.25	02/2019 -	02/2020	116.86
	<u>Northern Railway</u>							
211	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	111.51	- -	03/2024	129.17
212	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	211.31
213	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	572.99	- -	03/2023	134.90
214	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	127.91	- -	09/2023	41.71
215	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	204.53	- -	-	57.68
216	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	2.93
217	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	1.73	- -	03/2024	310.24
218	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	388.89
219	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	23,132.28	11/2002 -	12/2022	1,017.96
220	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.09	03/2023 -	03/2025	369.35
221	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>							
222	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	55.57
223	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92
224	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	196.83
225	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	59.22
226	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	926.84	12/2026 -	12/2025	127.62
227	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022	41.04

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
228	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	7.78
229	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95
230	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	124.58
231	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021	53.75
232	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	35.42
233	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	20.68
234	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	50.15
235	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023	9.32
236	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	5.98
237	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	705.50	12/2024 -	12/2024	9.83
238	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	51.02
239	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	40.08
240	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	281.93
241	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	42.47
242	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	111.91
243	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	62.89
244	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	54.24
245	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>							
246	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
247	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	102.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
248	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	- -	-	161.86
249	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	5.16
250	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	15.49
251	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	534.34	03/2020 -	06/2021	31.75
252	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	42.44
253	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	538.84
254	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	98.57
255	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	7.06
256	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	275.34
South East Central Railway								
257	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	1,416.77	- -	-	268.37
258	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	291.76
259	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	84.69
260	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	116.46
261	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	378.60
262	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	1,131.91	12/2019 -	-	40.65
263	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	8.23
264	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	.07
South Eastern Railway								
265	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
266	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	195.84	12/2016 -	08/2020	153.41
267	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	40.99	- -	03/2025	131.89

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
268	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
269	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
270	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	302.95	12/2018 -	06/2021	38.92
271	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	901.11	03/2020 -	12/2021	35.38
272	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>							
273	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	71.56	- -	12/2023	9.22
274	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	296.10	0.01	- -	12/2023	.03
275	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	1,127.71	- -	03/2025	17.95
276	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	0.34	- -	12/2023	14.14
277	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	68.97
278	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	1,160.49	03/2020 -	03/2023	43.14
279	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	33.31
280	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	620.29	03/2020 -	06/2021	35.47
281	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 -	03/2024	15.84
282	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	998.00	463.45	03/2017 -	03/2025	54.78
	<u>Southern Railway</u>							
283	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	301.67
284	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	465.83
285	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	262.68	- -	-	79.80
286	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	3.34	02/2019 -	-	247.32
287	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	130.17
288	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	0.62	- -	-	78.78

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
289	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	319.22	- -	03/2024	181.84
290	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	439.49	- -	12/2021	69.20
291	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	8.50	- -	-	46.09
292	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	1.63	- -	-	295.05
293	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	600.30	355.13	- -	09/2021	265.12
294	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,121.00	906.57	- -	04/2021	20.28
295	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	6.73	- -	-	45.43
296	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	1,699.64
297	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	332.00	265.41	04/2014 -	12/2020	77.29
298	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,246.00	0.81	- -	-	24.60
299	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	253.33
300	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11
	<u>West Central Railway</u>							
301	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,229.79	03/2021 -	03/2023	585.35
302	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57
303	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	296.52	03/2022 -	03/2023	114.32
	<u>Western Railway</u>							
304	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	5,912.40	2,161.74	03/2022 -	03/2024	68.75
305	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	72.42
306	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	411.62	126.05	03/2012 -	03/2023	29.34
307	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,959.74	1,799.00	03/2020 -	03/2024	136.19
308	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
309	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,389.05	1,125.73	03/2021 -	12/2021	33.93
310	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	890.76	745.11	03/2019 -	10/2021	61.51
311	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	04/2017	691.84 -	1,017.91	719.56	03/2020 -	02/2021	47.13
	Total		2,29,432.02 -	4,78,444.49	206,936.30			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
312	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	175.00	- -	-	58.68
313	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	58.98
314	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	-	02/2012 -	-	76.21
315	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	295.96	10/2010 -	06/2021	69.30
316	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 -	389.45	349.94	05/2012 -	-	88.11
317	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	274.07	02/2013 -	-	47.65
318	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	223.10	08/2015 -	-	3.84
319	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	3.07
320	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	219.47	- -	-	3.72
321	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	36.24
322	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	-	46.51

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
323	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	77.26
324	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	267.46	05/2017 -	-	45.75
325	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	754.06	- -	12/2020	1.75
326	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	386.98	02/2011 -	-	34.06
327	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	318.64	08/2016 -	-	14.02
328	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84
329	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 -	377.64	343.70	10/2016 -	-	5.42
330	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 -	353.89	256.11	11/2015 -	-	6.21
331	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	325.42	10/2010 -	06/2021	93.80
332	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	369.77	238.01	- -	-	15.67
333	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	.26
334	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	.02
335	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	-	- -	-	.06
336	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	-	.08
337	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]	08/2014	600.87 720.97	720.97	682.36	11/2017 -	-	19.99
338	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]	08/2014	823.20 937.76	937.76	807.99	11/2017 -	-	13.92
339	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	173.41	141.65	08/2018 -	-	4.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
340	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	25.03	08/2019 -	11/2022	33.51
341	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	12/2021	11.18
342	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	331.86	08/2017 -	02/2020	42.48
343	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	170.96	08/2018 -	-	4.45
344	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	315.57	12/2015 -	-	6.81
345	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	188.64	07/2019 -	-	.31
346	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	46.51
347	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	351.92	03/2018 -	06/2021	9.23
348	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	292.10	09/2014 -	-	72.36
349	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	1,217.25	- -	-	2.93
350	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	572.66	270.56	08/2016 -	06/2021	15.19
351	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	400.38	09/2016 -	06/2021	14.24
352	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	416.16	10/2016 -	06/2021	17.04
353	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223	03/2010	179.89 271.00	271.00	270.91	03/2013 -	-	50.65
354	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225	12/2010	169.26 299.00	299.00	-	01/2019 -	-	76.65
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
355	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	11.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
356	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 -	252.79	100.63	04/2017 -	-	29.48
357	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 -	263.31	116.97	04/2017 -	-	29.48
358	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]	01/2017	194.66 -	252.05	111.22	04/2017 -	-	29.48
359	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	298.08	08/2016 -	05/2021	3.73
360	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]	01/2017	198.22 -	252.05	111.21	04/2017 -	-	27.16
361	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	261.20	10/2017 -	-	15.30
362	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]	10/2017	818.00 -	887.68	259.50	- -	-	8.52
<u>National Highways Authority Of India</u>								
363	HARANGAJAO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	520.00	612.58	02/2009 -	-	85.71
364	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	325.28	04/2009 -	-	70.23
365	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	435.78	427.96	11/2008 -	-	159.95
366	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	255.23	251.39	11/2008 -	-	64.62
367	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019	4.99
368	HARANGAJAO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	655.17	07/2009 -	-	234.27
369	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-	167.82
370	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
371	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	65.82
372	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021	10.58
373	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
374	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 -	2,519.00	4,709.65	06/2015 -	-	16.67
375	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
376	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	575.99	11/2013 -	01/2021	15.53
377	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	459.07	01/2014 -	12/2020	61.08
378	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	52.73
379	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 -	417.68	433.68	01/2016 -	12/2020	18.88
380	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 -	627.93	633.24	01/2016 -	01/2020	26.66
381	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	642.54	05/2018 -	06/2021	37.63
382	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	272.98	- -	-	.77
383	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	594.57	05/2018 -	06/2021	16.34
384	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	889.83	- -	01/2020	11.33
385	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	68.71
386	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	512.04	- -	10/2021	1.37
387	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
388	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	676.33	12/2017 -	-	66.88
389	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	400.60	- -	-	6.11
390	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	186.70	- -	-	1.33
391	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,472.01	- -	-	41.78
392	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,160.00	- -	-	21.50
393	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	712.15	04/2018 -	-	25.80
394	MEERUT-BULANDSHAHAHAR - [N24000539]	01/2016	683.24 -	987.94	867.27	- -	-	44.60
395	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	02/2016	997.15 -	1,115.95	975.08	03/2019 -	-	11.91
396	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
397	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	353.42	- -	03/2021	7.53
398	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 -	486.00	432.16	- -	-	6.11
399	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	86.37
400	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,282.04	- -	-	94.94
401	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	312.79	08/2018 -	-	3.98
402	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82 -	1,727.66	1,674.80	- -	01/2021	39.35
403	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-	16.55
404	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021	4.10
405	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	309.40	- -	-	8.35
406	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	722.46	07/2018 -	-	19.25
407	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	1,039.23	03/2020 -	-	10.58
408	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	-	03/2020 -	-	31.88
409	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	3.40
410	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-	5.56
411	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	-	1.06
412	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	-	5.70
413	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	363.86	03/2020 -	09/2021	.23
414	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	31.82	03/2020 -	-	9.38
415	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	951.13	03/2020 -	-	13.97

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
416	REHABILITATION AND UPGADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	10.24
417	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	18.50
418	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	41.54
419	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	1,150.56	03/2020 -	-	44.39
420	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	3.95
421	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78
422	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	9.67
423	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	419.23	- -	10/2020	10.68
424	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	72.53	- -	-	.99
425	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	14.19	- -	-	30.09
426	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	11.20
427	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	20.28
428	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	2,244.98	- -	-	12.50
429	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	54.69
430	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	1,011.70	- -	-	29.35
431	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	1,118.92	- -	-	18.87
432	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	394.36	- -	01/2021	37.71

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
433	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	1,582.36	03/2021 -	04/2021	63.05
434	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	38.11	- -	-	8.26
435	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	299.11	- -	03/2021	22.44
436	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDER - [N24000829	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	5.32
437	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	- -	-	4.99
438	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	- -	-	.12
439	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	268.17	- -	07/2021	46.72
440	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	213.17	- -	07/2021	.48
441	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	666.56	- -	-	25.68
442	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	263.60	- -	12/2021	.00
443	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	76.17	- -	11/2022	27.86
444	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	193.30	- -	-	305.58
	Total		94,385.49 -	1,20,598.50	89,635.35			
	RURAL DEVELOPMENT							
	Hindustan Steelwork Construction Limited							
445	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	2.23
446	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	3.96

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	Total		352.34 -	362.78	335.17			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
447	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	18,486.77	05/2015 -	07/2021	41.32
	Total		15,525.00 -	21,940.00	18,486.77			
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
448	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	84.97
	Total		13,334.00 -	24,664.00	16,594.00			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
449	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	8,706.79	12/2018 -	08/2022	18.69
	<u>Bangalore Metro Rail Corporation Limited</u>							
450	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	02/2014	26,405.14 -	30,695.12	17,021.86	02/2019 -	06/2024	16.25
	<u>Central Public Works Department</u>							
451	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	-	12/2013 -	-	132.80
	<u>Chennai Metro Rail Ltd</u>							
452	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-	30.53
	<u>Kochi Metro Rail Corporation Ltd</u>							
453	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	09/2020	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>							
454	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	44.39
	<u>National Building Construction Corporation Ltd</u>							
455	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	10.71
	Total		84,474.19 -	1,07,150.99	69,876.13			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>WATER RESOURCES</u>							
	<u>Kolkata Metropolitan Development Authority</u>							
456	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23
	<u>Polavaram Project Authority</u>							
457	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	17,025.01	03/2020 -	04/2022	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
458	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022	22.24
459	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]	10/2016	370.40 -	430.49	376.22	08/2020 -	03/2021	16.22
460	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]	02/2011	279.91 -	330.05	222.79	12/2019 -	01/2021	17.91
461	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	-	12/2021 -	12/2021	.97
462	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	-	06/2022 -	06/2022	1.31
	Total		12,126.97 -	57,719.96	17,624.02			
	Grand Total		7,71,374.01	12,48,797.90	747,029.11			

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75				2/6
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
2	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80	229.80	81.43	-	05/2022	0(R3)	17/26
3	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20	730.20	77.30	-	05/2023	0(R3)	12/17
	Total		818.00	960.00	158.73				29/43
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
4	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84	268.84	244.88	-	03/2021	-	0/0
5	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	190.34	143.04	-	06/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	382.25	-	06/2021	-	0/0
7	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	470.24	-	06/2021	-	0/0
8	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	490.55	-	06/2021	-	0/0
	Total		2,261.40	2,295.18	1,730.96				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
9	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00	735.20	380.48	-	03/2021	-	0/0
10	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07	3,550.00	3,528.48	-	03/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
11	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	1,483.14	1,207.34	- -	03/2022	-	0/0
12	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	2,066.78	1,551.38	- -	03/2023	-	0/0
13	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	1,625.87	767.07	- -	03/2023	-	0/0
14	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	-	0/0
15	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	52.72	- -	03/2023	-	0/0
16	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	1,470.50	1,085.63	- -	03/2023	-	0/0
17	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	614.45	340.21	- -	12/2023	-	0/0
18	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	-	0/0
19	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
20	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	519.33	278.52	- -	03/2025	-	0/0
	<u>Eastern Railways</u>								
21	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	502.48	427.64	- -	03/2021	-	0/0
22	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	284.21	- -	03/2022	-	0/0
23	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	272.20	241.02	- -	03/2022	-	0/0
24	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	360.96	- -	03/2024	-	0/0
25	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
26	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	11.43	- -	03/2025	-	0/0
27	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
28	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.11	- -	03/2025	-	0/0
29	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
30	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
31	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	- -	03/2025	-	0/0
32	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
33	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
34	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	287.09	- -	12/2021	-	0/0
	<u>North Eastern Railway</u>								
35	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	714.34	63.70	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
36	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	791.39	572.99	- -	03/2023	-	0/0
37	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
38	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	127.91	- -	09/2023	-	0/0
39	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	359.00	111.51	- -	03/2024	-	0/0
40	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	<u>South Eastern Railway</u>								
41	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
42	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,967.00	71.56	- -	12/2023	-	0/0
43	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	558.00	-	- -	12/2023	-	0/0
44	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	296.10	.01	- -	12/2023	-	0/0
45	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	- -	12/2023	-	0/0
46	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
47	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	- -	12/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
48	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	-	0/0
49	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,432.50	1,127.71	- -	03/2025	-	2/2
	<u>Southern Railway</u>								
50	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,121.00	906.57	- 02/2021	04/2021	2(R3)	0/0
51	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	600.30	355.13	- 10/2021	09/2021	-1(R3)	0/0
52	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	457.08	439.49	- -	12/2021	-	0/0
53	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,205.00	2.28	- 03/2024	03/2024	0(R3)	0/0
54	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	559.95	319.22	- -	03/2024	-	0/0
55	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	582.83	239.11	- -	12/2025	-	0/0
	<u>Western Railway</u>								
56	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	186.59	- 03/2024	03/2024	0(R3)	0/0
	Total		24,793.81 -	44,641.02	16,237.68				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
57	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	291.05	200.71	- -	03/2021	-	0/0
58	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	178.13	139.26	- -	03/2021	-	0/0
59	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	3(R3)	0/0
60	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	105.65	- -	09/2021	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
61	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	119.35	- -	09/2021	-	2/4
62	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	81.01	- -	04/2022	-	0/4
63	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	65.25	- -	04/2022	-	0/4
National Highways Authority Of India									
64	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	1,005.08	-	- -	03/2021	-	0/0
65	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	-	0/0
66	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	353.42	- -	03/2021	-	0/0
67	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021	-	0/0
68	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	203.77	- -	03/2021	-	0/0
69	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	1,261.05	299.11	- -	03/2021	-	0/0
70	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	621.00	591.21	- -	04/2021	-	2/3
71	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	189.70	- -	04/2021	-	0/0
72	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,590.00	- -	05/2021	-	0/0
73	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	478.74	127.42	- -	05/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
74	REHABILITATION AND UPGRADATION TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	-	0/0
75	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA	12/2017	686.65 -	686.65	227.63	- -	06/2021	-	0/0
76	REHABILITATION AND UPGRADATION OF FOUR LANE OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA	12/2017	417.51 -	417.51	127.61	- -	06/2021	-	0/0
77	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA	01/2018	668.86 -	668.86	276.59	- -	06/2021	-	0/0
78	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI, ODISHA	01/2018	686.65 -	686.65	261.74	- -	06/2021	-	0/0
79	REHABILITATION SIX LANEING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0
80	REHABILITATION AND UPGRADATION OF SIX LANEING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA	01/2018	999.00 -	999.00	102.70	- -	06/2021	-	0/0
81	REHABILITATION AND UP-GRADATION TO 4-LANEING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	503.88	25.40	- -	06/2021	-	0/0
82	CONSTRUCTION OF SIX LANEING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI, ANDHRA PRADESH	03/2018	314.43 -	314.43	86.83	- -	06/2021	-	0/0
83	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
84	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	479.00	456.80	- -	07/2021	-	0/0
85	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	1,048.10	921.02	- -	07/2021	-	3/4
86	4-LANNING OF TARSOD-FAGNE (FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	1,021.00	296.60	- 01/2022	07/2021	-6(R3)	1/4
87	SIX LANEING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI, ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
89	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB	02/2018	261.76 -	207.00	193.26	- -	07/2021	-	0/0
90	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT	03/2018	1,437.64 -	1,437.64	584.17	- -	07/2021	-	0/0
91	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	931.21	268.17	- -	07/2021	-	0/0
92	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI, HARYANA	03/2018	795.50 -	799.30	213.17	- -	07/2021	-	0/0
93	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA	03/2018	1,162.92 -	1,162.92	75.68	- -	07/2021	-	0/0
94	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI, MADHYA PRADESH	12/2017	950.27 -	950.27	224.81	- -	08/2021	-	3/4
95	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA	01/2018	607.00 -	607.00	440.92	- -	08/2021	-	0/1
96	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI, ODISHA	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0
97	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI, ODISHA	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1
98	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI, TAMIL NADU	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	-	0/0
99	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI, TAMIL NADU	03/2018	505.35 -	505.35	243.30	- -	08/2021	-	0/0
100	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI, MAHARASHTRA	03/2018	289.21 -	289.21	194.57	- 02/2021	08/2021	6(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
101	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
102	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,401.00	- -	09/2021	-	0/0
103	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
104	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
105	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	-	0/0
106	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
107	FOUR LANING OF MADURAI- CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	310.06	- -	12/2021	-	0/0
108	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	263.60	- -	12/2021	-	0/3
109	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	-	0/0
110	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	150.06	- 08/2021	02/2022	6(R3)	0/0
111	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	425.85	- -	02/2022	-	1/4
112	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	213.52	- -	03/2022	-	0/1
113	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	332.04	- -	03/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
114	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI, MADHYA PRADESH	12/2017	656.98 -	840.00	76.17	- -	11/2022	-	0/4
	Total		48,711.82 -	50,008.37	24,876.71				14/45
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								
115	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	2,694.00	679.91	- -	12/2022	-	0/9
	Total		2,694.00 -	2,694.00	679.91				0/9
	Grand Total		79,551.76	1,00,871.30	43,837.74				47/105

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 -	-
	Total		438.28 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TALABIRA II AND III OCP - [N06000189]NLC, ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
7	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Western Coal Fields Limited</u>				
10	SINGHORI OC MINE - [N06000130]WCL, MAHARASHTRA	06/2015	205.49 -	03/2020 -	03/2020
11	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020
	Total		17,152.93 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
12	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO, TAMIL NADU	09/2017	166.62 163.17	06/2019 06/2021	12/2020
13	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO, ODISHA	12/2015	355.00 -	11/2020 -	02/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	UTKAL D AND E COAL BLOCK - [N10000011]NALCO, ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		1,055.62 -		
	<u>STEEL</u>				
	<u>Raistriya Ispat Nigam Limited</u>				
15	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 12/2020	12/2020
	Total		2,858.00 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
16	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU	09/2017	1,858.00 -	12/2019 -	01/2021
	<u>Hindustan Petroleum Corporation Limited</u>				
17	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL, MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
18	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	Total		6,768.00 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
19	LOKTAK D/S HEP(NHPC) - [180100078]NHPC, MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
20	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	02/2017 06/2020	01/2021
21	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC, UTTAR PRADESH	12/2018	587.44 -	09/2020 01/2021	01/2021
22	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC, MADHYA PRADESH	03/2013	11,638.55 15,105.22	01/2018 10/2020	02/2021
23	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
24	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-
25	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
26	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC, MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-
27	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
28	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>North East Electric Power Corporation</u>				
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	12/2009 02/2021	02/2021
	<u>Power Grid Corporation Of India Limited</u>				
30	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 516.12	01/2019 09/2020	04/2020
31	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 09/2020	05/2020
32	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 09/2020	07/2020
33	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 11/2020	09/2020
34	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	06/2019 11/2020	09/2020
35	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62 902.49	10/2017 05/2021	01/2021
36	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 675.73	02/2019 02/2021	02/2021
37	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	06/2014 -	-
38	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
39	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL, MULTI STATE	01/2015	203.28 -	07/2017 -	-
40	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
41	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL, MULTI STATE	03/2017	283.72 -	11/2019 -	-
42	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	-
43	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
	Total		81,024.79 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
44	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL, DELHI	08/2016	1,554.00 -	09/2019 -	-
	Total		1,554.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Hospital Services Consultancy Corporation Ltd</u>				
45	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
46	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
47	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
48	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	03/2018 -	09/2019
49	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	05/2017 -	01/2020
50	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
51	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	-	01/2021
	Total		1,910.90 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
52	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 -	03/2019 -	03/2020
53	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
54	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 12/2020	12/2020
55	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	-
56	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
57	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
58	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
59	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
60	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
61	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
62	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 -	03/2020 -	-
63	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
64	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR	04/2008	633.87 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
65	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
66	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
67	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
68	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
69	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
70	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
71	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
72	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
73	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
74	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
75	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-
<u>Eastern Railways</u>					
76	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
<u>Kolkata Metro Rail Corporation Limited</u>					
77	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
<u>Metropolitan Rapid Transport Projects</u>					
78	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
79	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
<u>North Central Railway</u>					
80	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
81	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
82	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
<u>North East Frontier Railway</u>					
83	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
84	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-
85	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-
87	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-
88	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
89	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-
90	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	-
91	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
92	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
93	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
94	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
95	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
96	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
97	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
98	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021
99	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
100	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-
101	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
102	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
103	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
104	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
105	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
106	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
107	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
	<u>Railway Electrification</u>				
108	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
109	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
110	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00 -	- -	-
111	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	761.37 -	- -	-
112	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH	04/2013	829.00 -	- -	-
113	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
114	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	-
115	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR, CHHATISGARH	04/2008	872.00 -	12/2019 -	-
	<u>South Eastern Railway</u>				
116	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
117	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
118	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>Southern Railway</u>				
119	OMALUR-METTURDAM- DOUBLING WITH ELECTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU	10/2013	187.26 -	04/2014 03/2021	12/2020
120	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	1,566.00 -	- -	-
121	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	227.40 -	- -	-
122	ATTIPPATTU PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	151.84 -	02/2019 -	-
123	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-
124	KUMBALAM-TURAVUR - [N22000191]SR, KERALA	04/2011	252.96 -	- -	-
125	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 -	- -	-
126	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	- -	-
127	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR, KERALA	02/2015	1,431.90 -	- -	-
128	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR, KERALA	02/2015	1,000.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
129	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
130	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
131	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 02/2021	02/2021
132	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
133	GANDHINAGAR REDEVELOPMENT OF STATION ALOGLWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
134	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
135	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
136	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
137	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		81,111.17 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
138	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
139	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 -	05/2019
140	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 -	06/2019
141	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020
142	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 05/2021	08/2019
143	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020
144	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 05/2020	05/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
145	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	06/2020
146	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
147	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020
148	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
149	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020
150	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020
151	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020
152	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2020	12/2020
153	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020
154	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020
155	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	01/2021
156	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 04/2021	01/2021
157	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021
158	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021
159	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
160	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021
161	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	02/2021
162	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	08/2018 06/2021	02/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
163	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	02/2021
164	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
165	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
166	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
167	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
168	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
169	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
170	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
171	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
172	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
173	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
174	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
175	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
176	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
177	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
178	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
179	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
180	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
181	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
182	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
183	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
184	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
185	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
186	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
187	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 12/2020	-
188	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 12/2020	-
189	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 12/2020	-
190	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
191	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
192	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
193	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
194	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
195	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
196	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
197	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
198	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
199	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
200	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
201	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
202	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
203	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
205	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
206	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
207	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 390.73	05/2017 -	-
208	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
209	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
210	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
213	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
214	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
215	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
216	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
217	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
218	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
219	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
220	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
221	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
222	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
223	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
224	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
225	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
228	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
229	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
231	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
233	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
234	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
235	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
236	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH, BIHAR	08/2015	288.24 -	11/2015 -	-
237	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH, MAHARASHTRA	03/2016	1,142.62 -	- -	-
238	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH, MAHARASHTRA	03/2016	1,101.58 -	- -	-
239	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH, BIHAR	08/2016	1,742.01 -	12/2016 -	-
240	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH, ODISHA	03/2014	191.50 192.00	05/2016 -	-
241	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MoRTH, ODISHA	01/2015	326.63 327.00	04/2018 -	-
242	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH, ODISHA	02/2015	239.91 240.00	10/2017 -	-
243	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH, ODISHA	07/2014	342.05 342.00	01/2017 -	-
244	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH, ODISHA	08/2013	171.96 172.00	06/2016 -	-
245	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH, ODISHA	06/2016	157.30 157.00	06/2018 -	-
246	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH, UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
247	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH, UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
248	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH, UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
249	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH, UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
250	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH, UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
251	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH, UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
252	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH, UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
253	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH, UTTARAKHAND	02/2018	418.88 -	02/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
254	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
255	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
256	REHABILITATION AND UPGADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
257	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
258	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
259	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
260	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-
261	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
262	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-
263	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
264	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
265	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
266	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
267	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
268	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
269	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
270	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
271	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
272	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
273	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
274	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
275	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
276	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-
277	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-
278	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	-
279	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
280	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
281	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-
282	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 -	-
283	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 -	-
284	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 -	-
285	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	01/2018 -	-
286	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
287	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
288	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
289	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
290	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
291	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
292	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
293	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
294	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
295	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
296	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
297	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
298	REHABILITATION AND UPGADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
299	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
300	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
301	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
302	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
303	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
304	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-
305	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
306	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
307	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
308	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
309	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
310	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
311	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
312	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
313	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
314	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
315	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
316	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
317	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
318	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
319	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
320	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
321	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
322	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
323	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
324	AMD I TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
325	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
326	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
327	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
328	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
329	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
330	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
331	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
332	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
333	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
334	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
335	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
336	MANHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
337	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
338	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
339	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
340	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
341	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
342	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
343	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
344	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
345	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
346	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
347	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
348	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
349	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
350	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
351	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
352	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
353	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
354	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
355	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
356	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
357	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
358	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
359	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
360	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
361	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
362	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
363	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
364	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
365	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
366	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
367	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
368	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
369	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
370	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
371	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
372	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
373	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
374	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
375	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
376	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
377	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
378	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
379	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
380	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
381	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
382	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
383	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
384	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
385	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
386	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
387	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
388	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
389	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
390	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
391	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
392	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
393	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
394	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
395	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
396	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
397	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
398	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
399	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
400	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
401	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
402	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
403	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
404	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
405	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
406	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
407	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
408	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
409	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
410	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
411	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
412	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
413	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
414	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
415	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
416	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
417	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
418	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
419	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
420	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
421	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-
422	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
423	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
424	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
425	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
426	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
427	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
428	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
429	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
430	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
431	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
432	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
433	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
434	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
435	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
436	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
437	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
438	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-
439	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-
440	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
441	REHABILITATION AND UPGRADATION OF PRATAPGARH- ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-
442	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
443	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
444	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-
445	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
446	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
447	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
448	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
449	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
450	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
451	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
452	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
453	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
454	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
455	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
456	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
457	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
458	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
459	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
460	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
461	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
462	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-
463	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2020	-
464	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
465	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
466	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
467	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-
468	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
469	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-
470	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
471	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
472	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-
473	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
474	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-
475	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
476	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
477	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
478	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
479	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
480	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
481	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
482	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
483	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
484	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
485	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
486	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	02/2021
487	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	09/2018
488	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
489	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2020
490	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	12/2020
491	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
492	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
493	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
494	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
495	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
496	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
497	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
498	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
499	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
500	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
501	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
502	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
503	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
504	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-
505	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
506	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
507	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
508	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
509	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
510	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
511	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
512	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
513	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
514	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
515	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
516	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
517	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
518	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
519	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
520	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
521	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
522	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
523	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
524	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
525	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
526	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
527	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
528	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
529	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
530	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
531	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
532	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
533	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
534	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
535	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
536	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
537	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
538	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
539	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
540	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
<u>National Highways Authority Of India</u>					
541	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	10/2019
542	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020
543	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
544	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
545	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
546	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
547	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
548	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
549	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
550	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020
551	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
552	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
553	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
554	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
555	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020
556	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
557	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
558	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020
559	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
560	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
561	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020
562	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
563	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
564	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020
565	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020
566	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020
567	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
568	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020
569	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020
570	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
571	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
572	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021
573	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021
574	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	01/2021
575	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	01/2021
576	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
577	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021
578	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	02/2021
579	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	02/2021
580	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021
581	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	02/2021
582	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	02/2021
583	REHABILITATION AND UPGRADEATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
584	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
585	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
586	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
587	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
588	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
589	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
590	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
591	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
592	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
593	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
594	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
595	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
596	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
597	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
598	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
599	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
600	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
601	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
602	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
603	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
604	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
605	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
606	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
607	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
608	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
609	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
610	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
611	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
612	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
613	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
614	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
615	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
616	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
617	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
618	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	-
619	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	-
620	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
621	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	-
622	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
623	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
624	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
625	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
626	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	-
627	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
628	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	-	-
629	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
630	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	-
631	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	-
632	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	-
633	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
634	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
635	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
636	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
637	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-
638	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	-	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
639	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
640	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
641	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
642	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
643	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
644	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
645	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
646	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
647	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 -	-
648	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
649	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
650	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
651	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
652	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	-
653	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
654	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-
655	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
656	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
657	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
658	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
659	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	-
660	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
661	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
662	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
663	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
664	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
665	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
666	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
667	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
668	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
669	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
670	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
671	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
672	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
673	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-
674	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
675	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
676	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
677	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
678	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
679	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
680	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
681	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
682	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
683	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
684	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
685	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
686	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
687	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
688	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
689	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
690	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
691	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 486.00	- -	-
692	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
693	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
694	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
695	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
696	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
697	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
698	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-
699	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
700	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
701	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-
702	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
703	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
704	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
705	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
706	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
707	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
708	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
709	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
710	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
711	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
712	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	-
713	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
714	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
715	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
716	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
717	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
718	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
719	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
720	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
721	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
722	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
723	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
724	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
725	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
726	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
727	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
728	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
729	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
730	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
731	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
732	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
733	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
734	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
735	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
736	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
737	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
738	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
739	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
740	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
741	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
742	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
743	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
744	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
745	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
746	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
747	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
748	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
749	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
750	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
751	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
752	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
753	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
754	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
755	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
756	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
757	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
758	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
759	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
760	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
761	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI, BIHAR	03/2018	496.20 -	- -	-
762	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-
763	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
764	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
765	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
766	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-
767	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-
768	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-
769	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
770	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-
771	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI, HARYANA	03/2018	307.79 -	- -	-
772	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-
773	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
774	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-
775	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	- -	-
776	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA	03/2018	198.05 -	- -	-
777	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA	03/2018	181.78 -	- -	-
778	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI, HARYANA	03/2018	551.58 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
779	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA	03/2018	642.13 -	- -	-
780	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
781	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI, HARYANA	01/2019	1,051.91 -	- 02/2020	-
782	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI, HARYANA	01/2019	1,120.06 -	- -	-
783	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI, HARYANA	01/2019	1,137.42 -	- -	-
784	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI, HARYANA	01/2019	1,033.19 -	- -	-
785	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI, HARYANA	01/2019	1,243.45 -	- 01/2020	-
786	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI, HARYANA	01/2019	889.36 -	- 06/2020	-
787	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI, HARYANA	01/2019	1,018.79 -	- 02/2020	-
788	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI, HARYANA	01/2019	996.65 -	- -	-
789	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI, MADHYA PRADESH	12/2017	217.96 -	- -	-
790	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI, MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
791	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI, ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
792	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI, ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
793	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI, ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
794	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI, ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
795	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI, BIHAR	10/2013	649.90 -	12/2020 -	-
796	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI, BIHAR	10/2013	446.97 -	11/2020 -	-
797	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI, BIHAR	10/2013	464.09 -	11/2020 -	-
798	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		3,87,145.88		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
799	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00	11/2020	11/2020
800	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	12/2015	-
801	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013	-
802	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56	05/2020	-
803	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72	11/2020	-
804	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97	09/2020	-
	<u>Chennai Metro Rail Ltd</u>				
805	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00	12/2015	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
806	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
807	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
808	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA	08/2014	8,680.00	03/2018	-
	<u>National Building Construcion Corporation Ltd</u>				
809	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00	11/2019	-
	Total		41,941.60		
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
810	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13	09/2020	-
811	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63	01/2021	-
	<u>Delhi Jal Board</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
812	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Uttar Pradesh Jal Nigam</u>				
813	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
	<u>Uttarakhand Pey Jal Nigam</u>				
814	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
	Total		1,420.85 -		
	<u>COMMERCE</u>				
	<u>National Building Construcion Corporation Ltd</u>				
815	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
816	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
817	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
818	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
819	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
820	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				
821	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
822	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	<u>Rail India Technical And Economic Service</u>				
823	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		2,641.45 -		
	Grand Total		6,27,326.11		

Details of Projects Without Date of Commissioning

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 -	04/2020 -	05/2021	0/0
2	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	03/2020 12/2021	12/2021	0/0
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI, ASSAM	12/2016	1,142.00 -	03/2021 -	03/2022	0/0
4	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]AAI, TELANGANA	05/2020	353.61 -	05/2022 -	05/2022	0/0
5	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI, GUJARAT	01/2018	1,405.00 -	08/2022 -	08/2022	0/0
6	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI, UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2022	0/0
7	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI, BIHAR	05/2018	1,216.90 -	10/2022 -	10/2022	0/0
8	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI, ANDHRA PRADESH	04/2020	611.80 -	03/2023 -	03/2023	0/0
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 -	-	0/0
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					
10	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	03/2017 -	03/2022	0/0
11	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	04/2018 -	06/2022	0/0
	<u>Eastern Coal Fields Limited</u>					
12	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL, WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
	<u>Neyveli Lignite Corporation</u>					
13	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
14	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
15	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
16	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>South-Eastern Coal Fields Limited</u>					
17	JAMPALI OCP RCE - [N06000198]SECL, CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
18	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL, CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
19	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]SECL, CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
20	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL, CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>Western Coal Fields Limited</u>					
21	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
22	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL, MADHYA PRADESH	07/2016	281.25 -	03/2022 -	03/2026	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (SAIL)</u>					
23	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL, ODISHA	11/2020	377.18 -	05/2023 -	05/2023	0/0
24	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL, CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
25	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	12/2021 -	12/2021	0/0
26	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
27	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
28	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	08/2022	0/0
29	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL, KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
30	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL, MAHARASHTRA	08/2020	697.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
31	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU	09/2017	1,858.00 -	12/2019 -	01/2021	0/0
32	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	08/2020 -	09/2021	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
33	220 KV GRID SUPPLY - [N16000407]HPCL, ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	03/2021	0/0
34	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL, ANDHRA PRADESH	10/2020	210.94 -	08/2021 -	08/2021	0/0
35	RUF PITCH LOADING GANTRY - [N16000406]HPCL, ANDHRA PRADESH	10/2020	332.61 -	11/2022 -	11/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
36	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	09/2026 02/2027	02/2027	0/0
37	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	03/2029 08/2029	08/2029	0/0
38	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL	03/2019	5,830.20 -	03/2031 08/2029	08/2029	0/0
<u>Indian Oil Corporation Limited</u>						
39	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021	0/0
40	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
41	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	04/2021	0/0
42	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
43	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
44	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 293.00	06/2020 09/2021	09/2021	0/0
45	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
46	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
47	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	10/2021 -	10/2021	0/0
48	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
49	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 12/2021	12/2021	0/0
50	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	07/2021 03/2022	03/2022	0/0
51	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	07/2022	0/0
52	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	07/2022 -	07/2022	0/0
53	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0
54	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	12/2022	0/0
55	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00 -	01/2023 -	01/2023	0/0
56	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
57	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	12/2022 07/2023	07/2023	0/0
58	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
59	AUGMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	08/2023	0/0
60	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	09/2023	0/0
61	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	12/2023	0/0
62	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	01/2024 -	01/2024	0/0
63	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT	09/2020	18,936.00 -	09/2024 -	09/2024	0/0
64	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
	<u>Numaligarh Refinery Limited</u>					
65	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM	01/2019	12,366.00 -	10/2024 -	10/2024	0/0
66	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM	01/2019	10,228.00 -	10/2024 -	10/2024	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
67	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT	02/2020	444.87 -	08/2022 -	08/2022	0/0
	<u>Oil India Limited</u>					
68	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	04/2021	0/0
	<u>POWER</u>					
	<u>Central Public Works Department</u>					
69	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	06/2021	0/0
	<u>Chenab Valley Power Projects [P] Limited</u>					
70	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	07/2025	0/0
	<u>National Hydro-Electric Power Corporation</u>					
71	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
72	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
73	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	03/2021 -	03/2021	0/0
74	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 01/2021	01/2021	0/0
75	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	04/2021	0/0
76	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	04/2021 -	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
77	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 -	12/2018 -	07/2021	0/0
78	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 -	11/2018 -	07/2021	0/0
79	FATEHGARH SOLAR 296MW - [N18000289]NTPC, RAJASTHAN	03/2020	1,749.31 -	09/2021 -	09/2021	0/0
80	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC, TAMIL NADU	03/2020	1,316.22 -	09/2021 -	09/2021	0/0
81	KAWAS SOLAR 56 MW - [N18000283]NTPC, GUJARAT	08/2020	261.80 -	10/2021 -	10/2021	0/0
82	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC, KERALA	09/2019	403.62 -	06/2021 10/2021	10/2021	0/0
83	DEVIKOT SOLAR 90MW - [N18000280]NTPC, UTTAR PRADESH	03/2020	501.29 -	09/2021 01/2022	01/2022	0/0
84	DEVIKOT SOLAR 150MW - [N18000281]NTPC, UTTAR PRADESH	01/2020	798.24 -	09/2021 01/2022	01/2022	0/0
85	NOKHRA - [N18000282]NTPC, UTTAR PRADESH	03/2020	1,722.14 -	09/2021 01/2022	01/2022	0/0
86	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC, RAJASTHAN	01/2020	1,522.71 -	09/2021 01/2022	01/2022	0/0
87	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC, RAJASTHAN	03/2020	1,782.00 -	09/2021 01/2022	01/2022	0/0
88	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
89	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-	0/0
Power Grid Corporation Of India Limited						
90	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 516.12	01/2019 09/2020	04/2020	0/0
91	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 09/2020	05/2020	0/0
92	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 11/2020	09/2020	0/0
93	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	06/2019 11/2020	09/2020	0/0
94	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 675.73	02/2019 02/2021	02/2021	0/0
95	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 04/2021	04/2021	0/0
96	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	04/2021	0/0
97	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	11/2019 04/2021	04/2021	0/0
98	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 219.66	07/2019 04/2021	04/2021	0/0
99	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	05/2020 05/2021	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 08/2021	05/2021	0/0
101	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 12/2020	05/2021	0/0
102	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	06/2021	0/0
103	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	06/2021	0/0
104	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 06/2021	06/2021	0/0
105	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 06/2021	06/2021	0/0
106	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 06/2021	06/2021	0/0
107	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 06/2021	06/2021	0/0
108	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	12/2018 -	12/2021	0/0
109	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	12/2018 -	03/2024	0/0
110	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-	0/0
111	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-	0/0
112	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-	0/0
113	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-	0/0
	<u>Satuj Jal Vidyut Nigam Limited</u>					
114	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH	11/2020	1,810.56 -	01/2026 -	01/2026	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
115	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Central Public Works Department</u>					
116	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
117	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
118	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
119	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>HII Infra Tech Services Limited</u>					
120	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	07/2021	0/0
121	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	07/2021	0/0
122	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	07/2022	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
123	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
124	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
125	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
126	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	-	01/2021	0/0
127	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
128	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	-	03/2021	0/0
129	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	05/2021	0/0
130	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	06/2021	0/0
131	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	-	06/2021	0/0
132	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	-	06/2021	0/0
133	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	-	06/2021	0/0
134	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	-	06/2021	0/0
135	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	12/2021	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
136	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	03/2020	0/0
137	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2023	0/0
138	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
139	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
140	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
141	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
142	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
143	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
144	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
145	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
146	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
147	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
148	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
149	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-	0/0
<u>Container Corporation Of India</u>						
150	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 12/2020	12/2020	0/0
151	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2021	0/0
152	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2021	0/0
153	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-	0/0
154	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
155	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-	0/0
156	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-	0/0
157	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-	0/0
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
158	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
159	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
<u>East Central Railways</u>						
160	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
161	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	03/2012 -	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
162	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, JHARKHAND	03/1999	1,033.07	-	03/2022	0/0
163	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419] ECR, UTTAR PRADESH	08/2015	528.57	03/2019	03/2022	0/0
164	GARHWA ROAD-RAMNA - [N22000465] ECR, JHARKHAND	03/2015	348.23	03/2021	03/2022	0/0
165	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476] ECR, BIHAR	04/1991	329.39	-	03/2022	0/0
166	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473] ECR, BIHAR	04/2016	731.64	03/2021	06/2022	0/0
167	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240] ECR, BIHAR	04/1997	324.73	03/2012	11/2022	0/0
168	HAJIPUR-SUGALI VIA VAISHALI (NL), ECR - [220100303] ECR, BIHAR	04/2003	528.65	-	03/2023	0/0
169	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, JHARKHAND	04/2002	459.91	-	03/2023	0/0
170	CHHAPRA-MUZAFFARPUR (NL) - [N22000172] ECR, BIHAR	04/2006	378.56	-	03/2023	0/0
171	ARARIA-SUPAUL (NL) - [N22000177] ECR, BIHAR	04/2008	1,605.17	-	03/2023	0/0
172	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180] ECR, BIHAR	04/2004	372.14	-	03/2023	0/0
173	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181] ECR, BIHAR	04/2009	548.00	03/2020	03/2023	0/0
174	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, BIHAR	04/1997	162.87	-	12/2023	0/0
175	BIHTA-AURANGABAD (NL) - [N22000170] ECR, BIHAR	04/2008	326.20	-	03/2024	0/0
176	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176] ECR, BIHAR	04/2008	228.05	-	03/2024	0/0
177	RAMNA - SINGRAULI DOUBLING - [N22000417] ECR, UTTAR PRADESH	08/2015	2,436.21	03/2020	03/2024	0/0
178	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472] ECR, BIHAR	04/2016	744.04	03/2021	03/2024	0/0
179	SAMASTIPUR-DARBANGHA - [N22000329] ECR, BIHAR	05/2015	380.00	-	03/2025	0/0
180	KOSI BRIDGE (NL), ECR - [220100304] ECR, BIHAR	04/2002	499.41	03/2020	-	0/0
181	DANIAWAN-BIHARSARIF (NL), ECR - [220100311] ECR, BIHAR	04/2001	406.92	-	-	0/0
182	ARA-BHABHUA ROAD (NL) - [N22000166] ECR, BIHAR	04/2008	633.87	-	-	0/0
183	NAWADA-LAXMIPUR (NL) - [N22000167] ECR, BIHAR	04/2008	620.57	-	-	0/0
184	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168] ECR, BIHAR	04/2008	445.25	-	-	0/0
185	GAYA-CHATRA (NL) - [N22000169] ECR, MULTI STATE	04/2008	415.67	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
186	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
187	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
188	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
189	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
190	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
191	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
192	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-	0/0
	<u>East Coast Railway</u>					
193	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	12/2021	0/0
194	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	03/2020 03/2021	03/2022	0/0
195	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
196	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2024	03/2024	0/0
197	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2024	03/2024	0/0
198	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2024	0/0
199	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2024	03/2024	0/0
200	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 03/2025	03/2025	0/0
201	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 03/2026	03/2026	0/0
202	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
	<u>Eastern Railways</u>					
203	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
204	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021	0/0
205	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
206	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
207	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64	-	03/2022	0/0
209	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09	02/2013	03/2024	0/0
210	MONIGRAM- NIMTITA - [N22000301]ER, MULTI STATE	04/2012	250.93	-	03/2024	0/0
211	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91	03/2019 12/2009	03/2025	0/0
212	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99	03/2006	03/2025	0/0
213	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	450.00	-	03/2025	0/0
214	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03	-	03/2025	0/0
215	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98	03/2022	03/2025	0/0
216	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	923.52	03/2016	03/2025	0/0
217	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.51	03/2017	03/2025	0/0
218	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER, MULTI STATE	04/2010	174.56	-	03/2025	0/0
219	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28	03/2016	03/2025	0/0
220	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	365.17	03/2017	03/2025	0/0
221	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55	-	03/2025	0/0
222	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17	-	03/2025	0/0
223	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	494.54	03/2005	03/2025	0/0
224	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER, MULTI STATE	04/2000	297.47	-	03/2025	0/0
225	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER, MULTI STATE	04/2003	337.96	-	03/2025	0/0
226	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER, MULTI STATE	04/2009	499.96	02/2012	03/2025	0/0
227	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE	04/2009	257.42	03/2014	03/2025	0/0
228	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER, MULTI STATE	04/2011	166.89	-	03/2025	0/0
229	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60	03/2017	03/2026	0/0
<u>Indian Railway Construction Company Limited</u>						
230	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON, ODISHA	04/2016	5,200.00	03/2020	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Kolkata Metro Rail Corporation Limited</u>					
231	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
232	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2021	0/0
233	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
234	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 -	03/2004 -	03/2022	0/0
235	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
236	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
237	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
238	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
239	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
240	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
241	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	03/2021	0/0
242	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	03/2021	0/0
243	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	04/2021	0/0
244	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	04/2021	0/0
245	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	05/2021	0/0
246	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- -	12/2021	0/0
247	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2023	0/0
248	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 5,021.45	03/2014 -	03/2023	0/0
249	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
250	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	12/2023	0/0
251	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
252	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	03/2019 -	03/2024	0/0
253	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	12/2024	0/0
254	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-	0/0
255	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-	0/0
256	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
257	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
258	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-	0/0
259	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
260	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
261	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	-	0/0
262	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-	0/0
<u>North Eastern Railway</u>						
263	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021	0/0
264	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
265	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
266	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0
267	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0
268	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
269	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022	0/0
270	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
271	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
272	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
273	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
274	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
275	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
276	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
277	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
278	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
279	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
<u>North Western Railway</u>						
280	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020	0/0
281	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021	0/0
282	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	03/2021	0/0
283	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2021	0/0
284	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	11/2021	0/0
285	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
286	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	06/2022	0/0
287	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-	0/0
288	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
289	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
<u>Northern Railway</u>						
290	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021	0/0
291	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	06/2021	0/0
292	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2022	0/0
293	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	- -	03/2023	0/0
294	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
295	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0
296	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
297	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
298	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
299	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	03/2023 03/2025	03/2025	0/0
300	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	08/2016 -	08/2025	0/0
301	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
302	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
303	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
304	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
305	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
306	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2021	0/0
307	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	12/2021	0/0
308	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	12/2021	0/0
309	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	12/2021	0/0
310	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2021	0/0
311	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
312	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
313	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	06/2022	0/0
314	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	06/2022	0/0
315	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
316	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
317	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
318	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76 -	12/2023 -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
319	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
320	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
321	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
322	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
323	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
324	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
325	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
326	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
327	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
328	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2026	0/0
329	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-	0/0
<u>Railway Electrification</u>						
330	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
331	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	12/2022	0/0
332	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2023	0/0
333	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2024	0/0
334	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
335	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
336	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2024	0/0
337	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
338	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
339	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
340	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
341	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
342	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	-	0/0
	<u>South Eastern Railway</u>					
343	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020	0/0
344	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	12/2018 12/2018	06/2021	0/0
345	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 03/2020	12/2021	0/0
346	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 03/2021	12/2023	0/0
347	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	03/2025	0/0
348	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
349	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 -	03/2030	0/0
350	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
351	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
	<u>South Western Railway</u>					
352	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	06/2021	0/0
353	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
354	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
355	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
356	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
357	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
358	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
359	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
360	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
361	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
362	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 03/2024	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
363	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
364	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 03/2025	03/2025	0/0
365	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	06/2025	0/0
<u>Southern Railway</u>						
366	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 03/2021	12/2020	0/0
367	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- 02/2021	04/2021	0/0
368	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- 10/2021	09/2021	0/0
369	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021	0/0
370	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	12/2021	0/0
371	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	06/2022	0/0
372	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2022	0/0
373	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- 03/2024	03/2024	0/0
374	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	03/2024	0/0
375	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2025	0/0
376	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
377	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
378	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
379	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0
380	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
381	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
382	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
383	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
384	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
385	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
386	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
387	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
388	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
389	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
390	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
	<u>Western Railway</u>					
391	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 02/2021	02/2021	0/0
392	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 890.76	03/2019 10/2021	10/2021	0/0
393	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	03/2021 12/2021	12/2021	0/0
394	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 12/2022	12/2022	0/0
395	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 411.62	03/2012 03/2023	03/2023	0/0
396	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2023	03/2023	0/0
397	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
398	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	03/2019 03/2023	03/2023	0/0
399	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 03/2023	03/2023	0/0
400	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	03/2022 03/2024	03/2024	0/0
401	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	03/2020 03/2024	03/2024	0/0
402	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2024	03/2024	0/0
403	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
404	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
405	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
406	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
407	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
408	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Central Public Works Department</u>					
409	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-	0/0
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
410	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	-	03/2021	0/0
411	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	03/2021	0/0
412	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	08/2018 09/2021	03/2021	0/0
413	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 -	05/2019	0/0
414	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 -	06/2019	0/0
415	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020	0/0
416	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020	0/0
417	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 05/2020	05/2020	0/0
418	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	06/2020	0/0
419	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	-	09/2020	0/0
420	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020	0/0
421	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
422	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020	0/0
423	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020	0/0
424	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	-	12/2020	0/0
425	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020	0/0
426	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020	0/0
427	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	01/2021	0/0
428	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021	0/0
429	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
430	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021	0/0
431	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021	0/0
432	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	02/2021	0/0
433	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	02/2021	0/0
434	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	03/2021	0/0
435	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	03/2021	0/0
436	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 634.30	12/2019 03/2021	03/2021	0/0
437	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021	0/0
438	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	03/2021	0/0
439	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	03/2021	0/0
440	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2021	0/0
441	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021	0/0
442	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2021	0/0
443	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 03/2021	03/2021	0/0
444	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	04/2021	0/0
445	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 04/2021	04/2021	0/0
446	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2020	04/2021	0/0
447	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 03/2021	04/2021	0/0
448	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 04/2021	04/2021	0/0
449	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	04/2021	0/0
450	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	04/2021	0/0
451	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2020	05/2021	0/0
452	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	05/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
453	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	05/2021	0/0
454	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
455	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	05/2021	0/0
456	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 06/2021	06/2021	0/0
457	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- 03/2021	06/2021	0/0
458	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 06/2021	06/2021	0/0
459	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 01/2021	06/2021	0/0
460	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	06/2021	0/0
461	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	06/2021	0/0
462	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	06/2021	0/0
463	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 06/2021	06/2021	0/0
464	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	06/2021	0/0
465	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	06/2021	0/0
466	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2021	06/2021	0/0
467	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 12/2020	06/2021	0/0
468	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 06/2021	06/2021	0/0
469	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	03/2018 06/2021	06/2021	0/0
470	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	08/2016 06/2021	06/2021	0/0
471	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 06/2021	06/2021	0/0
472	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	09/2016 06/2021	06/2021	0/0
473	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	10/2016 06/2021	06/2021	0/0
474	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	07/2016 06/2021	06/2021	0/0
475	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 06/2021	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
476	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 06/2021	06/2021	0/0
477	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 06/2021	06/2021	0/0
478	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	12/2020 -	06/2021	0/0
479	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 07/2021	07/2021	0/0
480	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	07/2020 -	08/2021	0/0
481	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021	0/0
482	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	09/2021	0/0
483	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	09/2021	0/0
484	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
485	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	10/2021	0/0
486	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 11/2021	11/2021	0/0
487	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	12/2021	0/0
488	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	08/2019 -	12/2021	0/0
489	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN	03/2020	370.36 -	08/2022 -	08/2022	0/0
490	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	08/2022	0/0
491	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	08/2022	0/0
492	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	11/2022	0/0
493	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
494	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
495	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
496	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
497	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
498	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
499	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
500	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
501	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
502	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
503	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
504	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
505	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
506	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-	0/0
507	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 12/2020	-	0/0
508	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 12/2020	-	0/0
509	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 12/2020	-	0/0
510	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
511	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
512	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
513	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
514	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
515	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
516	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
517	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
518	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
519	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
520	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
521	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
522	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
523	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-	0/0
524	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-	0/0
525	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-	0/0
526	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 390.73	05/2017 -	-	0/0
527	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
528	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
529	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
530	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
531	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
532	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
533	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
534	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
535	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-	0/0
536	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
537	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
538	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-	0/0
539	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUARI - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-	0/0
540	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-	0/0
541	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
542	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-	0/0
543	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
544	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
545	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH, BIHAR	01/1991	319.68 -	- -	-	0/0
546	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH, BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
547	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH, BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
548	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH, BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
549	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH, BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
550	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH, BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
551	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH, BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
552	FOUR LANEING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH, BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
553	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH, BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
554	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH, BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
555	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH, MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
556	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH, MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
557	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH, BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
558	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH, ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
559	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MoRTH, ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
560	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH, ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
561	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH, ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
562	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH, ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
563	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH, ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
564	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH, UTTARAKHAND	12/2017	257.34 -	12/2019 -	-	0/0
565	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH, UTTARAKHAND	12/2017	200.34 -	12/2019 -	-	0/0
566	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH, UTTARAKHAND	12/2017	248.22 -	12/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
567	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-	0/0
568	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-	0/0
569	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-	0/0
570	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-	0/0
571	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-	0/0
572	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
573	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-	0/0
574	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
575	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-	0/0
576	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-	0/0
577	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-	0/0
578	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-	0/0
579	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-	0/0
580	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-	0/0
581	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
582	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
583	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
584	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
585	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
586	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
587	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
588	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
589	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
590	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
591	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-	0/0
592	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0
593	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0
594	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
595	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
596	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
597	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
598	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
599	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
600	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
601	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
602	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
603	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
604	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0
605	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
606	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
607	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
608	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
609	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
610	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-	0/0
611	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-	0/0
612	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
613	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-	0/0
614	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-	0/0
615	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
616	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
617	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
618	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-	0/0
619	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-	0/0
620	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
621	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
622	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-	0/0
623	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-	0/0
624	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
625	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-	0/0
626	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-	0/0
627	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-	0/0
628	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-	0/0
629	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-	0/0
630	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-	0/0
631	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
632	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-	0/0
633	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
634	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-	0/0
635	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
636	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
637	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-	0/0
638	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-	0/0
639	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-	0/0
640	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-	0/0
641	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-	0/0
642	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-	0/0
643	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
644	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
645	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
646	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
647	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
648	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
649	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
650	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
651	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
652	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
653	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
654	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
655	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
656	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
657	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0
658	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
659	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
660	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
661	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2020	-	0/0
662	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-	0/0
663	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
664	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-	0/0
665	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0
666	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
667	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-	0/0
668	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-	0/0
669	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ - [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-	0/0
670	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-	0/0
671	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-	0/0
672	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-	0/0
673	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-	0/0
674	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-	0/0
675	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-	0/0
676	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-	0/0
677	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-	0/0
678	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-	0/0
679	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-	0/0
680	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-	0/0
681	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-	0/0
682	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020	0/0
683	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
National Highways And Infrastructure Development Corporation Ltd.						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
684	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	07/2022	0/0
685	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	09/2018 -	11/2022	0/0
686	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	04/2023	0/0
687	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	04/2023	0/0
688	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	04/2023	0/0
689	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	06/2023	0/0
690	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	06/2023	0/0
691	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	07/2023	0/0
692	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2023	0/0
693	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	04/2024	0/0
694	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-	0/0
695	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
696	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
697	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
698	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
699	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-	0/0
700	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0
National Highways Authority Of India						
701	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	03/2021	0/0
702	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	10/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
703	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
704	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015	0/0
705	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
706	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018	0/0
707	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
708	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
709	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019	0/0
710	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
711	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020	0/0
712	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020	0/0
713	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020	0/0
714	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020	0/0
715	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
716	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
717	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020	0/0
718	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020	0/0
719	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
720	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020	0/0
721	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020	0/0
722	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020	0/0
723	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
724	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
725	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020	0/0
726	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
727	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
728	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
729	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020	0/0
730	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020	0/0
731	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020	0/0
732	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021	0/0
733	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021	0/0
734	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021	0/0
735	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	02/2021	0/0
736	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	02/2021	0/0
737	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
738	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	02/2021	0/0
739	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
740	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2021	0/0
741	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 03/2021	03/2021	0/0
742	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021	0/0
743	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 07/2019	03/2021	0/0
744	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2021	0/0
745	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 10/2020	03/2021	0/0
746	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	03/2021	0/0
747	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021	0/0
748	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	03/2021	0/0
749	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
750	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
751	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021	0/0
752	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
753	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	05/2021	0/0
754	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 05/2021	05/2021	0/0
755	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
756	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	05/2021	0/0
757	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	05/2021	0/0
758	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 06/2021	06/2021	0/0
759	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	06/2021	0/0
760	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	06/2021	0/0
761	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	06/2021	0/0
762	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	06/2021	0/0
763	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	06/2021	0/0
764	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	06/2021	0/0
765	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	06/2021	0/0
766	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	06/2021	0/0
767	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	06/2021	0/0
768	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
769	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2021	0/0
770	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2021	0/0
771	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	07/2021	0/0
772	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	07/2021	0/0
773	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
774	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
775	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	07/2021	0/0
776	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
777	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	07/2021	0/0
778	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
779	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
780	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	08/2021	0/0
781	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
782	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	08/2021	0/0
783	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	08/2021	0/0
784	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- 02/2021	08/2021	0/0
785	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021	0/0
786	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	09/2021	0/0
787	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	09/2021	0/0
788	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
789	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
790	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
791	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
792	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 06/2021	12/2021	0/0
793	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 06/2021	12/2021	0/0
794	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 01/2021	12/2021	0/0
795	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	03/2020 -	12/2021	0/0
796	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
797	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	12/2021	0/0
798	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
799	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	01/2022	0/0
800	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	01/2022	0/0
801	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
802	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 08/2021	02/2022	0/0
803	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 12/2021	03/2022	0/0
804	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 03/2022	03/2022	0/0
805	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	03/2022	0/0
806	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022	0/0
807	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022	0/0
808	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
809	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 -	03/2023 -	03/2023	0/0
810	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
811	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
812	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
813	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
814	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
815	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
816	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
817	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
818	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
819	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
820	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
821	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
822	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
823	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
824	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
825	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
826	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
827	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
828	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
829	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
830	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
831	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-	0/0
832	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
833	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
834	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
835	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
836	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
837	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-	0/0
838	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
839	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
840	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
841	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
842	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
843	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
844	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	-	0/0
845	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
846	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
847	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
848	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-	0/0
849	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0
850	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
851	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
852	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
853	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-	0/0
854	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
855	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
856	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-	0/0
857	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
858	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
859	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
860	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
861	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
862	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
863	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
864	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
865	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
866	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
867	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
868	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-	0/0
869	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
870	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
871	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
872	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
873	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
874	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0
875	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
876	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-	0/0
877	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
878	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
879	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
880	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-	0/0
881	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
882	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
883	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
884	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-	0/0
885	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-	0/0
886	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
887	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
888	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
889	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
890	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
891	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
892	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-	0/0
893	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
894	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
895	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
896	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
897	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND	07/2016	458.03 486.00	- -	-	0/0
898	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-	0/0
899	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-	0/0
900	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
901	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
902	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-	0/0
903	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-	0/0
904	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
905	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-	0/0
906	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-	0/0
907	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-	0/0
908	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
909	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
910	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
911	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-	0/0
912	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
913	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
914	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-	0/0
915	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-	0/0
916	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
917	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-	0/0
918	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
919	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-	0/0
920	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-	0/0
921	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
922	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
923	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
924	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0
925	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
926	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
927	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
928	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
929	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
930	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
931	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
932	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
933	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
934	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
935	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
936	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
937	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
938	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
939	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
940	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
941	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
942	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
943	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
944	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
945	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
946	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
947	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
948	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
949	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
950	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
951	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
952	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
953	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
954	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
955	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
956	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
957	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
958	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
959	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
960	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965,) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
961	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
962	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
963	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
964	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
965	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
966	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-	0/0
967	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
968	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
969	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
970	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-	0/0
971	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0
972	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
973	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-	0/0
974	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
975	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
976	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- 02/2020	-	0/0
977	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
978	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
979	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
980	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-	0/0
981	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-	0/0
982	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-	0/0
983	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
984	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-	0/0
985	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-	0/0
986	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-	0/0
987	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-	0/0
988	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STATE - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-	0/0
989	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
990	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-	0/0
991	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Inland Waterways Authority Of India</u>					
992	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	5,369.18 4,633.81	03/2023 -	03/2023	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
993	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	06/2021 -	11/2021	0/0
	<u>Central Public Works Department</u>					
994	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	03/2018 -	06/2021	0/0
	<u>Department Of Telecommunication</u>					
995	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	06/2021	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
996	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12/2018 -	08/2022	0/0
997	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT	03/2019	5,384.17 -	03/2024 -	03/2024	0/0
998	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	03/2024 -	03/2024	0/0
	<u>Central Public Works Department</u>					
999	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 -	11/2020	0/0
1000	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	03/2021 07/2021	07/2021	0/0
1001	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	08/2020 -	03/2022	0/0
1002	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 -	03/2022	0/0
1003	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	07/2021 -	12/2024	0/0
1004	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
1005	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1006	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE-VI-5), SHOPS, CO - [N28000149]CPWD, CHHATISGARH	05/2019	299.97 -	09/2020 -	-	0/0
	<u>Delhi Metro Rail Corporation</u>					
1007	DELHI MRTS PHASE-III - [N28000056]DMRC, DELHI	09/2011	38,585.00 -	03/2016 -	09/2021	0/0
1008	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC, DELHI	05/2017	565.00 -	12/2020 -	09/2021	0/0
1009	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC, DELHI	07/2019	24,948.65 -	03/2025 -	03/2025	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1010	KOCHI METRO RAIL PROJECT - [N28000081]KMRL, KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1011	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL, UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	03/2024	0/0
1012	AGRA METRO RAIL PROJECT - [N28000145]LMRCL, UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	03/2024	0/0
1013	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1014	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC, MAHARASHTRA	12/2016	11,420.00 -	11/2021 -	11/2021	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1015	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 09/2022	03/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1016	BHOPAL METRO RAIL - [N28000124]MPMRCL, MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1017	INDORE METRO RAIL - [N28000125]MPMRCL, MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1018	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-	0/0
	<u>National Capital Region Transport Corp</u>					
1019	DELHI GHAZIABAD MEERUT RTS CORRIDOR - [N28000134]NCRTC, MULTI STATE	03/2019	30,274.00 -	06/2025 -	06/2025	0/0
	<u>Patna Metro Rail Corporation</u>					
1020	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL, BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1021	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB, MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2021	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1022	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021	0/0
1023	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	03/2021	0/0
1024	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
1025	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021	0/0
1026	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0
1027	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	06/2021	0/0
1028	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	04/2020 -	06/2021	0/0
1029	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
1030	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
1031	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	12/2021	0/0
1032	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0
1033	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
1034	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-	0/0
1035	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-	0/0
<u>Delhi Jal Board</u>						
1036	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021	0/0
1037	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
1038	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
1039	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
1040	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-	0/0
<u>Kolkata Metropolitan Development Authority</u>						
1041	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021	0/0
1042	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	05/2021	0/0
1043	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1044	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
1045	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
1046	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
1047	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
1048	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0
1049	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	02/2022 -	06/2022	0/0
1050	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
1051	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	09/2022 -	09/2022	0/0
1052	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	02/2022 -	10/2022	0/0
<u>Uttar Pradesh Jal Nigam</u>						
1053	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP JalNigam, UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021	0/0
1054	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UP JalNigam, UTTAR PRADESH	10/2016	370.40 430.49	08/2020 03/2021	03/2021	0/0
1055	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UP JalNigam, UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021	0/0
1056	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021	0/0
1057	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
1058	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
1059	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UP JalNigam, UTTAR PRADESH	03/2018	904.00 -	09/2021 -	09/2021	0/0
1060	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
1061	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0
1062	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam, UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
1063	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam, UTTAR PRADESH	10/2017	213.62 261.12	03/2022 -	03/2022	0/0
1064	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UP JalNigam, UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
1065	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12 213.91	07/2021 -	06/2022	0/0
<u>Uttarakhand Pey Jal Nigam</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
1066	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	03/2021	0/0
1067	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-	0/0
	<u>COMMERCE</u>					
	<u>National Building Construcion Corporation Ltd</u>					
1068	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	-	0/0
	<u>HUMAN RESOURCE DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
1069	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	06/2021	0/0
1070	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	03/2021 -	06/2022	0/0
1071	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH	09/2018	392.51 -	06/2022 -	06/2022	0/0
1072	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	07/2022 -	07/2022	0/0
1073	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD,CHHATISGARH	03/2020	808.62 -	07/2022 -	07/2022	0/0
1074	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	03/2022 -	09/2022	0/0
1075	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 375.00	09/2020 -	11/2022	0/0
1076	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	09/2022 -	01/2023	0/0
1077	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	04/2023 -	04/2023	0/0
1078	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-	0/0
	<u>Edcil(India) Limited</u>					
1079	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-	0/0
	<u>Indian Institute Of Technology, Kharagpur</u>					
1080	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
1081	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-	0/0
	<u>HOME AFFAIRS</u>					
	<u>Central Public Works Department</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1082	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]CPWD,HARYANA	01/2020	166.98 -	05/2022 -	05/2022	0/0
1083	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]CPWD,DELHI	06/2019	277.35 -	07/2022 -	07/2022	0/0
1084	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE - - [N28000147]CPWD,HARYANA	01/2020	166.98 167.00	10/2023 -	10/2023	0/0
	<u>DPIIT</u>					
	<u>Delhi Mumbai Industrial Corridor</u>					
1085	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021	0/0
	<u>India International Convention And Expo Centre</u>					
1086	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	12/2019 -	12/2021	0/0
	Total		13,11,039.98 -			0/0
	Grand Total		13,11,039.98			0/0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	166.90	05/2013 -	08/2021	-55.37	99
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	364.59	12/2009 -	-	-39.64	0
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	469.31	01/2014 -	12/2020	61.08	83
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
5	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	-	.00	0
6	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
7	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	06/2020	.00	46
8	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
9	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
10	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	-	.00	0
11	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	591.00	11/2013 -	01/2021	15.53	86
12	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	-	.00	0
13	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	01/2022	.00	93
14	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
15	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	-	.00	0
16	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	-	.00	0
17	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (March 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	-	.00	0
19	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	-	.00	0
20	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	0
21	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	-	.00	0
22	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2022	.00	103
23	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2021	.00	81
24	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	05/2021	.00	93
25	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	10/2020	.00	76
26	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
27	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
28	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88 -	1,226.88	02/2021 -	-	.00	0
29	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	-	.00	0
30	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	0
31	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	-	.00	0
32	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	-	.00	0
33	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	-	.00	0
34	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
35	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	-	.00	0
36	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	-	.00	0
37	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (March 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	-	.00	0
39	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10 -	1,601.10	02/2021 -	-	.00	0
40	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
41	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	12/2020	.00	52
42	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	01/2019 -	-	.00	0
43	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	-	.00	0
44	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	-	.00	0
45	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	03/2021	.00	96
46	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	-	.00	0
47	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	-	.00	0
48	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	-	.00	0
49	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	09/2020	.00	62
50	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	-	.00	0
51	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	04/2019 -	09/2021	.00	29
52	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00 -	2,159.00	01/2019 -	-	.00	0
53	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	-	.00	0
54	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	2,360.65	-	-	41.78	0
55	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
56	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
57	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	03/2021	52.73	71
58	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	-	167.82	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (March 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		74,577.61 -	79,826.06				
	Grand Total		74,577.61	79,826.06				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	12320	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	11459	74
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	03/2023	380.87	12
6	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	06/2021	177.1	16
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2022	1142	12
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	07/2021	456.86	10
9	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	12/2021	458	21
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2021	417.23	33
11	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	05/2021	303.8	13
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	09/2022	2467	7
13	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	09/2022	1383	12
14	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	10/2022	389.71	11

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
15	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	03/2022	304.13	60
16	PACHWARA SOUTH COAL BLOCK	NLC	07/2013	08/2022	09/2023	1795.01	13
17	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	06/2022	243	50
18	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	03/2022	1230.27	83
19	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2022	447.06	84
20	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2022	417.33	68
22	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2021	430.45	60
23	RECAST EPR AMRAPALI OC	CCL	02/2012	03/2020	03/2024	4983.58	48
24	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2022	869.44	12
25	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	03/2022	198.68	36
26	BHATADI EXPANSION OC MINE	WCL	02/2016	03/2019	03/2026	304.52	84
27	DURGAPUR OPENCAST PROJECT	SECL	02/2015	03/2023	03/2026	916.24	36
28	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2022	510.85	72
29	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	MCL	12/2007	03/2013	03/2028	8416.19	180
30	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
31	BHUBANESWARI EXPENSION OCP(40.0 MTY)	MCL	12/2007	03/2017	03/2031	3145.45	168
32	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
33	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2022	479.53	108
34	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	MCL	12/2007	03/2010	03/2029	3504.21	228
35	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	04/2023	339.88	108
36	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2024	1375.38	36
37	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	WCL	11/2014	03/2020	03/2027	1184.33	84
38	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
39	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
40	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	07/2021	289.45	86
41	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	03/2025	295.56	72
42	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2022	397.09	36
43	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
45	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2022	1783.09	12
46	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	84
47	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2025	6964.33	152
48	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
49	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2022	163.51	132
50	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2022	162.46	96
51	EXPANSION PR OF JHANJRA UG(5.00 MTY)	ECL	11/2015	03/2022	03/2029	1210.12	84
52	KISTARAM OCP	SCCL	11/2010	03/2015	03/2022	242.29	84
53	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2022	178.44	96
54	CHHAL OC SEAM -III (6.00 MTY)	SECL	12/2013	03/2022	03/2025	610.63	36
55	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	03/2025	1458.17	117
56	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	WCL	11/2015	03/2021	03/2024	313.34	36
57	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	WCL	11/2015	03/2020	03/2026	851.6	72
58	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2021	1055.05	36
59	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
60	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	07/2022	17237	8
61	RPR FOR JAMUNIA UG (0.90 MTY)	WCL	07/2016	03/2022	03/2026	281.25	48
62	RECAST PR FOR DHANKASA UG (1.00 MTY)	WCL	09/2016	03/2022	03/2025	289.29	36
63	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
64	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

CULTURE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
65	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	03/2021	151.33	42

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
66	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	06/2021	246.31	16

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
67	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	12/2021	4773	24
68	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	12579.09	22

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
69	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	05/2021	426.72	13
70	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	NFL	01/2018	11/2019	04/2021	215.92	17
71	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	NFL	01/2018	11/2019	04/2021	218.83	17
72	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	NFL	01/2018	11/2019	04/2021	239.81	17

FINANCE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
73	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD	12/2015	10/2019	04/2021	209	18

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
74	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD	03/2018	09/2020	04/2022	195	19
75	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD	12/2018	06/2021	05/2022	260	11
76	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	HITES	07/2016	06/2020	07/2021	703	13
77	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	HITES	07/2016	04/2020	07/2021	785	15
78	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	03/2021	272.19	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	06/2021	355.15	27
80	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	05/2021	414.11	90
81	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	03/2021	204.44	46
82	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	03/2021	152.95	37
83	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	12/2021	363.99	43
84	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
85	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	CPWD	09/2017	03/2020	12/2021	150.29	21
86	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	HITES	05/2017	05/2021	07/2022	875	14

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
87	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	12/2021	1219.21	26
88	NSG AT KOLKATA	CPWD	10/2014	04/2018	12/2021	162.88	44

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
89	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD	09/2018	09/2020	11/2022	375	26
90	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	CPWD	02/2019	09/2020	03/2021	186	6
91	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	CPWD	11/2017	03/2020	06/2021	171.72	15
92	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE 1A AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD	07/2019	03/2021	06/2022	753.63	15
93	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD	07/2019	03/2022	09/2022	851	6
94	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	06/2021	171.86	63
95	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2021	496.18	52
96	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	04/2021	294	24
97	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	CPWD	01/2018	07/2020	06/2021	223.37	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
98	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	CPWD	12/2016	07/2019	03/2021	549.31	20
99	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	02/2022	430	21

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
100	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	12/2022	5540	20
101	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	03/2023	483	23

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	GAIL	08/2018	04/2021	10/2021	217.92	6
103	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	03/2022	164.69	8
104	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1933	12
105	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2021	2433	6
106	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	3437	12
107	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1740	12
108	PIPELINE NETWORK PROJECT GELEKI, ASSAM	ONGC	07/2016	05/2020	05/2021	249.85	12
109	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677	14
110	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	10/2021	163.02	18
111	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	09/2021	421	13
112	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND	IOCL	08/2017	06/2020	09/2021	236	15
113	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
114	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	HPCL	11/2017	11/2020	06/2021	255	7
115	PUNE POL STORAGE DEPOT	BPCL	08/2016	08/2020	03/2021	282.64	7
116	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
117	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE	OIL	01/2018	02/2020	04/2021	543.91	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	OIL AND NATURAL GAS FROM NA						
118	BS VI PROJECT AT GUWAHATI REFINERY	IOCL	08/2018	02/2020	06/2021	557	16
119	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	04/2022	1636	20
120	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
121	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	12/2021	522	9
122	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	12/2021	225.54	10
123	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
124	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	03/2022	909	14
125	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	02/2022	598	24
126	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	06/2021	286.42	10
127	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	04/2021	224.75	8
128	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14
129	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	05/2021	3313	15
130	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
131	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15
132	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
133	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	09/2021	206.5	6
134	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	08/2021	206.63	18
135	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	11/2021	255.4	15
136	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	08/2022	199.36	22
137	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2021	906	20
138	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
139	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
140	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM	IOCL	06/2016	08/2019	06/2021	423	22

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AS RESITEMENT OF RAMNAGAR DEPOT						
141	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2021	650.82	26
142	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	06/2022	34012	24
143	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497	38
144	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	10/2021	1810	22
145	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	04/2021	571.66	16
146	MMPL PIPELINE REROUTING PROJECT	BPCL	04/2013	12/2019	04/2021	449.58	16
147	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2021	3190.69	37
148	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	06/2021	160.1	16
149	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	03/2022	161.59	27
150	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
151	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	06/2021	581	15
152	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2021	352.56	48
153	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	53
154	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321	15
155	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	05/2021	690	34
156	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2021	861.79	94
157	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2021	4588.29	33
158	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	06/2021	327.78	38
159	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	06/2022	462.3	9
160	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	07/2022	278.6	13
161	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2023	371	6
162	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2023	2281.94	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
163	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	07/2021	196.26	12

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
164	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	07/2021	529.68	32
165	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	07/2021	1885.13	31
166	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	09/2024	18668	18
167	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	PGCIL	05/2016	11/2019	04/2021	14733.37	17
168	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	06/2021	322.3	28
169	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	05/2021	235.53	23
170	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	06/2021	379.95	18
171	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	PGCIL	02/2017	04/2020	06/2021	5070.13	14
172	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	63
173	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	36
174	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	04/2021	358.83	11
175	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	CPWD	10/2017	11/2019	06/2021	271.9	19
176	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	11130.19	108
177	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	06/2021	374.63	62
178	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	05/2021	522.29	54
179	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	117
180	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
181	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	03/2021	9188.98	20
182	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	05/2021	12532.44	29
183	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	14366.58	40
184	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	63

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
185	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	05/2021	3500	10
186	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	04/2021	186.17	21
187	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	06/2021	1931.39	16
188	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	12964.6	43
189	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	07/2022	3919.59	154
190	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
191	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2021	4824.12	101
192	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	06/2021	197.4	39
193	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2021	1394.52	49
194	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	06/2021	5353	107
195	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	126
196	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	141
197	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	07/2022	10598.98	20
198	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	04/2021	808.63	39
199	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	04/2021	454.11	36
200	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
201	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
202	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108
203	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625	63
204	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
205	CONSTRUCTION OF 3RD LINE BETWEEN	BITES	02/2016	03/2020	06/2021	393.98	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW						
206	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	03/2022	3055	42
207	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	31
208	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
209	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	198
210	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
211	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760	27
212	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	12/2021	213	68
213	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
214	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
215	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	03/2021	622.5	47
216	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
217	GARHWA ROAD-RAMNA	ECR	03/2015	03/2021	03/2022	348.23	12
218	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	24
219	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
220	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	36
221	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	15
222	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
223	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
224	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	21
225	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
226	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	21
227	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2021	1402.02	21
228	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
229	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
230	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	12
231	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
232	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	12
233	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
234	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
235	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631	24
236	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
237	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	2499.71	24
238	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
239	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	64
240	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63
241	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
242	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
243	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2021	258.2	30
244	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548	36
245	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2024	1798	60
246	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	24
247	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2021	314	24
248	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	69
249	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
250	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
251	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.2	180

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
252	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
253	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
254	RAMGANJMUHDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.6	24
255	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
256	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
257	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
258	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
259	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2023	2393.47	108
260	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	07/2021	477.88	112
261	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	168
262	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
263	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	24
264	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
265	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
266	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28
267	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
268	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	12
269	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
270	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
271	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
272	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
273	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
274	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
275	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
276	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287	114
277	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
278	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
279	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	15
280	KADAPA-BANGALORE (NL), KADAPA- PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	156
281	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
282	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
283	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
284	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	216
285	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
286	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	128
287	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	04/2021	1180.19	148
288	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	204
289	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
290	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2021	495.74	102
291	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.2	48
292	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
293	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2024	2326.52	117
294	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2021	5300	84
295	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	11/2021	410.08	33
296	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
297	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500	241
298	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
299	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
300	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
301	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	04/2021	511.86	12
302	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
303	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60
304	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2023	318.24	132
305	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	48
306	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
307	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	34
308	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
309	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
310	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2022	155.81	24
311	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	36
312	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
313	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	15
314	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	06/2021	578	15
315	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	60
316	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	05/2021	678.54	26
317	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
318	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	63
319	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
320	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
321	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	48
322	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2021	1037.15	9
323	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
324	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	NWR	04/2013	03/2020	06/2021	420.18	15
325	AJMER-BANGURGRAM	NWR	04/2011	11/2019	03/2021	213.39	16
326	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
327	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
328	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
329	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36
330	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	03/2023	1491.47	36
331	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2023	1763.93	36
332	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
333	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
334	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
335	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
336	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	21
337	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33
338	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
339	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
340	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	39
341	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
342	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
343	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	03/2024	5200	48
344	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2022	528.57	36
345	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
346	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	CCOI	01/2013	03/2018	03/2021	387.7	36
347	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2021	346.32	24
348	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	9
349	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	34
350	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2025	644.78	96
351	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2023	2288	21

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
352	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	MoRTH	08/2020	11/2020	08/2022	196.23	21
353	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	NHAI	03/2019	05/2020	05/2022	1047	24
354	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	MoRTH	11/2018	12/2020	06/2021	281.45	6
355	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	12/2021	990.97	24
356	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	04/2022	847	25
357	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO	MoRTH	03/2020	08/2020	08/2022	255.23	24
358	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 0	MoRTH	03/2016	05/2016	04/2021	995.09	59
359	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	MoRTH	11/2017	04/2018	03/2021	187.82	35
360	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	MoRTH	11/2017	04/2018	03/2021	163.95	35
361	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	06/2018	04/2021	370.3	34
362	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	05/2018	06/2021	341.79	37

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
363	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MoRTH	01/2018	08/2018	05/2021	418.03	33
364	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MoRTH	01/2016	08/2016	07/2021	348.95	59
365	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	05/2021	263.45	44
366	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MoRTH	01/2016	08/2016	06/2021	497.14	58
367	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	06/2021	205.05	51
368	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	09/2021	214.69	42
369	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2021	217.22	31
370	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2021	233.04	39
371	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	04/2021	249.05	33
372	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	06/2021	254.17	40
373	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	06/2021	279.44	39
374	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	06/2021	373.82	21
375	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	05/2021	809.16	34
376	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	06/2021	193.69	128
377	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2021	195.04	128
378	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
379	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	07/2022	1176.37	59
380	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
381	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	44
382	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	07/2022	1227.87	58
383	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	MoRTH	03/2015	10/2015	03/2021	271.45	65
384	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
385	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
386	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	04/2021	497.05	47
387	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	06/2021	628.45	17
388	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	04/2021	957.54	14
389	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	06/2021	511.83	46
390	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	04/2021	294.17	63
391	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	73
392	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	MoRTH	01/2012	04/2015	03/2021	410.72	71
393	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	08/2021	374	99
394	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM)	NHAI	04/2012	04/2014	01/2022	624	93
395	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	03/2021	1724.55	96
396	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105
397	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	05/2021	1078.84	93
398	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	03/2022	998.79	103
399	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2021	1047	81
400	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	03/2021	1928.22	71
401	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	09/2021	2128.72	29
402	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2021	531.13	37
403	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2021	593.26	37
404	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	03/2022	649.5	36
405	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	06/2021	505	37
406	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	03/2021	1423.96	28
407	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
408	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2021	707.82	31
409	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2021	546	29
410	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2021	591.66	29
411	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	03/2021	804.97	33
412	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	12/2021	1167.42	33
413	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	03/2021	2510.04	19
414	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	03/2021	446.17	24
415	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	12/2021	848.45	21
416	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	09/2021	754.54	18
417	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	NHAI	03/2017	03/2020	05/2021	639.79	14
418	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
419	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	15
420	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
421	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
422	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	05/2021	373.07	57
423	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	05/2021	396.52	57
424	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	05/2021	429.52	57
425	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	07/2021	894	15
426	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
427	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
428	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	07/2022	339.57	46
429	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
430	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD	NHIDCL	03/2018	09/2018	09/2022	285.68	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	FROM EXISTING KM 52.370 TO						
431	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	NHIDCL	03/2018	09/2018	12/2021	315.03	39
432	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	NHIDCL	03/2018	09/2018	12/2021	240.64	39
433	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	11/2021	215.12	38
434	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2021	215.79	39
435	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
436	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	NHIDCL	03/2018	09/2018	11/2022	323.98	50
437	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
438	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	07/2023	640.07	46
439	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
440	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
441	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
442	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
443	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
444	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	09/2023	428.11	48
445	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
446	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2021	162.56	39
447	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2021	166.21	31
448	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	06/2021	169.63	39
449	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	MoRTH	01/2017	09/2019	05/2021	396.86	20
450	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	12/2021	426.18	15
451	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	06/2021	184.62	40
452	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	11/2022	160.27	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
453	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	12/2021	236.78	28
454	REHABILITATION AND UPGRADE OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	04/2021	877.79	22
455	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	MoRTH	03/2018	07/2020	08/2021	322.48	13
456	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	08/2021	1069.59	22
457	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	05/2021	170.57	6
458	REHABILITATION AND UPGRADE OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	MoRTH	09/2016	02/2017	06/2021	372.68	52
459	REHABILITATION AND UPGRADE OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MoRTH	11/2016	05/2017	07/2021	290.15	50
460	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MoRTH	02/2017	11/2017	04/2021	429.43	41
461	REHABILITATION AND UPGRADE OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MoRTH	03/2018	08/2018	03/2021	228.32	31
462	REHABILITATION AND UPGRADE OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MoRTH	11/2015	06/2017	06/2021	335.32	48
463	REHABILITATION AND UPGRADE OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MoRTH	01/2016	09/2016	06/2021	476.2	57
464	REHABILITATION AND UPGRADE OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2021	624.98	56
465	REHABILITATION AND UPGRADE OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	06/2021	452.94	59
466	REHABILITATION AND UPGRADE OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	MoRTH	03/2017	01/2018	03/2021	423.79	38
467	REHABILITATION AND UPGRADE OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	06/2021	496.02	75
468	UPGRADE AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	06/2021	188.8	25
469	UPGRADE AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	06/2021	379.16	43
470	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	MoRTH	03/2016	12/2019	03/2021	536.65	15
471	BARASGAON TO RAHATEE	MoRTH	07/2016	09/2018	04/2021	289.11	31
472	REHABILITATION AND UPGRADE OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	MoRTH	03/2016	01/2020	03/2021	240.3	14
473	REHABILITATION AND UPGRADE OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MoRTH	10/2013	03/2017	04/2021	445.89	49
474	REHABILITATION AND UPGRADE OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	MoRTH	03/2016	05/2019	03/2021	249.5	22
475	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	06/2021	392.33	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
476	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	MoRTH	02/2017	05/2019	05/2021	157.32	24
477	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	MoRTH	10/2016	08/2020	07/2021	171.9	11
478	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	MoRTH	01/2019	03/2021	11/2021	264.5	8
479	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	MoRTH	10/2016	03/2020	03/2021	218.9	12
480	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	MoRTH	07/2016	10/2019	03/2021	208.88	17
481	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MoRTH	03/2018	04/2020	04/2021	263.89	12
482	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	MoRTH	03/2018	08/2020	03/2021	288.3	7
483	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	MoRTH	03/2016	09/2020	05/2021	296.5	8

RURAL DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
484	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	10/2021	149.73	70
485	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSCL	12/2007	12/2016	10/2021	202.61	58
486	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	12/2021	175.49	60

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
487	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	SAIL	12/2018	09/2020	05/2021	263.36	8
488	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	05/2021	262.87	23
489	FORGED WHEEL PLANT	RINL	04/2014	09/2018	04/2021	1682.85	31
490	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2021	1034.01	50
491	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2021	15525	74

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
492	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD	10/2016	03/2018	06/2021	248.2	39
493	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2021	13334	71

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
494	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	DMRC	05/2017	12/2020	09/2021	565	9
495	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	12/2024	1180	41
496	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	06/2024	26405.14	64
497	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	12/2021	197.33	32
498	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	03/2023	23136	98
499	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	09/2021	38585	66
500	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	CMRL	06/2016	03/2018	03/2021	3770	36
501	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	CPWD	10/2016	08/2020	03/2022	392	19
502	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	10773	44

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
503	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	KMDA	12/2014	04/2020	03/2021	272.32	11
504	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	KMDA	02/2014	12/2019	05/2021	274.76	17
505	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	KMDA	05/2018	02/2022	10/2022	160	8
506	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	BUIDCO	04/2015	04/2020	06/2021	184.93	14
507	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	03/2021	225.77	12
508	I AND D AND STP AT CHAPPRA	BUIDCO	11/2018	12/2020	06/2021	236.15	6
509	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	06/2022	298.12	11
510	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
511	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
512	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
513	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	BPB	03/2017	12/2019	12/2021	233.57	24
514	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12
515	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	UPJalNigam	02/2017	11/2019	03/2021	161.31	16
516	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	UPJalNigam	10/2016	08/2020	03/2021	370.4	7
517	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	UKJalNigam	03/2017	11/2019	03/2021	158	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(MARCH 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
7	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
8	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
9	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	198.68	325.18	126.5
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	12579.09	13812.3	1233.21
12	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
13	AIIMS BILASPUR	NBCC	04/2018	09/2021	1351	1471	120
14	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD	03/2019	09/2025	1577	1828	251

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
16	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	484.32	626.26	141.94

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
17	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	352.56	490.24	137.68
18	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
19	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
20	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3072	395
21	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
22	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
23	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
24	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
25	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
26	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
27	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
28	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
29	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
30	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
31	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	652.1	108.19
32	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1846.46	984.67
34	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	1236	628.94

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
35	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
36	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
37	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
38	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	15105.22	3466.67
39	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
40	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
41	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
42	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
43	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	408.46	516.12	107.66
44	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
45	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10997.7	398.72
46	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
47	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
48	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
49	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
50	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	445.89	675.73	229.84
51	EASTERN REGION STRENGTHENING SCHEME- XVIII	PGCIL	03/2017	07/2020	3500	3994	494
52	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
53	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
54	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
55	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
56	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	10566	5213
57	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15389.42	1022.84
58	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13140.91	608.47

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
59	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	9188.98	9842.02	653.04
60	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	947.89	299.56
61	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
62	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
63	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
64	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3550	2516.93
65	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
66	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
67	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
68	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
69	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
70	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
71	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
72	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5521.45	3127.98
73	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
74	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2910.84	2186.15
75	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
76	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	396	262.59
77	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83
78	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2432.5	370.2
79	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
80	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
81	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
82	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35
83	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
84	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	1967	165.99
85	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	315	130.94
86	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
87	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1043	657.8
88	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
89	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12264.15	7809.98
90	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
91	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	1180.19	4541.38	3361.19
92	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
93	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1070	745.27
94	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
95	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
96	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
97	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3377	1873.29
98	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1959.74	1130
99	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	1720	1416.02
100	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	2315	3911.65	1596.65
101	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
102	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	2005.25	1493.39

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
103	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
104	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
105	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
106	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	187.26	332	144.74
107	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
108	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
109	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
110	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
111	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
112	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
113	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
114	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	565	303.62
115	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	502.48	214.13
116	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
117	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
118	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
119	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2172.16	2051.46
120	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
121	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	800	486
122	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
123	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	1040	625.16
124	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
125	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
126	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
127	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	931.98	1121	189.02
128	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	600.3	435.89
129	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
130	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	742	172.37
131	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
132	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	369.55	116.59
133	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
134	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	559.95	361.27
135	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
136	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1205	681.48
137	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	527.37	375.53
138	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2042.51	244.51
139	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	480	266.99
140	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
141	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
142	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
143	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
144	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
145	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
146	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
147	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
148	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
149	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
150	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	525	282.91
151	AJMER-BANGURGRAM	NWR	04/2011	11/2019	213.39	375	161.61
152	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
153	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099	277
154	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	236.93	350.45	113.52
155	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
156	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
157	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1389.05	351.9
158	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	1868.89	320.23
159	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
160	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	872.65	228.27
161	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1500	524.38
162	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	395	148.92
163	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
164	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
165	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
166	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
167	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
168	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
169	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	929.86	251.32
170	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
171	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	783	205
172	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
173	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
174	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1147	286.57
175	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
176	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1656	499.06
177	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
178	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	NFR	02/1999	04/2010	380.6	1090.6	710
179	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	691.84	1017.91	326.07
180	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	859	234
181	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
182	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	890.76	339.25
183	KADUR CHIKMAGALUR SAKLIESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	998	353.22
184	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
185	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
186	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
187	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
188	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
189	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
190	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
191	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
192	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
193	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
194	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
195	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1536	776
196	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
197	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
198	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	449.39	329.66
199	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3524.81	1616.3
200	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
201	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
202	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	1825	641.75
203	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1536	593.05
204	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96
205	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
206	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2725	2011.52
207	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	22716.11	6500.11
208	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1400	472.99
209	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
210	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1246	246
211	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
212	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	12/2021	602.27	2144.78	1542.51
213	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25
214	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68
215	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
216	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
217	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
218	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
219	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2200	1750
220	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
221	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
222	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6911	4584.48
223	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
224	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4517.49	2245.99
225	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3000	873
226	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
227	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
228	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	2132.77	3037.95	905.18
229	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
230	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	2643.25	354.55
231	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
232	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
233	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	663.13	120.95
234	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
235	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59
236	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	5912.4	2408.71
237	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
238	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	346	226
239	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
241	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	520	240
242	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
243	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
244	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
245	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
246	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
247	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
248	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	MORTH	12/2010	01/2019	169.26	299	129.74
249	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	624.98	731.5	106.52
250	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
251	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
252	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	186.96	322.24	135.28
253	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653.29	207.4
254	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MORTH	04/2014	08/2017	279.7	398.52	118.82
255	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	MORTH	08/2014	11/2017	823.2	937.76	114.56
256	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	MORTH	08/2014	11/2017	600.87	720.97	120.1
257	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
258	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
259	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
260	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
261	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-	NHAI	03/2018	03/2021	1532.62	2499	966.38

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)						
262	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
263	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
264	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
265	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	1952.2	690.22
266	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
267	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
268	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	NHAI	02/2018	N.A.	1166.26	1296.93	130.67
269	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
270	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
271	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
272	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	NHAI	09/2016	N.A.	1239.82	1727.66	487.84
273	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
274	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2587.5	1199.16
275	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
276	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	NHAI	02/2016	03/2019	997.15	1115.95	118.8
277	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
278	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
279	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
280	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
281	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
282	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
283	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1827.15	744.15

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
285	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
286	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
287	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
288	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MORTH	03/2012	05/2012	207.03	389.45	182.42
289	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	MORTH	12/2011	02/2012	156.63	276	119.37
290	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
291	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
292	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19
293	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
294	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
295	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
296	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
297	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
298	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
299	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
300	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
301	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	730.97	199.84
302	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
303	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MORTH	11/2011	09/2015	954.43	1191.51	237.08
304	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	MORTH	11/2010	02/2011	470.2	630.36	160.16
305	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	268.08	390.73	122.65
306	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MORTH	11/2013	05/2017	497.05	881.05	384

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
307	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	MORTH	10/2013	03/2017	445.89	653.29	207.4
308	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
309	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
310	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
311	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
312	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	26405.14	30695.12	4289.98
313	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
314	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
315	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
316	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	23136	33406	10270
317	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4720.73	456.73
318	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
319	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	1,2320.00	1,7079.00	4759	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	1,1459.00	1,6580.00	5121	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	03/2022	198.68	325.18	126.5	36
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	459.49	307.06	84
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	349.28	186.52	84

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	12/2021	4773.00	5178.00	405	24
8	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	1,2579.09	1,3812.30	1233.21	22

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	12/2021	1219.21	2000.00	780.79	26

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14
11	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
12	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497.00	6025.00	1528	38

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

476

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	04/2021	543.91	652.10	108.19	14
14	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677.00	3072.00	395	14
15	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
16	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2021	4588.29	5245.96	657.67	33
17	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2021	3190.69	3375.90	185.21	37
18	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	5909.00	2994	110
19	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2021	352.56	490.24	137.68	48
20	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	1236.00	628.94	53
21	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321.00	3338.00	1017	15
22	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2021	861.79	1846.46	984.67	94
23	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678.00	1472.00	794	66

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
24	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	6700.00	1588.67	36
25	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	07/2022	1,0598.98	1,0997.70	398.72	20
26	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	9129.32	4374.9	63
27	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	3860.35	1368.77	126
28	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	05/2021	1,2532.44	1,3140.91	608.47	29

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

477

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	05/2021	3500.00	3994.00	494	10
30	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	1,2964.60	1,7304.00	4339.4	43
31	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	07/2022	3919.59	9897.59	5978	154
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
33	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2021	4824.12	5071.94	247.82	101
34	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	1,1130.19	1,4719.10	3588.91	108
35	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	5867.38	2888.9	117
36	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	03/2021	9188.98	9842.02	653.04	20
37	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	1,4366.58	1,5389.42	1022.84	40
38	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	06/2021	5353.00	1,0566.00	5213	107
39	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	2,1312.11	12619.1	141

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
40	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625.00	859.00	234	63
41	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2023	2288.00	4970.11	2682.11	21
42	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2025	644.78	998.00	353.22	96
43	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
44	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	1215.54	471.5	36

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

478

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	950.00	317.32	69
46	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2172.16	2051.46	105
47	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
48	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
49	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
50	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631.00	3887.48	256.48	24
51	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	810.02	108.41	64
52	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
53	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	1825.00	641.75	24
54	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600.00	701.81	101.81	25
55	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	1147.00	286.57	15
56	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	06/2021	578.00	783.00	205	15
57	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	1870.41	255.82	60
58	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	05/2021	678.54	929.86	251.32	26
59	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	477.31	182.31	37
60	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
61	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	1378.11	1057.45	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

479

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
62	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2021	1037.15	1389.05	351.9	9
63	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
65	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
66	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	04/2021	511.86	2005.25	1493.39	12
67	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	1720.00	1416.02	60
68	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	1959.74	1130	48
69	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	3377.00	1873.29	24
70	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	1539.28	427.29	34
71	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	1656.00	499.06	36
72	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.70	2643.25	354.55	36
73	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	927.94	223.63	15
74	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	3037.95	905.18	156
75	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4517.49	2245.99	24
76	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2022	495.44	2980.41	2484.97	216
77	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	1070.00	745.27	128
79	NEW MAYNAGURI TO JOGIGHOPA VIA	NFR	04/2000	12/2008	04/2021	1180.19	4541.38	3361.19	148

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

480

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	CHANGRABANDHA (NL), NEFR								
80	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	3791.66	868.53	204
81	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.20	2120.16	1074.96	180
82	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
83	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
84	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
85	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
86	TALCHER-BIMALAGARH(NL) (ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
87	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	2910.84	2186.15	73
88	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2023	2393.47	5521.45	3127.98	108
89	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	07/2021	477.88	751.55	273.67	112
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
91	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	5912.40	2408.71	24
92	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	1377.48	584.59	24
93	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	663.13	120.95	12
94	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
95	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287.00	893.45	606.45	114
96	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,2264.15	7809.98	153

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

481

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
97	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2021	495.74	734.01	238.27	102
98	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.20	1043.00	657.8	48
99	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60
100	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2024	2326.52	6911.00	4584.48	117
101	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	11/2021	410.08	860.41	450.33	33
102	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450.00	2200.00	1750	140
103	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500.00	2,7949.00	25449	241
104	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
105	AJMER-BANGURGRAM	NWR	04/2011	11/2019	03/2021	213.39	375.00	161.61	16
106	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
107	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2021	258.20	358.68	100.48	30
108	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548.00	819.01	271.01	36
109	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2024	1798.00	2042.51	244.51	60
110	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	742.00	172.37	24
111	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2021	314.00	800.00	486	24
112	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	1835.83	349.98	12
113	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	1247.64	665.51	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

482

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
114	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3524.81	1616.3	9
115	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	449.39	329.66	9
116	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	1268.32	682.39	34
117	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	950.00	681.13	198
118	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760.00	1536.00	776	27
119	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	1540.13	1211.99	24
120	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	1312.96	343.13	21
121	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
122	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	1400.00	472.99	39
123	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	2725.00	2011.52	21
124	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
125	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	2009.00	1060.96	21
126	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1536.00	593.05	39
127	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	1185.73	454.09	15
128	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33
129	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	890.76	339.25	31

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

483

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
130	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2021	624.98	731.50	106.52	56
131	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2021	531.13	730.97	199.84	37
132	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	1420.00	131.93	15
133	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105
134	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	04/2021	497.05	881.05	384	47
135	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2021	195.04	377.99	182.95	128
136	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	06/2021	193.69	327.92	134.23	128
137	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	1232.76	108.65	44
138	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	1191.51	237.08	73
139	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	03/2021	1928.22	2945.00	1016.78	71
140	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MoRTH	10/2013	03/2017	04/2021	445.89	653.29	207.4	49

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
141	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2021	1,5525.00	2,1940.00	6415	74

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
142	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2021	1,3334.00	2,4664.00	11330	71

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
143	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	1,0773.00	1,2787.00	2014	44

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

484

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
144	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	03/2023	2,3136.00	3,3406.00	10270	98
145	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	06/2024	2,6405.14	3,0695.12	4289.98	64

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
146	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.63	03/2021 04/2024	03/2021
	<u>Western Coal Fields Limited</u>						
2	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	226.81	03/2022 -	03/2021
	Total		677.56 -	677.56	327.44		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
3	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	-	09/2025 -	05/2024
	Total		1,828.00 -	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
4	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	2,109.70	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
5	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA [N16000315]	6/2017	249.26 -	249.26	130.48	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY [N16000308]	8/2017	315.00	315.00	206.17	12/2021 -	06/2021
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	1,951.62	09/2022 -	03/2022
	Total		6,709.26 -	6,693.26	4,397.97		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
8	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 546.36	546.36	477.69	11/2016 09/2021	05/2021
9	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	246.14	05/2020 05/2021	04/2021
10	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	148.70	06/2019 08/2021	05/2021

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) [N18000188]	3/2015	1,394.52 -	1,394.52	532.79	05/2017 09/2021	06/2021
	Total		2,511.17 -	2,535.24	1,405.32		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
12	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,204.21	03/2024 -	03/2023
	<u>North East Frontier Railway</u>						
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	2,144.78	824.96	12/2021 -	04/2021
	<u>North Western Railway</u>						
14	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	184.11	08/2022 -	06/2022
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	926.84	12/2026 -	12/2025
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
17	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022
	<u>South Central Railway</u>						
18	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	534.34	03/2020 03/2022	06/2021
	<u>Southern Railway</u>						
19	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	600.30	355.13	- 10/2021	09/2021
	<u>West Central Railway</u>						
20	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60	2,909.99	1,229.79	03/2021 03/2029	03/2023
	Total		12,149.68 -	21,496.53	7,468.03		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
21	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	3/2018	217.22	226.88	170.96	08/2018 09/2021	03/2021
22	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09 -	995.09	476.77	05/2016 08/2021	04/2021
	<u>National Highways Authority Of India</u>						
23	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]	11/2016	1,064.88 -	1,021.00	296.60	- 01/2022	07/2021

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
24	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	3/2018	1,532.62 -	2,499.00	1,582.36	03/2021 10/2021	04/2021
	Total		3,809.81 -	4,741.97	2,526.69		
	Grand Total		27,685.48	37,972.56	16,125.45		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	51.11	09/2021 -	09/2021
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	475.39 -	475.39	88.11	04/2021 -	04/2021
3	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71 -	389.71	140.62	11/2021 10/2022	10/2022
4	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]	1/2016	458.00 -	458.00	135.60	03/2020 12/2021	12/2021
5	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,216.90 -	1,216.90	122.19	10/2022 -	10/2022
6	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24 -	412.24	-	06/2021 -	06/2021
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT [N04000091]	4/2020	611.80 -	611.80	8.46	03/2023 -	03/2023
8	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]	1/2018	1,405.00 -	1,405.00	199.55	08/2022 -	08/2022
9	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD [N04000086]	5/2020	353.61 -	353.61	-	05/2022 -	05/2022
	Total		5,668.92 -	5,802.98	745.64		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
10	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.87	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
11	MAGADH EXPANSION OC(51 MTY) - [N06000015]	8/2008	6,964.33 6,964.33	706.40	706.20	07/2012 03/2025	03/2025
12	RECAST EPR AMRAPALI OC - [N06000103]	2/2012	4,983.58 4,983.58	4,983.58	245.85	03/2020 03/2024	03/2024
13	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	277.47	03/2023 -	03/2023
14	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
15	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]	11/2015	1,210.12 -	1,210.12	24.49	03/2022 03/2029	03/2029
16	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	10.11	03/2029 -	03/2029
17	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	.61	03/2027 -	03/2027
18	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	-	03/2025 -	03/2025
19	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	.03	03/2027 -	03/2027
20	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	98.11	03/2024 -	03/2024
21	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.39	03/2026 -	03/2026
22	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	163.16	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
23	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026
24	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029
25	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027
26	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029
27	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028
	<u>Neyveli Lignite Corporation</u>						
28	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	484.65	06/2015 03/2025	03/2025
29	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	11,452.38	11/2021 07/2022	07/2022
	<u>Northern Coal Fields Limited</u>						
30	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
31	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
32	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
33	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
	<u>South-Eastern Coal Fields Limited</u>						
34	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	8.28	03/2023 -	03/2023
35	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	1.09	03/2022 -	03/2022
37	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,931.04	03/2029 -	03/2029
38	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
39	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	182.99	03/2024 -	03/2024
40	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	276.19	03/2029 -	03/2029
41	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
42	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	28.26	03/2026 -	03/2026
43	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.95	03/2026 -	03/2026
44	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,630.04	03/2023 -	03/2023
45	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
46	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	85.82	03/2023 -	03/2023
47	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	211.41	03/2021 -	03/2021
48	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	99.77	03/2021 -	03/2021
49	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	.87	03/2026 -	03/2026
50	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
51	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	281.92	03/2025 -	03/2025
52	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	274.95	03/2021 -	03/2021
53	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	251.34	03/2021 -	03/2021
	Total		89,905.68 -	83,121.18	24,815.68		
	<u>FINANCE</u>						
	<u>Central Public Works Department</u>						
54	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	113.99	11/2021 -	11/2021
	Total		348.77 -	348.77	113.99		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
55	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	199.99	09/2023 -	09/2023
56	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
57	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	682.54	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	882.53		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
58	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	171.19	04/2018 12/2021	12/2021
59	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	.29	05/2022 -	05/2022
60	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
61	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]	6/2019	277.35 -	277.35	5.30	07/2022 -	07/2022
	Total		774.19 -	849.31	176.78		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
62	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
63	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
64	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	35.88	06/2022 -	06/2022
65	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
	Total		2,206.13 -	2,206.13	93.30		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
66	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	721.87	04/2021 12/2022	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
67	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	.92	04/2021 03/2023	03/2023
	Total		6,023.00 -	6,023.00	722.79		
	PETROLEUM						
	Bharat Petroleum Corporation Limited						
68	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	18.80	02/2017 08/2022	08/2022
69	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	106.83	06/2022 -	06/2022
70	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	772.75	12/2021 -	12/2021
71	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	377.64	03/2023 -	03/2023
72	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	212.84	08/2022 -	08/2022
73	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	77.84	03/2023 -	03/2023
74	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	321.21	12/2021 -	12/2021
	Gas Authority Of India Limited						
75	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,263.80	12/2020 12/2021	12/2021
76	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	831.40	12/2020 12/2021	12/2021
77	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	200.10	04/2022 -	04/2022
78	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	114.73	07/2022 -	07/2022
79	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	77.27	07/2022 -	07/2022
80	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,200.60	12/2021 -	12/2021
81	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,022.40	05/2023 -	05/2023
82	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	71.90	11/2022 -	11/2022
83	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	92.04	10/2022 -	10/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
84	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	245.60	07/2022 -	07/2022
85	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	109.54	10/2022 -	10/2022
86	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	142.34	10/2022 -	10/2022
87	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,607.20	12/2012 02/2022	02/2022
88	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,048.00	1,840.50	12/2020 12/2021	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
89	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	26,264.00	14,820.60	07/2020 07/2022	07/2022
90	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	189.70	11/2022 -	11/2022
91	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	117.00	08/2021 -	08/2021
92	220 KV GRID SUPPLY - [N16000407]	10/2020	303.40 -	303.40	199.11	03/2021 -	03/2021
93	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	-	11/2022 -	11/2022
94	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,244.50	68.76	02/2023 -	02/2023
95	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	14.63	03/2031 08/2029	08/2029
96	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	153.20	03/2029 08/2029	08/2029
97	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	91.57	09/2026 02/2027	02/2027
98	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	222.20	11/2021 -	11/2021
99	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	269.18	11/2020 06/2021	06/2021
100	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	875.03	06/2022 -	06/2022
101	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	147.24	12/2022 -	12/2022
102	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	75.31	06/2020 09/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
103	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	393.38	10/2017 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
104	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	286.33	02/2020 02/2022	02/2022
105	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	301.41	01/2021 03/2022	03/2022
106	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	95.40	10/2021 -	10/2021
107	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	318.04	03/2021 12/2021	12/2021
108	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	710.21	08/2020 04/2022	04/2022
109	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	487.25	02/2020 06/2021	06/2021
110	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,754.90	10/2021 -	10/2021
111	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	144.29	01/2021 06/2021	06/2021
112	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	77.30	- 05/2023	05/2023
113	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	430.93	08/2022 -	08/2022
114	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00 -	18,936.00	685.07	09/2024 -	09/2024
115	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00 -	1,398.00	80.68	12/2023 -	12/2023
116	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00 -	921.00	3.05	09/2023 -	09/2023
117	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	24.66	12/2022 -	12/2022
118	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	1.77	08/2022 -	08/2022
119	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	92.44	01/2024 -	01/2024
120	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	11.85	07/2022 -	07/2022
121	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	58.06	01/2023 -	01/2023
122	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	143.52	05/2023 -	05/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
123	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	-	08/2023 -	08/2023
124	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	8.95	07/2022 -	07/2022
125	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	101.64	12/2021 -	12/2021
126	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	179.69	10/2021 -	10/2021
127	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	431.31	12/2022 07/2023	07/2023
128	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	4.44	09/2022 03/2023	03/2023
129	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	44.73	06/2021 07/2022	07/2022
130	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	1,652.79	08/2021 -	08/2021
131	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	22.97	09/2021 06/2022	06/2022
132	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	865.95	04/2023 -	04/2023
133	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	13.16	07/2021 03/2022	03/2022
134	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	272.27	02/2020 10/2021	10/2021
135	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	34.40	10/2020 08/2022	08/2022
136	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	63.74	08/2020 11/2021	11/2021
137	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	89.71	02/2020 08/2021	08/2021
138	LPG BP PROJECT JODHPUR - [N16000318]	3/2018	229.80 -	229.80	81.43	- 05/2022	05/2022
139	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	134.82	03/2021 09/2021	09/2021
140	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	293.00	155.76	06/2020 09/2021	09/2021
141	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	247.72	04/2021 03/2021	03/2021
142	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	94.21	04/2020 10/2021	10/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
143	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	135.89	11/2021 -	11/2021
144	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	49.54	12/2019 03/2022	03/2022
145	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	93.23	02/2020 06/2021	06/2021
146	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,525.53	02/2022 -	02/2022
147	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	540.76	07/2018 05/2021	05/2021
148	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	502.00	421.03	08/2019 06/2021	06/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
149	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	2.09	06/2023 -	06/2023
	<u>Numaligarh Refinery Limited</u>						
150	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024
151	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
152	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,375.90	2,775.79	04/2018 05/2021	05/2021
153	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	87.19	08/2022 -	08/2022
154	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	637.29	12/2020 05/2021	05/2021
155	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,302.43	03/2022 -	03/2022
156	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	2,521.33	05/2021 -	05/2021
157	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	1,005.13	03/2022 05/2023	05/2023
158	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	1,595.82	05/2021 -	05/2021
159	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) [N16000297]	2/2017	4,006.83 -	3,596.00	3,507.79	05/2021 05/2021	05/2021
160	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	303.75	197.20	05/2020 05/2021	05/2021
161	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	827.75	03/2026 -	03/2026
162	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	25,090.00	11,190.15	06/2020 06/2022	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
163	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]	11/2015	650.82 -	624.35	446.72	03/2019 05/2021	05/2021
164	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	667.03	03/2023 03/2022	03/2022
	Total		2,47,405.50 -	2,48,295.65	72,366.94		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
165	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	9,897.59	8,866.70	09/2009 07/2022	07/2022
166	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	19,992.43	13,537.76	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
167	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,842.02	8,146.60	07/2019 03/2021	03/2021
168	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.54	660.06	09/2019 12/2024	12/2024
169	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	18,530.80	10/2011 07/2023	07/2023
170	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,389.42	11,672.15	06/2019 10/2022	10/2022
171	DEVIKOT SOLAR 150MW - [N18000281]	1/2020	798.24 -	798.24	31.64	09/2021 01/2022	01/2022
172	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	261.80	-	10/2021 -	10/2021
173	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71 -	1,522.71	203.13	09/2021 01/2022	01/2022
174	JETSAR SOLAR 160 MW - [N18000287]	12/2019	702.28 -	702.28	-	03/2021 -	03/2021
175	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	-	09/2021 -	09/2021
176	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	-	09/2021 -	09/2021
177	KAYAMKULAM SOLAR 70 MW - [N18000288]	9/2019	403.62 -	403.62	46.03	06/2021 10/2021	10/2021
178	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]	3/2020	1,782.00 -	1,782.00	69.21	09/2021 01/2022	01/2022
179	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	-	04/2021 -	04/2021
180	NOKHRA - [N18000282]	3/2020	1,722.14 -	1,722.14	103.85	09/2021 01/2022	01/2022
181	DEVIKOT SOLAR 90MW - [N18000280]	3/2020	501.29 -	501.29	49.76	09/2021 01/2022	01/2022
182	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,997.70	8,310.67	11/2020 07/2022	07/2022
	<u>Power Grid Corporation Of India Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
183	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,886.91	08/2013 08/2022	08/2022
184	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	652.14	01/2018 04/2021	04/2021
185	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	201.10	02/2019 06/2021	06/2021
186	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	1,677.06	02/2020 06/2021	06/2021
187	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	219.66	157.13	07/2019 04/2021	04/2021
188	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	4,060.04	04/2020 06/2021	06/2021
189	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	229.18	12/2019 06/2021	06/2021
190	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	11,505.07	11/2019 04/2021	04/2021
	<u>Satluj Jal Vidyut Nigam Limited</u>						
191	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	1,998.39	01/2024 -	01/2024
192	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	569.80	12/2021 -	12/2021
193	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	417.95	01/2026 -	01/2026
	<u>Thdc India Limited</u>						
194	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	495.34	09/2020 08/2022	08/2022
	Total		1,15,160.10 -	1,52,943.55	1,05,078.47		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
195	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023
196	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
197	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023
198	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>East Coast Railway</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
199	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	4/2005	810.78 -	1,928.07	864.71	06/2021 03/2025	03/2025
200	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	4/1994	2,923.13 -	3,791.66	1,493.80	03/2009 03/2026	03/2026
201	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	610.79	12/2018 03/2024	03/2024
202	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379	4/2015	2,361.74 -	2,361.74	432.17	03/2022 03/2026	03/2026
203	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	2,499.71	665.93	03/2022 03/2024	03/2024
204	JAGADALPUR-KORAPUT DOUBLING - [N22000376	4/2015	1,547.38 -	1,547.38	635.77	03/2022 03/2023	03/2023
205	BHADRAK - NERGUNDI 3RD LINE - [N22000316	3/2013	843.04 -	843.04	223.65	10/2020 03/2024	03/2024
	<u>North Central Railway</u>						
206	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495	3/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023
207	JHANSI BINA DOUBLING - [N22000496	9/2016	2,001.00 -	2,001.00	809.66	03/2021 -	03/2021
	<u>North East Frontier Railway</u>						
208	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	4/2010	906.46 -	4,083.02	263.68	03/2021 -	03/2021
	<u>North Eastern Railway</u>						
209	HATHUA-BHATNI (N L) (NER) - [220100319	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
210	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	3/2007	243.78 -	895.00	112.02	12/2021 -	12/2021
211	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42 -	1,295.42	929.79	03/2022 -	03/2022
	<u>Northern Railway</u>						
212	CHANDIGARH-BADDI - [N22000467	4/2007	328.14 -	1,540.13	242.09	03/2023 03/2025	03/2025
	<u>National High Speed Rail Corporation Limited</u>						
213	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463	12/2015	1,08,000.00 -	1,08,000.00	12,039.69	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
214	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394	3/2015	636.38 -	636.38	549.50	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
215	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021
216	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501	6/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023
217	DHASA-JETALSAR (GC) - [N22000141	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
218	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	705.50	12/2024 -	12/2024
219	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
	<u>South Western Railway</u>						
220	HUBLI- CHIKJAJUR - [N22000325]	3/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023
221	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021
222	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,870.41	1,341.15	03/2019 03/2024	03/2024
223	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	3/1996	644.78 -	998.00	463.45	03/2017 03/2025	03/2025
	<u>Southern Railway</u>						
224	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	4/2008	523.52 -	1,205.00	2.28	- 03/2024	03/2024
	<u>Western Railway</u>						
225	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	5,912.40	2,161.74	03/2022 03/2024	03/2024
226	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	411.62	126.05	03/2012 03/2023	03/2023
227	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	907.54	03/2022 03/2023	03/2023
228	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	186.59	- 03/2024	03/2024
229	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	890.76	745.11	03/2019 10/2021	10/2021
230	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	254.73	06/2020 03/2023	03/2023
231	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	653.86	03/2021 12/2022	12/2022
232	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,389.05	1,125.73	03/2021 12/2021	12/2021
233	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	1,378.11	540.09	03/2019 03/2023	03/2023
234	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	866.42	03/2022 03/2023	03/2023
235	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,959.74	1,799.00	03/2020 03/2024	03/2024
	Total		1,73,497.30 -	1,92,054.93	40,610.06		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
236	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301	3/2015	271.45 -	271.45	225.81	10/2015 03/2021	03/2021
237	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	295.96	10/2010 06/2021	06/2021
238	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229	12/2014	379.16 -	379.16	272.43	11/2017 06/2021	06/2021
239	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228	11/2017	188.80 -	188.80	78.69	05/2019 06/2021	06/2021
240	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	1/2018	418.03 -	418.03	279.86	08/2018 05/2021	05/2021
241	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	105.72	08/2018 03/2021	03/2021
242	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43 -	429.43	293.60	11/2017 04/2021	04/2021
243	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931	11/2016	290.15 -	290.15	214.00	05/2017 07/2021	07/2021
244	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929	9/2016	372.68 -	372.68	214.00	02/2017 06/2021	06/2021
245	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	3/2016	877.79 -	877.79	687.99	06/2019 04/2021	04/2021
246	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898	1/2016	809.16 -	809.16	573.85	07/2018 05/2021	05/2021
247	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896	1/2017	373.82 -	373.82	197.04	09/2019 06/2021	06/2021
248	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881	11/2017	184.62 -	184.62	117.94	02/2018 06/2021	06/2021
249	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	197.67	5.75	12/2022 -	12/2022
250	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	128.31	06/2021 -	06/2021
251	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	50.27	12/2022 -	12/2022
252	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177	10/2016	171.90 -	171.90	110.19	08/2020 07/2021	07/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
253	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	70.46	09/2021 -	09/2021
254	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	351.92	03/2018 06/2021	06/2021
255	BHOGAN KHURD TO KASHEDI - [N24001132	9/2017	743.21 743.00	743.21	193.08	06/2021 -	06/2021
256	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	539.22	12/2019 03/2021	03/2021
257	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	97.45	09/2017 05/2021	05/2021
258	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966	1/2016	348.95 -	348.95	200.57	08/2016 07/2021	07/2021
259	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240	3/2020	370.36 -	370.36	90.45	08/2022 -	08/2022
260	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226	12/2014	496.02 -	496.02	240.11	03/2015 06/2021	06/2021
261	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224	3/2017	423.79 -	423.79	273.27	01/2018 03/2021	03/2021
262	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222	3/2016	452.94 -	435.61	94.34	07/2016 06/2021	06/2021
263	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	1/2016	624.98 -	731.50	416.16	10/2016 06/2021	06/2021
264	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	1/2016	476.20 544.00	544.00	400.38	09/2016 06/2021	06/2021
265	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218	11/2015	335.32 -	335.32	269.15	06/2017 06/2021	06/2021
266	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	1/2016	497.14 -	572.66	270.56	08/2016 06/2021	06/2021
267	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021
268	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198	1/2019	264.50 -	264.50	85.70	03/2021 11/2021	11/2021
269	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	375.50	08/2017 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
270	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	957.54 -	957.54	756.69	02/2020 04/2021	04/2021
271	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	8/2010	195.04 -	377.99	325.42	10/2010 06/2021	06/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
272	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]	8/2020	301.06 -	301.06	-	04/2022 -	04/2022
273	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	4.21	05/2022 -	05/2022
274	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]	3/2020	247.76 -	247.76	2.60	01/2022 -	01/2022
275	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]	6/2020	347.36 -	347.36	-	01/2022 -	01/2022
276	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]	3/2019	402.94 -	402.94	.78	04/2022 -	04/2022
277	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
278	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
279	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	-	04/2022 -	04/2022
280	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	20.53	08/2022 -	08/2022
281	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]	3/2020	167.95 -	167.95	22.24	06/2022 -	06/2022
282	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]	6/2020	365.53 -	365.53	17.51	08/2022 -	08/2022
283	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]	3/2020	292.24 -	292.24	12.44	06/2022 -	06/2022
284	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 1B) - [N24001269]	3/2020	216.49 -	216.49	15.29	03/2022 -	03/2022
285	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]	3/2019	471.00 -	471.00	101.20	07/2022 -	07/2022
286	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]	3/2020	178.43 -	178.43	-	07/2022 -	07/2022
287	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]	7/2020	210.79 -	210.79	-	04/2022 -	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
288	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265	3/2020	154.51 -	154.51	-	07/2022 -	07/2022
289	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264	7/2020	228.39 -	228.39	-	04/2022 -	04/2022
290	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263	6/2020	277.50 -	277.50	-	01/2022 -	01/2022
291	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001262	7/2020	345.38 -	345.38	-	04/2023 -	04/2023
292	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001261	8/2020	311.00 -	311.00	-	04/2023 -	04/2023
293	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260	9/2020	257.15 -	257.15	5.29	04/2022 -	04/2022
294	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	9/2020	315.63 -	315.63	-	04/2022 -	04/2022
295	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
296	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257	8/2020	159.85 -	159.85	-	10/2022 -	10/2022
297	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	-	10/2022 -	10/2022
298	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	63.83	09/2026 -	09/2026
299	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	-	06/2022 -	06/2022
300	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	29.22	12/2023 -	12/2023
301	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	-	04/2023 -	04/2023
302	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	56.77	06/2022 -	06/2022
303	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284	3/2020	361.53 -	361.53	7.61	06/2022 -	06/2022
304	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283	3/2020	281.78 -	281.78	-	07/2022 -	07/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
305	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79 -	355.79	24.01	06/2022 -	06/2022
306	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]	3/2020	292.24 -	292.24	-	07/2022 -	07/2022
307	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97 -	320.97	13.88	06/2022 -	06/2022
308	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]	3/2020	216.49 -	216.49	-	07/2022 -	07/2022
309	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	-	07/2022 -	07/2022
310	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	4.72	10/2022 -	10/2022
311	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288]	8/2020	232.29 -	232.29	-	04/2022 -	04/2022
312	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]	4/2020	330.80 -	330.80	6.57	12/2021 -	12/2021
313	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]	3/2020	330.78 -	330.78	19.71	12/2021 -	12/2021
314	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]	8/2020	278.46 -	278.46	-	03/2022 -	03/2022
315	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	-	04/2022 -	04/2022
316	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]	3/2020	220.20 -	220.20	-	12/2022 -	12/2022
National Highways Authority Of India							
317	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 03/2021	03/2021
318	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]	3/2016	701.40 -	701.40	125.51	03/2019 03/2022	03/2022
319	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	642.54	05/2018 06/2021	06/2021
320	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	597.77	03/2020 05/2021	05/2021
321	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	594.57	05/2018 06/2021	06/2021
322	TWO / FOUR LANING OF RAEARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]	10/2020	724.60 -	724.60	-	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
323	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
	Total		43,243.44 -	44,039.21	13,213.02		
	<u>RURAL DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
324	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021
	Total		361.60 -	361.60	12.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
325	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,814.28	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,814.28		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
326	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	21,940.00	18,486.77	05/2015 07/2021	07/2021
327	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124	11/2015	2,907.00 -	2,907.00	254.56	06/2023 -	06/2023
	<u>Rastriya Ispat Nigam Limited</u>						
328	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	1,551.82	09/2018 04/2021	04/2021
	<u>Steel Authority Of India Limited (Sail)</u>						
329	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	536.50	10/2017 12/2021	12/2021
330	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	31.60	12/2023 -	12/2023
331	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	16.12	05/2023 -	05/2023
332	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	185.40	06/2019 05/2021	05/2021
	Total		22,331.15 -	28,746.15	21,062.77		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
333	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	61.94	03/2024 -	03/2024
334	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	18.27	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
335	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]	10/2016	422.00 -	422.00	69.02	03/2021 07/2021	07/2021
336	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022
	<u>Delhi Metro Rail Corporation</u>						
337	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS [N28000135]	7/2019	24,948.65 -	24,948.65	1,248.28	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
338	KANPUR METRO RAIL PROJECT - [N28000144]	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
339	AGRA METRO RAIL PROJECT - [N28000145]	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
340	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	5,696.05	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
341	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	126.50	02/2023 -	02/2023
342	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	117.53	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
343	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	3,320.23	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
344	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,365.77	231.97	06/2024 -	06/2024
	Total		1,32,861.21 -	1,32,861.21	10,911.79		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
345	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	55.02	07/2021 -	07/2021
346	I AND D AND STP AT CHAPPRA - [N30000028]	11/2018	236.15 -	236.15	28.53	12/2020 06/2021	06/2021
347	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
348	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	40.09	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
349	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	40.09	06/2022 -	06/2022
350	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	133.75	05/2021 -	05/2021
351	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]	5/2017	191.62 -	191.62	53.08	11/2020 03/2021	03/2021
352	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	152.78	05/2021 -	05/2021
353	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	90.77	04/2021 -	04/2021
	<u>Delhi Jal Board</u>						
354	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	160.36	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
355	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
356	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]	2/2014	274.76 -	274.76	201.30	12/2019 05/2021	05/2021
357	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
358	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
359	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
360	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
361	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
362	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
363	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGA PURI - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
	<u>Uttar Pradesh Jal Nigam</u>						
364	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	49.66	09/2021 -	09/2021
365	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	21.10	10/2021 -	10/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
366	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
367	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
368	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
369	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007	3/2018	904.00 -	904.00	136.55	09/2021 -	09/2021
370	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008	10/2017	213.62 -	261.12	-	03/2022 -	03/2022
371	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010	3/2018	967.23 -	967.23	54.21	09/2021 -	09/2021
372	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009	10/2016	370.40 -	430.49	376.22	08/2020 03/2021	03/2021
	<u>Uttarakhand Pey Jal Nigam</u>						
373	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004	3/2017	158.00 -	158.00	78.59	11/2019 03/2021	03/2021
	Total		10,787.11 -	10,905.87	1,672.10		
	Grand Total		8,60,275.28	9,17,896.35	2,94,292.58		

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2021)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,922.21	09/2010 09/2016	10/2022	145	73
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	74	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,158.00	12/2016 -	03/2023	75	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	23,648.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	59,216.21				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 -	303.80	115.88	04/2020 -	05/2021	13	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	417.23 -	441.33	291.75	09/2018 -	06/2021	33	-
7	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	-	02/2020 -	06/2021	16	-
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	203.76	09/2020 -	07/2021	10	-
9	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	249.79	10/2021 -	03/2022	5	-
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	323.90	03/2021 -	03/2022	12	-
11	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	303.07	02/2022 -	09/2022	7	-
12	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12	-
13	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	-	03/2022 -	03/2023	12	-
	Total		7,679.14 -	7,793.24	1,857.81				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	281.27	05/2014 -	07/2021	86	-
15	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	461.54	04/2015 -	03/2022	83	-
16	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	38.59	03/2017 -	03/2022	60	-
17	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	18.35	04/2018 -	06/2022	50	-
18	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	23.47	04/2014 -	04/2023	108	-
	<u>Central Coal Fields Limited</u>								
19	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	107.27	03/2011 -	03/2022	132	-
20	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	426.30	03/2016 -	03/2022	72	-
21	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	98.21	03/2014 -	03/2022	96	-
	<u>Eastern Coal Fields Limited</u>								
22	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	658.63	03/2018 -	03/2021	36	-
	<u>Mahanadi Coal Fields Limited</u>								
23	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	168.13	03/2012 -	03/2021	108	-
24	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108	-
25	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60	-
26	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36	-
27	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168	-
	<u>Neyveli Lignite Corporation</u>								
28	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	34.62	08/2022 -	09/2023	13	-
	<u>Northern Coal Fields Limited</u>								
29	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	622.66	03/2021 -	03/2022	12	-
30	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	152.16	03/2022 -	03/2023	12	-
	<u>Singareni Colliers Company Limited</u>								
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	193.00	03/2016 -	03/2021	60	-
32	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84	-
33	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	288.72	03/2015 -	03/2022	84	-
34	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	49.77	03/2015 -	03/2022	84	-
35	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	131.63	07/2016 -	03/2022	68	-
36	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	108.64	03/2019 -	03/2022	36	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
37	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	169.95	03/2019 -	03/2022	36	-
38	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	-
	<u>South-Eastern Coal Fields Limited</u>								
39	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	209.24	03/2014 -	03/2021	84	-
40	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	201.48	03/2015 03/2020	03/2022	84	24
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	6.50	03/2014 -	03/2022	96	-
42	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	121.28	03/2021 -	03/2022	12	-
43	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH	06/2010	11,816.40 -	11,816.40	4,268.97	03/2023 03/2016	03/2023	0	84
44	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	-
45	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	130.17	03/2020 -	03/2023	36	-
46	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	64.12	03/2021 -	03/2024	36	-
47	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.63	145.83	03/2022 -	03/2025	36	-
48	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	9.71	03/2023 -	03/2026	36	-
	<u>Western Coal Fields Limited</u>								
49	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	325.18	246.55	03/2019 -	03/2022	36	-
50	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	121.25	03/2023 -	03/2024	12	-
51	REVISED PR FOR AMALGAMATED INDER KAMPTTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	141.08	03/2021 -	03/2024	36	-
52	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	295.56	160.23	03/2019 -	03/2025	72	-
53	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	35.67	03/2022 -	03/2025	36	-
54	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 -	826.80	194.28	03/2020 -	03/2026	72	-
55	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	304.52	142.28	03/2019 -	03/2026	84	-
56	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	281.25	20.99	03/2022 -	03/2026	48	-
57	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA	11/2014	1,184.33 -	1,184.33	368.56	03/2020 -	03/2027	84	-
	Total		37,644.11 -	38,428.09	13,100.25				
	<u>FINANCE</u>								
	<u>Central Public Works Department</u>								

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
58	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD, TAMIL NADU	12/2015	209.00 -	208.96	205.40	10/2019 -	04/2021	18	-
	Total		209.00 -	208.96	205.40				
	<u>FERTILISERS</u>								
	<u>National Fertiliser Limited</u>								
59	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL, HARYANA	01/2018	215.92 -	215.92	167.49	11/2019 -	04/2021	17	-
60	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL, PUNJAB	01/2018	218.83 -	218.83	187.51	11/2019 -	04/2021	17	-
61	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL, PUNJAB	01/2018	239.81 -	239.81	186.72	11/2019 -	04/2021	17	-
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
62	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF, MAHARASHTRA	04/2018	426.72 -	426.72	325.19	04/2020 03/2021	05/2021	13	2
	Total		1,101.28 -	1,101.28	866.91				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (Sail)</u>								
63	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL	12/2018	263.36 -	263.36	213.22	09/2020 -	05/2021	8	-
	Total		263.36 -	263.36	213.22				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
64	PUNE POL STORAGE DEPOT - [N16000313]BPCL, MAHARASHTRA	08/2016	282.64 -	282.64	246.11	08/2020 -	03/2021	7	-
65	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL, MAHARASHTRA	04/2013	449.58 -	449.58	396.13	12/2019 03/2021	04/2021	16	1
66	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA	11/2014	4,588.29 -	5,245.96	4,977.00	08/2018 11/2019	05/2021	33	18
67	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA	02/2016	3,313.00 -	3,288.96	2,925.17	02/2020 03/2021	05/2021	15	2
68	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL, KARNATAKA	10/2018	206.26 -	206.26	129.96	03/2021 -	05/2021	2	-
69	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH	07/2017	580.20 -	580.20	151.16	02/2021 -	05/2021	3	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
70	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	725.00	06/2019 -	02/2022	32	-
	<u>Chennai Petroleum Corporation Limited</u>								
71	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13	-
	<u>Gas Authority Of India Limited</u>								
72	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,612.80	12/2020 -	05/2021	5	-
73	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	197.30	04/2018 -	06/2021	38	-
74	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	181.70	08/2020 05/2021	06/2021	10	1
75	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 -	217.92	86.30	04/2021 -	10/2021	6	-
76	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	40.10	02/2021 -	12/2021	10	-
	<u>Hindustan Petroleum Corporation Limited</u>								
77	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	92.33	07/2020 -	07/2021	12	-
78	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 -	3,072.00	2,201.31	06/2021 -	08/2022	14	-
	<u>Indian Oil Corporation Limited</u>								
79	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	146.57	01/2021 -	04/2021	3	-
80	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	157.94	01/2021 -	04/2021	3	-
81	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	254.90	04/2021 -	07/2021	3	-
82	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	3,027.90	1,933.53	03/2021 -	08/2021	5	-
83	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	205.98	10/2020 -	08/2021	10	-
84	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	156.30	01/2021 -	10/2021	9	-
85	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	146.91	08/2021 -	11/2021	3	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
86	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	6,025.00	3,636.76	12/2018 -	02/2022	38	-
87	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	3,338.00	2,888.48	12/2020 -	03/2022	15	-
88	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	689.83	10/2021 -	03/2022	5	-
89	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	92.80	04/2022 -	02/2023	10	-
90	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	76.47	04/2022 -	08/2023	16	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
91	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	466.87	03/2020 11/2020	06/2021	15	7
92	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,607.38	12/2019 04/2021	10/2021	22	6
	<u>Oil & Natural Gas Corporation Limited</u>								
93	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	1,846.46	1,550.87	05/2013 12/2020	03/2021	94	3
	<u>Oil India Limited</u>								
94	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	490.24	455.00	03/2017 01/2021	03/2021	48	2
95	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	187.00	10/2020 -	03/2021	5	-
96	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	457.91	12/2019 -	04/2021	16	-
97	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 638.60	652.10	136.05	02/2020 -	04/2021	14	-
98	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	222.21	144.80	08/2020 -	04/2021	8	-
	Total		36,093.69 -	41,484.23	29,595.73				
	<u>POWER</u>								
	<u>Central Public Works Department</u>								
99	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	240.96	11/2019 -	06/2021	19	-
	<u>Chenab Valley Power Projects [P] Limited</u>								
100	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,706.23	04/2020 -	07/2025	63	-
	<u>National Thermal Power Corporation</u>								
101	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	349.00	226.00	11/2020 -	04/2021	5	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
102	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 13,140.91	13,140.91	11,701.78	12/2018 02/2021	05/2021	29	3
103	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,839.26	07/2012 06/2020	06/2021	107	12
104	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	1,763.69	12/2018 -	07/2021	31	-
105	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	418.49	11/2018 -	07/2021	32	-
106	NGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,761.92	05/2018 -	12/2021	43	-
107	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,891.26	03/2013 12/2021	12/2022	117	12
108	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,112.00	4,295.79	03/2023 -	09/2024	18	-
	<u>Power Grid Corporation Of India Limited</u>								
109	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,634.56	10/2012 11/2020	03/2021	101	4
110	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	343.25	04/2018 03/2021	04/2021	36	1
111	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	2,868.53	07/2020 12/2020	05/2021	10	5
112	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	241.68	04/2016 12/2017	06/2021	62	42
113	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	89.76	03/2018 -	06/2021	39	-
114	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	2,605.89	12/2018 -	12/2021	36	-
115	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	9,129.32	2,056.36	12/2018 -	03/2024	63	-
	<u>Thdc India Limited</u>								
116	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,860.35	2,207.95	06/2013 -	12/2023	126	-
117	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	1,728.08	09/2023 -	08/2024	11	-
	Total		96,441.36 -	1,16,009.29	66,621.44				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Central Public Works Department</u>								
118	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	136.48	03/2020 -	05/2021	14	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
119	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	43.43	03/2020 -	12/2021	21	-
120	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
121	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>HII Infra Tech Services Limited</u>								
122	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	548.39	04/2020 -	07/2021	15	-
123	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	469.13	06/2020 -	07/2021	13	-
124	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	331.55	05/2021 -	07/2022	14	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
125	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	250.00	233.39	05/2017 -	03/2021	46	-
126	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	37	-
127	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	258.51	03/2019 -	03/2021	24	-
128	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	488.22	11/2013 -	05/2021	90	-
129	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	295.16	03/2019 -	06/2021	27	-
130	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	237.89	05/2018 -	12/2021	43	-
	Total		4,940.96 -	4,754.30	3,248.11				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
131	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24	-
132	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24	-
133	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12	-
134	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24	-
135	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
136	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24	-
137	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
138	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	36	-
139	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	316.04	03/2019 -	03/2021	24	-
	<u>East Central Railways</u>								
140	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	929.86	819.61	03/2019 -	05/2021	26	-
141	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	751.55	683.91	03/2012 -	07/2021	112	-
142	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	235.00	03/2019 -	03/2022	36	-
143	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	348.23	340.60	03/2021 -	03/2022	12	-
144	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	165.55	03/2021 -	06/2022	15	-
145	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,070.00	1,062.07	03/2012 -	11/2022	128	-
146	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	530.12	03/2020 -	03/2023	36	-
147	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	925.70	03/2020 -	03/2023	36	-
148	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	510.65	03/2020 -	03/2023	36	-
149	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,165.22	03/2020 -	03/2024	48	-
150	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	398.20	03/2021 -	03/2024	36	-
	<u>East Coast Railway</u>								
151	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	34	-
152	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	221.37	03/2020 03/2021	03/2022	24	12
153	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	902.85	03/2020 -	03/2023	36	-
154	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	64	-
	<u>Eastern Railways</u>								
155	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	28	-
156	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	663.13	520.48	03/2020 -	03/2021	12	-
157	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.94	02/2013 -	03/2024	133	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
158	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	906.05	03/2019 12/2009	03/2025	72	183
159	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	983.60	12/2010 -	03/2025	171	-
160	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	545.70	149.30	03/2006 -	03/2025	228	-
161	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	2,137.81	373.47	03/2022 -	03/2025	36	-
162	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	923.52 -	995.10	643.11	03/2016 -	03/2025	108	-
163	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.51 -	769.40	103.64	03/2017 -	03/2025	96	-
164	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 -	266.32	186.14	03/2016 -	03/2025	108	-
165	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	365.17 -	439.30	385.60	03/2017 -	03/2025	96	-
166	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
167	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER, MULTI STATE	04/2009	499.96 -	680.68	164.05	02/2012 -	03/2025	157	-
168	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE	04/2009	257.42 -	257.42	106.75	03/2014 -	03/2025	132	-
169	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
170	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]JRCON, CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42	-
171	GEVRA ROAD PENDRA ROAD - [N22000488]JRCON, CHHATISGARH	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21	-
172	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]JRCON, ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-
	<u>Metropolitan Rapid Transport Projects</u>								
173	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-
174	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
175	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	481.29	06/2013 -	12/2021	102	-
176	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216	-
	<u>North Central Railway</u>								
177	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
178	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 486.96	800.00	799.87	03/2019 -	03/2021	24	-
179	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,683.54	12/2008 -	04/2021	148	-
180	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,162.39	03/2021 -	05/2021	2	-
181	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	-
182	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,043.00	798.53	03/2019 -	03/2023	48	-
183	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	3,838.64	03/2014 -	03/2023	108	-
184	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,496.25	03/2022 -	03/2023	12	-
185	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	10,842.65	03/2011 -	12/2023	153	-
186	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	970.88	03/2019 -	03/2024	60	-
187	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	83.64	03/2019 -	03/2024	60	-
188	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,911.00	1,148.65	03/2015 -	12/2024	117	-
	<u>North Eastern Railway</u>								
189	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	476.60	04/2017 -	03/2021	47	-
190	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	80.76	12/2019 -	04/2021	16	-
191	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	44.84	04/2016 -	12/2021	68	-
192	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	506.99	01/2019 -	02/2022	37	-
193	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	238.15	01/2022 -	03/2022	2	-
194	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
195	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
196	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
	<u>North Western Railway</u>								
197	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	375.00	345.38	11/2019 -	03/2021	16	-
198	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	480.00	313.18	03/2020 -	06/2021	15	-
199	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	699.06	02/2019 -	11/2021	33	-
200	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	207.09	03/2020 -	04/2022	25	-
	<u>Northern Railway</u>								
201	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	114	-
202	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	63	-
203	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	27,949.00	23,132.28	11/2002 -	12/2022	241	-
204	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	-
205	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108	-
	<u>Rail India Technical And Economic Service</u>								
206	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15	-
	<u>Rail Vikas Nigam Ltd.</u>								
207	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	69	-
208	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	21	-
209	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	21	-
210	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,294.72	03/2020 -	12/2021	21	-
211	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	12	-
212	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	3	-
213	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24	-
214	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	-
215	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	39	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
216	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	-
217	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	-
218	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	-
219	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	887.48	03/2023 -	12/2024	21	-
220	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	108	-
221	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	108	-
222	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	3	-
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-
224	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	24	-
	<u>South Central Railway</u>								
225	MANMAD-PARBHANI-NANDED- SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	-
226	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	276	-
227	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	180	-
228	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	502.93	03/2010 -	03/2024	168	-
229	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	12	-
230	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	36	-
231	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,416.78	03/2021 -	03/2024	36	-
232	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	24	-
233	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	156	-
	<u>South East Central Railway</u>								
234	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
235	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34	-
236	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	9	-
237	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33	-
238	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24	-
239	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36	-
	<u>South Eastern Railway</u>								
240	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	302.95	12/2018 12/2018	06/2021	30	30
241	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	901.11	03/2020 03/2020	12/2021	21	21
242	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	748.34	03/2021 03/2021	12/2023	33	33
243	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
244	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
245	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	15	-
246	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	312.23	03/2016 -	12/2023	93	-
247	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	35.29	03/2016 -	12/2023	93	-
248	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-
249	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
250	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	304.83	12/2018 -	06/2025	78	-
	<u>Southern Railway</u>								
251	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,121.00	906.57	- 02/2021	04/2021	-	2
252	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	-
253	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-
254	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	-
255	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	697.29	03/2020 -	03/2025	60	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
256	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,597.41	02/2019 -	03/2025	73	-
257	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
258	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	243.01	03/2019 -	12/2027	105	-
	<u>West Central Railway</u>								
259	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,762.94	1,153.73	03/2020 -	03/2023	36	-
260	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	-
261	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	296.52	03/2022 -	03/2023	12	-
262	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	-
	Total		1,73,007.08 -	2,81,600.00	1,40,089.61				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
263	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	173.41	141.65	08/2018 -	03/2021	31	-
264	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	71	-
265	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO) - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	254.30	99.36	10/2020 -	03/2021	5	-
266	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	187.82	131.74	04/2018 -	03/2021	35	-
267	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	35	-
268	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	14	-
269	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	210.31	05/2019 -	03/2021	22	-
270	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	218.90	129.83	03/2020 -	03/2021	12	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
271	REHABILITATION AND UPGRADE OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	175.51	10/2019 -	03/2021	17	-
272	FOUR LANE WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	120.68	08/2020 -	03/2021	7	-
273	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47	-
274	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	218.70	103.81	11/2020 04/2020	04/2021	5	12
275	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	195.13	07/2018 03/2021	04/2021	33	1
276	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34	-
277	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	61.53	09/2018 -	04/2021	31	-
278	REHABILITATION AND UPGRADE OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	49	-
279	REHABILITATION AND UPGRADE OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.43	04/2020 -	04/2021	12	-
280	REHABILITATION AND UPGRADE TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	242.97	09/2019 11/2020	05/2021	20	6
281	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	170.57	54.53	11/2020 -	05/2021	6	-
282	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
283	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	172.63	09/2020 -	05/2021	8	-
284	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	-	3
285	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	439.63	01/2020 01/2021	06/2021	17	5
286	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	129.98	03/2018 -	06/2021	39	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
287	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	46.52	03/2018 -	06/2021	39	-
288	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	123.20	03/2017 -	06/2021	51	-
289	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	158.22	03/2018 -	06/2021	39	-
290	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	06/2021	40	3
291	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	06/2021	39	6
292	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37	-
293	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6	-
294	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	322.48	271.72	07/2020 -	08/2021	13	-
295	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	692.14	10/2019 -	08/2021	22	-
296	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	69.34	03/2018 -	09/2021	42	-
297	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	-
298	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	242.25	09/2020 -	12/2021	15	-
299	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	12/2021	28	-
300	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24	-
301	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	-	11/2020 -	08/2022	21	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
302	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	213.97	25.03	08/2019 -	11/2022	39	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
303	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	149.44	04/2017 03/2018	03/2021	47	36
304	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	201.60	01/2016 -	04/2021	63	-
305	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	387.00	298.08	08/2016 -	05/2021	57	-
306	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	339.55	282.82	08/2016 -	05/2021	57	-
307	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	340.00	238.26	08/2016 -	05/2021	57	-
308	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	457.77	161.37	10/2018 -	10/2021	36	-
309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL, NAGALAND	03/2018	215.12 -	215.12	100.90	09/2018 -	11/2021	38	-
310	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	407.30	100.07	06/2018 -	12/2021	42	-
311	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	398.06	145.21	06/2018 -	12/2021	42	-
312	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	315.03	88.48	09/2018 -	12/2021	39	-
313	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	240.64	102.94	09/2018 -	12/2021	39	-
314	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	60.55	09/2018 -	12/2021	39	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
315	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	-
316	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	102.00	09/2018 -	05/2022	44	-
317	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57 -	339.57	141.44	09/2018 -	07/2022	46	-
318	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL, NAGALAND	03/2018	285.68 -	285.68	77.86	09/2018 -	09/2022	48	-
319	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL, NAGALAND	03/2018	272.89 -	272.89	44.52	09/2018 -	10/2022	49	-
320	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL, NAGALAND	03/2018	500.09 336.49	336.49	79.44	09/2018 -	11/2022	50	-
321	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL, NAGALAND	03/2018	323.98 -	323.98	42.55	09/2018 -	11/2022	50	-
322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL, MIZORAM	04/2017	519.09 -	519.09	65.01	09/2019 -	04/2023	43	-
323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL, MIZORAM	04/2017	473.18 -	473.18	47.39	09/2019 -	04/2023	43	-
324	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL, MIZORAM	04/2017	537.82 -	537.82	58.49	09/2019 -	04/2023	43	-
325	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL, MIZORAM	04/2017	642.96 -	642.96	33.18	09/2019 -	06/2023	45	-
326	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL, MIZORAM	04/2017	518.53 -	518.53	72.44	09/2019 -	06/2023	45	-
327	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL, MIZORAM	04/2017	640.07 -	640.07	18.08	09/2019 -	07/2023	46	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
328	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	59.92	09/2019 -	09/2023	48	-
329	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	50.49	09/2019 -	04/2024	55	-
	<u>National Highways Authority Of India</u>								
330	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,559.00	03/2013 -	03/2021	96	-
331	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	03/2021	71	-
332	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	974.60	11/2018 07/2019	03/2021	28	20
333	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	421.01	08/2018 -	03/2021	31	-
334	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	522.80	06/2018 10/2020	03/2021	33	5
335	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	555.68	08/2019 -	03/2021	19	-
336	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	70.85	03/2019 -	03/2021	24	-
337	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,288.54	08/2013 -	05/2021	93	-
338	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-
339	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	44	-
340	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	373.68	05/2018 04/2019	06/2021	37	26
341	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15	-
342	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	-
343	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15	-
344	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	54.22	05/2013 -	08/2021	99	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
345	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	194.57	- 02/2021	08/2021	-	6
346	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	-
347	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	363.86	03/2020 -	09/2021	18	-
348	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15	-
349	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	307.08	07/2019 06/2021	12/2021	29	6
350	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	318.30	07/2019 06/2021	12/2021	29	6
351	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	336.58	03/2019 01/2021	12/2021	33	11
352	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	848.45	222.06	03/2020 -	12/2021	21	-
353	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	537.28	12/2019 -	12/2021	24	-
354	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	8.56	04/2014 -	01/2022	93	-
355	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54	-
356	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	150.06	- 08/2021	02/2022	-	6
357	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,868.67	08/2013 -	03/2022	103	-
358	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	209.18	03/2019 12/2021	03/2022	36	3
359	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	333.22	03/2020 -	04/2022	25	-
360	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	349.24	05/2020 -	05/2022	24	-
361	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	462.14	08/2017 -	07/2022	59	-
362	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	566.14	09/2017 -	07/2022	58	-
363	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105	-

Costing Rs. 150 Crore and above

(March 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		60,072.54 -	61,459.60	34,695.27				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
364	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	431.16	-	06/2021 -	11/2021	5	-
	<u>Central Public Works Department</u>								
365	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	133.09	03/2018 -	06/2021	39	-
	<u>Department Of Telecommunication</u>								
366	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	16,594.00	07/2015 -	06/2021	71	-
	Total		14,013.36 -	25,343.36	16,727.09				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
367	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	8,706.79	12/2018 -	08/2022	44	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
368	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	17,021.86	02/2019 03/2021	06/2024	64	39
	<u>Central Public Works Department</u>								
369	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	106.16	04/2019 06/2021	12/2021	32	6
370	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19	-
371	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41	-
	<u>Chennai Metro Rail Ltd</u>								
372	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	3,770.00	3,088.12	03/2018 -	03/2021	36	-
	<u>Delhi Metro Rail Corporation</u>								
373	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,838.90	03/2016 -	09/2021	66	-
374	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	511.60	12/2020 -	09/2021	9	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
375	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 09/2022	03/2023	98	6

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		1,05,003.47	1,21,498.25	86,422.21				
	<u>WATER RESOURCES</u>								
	<u>Brahmaputra Board</u>								
376	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57	233.57	173.71	12/2019	12/2021	24	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
377	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77	225.77	271.22	03/2020	03/2021	12	-
378	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93	184.93	163.36	04/2020	06/2021	14	-
379	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19	305.19	-	08/2021	12/2021	4	-
	<u>Delhi Jal Board</u>								
380	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07	515.07	314.33	01/2021	06/2021	5	-
381	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79	211.79	64.03	12/2021	12/2022	12	-
382	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11	239.11	129.67	02/2022	12/2022	10	-
	<u>Hindustan Steelwork Construction Limited</u>								
383	IRRIGATION WORK OF BAGMATI - [N12000108]HSCCL,BIHAR	10/2005	956.00	721.37	712.37	03/2015	03/2021	72	-
	<u>Kolkata Metropolitan Development Authority</u>								
384	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32	272.32	214.52	04/2020	03/2021	11	-
385	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022	06/2022	4	-
386	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022	10/2022	8	-
	<u>Polavaram Project Authority</u>								
387	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	17,025.01	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								
388	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31	161.31	91.38	11/2019	03/2021	16	-
389	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45	460.45	216.89	12/2020	05/2021	5	-
390	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021	06/2022	11	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		14,573.10 -	59,673.08	19,376.49				
	<u>DEFENCE PRODUCTION</u>								
	<u>Central Public Works Department</u>								
391	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA	12/2016	246.31 -	246.31	123.83	02/2020 -	06/2021	16	-
	Total		246.31 -	246.31	123.83				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
392	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD, RAJASTHAN	12/2016	549.31 -	559.47	458.38	07/2019 -	03/2021	20	-
393	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD, ANDHRA PRADESH	02/2019	186.00 199.00	205.00	130.63	09/2020 -	03/2021	6	-
394	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD, PUNJAB	08/2016	294.00 -	350.69	274.98	04/2019 -	04/2021	24	-
395	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	-
396	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD, UTTAR PRADESH	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15	-
397	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD, MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	-
398	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52	-
399	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD, PUNJAB	01/2018	430.00 -	387.83	194.72	05/2020 -	02/2022	21	-
400	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD, ODISHA	01/2019	790.79 -	790.79	149.00	03/2022 -	06/2022	3	-
401	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD, KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	-
402	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD, PUNJAB	10/2019	348.24 -	348.24	15.55	05/2022 -	08/2022	3	-
403	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD, KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	-
404	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD, BIHAR	09/2018	375.00 375.00	375.00	48.46	09/2020 -	11/2022	26	-

Costing Rs. 150 Crore and above

(March 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
405	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD, ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	-
	Total		6,229.82 -	6,276.31	1,822.25				
	<u>HOME AFFAIRS</u>								
406	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	26	-
	Total		1,219.21 -	2,000.00	906.04				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
407	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	70	-
408	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	58	-
409	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	12/2021	60	-
	Total		527.83 -	538.27	460.04				
	<u>CULTURE DEVELOPMENT</u>								
410	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	148.33	09/2017 -	03/2021	42	-
	Total		151.33 -	151.33	148.33				
	<u>DPIIT</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
411	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC, MULTI STATE	09/2011	12,579.09 -	13,812.30	8,715.07	09/2019 01/2014	07/2021	22	90
	<u>India International Convention And Expo Centre</u>								
412	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC, DELHI	11/2017	4,773.00 -	5,178.00	2,432.15	12/2019 -	12/2021	24	-
	Total		17,352.09 -	18,990.30	11,147.22				
	Grand Total		6,43,889.04	8,68,167.56	4,86,843.46				

List of projects original without Date of Commissioning

Costing Rs. 150 Crore and above						(March 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1	<u>COAL</u> <u>Singareni Colliers Company Limited</u> SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA Total	11/2016	272.73 - 272.73	272.73 - 272.73	153.75 - 153.75	- - -	03/2022	-	2/6 - 2/6
2	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u> HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	268.84 -	244.88 -	- -	03/2021	-	0/0
3	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	190.34 -	143.04 -	- -	06/2021	-	0/0
4	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	601.02 -	382.25 -	- -	06/2021	-	0/0
5	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	582.99 -	470.24 -	- -	06/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL Total	04/2018	651.99 - 2,261.40	651.99 - 2,295.18	490.55 - 1,730.96	- - -	06/2021	-	0/0 - 0/0
7	<u>RAILWAYS</u> <u>East Central Railways</u> SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 -	735.20 -	380.48 -	- -	03/2021	-	0/0
8	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 -	3,550.00 -	3,528.48 -	- -	03/2022	-	0/0
9	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39 -	1,483.14 -	1,207.34 -	- -	03/2022	-	0/0
10	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	2,066.78 -	1,551.38 -	- -	03/2023	-	0/0
11	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	1,625.87 -	767.07 -	- -	03/2023	-	0/0
12	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56 -	1,858.75 -	386.36 -	- -	03/2023	-	0/0
13	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	1,605.17 -	1,605.17 -	52.72 -	- -	03/2023	-	0/0

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14	1,470.50	1,085.63	-	03/2023	-	0/0
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87	614.45	340.21	-	12/2023	-	0/0
16	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20	2,995.01	2.04	-	03/2024	-	0/0
17	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
18	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00	519.33	278.52	-	03/2025	-	0/0
<u>Eastern Railways</u>									
19	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35	502.48	427.64	-	03/2021	-	0/0
20	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80	495.10	284.21	-	03/2022	-	0/0
21	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64	272.20	241.02	-	03/2022	-	0/0
22	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93	310.70	360.96	-	03/2024	-	0/0
23	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00	1,261.34	-	-	03/2025	-	0/0
24	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	260.10	11.43	-	03/2025	-	0/0
25	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	71.43	-	03/2025	-	0/0
26	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	250.55	20.11	-	03/2025	-	0/0
27	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17	527.54	1.76	-	03/2025	-	0/0
28	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47	298.22	52.09	-	03/2025	-	0/0
29	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96	336.96	70.20	-	03/2025	-	0/0
30	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
<u>Metropolitan Rapid Transport Projects</u>									
31	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
<u>North East Frontier Railway</u>									

Costing Rs. 150 Crore and above (March 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
32	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE <u>North Eastern Railway</u>	04/2010	241.52 -	373.87	287.09	- -	12/2021	-	0/0
33	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH <u>Northern Railway</u>	04/2016	602.50 -	714.34	63.70	- -	12/2023	-	0/0
34	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	791.39	572.99	- -	03/2023	-	0/0
35	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
36	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	127.91	- -	09/2023	-	0/0
37	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	359.00	111.51	- -	03/2024	-	0/0
38	QADIAN-BEAS - [N22000295]NR,PUNJAB <u>South Eastern Railway</u>	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
39	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL <u>South Western Railway</u>	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
40	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,967.00	71.56	- -	12/2023	-	0/0
41	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	558.00	-	- -	12/2023	-	0/0
42	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	296.10	.01	- -	12/2023	-	0/0
43	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	- -	12/2023	-	0/0
44	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
45	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	- -	12/2023	-	0/0
46	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	-	0/0
47	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE <u>Southern Railway</u>	04/2007	2,062.30 -	2,432.50	1,127.71	- -	03/2025	-	2/2
48	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	457.08	439.49	- -	12/2021	-	0/0
49	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	559.95	319.22	- -	03/2024	-	0/0
50	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	582.83	239.11	- -	12/2025	-	0/0
	Total		22,329.80 -	40,870.62	14,787.11				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								

Costing Rs.		150 Crore and above				(March 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
51	<u>Ministry Of Road Transport And Highways (State Pwds)</u> REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	291.05	200.71	- -	03/2021	-	0/0
52	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	178.13	139.26	- -	03/2021	-	0/0
53	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	105.65	- -	09/2021	-	0/0
54	<u>National Highways And Infrastructure Development Corporation Ltd.</u> WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	119.35	- -	09/2021	-	2/4
55	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	81.01	- -	04/2022	-	0/4
56	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	65.25	- -	04/2022	-	0/4
57	<u>National Highways Authority Of India</u> 4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	1,005.08	-	- -	03/2021	-	0/0
58	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	-	0/0
59	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	353.42	- -	03/2021	-	0/0
60	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021	-	0/0
61	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	203.77	- -	03/2021	-	0/0
62	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	1,261.05	299.11	- -	03/2021	-	0/0
63	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	621.00	591.21	- -	04/2021	-	2/3

Costing Rs. 150 Crore and above (March 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
64	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11	806.11	189.70	-	04/2021	-	0/0
65	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10	1,244.10	1,590.00	-	05/2021	-	0/0
66	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74	478.74	127.42	-	05/2021	-	0/0
67	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96	1,008.96	930.39	-	06/2021	-	0/0
68	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65	686.65	227.63	-	06/2021	-	0/0
69	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51	417.51	127.61	-	06/2021	-	0/0
70	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86	668.86	276.59	-	06/2021	-	0/0
71	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65	686.65	261.74	-	06/2021	-	0/0
72	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00	1,522.00	304.40	-	06/2021	-	0/0
73	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00	999.00	102.70	-	06/2021	-	0/0
74	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88	503.88	25.40	-	06/2021	-	0/0
75	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43	314.43	86.83	-	06/2021	-	0/0
76	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05	2,043.00	1,327.65	-	06/2021	-	0/0
77	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00	479.00	456.80	-	07/2021	-	0/0

Costing Rs. 150 Crore and above (March 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
78	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	921.02	- -	07/2021	-	3/4
79	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0
80	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
81	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	193.26	- -	07/2021	-	0/0
82	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	584.17	- -	07/2021	-	0/0
83	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	931.21	268.17	- -	07/2021	-	0/0
84	SIX LANING AND STREGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	213.17	- -	07/2021	-	0/0
85	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	75.68	- -	07/2021	-	0/0
86	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	224.81	- -	08/2021	-	3/4
87	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	440.92	- -	08/2021	-	0/1
88	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0
89	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1
90	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	-	0/0

Costing Rs. 150 Crore and above (March 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
91	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	243.30	- -	08/2021	-	0/0
92	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
93	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,401.00	- -	09/2021	-	0/0
94	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
95	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
96	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	-	0/0
97	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
98	FOUR LANING OF MADURAI-CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	310.06	- -	12/2021	-	0/0
99	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	263.60	- -	12/2021	-	0/3
100	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	-	0/0
101	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	425.85	- -	02/2022	-	1/4
102	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	213.52	- -	03/2022	-	0/1
103	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	332.04	- -	03/2022	-	0/0

Costing Rs. 150 Crore and above (March 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
104	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH Total	12/2017	656.98 - 46,675.69 -	840.00 48,016.12	76.17 23,978.47	- -	11/2022	-	0/4 13/41
	<u>URBAN DEVELOPMENT</u> <u>National Building Construcion Corporation Ltd</u>								
105	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI Total	07/2016	2,694.00 - 2,694.00 -	2,694.00 2,694.00	679.91 679.91	- -	12/2022	-	0/9 0/9
	Grand Total		74,233.62	94,148.65	41,330.20				17/58

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 -	-
	Total		438.28 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Neyveli Lignite Corporation</u>				
4	TALABIRA II AND III OCP - [N06000189]NLC, ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
7	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Western Coal Fields Limited</u>				
10	SINGHORI OC MINE - [N06000130]WCL, MAHARASHTRA	06/2015	205.49 -	03/2020 -	03/2020
11	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020
	Total		17,152.93 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
12	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO, TAMIL NADU	09/2017	166.62 163.17	06/2019 06/2021	12/2020
13	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO, ODISHA	12/2015	355.00 -	11/2020 -	02/2021

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	UTKAL D AND E COAL BLOCK - [N1000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		1,055.62 -		
	<u>STEEL</u>				
	<u>Rastriya Ispat Nigam Limited</u>				
15	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 12/2020	12/2020
	Total		2,858.00 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
16	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	01/2021
	<u>Hindustan Petroleum Corporation Limited</u>				
17	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
18	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	Total		6,768.00 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
19	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
20	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	02/2017 06/2020	01/2021
21	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 01/2021	01/2021
22	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 15,105.22	01/2018 10/2020	02/2021
23	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
24	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-
25	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
26	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-
27	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
28	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>North East Electric Power Corporation</u>				
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	12/2009 02/2021	02/2021
	<u>Power Grid Corporation Of India Limited</u>				
30	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 516.12	01/2019 09/2020	04/2020
31	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 09/2020	05/2020
32	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 09/2020	07/2020
33	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 11/2020	09/2020
34	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	06/2019 11/2020	09/2020
35	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62 902.49	10/2017 05/2021	01/2021
36	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 675.73	02/2019 02/2021	02/2021
37	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	06/2014 -	-
38	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
39	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL, MULTI STATE	01/2015	203.28 -	07/2017 -	-
40	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
41	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL, MULTI STATE	03/2017	283.72 -	11/2019 -	-
42	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	-
43	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
	Total		81,024.79 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
44	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL, DELHI	08/2016	1,554.00 -	09/2019 -	-
	Total		1,554.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
45	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
46	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
47	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
48	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
49	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
50	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
51	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021
	Total		1,910.90 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
52	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	03/2020
53	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
54	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 12/2020	12/2020
55	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-
56	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
57	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
58	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
59	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
60	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
61	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
62	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	-
63	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
64	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
65	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
66	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
67	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
68	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
69	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
70	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
71	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
72	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
73	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
74	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
75	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-
	<u>Eastern Railways</u>				
76	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				
77	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
78	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
79	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
80	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
81	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
82	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
	<u>North East Frontier Railway</u>				
83	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
84	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-
85	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-
87	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-
88	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
89	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
90	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	-
91	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
92	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
93	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
94	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
95	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
96	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
97	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
98	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021
99	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
100	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	-
101	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
102	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
103	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
104	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
105	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
106	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
107	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
	<u>Railway Electrification</u>				
108	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
109	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
110	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00 -	- -	-
111	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	761.37 -	- -	-
112	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH	04/2013	829.00 -	- -	-
113	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
114	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	-
115	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR, CHHATISGARH	04/2008	872.00 -	12/2019 -	-
	<u>South Eastern Railway</u>				
116	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
117	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
118	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>Southern Railway</u>				
119	OMALUR-METTURDAM- DOUBLING WITH ELCTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU	10/2013	187.26 -	04/2014 03/2021	12/2020
120	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	1,566.00 -	- -	-
121	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	227.40 -	- -	-
122	ATTIPPATTU PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	151.84 -	02/2019 -	-
123	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-
124	KUMBALAM-TURAVUR - [N22000191]SR, KERALA	04/2011	252.96 -	- -	-
125	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 -	- -	-
126	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	- -	-
127	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR, KERALA	02/2015	1,431.90 -	- -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
128	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
129	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
130	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
131	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 02/2021	02/2021
132	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
133	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
134	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
135	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
136	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
137	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		81,111.17 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
138	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
139	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 -	05/2019
140	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 -	06/2019
141	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020
142	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 05/2021	08/2019
143	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020
144	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 05/2020	05/2020

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
145	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	06/2020
146	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
147	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020
148	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
149	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020
150	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020
151	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020
152	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2020	12/2020
153	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020
154	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020
155	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	01/2021
156	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 04/2021	01/2021
157	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021
158	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021
159	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
160	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021
161	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	02/2021
162	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	08/2018 06/2021	02/2021

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
163	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	02/2021
164	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
165	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
166	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
167	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
168	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
169	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
170	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
171	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
172	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
173	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
174	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
175	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
176	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
177	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
178	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
179	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
180	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
181	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
182	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
183	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
184	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
185	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
186	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
187	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 12/2020	-
188	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 12/2020	-
189	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 12/2020	-
190	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
191	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
192	REHABILITATION AND UPGADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
193	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
194	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
195	REHABILITATION AND UPGADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
196	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
197	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
198	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
199	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
200	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
201	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
202	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
203	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
205	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
206	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
207	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 390.73	05/2017 -	-
208	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
209	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
210	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
213	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
214	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
215	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
216	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
217	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
218	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
219	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
220	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
221	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
222	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
223	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
224	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
225	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
228	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
229	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
231	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
233	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
234	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
235	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
236	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-
237	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
238	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
239	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
240	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
241	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
242	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
243	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
244	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
245	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
246	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
247	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
248	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
249	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
250	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
251	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
252	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
253	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-
254	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
255	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
256	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
257	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
259	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH, WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
260	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH, PUNJAB	03/2018	173.24 -	06/2020 -	-
261	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH, PUNJAB	03/2018	293.10 -	08/2020 -	-
262	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH, HARYANA	01/2017	276.01 -	03/2019 -	-
263	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH, ODISHA	03/2016	165.06 -	12/2016 -	-
264	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH, ODISHA	08/2016	287.70 -	02/2017 -	-
265	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH, ODISHA	09/2016	295.67 -	02/2017 -	-
266	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH, ODISHA	12/2016	223.50 -	08/2018 -	-
267	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH, ODISHA	12/2016	206.88 -	04/2018 -	-
268	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH, ODISHA	03/2018	214.23 -	08/2018 -	-
269	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH, ODISHA	03/2018	199.16 -	08/2018 -	-
270	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH, GUJARAT	12/2017	867.97 -	11/2018 -	-
271	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH, GUJARAT	03/2018	464.07 -	11/2018 -	-
272	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH, GUJARAT	10/2018	400.76 -	05/2019 -	-
273	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH, GUJARAT	08/2017	962.43 -	03/2018 -	-
274	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH, PUNJAB	03/2018	293.64 -	08/2020 -	-
275	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH, ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
276	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH, ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-
277	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH, ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
278	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	-
279	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
280	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
281	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-
282	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 -	-
283	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 -	-
284	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 -	-
285	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	01/2018 -	-
286	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
287	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
288	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
289	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAN-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
290	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
291	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
292	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
293	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
294	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
295	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
296	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
297	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
298	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
299	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
300	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
301	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
302	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
303	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
304	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-
305	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
306	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
307	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
308	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
309	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
310	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
311	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
312	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
313	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
314	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
315	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
316	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
317	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
318	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
319	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
320	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
321	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
322	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
323	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
324	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
325	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
326	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
327	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
328	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
329	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
330	SHAHUPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
331	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
332	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
333	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
334	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
335	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
336	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
337	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
338	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
339	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
340	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
341	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
342	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
343	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
344	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
345	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
346	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
347	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
348	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
349	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
350	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
351	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
352	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
353	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
354	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
355	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
356	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
357	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
358	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
359	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
360	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
361	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
362	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
363	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
364	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
365	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
366	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
367	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
368	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
369	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
370	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
371	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
372	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
373	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
374	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
375	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
376	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
377	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
378	OSMANNAGAR TO KUNDRAI - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
379	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
380	KUNDRAI TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
381	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
382	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
383	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
384	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
385	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
386	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
387	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
388	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
389	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
390	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
391	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
392	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
393	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
394	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
395	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
396	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
397	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
398	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
399	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
400	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
401	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
402	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
403	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
404	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
405	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
406	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
407	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
408	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
409	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
410	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
411	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
412	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
413	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
414	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
415	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
416	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
417	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
418	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
419	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
420	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
421	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-
422	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
423	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
424	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
425	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
426	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
427	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
428	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
429	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
430	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
431	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
432	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
433	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
434	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
435	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
436	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
437	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
438	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-
439	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
440	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
441	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-
442	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
443	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
444	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-
445	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
446	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
447	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
448	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
449	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
450	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
451	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
452	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
453	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
454	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
455	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
456	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
457	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
458	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
459	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
460	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
461	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
462	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 09/2020	-
463	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2020	-
464	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
465	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
466	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
467	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-
468	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
469	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-
470	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
471	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ - [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-
472	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-
473	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
474	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-
475	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
476	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
477	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
478	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
479	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
480	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
481	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
482	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
483	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
484	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
485	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
486	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	02/2021
487	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	09/2018
488	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
489	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2020
490	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	12/2020
491	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
492	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
493	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
494	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
495	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
496	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
497	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
498	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
499	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
500	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
501	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
502	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
503	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
504	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-
505	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
506	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
507	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
508	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
509	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
510	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
511	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
512	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
513	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
514	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
515	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
516	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
517	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
518	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
519	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
520	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
521	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
522	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWAY TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
523	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
524	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
525	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
526	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
527	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
528	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
529	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
530	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
531	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
532	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
533	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
534	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
535	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
536	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
537	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
538	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
539	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
540	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
<u>National Highways Authority Of India</u>					
541	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	10/2019
542	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020
543	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
544	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
545	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
546	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
547	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
548	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
549	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
550	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
551	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
552	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
553	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
554	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
555	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020
556	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
557	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
558	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020
559	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENMORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
560	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
561	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020
562	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
563	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
564	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020
565	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020
566	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020
567	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
568	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020
569	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020
570	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
571	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
572	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021
573	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
574	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	01/2021
575	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	01/2021
576	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
577	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021
578	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	02/2021
579	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	02/2021
580	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021
581	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	02/2021
582	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	02/2021
583	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
584	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
585	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
586	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
587	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
588	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
589	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
590	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
591	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
592	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
593	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
594	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
595	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
596	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
597	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
598	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
599	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
600	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
601	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
602	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
603	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
604	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
605	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
606	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
607	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
608	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
609	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
610	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
611	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
612	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
613	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
614	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
615	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
616	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
617	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
618	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
619	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
620	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
621	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	-
622	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
623	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
624	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
625	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
626	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	-
627	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
628	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	-
629	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
630	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	-
631	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	-
632	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	-
633	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
634	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
635	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
636	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
637	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-
638	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
639	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
640	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
641	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
642	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
643	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
644	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
645	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
646	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
647	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
648	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
649	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
650	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
651	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
652	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-
653	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
654	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
655	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
656	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
657	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
658	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-
659	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	-
660	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
661	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
662	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
663	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
664	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
665	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
666	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
667	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
668	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
669	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
670	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
671	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
672	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
673	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-
674	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
675	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
676	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
677	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
678	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
679	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
680	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
681	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
682	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
683	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
684	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
685	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
686	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
687	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
688	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
689	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
690	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
691	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 486.00	- -	-
692	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
693	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
694	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
695	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
696	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
697	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
698	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-
699	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
700	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
701	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-
702	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-
703	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
704	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
705	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
706	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
707	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
708	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
709	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
710	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
711	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
712	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	-
713	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
714	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
715	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
716	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
717	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
718	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
719	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
720	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
721	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
722	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
723	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
724	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
725	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
726	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
727	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
728	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
729	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
730	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
731	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
732	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
733	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
734	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
735	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
736	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
737	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
738	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
739	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
740	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
741	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
742	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
743	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
744	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
745	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
746	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
747	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
748	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-

Costing Rs. 150 Crore and above				(March 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
749	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
750	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
751	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
752	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
753	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
754	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
755	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
756	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
757	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
758	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
759	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
760	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
761	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
762	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
763	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
764	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
765	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
766	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
767	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
768	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
769	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
770	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
771	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
772	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
773	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
774	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
775	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
776	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
777	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
778	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
779	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
780	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
781	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- 02/2020	-
782	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
783	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
784	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
785	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- 01/2020	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
786	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- 06/2020	-
787	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- 02/2020	-
788	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
789	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
790	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
791	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
792	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
793	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
794	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
795	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
796	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
797	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
798	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
	Total		3,87,145.88 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
799	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 -	11/2020
800	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
801	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
802	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	-

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
803	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	11/2020 -	-
804	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO - [N28000149]CPWD, CHHATISGARH	05/2019	299.97 -	09/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
805	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
806	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
807	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
808	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-
	<u>National Building Construcion Corporation Ltd</u>				
809	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI	06/2012	4,264.00 -	11/2019 -	-
	Total		41,941.60 -		
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
810	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 -	09/2020 -	-
811	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR	04/2015	268.63 -	01/2021 -	-
	<u>Delhi Jal Board</u>				
812	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB, DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Uttar Pradesh Jal Nigam</u>				
813	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam, UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
	<u>Uttarakhand Pey Jal Nigam</u>				
814	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam, UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
	Total		1,420.85 -		
	<u>COMMERCE</u>				
	<u>National Building Construcion Corporation Ltd</u>				
815	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC, DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		

Costing Rs. 150 Crore and above					(March 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
816	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
817	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
818	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
819	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
820	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				
821	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
822	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	<u>Rail India Technical And Economic Service</u>				
823	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		2,641.45 -		
	Grand Total		6,27,326.11		

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	03/2023	38.63	75
	Total		27,271.00 -	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	441.33	09/2018 -	06/2021	5.78	33
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	09/2021 -	09/2021	38.72	0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	03/2021 -	03/2022	7.88	12
	Total		1,905.50 -	2,153.66				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
7	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	08/2019 -	-	93.35	0
	<u>Neyveli Lignite Corporation</u>							
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	07/2022	.00	8
	<u>Singareni Colliers Company Limited</u>							
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2022	114.60	84
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2022	11.42	36
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2022	5.85	84

Costing Rs. 150 Crore and above						(March 2021)		
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>Western Coal Fields Limited</u>							
13	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	03/2022 -	03/2025	.00	36
14	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 -	325.18	03/2019 -	03/2022	63.67	36
15	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
16	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98	0
	Total		22,289.42 -	25,496.41				
	<u>DPIIT</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>							
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	12/2021	8.49	24
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	09/2025 -	09/2025	15.92	0
	<u>Hospital Services Consultancy Corporation Ltd</u>							
20	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	03/2021	16.33	37
21	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	- -	06/2021	21.58	0
22	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20	26
23	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64	8
24	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	01/2021	.02	0
25	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29	46
26	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13	24
27	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
28	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	11/2013 -	05/2021	20.55	90
29	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR [N21000011	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71	18
	<u>National Building Construcion Corporation Ltd</u>							
30	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	09/2021 -	09/2021	8.88	0
	Total		5,589.39 -	6,287.30				
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	10/2019 -	12/2021	64.04	26
	Total		1,219.21 -	2,000.00				
	<u>HUMAN RESOURCE DEVELOPMENT</u>							
32	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	02/2019	186.00 199.00	205.00	09/2020 -	-	10.22	6
33	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102	08/2016	294.00 -	350.69	04/2019 -	04/2021	19.28	24
34	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	10/2021	.57	52
35	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	559.47	07/2019 -	-	1.85	20
	<u>Rail India Technical And Economic Service</u>							
36	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	09/2014 -	-	29.31	0
	Total		2,009.81 -	2,240.41				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
37	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2021	14.33	33
	<u>Hindustan Petroleum Corporation Limited</u>							
38	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	06/2021 -	08/2022	14.76	14

Costing Rs. 150 Crore and above

(March 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Indian Oil Corporation Limited</u>							
39	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	08/2019 -	06/2021	18.68	22
40	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	03/2021 -	08/2021	66.09	5
41	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	03/2022	43.82	15
42	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2022	33.98	38
	<u>Oil India Limited</u>							
43	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	03/2017 -	03/2021	39.05	48
44	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	02/2020 -	04/2021	19.89	14
	Total		17,225.76 -	22,353.20				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							
45	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95	0
46	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 - 4,238.00	4,552.00	10/2017 -	-	7.41	0
47	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	9,842.02	07/2019 -	03/2021	7.11	20
48	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	-	12.95	0
49	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	01/2021	24.87	47
50	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	-	7.55	0
51	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	06/2019 -	10/2022	7.12	40
	<u>Power Grid Corporation Of India Limited</u>							
52	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	-	27.92	0
53	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	-	31.17	0
54	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 - 3,500.00	3,994.00	07/2020 -	05/2021	14.11	10
	<u>Satluj Jal Vidyut Nigam Limited</u>							
55	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	12/2021 -	12/2021	46.20	0

Costing Rs. 150 Crore and above

(March 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Thdc India Limited</u>							
56	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	06/2013 -	12/2023	54.94	126
	Total		68,118.60 -	77,351.20				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
57	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	315.00	03/2019 -	-	71.14	12
58	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	03/2022 -	03/2023	.89	12
59	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2023	73.73	24
60	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94	0
61	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04	0
62	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2023	.00	-12
63	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	03/2021 -	03/2023	98.88	24
64	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28	0
	<u>Container Corporation Of India</u>							
65	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	-	.21	0
66	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	03/2018 -	03/2021	25.65	36
	<u>East Central Railways</u>							
67	HAJIPUR-RAMDHALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	480.00	- -	-	125.34	0
68	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	-	3.33	0
69	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	- -	03/2025	36.67	0
70	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	07/2014 -	-	64.60	0
71	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26	0
72	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	- -	12/2023	277.26	0
73	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	726.31	- -	-	301.68	0
74	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	- -	03/2021	126.22	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
75	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	03/2012 -	07/2021	57.27	112
76	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2023	49.45	36
77	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	03/2019 -	05/2021	37.04	26
78	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	-	376.78	0
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,070.00	03/2012 -	11/2022	229.50	128
80	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	06/2022	62.06	15
81	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2024	63.37	36
82	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,470.50	- -	03/2023	295.15	0
83	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	03/2022	350.27	0
84	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	- -	03/2023	253.52	0
85	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	- -	03/2023	391.01	0
86	HAJIPUR-SUGALI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	- -	03/2023	290.95	0
87	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15	0
88	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,550.00	- -	03/2022	243.64	0
	<u>East Coast Railway</u>							
89	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2024	15.45	64
90	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07	36
91	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	12/2021	38.43	34
	<u>Eastern Railways</u>							
92	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19	0
93	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	03/2022	6.48	0
94	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25	0
95	MONIGRAM- NIMITTA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
96	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
97	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	03/2017 -	03/2025	20.30	96
98	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
99	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	495.10	- -	03/2022	181.63	0
100	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	- -	03/2021	74.26	0
101	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46	0
102	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
103	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	565.00	- -	05/2019	116.16	0
104	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	03/2020 -	03/2021	22.31	12
105	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
106	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
107	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
108	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30	0
109	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
110	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
111	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
<u>Indian Railway Construction Company Limited</u>								
112	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489]	04/2013	3,055.00 -	3,055.15	09/2018 -	03/2022	.00	42
113	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2023	117.23	21
<u>Metropolitan Rapid Transport Projects</u>								
114	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP [N22000028]	04/2006	495.74 -	734.01	06/2013 -	12/2021	48.06	102

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
115	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2022	501.57	216
116	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37	0
117	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>							
118	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	346.00	12/2008 -	-	188.33	0
119	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	03/2020 -	-	1.69	0
120	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
121	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	- -	-	7.86	0
122	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	- -	12/2021	54.80	0
123	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	- -	-	71.62	0
124	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
125	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	03/2019 -	-	106.51	0
126	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	03/2020 -	03/2022	30.26	24
127	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	800.00	03/2019 -	03/2021	154.78	24
128	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	1,040.00	03/2020 -	-	150.70	0
129	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086	09/2006	385.20 -	1,043.00	03/2019 -	03/2023	170.77	48
130	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499	02/1999	380.60 -	1,090.60	04/2010 -	-	186.55	0
131	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	- -	-	128.39	0
132	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	1,873.21	03/2021 -	05/2021	115.07	2
133	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	04/2016	602.27 -	2,144.78	12/2021 -	04/2021	256.12	-8
134	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2024	302.54	60

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
135	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15	12
136	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	03/2021 -	03/2021	350.44	0
137	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266	04/2000	1,180.19 -	4,541.38	12/2008 -	04/2021	284.80	148
138	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,521.45	03/2014 -	03/2023	130.69	108
139	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 -	6,911.00	03/2015 -	12/2024	197.05	117
140	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	8,600.00	12/2015 -	-	542.04	0
141	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	12,264.15	03/2011 -	12/2023	175.34	153
	<u>North Eastern Railway</u>							
142	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10	0
143	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00 -	213.35	04/2016 -	12/2021	.16	68
144	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	- -	-	60.34	0
145	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	477.31	01/2019 -	02/2022	61.80	37
146	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136	03/2013	643.00 -	644.00	- -	-	.16	0
147	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50 -	714.34	- -	12/2023	18.56	0
148	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13	0
149	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	1,409.09	- -	-	358.99	0
150	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91	0
	<u>North Western Railway</u>							
151	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	350.45	10/2018 -	-	47.91	0
152	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	375.00	11/2019 -	03/2021	75.73	16
153	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137	04/2012	246.08 -	395.00	12/2019 -	02/2021	60.52	14
154	PUSHKAR-MERTA - [N22000151	04/2013	323.00 -	432.22	- -	-	33.81	0
155	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152	04/2013	420.18 -	480.00	03/2020 -	06/2021	14.24	15

Costing Rs. 150 Crore and above

(March 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
156	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	02/2019 -	02/2020	116.86	12
157	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	03/2020 -	04/2022	16.97	25
158	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	11/2021	109.82	33
159	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	- -	-	33.70	0
160	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64	0
161	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	- -	-	104.65	0
	<u>Northern Railway</u>							
162	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68	0
163	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
164	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
165	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	- -	03/2024	310.24	0
166	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	03/2016 -	06/2021	37.44	63
167	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	06/2021	211.31	114
168	UNCHAHAR-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	- -	03/2023	2.93	0
169	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	07/2012 -	03/2024	388.89	140
170	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>							
171	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	03/2009 03/2009	-	196.83	0
172	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
173	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	03/2021	35.42	0
174	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15	69
175	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98	33
176	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2022	51.02	39
177	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	12/2021 -	12/2021	53.75	0
178	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	03/2019 -	06/2022	62.89	39

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
179	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	12/2020 -	12/2022	54.24	24
180	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	12/2020 -	12/2021	23.55	12
181	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	-	55.57	0
182	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68	3
183	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	03/2020 -	12/2021	111.91	21
184	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
185	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	03/2020 -	12/2021	281.93	21
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
187	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04	-3
188	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
189	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58	24
190	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
192	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22	108
193	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62	-12
194	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08	3
	<u>Railway Electrification</u>							
195	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77	0
	<u>South Central Railway</u>							
196	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	03/2022 -	12/2022	275.34	9
197	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	03/2020 -	06/2021	31.75	15
198	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
199	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
200	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2024	102.85	180
201	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	03/2021 -	03/2024	15.49	36
202	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86	0
203	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	03/2014 -	03/2027	42.44	156
204	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
205	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>							
206	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
207	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	12/2019 -	-	40.65	0
208	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	02/2019 -	12/2021	116.46	34
209	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	12/2021 -	12/2023	.07	24
210	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	- -	-	268.37	0
211	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	04/2020 -	04/2021	291.76	12
212	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	03/2021 -	12/2023	8.23	33
213	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	03/2023 -	12/2023	84.69	9
	<u>South Eastern Railway</u>							
214	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44	0
215	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323]	04/2012	148.77 -	377.00	12/2016 -	08/2020	153.41	44
216	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89	0
217	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
218	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76	0
219	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
220	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14	0
221	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	296.10	- -	12/2023	.03	0
222	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	03/2020 -	06/2021	35.47	15
223	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	998.00	03/2017 -	03/2025	54.78	96
224	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	03/2020 -	06/2021	33.31	15
225	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	03/2020 -	03/2023	43.14	36
226	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2024	15.84	60
227	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	- -	12/2023	9.22	0
228	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	- -	03/2025	17.95	0
229	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	- -	12/2024	68.97	0
	<u>Southern Railway</u>							
230	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	- -	-	45.43	0
231	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	332.00	04/2014 -	12/2020	77.29	80
232	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	- -	-	46.09	0
233	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	12/2021	69.20	0
234	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	02/2019 -	-	247.32	0
235	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	- -	03/2024	181.84	0
236	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	600.30	- -	09/2021	265.12	0
237	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	09/2021	253.33	198
238	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,121.00	- -	04/2021	20.28	0
239	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05	0
240	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	- -	03/2024	130.17	0
241	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,246.00	- -	-	24.60	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
242	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78	0
243	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	03/2020 -	06/2022	102.11	27
244	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	1,720.00	03/2020 -	03/2025	465.83	60
245	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	2,172.16	03/2019 -	12/2027	1,699.64	105
246	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	- -	-	79.80	0
247	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,910.84	02/2019 -	03/2025	301.67	73
	<u>West Central Railway</u>							
248	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
249	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>							
250	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	03/2011 -	-	72.42	0
	Total		1,89,462.73 -	3,76,579.30				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
251	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00	157.30	06/2018 -	-	.00	0
252	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	173.41	08/2018 -	-	4.33	31
253	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	-	.00	0
254	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	-	.00	0
255	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	-	.00	0
256	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	-	.00	0
257	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	-	.00	0
258	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	-	.00	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
259	MANGRUPHIR TO MAHAN - [N24001087	03/2018	222.13 222.00	222.13	11/2019 -	-	.00	0
260	KUNDRAI TO WAZAR - [N24001077	01/2018	225.25 225.00	225.25	12/2019 -	-	.00	0
261	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	08/2018 -	-	4.45	31
262	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	-	.00	0
263	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	-	.08	0
264	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	-	.00	0
265	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	03/2021	.00	14
266	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00	244.04	03/2019 -	-	.00	0
267	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	- -	-	58.68	0
268	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	-	.00	0
269	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00	264.41	03/2019 -	-	.00	0
270	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84	0
271	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	-	.00	0
272	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	-	3.72	0
273	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00	294.12	07/2018 -	-	-1.01	0
274	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31	0
275	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	-	.00	0
276	MALEGAON TO RISOD - [N24001089	02/2018	303.24 303.00	303.24	12/2019 -	-	.00	0
277	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	08/2016 -	-	14.02	0
278	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	-	72.36	0
279	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.00	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
280	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	06/2021	69.30	128
281	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	-	.00	0
282	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	-	.00	0
283	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	-	.00	0
284	OSMANNAGAR TO KUNDRAL - [N24001075	09/2017	344.25 344.00	344.25	08/2020 -	-	.00	0
285	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	-	.00	0
286	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	0
287	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21	0
288	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	12/2015 -	-	6.81	0
289	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67	0
290	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	-	.00	0
291	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42	0
292	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2021	93.80	128
293	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00	381.08	05/2020 -	-	.00	0
294	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	05/2012 -	-	88.11	0
295	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	-	.00	0
296	CHIKLI TO TAKARKHED - [N24001083	03/2018	393.10 393.00	393.10	12/2019 -	-	.00	0
297	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00	404.33	05/2020 -	-	.00	0
298	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	-	.00	0
299	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00	0
300	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	06/2020 -	-	.00	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
301	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06	0
302	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	03/2018	504.19 504.00	504.19	11/2018 -	01/2021	.00	26
303	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	09/2016 -	06/2021	14.24	57
304	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00	548.03	06/2019 -	-	.00	0
305	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	02/2011 -	-	34.06	0
306	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	03/2017 -	-	46.51	0
307	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	03/2017 -	04/2021	46.51	49
308	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00	743.21	06/2021 -	06/2021	.00	0
309	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	05/2017 -	04/2021	77.26	47
310	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	- -	12/2020	1.75	0
311	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00	983.14	12/2019 -	-	.00	0
312	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	03/2011 -	12/2020	58.98	117
313	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00	995.09	05/2016 -	04/2021	.00	59
314	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	09/2015 -	10/2021	24.84	73
315	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00	0
316	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	-	.00	0
317	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	-	.00	0
318	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	- -	-	2.93	0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
319	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]	01/2017	194.66 -	252.05	04/2017 -	-	29.48	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
320	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	04/2017 -	-	27.16	0
321	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	04/2017 -	-	29.48	0
322	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	04/2017 -	-	29.48	0
323	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	08/2016 -	05/2021	3.73	57
324	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30	0
325	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902	10/2017	818.00 -	887.68	- -	-	8.52	0
	<u>National Highways Authority Of India</u>							
326	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99	133
327	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	02/2021	10.58	154
328	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	-	64.62	0
329	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	- -	-	.99	0
330	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	- -	-	8.35	0
331	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501	08/2015	322.09 -	322.09	04/2018 -	12/2020	.00	32
332	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 -	336.60	08/2018 -	-	3.98	0
333	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	04/2009 -	-	70.23	0
334	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82	111
335	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437	10/2015	361.15 -	363.93	- -	-	.77	0
336	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56 -	392.00	- -	03/2021	7.53	0
337	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	11/2008 -	-	159.95	0
338	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	- -	10/2020	10.68	0
339	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
340	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	520.00	02/2009 -	-	85.71	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
341	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	- -	-	8.26	0
342	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	11/2013 -	01/2021	15.53	86
343	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	08/2015	516.13 -	649.27	04/2018 -	-	25.80	0
344	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	07/2009 -	-	234.27	0
345	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	- -	-	6.11	0
346	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	690.17	05/2018 -	06/2021	16.34	37
347	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469	03/2015	794.30 -	691.38	- -	05/2020	-12.96	0
348	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	07/2018 -	-	19.25	0
349	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	730.97	05/2018 -	06/2021	37.63	37
350	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	-	9.38	0
351	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	- -	12/2021	.00	0
352	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	12/2017 -	-	66.88	0
353	CONSTRUCTION OF PARTIALLY ACESSED CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	09/2021	.23	18
354	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	- -	07/2021	.48	0
355	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	- -	-	25.68	0
356	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	- -	10/2021	1.37	0
357	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	- -	11/2022	27.86	0
358	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	- -	-	305.58	0
359	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	04/2020 -	07/2021	3.95	15

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
360	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	- -	07/2021	46.72	0
361	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	- -	01/2020	11.33	0
362	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	-	31.88	0
363	MEERUT-BULANDSHAHAH - [N24000539	01/2016	683.24 -	987.94	- -	-	44.60	0
364	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521	08/2015	854.80 -	1,038.56	- -	-	21.50	0
365	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	-	5.56	0
366	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	-	3.40	0
367	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	- -	01/2022	5.32	0
368	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06	44
369	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	08/2019 -	-	16.55	0
370	4-LANNING OF MAHULIA BAHARAGORA-JHWB BORDER SECTION - [N24000548	02/2016	997.15 -	1,115.95	03/2019 -	-	11.91	7
371	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 -	1,145.31	- -	03/2021	4.10	0
372	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	-	5.70	0
373	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	-	41.54	0
374	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507	12/2015	1,167.45 -	1,182.94	- -	-	1.33	0
375	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	-	13.97	0
376	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	- -	-	29.35	0
377	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	05/2021	9.67	44

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
378	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44	0
379	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12	0
380	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,296.93	- -	08/2021	11.20	0
381	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	0
382	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
383	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	06/2021	10.24	15
384	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
385	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	- -	01/2021	37.71	0
386	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
387	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
388	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	09/2016	1,239.82 -	1,727.66	- -	01/2021	39.35	0
389	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,827.15	06/2018 -	-	68.71	0
390	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09	0
391	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	- -	07/2021	54.69	0
392	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	06/2020 -	02/2021	1.78	8
393	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	-	4.99	0
394	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 -	2,280.00	- -	-	94.94	0
395	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 -	2,360.65	- -	-	41.78	0

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
396	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28	0
397	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	-	18.50	0
398	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50	0
399	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05	1
400	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
401	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	09/2019 -	-	86.37	0
402	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	03/2021	52.73	71
403	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	11/2011 -	-	167.82	0
404	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84	0
405	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		1,06,285.04 -	1,30,764.64				
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
406	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00	431.16	06/2021 -	11/2021	.00	5
	<u>Department Of Telecommunication</u>							
407	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2021	84.97	71
	Total		13,765.16 -	25,095.16				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
408	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	12/2018 -	08/2022	18.69	44
	<u>Chennai Metro Rail Ltd</u>							
409	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53	0
	<u>Mumbai Metro Rail Corporation Ltd</u>							

Costing Rs. 150 Crore and above					(March 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
410	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	01/2015 -	03/2023	44.39	98
	<u>National Building Construcion Corporation Ltd</u>							
411	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,720.73	11/2019 -	-	10.71	0
	Total		52,773.00 -	69,971.73				
	<u>WATER RESOURCES</u>							
	<u>Uttar Pradesh Jal Nigam</u>							
412	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	12/2021 -	12/2021	.97	0
413	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	06/2022 -	06/2022	1.31	0
	Total		913.57 -	924.74				
	Grand Total		5,26,180.28	8,00,707.05				

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost
Annexure - XIII

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 5,677.00	6,840.00	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 - 12,320.00	17,079.00	12/2016 -	03/2023	38.63
	Total		27,271.00 .00 29,456.00	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 - 417.23	441.33	09/2018 -	06/2021	5.78
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	09/2021	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2022	7.88
	Total		1,905.50 .00 1,905.50	2,153.66			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
7	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	-	93.35
	<u>Neyveli Lignite Corporation</u>						
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	07/2022	.00
	<u>Singareni Colliers Company Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2022	11.42
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 - 447.06	473.22	03/2015 -	03/2022	5.85
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2022	114.60
	<u>Western Coal Fields Limited</u>						
13	BHANEGAON OC - [N06000121]	02/2015	187.94 - 187.94	409.68	03/2023 -	03/2023	117.98
14	ADASA UG TO OC - [N06000133]	08/2015	288.90 - 288.90	333.43	03/2023 -	03/2024	15.41
15	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 - 198.68	325.18	03/2019 -	03/2022	63.67
16	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 - 289.29	289.30	03/2022 -	03/2025	.00
	Total		22,289.42 .00 22,289.42	25,496.41			
	<u>DPIIT</u>						
	<u>Delhi Mumbai Industrial Corridor</u>						
17	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>						
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	12/2021	8.49
	Total		17,352.09 .00 17,352.09	18,990.30			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 - 1,577.00	1,828.00	09/2025 -	09/2025	15.92

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Hospital Services Consultancy Corporation Ltd</u>						
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 - 414.11	499.23	11/2013 -	05/2021	20.55
21	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 - 204.44	250.00	05/2017 -	03/2021	22.29
22	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
23	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 - 168.90	191.20	05/2017 -	07/2019	13.20
24	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 - 505.58	585.00	03/2018 -	09/2019	15.71
25	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 - 152.95	177.92	02/2018 -	03/2021	16.33
26	CNCI KOLKATA WEST BENGAL - [N21000015	08/2016	244.00 - 244.00	248.00	09/2018 -	05/2019	1.64
27	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 - 272.19	272.54	03/2019 -	03/2021	.13
28	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 - 156.56	190.34	- -	06/2021	21.58
29	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022	01/2018	249.01 - 249.01	249.07	- -	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>						
30	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 - 1,351.00	1,471.00	09/2021 -	09/2021	8.88
	Total		5,589.39 .00 5,589.39	6,287.30			
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	12/2021	64.04
	Total		1,219.21 .00 1,219.21	2,000.00			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
32	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00 496.00	498.99	06/2017 -	10/2021	.60
33	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 - 294.00	350.69	04/2019 -	04/2021	19.28
34	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 - 549.31	559.47	07/2019 -	-	1.85
35	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00 199.00	205.00	09/2020 -	-	3.02
	<u>Rail India Technical And Economic Service</u>						
36	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 - 484.32	626.26	09/2014 -	-	29.31
	Total		2,009.81 695.00 2,022.63	2,240.41			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
37	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 - 4,588.29	5,245.96	08/2018 -	05/2021	14.33
	<u>Hindustan Petroleum Corporation Limited</u>						
38	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 - 2,677.00	3,072.00	06/2021 -	08/2022	14.76
	<u>Indian Oil Corporation Limited</u>						
39	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 - 1,823.00	3,027.90	03/2021 -	08/2021	66.09
40	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 - 2,321.00	3,338.00	12/2020 -	03/2022	43.82
41	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 - 423.00	502.00	08/2019 -	06/2021	18.68
42	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 - 4,497.00	6,025.00	12/2018 -	02/2022	33.98
	<u>Oil India Limited</u>						
43	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 - 352.56	490.24	03/2017 -	03/2021	39.05

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
44	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 - 638.60	652.10	02/2020 -	04/2021	19.89
	Total		17,225.76 .00 17,320.45	22,353.20			
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
45	TANDA TPP STAGE-II (2X660 MW) - [N18000175	09/2014	9,188.98 - 9,188.98	9,842.02	07/2019 -	03/2021	7.11
46	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 - 14,366.58	15,389.42	06/2019 -	10/2022	7.12
47	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	04/2012	9,750.89 - 9,750.89	12,176.28	02/2017 -	01/2021	24.87
48	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 - 11,846.00	12,739.82	10/2017 -	-	7.55
49	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
50	KHARGONE STPP STAGE I (1320 MW) - [N18000205	03/2015	9,870.51 - 9,870.51	11,148.86	01/2020 -	-	12.95
51	PAKRI BARWADIH COAL MINING PROJECT - [N18000225	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
52	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	01/2015	203.28 - 203.28	260.03	07/2017 -	-	27.92
53	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 - 487.49	639.46	06/2014 -	-	31.17
54	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	05/2021	14.11
	<u>Satluj Jal Vidyut Nigam Limited</u>						
55	NAITWAR MORI HEP - [N18000265	10/2017	648.33 - 648.33	947.89	12/2021 -	12/2021	46.20
	<u>Thdc India Limited</u>						
56	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 - 2,491.58	3,860.35	06/2013 -	12/2023	54.94

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		68,118.60 7,738.00 68,118.64	77,351.20			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
57	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	1,377.48	03/2021 -	03/2023	73.73
58	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 - 184.06	315.00	03/2019 -	-	71.14
59	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,517.49	03/2021 -	03/2023	98.88
60	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 - 2,425.00	5,341.68	03/2024 -	03/2024	120.28
61	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 - 2,750.00	3,438.51	03/2024 -	-	25.04
62	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,283.49	03/2022 -	03/2023	.89
63	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
64	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
65	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 - 387.70	487.13	03/2018 -	03/2021	25.65
66	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	-	.21
	<u>East Central Railways</u>						
67	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 - 1,033.07	3,550.00	- -	03/2022	243.64
68	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 - 528.65	2,066.78	- -	03/2023	290.95
69	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95 283.95	751.55	03/2012 -	07/2021	164.68

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
70	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 - 324.73	1,070.00	03/2012 -	11/2022	229.50
71	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 - 162.87	614.45	- -	12/2023	277.26
72	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 - 499.41	516.02	03/2020 -	-	3.33
73	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 - 380.00	519.33	- -	03/2025	36.67
74	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 - 678.54	929.86	03/2019 -	05/2021	37.04
75	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 - 459.91	1,625.87	- -	03/2023	253.52
76	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 - 415.67	549.75	- -	-	32.26
77	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 - 326.20	2,995.01	- -	03/2024	818.15
78	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 - 325.00	735.20	- -	03/2021	126.22
79	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 - 378.56	1,858.75	- -	03/2023	391.01
80	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 - 211.00	1,006.00	- -	-	376.78
81	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 - 372.14	1,470.50	- -	03/2023	295.15
82	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 - 548.00	819.01	03/2020 -	03/2023	49.45
83	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 - 213.01	480.00	- -	-	125.34
84	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 - 332.15	546.71	07/2014 -	-	64.60
85	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 - 744.04	1,215.54	03/2021 -	03/2024	63.37

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
86	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 - 731.64	1,185.73	03/2021 -	06/2022	62.06
87	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 - 180.82	726.31	- -	-	301.68
88	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 - 329.39	1,483.14	- -	03/2022	350.27
<u>East Coast Railway</u>							
89	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 - 1,111.99	1,539.28	02/2019 -	12/2021	38.43
90	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 - 1,160.00	1,160.83	03/2020 -	03/2023	.07
91	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2024	15.45
<u>Eastern Railways</u>							
92	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
93	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
94	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 - 365.17	439.30	03/2017 -	03/2025	20.30
95	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46
96	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 - 542.18	663.13	03/2020 -	03/2021	22.31
97	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 - 175.80	495.10	- -	03/2022	181.63
98	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
99	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01
100	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
101	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 - 499.96	680.68	02/2012 -	03/2025	36.15
102	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
103	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
104	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08
105	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30
106	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
107	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
108	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 - 288.35	502.48	- -	03/2021	74.26
109	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 - 261.38	565.00	- -	05/2019	116.16
110	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
111	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
112	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	12/2023	117.23
113	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	03/2022	.00
<u>Metropolitan Rapid Transport Projects</u>							
114	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37
115	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 - 495.44	2,980.41	03/2004 -	03/2022	501.57

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
116	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	734.01	06/2013 -	12/2021	48.06
117	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
118	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 - 120.00	346.00	12/2008 -	-	188.33
119	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
120	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00 668.00	680.00	03/2020 -	-	1.80
	<u>North East Frontier Railway</u>						
121	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 - 200.34	614.00	03/2019 -	-	106.51
122	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 5,021.45	5,521.45	03/2014 -	03/2023	130.69
123	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 - 2,531.34	4,541.38	12/2008 -	04/2021	284.80
124	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 4,454.17	12,264.15	03/2011 -	12/2023	175.34
125	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,043.00	03/2019 -	03/2023	170.77
126	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 - 2,132.03	2,145.00	03/2019 -	03/2024	302.54
127	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 - 2,326.52	6,911.00	03/2015 -	12/2024	197.05
128	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 - 333.76	360.00	- -	-	7.86
129	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 1,339.48	8,600.00	12/2015 -	-	542.04
130	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 - 221.42	380.00	- -	-	71.62

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
131	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 569.63	742.00	03/2020 -	03/2022	30.26
132	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	4,083.02	03/2021 -	03/2021	350.44
133	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
134	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	373.87	- -	12/2021	54.80
135	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	1,040.00	03/2020 -	-	150.70
136	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 - 819.23	1,871.00	- -	-	128.39
137	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 - 486.96	800.00	03/2019 -	03/2021	154.78
138	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	2,950.00	03/2022 -	03/2023	32.15
139	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	1,873.21	03/2021 -	05/2021	115.07
140	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 - 602.27	2,144.78	12/2021 -	04/2021	256.12
141	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 - 380.60	1,090.60	04/2010 -	-	186.55
<u>North Eastern Railway</u>							
142	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 - 142.45	228.40	- -	-	60.34
143	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 - 182.92	197.73	- -	-	8.10
144	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
145	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 - 243.78	895.00	12/2021 -	12/2021	267.13
146	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	477.31	01/2019 -	02/2022	61.80

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
147	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
148	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	12/2021	.16
149	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,476.15	01/2018 -	-	9.91
150	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	714.34	- -	12/2023	18.56
	<u>North Western Railway</u>						
151	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	11/2021	109.82
152	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	04/2022	16.97
153	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 - 873.71	1,980.21	- -	-	126.64
154	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 - 246.08	395.00	12/2019 -	02/2021	60.52
155	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
156	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 - 236.93	350.45	10/2018 -	-	47.91
157	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 - 822.00	1,099.00	- -	-	33.70
158	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 - 323.00	432.22	- -	-	33.81
159	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	04/2013	420.18 - 420.18	480.00	03/2020 -	06/2021	14.24
160	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 - 213.39	375.00	11/2019 -	03/2021	75.73
161	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 - 242.09	525.00	02/2019 -	02/2020	116.86
	<u>Northern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
162	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	359.00	- -	03/2024	129.17
163	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	06/2021	211.31
164	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
165	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 - 219.83	346.63	- -	-	57.68
166	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 - 1,229.00	1,265.00	- -	03/2023	2.93
167	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
168	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,200.00	07/2012 -	03/2024	388.89
169	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 - 2,500.00	27,949.00	11/2002 -	12/2022	1,017.96
170	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 625.00	859.00	03/2016 -	06/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>						
171	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 - 1,185.64	1,844.47	12/2017 -	-	55.57
172	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
173	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	396.00	03/2009 03/2009	-	91.30
174	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,639.00	03/2016 -	03/2025	59.22
175	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	12/2025	127.62
176	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,000.00	03/2023 -	12/2022	41.04
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,259.48	03/2016 -	03/2025	7.78

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
178	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
179	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	3,377.00	03/2020 -	03/2022	124.58
180	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 - 975.62	1,500.00	12/2021 -	12/2021	53.75
181	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 - 644.38	872.65	03/2021 -	03/2021	35.42
182	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 - 1,548.66	1,868.89	12/2021 -	03/2022	20.68
183	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	950.00	03/2016 -	12/2021	50.15
184	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32
185	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,000.00	03/2022 -	12/2024	5.98
186	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 - 773.94	850.00	12/2024 -	12/2024	9.83
187	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,400.00	03/2019 -	06/2022	51.02
188	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	22,716.11	12/2024 -	03/2025	40.08
189	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,725.00	03/2020 -	12/2021	281.93
190	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
191	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	12/2021	111.91
192	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,536.00	03/2019 -	06/2022	62.89
193	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	1,825.00	12/2020 -	12/2022	54.24

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
194	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>						
195	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
196	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2024	102.85
197	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86
198	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
199	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 - 2,288.70	2,643.25	03/2021 -	03/2024	15.49
200	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 - 704.31	927.94	03/2020 -	06/2021	31.75
201	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 - 2,132.77	3,037.95	03/2014 -	03/2027	42.44
202	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 - 164.36	1,050.00	02/2009 -	-	538.84
203	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
204	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2024	7.06
205	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 185.00	449.39	03/2022 -	12/2022	142.91
	<u>South East Central Railway</u>						
206	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 - 383.79	1,413.76	- -	-	268.37
207	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 - 511.86	2,005.25	04/2020 -	04/2021	291.76
208	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 - 1,908.51	3,524.81	03/2023 -	12/2023	84.69

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
209	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93 - 585.93	1,268.32	02/2019 -	12/2021	116.46
210	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 - 229.00	1,096.00	12/2021 -	12/2024	378.60
211	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 - 872.00	1,226.51	12/2019 -	-	40.65
212	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 - 1,973.00	2,135.34	03/2021 -	12/2023	8.23
213	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 - 1,370.00	1,370.94	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>						
214	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
215	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 - 148.77	377.00	12/2016 -	08/2020	153.41
216	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
217	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
218	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 - 149.90	230.00	03/2015 -	-	53.44
219	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 - 1,966.70	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
220	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 - 1,801.01	1,967.00	- -	12/2023	9.22
221	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	296.10	- -	12/2023	.03
222	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,432.50	- -	03/2025	17.95
223	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 - 146.75	167.50	- -	12/2023	14.14

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
224	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	3,911.65	- -	12/2024	68.97
225	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,656.00	03/2020 -	03/2023	43.14
226	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,147.00	03/2020 -	06/2021	33.31
227	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	783.00	03/2020 -	06/2021	35.47
228	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,614.59	1,870.41	03/2019 -	03/2024	15.84
229	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 - 644.78	998.00	03/2017 -	03/2025	54.78
	<u>Southern Railway</u>						
230	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 - 724.69	2,910.84	02/2019 -	03/2025	301.67
231	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,720.00	03/2020 -	03/2025	465.83
232	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
233	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	527.37	02/2019 -	-	247.32
234	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	1,205.00	- -	03/2024	130.17
235	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	1,500.00	- -	-	78.78
236	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 - 198.68	559.95	- -	03/2024	181.84
237	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 270.14	457.08	- -	12/2021	69.20
238	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 252.96	369.55	- -	-	46.09
239	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	1,140.00	- -	-	295.05

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
240	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	600.30	- -	09/2021	265.12
241	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	1,121.00	- -	04/2021	20.28
242	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 189.24	275.21	- -	-	45.43
243	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,172.16	03/2019 -	12/2027	1,699.64
244	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 - 187.26	332.00	04/2014 -	12/2020	77.29
245	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,000.00	1,246.00	- -	-	24.60
246	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	950.00	03/2005 -	09/2021	253.33
247	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	06/2022	102.11
<u>West Central Railway</u>							
248	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2023	585.35
249	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
<u>Western Railway</u>							
250	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95 196.95	202.35	03/2011 -	-	2.74
	Total		1,89,462.73 5,323.20 1,94,414.36	3,76,579.30			
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
251	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00 227.00	247.95	- -	-	9.23
252	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 - 624.41	992.67	03/2011 -	12/2020	58.98

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
253	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 - 193.69	327.92	10/2010 -	06/2021	69.30
254	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 - 207.03	389.45	05/2012 -	-	88.11
255	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 - 258.97	268.92	08/2015 -	-	3.84
256	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 - 280.16	290.59	- -	-	3.72
257	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00 348.00	348.43	09/2017 -	-	.12
258	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 - 445.89	653.29	03/2017 -	-	46.51
259	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 - 497.05	881.05	05/2017 -	04/2021	77.26
260	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 - 889.24	904.82	- -	12/2020	1.75
261	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 - 470.20	630.36	02/2011 -	-	34.06
262	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 - 282.41	322.01	08/2016 -	-	14.02
263	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401	11/2011	954.43 - 954.43	1,191.51	09/2015 -	10/2021	24.84
264	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 - 358.22	377.64	10/2016 -	-	5.42
265	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 - 333.21	353.89	11/2015 -	-	6.21
266	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 - 195.04	377.99	10/2010 -	06/2021	93.80
267	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 - 319.68	369.77	- -	-	15.67
268	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00 157.00	157.30	06/2018 -	-	.19

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
269	REHABILITATION AND UPGADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 - 460.73	461.00	- -	-	.06
270	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 - 237.80	238.00	11/2019 -	-	.08
271	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 - 166.21	173.41	08/2018 -	-	4.33
272	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 - 217.22	226.88	08/2018 -	-	4.45
273	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 - 333.21	355.89	12/2015 -	-	6.81
274	REHABILITATION AND UPGADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00 294.00	294.12	07/2018 -	-	.04
275	REHABILITATION AND UPGADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00 504.00	504.19	11/2018 -	01/2021	.04
276	REHABILITATION AND UPGADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00 995.00	995.09	05/2016 -	04/2021	.01
277	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00 203.00	203.21	05/2019 -	-	.10
278	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00 373.00	373.10	05/2019 -	-	.03
279	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15
280	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00 548.00	548.03	06/2019 -	-	.01
281	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00 391.00	391.06	06/2019 -	-	.02
282	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
283	KARAD TO VITA - [N24001049	01/2018	344.85 245.00 245.00	344.85	12/2019 -	-	40.76
284	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00 257.00	257.38	12/2019 -	-	.15

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
285	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
286	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	-	.05
287	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	-	.08
288	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	-	.24
289	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	-	.06
290	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	-	.12
291	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	-	.06
292	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	-	.08
293	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	-	.14
294	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	-	.01
295	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	-	.13
296	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	-	.07
297	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	-	.11
298	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	-	.01
299	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	-	.03
300	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	-	.06

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
301	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	-	.47
302	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	-	.08
303	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	-	.02
304	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	-	.16
305	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	-	.08
306	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	-	26.19
307	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	-	2.47
308	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31
309	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	06/2021	.03
310	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01
311	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00
312	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	-	.01
313	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00 215.00	215.16	09/2019 -	-	.07
314	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	03/2021	.13
315	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00 653.00	653.29	03/2017 -	04/2021	.04
316	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 - 186.96	322.24	09/2014 -	-	72.36

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
317	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 - 1,979.00	2,036.90	- -	-	2.93
318	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00 543.73	544.00	09/2016 -	06/2021	.00
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
319	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 - 195.23	252.79	04/2017 -	-	29.48
320	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 - 203.36	263.31	04/2017 -	-	29.48
321	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681	01/2017	194.66 - 194.66	252.05	04/2017 -	-	29.48
322	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 - 373.07	387.00	08/2016 -	05/2021	3.73
323	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 - 198.22	252.05	04/2017 -	-	27.16
324	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
325	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902	10/2017	818.00 - 818.00	887.68	- -	-	8.52
	<u>National Highways Authority Of India</u>						
326	HARANGAJAO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 - 280.00	520.00	02/2009 -	-	85.71
327	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23
328	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95
329	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
330	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 - 160.00	167.98	05/2008 -	06/2019	4.99
331	HARANGAJAO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 - 196.00	655.17	07/2009 -	-	234.27

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
332	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 - 1,108.00	2,967.50	11/2011 -	-	167.82
333	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
334	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 - 217.61	360.84	04/2010 -	07/2019	65.82
335	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 - 208.00	230.00	04/2008 -	02/2021	10.58
336	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
337	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
338	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
339	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 - 585.00	591.00	11/2013 -	01/2021	15.53
340	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 - 1,928.22	2,945.00	04/2015 -	03/2021	52.73
341	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 - 531.13	730.97	05/2018 -	06/2021	37.63
342	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 - 361.15	363.93	- -	-	.77
343	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 - 593.26	690.17	05/2018 -	06/2021	16.34
344	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
345	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 - 1,083.00	1,827.15	06/2018 -	-	68.71
346	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]	03/2015	794.30 - 679.94	691.38	- -	05/2020	-12.96
347	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	10/2021	1.37

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
348	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
349	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]	08/2015	322.09 - 247.00	322.09	04/2018 -	12/2020	.00
350	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 - 447.29	746.43	12/2017 -	-	66.88
351	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	-	6.11
352	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	-	1.33
353	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	-	41.78
354	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	-	21.50
355	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	-	25.80
356	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	-	44.60
357	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	02/2016	997.15 - 997.15	1,115.95	03/2019 -	-	11.91
358	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84
359	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	03/2021	7.53
360	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	2,587.50	09/2019 -	-	86.37
361	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 - 1,169.61	2,280.00	- -	-	94.94
362	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 - 323.72	336.60	08/2018 -	-	3.98
363	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82 - 1,239.82	1,727.66	- -	01/2021	39.35

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
364	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 - 950.69	1,108.00	08/2019 -	-	16.55
365	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 - 1,100.19	1,145.31	- -	03/2021	4.10
366	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 - 290.73	315.00	- -	-	8.35
367	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 - 605.84	722.46	07/2018 -	-	19.25
368	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
369	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 - 744.64	982.00	03/2020 -	-	31.88
370	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	-	3.40
371	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 - 988.34	1,043.28	03/2020 -	-	5.56
372	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	-	1.06
373	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	-	5.70
374	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 - 754.54	756.27	03/2020 -	09/2021	.23
375	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 - 672.89	736.01	03/2020 -	-	9.38
376	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
377	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	06/2021	10.24
378	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
379	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
380	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48/O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
381	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	07/2021	3.95
382	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	02/2021	1.78
383	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 - 1,124.11	1,232.76	09/2017 -	05/2021	9.67
384	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 - 404.94	448.18	- -	10/2020	10.68
385	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 - 273.46	276.17	- -	-	.99
386	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
387	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 - 1,166.26	1,296.93	- -	08/2021	11.20
388	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 - 1,995.34	2,400.00	- -	11/2021	20.28
389	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
390	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 - 1,261.98	1,952.20	- -	07/2021	54.69
391	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35
392	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
393	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 - 1,052.21	1,449.00	- -	01/2021	37.71
394	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 - 1,532.62	2,499.00	03/2021 -	04/2021	63.05
395	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 - 496.20	537.17	- -	-	8.26

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
396	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
397	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	01/2022	5.32
398	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	-	4.99
399	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
400	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 - 634.70	931.21	- -	07/2021	46.72
401	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 795.50	799.30	- -	07/2021	.48
402	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	-	25.68
403	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 - 743.88	743.89	- -	12/2021	.00
404	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	11/2022	27.86
405	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 - 217.96	884.00	- -	-	305.58
	Total		1,06,285.04 19,154.00 1,06,378.03	1,30,764.64			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
406	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00 431.00	431.16	06/2021 -	11/2021	.04
	<u>Department Of Telecommunication</u>						
407	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 - 13,334.00	24,664.00	07/2015 -	06/2021	84.97
	Total		13,765.16 431.00 13,765.00	25,095.16			
	<u>URBAN DEVELOPMENT</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(March 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Ahmedabad Metro Rail</u>						
408	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 - 10,773.00	12,787.00	12/2018 -	08/2022	18.69
	<u>Chennai Metro Rail Ltd</u>						
409	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 - 14,600.00	19,058.00	12/2015 -	-	30.53
	<u>Mumbai Metro Rail Corporation Ltd</u>						
410	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 - 23,136.00	33,406.00	01/2015 -	03/2023	44.39
	<u>National Building Construcion Corporation Ltd</u>						
411	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 - 4,264.00	4,720.73	11/2019 -	-	10.71
	Total		52,773.00 .00 52,773.00	69,971.73			
	<u>WATER RESOURCES</u>						
	<u>Uttar Pradesh Jal Nigam</u>						
412	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 - 231.79	234.03	12/2021 -	12/2021	.97
413	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 - 681.78	690.71	06/2022 -	06/2022	1.31
	Total		913.57 .00 913.57	924.74			
	Grand Total		5,26,180.28 33,341.20 5,33,517.29	8,00,707.05			

Details of Central Sector Projects Costing Rs.150 crore and above (as on)					31.03.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2021]	417.23 (-) [441.33]	291.75 (24.10) [33]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	47.28 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	164.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	172.78 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	26.44 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	39.86 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	24.96 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [0/0]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [3/2023]	611.80 (-) [611.80]	8.46 (0.00) [0]
11	EXT & STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (-) [6/2021]	177.10 (-) [177.10]	0.00 (0.00) [16]
	<u>Health And Family Welfare</u>				
12	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [6/2021]	601.02 (-) [601.02]	382.25 (0.00) [-]
13	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2021]	272.19 (-) [272.54]	258.51 (0.35) [24]
	<u>Human Resource Development</u>				
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-)	186.00 (199.00)	130.63 (19.00)

			[3/2021]	[205.00]	[6]
15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	9/2019	9/2022 (-) [1/2023]	588.72 (-) [588.72]	14.80 (0.00) [4]
16	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [0/0]	655.34 (-) [655.34]	49.89 (0.00) [0]
	<u>Petroleum</u>				
17	220 KV GRID SUPPLY	10/2020	3/2021 (-) [3/2021]	303.40 (-) [303.40]	199.11 (0.00) [0]
18	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	254.90 (0.00) [3]
19	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (3/2021) [3/2021]	384.58 (-) [384.58]	247.72 (0.00) [-1]
20	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [5/2021]	580.20 (-) [580.20]	151.16 (0.00) [3]
21	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (6/2022) [6/2022]	34,012.00 (-) [25,090.00]	11,190.15 (-8,922.00) [24]
22	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [7/2022]	167.00 (-) [167.00]	8.95 (0.00) [0]
23	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	92.80 (0.00) [10]
24	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	95.40 (0.00) [0]
25	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [11/2022]	332.61 (-) [332.61]	0.00 (0.00) [0]
26	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [8/2021]	210.94 (-) [210.94]	117.00 (0.00) [0]
27	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [7/2021]	196.26 (-) [196.26]	92.33 (0.00) [12]
28	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	14,820.60 (5,336.00) [24]
	<u>Railways</u>				
29	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [829.00]	0.94 (0.00) [0]
30	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
31	GUDUR-DURGARA JAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
32	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2024]	3,631.00 (-) [3,887.48]	1,144.64 (256.48) [24]
33	KOTLAPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2024]	1,045.20 (-) [2,120.16]	883.52 (1,074.96) [180]
34	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022	2,499.71	665.93

			(3/2024) [3/2024]	(-) [2,499.71]	(0.00) [24]
35	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [0/0]	234.50 (-) [235.00]	14.14 (0.50) [0]
36	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [3/2021]	387.70 (-) [487.13]	434.63 (99.43) [36]
37	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,643.25]	1,231.85 (354.55) [36]
38	NANDYAL-YERRAGUNTLA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
39	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	2,224.17 (302.42) [0]
40	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [3,377.00]	2,683.67 (1,873.29) [24]
Road Transport And Highways					
41	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/	328.67	234.49
			(-)	(-)	(0.00)
			[0/0]	[328.67]	[0]
42	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021	1,226.88	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,226.88]	[0]
43	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021	1,601.10	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,601.10]	[0]
44	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/	357.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[357.00]	[0]
45	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/	557.30	351.02
			(-)	(-)	(0.00)
			[0/0]	[557.30]	[0]
46	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017	263.45	97.45
			(5/2021)	(-)	(0.00)
			[5/2021]	[263.45]	[44]
47	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017	429.43	293.60
			(4/2021)	(-)	(0.00)
			[4/2021]	[429.43]	[41]
48	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/	314.43	86.83
			(-)	(-)	(0.00)
			[6/2021]	[314.43]	[-]
49	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017	350.61	323.06
			(12/2020)	(-)	(0.00)
			[12/2020]	[350.61]	[0]
50	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015	333.21	256.11
			(-)	(-)	(20.68)
			[0/0]	[353.89]	[0]
51	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015	333.21	256.11
			(-)	(333.21)	(0.00)
			[0/0]	[333.21]	[0]
52	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015	333.21	256.11
			(-)	(-)	(0.00)
			[0/0]	[333.21]	[0]
53	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015	333.21	315.57
			(-)	(-)	(22.68)
			[0/0]	[355.89]	[0]
54	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-	3/2018	3/2021	1,532.62	1,582.36

	KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)		(10/2021) [4/2021]	(-) [2,499.00]	(966.38) [1]
55	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	1,634.05 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (-) [0/0]	576.48 (-) [576.48]	288.92 (0.00) [0]
57	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (7/2021) [7/2021]	348.95 (-) [348.95]	200.57 (0.00) [59]
58	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (-) [0/0]	386.09 (-) [386.09]	199.35 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (7/2021) [7/2021]	290.15 (-) [290.15]	214.00 (0.00) [50]
61	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	567.75 (0.00) [0]
63	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (8/2021) [4/2021]	995.09 (995.00) [995.09]	476.77 (0.00) [59]
64	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (-) [0/0]	444.84 (-) [444.84]	304.42 (0.00) [0]
65	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (-) [0/0]	376.25 (-) [376.25]	264.97 (0.00) [0]
66	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (-) [0/0]	297.12 (294.00) [294.12]	373.98 (-3.00) [0]
67	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (6/2021) [2/2021]	289.67 (290.00) [289.67]	177.78 (0.00) [0]
68	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (4/2021) [1/2021]	504.19 (504.00) [504.19]	427.08 (0.00) [0]
69	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (3/2021) [3/2021]	271.45 (-) [271.45]	225.81 (0.00) [65]
70	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (5/2021) [8/2019]	319.28 (-) [319.28]	214.00 (0.00) [0]
71	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (-) [0/0]	244.95 (245.00) [244.95]	136.22 (0.00) [0]
72	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (6/2021) [6/2021]	372.68 (-) [372.68]	214.00 (0.00) [52]
73	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2021) [3/2021]	228.32 (-) [228.32]	105.72 (0.00) [31]
74	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM	1/2018	8/2018 (5/2021)	418.03 (-)	279.86 (0.00)

	420.800(P		[5/2021]	[418.03]	[33]
75	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (-) [0/0]	378.24 (-) [378.24]	315.42 (0.00) [0]
76	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [10/2021]	1,959.00 (-) [1,959.00]	1,211.72 (0.00) [-]
77	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (-) [0/0]	597.67 (-) [597.67]	0.00 (0.00) [0]
78	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN	9/2018	2/2019 (-) [0/0]	617.41 (-) [617.41]	0.00 (0.00) [0]
79	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [7/2021]	1,323.15 (-) [1,323.15]	785.33 (0.00) [-]
80	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [9/2021]	1,550.98 (-) [1,550.98]	1,401.00 (0.00) [-]
81	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,275.58 (0.00) [0]
82	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	951.13 (145.48) [0]
83	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
84	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
85	COKE OVEN BATTERY-5	12/2011	12/2017 (12/2020) [12/2020]	2,858.00 (-) [2,558.00]	1,804.98 (-300.00) [0]
	<u>Water Resources</u>				
86	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2021) [4/2022]	10,151.04 (55,548.87) [55,548.87]	17,025.01 (45,397.83) [25]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
87	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (2/2021) [2/2021]	2,496.90 (7,927.34) [7,927.34]	8,154.50 (5,430.44) [0]
88	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	13,537.76 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
89	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	134.38 (0.00) [0]
90	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	400.56 (0.00) [0]
91	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	144.19 (0.00) [0]
92	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	163.66 (0.00) [0]
93	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN	3/2019	2/2020	403.68	25.52

	SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)		(-) [0/0]	(-) [403.68]	(0.00) [0]
94	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	66.14 (0.00) [0]
95	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	0.00 (0.00) [0]
96	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	30.34 (0.00) [0]
97	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	33.61 (0.00) [0]
98	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	35.38 (0.00) [0]
99	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	0.00 (0.00) [0]
100	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	107.43 (0.00) [0]
101	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	0.00 (0.00) [0]
102	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	115.89 (0.00) [0]
103	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	260.57 (0.00) [0]
104	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	91.23 (0.00) [0]
105	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]
106	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	178.10 (0.00) [0]
107	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	184.62 (0.00) [0]
108	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [9/2018]	197.16 (-) [197.16]	91.25 (0.00) [0]
109	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	376.69 (0.00) [0]
110	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	0.00 (0.00) [0]
111	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	4.21 (0.00) [0]
112	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	204.77 (0.00) [60]
113	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON	2/2017	4/2017 (-)	167.28 (-)	22.06 (0.00)

	EPC BASIS FROM EXI		[2/2021]	[167.28]	[0]
114	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-)	(-)	(0.00)
			[0/0]	[392.60]	[0]
115	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	172.89
			(-)	(-)	(0.00)
			[0/0]	[434.06]	[0]
116	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	149.44
			(3/2018)	(284.09)	(0.00)
			[3/2021]	[284.09]	[47]
117	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	100.63
			(-)	(-)	(57.56)
			[0/0]	[252.79]	[0]
118	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	116.97
			(-)	(-)	(59.95)
			[0/0]	[263.31]	[0]
119	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	111.22
			(-)	(-)	(57.39)
			[0/0]	[252.05]	[0]
120	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	111.21
			(-)	(-)	(53.83)
			[0/0]	[252.05]	[0]
121	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012	207.03	349.94
			(6/2018)	(-)	(182.42)
			[0/0]	[389.45]	[0]
122	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017	180.57	51.78
			(-)	(-)	(0.00)
			[2/2021]	[180.57]	[0]
123	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012	156.63	0.00
			(-)	(276.00)	(119.37)
			[0/0]	[276.00]	[0]
124	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011	305.49	131.08
			(-)	(-)	(0.00)
			[0/0]	[305.49]	[0]
125	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/	256.66	24.14
			(-)	(-)	(0.00)
			[0/0]	[256.66]	[0]
126	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/	175.06	81.01
			(-)	(-)	(0.00)
			[4/2022]	[175.06]	[-]
127	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/	176.12	65.25
			(-)	(-)	(0.00)
			[4/2022]	[176.12]	[-]
128	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/	1,979.00	1,217.25
			(3/2020)	(-)	(57.90)
			[0/0]	[2,036.90]	[0]
	ASSAM				
	Civil Aviation				
129	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021	1,142.00	323.90
			(-)	(-)	(90.00)
			[3/2022]	[1,232.00]	[12]
	Health And Family Welfare				
130	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021	875.00	331.55
			(-)	(-)	(-127.20)
			[7/2022]	[747.80]	[14]
131	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	163.37
			(-)	(-)	(0.00)
			[3/2018]	[175.57]	[0]
	Petroleum				
132	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	487.25
			(6/2021)	(-)	(0.00)

			[6/2021]	[557.00]	[16]
133	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [4/2021]	224.75 (-) [222.21]	144.80 (-2.54) [8]
134	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [6/2021]	423.00 (-) [502.00]	421.03 (79.00) [22]
135	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [4/2021]	543.91 (638.60) [652.10]	136.05 (108.19) [14]
136	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [12,366.00]	168.82 (0.00) [0]
137	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	117.34 (0.00) [0]
138	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2021) [5/2021]	249.85 (303.75) [303.75]	197.20 (53.90) [12]
	<u>Railways</u>				
139	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2021]	314.00 (486.96) [800.00]	799.87 (486.00) [24]
140	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,496.25 (717.68) [12]
141	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [5/2021]	870.96 (-) [1,873.21]	1,162.39 (1,002.25) [2]
142	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,043.00]	798.53 (657.80) [48]
	<u>Road Transport And Highways</u>				
143	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (390.73) [390.73]	267.46 (122.65) [0]
144	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
145	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	15.29 (0.00) [0]
146	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
147	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [303.49]	168.19 (-216.52) [0]
148	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	480.74 (0.00) [0]
149	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	75.42 (0.00) [0]
150	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	116.92 (-28.50) [0]
151	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.30]	100.07 (-30.09) [42]
152	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END	1/2016	1/2016	294.17	201.60

	OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O		(-) [4/2021]	(-) [294.17]	(0.00) [63]
153	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	0.00 (0.00) [0]
154	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2- LANE ROAD W	3/2020	12/2020 (-) [0/0]	166.94 (-) [166.94]	0.00 (0.00) [0]
155	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	489.84 (143.23) [0]
156	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [0/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
157	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	233.27 (7.98) [0]
158	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
159	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	125.80 (0.00) [0]
160	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [887.68]	259.50 (69.68) [0]
161	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	145.21 (-65.43) [42]
162	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	407.11 (0.00) [0]
163	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	291.45 (0.00) [0]
164	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
165	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
166	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
167	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
168	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
169	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [2/2021]	208.00 (-) [230.00]	370.56 (22.00) [0]
170	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	390.72 (0.00) [0]
171	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [273.40]	132.79 (-776.11) [0]
172	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-)	245.00 (-)	240.36 (-70.66)

			[8/2020]	[174.34]	[0]
173	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	70.46 (0.00) [0]
174	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	0.00 (0.00) [0]
175	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	0.00 (0.00) [0]
	BIHAR				
	Civil Aviation				
176	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	1,216.90 (-) [1,216.90]	122.19 (0.00) [0]
	Human Resource Development				
177	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [10/2021]	496.18 (496.00) [498.99]	224.58 (2.81) [52]
178	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (375.00) [375.00]	48.46 (0.00) [26]
	Petroleum				
179	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [4/2023]	14,810.00 (-) [14,810.00]	865.95 (0.00) [0]
180	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	142.34 (0.00) [0]
181	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (12/2021) [12/2021]	522.00 (-) [522.00]	318.04 (0.00) [9]
182	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (8/2022) [8/2022]	199.36 (-) [199.36]	34.40 (0.00) [22]
183	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021) [6/2021]	189.00 (-) [189.00]	144.29 (0.00) [5]
184	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (9/2021) [9/2021]	206.50 (-) [206.50]	134.82 (0.00) [6]
185	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	1.77 (0.00) [0]
	Power				
186	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [7/2023]	8,692.97 (21,312.11) [21,312.11]	18,530.80 (12,619.14) [141]
187	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (6/2020) [6/2021]	5,353.00 (10,566.00) [10,566.00]	8,839.26 (5,213.00) [107]
188	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	1,998.39 (0.00) [0]
189	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (-) [12/2021]	12,964.60 (17,304.00) [17,304.00]	15,761.92 (4,339.40) [43]
	Railways				
190	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]

191	ARARIA-SUPAUL (NL)	4/2008	/	1,605.17	52.72
			(-)	(-)	(0.00)
			[3/2023]	[1,605.17]	[-]
192	BIHTA-AURANGABAD (NL)	4/2008	/	326.20	2.04
			(-)	(-)	(2,668.81)
			[3/2024]	[2,995.01]	[-]
193	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/	378.56	386.36
			(-)	(-)	(1,480.19)
			[3/2023]	[1,858.75]	[-]
194	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/	406.92	200.00
			(-)	(-)	(-67.92)
			[0/0]	[339.00]	[0]
195	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-)	(-)	(0.00)
			[0/0]	[205.00]	[0]
196	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/	329.39	1,207.34
			(-)	(-)	(1,153.75)
			[3/2022]	[1,483.14]	[-]
197	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	1.15
			(-)	(-)	(0.00)
			[0/0]	[445.25]	[0]
198	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	485.99
			(-)	(-)	(266.99)
			[0/0]	[480.00]	[0]
199	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	1,551.38
			(-)	(-)	(1,538.13)
			[3/2023]	[2,066.78]	[-]
200	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	1,062.07
			(-)	(-)	(745.27)
			[11/2022]	[1,070.00]	[128]
201	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	530.12
			(-)	(-)	(271.01)
			[3/2023]	[819.01]	[36]
202	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	340.21
			(-)	(-)	(451.58)
			[12/2023]	[614.45]	[-]
203	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.74
			(-)	(-)	(26.24)
			[0/0]	[360.00]	[0]
204	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	925.70
			(-)	(1,200.20)	(0.00)
			[3/2023]	[1,200.20]	[36]
205	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	427.28
			(-)	(-)	(16.61)
			[0/0]	[516.02]	[0]
206	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.39
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
207	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	683.91
			(-)	(283.95)	(273.67)
			[7/2021]	[751.55]	[112]
208	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	24.74
			(-)	(-)	(795.00)
			[0/0]	[1,006.00]	[0]
209	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	165.55
			(-)	(-)	(454.09)
			[6/2022]	[1,185.73]	[15]
210	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.60
			(-)	(-)	(0.00)
			[0/0]	[281.30]	[0]
211	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.53

			(-) [3/2024]	(-) [228.05]	(0.00) [-]
212	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (-) [546.71]	541.83 (214.56) [0]
213	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [0/0]	620.57 (-) [620.57]	0.31 (0.00) [0]
214	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2024]	532.87 (2,132.03) [2,145.00]	970.88 (1,612.13) [60]
215	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (-) [0/0]	180.82 (-) [726.31]	540.19 (545.49) [0]
216	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [3/2023]	1,491.47 (-) [1,491.47]	510.65 (0.00) [36]
217	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [3/2024]	744.04 (-) [1,215.54]	398.20 (471.50) [36]
218	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (-) [735.20]	380.48 (410.20) [-]
219	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2023]	372.14 (-) [1,470.50]	1,085.63 (1,098.36) [-]
220	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [3/2025]	380.00 (-) [519.33]	278.52 (139.33) [-]
221	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [678.62]	17.20 (0.00) [0]
	Road Transport And Highways				
222	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (12/2020) [1/2021]	511.54 (585.00) [591.00]	575.99 (79.46) [0]
223	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
224	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [0/0]	575.00 (-) [575.00]	555.63 (0.00) [0]
225	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	89.69 (0.00) [0]
226	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [0/0]	464.09 (-) [464.09]	0.00 (0.00) [0]
227	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [0/0]	649.90 (-) [649.90]	0.00 (0.00) [0]
228	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [0/0]	446.97 (-) [446.97]	0.00 (0.00) [0]
229	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	14.94 (0.00) [0]
230	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	9.02 (0.00) [0]
231	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM	8/2015	11/2015	288.24	303.16

	124/175 TO 140/200 OF NH-80 UNDER EPC MODE		(-) [0/0]	(-) [288.24]	(0.00) [0]
232	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-) [0/0]	(-) [2,598.00]	(0.00) [0]
233	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	36.08 (-7.71) [14]
234	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20	38.11
			(-) [0/0]	(-) [537.17]	(40.97) [0]
235	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [560.70]	664.50 (-123.13) [0]
236	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [478.35]	289.14 (-74.95) [0]
237	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
238	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [152.62]	95.10 (-26.23) [0]
239	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/	1,167.45	186.70
			(-) [0/0]	(-) [1,182.94]	(15.49) [0]
240	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/	642.41	400.60
			(-) [0/0]	(-) [681.67]	(39.26) [0]
241	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [12/2020]	322.09 (247.00) [322.09]	77.53 (0.00) [0]
242	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [925.87]	699.76 (-482.98) [0]
243	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/	814.04	512.04
			(-) [10/2021]	(-) [825.17]	(11.13) [-]
244	FOUR LANING OF PATNA TO KOILWAR	8/2015	/	556.07	0.00
			(-) [0/0]	(-) [556.07]	(0.00) [0]
245	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	343.52 (0.00) [0]
246	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
247	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	1,360.63 (0.00) [0]
248	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	1,504.21 (0.00) [0]
249	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/	573.70	44.46
			(-) [0/0]	(-) [573.70]	(0.00) [0]
250	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
251	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/	478.35	446.62
			(-)	(-)	(0.00)

			[0/0]	[478.35]	[0]
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	238.01 (50.09) [0]
253	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
254	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	318.64 (39.60) [0]
255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	343.70 (19.42) [0]
256	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	253.10 (0.00) [0]
257	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
258	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
259	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	200.18 (0.00) [54]
260	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	39.82 (0.00) [0]
261	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
262	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [0/0]	399.54 (-) [297.27]	271.39 (-102.27) [0]
263	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [1,038.56]	1,160.00 (183.76) [0]
264	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [649.27]	712.15 (133.14) [0]
265	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [0/0]	672.89 (-) [736.01]	31.82 (63.12) [0]
266	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	174.35 (0.00) [0]
267	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [0/0]	230.34 (-) [230.34]	210.12 (0.00) [0]
	<u>Urban Development</u>				
268	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [6/2024]	13,365.77 (-) [13,365.77]	231.97 (0.00) [0]
	<u>Water Resources</u>				
269	I AND D AND STP AT CHAPRA	11/2018	12/2020 (6/2021) [6/2021]	236.15 (-) [236.15]	28.53 (0.00) [6]
270	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [0/0]	254.13 (-) [254.13]	0.05 (0.00) [0]
271	IRRIGATION WORK OF BAGMATI	10/2005	3/2015	956.00	712.37

			(-) [3/2021]	(-) [721.37]	(-234.63) [72]
272	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [0/0]	268.63 (-) [268.63]	286.36 (0.00) [0]
273	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	4/2015	4/2020 (-) [6/2021]	184.93 (-) [184.93]	163.36 (0.00) [14]
274	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [7/2021]	230.06 (-) [230.06]	55.02 (0.00) [0]
275	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [12/2021]	305.19 (-) [305.19]	0.00 (0.00) [4]
276	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [10/2021]	294.02 (-) [294.02]	0.00 (0.00) [0]
277	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	5/2021 (-) [5/2021]	184.86 (-) [184.86]	152.78 (0.00) [0]
278	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [4/2021]	356.37 (-) [356.37]	90.77 (0.00) [0]
279	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [6/2022]	824.00 (-) [824.00]	40.09 (0.00) [0]
280	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [6/2022]	578.89 (-) [578.89]	40.09 (0.00) [0]
281	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [3/2021]	225.77 (-) [225.77]	271.22 (0.00) [12]
282	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [5/2021]	277.42 (-) [277.42]	133.75 (0.00) [0]
283	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (3/2021) [3/2021]	191.62 (-) [191.62]	53.08 (0.00) [4]
	CHANDIGARH				
	Road Transport And Highways				
284	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	3/2010	3/2013 (5/2019) [0/0]	179.89 (271.00) [271.00]	270.91 (91.11) [0]
285	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	1/2019 (-) [0/0]	169.26 (299.00) [299.00]	0.00 (129.74) [0]
	CHHATISGARH				
	Coal				
286	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	49.42 (0.00) [60]
287	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2023]	316.10 (-) [316.10]	130.17 (0.00) [36]
288	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	276.19 (0.00) [0]
289	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2025]	610.63 (-) [610.63]	145.83 (0.00) [36]
290	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029	5,241.40	1,931.04

			(-) [3/2029]	(-) [5,241.40]	(0.00) [0]
291	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2026]	916.24 (-) [916.24]	9.71 (0.00) [36]
292	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	4,268.97 (0.00) [0]
293	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2022]	152.43 (459.49) [459.49]	201.48 (307.06) [84]
294	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	182.99 (0.00) [0]
295	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
296	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2022]	178.44 (-) [178.44]	6.50 (0.00) [96]
297	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,630.04 (0.00) [0]
298	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
299	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	28.26 (0.00) [0]
300	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	209.24 (0.00) [84]
301	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	8.28 (0.00) [0]
302	PORDA CHIMTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
303	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.95 (0.00) [0]
	<u>Human Resource Development</u>				
304	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [7/2022]	808.62 (-) [808.62]	57.42 (0.00) [0]
	<u>Power</u>				
305	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (-) [0/0]	11,846.00 (-) [12,739.82]	13,766.78 (893.82) [0]
306	TALAIPELLI COAL MINING PROJECT	9/2015	11/2019 (-) [0/0]	3,004.00 (-) [3,004.00]	2,369.23 (0.00) [0]
	<u>Railways</u>				
307	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (-) [0/0]	872.00 (-) [1,226.51]	1,131.91 (354.51) [0]
308	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [6/2021]	393.98 (-) [393.98]	350.81 (0.00) [15]
309	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-)	2,288.00 (-)	866.16 (2,682.11)

			[12/2023]	[4,970.11]	[21]
310	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (-) [12/2023]	1,973.00 (-) [2,135.34]	351.35 (162.34) [33]
311	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [3/2022]	3,055.00 (-) [3,055.15]	2,431.72 (0.15) [42]
312	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2023]	1,160.00 (-) [1,160.83]	902.85 (0.83) [36]
313	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
314	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2021]	1,402.02 (-) [1,300.00]	1,294.72 (-102.02) [21]
	<u>Road Transport And Highways</u>				
315	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	299.11 (231.09) [-]
316	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
317	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	439.27 (0.00) [0]
318	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [3/2021]	291.05 (-) [291.05]	200.71 (0.00) [-]
319	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (6/2021) [6/2021]	335.32 (-) [335.32]	269.15 (0.00) [48]
320	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION	3/2016	9/2016 (10/2020) [10/2020]	491.52 (512.77) [491.52]	474.52 (0.00) [0]
321	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (6/2021) [6/2021]	476.20 (543.73) [544.00]	400.38 (67.80) [57]
322	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (6/2021) [6/2021]	496.02 (-) [496.02]	240.11 (0.00) [75]
323	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (6/2021) [6/2021]	497.14 (572.66) [572.66]	270.56 (75.52) [58]
324	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (6/2021) [6/2021]	624.98 (731.50) [731.50]	416.16 (106.52) [56]
325	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (6/2021) [6/2021]	452.94 (435.61) [435.61]	94.34 (-17.33) [59]
326	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (3/2021) [3/2021]	423.79 (-) [423.79]	273.27 (0.00) [38]
327	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (5/2020) [5/2020]	485.44 (-) [485.44]	447.13 (0.00) [0]
328	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (6/2021) [6/2021]	188.80 (-) [188.80]	78.69 (0.00) [25]
329	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (6/2021)	379.16 (-)	272.43 (0.00)

			[6/2021]	[379.16]	[43]
	<u>Steel</u>				
330	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2021) [7/2021]	15,525.00 (21,940.00) [21,940.00]	18,486.77 (6,415.00) [74]
331	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (-) [6/2023]	2,907.00 (-) [2,907.00]	254.56 (0.00) [0]
332	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	31.60 (0.00) [0]
	<u>Urban Development</u>				
333	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO	5/2019	9/2020 (-) [0/0]	299.97 (-) [299.97]	0.29 (0.00) [0]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
334	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [5/2021]	303.80 (-) [303.80]	115.88 (0.00) [13]
	<u>Commerce</u>				
335	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [0/0]	302.64 (-) [302.64]	60.00 (0.00) [0]
	<u>Dpiit</u>				
336	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [12/2021]	4,773.00 (-) [5,178.00]	2,432.15 (405.00) [24]
	<u>Health And Family Welfare</u>				
337	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [3/2021]	204.44 (-) [250.00]	233.39 (45.56) [46]
338	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
339	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [6/2021]	156.56 (-) [190.34]	143.04 (33.78) [-]
340	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [5/2021]	414.11 (-) [499.23]	488.22 (85.12) [90]
	<u>Heavy Industry</u>				
341	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [0/0]	1,554.00 (-) [900.00]	815.00 (-654.00) [0]
	<u>Home Affairs</u>				
342	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ RAF	6/2019	7/2022 (-) [7/2022]	277.35 (-) [277.35]	5.30 (0.00) [0]
343	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [12/2021]	1,219.21 (-) [2,000.00]	906.04 (780.79) [26]
	<u>Power</u>				
344	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [6/2021]	271.90 (-) [271.90]	240.96 (0.00) [19]
345	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (9/2021) [6/2021]	1,394.52 (-) [1,394.52]	532.79 (0.00) [49]
	<u>Railways</u>				
346	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/	295.68	127.91

			(-) [9/2023]	(-) [419.00]	(123.32) [-]
347	GRADE SEPERATOR AT DAYABASTI	4/1999	/	156.65	111.51
			(-) [3/2024]	(-) [359.00]	(202.35) [-]
	<u>Road Transport And Highways</u>				
348	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019 (-) [0/0]	269.69 (-) [269.69]	0.00 (0.00) [0]
	<u>Rural Development</u>				
349	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [7/2021]	361.60 (-) [361.60]	12.44 (0.00) [0]
	<u>Telecommunications</u>				
350	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	3/2018 (-) [6/2021]	248.20 (-) [248.20]	133.09 (0.00) [39]
	<u>Urban Development</u>				
351	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG	2/2020	11/2020 (-) [11/2020]	532.00 (-) [532.00]	150.00 (0.00) [0]
352	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2021) [12/2021]	197.33 (-) [197.33]	106.16 (0.00) [32]
353	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	11/2020 (-) [0/0]	218.72 (-) [218.72]	126.16 (0.00) [0]
354	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	812.00 (0.00) [0]
355	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	1,248.28 (0.00) [0]
356	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (-) [9/2021]	565.00 (-) [565.00]	511.60 (0.00) [9]
357	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [9/2021]	38,585.00 (-) [38,585.00]	39,838.90 (0.00) [66]
358	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [0/0]	238.56 (-) [238.56]	157.67 (0.00) [0]
359	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [0/0]	4,264.00 (-) [4,720.73]	4,683.08 (456.73) [0]
360	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [12/2024]	1,180.00 (-) [1,100.80]	35.63 (-79.20) [41]
361	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (-) [3/2022]	392.00 (-) [392.00]	73.79 (0.00) [19]
362	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [3/2022]	1,128.00 (-) [1,128.00]	22.00 (0.00) [0]
363	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (7/2021) [7/2021]	422.00 (-) [422.00]	69.02 (0.00) [4]
364	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/	2,694.00	679.91
			(-) [12/2022]	(-) [2,694.00]	(0.00) [-]
	<u>Water Resources</u>				

365	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
366	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [6/2021]	515.07 (-) [515.07]	314.33 (0.00) [5]
367	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	160.36 (0.00) [0]
368	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	64.03 (0.00) [12]
369	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	129.67 (0.00) [10]
	GOA				
	Health And Family Welfare				
370	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [1/2021]	249.01 (-) [249.07]	231.05 (0.06) [0]
	Human Resource Development				
371	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [0/0]	303.90 (-) [303.90]	16.50 (0.00) [0]
	Road Transport And Highways				
372	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	219.47 (10.43) [0]
373	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	91.39 (0.00) [0]
374	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	478.46 (0.00) [0]
375	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	310.72 (0.00) [0]
376	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	290.64 (0.00) [0]
377	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [0/0]	852.67 (-) [852.67]	138.14 (0.00) [0]
378	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [0/0]	634.32 (-) [634.32]	278.30 (0.00) [0]
379	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	336.25 (0.00) [0]
380	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	205.20 (0.00) [0]
	GUJARAT				
	Atomic Energy				
381	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [2/2022]	11,459.00 (-) [16,580.00]	16,488.00 (5,121.00) [74]
	Civil Aviation				
382	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022 (-) [8/2022]	1,405.00 (-) [1,405.00]	199.55 (0.00) [0]

	Petroleum				
383	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	143.52 (0.00) [0]
384	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (5/2023) [5/2023]	588.20 (730.20) [730.20]	77.30 (142.00) [-]
385	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023 (-) [8/2023]	1,614.00 (-) [1,614.00]	0.00 (0.00) [0]
386	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [6/2021]	327.78 (-) [200.00]	197.30 (-127.78) [38]
387	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2021) [10/2021]	906.00 (-) [906.00]	272.27 (0.00) [20]
388	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021 (-) [12/2021]	403.00 (-) [403.00]	101.64 (0.00) [0]
389	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024 (-) [9/2024]	18,936.00 (-) [18,936.00]	685.07 (0.00) [0]
390	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022 (-) [8/2022]	444.87 (-) [444.87]	87.19 (0.00) [0]
391	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [970.30]	827.75 (-192.26) [0]
392	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (-) [12/2022]	1,378.00 (-) [1,378.00]	24.66 (0.00) [0]
393	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [12/2021]	225.54 (247.90) [247.90]	40.10 (22.36) [10]
	Power				
394	KAWAS SOLAR 56 MW	8/2020	10/2021 (-) [10/2021]	261.80 (-) [261.80]	0.00 (0.00) [0]
395	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (11/2020) [9/2020]	193.14 (-) [193.14]	123.36 (0.00) [0]
396	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (11/2020) [9/2020]	175.64 (-) [175.64]	122.47 (0.00) [0]
	Railways				
397	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,500.00]	1,497.74 (524.38) [0]
398	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2024) [3/2024]	829.74 (1,959.74) [1,959.74]	1,799.00 (1,130.00) [48]
399	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
400	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (10/2021) [10/2021]	551.51 (890.76) [890.76]	745.11 (339.25) [31]
401	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2023) [3/2023]	318.24 (411.62) [411.62]	126.05 (93.38) [132]
402	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION	4/2017	3/2020	691.84	719.56

	UPTO KEVADIYA(32.68KM) =49.75KM		(2/2021) [2/2021]	(1,017.91) [1,017.91]	(326.07) [0]
403	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [872.65]	800.30 (228.27) [0]
404	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
405	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2024) [3/2024]	844.10 (844.10) [844.10]	186.59 (0.00) [-]
406	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
407	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
408	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,868.89]	1,831.45 (320.23) [3]
409	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2023) [3/2023]	320.66 (1,378.11) [1,378.11]	540.09 (1,057.45) [48]
410	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,002.39) [1,002.39]	653.86 (0.00) [21]
411	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (12/2021) [12/2021]	1,037.15 (1,389.05) [1,389.05]	1,125.73 (351.90) [9]
412	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	Road Transport And Highways				
413	2-LANE WITH PAVED SHOULDERS OF GADU- PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	303.96 (0.00) [0]
414	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH- 8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	248.88 (0.00) [0]
415	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [2/2021]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [0]
416	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,669.71 (0.00) [0]
417	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [3/2021]	364.56 (-) [392.00]	353.42 (27.44) [-]
418	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	37.17 (0.00) [0]
419	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	584.17 (0.00) [-]
420	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [6/2021]	2,702.05 (-) [2,043.00]	1,327.65 (-659.05) [-]
421	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	131.34 (0.00) [0]
422	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN	8/2017	3/2018	962.43	235.26

	DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU		(-) [0/0]	(-) [962.43]	(0.00) [0]
423	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	447.81 (0.00) [0]
424	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	715.10 (0.00) [0]
425	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	503.45 (0.00) [0]
426	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	203.40 (0.00) [0]
427	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	450.54 (0.00) [0]
428	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.89 (0.00) [0]
429	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
430	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [0/0]	953.88 (-) [953.88]	976.79 (0.00) [0]
431	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (-) [1,449.00]	394.36 (396.79) [0]
432	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [0]
433	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	134.77 (0.00) [0]
434	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	128.31 (0.00) [0]
435	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	288.07 (0.00) [0]
436	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
	<u>Urban Development</u>				
437	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [8/2022]	10,773.00 (-) [12,787.00]	8,706.79 (2,014.00) [44]
438	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	61.94 (0.00) [0]
439	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	18.27 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
440	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [4/2021]	215.92 (-) [215.92]	167.49 (0.00) [17]
	<u>Health And Family Welfare</u>				
441	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI	9/2014	3/2018	505.58	586.96

	JHAJJAR		(-) [9/2019]	(-) [585.00]	(79.42) [0]
	<u>Home Affairs</u>				
442	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	1/2020	10/2023 (-) [10/2023]	166.98 (167.00) [166.98]	0.00 (0.00) [0]
443	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96	1/2020	5/2022 (-) [5/2022]	166.98 (-) [166.98]	0.29 (0.00) [0]
	<u>Petroleum</u>				
444	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [3/2022]	909.00 (-) [909.00]	301.41 (0.00) [14]
445	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (8/2021) [8/2021]	206.63 (-) [206.63]	89.71 (0.00) [18]
446	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (2/2027) [2/2027]	520.00 (-) [520.00]	91.57 (0.00) [5]
447	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [3/2022]	164.69 (-) [164.69]	13.16 (0.00) [8]
448	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (6/2021) [6/2021]	255.00 (300.00) [300.00]	269.18 (45.00) [7]
449	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (2/2022) [2/2022]	598.00 (-) [598.00]	286.33 (0.00) [24]
450	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [7/2022]	278.60 (-) [278.60]	44.73 (0.00) [13]
451	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (4/2022) [4/2022]	1,636.00 (-) [1,636.00]	710.21 (0.00) [20]
452	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [10/2021]	1,255.00 (-) [1,255.00]	179.69 (0.00) [0]
453	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (-) [2,281.94]	431.31 (0.00) [7]
454	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (5/2021) [6/2021]	286.42 (327.01) [327.01]	181.70 (40.59) [10]
	<u>Railways</u>				
455	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2021]	346.32 (-) [346.32]	316.04 (0.00) [24]
456	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [6/2021]	287.00 (-) [893.45]	705.53 (606.45) [114]
	<u>Road Transport And Highways</u>				
457	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [507.70]	496.22 (-95.25) [0]
458	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	516.32 (-37.12) [0]
459	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (5/2021) [5/2021]	639.79 (-) [552.90]	597.77 (-86.89) [14]
460	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019	2,128.72	1,070.00

			(-) [9/2021]	(-) [2,128.72]	(0.00) [29]
461	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (-) [0/0]	276.01 (-) [276.01]	187.39 (0.00) [0]
462	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [2/2021]	247.25 (-) [247.25]	178.64 (0.00) [0]
463	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [0/0]	248.97 (-) [248.97]	270.65 (0.00) [0]
464	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (6/2021) [12/2020]	1,484.30 (-) [1,484.30]	444.49 (0.00) [0]
465	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [0/0]	1,004.67 (-) [813.45]	577.21 (-191.22) [0]
466	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]
467	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (1/2020) [0/0]	996.65 (-) [996.65]	567.52 (0.00) [0]
468	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (1/2020) [0/0]	1,243.45 (-) [1,243.45]	659.79 (0.00) [0]
469	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (6/2020) [0/0]	889.36 (-) [889.36]	438.38 (0.00) [0]
470	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (2/2020) [0/0]	1,018.79 (-) [1,018.79]	468.24 (0.00) [0]
471	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (2/2020) [0/0]	1,051.91 (-) [1,051.91]	526.09 (0.00) [0]
472	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (1/2020) [0/0]	1,120.06 (-) [1,120.06]	501.73 (0.00) [0]
473	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (1/2020) [0/0]	1,137.42 (-) [1,137.42]	690.88 (0.00) [0]
474	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (1/2020) [0/0]	1,033.19 (-) [1,033.19]	604.45 (0.00) [0]
475	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [0/0]	1,108.00 (-) [2,967.50]	3,996.01 (1,859.50) [0]
476	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (1/2020) [0/0]	551.58 (-) [551.58]	306.06 (0.00) [0]
477	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (1/2020) [0/0]	275.12 (-) [275.12]	169.48 (0.00) [0]
478	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING	3/2018	/ (1/2020) [0/0]	307.79 (-) [307.79]	197.30 (0.00) [0]
479	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (1/2020) [0/0]	181.78 (-) [181.78]	129.29 (0.00) [0]
480	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM	3/2018	/ (1/2020) [0/0]	198.05 (-) [0/0]	117.51 (0.00) [0/0]

	DESIGN CHAIN		[0/0]	[198.05]	[0]
481	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [7/2021]	795.50 (-) [799.30]	213.17 (3.80) [-]
482	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [7/2021]	634.70 (-) [931.21]	268.17 (296.51) [-]
	HIMACHAL PRADESH				
	Health And Family Welfare				
483	AIIMS BILASPUR	4/2018	9/2021 (-) [9/2021]	1,351.00 (-) [1,471.00]	682.54 (120.00) [0]
484	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [5/2022]	260.00 (-) [260.00]	25.38 (0.00) [11]
	Human Resource Development				
485	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [0/0]	270.83 (-) [270.83]	226.16 (0.00) [0]
486	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022 (-) [6/2022]	392.51 (-) [392.51]	35.88 (0.00) [0]
	Power				
487	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	417.95 (0.00) [0]
488	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (7/2022) [7/2022]	3,919.59 (9,897.59) [9,897.59]	8,866.70 (5,978.00) [154]
	Railways				
489	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2025]	2,966.99 (-) [6,753.42]	926.84 (3,786.43) [-12]
	Road Transport And Highways				
490	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [0/0]	273.20 (-) [273.20]	667.10 (0.00) [0]
491	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	827.64 (0.00) [15]
492	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,960.92 (0.00) [0]
493	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [0/0]	934.46 (-) [934.46]	697.33 (0.00) [0]
494	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [5/2021]	478.74 (-) [478.74]	127.42 (0.00) [-]
495	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	663.25 (0.00) [0]
496	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [8/2020]	447.75 (-) [447.75]	1,160.74 (0.00) [0]
497	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	271.06 (0.00) [0]
	JAMMU AND KASHMIR				
	Civil Aviation				
498	CONSTRUCTION OF TERMINAL BUILDING AND	7/2018	9/2021	346.27	51.11

	ASSOCIATED WORKS AT LEH AIRPORT		(-) [9/2021]	(-) [480.33]	(134.06) [0]
	<u>Health And Family Welfare</u>				
499	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	0.00 (0.00) [-16]
500	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
501	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	199.99 (0.00) [0]
	<u>Human Resource Development</u>				
502	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (-) [676.00]	0.00 (0.00) [0]
503	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (-) [7/2022]	329.00 (-) [329.00]	0.00 (0.00) [0]
	<u>Power</u>				
504	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [7/2025]	8,112.12 (-) [8,112.12]	1,706.23 (0.00) [63]
	<u>Railways</u>				
505	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2022]	2,500.00 (-) [27,949.00]	23,132.28 (25,449.00) [241]
	<u>Road Transport And Highways</u>				
506	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	63.83 (0.00) [0]
507	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	840.31 (-132.75) [0]
508	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	29.22 (0.00) [0]
509	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	816.46 (0.00) [0]
510	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,615.66 (0.00) [0]
511	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,651.77 (0.00) [0]
512	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,709.65 (360.00) [0]
513	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,107.29 (0.00) [0]
514	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [10/2020]	1,100.70 (-) [1,100.70]	2,922.79 (0.00) [0]
515	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [4/2022]	228.39 (-) [228.39]	0.00 (0.00) [0]
516	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (-) [4/2022]	210.79 (-) [210.79]	0.00 (0.00) [0]

517	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	37.58 (0.00) [0]
518	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	151.80 (0.00) [0]
519	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	78.40 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
520	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	98.11 (0.00) [0]
521	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2022]	163.51 (-) [163.51]	107.27 (0.00) [132]
522	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	163.16 (0.00) [0]
523	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2022]	162.46 (-) [162.46]	98.21 (0.00) [96]
524	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [7/2021]	289.45 (-) [289.45]	281.27 (0.00) [86]
525	MAGADH EXPANSION OC(51 MTY)	8/2008	7/2012 (3/2025) [3/2025]	6,964.33 (6,964.33) [706.40]	706.20 (-6,257.93) [152]
526	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [3/2022]	1,230.27 (-) [1,230.27]	461.54 (0.00) [83]
527	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [4/2023]	339.88 (-) [339.88]	23.47 (0.00) [108]
528	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.87 (0.00) [0]
529	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	277.47 (0.00) [0]
530	PACHWARA SOUTH COAL BLOCK	7/2013	8/2022 (-) [9/2023]	1,795.01 (-) [1,795.01]	34.62 (0.00) [13]
531	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [6/2022]	243.00 (334.27) [334.27]	18.35 (91.27) [50]
532	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2020]	269.82 (-) [269.82]	208.76 (0.00) [0]
533	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2022]	510.85 (-) [510.85]	426.30 (0.00) [72]
534	RECAST EPR AMRAPALI OC	2/2012	3/2020 (3/2024) [3/2024]	4,983.58 (4,983.58) [4,983.58]	245.85 (0.00) [48]
535	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	39.79 (0.00) [0]
	<u>Human Resource Development</u>				
536	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT	9/2012	3/2016	171.86	111.29

	ISM DHANBAD		(-) [6/2021]	(-) [171.86]	(0.00) [63]
	<u>Petroleum</u>				
537	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (9/2021) [9/2021]	161.50 (-) [161.50]	75.31 (0.00) [15]
538	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	109.54 (0.00) [0]
539	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	92.04 (0.00) [0]
540	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	667.03 (314.52) [-12]
541	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	106.83 (0.00) [0]
	<u>Power</u>				
542	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [10/2022]	14,366.58 (-) [15,389.42]	11,672.15 (1,022.84) [40]
543	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,380.97 (314.04) [0]
544	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [9/2024]	18,668.00 (-) [17,112.00]	4,295.79 (-1,556.00) [18]
	<u>Railways</u>				
545	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2023]	1,724.20 (-) [1,724.20]	748.34 (0.00) [33]
546	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [3/2022]	348.23 (-) [348.23]	340.60 (0.00) [12]
547	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	3/1999	/ (-) [3/2022]	1,033.07 (-) [3,550.00]	3,528.48 (2,516.93) [-]
548	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2023]	459.91 (-) [1,625.87]	767.07 (1,165.96) [-]
549	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (12/2018) [6/2021]	258.20 (358.68) [358.68]	302.95 (100.48) [30]
550	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (-) [8/2020]	148.77 (-) [377.00]	195.84 (228.23) [0]
	<u>Road Transport And Highways</u>				
551	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [3/2021]	1,005.08 (-) [1,005.08]	0.00 (0.00) [-]
552	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [10/2019]	997.15 (-) [1,115.95]	975.08 (118.80) [0]
553	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	72.53 (2.71) [0]
554	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [0/0]	323.72 (-) [336.60]	312.79 (12.88) [0]
555	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015	1,479.00	740.26

			(-) [0/0]	(-) [1,479.00]	(0.00) [0]
556	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [1/2021]	212.99 (-) [212.99]	155.56 (0.00) [0]
557	SIX LANEING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	366.61 (0.00) [0]
558	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (486.00) [486.00]	432.16 (27.97) [0]
559	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	47.95 (0.00) [0]
	<u>Steel</u>				
560	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [12/2021]	1,034.01 (-) [1,034.01]	536.50 (0.00) [50]
561	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (5/2021) [5/2021]	262.87 (-) [262.87]	185.40 (0.00) [23]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
562	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [6/2021]	246.31 (-) [246.31]	123.83 (0.00) [16]
	<u>Human Resource Development</u>				
563	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (-) [9/2022]	851.00 (851.00) [851.00]	26.10 (0.00) [6]
	<u>Petroleum</u>				
564	BSVI UPGRADATION	9/2016	12/2019 (4/2021) [10/2021]	1,810.00 (1,810.00) [1,810.00]	1,607.38 (0.00) [22]
565	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	147.24 (0.00) [0]
566	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (-) [6/2023]	200.00 (-) [200.00]	2.09 (0.00) [0]
567	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	875.03 (0.00) [0]
568	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [5/2021]	206.26 (-) [206.26]	129.96 (0.00) [2]
569	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [6/2021]	581.00 (637.00) [637.00]	466.87 (56.00) [15]
570	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (-) [11/2021]	380.00 (-) [380.00]	222.20 (0.00) [0]
	<u>Power</u>				
571	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (2/2021) [2/2021]	445.89 (675.73) [675.73]	463.08 (229.84) [0]
	<u>Railways</u>				
572	ARSIKERE-TUMKUR	3/2015	3/2020 (6/2021) [6/2021]	578.00 (-) [783.00]	620.29 (205.00) [15]
573	BAGALKOT-KUDACHI NL	4/2010	3/2016	986.30	312.23

			(-) [12/2023]	(-) [986.30]	(0.00) [93]
574	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
575	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [327.25]	0.00 (0.00) [-]
576	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [558.00]	0.00 (0.00) [-]
577	GADAG-WADI NL	4/2013	12/2018 (-) [6/2025]	2,841.84 (-) [2,841.84]	304.83 (0.00) [78]
578	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [12/2022]	2,127.00 (-) [3,000.00]	2,208.46 (873.00) [-3]
579	HUBLI- CHIKJAJUR	3/2015	3/2020 (3/2023) [3/2023]	1,156.94 (-) [1,656.00]	1,160.49 (499.06) [36]
580	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [3,911.65]	157.01 (1,596.65) [-]
581	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (3/2025) [3/2025]	644.78 (-) [998.00]	463.45 (353.22) [96]
582	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	35.29 (0.00) [93]
583	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
584	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
585	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [1,967.00]	71.56 (165.99) [-]
586	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (-) [348.85]	0.36 (0.00) [-]
	Road Transport And Highways				
587	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (1/2021) [12/2021]	1,167.42 (-) [870.00]	336.58 (-297.42) [33]
588	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	273.86 (0.00) [0]
589	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [0]
590	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (3/2022) [3/2022]	701.40 (-) [701.40]	125.51 (0.00) [36]
591	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [0]
592	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]
593	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE	5/2018	5/2018	171.60	0.86

	FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT		(-) [0/0]	(-) [171.60]	(0.00) [0]
594	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [0/0]	1,388.00 (-) [1,388.00]	1,287.50 (0.00) [0]
595	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [12/2020]	1,664.20 (-) [1,664.20]	981.12 (0.00) [0]
596	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [0/0]	946.00 (-) [946.00]	818.53 (0.00) [0]
597	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	326.88 (0.00) [0]
598	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
599	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
600	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
601	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
602	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,434.00]	1,150.56 (440.84) [0]
603	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.58 (-) [1,177.00]	912.41 (345.42) [0]
604	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,244.98 (272.20) [0]
605	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,088.59 (404.66) [-]
606	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
607	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
608	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [0/0]	950.69 (-) [1,108.00]	1,429.25 (157.31) [0]
609	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
610	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
611	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
612	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
613	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-	9/2017	10/2018 (-)	191.60 (-)	26.24 (0.00)

	HULIYAR		[0/0]	[191.60]	[0]
614	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	130.00 (0.00) [0]
615	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
616	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
617	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
618	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
619	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
620	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	<u>Urban Development</u>				
621	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (3/2021) [6/2024]	26,405.14 (30,695.12) [30,695.12]	17,021.86 (4,289.98) [64]
	<u>KERALA</u>				
	<u>Health And Family Welfare</u>				
622	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	43.43 (0.00) [21]
	<u>Human Resource Development</u>				
623	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [6/2022]	753.63 (-) [753.63]	58.47 (0.00) [15]
624	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [0/0]	165.23 (-) [165.23]	118.52 (0.00) [0]
	<u>Petroleum</u>				
625	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	725.00 (395.24) [32]
626	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [3/2022]	607.06 (1,236.00) [1,236.00]	393.38 (628.94) [53]
627	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (3/2021) [5/2021]	3,313.00 (-) [3,288.96]	2,925.17 (-24.04) [15]
628	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [5/2021]	4,588.29 (-) [5,245.96]	4,977.00 (657.67) [33]
629	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	377.64 (0.00) [0]
	<u>Power</u>				
630	KAYAMKULAM SOLAR 70 MW	9/2019	6/2021 (10/2021) [10/2021]	403.62 (-) [403.62]	46.03 (0.00) [4]
	<u>Railways</u>				
631	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-)	1,566.00 (-)	262.68 (1,249.62)

			[0/0]	[2,815.62]	[0]
632	ERNAKULAM-KUMBALAM	4/2010	/	189.24	6.73
			(-)	(-)	(85.97)
			[0/0]	[275.21]	[0]
633	KUMBALAM-TURAVUR	4/2011	/	252.96	8.50
			(-)	(-)	(116.59)
			[0/0]	[369.55]	[0]
634	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016	550.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[550.00]	[0]
635	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/	1,431.90	198.81
			(-)	(-)	(0.00)
			[0/0]	[1,431.90]	[0]
636	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/	1,000.00	0.81
			(-)	(-)	(246.00)
			[0/0]	[1,246.00]	[0]
	<u>Road Transport And Highways</u>				
637	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/	845.24	889.83
			(1/2020)	(-)	(95.76)
			[1/2020]	[941.00]	[0]
638	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018	804.97	522.80
			(10/2020)	(-)	(0.00)
			[3/2021]	[804.97]	[33]
639	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017	1,124.11	527.67
			(-)	(-)	(108.65)
			[5/2021]	[1,232.76]	[44]
640	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/	1,424.77	14.19
			(-)	(-)	(428.65)
			[0/0]	[1,853.42]	[0]
641	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017	255.75	290.12
			(-)	(348.00)	(92.68)
			[0/0]	[348.43]	[0]
642	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012	617.00	943.17
			(-)	(-)	(0.00)
			[0/0]	[617.00]	[0]
	<u>Urban Development</u>				
643	KOCHI METRO RAIL PROJECT	7/2012	7/2017	5,181.79	6,059.17
			(9/2020)	(6,218.14)	(1,036.35)
			[9/2020]	[6,218.14]	[0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
644	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021	412.24	0.00
			(-)	(-)	(0.00)
			[6/2021]	[412.24]	[0]
	<u>Coal</u>				
645	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021	869.44	121.28
			(-)	(-)	(0.00)
			[3/2022]	[869.44]	[12]
646	AMRITDHARA OC PROJECT	2/2015	3/2023	481.60	0.00
			(-)	(-)	(0.00)
			[3/2023]	[481.60]	[0]
647	BATURA HIGHWALL PROJECT	7/2015	3/2022	231.92	1.09
			(-)	(-)	(0.00)
			[3/2022]	[231.92]	[0]
648	BLOCK-B EXPANSION OPENCASE PROJECT	7/2019	3/2023	998.71	0.00
			(-)	(-)	(0.00)
			[3/2023]	[998.71]	[0]
649	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022	1,255.17	152.16
			(-)	(-)	(0.00)
			[3/2023]	[1,255.17]	[12]
650	GANDHIGRAM UG MINE	8/2019	3/2026	414.16	0.87

			(-) [3/2026]	(-) [414.16]	(0.00) [0]
651	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2022]	1,783.09 (-) [1,783.09]	622.66 (0.00) [12]
652	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	64.12 (0.00) [36]
653	NIGAHI EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
654	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (4/2024) [3/2021]	357.80 (-) [357.80]	100.63 (0.00) [0]
655	RPR FOR JAMUNIA UG (0.90 MTY)	7/2016	3/2022 (-) [3/2026]	281.25 (-) [281.25]	20.99 (0.00) [48]
656	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
657	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
658	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (9/2021) [9/2021]	236.00 (293.00) [293.00]	155.76 (57.00) [15]
	<u>Power</u>				
659	AMELIA COAL MINE	1/2017	9/2020 (8/2022) [8/2022]	2,104.21 (-) [1,587.16]	495.34 (-517.05) [23]
660	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (10/2020) [2/2021]	11,638.55 (15,105.22) [15,105.22]	13,657.43 (3,466.67) [0]
661	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [0/0]	9,870.51 (-) [11,148.86]	10,019.31 (1,278.35) [0]
	<u>Railways</u>				
662	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2023]	1,370.00 (-) [1,370.94]	470.49 (0.94) [24]
663	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2021]	1,485.85 (-) [1,835.83]	1,571.35 (349.98) [12]
664	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,413.76]	1,416.77 (1,029.97) [0]
665	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [12/2021]	585.93 (-) [1,268.32]	941.56 (682.39) [34]
666	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [603.69]	254.73 (-96.31) [33]
667	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,763.93 (-) [1,762.94]	1,153.73 (-0.99) [36]
668	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2023]	582.13 (1,247.64) [1,247.64]	296.52 (665.51) [12]
669	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-)	2,478.23 (-)	477.93 (0.00)

			[3/2023]	[2,478.23]	[12]
670	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [0/0]	174.00 (-) [174.00]	172.08 (0.00) [0]
671	RAMGANJMUUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2029) [3/2023]	424.60 (-) [2,909.99]	1,229.79 (2,485.39) [24]
672	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2024) [3/2024]	3,503.69 (5,912.40) [5,912.40]	2,161.74 (2,408.71) [24]
Road Transport And Highways					
673	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [1/2021]	191.21 (-) [191.21]	127.13 (0.00) [0]
674	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (3/2021) [4/2021]	249.05 (-) [249.05]	195.13 (0.00) [33]
675	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	308.11 (0.00) [0]
676	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [8/2021]	950.27 (-) [950.27]	224.81 (0.00) [-]
677	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [6/2021]	392.33 (428.55) [428.55]	351.92 (36.22) [39]
678	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	195.73 (0.00) [0]
679	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [204.65]	221.79 (-169.75) [0]
680	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	648.40 (0.00) [0]
681	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
682	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (3/2021) [6/2021]	390.51 (-) [390.51]	257.01 (0.00) [-]
683	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	76.17 (183.02) [-]
684	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [12/2021]	743.88 (-) [743.89]	263.60 (0.01) [-]
685	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [2/2022]	1,094.97 (-) [1,094.97]	425.85 (0.00) [-]
686	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [0/0]	217.96 (-) [884.00]	193.30 (666.04) [0]
687	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [6/2021]	205.05 (-) [205.05]	123.20 (0.00) [51]
688	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (11/2021) [11/2021]	264.50 (-) [264.50]	85.70 (0.00) [8]
689	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM	1/2018	/ (-)	960.24 (-)	738.74 (0.00)

	624.480 TO		[0/0]	[960.24]	[0]
690	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
691	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
692	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [6/2015]	928.83 (-) [928.83]	824.83 (0.00) [0]
693	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [5/2020]	794.30 (679.94) [691.38]	669.35 (-102.92) [0]
694	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [5/2020]	795.76 (686.13) [686.13]	669.94 (-109.63) [0]
695	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	771.23 (0.00) [0]
696	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [0/0]	639.97 (-) [639.97]	473.85 (0.00) [0]
697	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [7/2018]	770.73 (-) [770.73]	350.68 (0.00) [0]
698	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (4/2021) [4/2021]	957.54 (-) [957.54]	756.69 (0.00) [14]
699	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [4/2021]	497.05 (-) [881.05]	754.27 (384.00) [47]
700	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
701	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
702	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (1/2021) [6/2021]	628.45 (-) [628.45]	439.63 (0.00) [17]
703	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [3/2021]	410.72 (-) [410.72]	390.00 (0.00) [71]
704	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [12/2021]	990.97 (-) [990.97]	537.28 (0.00) [24]
705	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [5/2022]	1,047.00 (-) [1,047.00]	349.24 (0.00) [24]
706	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [4/2022]	847.00 (-) [847.00]	333.22 (0.00) [25]
707	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [0/0]	996.27 (-) [996.27]	330.36 (0.00) [0]
708	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [6/2021]	169.63 (-) [169.63]	46.52 (0.00) [39]
709	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [0/0]	178.23 (-) [178.23]	122.99 (0.00) [0]

710	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (9/2020) [11/2020]	287.34 (-) [287.34]	194.85 (0.00) [0]
711	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (4/2021) [4/2021]	877.79 (-) [877.79]	687.99 (0.00) [22]
712	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (2/2021) [2/2021]	235.91 (-) [235.91]	176.23 (0.00) [0]
713	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (5/2021) [5/2021]	809.16 (-) [809.16]	573.85 (0.00) [34]
714	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
715	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [10/2021]	954.43 (-) [1,191.51]	235.61 (237.08) [73]
716	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (6/2021) [6/2021]	511.83 (-) [511.83]	375.50 (0.00) [46]
717	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (3/2021) [6/2021]	254.17 (-) [254.17]	164.68 (0.00) [40]
718	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [6/2021]	233.04 (-) [233.04]	158.22 (0.00) [39]
719	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (12/2020) [6/2021]	279.44 (-) [279.44]	156.14 (0.00) [39]
720	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [3/2021]	166.21 (-) [173.41]	141.65 (7.20) [31]
721	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (6/2021) [6/2021]	184.62 (-) [184.62]	117.94 (0.00) [40]
722	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [9/2021]	214.69 (-) [214.69]	69.34 (0.00) [42]
723	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (9/2021) [3/2021]	217.22 (-) [226.88]	170.96 (9.66) [31]
724	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [6/2021]	162.56 (-) [162.56]	129.98 (0.00) [39]
725	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (6/2021) [6/2021]	373.82 (-) [373.82]	197.04 (0.00) [21]
	<u>Urban Development</u>				
726	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	126.50 (0.00) [0]
727	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	117.53 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
728	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	475.39 (-) [475.39]	88.11 (0.00) [0]
	<u>Coal</u>				

729	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	121.25 (44.53) [12]
730	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2022]	198.68 (-) [325.18]	246.55 (126.50) [36]
731	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	251.34 (0.00) [0]
732	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	281.92 (0.00) [0]
733	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [3/2021]	252.71 (-) [252.71]	99.77 (0.00) [0]
734	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	85.82 (221.74) [0]
735	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2026]	304.52 (-) [304.52]	142.28 (0.00) [84]
736	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	330.34 (0.00) [0]
737	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2025]	295.56 (-) [295.56]	160.23 (0.00) [72]
738	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	3/2020 (-) [3/2027]	1,184.33 (-) [1,184.33]	368.56 (0.00) [84]
739	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	11/2015	3/2021 (-) [3/2024]	313.34 (-) [313.34]	141.08 (0.00) [36]
740	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	11/2015	3/2020 (-) [3/2026]	851.60 (-) [826.80]	194.28 (-24.80) [72]
741	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	135.36 (0.00) [0]
742	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	318.14 (-) [318.14]	211.41 (0.00) [0]
	Fertilisers				
743	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (3/2021) [5/2021]	426.72 (-) [426.72]	325.19 (0.00) [13]
	Health And Family Welfare				
744	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [6/2021]	582.99 (-) [582.99]	470.24 (0.00) [-]
745	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	256.37 (0.00) [0]
	Human Resource Development				
746	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [6/2021]	223.37 (-) [223.37]	61.35 (0.00) [11]
	Petroleum				
747	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (12/2021) [9/2021]	249.26 (-) [249.26]	130.48 (0.00) [15]

748	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	261.00 (-) [261.00]	157.94 (0.00) [3]
749	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	146.57 (0.00) [3]
750	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	156.30 (0.00) [9]
751	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2020) [3/2021]	861.79 (1,846.46) [1,846.46]	1,550.87 (984.67) [94]
752	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,203.71]	1,595.82 (-88.75) [0]
753	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,475.92) [3,596.00]	3,507.79 (-410.83) [0]
754	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-) [12/2021]	640.00 (-) [640.00]	321.21 (0.00) [0]
755	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2022]	2,494.68 (-) [2,354.72]	1,302.43 (-139.96) [0]
756	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R	8/2020	3/2023 (-) [3/2023]	697.00 (-) [697.00]	77.84 (0.00) [0]
757	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (-) [2/2022]	1,945.00 (-) [1,945.00]	1,525.53 (0.00) [0]
758	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2021) [5/2021]	3,190.69 (3,375.90) [3,375.90]	2,775.79 (185.21) [37]
759	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (3/2021) [4/2021]	449.58 (-) [449.58]	396.13 (0.00) [16]
760	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	1,005.13 (747.87) [14]
761	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (-) [5/2021]	3,660.71 (3,740.05) [3,740.05]	2,521.33 (79.34) [0]
762	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [0/0]	4,199.00 (5,060.00) [5,060.00]	4,486.77 (861.00) [0]
763	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (5/2021) [5/2021]	763.92 (-) [733.86]	637.29 (-30.06) [5]
764	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [3/2021]	282.64 (-) [282.64]	246.11 (0.00) [7]
Power					
765	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
Railways					
766	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [3/2020]	184.06 (-) [315.00]	312.62 (130.94) [0]
767	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-)	2,271.50 (-)	2,648.51 (2,245.99)

			[3/2023]	[4,517.49]	[24]
768	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2022]	495.44 (-) [2,980.41]	1,768.25 (2,484.97) [216]
769	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	445.15 (205.27) [0]
770	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [12/2021]	713.48 (-) [2,725.00]	2,554.71 (2,011.52) [21]
771	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
772	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
773	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	332.19 (0.00) [12]
774	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [1,377.48]	335.23 (584.59) [24]
775	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	244.12 (0.00) [24]
776	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (12/2020) [12/2020]	305.00 (-) [305.00]	269.73 (0.00) [0]
777	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
778	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2021]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [84]
779	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	1,204.21 (0.00) [-12]
780	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
781	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (-) [12/2023]	1,908.51 (-) [3,524.81]	982.38 (1,616.30) [9]
782	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
783	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
784	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
785	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2024]	229.00 (-) [1,096.00]	39.79 (867.00) [36]
786	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	182.65 (0.00) [12]
787	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	408.70 (11.30) [12]

788	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,352.27 (0.00) [0]
789	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	272.55 (0.00) [24]
	Road Transport And Highways				
790	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
791	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
792	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
793	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	440.92 (0.00) [-]
794	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [4/2021]	621.00 (-) [621.00]	591.21 (0.00) [-]
795	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	861.99 (0.00) [0]
796	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [0/0]	744.64 (-) [982.00]	0.00 (237.36) [0]
797	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,048.10]	921.02 (-23.51) [-]
798	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	70.85 (0.00) [24]
799	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [0/0]	1,098.06 (-) [1,160.64]	1,068.76 (62.58) [0]
800	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	585.85 (0.00) [0]
801	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	324.00 (0.00) [0]
802	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [2/2021]	400.25 (-) [400.25]	105.20 (0.00) [0]
803	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (1/2022) [7/2021]	1,064.88 (-) [1,021.00]	296.60 (-43.88) [-]
804	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [11/2020]	1,059.73 (-) [1,071.00]	610.87 (11.27) [0]
805	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [0/0]	1,030.44 (-) [1,065.51]	1,015.76 (35.07) [0]
806	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [0/0]	988.34 (-) [1,043.28]	1,035.00 (54.94) [0]
807	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [6/2021]	505.00 (-) [504.00]	373.68 (-1.00) [37]

808	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [0/0]	422.38 (-) [422.38]	218.78 (0.00) [0]
809	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [0/0]	955.40 (-) [955.40]	446.67 (0.00) [0]
810	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [0/0]	211.42 (-) [211.42]	136.85 (0.00) [0]
811	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	49.38 (0.00) [0]
812	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	197.90 (0.00) [0]
813	AMDNI TO SAONER	1/2017	6/2019 (-) [0/0]	396.91 (397.00) [396.91]	280.56 (0.00) [0]
814	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [0/0]	426.06 (426.00) [426.06]	162.57 (0.00) [0]
815	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [0/0]	309.94 (310.00) [309.94]	181.32 (0.00) [0]
816	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	289.08 (0.00) [0]
817	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	151.11 (0.00) [0]
818	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [0/0]	241.69 (242.00) [241.69]	149.29 (0.00) [0]
819	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	61.53 (0.00) [31]
820	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [0/0]	259.55 (260.00) [259.55]	202.34 (0.00) [0]
821	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	273.42 (0.00) [0]
822	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2021]	743.21 (743.00) [743.21]	193.08 (0.00) [0]
823	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	188.64 (0.90) [0]
824	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	124.95 (0.00) [0]
825	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [0/0]	206.97 (207.00) [206.97]	135.41 (0.00) [0]
826	CHIKALI TO DHAD	3/2018	12/2019 (-) [0/0]	189.46 (189.00) [189.46]	97.66 (0.00) [0]
827	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [0/0]	548.03 (548.00) [548.03]	353.00 (0.00) [0]
828	CHIKLI TO TAKARKHED	3/2018	12/2019	393.10	222.37

			(-) [0/0]	(393.00) [393.10]	(0.00) [0]
829	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	164.90 (0.00) [0]
830	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	75.68 (0.00) [-]
831	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2021) [3/2022]	649.50 (-) [649.50]	209.18 (0.00) [36]
832	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (8/2021) [2/2022]	291.53 (-) [291.53]	150.06 (0.00) [-]
833	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [0/0]	244.90 (-) [244.90]	251.87 (0.00) [0]
834	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (2/2021) [8/2021]	289.21 (-) [289.21]	194.57 (0.00) [-]
835	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2021) [6/2021]	593.26 (-) [690.17]	594.57 (96.91) [37]
836	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
837	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (6/2021) [6/2021]	531.13 (-) [730.97]	642.54 (199.84) [37]
838	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	80.00 (0.00) [0]
839	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
840	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	63.76 (-89.53) [0]
841	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (-) [414.00]	409.40 (-0.51) [0]
842	DAHEGAON TO KUHI	1/2017	6/2019 (-) [0/0]	228.89 (229.00) [228.89]	152.57 (0.00) [0]
843	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [0/0]	182.63 (-) [182.63]	132.40 (0.00) [0]
844	DEORI TO AMGAON	1/2017	5/2019 (-) [0/0]	409.62 (410.00) [409.62]	227.76 (0.00) [0]
845	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [0/0]	219.91 (-) [219.91]	123.76 (0.00) [0]
846	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [0/0]	296.19 (-) [254.00]	254.85 (-42.19) [0]
847	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [0/0]	336.21 (336.00) [336.21]	142.66 (0.00) [0]
848	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-)	217.14 (217.00)	131.55 (0.00)

			[0/0]	[217.14]	[0]
849	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [0/0]	391.06 (391.00) [391.06]	215.41 (0.00) [0]
850	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	185.74 (0.00) [0]
851	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
852	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [807.00]	666.56 (164.87) [0]
853	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [0/0]	1,871.34 (-) [1,871.34]	3,443.43 (0.00) [0]
854	FOUR LANNING OF TULJPUR-AUSA SECTION	2/2017	2/2020 (-) [0/0]	904.16 (-) [904.16]	855.25 (0.00) [0]
855	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	309.38 (0.00) [0]
856	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	208.63 (0.00) [0]
857	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [0/0]	294.87 (295.00) [294.87]	96.59 (0.00) [0]
858	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [0/0]	355.17 (-) [355.17]	268.87 (0.00) [0]
859	INDAPUR TO VADPALE	1/2017	12/2019 (-) [0/0]	1,202.52 (1,203.00) [1,202.52]	973.05 (0.00) [0]
860	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [0/0]	461.96 (-) [461.96]	250.79 (0.00) [0]
861	JALGAON TO BHADGAON	1/2018	11/2019 (-) [0/0]	307.54 (308.00) [307.54]	198.65 (0.00) [0]
862	JALGAON TO NANDURA	3/2018	12/2019 (-) [0/0]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
863	JALKOT TO TOGRI	7/2018	8/2020 (-) [0/0]	299.92 (300.00) [299.92]	66.25 (0.00) [0]
864	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (-) [356.66]	98.05 (0.00) [0]
865	KAIJ TO KUSALAM	1/2017	7/2019 (-) [0/0]	554.78 (-) [554.78]	252.45 (0.00) [0]
866	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	317.91 (0.00) [0]
867	KALMATH TO ZARAP	9/2016	3/2020 (-) [0/0]	1,338.13 (1,338.00) [1,338.13]	1,303.81 (0.00) [0]
868	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	627.00 (0.00) [0]

869	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [0/0]	407.19 (407.00) [407.19]	108.68 (0.00) [0]
870	KARAD TO TAGAON	1/2017	6/2019 (-) [0/0]	537.81 (538.00) [537.81]	154.48 (0.00) [0]
871	KARAD TO VITA	1/2018	12/2019 (-) [0/0]	344.85 (245.00) [344.85]	181.55 (0.00) [0]
872	KARWANDI TO RAJURI	3/2018	12/2019 (-) [0/0]	276.95 (277.00) [276.95]	255.47 (0.00) [0]
873	KATOL TO WARUD	1/2017	6/2019 (-) [0/0]	463.62 (664.00) [463.62]	253.23 (0.00) [0]
874	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [0/0]	249.29 (-) [249.29]	155.48 (0.00) [0]
875	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [0/0]	203.21 (203.00) [203.21]	173.79 (0.00) [0]
876	KHERDA TO NAGZARI	3/2018	12/2019 (-) [0/0]	181.30 (-) [181.30]	138.50 (0.00) [0]
877	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	261.97 (0.00) [0]
878	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [0/0]	281.78 (282.00) [281.78]	362.73 (0.00) [0]
879	KOTHARI TO DHANORA	9/2018	8/2020 (-) [0/0]	301.38 (301.00) [301.38]	152.42 (0.00) [0]
880	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	290.69 (0.00) [0]
881	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [0/0]	225.25 (225.00) [225.25]	254.75 (0.00) [0]
882	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	190.69 (0.00) [0]
883	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [0/0]	243.45 (244.00) [243.45]	140.20 (0.00) [0]
884	LATUR TO PANGAON	3/2018	12/2019 (-) [0/0]	336.47 (336.00) [336.47]	345.00 (0.00) [0]
885	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [0/0]	237.40 (-) [237.40]	9.66 (0.00) [0]
886	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [0/0]	413.99 (-) [413.99]	299.10 (0.00) [0]
887	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [0/0]	256.15 (-) [256.15]	262.63 (0.00) [0]
888	MALEGAON TO RISOD	2/2018	12/2019 (-) [0/0]	303.24 (303.00) [303.24]	223.97 (0.00) [0]
889	MALEWADA TO CHIMUR	10/2016	6/2019	322.55	189.91

			(-) [0/0]	(-) [322.55]	(0.00) [0]
890	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [0/0]	457.52 (-) [457.52]	352.94 (0.00) [0]
891	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [0/0]	222.13 (222.00) [222.13]	153.84 (0.00) [0]
892	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [0/0]	228.54 (-) [228.54]	162.30 (0.00) [0]
893	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [0/0]	418.36 (-) [418.36]	270.13 (0.00) [0]
894	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [0/0]	486.19 (-) [486.19]	293.39 (0.00) [0]
895	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	148.53 (0.00) [0]
896	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	230.03 (0.00) [0]
897	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	223.28 (0.00) [0]
898	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	228.07 (0.00) [0]
899	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
900	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [0/0]	162.34 (-) [162.34]	53.94 (0.00) [0]
901	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [0/0]	376.72 (377.00) [376.72]	224.81 (0.00) [0]
902	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	222.60 (0.00) [0]
903	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (6/2021) [12/2021]	546.00 (-) [546.00]	307.08 (0.00) [29]
904	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (6/2021) [12/2021]	591.66 (-) [591.66]	318.30 (0.00) [29]
905	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [0/0]	244.04 (244.00) [244.04]	142.76 (0.00) [0]
906	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [0/0]	274.50 (275.00) [274.50]	146.39 (0.00) [0]
907	NANDED TO JALKOT	12/2017	9/2019 (-) [0/0]	456.93 (457.00) [456.93]	456.93 (0.00) [0]
908	NANDGAON TO MORSHI	1/2017	6/2019 (-) [0/0]	385.87 (386.00) [385.87]	258.29 (0.00) [0]
909	NASHIK TO PETH	12/2015	11/2018 (-)	289.60 (-)	213.10 (0.00)

			[0/0]	[289.60]	[0]
910	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [0/0]	406.54 (407.00) [406.54]	163.36 (0.00) [0]
911	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [0/0]	420.63 (421.00) [420.63]	112.39 (0.00) [0]
912	OMREGA TO AUSA	3/2018	12/2019 (-) [0/0]	272.04 (272.00) [272.04]	218.03 (0.00) [0]
913	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [0/0]	344.25 (344.00) [344.25]	107.35 (0.00) [0]
914	PAHUR TO BODHWAD	1/2017	5/2020 (-) [0/0]	244.93 (-) [244.93]	127.80 (0.00) [0]
915	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	128.89 (0.00) [0]
916	PALPHATA TO PHULAMBAR	3/2018	12/2019 (-) [0/0]	227.19 (227.00) [227.19]	125.23 (0.00) [0]
917	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [0/0]	381.08 (302.00) [381.08]	9.66 (0.00) [0]
918	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
919	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [0/0]	238.19 (238.00) [238.19]	139.93 (0.00) [0]
920	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [0/0]	205.72 (206.00) [205.72]	41.48 (0.00) [0]
921	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	709.06 (0.00) [0]
922	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [0/0]	420.57 (-) [420.57]	252.78 (0.00) [0]
923	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [0/0]	170.00 (-) [170.00]	104.11 (0.00) [0]
924	PEN TO KHOPOLI	3/2018	3/2018 (-) [0/0]	301.39 (302.00) [301.39]	50.71 (0.00) [0]
925	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [0/0]	595.77 (-) [595.77]	264.93 (0.00) [0]
926	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [0/0]	223.46 (-) [223.46]	26.85 (0.00) [0]
927	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [0/0]	228.31 (-) [228.31]	73.50 (0.00) [0]
928	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [3/2021]	1,724.55 (-) [1,724.55]	2,559.00 (0.00) [96]
929	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	128.94 (0.00) [0]

930	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	300.50 (0.00) [0]
931	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	89.93 (0.00) [0]
932	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (3/2021) [3/2021]	536.65 (634.30) [536.65]	539.22 (0.00) [15]
933	RISOD TO HINGOLI	2/2018	12/2019 (-) [0/0]	355.99 (-) [355.99]	238.22 (0.00) [0]
934	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [0/0]	362.96 (-) [362.96]	87.43 (0.00) [0]
935	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [0/0]	415.25 (415.25) [415.25]	219.78 (0.00) [0]
936	SANGOLA TO JATH	1/2018	12/2019 (-) [0/0]	257.38 (257.00) [257.38]	155.57 (0.00) [0]
937	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	137.63 (0.00) [0]
938	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	160.89 (0.00) [0]
939	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	187.77 (0.00) [0]
940	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	252.00 (0.00) [0]
941	SELDOH TO PANVAR	7/2018	5/2020 (-) [0/0]	404.33 (404.00) [404.33]	22.40 (0.00) [0]
942	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [0/0]	150.79 (-) [150.79]	58.79 (0.00) [0]
943	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [0/0]	373.10 (373.00) [373.10]	311.65 (0.00) [0]
944	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [0/0]	211.34 (-) [211.34]	125.44 (0.00) [0]
945	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	177.79 (0.00) [0]
946	SHIVUR TO YEOLA	3/2018	12/2019 (-) [0/0]	181.08 (-) [181.08]	97.86 (0.00) [0]
947	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	94.22 (0.00) [0]
948	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (-) [448.18]	419.23 (43.24) [0]
949	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [0/0]	290.73 (-) [315.00]	309.40 (24.27) [0]
950	TAKARKHED TO JALNA	9/2017	6/2019	417.90	199.01

			(-) [0/0]	(418.00) [417.90]	(0.00) [0]
951	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [0/0]	264.41 (264.00) [264.41]	165.67 (0.00) [0]
952	TALGAON TO KALMATH	10/2016	3/2020 (-) [0/0]	904.70 (905.00) [904.70]	637.41 (0.00) [0]
953	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [0/0]	195.64 (196.00) [195.64]	116.30 (0.00) [0]
954	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	278.82 (0.00) [0]
955	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [0/0]	1,598.47 (1,560.00) [1,598.47]	995.57 (0.00) [0]
956	VITA TO NAGAJ	3/2018	12/2019 (-) [0/0]	304.58 (305.00) [304.58]	86.72 (0.00) [0]
957	WADI TO ASOLA	1/2017	9/2019 (-) [0/0]	363.82 (364.00) [363.82]	26.75 (0.00) [0]
958	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [0/0]	194.23 (194.00) [194.23]	99.17 (0.00) [0]
959	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [0/0]	376.19 (-) [376.19]	49.47 (0.00) [0]
960	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	837.21 (0.00) [0]
961	WARDHA TO ARVI	2/2018	4/2020 (-) [0/0]	313.58 (-) [313.58]	113.34 (0.00) [0]
962	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [0/0]	216.90 (217.00) [216.90]	136.15 (0.00) [0]
963	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [0/0]	165.51 (-) [165.51]	149.54 (0.00) [0]
964	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
965	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Urban Development</u>				
966	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (9/2022) [3/2023]	23,136.00 (-) [33,406.00]	17,039.36 (10,270.00) [98]
967	NAGPUR METRO RAIL	8/2014	3/2018 (-) [0/0]	8,680.00 (-) [8,680.00]	7,068.52 (0.00) [0]
968	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (-) [11,420.00]	5,696.05 (0.00) [0]
	<u>Water Resources</u>				
969	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2021]	233.57 (-) [233.57]	173.71 (0.00) [24]

	MANIPUR				
	Power				
970	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	Railways				
971	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	10,842.65 (7,809.98) [153]
	Road Transport And Highways				
972	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	12.44 (0.00) [0]
973	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	17.51 (0.00) [0]
974	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	22.24 (0.00) [0]
975	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	20.53 (0.00) [0]
976	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
977	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
978	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	0.00 (0.00) [0]
979	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	101.20 (0.00) [0]
980	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	170.53 (0.00) [0]
981	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	161.37 (-59.80) [36]
	MEGHALAYA				
	Culture Development				
982	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	148.33 (0.00) [42]
	Health And Family Welfare				
983	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	237.89 (0.00) [43]
	Human Resource Development				
984	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	Railways				
985	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [4,083.02]	263.68 (3,176.56) [0]
	Road Transport And Highways				
986	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	109.41 (0.00) [0]

987	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
988	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	119.35 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
989	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2023]	2,393.47 (5,021.45) [5,521.45]	3,838.64 (3,127.98) [108]
	<u>Road Transport And Highways</u>				
990	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2021) [6/2021]	195.04 (-) [377.99]	325.42 (182.95) [128]
991	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2020) [0/0]	186.96 (-) [322.24]	292.10 (135.28) [0]
992	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2021) [6/2021]	193.69 (-) [327.92]	295.96 (134.23) [128]
993	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	4.72 (0.00) [0]
994	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	0.00 (0.00) [0]
995	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	0.00 (0.00) [0]
996	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	0.00 (0.00) [0]
997	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	0.00 (0.00) [0]
998	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	65.01 (0.00) [43]
999	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	33.18 (0.00) [45]
1000	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	47.39 (0.00) [43]
1001	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	18.08 (0.00) [46]
1002	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	58.49 (0.00) [43]
1003	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	50.49 (0.00) [55]
1004	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	59.92 (0.00) [48]
1005	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	72.44 (0.00) [45]
1006	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC	11/2010	3/2011	624.41	890.74

	IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN		(-) [12/2020]	(-) [992.67]	(368.26) [0]
	MULTI STATE				
	Coal				
1007	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
1008	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	274.95 (0.00) [0]
1009	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2021]	319.76 (-) [319.76]	226.81 (0.00) [-12]
1010	RECAST PR FOR DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2025]	289.29 (-) [289.30]	35.67 (0.01) [36]
	Dpiit				
1011	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (1/2014) [7/2021]	12,579.09 (-) [13,812.30]	8,715.07 (1,233.21) [22]
	Human Resource Development				
1012	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	8/2018	3/2019 (-) [0/0]	418.00 (-) [418.00]	110.00 (0.00) [0]
1013	STUDY IN INDIA	3/2018	4/2018 (-) [0/0]	150.00 (-) [150.00]	0.00 (0.00) [0]
	Petroleum				
1014	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	3/2021 (-) [8/2021]	1,823.00 (-) [3,027.90]	1,933.53 (1,204.90) [5]
1015	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [4/2021]	571.66 (-) [571.66]	457.91 (0.00) [16]
1016	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (3,060.00) [3,060.00]	2,200.60 (-248.00) [0]
1017	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	189.70 (0.00) [0]
1018	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	3,437.00 (3,048.00) [3,048.00]	1,840.50 (-389.00) [12]
1019	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	71.90 (0.00) [0]
1020	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2021]	2,433.00 (-) [2,433.00]	2,109.70 (0.00) [6]
1021	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (-) [8/2022]	2,677.00 (-) [3,072.00]	2,201.31 (395.00) [14]
1022	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (5,909.00) [5,909.00]	3,607.20 (2,994.00) [110]
1023	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [5/2021]	2,881.40 (-) [2,000.00]	1,612.80 (-881.40) [5]
1024	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	1,022.40 (0.00) [0]

1025	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [3/2022]	2,321.00 (-) [3,338.00]	2,888.48 (1,017.00) [15]
1026	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (5/2021) [5/2021]	690.00 (-) [690.00]	540.76 (0.00) [34]
1027	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2021]	406.00 (-) [406.00]	187.00 (0.00) [5]
1028	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (1/2021) [3/2021]	352.56 (-) [490.24]	455.00 (137.68) [48]
1029	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	245.60 (0.00) [0]
	Power				
1030	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (9/2020) [5/2020]	198.49 (-) [198.49]	140.97 (0.00) [0]
1031	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [3/2024]	4,754.42 (9,129.32) [9,129.32]	2,056.36 (4,374.90) [63]
1032	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (5/2021) [4/2021]	358.83 (-) [358.83]	246.14 (0.00) [11]
1033	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (9/2020) [7/2020]	1,364.52 (1,891.41) [1,891.41]	1,326.81 (526.89) [0]
1034	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (9/2021) [5/2021]	522.29 (546.36) [546.36]	477.69 (24.07) [54]
1035	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (12/2020) [5/2021]	3,500.00 (3,500.00) [3,994.00]	2,868.53 (494.00) [10]
1036	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (8/2021) [5/2021]	235.53 (-) [235.53]	148.70 (0.00) [23]
1037	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (6/2021) [6/2021]	322.30 (-) [322.30]	201.10 (0.00) [28]
1038	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [6/2021]	197.40 (-) [197.40]	89.76 (0.00) [39]
1039	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [0/0]	3,519.59 (-) [3,519.59]	2,562.41 (0.00) [0]
1040	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (6/2021) [6/2021]	5,070.13 (-) [5,070.13]	4,060.04 (0.00) [14]
1041	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (4/2021) [4/2021]	14,733.37 (-) [14,733.37]	11,505.07 (0.00) [17]
1042	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (6/2021) [6/2021]	1,931.39 (-) [1,931.39]	1,677.06 (0.00) [16]
1043	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2021]	5,111.33 (6,700.00) [6,700.00]	2,605.89 (1,588.67) [36]
1044	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (8/2022) [8/2022]	11,130.19 (14,719.10) [14,719.10]	12,886.91 (3,588.91) [108]

1045	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [0/0]	283.72 (-) [283.72]	196.10 (0.00) [0]
1046	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [0/0]	3,654.00 (-) [3,654.00]	3,508.04 (0.00) [0]
1047	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [0/0]	608.24 (-) [608.24]	425.04 (0.00) [0]
1048	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [0/0]	203.28 (-) [260.03]	200.16 (56.75) [0]
1049	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (6/2021) [6/2021]	379.95 (-) [379.95]	229.18 (0.00) [18]
1050	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [0/0]	487.49 (-) [639.46]	590.30 (151.97) [0]
1051	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (11/2020) [3/2021]	4,824.12 (5,071.94) [5,071.94]	4,634.56 (247.82) [101]
1052	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (5/2021) [1/2021]	871.62 (902.49) [902.49]	648.77 (30.87) [0]
1053	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (9/2020) [4/2020]	408.46 (516.12) [516.12]	417.12 (107.66) [0]
1054	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [0/0]	5,151.37 (-) [5,151.37]	3,269.93 (0.00) [0]
1055	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (4/2021) [4/2021]	808.63 (-) [808.63]	652.14 (0.00) [39]
1056	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [6/2021]	374.63 (-) [374.63]	241.68 (0.00) [62]
	<u>Railways</u>				
1057	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	12,039.69 (0.00) [0]
1058	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2021]	288.35 (-) [502.48]	427.64 (214.13) [-]
1059	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.11 (-200.00) [-]
1060	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2022) [6/2021]	704.31 (-) [927.94]	534.34 (223.63) [15]
1061	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2022]	175.80 (-) [495.10]	284.21 (319.30) [-]
1062	CHANDIGARH-BADDI	4/2007	3/2023 (3/2025) [3/2025]	328.14 (1,540.13) [1,540.13]	242.09 (1,211.99) [24]
1063	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1064	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (3/2024) [3/2024]	523.52 (-) [1,205.00]	2.28 (681.48) [-]

1065	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2022]	295.00 (-) [477.31]	506.99 (182.31) [37]
1066	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	112.02 (651.22) [0]
1067	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	103.64 (173.89) [96]
1068	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2023) [3/2023]	1,347.26 (1,347.26) [1,347.26]	907.54 (0.00) [12]
1069	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	866.42 (0.00) [12]
1070	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [439.30]	385.60 (74.13) [96]
1071	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2023]	336.91 (791.39) [791.39]	572.99 (454.48) [-]
1072	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	637.94 (818.35) [133]
1073	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1074	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1075	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1076	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.55 (134.08) [0]
1077	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (-) [4/2021]	511.86 (-) [2,005.25]	1,777.22 (1,493.39) [12]
1078	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1079	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	148.26 (932.64) [33]
1080	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [5/2021]	678.54 (678.54) [929.86]	819.61 (251.32) [26]
1081	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [663.13]	520.48 (120.95) [12]
1082	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	11.43 (88.07) [-]
1083	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1084	HOTGI-KUDGI-GADAG	3/2015	3/2019 (3/2024) [3/2024]	1,614.59 (-) [1,870.41]	1,341.15 (255.82) [60]
1085	HOWRAH DIVISION- PLATFORM SHELTER (40 C	4/2010	11/2018	157.94	51.74

	CATEGORY STATIONS)		(-) [3/2021]	(-) [157.94]	(0.00) [28]
1086	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	0.02
			(-) [3/2025]	(-) [166.89]	(0.00) [-]
1087	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016	625.00	852.73
			(-) [6/2021]	(-) [859.00]	(234.00) [63]
1088	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014	2,132.77	350.54
			(-) [3/2027]	(-) [3,037.95]	(905.18) [156]
1089	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016	923.52	643.11
			(-) [3/2025]	(-) [995.10]	(71.58) [108]
1090	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/	174.56	71.43
			(-) [3/2025]	(-) [174.56]	(0.00) [-]
1091	KAZIPET-BALHRSHA	4/2015	3/2021	2,063.03	1,416.78
			(-) [3/2024]	(-) [2,063.03]	(0.00) [36]
1092	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023	1,856.95	567.51
			(-) [3/2024]	(-) [1,952.68]	(95.73) [12]
1093	KURUPPANTHARA-CHINGAVANAM	4/2007	/	270.14	439.49
			(-) [12/2021]	(-) [457.08]	(186.94) [-]
1094	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006	406.99	149.30
			(-) [3/2025]	(-) [545.70]	(138.71) [228]
1095	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008	247.66	2,131.17
			(-) [3/2025]	(-) [8,248.50]	(8,000.84) [202]
1096	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014	257.42	106.75
			(-) [3/2025]	(-) [257.42]	(0.00) [132]
1097	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	4/2011	3/2019	120.70	243.01
			(-) [12/2027]	(-) [2,172.16]	(2,051.46) [105]
1098	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012	499.96	164.05
			(-) [3/2025]	(-) [680.68]	(180.72) [157]
1099	MONIGRAM- NIMTITA	4/2012	/	250.93	360.96
			(-) [3/2024]	(-) [310.70]	(59.77) [-]
1100	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000	1,723.00	1,895.77
			(-) [3/2023]	(1.00) [3,421.35]	(1,698.35) [276]
1101	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020	414.84	155.65
			(-) [0/0]	(-) [1,040.00]	(625.16) [0]
1102	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012	450.00	714.78
			(-) [3/2024]	(-) [2,200.00]	(1,750.00) [140]
1103	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005	494.54	32.00
			(-) [3/2025]	(-) [494.59]	(0.05) [240]
1104	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020	242.22	73.97
			(-) [0/0]	(-) [471.00]	(228.78) [0]
1105	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/	241.52	287.09
			(-)	(-)	(132.35)

			[12/2021]	[373.87]	[-]
1106	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [3/2024]	1,798.00 (2,042.51) [2,042.51]	83.64 (244.51) [60]
1107	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1108	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [4/2021]	1,180.19 (2,531.34) [4,541.38]	3,683.54 (3,361.19) [148]
1109	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [701.81]	207.09 (101.81) [25]
1110	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [565.00]	539.40 (303.62) [0]
1111	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	373.47 (1,221.83) [36]
1112	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1113	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,262.36]	186.12 (2,179.61) [0]
1114	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2025]	2,062.30 (-) [2,432.50]	1,127.71 (370.20) [-]
1115	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [298.22]	52.09 (0.75) [-]
1116	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	186.14 (-10.96) [108]
1117	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [296.10]	0.01 (0.10) [-]
1118	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	0.00 (811.34) [-]
1119	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1120	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [0/0]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1121	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [6/2021]	860.43 (-) [1,147.00]	911.86 (286.57) [15]
	<u>Road Transport And Highways</u>				
1122	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1123	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [3/2021]	1,928.22 (-) [2,945.00]	2,467.00 (1,016.78) [71]
1124	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1125	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM	3/2018	/ (-)	998.70 (-)	0.00 (-36.70)

	29.000 (DE		[0/0]	[962.00]	[0]
1126	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [0/0]	604.00 (-) [364.59]	334.71 (-239.41) [0]
1127	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [0/0]	754.00 (-) [754.00]	1,364.18 (0.00) [0]
1128	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [5/2021]	1,244.10 (-) [1,244.10]	1,590.00 (0.00) [-]
1129	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,848.49 (0.00) [0]
1130	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	2,901.20 (531.45) [105]
	<u>Shipping And Ports</u>				
1131	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	5,369.18 (4,633.81) [4,633.81]	1,814.28 (-735.37) [0]
	<u>Telecommunications</u>				
1132	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [6/2021]	13,334.00 (-) [24,664.00]	16,594.00 (11,330.00) [71]
1133	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021 (-) [11/2021]	431.16 (431.00) [431.16]	0.00 (0.00) [5]
	<u>Urban Development</u>				
1134	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	3,320.23 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1135	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1136	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [12/2024]	2,326.52 (-) [6,911.00]	1,148.65 (4,584.48) [117]
	<u>Road Transport And Highways</u>				
1137	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	102.00 (0.00) [44]
1138	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	77.86 (0.00) [48]
1139	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	127.60 (-90.38) [0]
1140	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2020]	387.00 (-) [387.00]	283.11 (0.00) [0]
1141	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (336.49) [336.49]	79.44 (-163.60) [50]
1142	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	13.88 (0.00) [0]
1143	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	24.01 (0.00) [0]

1144	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	7.61 (0.00) [0]
1145	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	19.71 (0.00) [0]
1146	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	6.57 (0.00) [0]
1147	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	56.77 (0.00) [0]
1148	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	87.30 (0.00) [0]
1149	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	5.29 (0.00) [0]
1150	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
1151	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	0.00 (0.00) [0]
1152	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	0.00 (0.00) [0]
1153	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	0.00 (0.00) [0]
1154	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
1155	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	141.44 (0.00) [46]
1156	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	88.48 (0.00) [39]
1157	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	102.94 (0.00) [39]
1158	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	100.90 (0.00) [38]
1159	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	60.55 (0.00) [39]
1160	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	44.52 (0.00) [49]
1161	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	42.55 (0.00) [50]
1162	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	127.87 (0.00) [0]
1163	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	95.97 (0.00) [0]
1164	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM	3/2016	8/2016	373.07	298.08

	DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1		(-) [5/2021]	(-) [387.00]	(13.93) [57]
1165	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [339.55]	282.82 (-56.97) [57]
1166	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [5/2021]	429.52 (-) [340.00]	238.26 (-89.52) [57]
1167	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (9/2020) [0/0]	336.25 (369.96) [336.25]	301.49 (0.00) [0]
1168	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	98.42 (0.00) [0]
1169	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	123.44 (0.00) [0]
1170	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	0.00 (0.00) [0]
1171	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1172	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	50.27 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1173	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	168.13 (0.00) [108]
1174	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	278.53 (0.00) [60]
1175	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3/2017 (-) [3/2031]	3,145.45 (-) [3,145.45]	612.55 (0.00) [168]
1176	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	3/2010 (3/2029) [3/2029]	3,504.21 (3,504.21) [3,504.21]	607.83 (0.00) [228]
1177	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	3/2013 (3/2028) [3/2028]	8,416.19 (8,416.19) [8,416.19]	890.78 (0.00) [180]
1178	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2024]	1,375.38 (-) [1,375.38]	504.36 (0.00) [36]
1179	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2022]	479.53 (-) [479.53]	475.14 (0.00) [108]
1180	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	181.04 (0.00) [0]
1181	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,236.90 (0.00) [0]
1182	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,986.09 (0.00) [0]
1183	TALABIRA II AND III OCP	7/2017	7/2020 (-) [4/2020]	2,401.07 (-) [2,401.07]	854.37 (0.00) [0]

	<u>Human Resource Development</u>				
1184	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [6/2022]	790.79 (-) [790.79]	149.00 (0.00) [3]
	<u>Mines</u>				
1185	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (12/2022) [12/2022]	5,540.00 (6,435.90) [5,540.00]	721.87 (0.00) [20]
1186	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [2/2021]	355.00 (-) [355.00]	94.25 (0.00) [0]
1187	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (3/2023) [3/2023]	483.00 (483.00) [483.00]	0.92 (0.00) [23]
1188	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [0/0]	534.00 (-) [534.00]	359.06 (0.00) [0]
	<u>Petroleum</u>				
1189	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [8/2022]	1,607.00 (-) [1,607.00]	212.84 (0.00) [0]
1190	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (6/2022) [6/2022]	462.30 (-) [462.30]	22.97 (0.00) [9]
1191	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [6/2021]	315.00 (-) [315.00]	206.17 (0.00) [-6]
1192	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	114.73 (0.00) [0]
1193	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	77.27 (0.00) [0]
1194	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,933.00 (-) [1,933.00]	1,263.80 (0.00) [12]
1195	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	2,754.90 (0.00) [0]
1196	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	1,652.79 (0.00) [0]
1197	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	11.85 (0.00) [0]
1198	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2023) [3/2023]	371.00 (-) [371.00]	4.44 (0.00) [6]
1199	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	92.44 (0.00) [0]
1200	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [3/2022]	161.59 (-) [161.59]	49.54 (0.00) [27]
1201	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [3/2022]	1,297.50 (-) [1,297.50]	689.83 (0.00) [5]
	<u>Power</u>				
1202	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (2/2021) [5/2021]	12,532.44 (13,140.91) [13,140.91]	11,701.78 (608.47) [29]

1203	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [7/2021]	1,885.13 (-) [1,885.13]	1,763.69 (0.00) [31]
	<u>Railways</u>				
1204	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,536.00]	1,089.84 (593.05) [39]
1205	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2024) [3/2024]	843.04 (843.04) [843.04]	223.65 (0.00) [41]
1206	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2024) [3/2024]	1,172.92 (1,172.92) [1,172.92]	610.79 (0.00) [63]
1207	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1208	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2024]	5,200.00 (-) [962.00]	54.75 (-4,238.00) [48]
1209	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [0/0]	1,185.64 (-) [1,844.47]	1,883.44 (658.83) [0]
1210	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2023]	1,547.38 (1,547.38) [1,547.38]	635.77 (0.00) [12]
1211	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2024]	701.61 (-) [810.02]	171.45 (108.41) [64]
1212	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [0/0]	133.41 (207.00) [396.00]	388.21 (262.59) [0]
1213	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (3/2026) [3/2026]	2,923.13 (3,791.66) [3,791.66]	1,493.80 (868.53) [204]
1214	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	432.17 (0.00) [48]
1215	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [12/2021]	969.83 (1,312.96) [1,312.96]	901.11 (343.13) [21]
1216	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (3/2021) [3/2022]	155.81 (238.03) [238.03]	221.37 (82.22) [24]
1217	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [12/2021]	948.04 (-) [2,009.00]	1,875.48 (1,060.96) [21]
1218	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [12/2021]	1,111.99 (-) [1,539.28]	1,109.06 (427.29) [34]
1219	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,337.54 (1,237.83) [88]
1220	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (3/2025) [3/2025]	810.78 (1,928.07) [1,928.07]	864.71 (1,117.29) [45]
1221	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	1,317.36 (992.05) [24]
	<u>Road Transport And Highways</u>				
1222	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/	1,282.94	468.69
			(-)	(-)	(0.00)

			[3/2021]	[1,282.94]	[-]
1223	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [3/2021]	2,510.04 (-) [2,510.04]	555.68 (0.00) [19]
1224	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [3/2022]	752.28 (-) [752.28]	213.52 (0.00) [-]
1225	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [1/2021]	1,069.65 (-) [1,069.65]	611.71 (0.00) [0]
1226	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,935.14 (0.00) [0]
1227	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [6/2021]	1,008.96 (-) [1,008.96]	930.39 (0.00) [-]
1228	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	240.00 (0.00) [-]
1229	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [6/2021]	476.56 (-) [476.56]	52.19 (0.00) [47]
1230	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	63.98 (0.00) [0]
1231	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [3/2022]	953.09 (-) [953.09]	332.04 (0.00) [-]
1232	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [6/2021]	668.86 (-) [668.86]	276.59 (0.00) [-]
1233	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	217.40 (0.00) [-]
1234	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	258.91 (0.00) [0]
1235	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	25.40 (0.00) [-]
1236	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [6/2021]	1,288.07 (-) [1,420.00]	842.24 (131.93) [15]
1237	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [6/2021]	686.65 (-) [686.65]	227.63 (0.00) [-]
1238	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [6/2021]	686.65 (-) [686.65]	261.74 (0.00) [-]
1239	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [6/2021]	417.51 (-) [417.51]	127.61 (0.00) [-]
1240	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	258.91 (-0.05) [0]
1241	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [6/2021]	999.00 (-) [999.00]	102.70 (0.00) [-]
1242	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	88.30 (0.04) [0]

1243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1245	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (-) [6/2021]	1,522.00 (-) [1,522.00]	304.40 (0.00) [-]
1246	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (3/2021) [3/2021]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [81]
1247	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	189.70 (0.00) [-]
1248	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	136.19 (0.50) [0]
1249	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1250	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1251	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1252	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	210.29 (0.00) [0]
1253	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	99.98 (0.00) [0]
1254	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1255	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1256	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1257	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1258	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1259	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1260	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	<u>Steel</u>				
1261	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023 (-) [5/2023]	377.18 (-) [377.18]	16.12 (0.00) [0]
	<u>PONDICHERRY</u>				
	<u>Health And Family Welfare</u>				
1262	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES	3/2018	9/2020	195.00	16.41

	HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT		(-) [4/2022]	(-) [195.00]	(0.00) [19]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1263	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [4/2021]	218.83 (-) [218.83]	187.51 (0.00) [17]
1264	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [4/2021]	239.81 (-) [239.81]	186.72 (0.00) [17]
	<u>Health And Family Welfare</u>				
1265	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [7/2021]	703.00 (-) [557.48]	469.13 (-145.52) [13]
1266	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [3/2021]	152.95 (-) [177.92]	164.17 (24.97) [37]
	<u>Human Resource Development</u>				
1267	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022 (-) [8/2022]	348.24 (-) [348.24]	15.55 (0.00) [3]
1268	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [2/2022]	430.00 (-) [387.83]	194.72 (-42.17) [21]
1269	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [4/2021]	294.00 (-) [350.69]	274.98 (56.69) [24]
	<u>Petroleum</u>				
1270	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,244.50]	68.76 (-176.96) [0]
	<u>Railways</u>				
1271	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	226.25 (0.00) [108]
1272	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	<u>Road Transport And Highways</u>				
1273	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (-) [2,280.00]	1,282.04 (1,110.39) [0]
1274	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	795.30 (0.00) [0]
1275	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [12/2020]	889.24 (-) [904.82]	754.06 (15.58) [0]
1276	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [0/0]	1,388.34 (-) [2,587.50]	1,569.38 (1,199.16) [0]
1277	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [9/2021]	754.54 (-) [756.27]	363.86 (1.73) [18]
1278	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (-) [0/0]	766.36 (-) [766.36]	685.36 (0.00) [0]
1279	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-) [0/0]	447.29 (-) [746.43]	676.33 (299.14) [0]
1280	FOUR LANING OF EXISTING TWO LANE WITH PS FROM	2/2018	/	261.76	193.26

	TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB		(-) [7/2021]	(-) [207.00]	(-54.76) [-]
1281	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	456.80
			(-) [7/2021]	(-) [479.00]	(0.00) [-]
1282	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019	1,069.59	692.14
			(-) [8/2021]	(-) [1,069.59]	(0.00) [22]
1283	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/	196.05	143.03
			(-) [0/0]	(-) [196.05]	(0.00) [0]
1284	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/	199.90	124.52
			(-) [0/0]	(-) [199.90]	(0.00) [0]
1285	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020	170.57	54.53
			(-) [5/2021]	(-) [170.57]	(0.00) [6]
1286	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020	173.24	114.55
			(-) [0/0]	(-) [173.24]	(0.00) [0]
1287	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020	322.48	271.72
			(-) [8/2021]	(-) [322.48]	(0.00) [13]
1288	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	28.24
			(-) [0/0]	(-) [293.64]	(0.00) [0]
1289	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	246.29
			(-) [0/0]	(-) [293.64]	(0.00) [0]
1290	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020	293.10	156.80
			(-) [0/0]	(-) [293.10]	(0.00) [0]
1291	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/	892.17	648.44
			(-) [0/0]	(-) [892.17]	(0.00) [0]
	RAJASTHAN				
	Atomic Energy				
1292	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12,320.00	13,158.00
			(-) [3/2023]	(-) [17,079.00]	(4,759.00) [75]
	Coal				
1293	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020	2,112.60	86.85
			(-) [0/0]	(-) [2,112.60]	(0.00) [0]
1294	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019	513.63	175.30
			(-) [0/0]	(-) [513.63]	(0.00) [0]
1295	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020	2,196.30	140.80
			(-) [0/0]	(-) [2,196.30]	(0.00) [0]
1296	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019	522.45	9.88
			(-) [0/0]	(-) [522.45]	(0.00) [0]
	Human Resource Development				
1297	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019	549.31	458.38
			(-) [3/2021]	(-) [559.47]	(10.16) [20]
	Petroleum				
1298	LPG BP PROJECT JODHPUR	3/2018	/	229.80	81.43
			(5/2022) [5/2022]	(-) [229.80]	(0.00) [-]

	Power				
1299	FATEHGARH SOLAR 296MW	3/2020	9/2021 (-) [9/2021]	1,749.31 (-) [1,749.31]	0.00 (0.00) [0]
1300	JETSAR SOLAR 160 MW	12/2019	3/2021 (-) [3/2021]	702.28 (-) [702.28]	0.00 (0.00) [0]
1301	SAMBHU KI BHURJ SOLAR 250 MW	1/2020	9/2021 (1/2022) [1/2022]	1,522.71 (-) [1,522.71]	203.13 (0.00) [4]
1302	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (1/2022) [1/2022]	1,782.00 (-) [1,782.00]	69.21 (0.00) [4]
	Railways				
1303	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,980.21]	4.60 (1,106.50) [0]
1304	AJMER-BANGURGRAM	4/2011	11/2019 (-) [3/2021]	213.39 (-) [375.00]	345.38 (161.61) [16]
1305	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.00]	0.00 (277.00) [0]
1306	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [2/2020]	242.09 (-) [525.00]	463.25 (282.91) [0]
1307	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [2/2021]	246.08 (-) [395.00]	340.45 (148.92) [0]
1308	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [11/2021]	410.08 (-) [860.41]	699.06 (450.33) [33]
1309	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [6/2022]	808.85 (-) [808.85]	184.11 (0.00) [-2]
1310	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2021]	420.18 (-) [480.00]	313.18 (59.82) [15]
1311	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [0/0]	493.17 (-) [493.17]	464.53 (0.00) [0]
1312	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1313	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [0/0]	236.93 (-) [350.45]	253.81 (113.52) [0]
	Road Transport And Highways				
1314	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [8/2022]	370.36 (-) [370.36]	90.45 (0.00) [0]
1315	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	587.64 (0.00) [0]
1316	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [0]
1317	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [0/0]	688.70 (-) [688.70]	880.00 (0.00) [0]
1318	6-LANNING OF KISHANGARH TO GULABPURA SECTION	12/2016	/	1,031.95	374.05

	OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-		(-) [9/2021]	(-) [1,031.95]	(0.00) [-]
1319	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/	178.13	139.26
			(-) [3/2021]	(-) [178.13]	(0.00) [-]
1320	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018	822.90	1,688.16
			(-) [0/0]	(-) [822.90]	(0.00) [0]
1321	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/	1,158.35	611.28
			(-) [0/0]	(-) [1,158.35]	(0.00) [0]
1322	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018	163.95	116.47
			(-) [3/2021]	(-) [163.95]	(0.00) [35]
1323	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/	716.76	610.56
			(-) [0/0]	(-) [716.76]	(0.00) [0]
1324	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/	741.86	168.78
			(-) [0/0]	(-) [741.86]	(0.00) [0]
1325	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/	1,308.73	330.46
			(-) [0/0]	(-) [1,308.73]	(0.00) [0]
1326	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019	763.23	191.80
			(-) [0/0]	(-) [763.23]	(0.00) [0]
1327	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019	649.00	567.49
			(-) [0/0]	(-) [649.00]	(0.00) [0]
1328	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017	964.17	773.03
			(-) [11/2020]	(-) [964.17]	(0.00) [0]
1329	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011	1,673.70	3,326.93
			(-) [0/0]	(-) [1,673.70]	(0.00) [0]
1330	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013	511.00	492.00
			(-) [0/0]	(-) [511.00]	(0.00) [0]
1331	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013	511.00	2,323.04
			(-) [0/0]	(-) [511.00]	(0.00) [0]
1332	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020	196.23	0.00
			(-) [8/2022]	(-) [196.00]	(-0.23) [21]
1333	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014	278.87	0.00
			(-) [0/0]	(-) [278.87]	(0.00) [0]
1334	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014	376.52	0.00
			(-) [0/0]	(-) [376.52]	(0.00) [0]
1335	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/	1,100.19	1,327.00
			(-) [3/2021]	(-) [1,145.31]	(45.12) [-]
1336	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/	1,239.82	1,674.80
			(-) [1/2021]	(-) [1,727.66]	(487.84) [0]
1337	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020	894.00	810.00
			(-) [7/2021]	(-) [929.32]	(35.32) [15]
1338	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016	425.19	276.40
			(-)	(-)	(0.00)

			[0/0]	[425.19]	[0]
1339	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR	8/2015	/ (-) [0/0]	275.90 (-) [275.90]	289.13 (0.00) [0]
1340	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1341	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGLAUR	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	550.35 (0.00) [0]
1342	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGLAUR SECTION BY EXECUTING BALANCE WORK FRO	3/2020	8/2020 (-) [8/2022]	255.23 (-) [255.23]	1.66 (0.00) [24]
1343	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	886.59 (0.00) [0]
1344	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [4/2021]	370.30 (-) [370.30]	290.00 (0.00) [34]
1345	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	673.70 (0.00) [0]
1346	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [6/2021]	341.79 (-) [341.79]	208.00 (0.00) [37]
1347	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1348	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	244.68 (0.00) [0]
1349	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1350	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	387.22 (0.00) [0]
1351	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [3/2021]	187.82 (-) [187.82]	131.74 (0.00) [35]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1352	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [8,600.00]	619.18 (7,260.52) [0]
	<u>Road Transport And Highways</u>				
1353	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	0.00 (0.00) [0]
1354	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	0.00 (0.00) [0]
1355	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (12/2020) [0/0]	182.28 (369.64) [269.14]	274.07 (86.86) [0]
1356	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (12/2020) [0/0]	151.59 (370.01) [151.59]	282.36 (0.00) [0]
1357	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (12/2020) [0/0]	166.27 (359.92) [166.27]	243.59 (0.00) [0]

1358	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	85.64 (0.00) [0]
1359	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	24.70 (0.00) [0]
1360	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
1361	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	11.03 (0.00) [0]
1362	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	0.78 (0.00) [0]
1363	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	0.00 (0.00) [0]
1364	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	0.00 (0.00) [0]
1365	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	261.20 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1366	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	23,648.00 (0.00) [36]
1367	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [10/2022]	3,492.00 (5,677.00) [6,840.00]	5,922.21 (3,348.00) [145]
	<u>Civil Aviation</u>				
1368	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (-) [3/2023]	380.87 (-) [380.87]	0.00 (0.00) [12]
1369	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [9/2022]	2,467.00 (-) [2,467.00]	303.07 (0.00) [7]
1370	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [3/2022]	951.28 (-) [951.28]	249.79 (0.00) [5]
	<u>Coal</u>				
1371	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (3/2025) [3/2025]	1,458.17 (709.06) [709.06]	484.65 (-749.11) [117]
1372	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (7,980.79) [7,980.79]	7,404.29 (2,073.68) [0]
	<u>Finance</u>				
1373	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [4/2021]	209.00 (-) [208.96]	205.40 (-0.04) [18]
1374	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	113.99 (0.00) [0]
	<u>Mines</u>				
1375	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (6/2021) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [0]
	<u>Petroleum</u>				

1376	AUGMENTATION OF CTMPL	12/2016	11/2021 (-) [11/2021]	228.00 (-) [228.00]	135.89 (0.00) [0]
1377	BS-VI PROJECTS	9/2017	12/2019 (-) [1/2021]	1,858.00 (-) [1,858.00]	1,528.75 (0.00) [0]
1378	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [9/2023]	921.00 (-) [921.00]	3.05 (0.00) [0]
1379	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	205.98 (0.00) [10]
1380	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2022]	4,497.00 (-) [6,025.00]	3,636.76 (1,528.00) [38]
1381	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1382	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2021) [5/2021]	650.82 (-) [624.35]	446.72 (-26.47) [26]
1383	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [8/2022]	678.00 (1,472.00) [1,472.00]	18.80 (794.00) [66]
1384	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [9/2021]	421.00 (-) [300.00]	241.01 (-121.00) [13]
1385	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [12/2023]	1,398.00 (-) [1,398.00]	80.68 (0.00) [0]
	<u>Power</u>				
1386	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (-) [9/2021]	1,316.22 (-) [1,316.22]	0.00 (0.00) [0]
1387	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (4/2021) [4/2021]	186.17 (219.66) [219.66]	157.13 (33.49) [21]
	<u>Railways</u>				
1388	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [238.00]	153.70 (-19.00) [0]
1389	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [527.37]	3.34 (375.53) [0]
1390	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (2/2021) [4/2021]	931.98 (-) [1,121.00]	906.57 (189.02) [-]
1391	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [3/2024]	198.68 (-) [559.95]	319.22 (361.27) [-]
1392	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1393	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [12/2021]	495.74 (-) [734.01]	481.29 (238.27) [102]
1394	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2022]	760.00 (-) [1,536.00]	1,233.08 (776.00) [27]
1395	MADURAI-BODINAYAKKANUR	4/2008	/ (10/2021)	164.41 (-)	355.13 (435.89)

			[9/2021]	[600.30]	[-]
1396	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [6/2022]	1,700.00 (-) [1,305.00]	756.45 (-395.00) [3]
1397	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [2,910.84]	1,597.41 (2,186.15) [73]
1398	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (3/2021) [12/2020]	187.26 (-) [332.00]	265.41 (144.74) [0]
1399	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]
1400	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [9/2021]	268.87 (-) [950.00]	928.36 (681.13) [198]
1401	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [12/2025]	582.83 (-) [582.83]	239.11 (0.00) [-]
1402	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [227.40]	63.90 (0.00) [0]
1403	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2025]	303.98 (-) [1,720.00]	697.29 (1,416.02) [60]
1404	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	Road Transport And Highways				
1405	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [1/2022]	624.00 (-) [624.00]	8.56 (0.00) [93]
1406	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	182.00 (0.00) [0]
1407	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	566.14 (0.00) [58]
1408	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/	5/2016	1/2017 (-) [0/0]	307.70 (-) [307.70]	312.82 (0.00) [0]
1409	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	223.10 (9.95) [0]
1410	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	140.64 (0.00) [0]
1411	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [10/2020]	600.00 (-) [600.00]	1.65 (0.00) [0]
1412	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [1/2022]	1,016.92 (-) [1,071.00]	218.47 (54.08) [-]
1413	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [0/0]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1414	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [12/2021]	628.71 (-) [628.71]	310.06 (0.00) [-]
1415	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM.	3/2018	/ (-)	2,065.96 (-)	0.00 (103.04)

	123+800) SECTION OF N		[0/0]	[2,169.00]	[0]
1416	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [8/2021]	1,166.26 (-) [1,296.93]	220.78 (130.67) [-]
1417	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [2/2021]	641.17 (-) [641.17]	394.32 (0.00) [0]
1418	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [8/2021]	505.35 (-) [505.35]	243.30 (0.00) [-]
1419	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	462.14 (0.00) [59]
1420	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2021]	707.82 (-) [707.82]	421.01 (0.00) [31]
1421	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [12/2021]	848.45 (932.23) [848.45]	222.06 (0.00) [21]
1422	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [2/2021]	641.17 (-) [641.17]	395.10 (0.00) [0]
1423	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	7/2020	12/2021 (-) [12/2021]	3,426.00 (-) [3,426.00]	0.00 (0.00) [0]
1424	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	146.79 (4.82) [0]
1425	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2021]	379.90 (-) [379.90]	203.77 (0.00) [-]
1426	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,337.11 (0.00) [0]
1427	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1428	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1429	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [8/2021]	374.00 (-) [166.90]	54.22 (-207.10) [99]
1430	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1431	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	93.53 (0.00) [0]
1432	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (-) [240.38]	74.56 (0.00) [0]
1433	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	45.52 (0.00) [0]
1434	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/	1/2016	9/2016 (-) [0/0]	162.72 (-) [162.72]	136.46 (0.00) [0]
Urban Development					
1435	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-)	3,770.00 (-)	3,088.12 (0.00)

			[3/2021]	[3,770.00]	[36]
1436	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,365.87 (4,458.00) [0]
	<u>TELANGANA</u>				
	<u>Civil Aviation</u>				
1437	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (-) [5/2022]	353.61 (-) [353.61]	0.00 (0.00) [0]
	<u>Coal</u>				
1438	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2022]	447.06 (-) [473.22]	49.77 (26.16) [84]
1439	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	169.95 (0.00) [36]
1440	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2022]	397.09 (-) [442.42]	108.64 (45.33) [36]
1441	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2022]	417.33 (-) [384.32]	131.63 (-33.01) [68]
1442	KISTARAM OCP	11/2010	3/2015 (-) [3/2022]	242.29 (-) [164.04]	143.08 (-78.25) [84]
1443	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	416.07 (70.65) [132]
1444	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2022]	162.76 (-) [349.28]	288.72 (186.52) [84]
1445	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2021]	430.45 (-) [415.37]	193.00 (-15.08) [60]
1446	SRP OC-II EXPANSION PROJECT	11/2016	/ (-) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [-]
	<u>Health And Family Welfare</u>				
1447	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	136.48 (0.00) [14]
	<u>Petroleum</u>				
1448	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	76.47 (0.00) [16]
	<u>Power</u>				
1449	RAMAGUNDAM FLOATING SOLAR 100 MW	6/2019	4/2021 (-) [4/2021]	401.90 (-) [401.90]	0.00 (0.00) [0]
1450	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [7/2022]	10,598.98 (10,997.70) [10,997.70]	8,310.67 (398.72) [20]
	<u>Railways</u>				
1451	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2021]	632.68 (-) [950.00]	810.96 (317.32) [69]
1452	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	549.50 (0.00) [0]
1453	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION	4/2017	3/2022 (-)	119.73 (185.00)	7.09 (329.66)

	AVOIDANCE SYSTEM (958 K		[12/2022]	[449.39]	[9]
1454	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2024]	1,160.48 (-) [1,160.48]	502.93 (0.00) [168]
1455	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92
			(-) [0/0]	(-) [2,911.84]	(1,799.84) [0]
1456	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [850.00]	705.50 (76.06) [0]
	<u>Road Transport And Highways</u>				
1457	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [0/0]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [0]
1458	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [0/0]	283.15 (-) [283.15]	98.36 (0.00) [0]
1459	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [0/0]	626.76 (-) [626.76]	170.47 (0.00) [0]
1460	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.95 (0.00) [0]
1461	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1462	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/	857.62	196.45
			(-) [0/0]	(-) [857.62]	(0.00) [0]
1463	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/	802.65	380.41
			(-) [0/0]	(-) [802.65]	(0.00) [0]
1464	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/	950.63	548.02
			(-) [0/0]	(-) [950.63]	(0.00) [0]
1465	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO	3/2018	/	828.29	0.00
	TELANGANA/MAHARASHT		(-) [0/0]	(-) [828.29]	(0.00) [0]
1466	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [3/2021]	1,423.96 (-) [1,056.08]	974.60 (-367.88) [28]
1467	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [0/0]	192.67 (-) [192.67]	146.55 (0.00) [0]
1468	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [0/0]	605.08 (-) [605.08]	398.45 (0.00) [0]
1469	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [0/0]	426.52 (-) [426.52]	388.63 (0.00) [0]
1470	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1471	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [0/0]	294.13 (-) [294.13]	116.46 (0.00) [0]
1472	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	122.17 (0.00) [0]
1473	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO	3/2018	9/2020 (-)	322.81 (-)	120.13 (0.00)

	KODAD SEC		[0/0]	[322.81]	[0]
1474	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [0/0]	248.83 (-) [248.83]	116.36 (0.00) [0]
1475	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [0/0]	298.32 (-) [298.32]	115.53 (0.00) [0]
1476	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [0/0]	230.03 (-) [230.03]	207.56 (0.00) [0]
1477	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [0/0]	206.13 (-) [206.13]	171.39 (0.00) [0]
1478	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	101.77 (0.00) [0]
1479	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	107.70 (0.00) [0]
1480	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	222.84 (0.00) [0]
1481	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	164.33 (0.00) [0]
1482	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	293.94 (0.00) [0]
1483	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	176.70 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1484	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [0/0]	438.28 (-) [438.28]	335.58 (0.00) [0]
	<u>Railways</u>				
1485	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
1486	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	359.11 (0.00) [0]
1487	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	2.60 (0.00) [0]
1488	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	0.00 (0.00) [0]
1489	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	0.00 (0.00) [0]
1490	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	0.00 (0.00) [0]
1491	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	0.00 (0.00) [0]
1492	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM	1/2017	12/2022 (-)	197.67 (-)	5.75 (0.00)

	422.00 (25 K		[12/2022]	[197.67]	[0]
1493	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (7/2021) [7/2021]	171.90 (-) [171.90]	110.19 (0.00) [11]
	Rural Development				
1494	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [10/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [70]
1495	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [10/2021]	202.61 (227.00) [207.12]	190.22 (4.51) [58]
1496	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [12/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [60]
	UTTAR PRADESH				
	Civil Aviation				
1497	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2022]	1,383.00 (-) [1,383.00]	369.66 (0.00) [12]
	Coal				
1498	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (7/2022) [7/2022]	17,237.00 (-) [17,237.80]	11,452.38 (0.80) [8]
	Health And Family Welfare				
1499	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [7/2021]	785.00 (-) [715.06]	548.39 (-69.94) [15]
1500	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [3/2021]	268.84 (-) [268.84]	244.88 (0.00) [-]
	Human Resource Development				
1501	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [6/2021]	171.72 (-) [171.72]	53.94 (0.00) [15]
	Petroleum				
1502	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	430.93 (0.00) [0]
1503	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (345.15) [345.15]	200.10 (57.66) [0]
1504	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (8/2029) [8/2029]	3,450.20 (-) [3,450.20]	153.20 (0.00) [5]
1505	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (-) [10/2021]	217.92 (-) [217.92]	86.30 (0.00) [6]
1506	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (11/2021) [11/2021]	255.40 (-) [255.40]	63.74 (0.00) [15]
1507	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	772.75 (0.00) [0]
1508	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	146.91 (0.00) [3]
	Power				
1509	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (1/2021) [1/2021]	587.44 (-) [587.44]	463.48 (0.00) [0]
1510	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020	349.00	226.00

			(-) [4/2021]	(-) [349.00]	(0.00) [5]
1511	DEVIKOT SOLAR 150MW	1/2020	9/2021 (1/2022) [1/2022]	798.24 (-) [798.24]	31.64 (0.00) [4]
1512	DEVIKOT SOLAR 90MW	3/2020	9/2021 (1/2022) [1/2022]	501.29 (-) [501.29]	49.76 (0.00) [4]
1513	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	1,728.08 (0.00) [11]
1514	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [1/2021]	9,750.89 (-) [12,176.28]	11,130.00 (2,425.39) [0]
1515	NOKHRA	3/2020	9/2021 (1/2022) [1/2022]	1,722.14 (-) [1,722.14]	103.85 (0.00) [4]
1516	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (3/2021) [3/2021]	9,188.98 (-) [9,842.02]	8,146.60 (653.04) [20]
	<u>Railways</u>				
1517	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/	307.00	0.00
			(-) [0/0]	(-) [1,409.09]	(1,102.09) [0]
1518	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	238.15 (-233.29) [2]
1519	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1520	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,825.00]	1,411.49 (641.75) [24]
1521	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/	602.50	63.70
			(-) [12/2023]	(-) [714.34]	(111.84) [-]
1522	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1523	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1524	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1525	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/	182.92	0.00
			(-) [0/0]	(-) [197.73]	(14.81) [0]
1526	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	44.84 (0.35) [68]
1527	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	809.66 (0.00) [0]
1528	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	33.37 (0.00) [0]
1529	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/	643.00	0.00
			(-) [0/0]	(-) [644.00]	(1.00) [0]
1530	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019	528.57	235.00

			(-) [3/2022]	(-) [528.57]	(0.00) [36]
1531	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [6/2022]	927.01 (-) [1,400.00]	1,331.76 (472.99) [39]
1532	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	446.65 (0.00) [0]
1533	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [0/0]	668.70 (668.00) [680.00]	330.00 (11.30) [0]
1534	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	887.48 (0.00) [21]
1535	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1536	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1537	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [3/2021]	622.50 (427.00) [426.74]	476.60 (-195.76) [47]
1538	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,165.22 (0.00) [48]
1539	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,295.42]	929.79 (0.00) [0]
1540	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	80.76 (-149.01) [16]
1541	UNCHAHAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,265.00]	103.72 (36.00) [-]
1542	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [1,000.00]	688.03 (56.40) [33]
	Road Transport And Highways				
1543	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	239.04 (0.00) [0]
1544	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1545	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (12/2020) [12/2020]	351.34 (417.68) [417.68]	433.68 (66.34) [0]
1546	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (1/2020) [1/2020]	495.78 (627.93) [627.93]	633.24 (132.15) [0]
1547	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (12/2020) [12/2020]	291.36 (469.31) [469.31]	459.07 (177.95) [0]
1548	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1549	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,118.92 (211.43) [0]
1550	4-LANING OF GAGALHERI- SAHARANPUR-	3/2016	/	1,668.00	946.08

	YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (		(-) [0/0]	(-) [1,668.00]	(0.00) [0]
1551	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1552	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [0/0]	1,408.00 (-) [1,408.00]	442.70 (0.00) [0]
1553	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [0/0]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [0]
1554	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	2,977.58 (0.00) [0]
1555	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1556	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1557	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [0/0]	1,657.20 (-) [1,657.20]	2,345.00 (0.00) [0]
1558	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,357.84 (382.01) [0]
1559	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	43.23 (0.00) [0]
1560	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	977.26 (0.00) [0]
1561	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1562	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1563	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1564	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1565	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1566	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1567	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [0/0]	1,081.57 (-) [1,057.60]	596.79 (-23.97) [0]
1568	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,087.00]	1,059.17 (-145.21) [0]
1569	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [0/0]	1,989.00 (-) [1,989.00]	756.92 (0.00) [0]
1570	ETAWAH CHAKERI	3/2013	9/2015 (-)	1,573.00 (-)	2,093.25 (0.00)

			[0/0]	[1,573.00]	[0]
1571	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	287.84 (0.00) [0]
1572	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	517.66 (0.00) [0]
1573	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [1,197.00]	1,011.70 (271.60) [0]
1574	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	549.07 (0.00) [0]
1575	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	464.05 (0.00) [0]
1576	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1577	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1578	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1579	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J)	3/2018	8/2020 (-) [3/2021]	288.30 (-) [288.30]	120.68 (0.00) [7]
1580	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [0/0]	1,373.28 (-) [1,373.28]	974.57 (0.00) [0]
1581	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [0/0]	1,184.71 (-) [1,310.00]	1,039.23 (125.29) [0]
1582	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [0/0]	899.00 (-) [899.00]	641.51 (0.00) [0]
1583	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1584	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [0/0]	281.45 (-) [281.45]	0.00 (0.00) [0]
1585	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	11/2018	12/2020 (-) [6/2021]	281.45 (-) [281.45]	72.05 (0.00) [6]
1586	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [987.94]	867.27 (304.70) [0]
1587	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019 (-) [6/2020]	209.10 (-) [209.10]	201.46 (0.00) [0]
1588	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [9/2021]	326.99 (327.00) [326.99]	105.65 (0.00) [-]
1589	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [5/2021]	296.50 (-) [296.50]	172.63 (0.00) [8]
1590	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	529.35 (-348.73) [0]

1591	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	655.03 (-345.24) [0]
1592	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	2/2019 (-) [0/0]	239.63 (-) [239.63]	212.53 (0.00) [0]
1593	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [0/0]	388.83 (-) [388.83]	304.70 (0.00) [0]
1594	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2021]	263.89 (-) [242.05]	188.43 (-21.84) [12]
1595	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [2/2021]	208.50 (-) [208.50]	165.82 (0.00) [0]
1596	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [4/2021]	445.89 (653.00) [653.29]	754.40 (207.40) [49]
1597	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [0/0]	599.34 (-) [599.34]	492.15 (0.00) [0]
1598	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [1/2021]	185.18 (-) [185.18]	124.43 (0.00) [0]
1599	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [3/2021]	249.50 (-) [249.50]	210.31 (0.00) [22]
1600	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [3/2021]	218.90 (-) [218.90]	129.83 (0.00) [12]
1601	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1602	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [0/0]	215.16 (215.00) [215.16]	160.61 (0.00) [0]
1603	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [3/2021]	240.30 (240.00) [240.30]	200.10 (0.00) [14]
1604	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [0/0]	218.94 (219.00) [218.94]	120.69 (0.00) [0]
1605	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [0/0]	176.94 (177.00) [176.94]	141.11 (0.00) [0]
1606	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [3/2021]	208.88 (-) [208.88]	175.51 (0.00) [17]
1607	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [653.29]	464.05 (207.40) [0]
1608	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	1,363.84 (0.00) [0]
1609	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,344.09 (0.00) [0]
1610	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [3/2023]	724.60 (-) [724.60]	0.00 (0.00) [0]
1611	VARANASI RING ROAD PKG - I	1/2018	/	450.77	0.00

			(-) [0/0]	(-) [450.77]	(0.00) [0]
1612	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [1/2021]	164.54 (165.00) [164.54]	141.33 (0.00) [0]
1613	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	128.54 (0.00) [0]
	<u>Steel</u>				
1614	FORGED WHEEL PLANT	4/2014	9/2018 (4/2021) [4/2021]	1,682.85 (-) [1,682.85]	1,551.82 (0.00) [31]
	<u>Urban Development</u>				
1615	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	8,379.62 (-) [8,379.62]	0.00 (0.00) [0]
1616	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	11,076.48 (-) [11,076.48]	0.00 (0.00) [0]
1617	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>Water Resources</u>				
1618	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [3/2022]	213.62 (261.12) [261.12]	0.00 (47.50) [0]
1619	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS	3/2018	9/2021 (-) [9/2021]	904.00 (-) [904.00]	136.55 (0.00) [0]
1620	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	21.10 (0.00) [0]
1621	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [234.03]	0.00 (2.24) [0]
1622	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1623	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [6/2022]	298.12 (213.91) [213.91]	0.00 (-84.21) [11]
1624	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	49.66 (0.00) [0]
1625	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [5/2021]	460.45 (-) [460.45]	216.89 (0.00) [5]
1626	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	2/2017	11/2019 (-) [3/2021]	161.31 (-) [161.31]	91.38 (0.00) [16]
1627	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [690.71]	0.00 (8.93) [0]
1628	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [1/2021]	279.91 (330.05) [330.05]	222.79 (50.14) [0]
1629	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	8/2020 (3/2021) [3/2021]	370.40 (430.49) [430.49]	376.22 (60.09) [7]
1630	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-)	967.23 (-)	54.21 (0.00)

			[9/2021]	[967.23]	[0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1631	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [7/2021]	456.86 (-) [456.86]	203.76 (0.00) [10]
	<u>Petroleum</u>				
1632	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [6/2021]	160.10 (-) [160.10]	93.23 (0.00) [16]
	<u>Power</u>				
1633	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.21 (274.07) [0]
1634	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [947.89]	569.80 (299.56) [0]
1635	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [12/2022]	2,978.48 (5,867.38) [5,867.38]	4,891.26 (2,888.90) [117]
1636	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2023]	2,491.58 (-) [3,860.35]	2,207.95 (1,368.77) [126]
	<u>Railways</u>				
1637	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	204.53 (126.80) [0]
1638	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1639	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [22,716.11]	2,997.71 (6,500.11) [3]
	<u>Road Transport And Highways</u>				
1640	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	139.26 (0.00) [0]
1641	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	157.79 (0.00) [0]
1642	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [0/0]	605.84 (-) [722.46]	722.46 (116.62) [0]
1643	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [0/0]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [0]
1644	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	64.03 (0.00) [0]
1645	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	215.91 (0.00) [0]
1646	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [0/0]	248.00 (-) [248.00]	0.00 (0.00) [0]
1647	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [0/0]	720.00 (-) [720.00]	348.16 (0.00) [0]
1648	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [0/0]	478.51 (-) [478.00]	315.11 (-0.51) [0]

1649	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	59.44 (0.00) [0]
1650	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [0/0]	283.51 (-) [283.51]	126.38 (0.00) [0]
1651	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	257.34 (-) [257.34]	62.79 (0.00) [0]
1652	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [0/0]	282.08 (-) [282.08]	77.05 (0.00) [0]
1653	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	200.34 (-) [200.34]	31.00 (0.00) [0]
1654	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [0/0]	418.88 (-) [418.88]	88.00 (0.00) [0]
1655	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	266.52 (-) [266.52]	144.27 (0.00) [0]
1656	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [0/0]	234.88 (-) [208.89]	118.26 (-25.99) [0]
1657	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1658	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1659	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [0/0]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1660	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOB LA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]
	<u>Water Resources</u>				
1661	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (3/2021) [3/2021]	158.00 (-) [158.00]	78.59 (0.00) [16]
1662	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	3/2017	8/2019 (-) [0/0]	273.37 (-) [273.37]	75.58 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1663	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (10/2022) [10/2022]	389.71 (-) [389.71]	140.62 (0.00) [11]
1664	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (12/2021) [12/2021]	458.00 (-) [458.00]	135.60 (0.00) [21]
	<u>Coal</u>				
1665	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [3/2022]	304.13 (341.22) [341.22]	38.59 (37.09) [60]
1666	EXPANSION PR OF JHANJRA UG(5.00 MTY)	11/2015	3/2022 (3/2029) [3/2029]	1,210.12 (-) [1,210.12]	24.49 (0.00) [84]
1667	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-)	502.68 (-)	10.11 (0.00)

			[3/2029]	[502.68]	[0]
1668	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	0.03 (0.00) [0]
1669	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [0/0]	2,661.73 (-) [5,146.48]	606.30 (2,484.75) [0]
1670	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	0.00 (0.00) [0]
1671	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	1.39 (0.00) [0]
1672	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2021]	1,055.05 (-) [1,055.05]	658.63 (0.00) [36]
1673	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.61 (0.00) [0]
	<u>Health And Family Welfare</u>				
1674	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1675	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1676	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [6/2021]	651.99 (-) [651.99]	490.55 (0.00) [-]
1677	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [6/2021]	355.15 (-) [355.15]	295.16 (0.00) [27]
	<u>Home Affairs</u>				
1678	NSG AT KOLKATA	10/2014	4/2018 (12/2021) [12/2021]	162.88 (238.00) [238.00]	171.19 (75.12) [44]
	<u>Human Resource Development</u>				
1679	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [0/0]	193.83 (-) [193.83]	0.45 (0.00) [0]
	<u>Petroleum</u>				
1680	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [3/2022]	3,712.00 (-) [3,696.00]	1,951.62 (-16.00) [-6]
1681	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (8/2029) [8/2029]	5,830.20 (-) [5,830.20]	14.63 (0.00) [-19]
1682	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,740.00 (-) [1,740.00]	831.40 (0.00) [12]
1683	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	58.06 (0.00) [0]
1684	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [10/2021]	163.02 (-) [163.02]	94.21 (0.00) [18]
	<u>Power</u>				
1685	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [7/2021]	529.68 (-) [529.68]	418.49 (0.00) [32]
1686	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018	454.11	343.25

			(3/2021) [4/2021]	(-) [454.11]	(0.00) [36]
1687	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [12/2024]	1,381.84 (-) [1,381.54]	660.06 (-0.30) [63]
	<u>Railways</u>				
1688	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (1,966.70) [2,373.00]	485.04 (1,345.60) [324]
1689	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [3/2025]	1,106.62 (-) [1,091.59]	983.60 (-15.03) [171]
1690	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	241.02 (16.56) [-]
1691	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1692	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1693	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1694	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1695	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [0/0]	221.42 (-) [380.00]	38.20 (158.58) [0]
1696	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [0/0]	297.32 (200.34) [614.00]	275.06 (316.68) [0]
1697	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,090.60]	1,087.60 (710.00) [0]
1698	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [4/2021]	602.27 (-) [2,144.78]	824.96 (1,542.51) [-8]
1699	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1700	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	1,119.31 (1,725.49) [108]
1701	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1702	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,734.83 (307.50) [108]
1703	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	906.05 (430.57) [72]
1704	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
	<u>Road Transport And Highways</u>				
1705	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (-) [1,827.15]	2,082.19 (744.15) [0]

1706	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [3/2022]	998.79 (-) [998.79]	1,868.67 (0.00) [103]
1707	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [5/2021]	1,078.84 (-) [1,078.84]	2,288.54 (0.00) [93]
1708	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [0]
1709	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [0/0]	361.15 (-) [363.93]	272.98 (2.78) [0]
1710	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [11/2022]	160.27 (213.97) [213.97]	25.03 (53.70) [39]
1711	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [0/0]	229.37 (-) [229.37]	130.72 (0.00) [0]
1712	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [12/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [28]
1713	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [3/2021]	254.30 (254.30) [254.30]	99.36 (0.00) [5]
1714	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [0/0]	767.03 (-) [767.03]	604.65 (0.00) [0]
1715	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (-) [5/2019]	600.87 (720.97) [720.97]	682.36 (120.10) [0]
1716	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (-) [6/2019]	823.20 (937.76) [937.76]	807.99 (114.56) [0]
1717	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [7/2021]	1,261.98 (-) [1,952.20]	934.06 (690.22) [-]
1718	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (1/2020) [2/2020]	279.70 (398.52) [398.52]	331.86 (118.82) [0]
1719	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (11/2020) [5/2021]	396.86 (396.86) [396.86]	242.97 (0.00) [20]
1720	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1721	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [2,360.65]	4,472.01 (695.65) [0]
1722	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [0/0]	202.69 (202.69) [202.69]	144.89 (0.00) [0]
1723	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (4/2020) [4/2021]	218.70 (218.70) [218.70]	103.81 (0.00) [5]
1724	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [12/2021]	426.18 (426.18) [426.18]	242.25 (0.00) [15]
	<u>Steel</u>				
1725	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [5/2021]	263.36 (-) [263.36]	213.22 (0.00) [8]

	<u>Water Resources</u>				
1726	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (5/2021) [5/2021]	274.76 (-) [274.76]	201.30 (0.00) [17]
1727	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1728	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1729	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]
1730	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [10/2022]	160.00 (154.73) [154.73]	0.00 (-5.27) [8]
1731	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1732	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	0.00 (0.00) [0]
1733	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [6/2022]	198.43 (224.69) [224.69]	0.00 (26.26) [4]
1734	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1735	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	0.00 (0.00) [0]
1736	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [12/2021]	185.22 (-) [185.22]	0.00 (0.00) [0]
1737	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [3/2021]	272.32 (-) [272.32]	214.52 (0.00) [11]
	Total			22,33,409.53 (6,35,788.05) [26,69,649.35]	13,06,617.54 (4,36,239.82)

Details of Central Sector Projects Costing Rs.150 crore and above (as on					31.03.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	ARUNACHAL PRADESH				
	Power				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (2/2021) [2/2021]	2,496.90 (7,927.34) [7,927.34]	8,154.50 (5,430.44) [0]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	13,537.76 (13,707.10) [155]
	Road Transport And Highways				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	134.38 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	400.56 (0.00) [0]
5	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	144.19 (0.00) [0]
6	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	163.66 (0.00) [0]
7	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	25.52 (0.00) [0]
8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	66.14 (0.00) [0]
9	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	0.00 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	30.34 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	33.61 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	35.38 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	0.00 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	107.43 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	0.00 (0.00) [0]

16	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	115.89 (0.00) [0]
17	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	260.57 (0.00) [0]
18	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	91.23 (0.00) [0]
19	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]
20	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	178.10 (0.00) [0]
21	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	184.62 (0.00) [0]
22	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [9/2018]	197.16 (-) [197.16]	91.25 (0.00) [0]
23	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	376.69 (0.00) [0]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	0.00 (0.00) [0]
25	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	4.21 (0.00) [0]
26	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	204.77 (0.00) [60]
27	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [2/2021]	167.28 (-) [167.28]	22.06 (0.00) [0]
28	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
29	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	172.89 (0.00) [0]
30	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	149.44 (0.00) [47]
31	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [252.79]	100.63 (57.56) [0]
32	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [263.31]	116.97 (59.95) [0]
33	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [252.05]	111.22 (57.39) [0]
34	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [252.05]	111.21 (53.83) [0]
35	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (-) [389.45]	349.94 (182.42) [0]
36	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON	2/2017	4/2017	180.57	51.78

	EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX		(-) [2/2021]	(-) [180.57]	(0.00) [0]
37	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	0.00 (119.37) [0]
38	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
39	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
40	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (-) [4/2022]	175.06 (-) [175.06]	81.01 (0.00) [-]
41	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (-) [4/2022]	176.12 (-) [176.12]	65.25 (0.00) [-]
42	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,217.25 (57.90) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
43	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2022]	1,142.00 (-) [1,232.00]	323.90 (90.00) [12]
	<u>Health And Family Welfare</u>				
44	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [7/2022]	875.00 (-) [747.80]	331.55 (-127.20) [14]
45	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
46	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [6/2021]	557.00 (-) [557.00]	487.25 (0.00) [16]
47	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [4/2021]	224.75 (-) [222.21]	144.80 (-2.54) [8]
48	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [6/2021]	423.00 (-) [502.00]	421.03 (79.00) [22]
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [4/2021]	543.91 (638.60) [652.10]	136.05 (108.19) [14]
50	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [12,366.00]	168.82 (0.00) [0]
51	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	117.34 (0.00) [0]
52	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2021) [5/2021]	249.85 (303.75) [303.75]	197.20 (53.90) [12]
	<u>Railways</u>				
53	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2021]	314.00 (486.96) [800.00]	799.87 (486.00) [24]
54	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,496.25 (717.68) [12]

55	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [5/2021]	870.96 (-) [1,873.21]	1,162.39 (1,002.25) [2]
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,043.00]	798.53 (657.80) [48]
	Road Transport And Highways				
57	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (390.73) [390.73]	267.46 (122.65) [0]
58	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
59	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	15.29 (0.00) [0]
60	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
61	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [303.49]	168.19 (-216.52) [0]
62	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	480.74 (0.00) [0]
63	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	75.42 (0.00) [0]
64	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	116.92 (-28.50) [0]
65	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.30]	100.07 (-30.09) [42]
66	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [4/2021]	294.17 (-) [294.17]	201.60 (0.00) [63]
67	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	0.00 (0.00) [0]
68	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (-) [0/0]	166.94 (-) [166.94]	0.00 (0.00) [0]
69	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	489.84 (143.23) [0]
70	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [0/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
71	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	233.27 (7.98) [0]
72	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
73	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	125.80 (0.00) [0]
74	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [887.68]	259.50 (69.68) [0]

75	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	145.21 (-65.43) [42]
76	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	407.11 (0.00) [0]
77	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	291.45 (0.00) [0]
78	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
79	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
80	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
81	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
82	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
83	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [2/2021]	208.00 (-) [230.00]	370.56 (22.00) [0]
84	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	390.72 (0.00) [0]
85	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [273.40]	132.79 (-776.11) [0]
86	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	240.36 (-70.66) [0]
87	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	70.46 (0.00) [0]
88	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	0.00 (0.00) [0]
89	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	0.00 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
90	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
91	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	10,842.65 (7,809.98) [153]
	<u>Road Transport And Highways</u>				
92	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	12.44 (0.00) [0]
93	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	17.51 (0.00) [0]

94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	22.24 (0.00) [0]
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	20.53 (0.00) [0]
96	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
97	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
98	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	0.00 (0.00) [0]
99	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	101.20 (0.00) [0]
100	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	170.53 (0.00) [0]
101	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	161.37 (-59.80) [36]
	<u>MEGHALAYA</u>				
	<u>Culture Development</u>				
102	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	148.33 (0.00) [42]
	<u>Health And Family Welfare</u>				
103	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	237.89 (0.00) [43]
	<u>Human Resource Development</u>				
104	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	<u>Railways</u>				
105	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [4,083.02]	263.68 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
106	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	109.41 (0.00) [0]
107	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
108	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	119.35 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
109	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2023]	2,393.47 (5,021.45) [5,521.45]	3,838.64 (3,127.98) [108]
	<u>Road Transport And Highways</u>				
110	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2021) [6/2021]	195.04 (-) [377.99]	325.42 (182.95) [128]
111	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM	8/2010	9/2014	186.96	292.10

	38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD		(12/2020) [0/0]	(-) [322.24]	(135.28) [0]
112	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2021) [6/2021]	193.69 (-) [327.92]	295.96 (134.23) [128]
113	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	4.72 (0.00) [0]
114	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	0.00 (0.00) [0]
115	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	0.00 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	0.00 (0.00) [0]
117	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	0.00 (0.00) [0]
118	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	65.01 (0.00) [43]
119	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	18.08 (0.00) [46]
120	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	33.18 (0.00) [45]
121	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	50.49 (0.00) [55]
122	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	59.92 (0.00) [48]
123	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	72.44 (0.00) [45]
124	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	58.49 (0.00) [43]
125	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	47.39 (0.00) [43]
126	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2020]	624.41 (-) [992.67]	890.74 (368.26) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
127	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [12/2024]	2,326.52 (-) [6,911.00]	1,148.65 (4,584.48) [117]
	<u>Road Transport And Highways</u>				
129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	102.00 (0.00) [44]
130	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM	3/2018	9/2018 (-)	285.68 (-)	77.86 (0.00)

	EXISTING KM 52.370 TO		[9/2022]	[285.68]	[48]
131	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	127.60 (-90.38) [0]
132	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2020]	387.00 (-) [387.00]	283.11 (0.00) [0]
133	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (336.49) [336.49]	79.44 (-163.60) [50]
134	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	13.88 (0.00) [0]
135	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	24.01 (0.00) [0]
136	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	7.61 (0.00) [0]
137	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	19.71 (0.00) [0]
138	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	6.57 (0.00) [0]
139	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	56.77 (0.00) [0]
140	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	87.30 (0.00) [0]
141	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	5.29 (0.00) [0]
142	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
143	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	0.00 (0.00) [0]
144	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	0.00 (0.00) [0]
145	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	0.00 (0.00) [0]
146	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
147	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	141.44 (0.00) [46]
148	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	88.48 (0.00) [39]
149	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	102.94 (0.00) [39]
150	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	100.90 (0.00) [38]

151	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	60.55 (0.00) [39]
152	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	44.52 (0.00) [49]
153	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	42.55 (0.00) [50]
154	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	127.87 (0.00) [0]
155	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	95.97 (0.00) [0]
156	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	298.08 (13.93) [57]
157	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [339.55]	282.82 (-56.97) [57]
158	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [5/2021]	429.52 (-) [340.00]	238.26 (-89.52) [57]
159	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (9/2020) [0/0]	336.25 (369.96) [336.25]	301.49 (0.00) [0]
160	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	98.42 (0.00) [0]
161	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	123.44 (0.00) [0]
162	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	0.00 (0.00) [0]
163	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
164	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	50.27 (0.00) [0]
	SIKKIM				
	Railways				
165	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [8,600.00]	619.18 (7,260.52) [0]
	Road Transport And Highways				
166	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	0.00 (0.00) [0]
167	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	0.00 (0.00) [0]
168	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (12/2020) [0/0]	182.28 (369.64) [269.14]	274.07 (86.86) [0]
169	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (12/2020) [0/0]	151.59 (370.01) [151.59]	282.36 (0.00) [0]
170	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI	4/2013	8/2013	166.27	243.59

	ROAD IN SOUTH SIKKIM.		(12/2020) [0/0]	(359.92) [166.27]	(0.00) [0]
171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	85.64 (0.00) [0]
172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	24.70 (0.00) [0]
173	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
174	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	11.03 (0.00) [0]
175	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	0.78 (0.00) [0]
176	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	0.00 (0.00) [0]
177	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	0.00 (0.00) [0]
178	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	261.20 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
179	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [0/0]	438.28 (-) [438.28]	335.58 (0.00) [0]
	<u>Railways</u>				
180	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
181	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	359.11 (0.00) [0]
182	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	2.60 (0.00) [0]
183	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	0.00 (0.00) [0]
184	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	0.00 (0.00) [0]
185	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	0.00 (0.00) [0]
186	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	0.00 (0.00) [0]
187	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [197.67]	5.75 (0.00) [0]
188	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (7/2021) [7/2021]	171.90 (-) [171.90]	110.19 (0.00) [11]
	<u>Rural Development</u>				

189	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [10/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [70]
190	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [10/2021]	202.61 (227.00) [207.12]	190.22 (4.51) [58]
191	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [12/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [60]
	Total			1,13,904.42 (39,301.91) [1,64,062.63]	68,368.47 (50,158.21)
