

**389th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
March 2018**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India

Ministry of Statistics and Programme Implementation

Infrastructure and Project Monitoring Division

R.K.Puarm, East Block 6, Level 7

New Delhi-110066

Website: www.cspm.gov.in

Abbreviations used in the report

AAI Airport Authority of India Ltd.
AERB Atomic Energy Regulatory Board
AIBP Accelerated Irrigation Benefit Programme
AIR All India Radio
APW Active Process Water
ATU Atomic Treating Unit
BCM Billion Cubic Meter
BHEL Bharat Heavy Electricals Ltd.
BHPV Bharat Heavy Plates & Vessel Ltd.
BLU Boiler Light Up
BOLT Build , Operate, Lease & Transfer
BPST Bureau of Parliamentary Studies & Training
CCEA Cabinet Committee on Economic Affairs
CCU Catalytic Cracking Unit
CDS Crude Distribution System
CDU Crude Distillation Unit
CEA Central Electricity Authority
CEC Central Empowered Committee
CHP Coal Handling Plant
CLW Chittaranjan Locomotive Works
CMPDI Central Mine Planning & Design Institute
COS Committee of Secretaries
COR Cost Overrun
CPP Captive Power Plant
CRIS Centre for Railway Information System
CRL Cochin Refinery Ltd.
CSL Cochin Shipyard Ltd.
CTU Crude Topping Unit
DAE Department of Atomic Energy
DB Dumb Barges
DCME Digital Circuit Multiplexing Equipment
DGMS Director General Mines Safety
DHDS Diesel Hydro Desulphurisation project
DOA Date of Approval
DOC Date of Commissioning
DOT Department of Telecommunication
DVC Damodar Valley Corporation
ECL Eastern Coalfields Ltd.
EIL Engineers India Ltd.
EMP Environment Management Plan
EOT Electrical Overhead Travelling crane
ESP Electrostatic Precipitator
FCCU Fluidised Catalytic Cracker Unit
ERP Enterprise Resource Planning
FE Foreign Exchange
FOIS Freight Operation Information System
FPU Feed Preparation Unit
GAIL Gas Authority of India Ltd.
GC Gauge Conversion
GDS Gateway Digital Switch
GIS Gas Insulated Station
GT Gas Turbine
GTPP Gas Turbine Power Plant
HCU Hydro- cracker Unit
HEC Heavy Engineering Corporation
HEMM Heavy Equipment & Mining Machinery
HEP Hydro Electric Project
HPCL Hindustan Petroleum Corporation Ltd.
HRT Head Race Tunnel
HSCL Hindustan Steel Construction Ltd.
HVDC High Voltage Direct Current
IAAI International Airport Authority of India
ICT Inter Connecting Transformer

IDC Interest During construction
IFFCO Indian Farmer Fertilizer Co-operative Ltd.
IMG Inter Ministrial Group
IOC Indian Oil Corporation Ltd.
IPCL Indian Petrochemicals Ltd.
KV Kilo Volts.
L&T Larsen & Toubro
LEP Life Extension Program
LOI Letter of Intent
LPG Liquified Petroleum Gas
LSTK Lump sum Turnkey contract
MAMC Minning & Allied Machinery Corporation.
MFL Madras Fertilizer Ltd.
MGCL Madras Gas Cracker Complex
MIS Management Information System
MMSCMD Million Metric Standard Cubic Meter day
MMT Million Metric Tonnes
MOE&F Ministry of Environment & Forest
MT Metric Tonnes
MTY Metric Tonne per year
MU Million Unit
MW Mega Watts
NAC New Anticipated Cost
NALCO National Aluminium Company
NBCC National Building Construction Corporation.
NCL Northern Coalfields Ltd
NEC North East Council
NEEPCO North-Eastern Electric Power Corporation Ltd.
NFL National Fertilizer Ltd.
NH National Highway
NHPC National Hydro-Electric Power Corporation
NIRE National Institute of Renewable Energy
NIT Notice Inviting Tender
NJPC Nathpa Jhakri Power Corporation Ltd.
NGN Next Generation Network
NLC Neyveli Lignite Corporation Ltd.
NMDC National Mineral Development Corporation Ltd.
NPC Nuclear Power Corporation Ltd.
NRL Numaligarh Refinery Ltd.
OB Over Burden
OC Opencast
OECE Overseas Economic Co-operation Fund
ONGC Oil & Natural Gas Commission
OPGC Orissa Power Generation Corporation
P & M Plant & Machinery
PERT Project Evaluation & Review Technique
PSTN Public Switched Telephone Network
PHT Primary Heat Transport
PIB Public Investment Board
PSLW Powered Support Longwall
QRC Quick Roll Changer
RAPP Rajasthan Atomic Power Plant
RCE Revised Cost Estimates
RCF Railway Coach Factory
ROB Road Over Bridge
ROH Regular Overhauling
RTU Remote Terminal Unit
SAIL Steel Authority of India Ltd.
SCI Shipping Corporation of India Ltd.
SDH Synchronous Digital Hierarchy
SG Steam Generator
SP Self Propelled
ST Steam Turbine
STPS Super Thermal Power Station
SUR Sulphur Recovery Unit
SWSU Sour Water Stripping Unit
TBM Tunnel Boring Machine
TG Turbo Generator

TPA Tonnes Per Annum
TPS Thermal Power Station
TOR Time Overrun
TPY Tonnes per year
UG Under Ground
ULDCS Unified Load Despatch & Communication Scheme
VDU Vacuum Distillation Unit
WHRB Waste Heat Recovery Boiler
WO_DOC With out Date of Commissioning
WO_ODC With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for March 2018 contains information on the status of the 1315 Central Sector Infrastructure Projects costing ₹150 crore and above. During March 2018, 8 projects (7 projects are in Power, 1 project in Petroleum Sector) has reported completion.

2. During the reference month, out of 1315 projects, 254 projects are delayed with respect to their original schedules and 44 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 44 projects, 16 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	530	46	2	1
2	RAILWAYS	334	29	2	0
3	PETROLEUM	124	27	1	1
4	POWER	117	62	23	11
5	COAL	92	37	7	0
6	URBAN DEVELOPMENT	39	21	4	0
7	STEEL	30	15	1	1
8	HEALTH AND FAMILY WELFARE	14	6	0	0
9	TELECOMMUNICATIONS	9	2	2	1
10	SHIPPING AND PORTS	7	2	1	0
11	FERTILISERS	6	2	0	0
12	ATOMIC ENERGY	4	4	1	1
13	MINES	4	0	0	0
14	CIVIL AVIATION	2	1	0	0
15	DEFENCE PRODUCTION	2	0	0	0
16	HEAVY INDUSTRY	1	0	0	0
Total		1315	254	44	16

3. Total original cost of implementation of the 1315 projects was ₹16,23,254.71 crore and their anticipated completion cost is likely to be ₹18,41,400.35 crore, which reflects

overall cost overruns of ₹2,18,145.64 crore (13.44% of original cost). The expenditure incurred on these projects till March 2018 is ₹6,63,626.77 crore, which is 36.04% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-04-2018)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	74.68
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	78.87
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	296.05	3.53
2	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	172.99	3.16
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	13.31
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	122.78
PETROLEUM					
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	330.35	62.78
4	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	45.83
5	PARADIP HALDIA DURGAPUR LPG PIPELINE	02/2011	913.00	1330.00	45.67
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	177.39
2	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4401.90	165.65
3	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1078.31	156.12
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
5	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1337.76	133.06

RAILWAYS					
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	614.00	1568.48
3	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	9658.00	1227.45
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27946.00	1017.84
5	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
ROAD TRANSPORT AND HIGHWAYS					
1	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	114.56
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
3	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
4	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	255.00	28.18
4	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED	12/2014	274.85	321.94	17.13
5	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	12.88
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	17.79
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	17.50
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	44.75
3	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN	08/2014	350.02	479.87	37.10

4	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58
5	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-04-2018)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	2608.00
CIVIL AVIATION					
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	244.07
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
2	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	BHANEAGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	296.05	10.10
2	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	172.99	5.30
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	22.48
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROLEUM					
1	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	05/2013	4124.35	5725.50	1601.15
2	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	03/2014	3076.00	4190.00	1114.00

3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
4	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	5245.96	657.67
5	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	11149.82
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9142.58	5020.58
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.75	4479.16
5	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9141.97	4387.55
RAILWAYS					
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27946.00	25446.00
2	RISHIKESH - KARNAPRAYAG NEW LINE	04/2011	4295.30	16216.00	11920.70
3	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	9658.00	8930.44
4	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
5	BHAIRABI SAIRONG, NL, NEFR	04/2008	619.34	4600.00	3980.66
ROAD TRANSPORT AND HIGHWAYS					
1	GUJARAT/MAHARASHTRA BORDSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	1728.77
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
3	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
4	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	03/2017	993.16	1434.00	440.84
5	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	03/2017	2064.99	2447.00	382.01
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	255.00	56.06
4	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED	12/2014	274.85	321.94	47.09

5	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	31.48
	STEEL				
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	31.22
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	26.21
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
	URBAN DEVELOPMENT				
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
3	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	151.74
4	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN	08/2014	350.02	479.87	129.85
5	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	108.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1315 projects, 315 are on schedule, 254 are delayed, 345 projects reported cost overrun and 98 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 190 if delay is calculated on the basis of latest schedule of completion. Further, 138 projects have been sanctioned without original commissioning date and for 593 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 254 delayed projects, 49 projects have overall delay in the range of 1 to 12 months, 47 projects have delay in the range of 13 to 24 months, 87 projects have delay in the range of 25 to 60 months and 71 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-04-2018)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	06/2018	93
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
COAL					
1	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2019	108
3	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2020	108
4	MAGADH OC 20 MTY (CCL)	08/2008	07/2012	03/2021	104
5	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2018	96
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	04/2019	29
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	02/2016	12/2017	04/2018	4
HEALTH AND FAMILY WELFARE					
1	AIIMS - OPD(NEW)	08/2014	05/2017	09/2018	16
2	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	08/2019	15
3	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	06/2018	13
4	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	03/2018	10
5	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	08/2018	6
PETROLEUM					
1	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	06/2019	93
2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2019	74
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
4	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	09/2018	66
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	11/2018	66
POWER					

1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2020	135
2	BARH STPP(3X660MW) NTPC	02/2005	01/2011	04/2021	123
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	09/2018	118
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	10/2018	106
5	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	03/2022	103
RAILWAYS					
1	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
3	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2020	192
4	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	05/2008	03/2023	178
5	GOELKERA-MANOHARPUR,(LD)(SER)	03/1997	02/2006	12/2019	166
ROAD TRANSPORT AND HIGHWAYS					
1	NALBARI T BIJNI (AS-7)	12/2003	04/2008	03/2018	119
2	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	09/2018	118
3	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	03/2018	117
4	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	04/2009	10/2018	114
5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008	03/2018	112
SHIPPING AND PORTS					
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	12/2018	96
2	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	12/2017	05/2020	29
STEEL					
1	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
2	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	06/2018	63
3	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	10/2018	41
4	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	03/2019	29
5	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	02/2014	12/2016	12/2018	24
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	04/2020	57
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	03/2018	9
URBAN DEVELOPMENT					
1	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	06/2018	75
2	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70

3	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2018	65
4	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	10/2018	47
5	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	11/2018	44

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2017, out of 1061 projects on the monitor of this Ministry, 241 projects reported cost overruns and 326 projects reported time overruns; while during March 2018, out of 1315 projects, 345 projects reported cost overruns and 254 projects reported time overruns. In comparison to April 2017, number of projects reporting cost overrun has increased from 22.71% to 26.23% whereas projects reporting time overruns have decreased from 30.73% to 19.32%.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-04-2018)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	522.95	01/2011	N.A.
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	26.44	09/2018	06/2020
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	168.58	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	6.22	09/2019	09/2019
3	NEYVELI SOLAR POWER PROJECT 130 MW	05/2016	687.28	767.00	756.08	06/2017	04/2018
4	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	15.30	03/2022	03/2022
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	1493.82	11/2021	11/2021
FERTILISERS							
1	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	426.72	426.72	1.32	04/2020	04/2020
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	414.11	141.00	11/2013	N.A.
3	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	77.50	09/2018	09/2018
4	NEIGRIHMS SHILLONG MEGHALYA	10/2016	363.99	363.99	21.00	05/2018	08/2019
5	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARAstra	08/2017	274.19	274.19	29.68	03/2019	03/2019
HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2289.00	09/2011	N.A.
MINES							
1	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	483.00	483.00	0.00	04/2021	04/2021
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY	06/2007	736.65	571.47	542.96	09/2011	06/2019

	VESSELS(OSV)						
3	SIX PIPELINE REPLACEMENT PROJECT	03/2009	181.02	181.02	168.93	01/2017	05/2018
4	TWENTY NOS. FEEDER GAS LINES	03/2009	228.64	256.41	147.21	12/2016	05/2018
5	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	1.03	01/2019	09/2019
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	9979.37	09/2010	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	2657.86	10/2017	12/2016
3	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	03/2012	198.63	198.63	137.93	09/2014	06/2018
4	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	01/2014	1788.41	2333.71	1223.54	09/2017	09/2018
5	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	156.50	04/2016	06/2018
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.48	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	484.14	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	614.00	262.63	N.A.	03/2020
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	749.69	0.00	06/2005	N.A.
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	634.48	629.43	03/1994	N.A.
ROAD TRANSPORT AND HIGHWAYS							
1	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	520.01	520.01	0.00	N.A.	N.A.
2	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	0.00	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	319.68	0.00	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	01/2018
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	N.A.

2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	413.91	12/2010	12/2018
4	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	600.00	257.90	1.45	12/2017	05/2020
STEEL							
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	200.00	200.00	131.15	03/2018	03/2018
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	7642.00	07/2015	04/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	172.30	06/2017	03/2018
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	215.30	0.00	05/2018	05/2018
4	MAHARASHTRA ACCESS (LOT 1)	08/2017	212.70	212.70	0.00	05/2018	05/2018
5	MAHARASHTRA CORE (LOT1)	08/2017	167.68	167.68	0.00	04/2018	04/2018
URBAN DEVELOPMENT							
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
2	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	10/2019
3	DELHI MRTS PHASE-III	09/2011	38585.00	38585.00	34270.32	03/2016	03/2018
4	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	884.30	884.30	582.84	12/2015	05/2018
5	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5181.79	0.00	07/2017	12/2019

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-04-2018)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	11554.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	522.95
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	302.96	0.00	334.77
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	0.00	410.19
3	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	260.71
4	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	565.86
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	219.29
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	0.00	2289.00
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	871.35	0.00	961.00
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	6684.84
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	9979.37
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	6424.41
4	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	0.00	3521.00
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	6974.42
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	484.14
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	274.56	629.43
3	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	538.21
4	KHURDA ROAD-BOLANGIR(NL)ECOR	04/1994	470.21	0.00	1004.23
5	AMRAVATI-NARKHER NL(CR)	06/1994	663.01	668.34	707.51
ROAD TRANSPORT AND HIGHWAYS					
1	NAGPUR - KONDHALI	09/2005	168.00	0.00	279.92
2	TRICHY - KARUR	03/2007	516.00	0.00	761.19
3	TALEGAON-AMRAVATI	11/2009	567.00	0.00	1055.94

4	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANON AND NAGPUR BYPASS	04/2010	1170.52	0.00	2263.02
5	MURADABAD-BAREILY	04/2010	1267.00	0.00	2667.96
SHIPPING AND PORTS					
1	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	247.00	255.02
2	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	275.98
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
3	EXPANSION OF BHILAI STEEL PLANT	08/2010	17265.00	0.00	18549.96
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	14784.59

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on as on 01-04-2018)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	N.A.	N.A.
COAL					
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	RAJMAHAL OC EXP.	09/2009	03/2014	N.A.	N.A.
3	KAPURIA UG(PSLW)	08/2011	04/2017	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	N.A.
3	AIIMS-RAE BARELI-HOUSING	10/2013	11/2013	N.A.	N.A.
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	09/2011	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT	01/2006	01/2012	N.A.	N.A.

	PADUR				
2	PARADIP-RAIPUR-RANCHI PIPELINE	08/2009	12/2016	N.A.	N.A.
3	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
4	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
5	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	03/2015	N.A.	11/2017
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	12/2016
3	BOKARO THERMAL POWER STATION-A	08/2006	12/2011	N.A.	N.A.
4	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	02/2011	N.A.	N.A.
5	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	N.A.	N.A.
4	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	03/1994	N.A.	N.A.
5	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	01/1991	05/2016	N.A.	05/2016

3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	08/2016
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	01/1991	10/2016	N.A.	10/2016
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	10/2016
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	N.A.	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
3	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	06/2017	N.A.	N.A.
4	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED	12/2014	04/2017	12/2017	N.A.
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.
4	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	07/2011	12/2015	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
URBAN DEVELOPMENT					
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON	08/2007	N.A.	N.A.	N.A.

	SOUTH OF MUSI IN ZONE 2				
2	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
3	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	N.A.	N.A.
4	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	06/2014	03/2017	N.A.	N.A.
5	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	07/2016	N.A.	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

12. The status as on 31.03.2018 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

13. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	530	2
2	RAILWAYS	334	2
3	PETROLEUM	124	1
4	POWER	117	23
5	COAL	92	7
6	URBAN DEVELOPMENT	39	4
7	STEEL	30	1
8	HEALTH AND FAMILY WELFARE	14	0
9	TELECOMMUNICATIONS	9	2
10	SHIPPING AND PORTS	7	1
11	FERTILISERS	6	0
12	ATOMIC ENERGY	4	1
13	MINES	4	0
14	CIVIL AVIATION	2	0
15	DEFENCE PRODUCTION	2	0
16	HEAVY INDUSTRY	1	0
	Total	1315	44

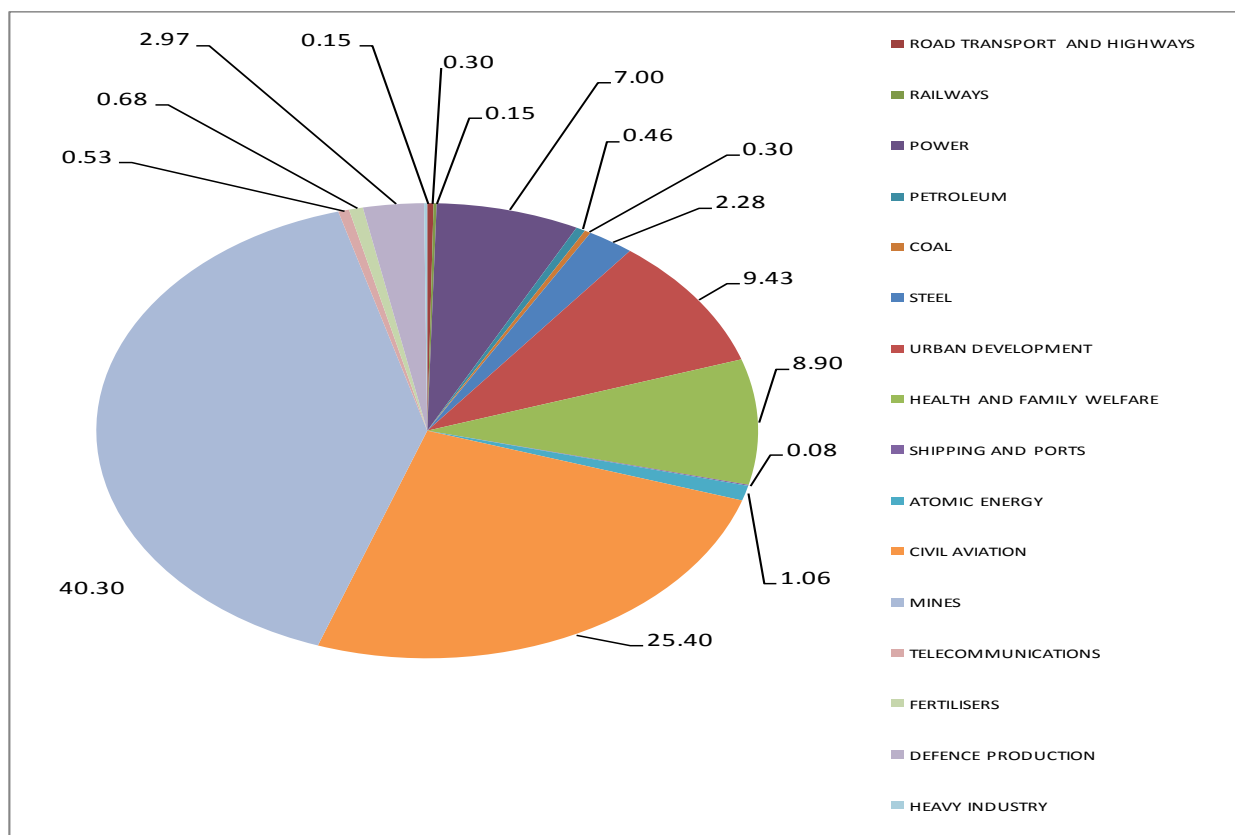


TABLE-2

Month wise List of Completed Projects Costing Rs.150 Crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2017			
	<u>PETROCHEMICALS</u>			
1	ASSAM GAS CRACKER PROJECT (BRAHMAPUTRA CRECKER & POLYMER LTD.) - [N16000106]	5,460.61	04/2012	9,895.05
	<u>POWER</u>			
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000053]	509.66	11/2011	566.26
3	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000081]	1,216.83	08/2012	1,074.89
4	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000101]	1,961.87	05/2014	1,817.05
5	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000117]	1,422.85	01/2015	1,490.42
6	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000145]	1,909.24	06/2015	1,093.03
7	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000163]	303.07	07/2016	48.50
8	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000173]	972.42	11/2017	92.20
	May,2017			
	<u>CIVIL AVIATION</u>			
9	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000071]	217.60	03/2015	196.94
	June,2017			
	<u>STEEL</u>			
10	SMS-1 CONVERTERS REVAMPING (RASTRIYA ISPAT NIGAM LIMITED) - [N12000090]	404.16	07/2015	394.74
	<u>POWER</u>			
11	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000166]	378.71	10/2016	257.90
12	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000167]	400.47	04/2017	265.20

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000211]	187.04	06/2018	54.60
	July,2017			
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000094]	752.64	07/2013	633.62
15	WARDHA-HYDERABAD 765 KV LINK (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000183]	3,662.02	05/2018	2,302.40
	August,2017			
16	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000153]	1,575.30	05/2016	1,328.51
	September,2017			
	ATOMIC ENERGY			
17	KUDANKULAM APP (NPCIL) (NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100040]	13,171.00	12/2008	22,340.00
	CIVIL AVIATION			
18	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000069]	335.61	05/2012	305.59
	PETROLEUM			
19	DE-BOTTLENECKING OF SMPL (INDIAN OIL CORPORATION LIMITED) - [N16000089]	1,584.00	03/2017	1,355.45
20	INTEGRATED REFINERY EXPANSION PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000143]	16,504.00	03/2017	15,090.99
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000146]	666.00	11/2015	606.13
22	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000149]	586.00	08/2015	440.20
23	MARKETING TOP AT KORBA (INDIAN OIL CORPORATION LIMITED) - [N16000186]	141.86	09/2016	174.37
24	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000205]	1,714.00	06/2017	1,067.89
	POWER			
25	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000112]	2,127.51	07/2014	2,582.69
26	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000125]	9,569.76	06/2015	7,311.17
27	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000191]	3,984.03	01/2013	3,290.44
	October,2017			

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>COAL</u>			
28	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU (NEYVELI LIGNITE CORPORATION) - [N06000110]	364.75	10/2014	333.05
	<u>STEEL</u>			
29	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS (RASTRIYA ISPAT NIGAM LIMITED) - [N12000089]	877.73	07/2015	747.81
30	TURBO BLOWER - 5 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000092]	280.00	09/2016	157.09
	<u>PETROLEUM</u>			
31	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000180]	163.88	07/2016	82.45
32	50 MW 10 PERCENT WIND ENERGY POWER PROJECT Central Sector Projects(OIL INDIA LIMITED) - [N16000208]	500.00	03/2017	368.24
33	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) (INDIAN OIL CORPORATION LIMITED) - [N16000217]	150.00	07/2014	251.90
	<u>RAILWAYS</u>			
34	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR (SOUTH WESTERN RAILWAY) - [220100183]	295.00	-	1,509.88
35	GURIYA-MARWAR AND KARJODA-PALANPUR (NORTH WESTERN RAILWAY) - [N22000154]	239.73	-	195.42
36	HOSADURGA - CHICKJAJUR (28.89 KM) (SOUTH WESTERN RAILWAY) - [N22000324]	203.40	-	282.69
	<u>URBAN DEVELOPMENT</u>			
37	BANGALORE METRO RAIL PROJECT (METROPOLITAN RAPID TRANSPORT PROJECTS) - [N28000008]	6,395.00	06/2011	14,200.11
38	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000074]	315.00	06/2015	302.82
39	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000077]	405.01	12/2014	349.54
	November, 2017			
	<u>MINES</u>			
40	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra Private(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [N10000008]	355.13	11/2016	355.13
41	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN PPP (ANNUITY)(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [N10000009]	344.50	11/2016	344.50

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
42	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000186]	550.06	03/2018	470.07
43	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000207]	244.19	07/2018	123.33
	December,2017			
	<u>COAL</u>			
44	PURNADIH OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000085]	210.98	03/2013	206.80
	<u>STEEL</u>			
45	3RD CONVERTER AND 4TH CASTER (RASTRIYA ISPAT NIGAM LIMITED) - [N12000088]	974.76	07/2016	676.93
	<u>HEALTH AND FAMILY WELFARE</u>			
46	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000004]	444.70	12/2015	326.30
47	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000005]	196.70	01/2016	170.00
	January,2018			
	<u>STEEL</u>			
48	REBUILDING OF COB-7 AT BSL (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000083]	245.67	05/2016	196.21
	<u>POWER</u>			
49	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000159]	908.08	06/2016	741.63
50	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000162]	829.98	08/2016	423.52
51	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000203]	302.49	02/2016	270.77
	<u>SHIPPING AND PORTS</u>			
52	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST (RAIL VIKAS NIGAM LTD.) - [N25000059]	245.67	04/2009	350.68
53	ACQUISITION OF SECONDHAND/ RESALE OF VLGC (SHIPPING CRP. OF INDIA) - [N25000071]	215.00	09/2017	0.01

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	February,2018			
	PETROLEUM			
54	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000136]	600.17	12/2014	707.33
55	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY Central Sector Projects(CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000218]	367.11	04/2017	251.63
56	PALAKKAD LPG PLANT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000225]	184.00	12/2017	100.20
	POWER			
57	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000116]	1,746.65	08/2014	1,977.30
58	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000119]	368.72	07/2006	1,341.24
	RAILWAYS			
59	KANPUR KASGANJ MATHURA(GC) NER (NORTH EASTERN RAILWAY) - [220100197]	677.97	-	1,781.64
60	RAJATGARH-BARANG(LD),ECOR (RAIL VIKAS NIGAM LTD.) - [220100286]	166.16	02/2009	371.62
61	RAICHUR-GUNTAKAL(DL)(SCR) (RAIL VIKAS NIGAM LTD.) - [220100329]	136.62	12/2007	379.62
62	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000082]	170.00	03/2011	440.72
63	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) (SOUTH WESTERN RAILWAY) - [N22000107]	482.00	03/2013	992.61
64	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) (NORTH WESTERN RAILWAY) - [N22000114]	516.23	03/2014	694.13
65	KATAKHAL TO BHAIRABI (NORTH EAST FRONTIER RAILWAY) - [N22000126]	227.90	12/2012	426.94
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000127]	1,676.31	03/2009	7,241.49
67	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) (NORTH WESTERN RAILWAY) - [N22000153]	739.65	-	796.25
68	TAMLUK-BASULYA-SUTAHATA DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000163]	171.02	06/2013	241.76
69	PEN ROHA DOUBLING (CENTRAL RAILWAYS) - [N22000254]	98.74	-	366.50
70	PANVEL PEN DOUBLING (CENTRAL RAILWAYS) - [N22000255]	96.16	-	274.54
71	JHARSUGUDA-RENGALI DOUBLING (EAST COAST RAILWAY) - [N22000317]	201.00	-	243.26
72	ROHTAK - BHIWANI DOUBLING (NORTH WESTERN RAILWAY) - [N22000331]	400.00	-	0.10

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
73	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) (NORTH EASTERN RAILWAY) - [N22000345]	836.26	-	1,026.65
74	DUDHNOI-MENDHIPATHAR (NORTH EAST FRONTIER RAILWAY) - [N22000378]	315.64	-	313.45
75	HARMUTI-NAHARLAGUN (NORTH EAST FRONTIER RAILWAY) - [N22000382]	614.54	-	564.68
76	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) (NORTH EAST FRONTIER RAILWAY) - [N22000385]	971.22	-	834.11
77	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS (NORTH EAST FRONTIER RAILWAY) - [N22000386]	4,300.00	-	4,465.80
78	NEW GUWAHATI-DIGARU-PATCH DOUBLING (NORTH EAST FRONTIER RAILWAY) - [N22000387]	180.09	-	157.12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
79	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000144]	852.00	03/2013	913.37
80	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000343]	341.61	09/2017	319.04
	<u>SHIPPING AND PORTS</u>			
81	ACQUISITION OF SECONDHAND/ RESALE OF SUEZMAX TANKER Central Sector Projects(SHIPPING CRP. OF INDIA) - [N25000069]	193.00	04/2017	193.00
	<u>URBAN DEVELOPMENT</u>			
82	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000059]	188.87	12/2015	193.29
	March,2018			
	<u>PETROLEUM</u>			
83	NEW 250 TMTPLPG PLANT AT PANAGARH (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000222]	190.45	09/2017	130.15
	<u>POWER</u>			
84	KISHANGANGA HEP (3X110 MW) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000031]	3,642.04	01/2016	5,301.63
85	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000077]	4,404.57	01/2015	3,700.95
86	SYSTEM STRENGTHENING XII OF SR (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000085]	232.34	06/2012	246.99
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000128]	723.63	11/2014	736.62
88	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000209]	162.11	05/2018	125.00

Month wise List of Completed Projects Costing Rs.150 Crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
89	NORTH EASTERN REGION STRENGTHENING SCHEME IV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000216]	409.19	05/2018	212.50
90	50 MW SOLAR POWER PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000251]	287.48	03/2018	187.57

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2018			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000123]	940.00	07/2012	1,415.36
2	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000153]	359.00	09/2013	2.74
3	BHUBANESWAR TO PURI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000195]	500.29	08/2013	869.91
4	4-LANING OF RAIGANJ-DALKOLA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000204]	580.43	08/2013	226.67
5	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000225]	828.00	09/2014	870.15
6	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH- 200 FROM KM 301.89 TO KM 427.85 INCLUDING KM(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000366]	996.37	12/2017	0.00
7	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000588]	725.95	06/2019	0.00
	September,2018			
	<u>POWER</u>			
8	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [180100261]	358.42	12/2008	0.00
9	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000099]	1,585.12	11/2013	1,452.46
10	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000114]	552.44	02/2014	501.60
11	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000170]	188.75	02/2017	0.00
12	PATAN WIND FARM SITE, GUJARAT 50 MW (THDC INDIA LIMITED) - [N18000204]	315.00	10/2016	311.96
13	KANDORNA AND BHANWAD WIND FARM (THDC INDIA LIMITED) - [N18000234]	415.49	03/2017	415.50
	October,2018			
14	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000259]	955.00	12/2015	74.00

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
15	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000260]	2,525.00	11/2017	564.00
	February,2018			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
16	BARSAT-KRISHNANAGAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000229]	867.00	02/2015	278.17
17	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000673]	985.41	03/2020	0.10
18	TWO LANE WITH PS OF KARAUKUDI-RAMANATHPURAM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000698]	652.55	08/2017	0.10


Summary of projects in the Flash Report for the month of March, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1304
Number of Projects completed/dropped/frozen in Current Month	8
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	21
Number of Projects in Current Month	1315

Brief Analysis

Project Status with respect to Original Schedule: Out of 1315 projects, 15 projects are ahead of schedule, 315 projects are on schedule 254 projects are delayed. 593 projects do not have fixed dates of commissioning. 138 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

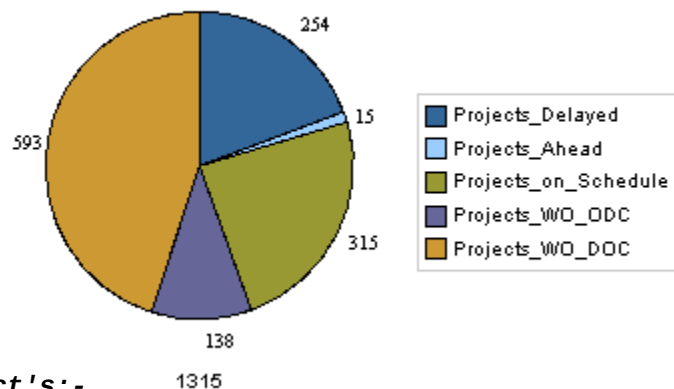

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1315 projects when sanctioned, was of the order of Rs. 1623254.71 crore but this was subsequently revised to Rs. 1841400.35 crore implying a cost overrun of 13.4%. The expenditure incurred on these projects till March, 2018 is Rs. 663626.77 crore, which is 36% of the anticipated cost of the projects.

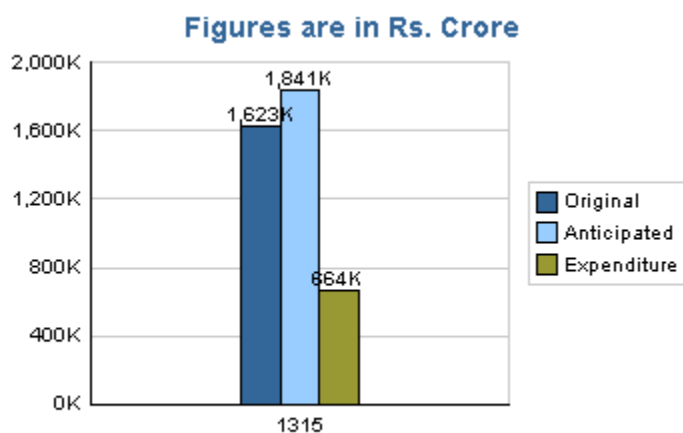


TABLE-4

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1304
No of Projects Completed/Dropped/Frozen in Current Month	8
No of Projects added in Current Month	21
No of Projects in Current Month	1315

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	254 (19.32%)	15 (1.14%)	315 (23.95%)	138 (10.49%)	593 (45.10%)	1315
Latest Approved (Date)	190 (14.45%)	11 (.84%)	387 (29.43%)	133 (10.11%)	594 (45.17%)	1315

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1145	14,12,598.76	15,68,920.84	5,07,180.94	32.30	1,56,322.08	11.10
Project with Revision in Cost	170	2,63,059.32	2,72,479.51	1,56,445.83	57.40	9,420.19	3.60
Total	1,315	16,75,658.08	18,41,400.35	6,63,626.77	36.04	1,65,742.27	9.89
Original Cost of All Projects							
Original Cost	1,315	16,23,254.71	18,41,400.35	6,63,626.77	36.04	2,18,145.64	13.44
Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	254	5,88,870.34	7,27,417.98	4,15,619.31	57.10	1,38,547.64	23.50
Latest Approved (RCE)	190	3,45,764.06	4,36,473.05	2,19,788.26	50.40	90,708.99	26.20
Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	44	91,664.03	1,12,638.55	78,853.68	70.00	20,974.52	22.90
Total	44	91,664.03	1,12,638.55	78,853.68	70.01	20,974.52	22.88

TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun[^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	74.69
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	92	89,695.08	89,199.09	-0.55	9	19,751.90	21,090.72	6.78
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	5.89
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	30	54,971.33	55,185.01	0.39	5	1,639.71	2,211.39	34.86
7	PETROLEUM	124	2,10,560.21	2,12,573.46	0.96	18	29,189.20	36,281.45	24.30
8	POWER	117	3,28,395.59	3,95,733.97	20.51	46	1,79,131.74	2,46,470.12	37.59
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	13.31
11	RAILWAYS	334	3,41,529.69	4,62,504.09	35.42	205	1,27,689.43	3,09,134.30	142.10
12	ROAD TRANSPORT AND HIGHWAYS	530	3,51,472.35	3,57,629.96	1.75	42	24,613.28	31,456.93	27.80
13	SHIPPING AND PORTS	7	4,262.08	4,807.68	12.80	5	1,234.68	2,122.38	71.90
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	39	1,42,902.14	1,47,933.23	3.52	6	17,021.00	22,244.19	30.69
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	2	453.64	469.04	3.39
Total		1315	16,23,254.71	18,41,400.35	13.44	345	4,20,259.34	7,07,467.50	68.34

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6
Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150 Crore and above

(All Cost/ Expenditure in Rs. Crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	61	97,970.05	1,02,492.35	4.62	9	7,754.42	13,515.83	74.30
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	6	9,755.78	25,584.87	162.25
3	ASSAM	44	26,450.20	36,075.50	36.39	14	9,855.89	19,638.74	99.26
4	BIHAR	81	69,841.31	86,662.38	24.08	21	33,916.51	51,033.53	50.47
5	GOA	9	4,043.51	4,058.91	0.38	2	453.64	469.04	3.39
6	GUJARAT	48	44,056.76	47,616.96	8.08	10	6,584.92	11,436.06	73.67
7	HARYANA	22	14,152.14	16,038.37	13.33	3	1,633.56	3,653.00	123.62
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	2	4,966.47	12,898.75	159.72
9	JAMMU AND KASHMIR	10	25,238.37	51,229.67	102.98	2	4,288.41	30,279.71	606.08
10	KARNATAKA	41	70,570.56	80,140.31	13.56	17	23,776.18	34,509.71	45.14
11	KERALA	20	22,456.58	29,047.66	29.35	7	7,359.98	13,951.06	89.55
12	MADHYA PRADESH	62	64,865.15	70,922.08	9.34	10	27,629.06	34,669.61	25.48
13	MAHARASHTRA	128	1,79,962.13	1,93,009.07	7.25	30	40,091.42	57,557.16	43.56
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	1227.45
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	642.73
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	252.94
18	ODISHA	80	81,553.38	90,298.41	10.72	19	19,508.27	28,269.59	44.91
19	PUNJAB	30	16,014.41	16,020.14	0.04	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	58	43,665.58	45,121.88	3.34	11	4,055.49	5,547.71	36.80
21	SIKKIM	6	2,537.08	5,585.45	120.15	3	2,036.94	5,085.59	149.67
22	TAMIL NADU	62	1,08,723.72	1,24,637.01	14.64	22	27,837.98	44,854.20	61.13
23	TRIPURA	10	3,991.45	8,658.23	116.92	7	2,909.18	7,575.96	160.42
24	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	1.62	18	28,085.24	31,019.93	10.45
25	WEST BENGAL	52	51,062.35	64,821.50	26.95	20	18,640.20	32,997.45	77.02
26	A & N ISLANDS	6	1,889.87	2016.59	6.70	1	314.61	441.33	40.28
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	18	53,421.22	53,688.53	0.50	2	1,375.86	1,789.17	30.04
29	CHHATISGARH	39	84,327.14	86,930.08	3.09	5	13,453.90	16,056.84	19.35
30	JHARKHAND	47	47,354.89	51,956.21	9.72	11	23,813.89	28,418.99	19.34
31	UTTARAKHAND	17	18,576.59	36,046.09	94.04	8	13,425.90	30,895.91	130.12
32	TELANGANA	36	24,952.57	27,652.97	10.82	11	3,122.03	6,013.52	92.62
33	MULTI STATE	176	2,99,041.56	3,01,840.01	0.94	68	76,005.19	1,34,684.97	77.21
Total		1315	16,23,254.71	18,41,400.35	13.44	345	4,20,259.34	7,07,467.50	68.34

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	4	67,120.00	69,728.00	36 - 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21 - 21
3	COAL	92	89,695.08	89,199.09	-0.55	37	20,254.10	20,473.06	10 - 132
4	FERTILISERS	6	1,781.92	1,793.57	0.65	2	680.64	692.29	4 - 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	30	54,971.33	55,185.01	0.39	15	46,113.39	45,900.79	2 - 72
7	PETROLEUM	124	2,10,560.21	2,12,573.46	0.96	27	52,800.78	56,324.77	1 - 93
8	POWER	117	3,28,395.59	3,95,733.97	20.51	62	2,27,593.11	2,74,183.52	3 - 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	6	1,689.51	1,711.99	6 - 16
11	RAILWAYS	334	3,41,529.69	4,62,504.09	35.42	29	39,411.20	1,10,498.39	12 - 261
12	ROAD TRANSPORT AND HIGHWAYS	530	3,51,472.35	3,57,629.96	1.75	46	33,499.34	36,060.12	2 - 119
13	SHIPPING AND PORTS	7	4,262.08	4,807.68	12.80	2	966.39	927.36	29 - 96
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	2	13,752.26	25,082.26	9 - 57
15	URBAN DEVELOPMENT	39	1,42,902.14	1,47,933.23	3.52	21	84,675.01	85,394.10	2 - 75
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	-
Total		1315	16,23,254.71	18,41,400.35	13.44	254	5,88,870.34	7,27,417.98	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	61	97,970.05	1,02,492.35	4.62	8	8,842.84	9,857.72	2 - 144
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	3	3,209.82	7,672.72	36 - 106
3	ASSAM	44	26,450.20	36,075.50	36.39	14	10,771.37	18,998.21	8 - 122
4	BIHAR	81	69,841.31	86,662.38	24.08	8	30,145.73	40,128.66	13 - 123
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	48	44,056.76	47,616.96	8.08	6	13,031.41	12,856.38	3 - 84
7	HARYANA	22	14,152.14	16,038.37	13.33	3	2,216.53	3,396.53	6 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	2	4,190.42	8,669.58	47 - 135
9	JAMMU AND KASHMIR	10	25,238.37	51,229.67	102.98	4	14,387.53	40,378.83	12 - 193
10	KARNATAKA	41	70,570.56	80,140.31	13.56	6	45,760.08	48,314.80	2 - 30
11	KERALA	20	22,456.58	29,047.66	29.35	5	10,696.37	11,461.23	9 - 65
12	MADHYA PRADESH	62	64,865.15	70,922.08	9.34	6	14,084.11	15,881.45	16 - 96
13	MAHARASHTRA	128	1,79,962.13	1,93,009.07	7.25	21	53,086.89	57,762.61	3 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	2	944.25	9,874.69	44 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	3	1,051.32	1,051.32	15 - 50
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	71 - 71
17	NAGALAND	7	8,126.79	10,276.79	26.46	4	2,049.11	4,199.11	36 - 60
18	ODISHA	80	81,553.38	90,298.41	10.72	14	25,222.81	27,449.44	5 - 108
19	PUNJAB	30	16,014.41	16,020.14	0.04	4	1,282.24	1,282.24	2 - 16
20	RAJASTHAN	58	43,665.58	45,121.88	3.34	7	15,246.13	15,931.75	6 - 63
21	SIKKIM	6	2,537.08	5,585.45	120.15	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	62	1,08,723.72	1,24,637.01	14.64	18	61,959.21	64,714.55	1 - 118
23	TRIPURA	10	3,991.45	8,658.23	116.92	1	813.34	3,451.00	72 - 72
24	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	1.62	7	22,219.45	22,318.63	4 - 61
25	WEST BENGAL	52	51,062.35	64,821.50	26.95	11	19,442.26	20,886.23	9 - 57
26	A & N ISLANDS	6	1,889.87	2016.59	6.70	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	18	53,421.22	53,688.53	0.50	7	42,999.38	43,372.17	5 - 29
29	CHHATISGARH	39	84,327.14	86,930.08	3.09	9	48,749.52	49,950.40	13 - 72
30	JHARKHAND	47	47,354.89	51,956.21	9.72	18	23,046.78	24,196.39	11 - 166
31	UTTARAKHAND	17	18,576.59	36,046.09	94.04	4	7,241.32	12,303.81	58 - 93
32	TELANGANA	36	24,952.57	27,652.97	10.82	13	15,416.24	15,770.36	3 - 132
33	MULTI STATE	176	2,99,041.56	3,01,840.01	0.94	42	82,404.37	1,20,318.84	3 - 261
Total		1315	16,23,254.71	18,41,400.35	13.44	254	5,88,870.34	7,27,417.98	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	4	69,305.00	69,728.00	36 - 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21 - 21
3	COAL	92	88,491.95	89,199.09	0.80	35	13,146.07	13,807.08	0 - 132
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	-
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	30	55,352.30	55,185.01	-0.30	14	30,588.39	30,375.79	2 - 72
7	PETROLEUM	124	2,14,323.69	2,12,573.46	-0.82	10	7,160.20	7,253.66	1 - 66
8	POWER	117	3,59,020.91	3,95,733.97	10.23	21	69,451.04	85,364.54	3 - 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	6	1,689.51	1,711.99	6 - 16
11	RAILWAYS	334	3,57,293.76	4,62,504.09	29.45	33	43,569.99	1,14,376.72	0 - 261
12	ROAD TRANSPORT AND HIGHWAYS	530	3,52,113.14	3,57,629.96	1.57	46	33,515.11	36,060.12	2 - 119
13	SHIPPING AND PORTS	7	4,344.09	4,807.68	10.67	1	669.46	669.46	96 - 96
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	418.26	418.26	9 - 9
15	URBAN DEVELOPMENT	39	1,43,054.99	1,47,933.23	3.41	18	75,936.42	76,266.10	5 - 75
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	-
Total		1315	16,75,658.08	18,41,400.35	9.89	190	3,45,764.06	4,36,473.05	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns[^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	7.45
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	92	88,491.95	89,199.09	0.80	7	19,411.53	20,221.55	4.17
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0.00
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	30	55,352.30	55,185.01	-0.30	3	1,586.97	1,777.68	12.02
7	PETROLEUM	124	2,14,323.69	2,12,573.46	-0.82	8	6,760.30	8,126.94	20.22
8	POWER	117	3,59,020.91	3,95,733.97	10.23	23	1,36,478.85	1,73,191.91	26.90
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	13.31
11	RAILWAYS	334	3,57,293.76	4,62,504.09	29.45	181	1,12,949.29	2,77,486.78	145.67
12	ROAD TRANSPORT AND HIGHWAYS	530	3,52,113.14	3,57,629.96	1.57	32	22,254.58	28,716.05	29.03
13	SHIPPING AND PORTS	7	4,344.09	4,807.68	10.67	3	655.33	1,130.98	72.58
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	39	1,43,054.99	1,47,933.23	3.41	4	16,317.21	21,387.55	31.07
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	2	454.00	469.04	3.31
Total		1315	16,75,658.08	18,41,400.35	9.89	269	3,38,390.03	5,68,286.02	67.94

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	93- 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21- 21
3	COAL	92	88,491.95	89,199.09	0.80	5	1,777.44	2,541.33	10- 132
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0- 0
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	30	55,352.30	55,185.01	-0.30	1	343.00	488.40	29- 29
7	PETROLEUM	124	2,14,323.69	2,12,573.46	-0.82	3	1,188.26	1,409.50	17- 20
8	POWER	117	3,59,020.91	3,95,733.97	10.23	9	35,848.14	51,761.64	12- 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	10- 10
11	RAILWAYS	334	3,57,293.76	4,62,504.09	29.45	22	25,343.51	95,152.71	34- 261
12	ROAD TRANSPORT AND HIGHWAYS	530	3,52,113.14	3,57,629.96	1.57	8	4,823.01	7,368.02	2- 112
13	SHIPPING AND PORTS	7	4,344.09	4,807.68	10.67	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	39	1,43,054.99	1,47,933.23	3.41	2	1,715.21	2,090.99	5- 36
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	0- 0
Total		1315	16,75,658.08	18,41,400.35	9.89	53	77,199.08	1,67,545.30	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	93- 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21- 21
3	COAL	92	89,695.08	89,199.09	-0.55	6	1,929.87	3,000.82	10- 132
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	29- 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	30	54,971.33	55,185.01	0.39	1	343.00	488.40	29- 29
7	PETROLEUM	124	2,10,560.21	2,12,573.46	0.96	11	22,117.54	27,360.33	9- 70
8	POWER	117	3,28,395.59	3,95,733.97	20.51	38	1,49,564.80	1,96,155.21	6- 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	0	0.00	0.00	0- 0
11	RAILWAYS	334	3,41,529.69	4,62,504.09	35.42	23	25,838.95	96,934.69	34- 261
12	ROAD TRANSPORT AND HIGHWAYS	530	3,51,472.35	3,57,629.96	1.75	9	4,961.94	7,523.02	2- 112
13	SHIPPING AND PORTS	7	4,262.08	4,807.68	12.80	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	13,334.00	24,664.00	57- 57
15	URBAN DEVELOPMENT	39	1,42,902.14	1,47,933.23	3.52	5	2,421.00	3,186.19	5- 70
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	0- 0
Total		1315	16,23,254.71	18,41,400.35	13.44	98	2,24,881.89	3,66,732.89	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	61	97,970.05	1,02,492.35	4.62	3	2,127.62	3,500.50	2 - 144
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	3	3,209.82	7,672.72	36 - 106
3	ASSAM	44	26,450.20	36,075.50	36.39	8	7,155.58	15,468.68	17 - 122
4	BIHAR	81	69,841.31	86,662.38	24.08	5	27,943.43	37,926.36	13 - 123
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	48	44,056.76	47,616.96	8.08	1	318.24	321.62	84 - 84
7	HARYANA	22	14,152.14	16,038.37	13.33	1	1,108.00	2,288.00	76 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	1	3,919.59	8,398.75	135 - 135
9	JAMMU AND KASHMIR	10	25,238.37	51,229.67	102.98	2	4,288.41	30,279.71	12 - 193
10	KARNATAKA	41	70,570.56	80,140.31	13.56	3	16,990.93	19,545.65	2 - 14
11	KERALA	20	22,456.58	29,047.66	29.35	2	5,195.35	5,960.21	9 - 17
12	MADHYA PRADESH	62	64,865.15	70,922.08	9.34	3	12,585.15	14,382.49	21 - 96
13	MAHARASHTRA	128	1,79,962.13	1,93,009.07	7.25	9	15,706.53	21,470.35	12 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	71 - 71
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	60 - 60
18	ODISHA	80	81,553.38	90,298.41	10.72	2	12,715.67	14,942.60	10 - 58
19	PUNJAB	30	16,014.41	16,020.14	0.04	0	0.00	0.00	-
20	RAJASTHAN	58	43,665.58	45,121.88	3.34	3	1,832.95	2,518.57	37 - 63
21	SIKKIM	6	2,537.08	5,585.45	120.15	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	62	1,08,723.72	1,24,637.01	14.64	4	7,898.70	11,756.97	10 - 118
23	TRIPURA	10	3,991.45	8,658.23	116.92	1	813.34	3,451.00	72 - 72
24	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	1.62	1	195.42	294.60	61 - 61
25	WEST BENGAL	52	51,062.35	64,821.50	26.95	2	7,027.98	8,449.48	9 - 57
26	A & N ISLANDS	5	1,575.26	1,575.26	0.00	0	0.00	0.00	-
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	18	53,421.22	53,688.53	0.50	1	1,219.21	1,592.00	5 - 5
29	CHHATISGARH	39	84,327.14	86,930.08	3.09	2	11,998.43	13,199.31	24 - 60
30	JHARKHAND	47	47,354.89	51,956.21	9.72	3	15,528.33	16,677.94	20 - 166
31	UTTARAKHAND	17	18,576.59	36,046.09	94.04	4	7,241.32	12,303.81	58 - 93
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
33	TELANGANA	36	24,952.57	27,652.97	10.82	3	830.76	1,287.76	60 - 132
34	MULTI STATE	176	2,99,041.56	3,01,840.01	0.94	26	53,180.14	91,259.79	6 - 261
Total		1315	16,23,254.71	18,41,400.35	13.44	98	2,24,881.89	3,66,732.89	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	128	0
2	ROAD TRANSPORT AND HIGHWAYS	111	1
3	POWER	62	11
4	PETROLEUM	47	1
5	COAL	12	0
6	URBAN DEVELOPMENT	11	0
7	STEEL	9	1
8	ATOMIC ENERGY	4	1
9	TELECOMMUNICATIONS	2	1
10	MINES	1	0
11	HEAVY INDUSTRY	1	0
12	SHIPPING AND PORTS	1	0
	Total	389	16

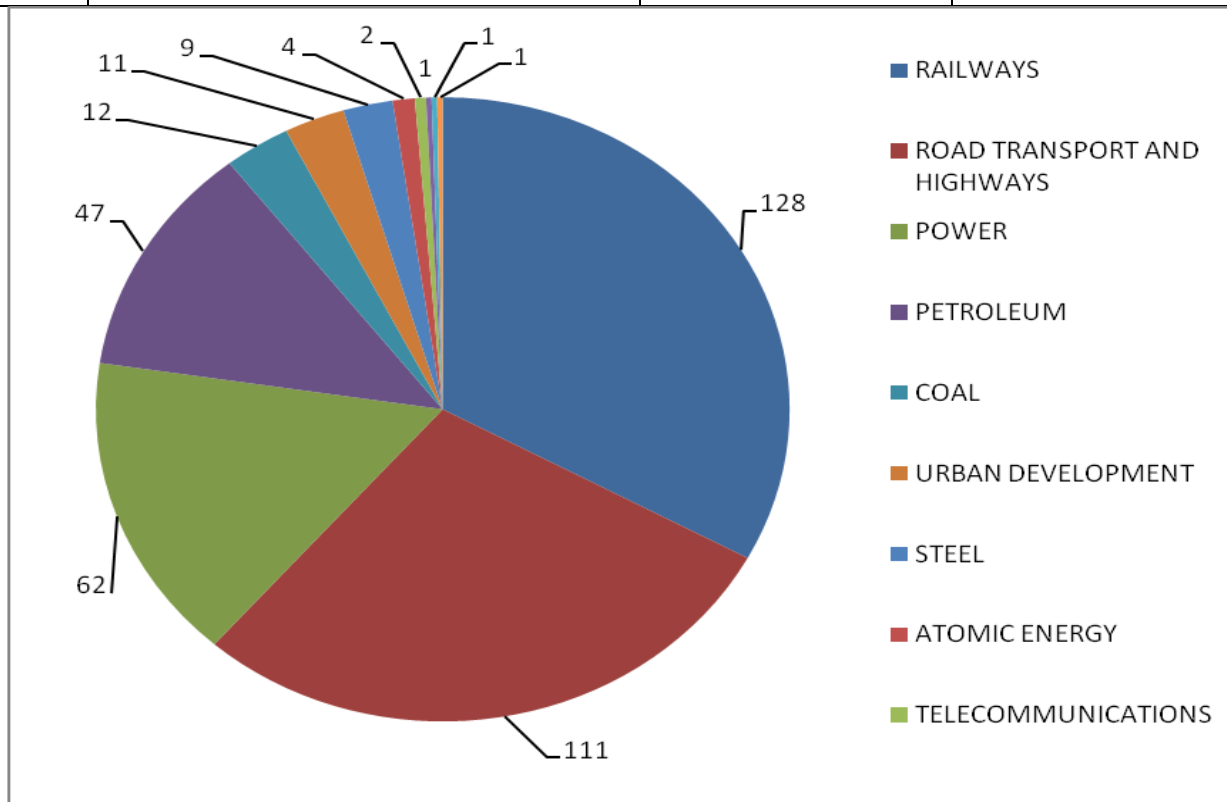


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	388
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	3
No of Projects in Current Month	389

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	113 (29.05%)	5 (1.29%)	80 (20.57%)	52 (13.37%)	139 (35.73%)	389
Latest Approved (Date)	73 (18.77%)	5 (1.29%)	122 (31.36%)	49 (12.60%)	140 (35.99%)	389

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	321	10,70,360.75	12,08,716.17	4,23,638.23	35.00	1,38,355.42	12.90
Project with Revision in Cost	68	2,22,822.25	2,29,682.11	1,37,059.94	59.70	6,859.86	3.10
Total	389	12,93,183.00	14,38,398.28	5,60,698.17	38.98	1,45,215.28	11.23
Original Cost of All Projects							
Original Cost	389	12,44,372.00	14,38,398.28	5,60,698.17	38.98	1,94,026.28	15.59

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	113	5,35,508.99	6,70,557.81	3,87,582.29	57.80	1,35,048.82	25.20
Latest Approved (RCE)	73	3,00,986.42	3,89,736.16	1,97,662.58	50.70	88,749.74	29.50

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	16	80,523.05	1,00,932.70	71,233.25	70.60	20,409.65	25.30
Total	16	80,523.05	1,00,932.70	71,233.25	70.57	20,409.65	25.35

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun[^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	74.69
2	COAL	12	56,404.18	56,404.98	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,164.22	48,150.68	-0.03	1	768.88	1,113.34	44.80
5	PETROLEUM	47	1,78,185.04	1,81,452.12	1.83	10	26,384.57	32,367.27	22.68
6	POWER	62	3,07,590.01	3,73,501.06	21.43	33	1,74,297.79	2,40,208.84	37.82
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	128	2,64,554.84	3,63,562.17	37.42	90	92,346.50	2,49,238.20	169.89
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	14	16,427.80	21,649.27	31.78
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	2	15,819.21	20,650.00	30.54
Total		389	12,44,372.00	14,38,398.28	15.59	154	3,61,825.75	6,17,056.02	70.54

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun[^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	17	83,610.97	87,179.24	4.27	5	6,674.36	10,969.63	64.35
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	3	9,356.22	24,952.87	166.70
3	ASSAM	7	15,057.54	23,024.26	52.91	3	6,746.70	14,800.00	119.37
4	BIHAR	14	39,632.94	54,365.80	37.17	7	28,983.86	43,716.72	50.83
5	GUJARAT	11	27,846.79	30,914.56	11.02	3	4,165.61	7,233.38	73.65
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	2	4,966.47	12,898.75	159.72
8	JAMMU AND KASHMIR	10	25,238.37	51,229.67	102.98	2	4,288.41	30,279.71	606.08
9	KARNATAKA	18	59,444.23	68,301.46	14.90	10	21,327.46	30,943.69	45.09
10	KERALA	8	17,769.19	23,924.38	34.64	3	6,038.29	12,193.48	101.94
11	MADHYA PRADESH	16	39,844.82	46,658.20	17.10	9	27,369.66	34,183.04	24.89
12	MAHARASHTRA	45	1,46,268.44	1,57,645.05	7.78	20	36,453.02	51,807.77	42.12
13	MANIPUR	1	727.56	9,658.00	1227.45	1	727.56	9,658.00	1227.45
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	642.73
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	25	57,615.98	65,411.17	13.53	7	16,265.64	24,060.83	47.92
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	1	829.74	1,143.70	37.84
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	10	24,589.22	39,230.47	59.54
22	TRIPURA	3	2,129.35	6,386.31	199.92	3	2,129.35	6,386.31	199.92
23	UTTAR PRADESH	31	84,597.70	85,907.82	1.55	6	23,760.85	25,525.55	7.43
24	WEST BENGAL	21	39,584.38	50,926.64	28.65	8	15,572.62	27,143.31	74.30
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
26	DELHI	5	48,156.73	48,383.52	0.47	1	1,219.21	1,592.00	30.58
27	CHHATISGARH	11	72,931.21	74,996.99	2.83	3	12,976.57	15,042.35	15.92
28	JHARKHAND	11	34,343.41	37,734.40	9.87	4	21,817.59	25,208.58	15.54
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	5	12,949.36	30,054.88	132.10
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	502.99	2,170.47	331.51
31	MULTI STATE	70	2,57,222.41	2,54,414.61	-1.09	31	64,115.15	1,15,887.84	80.75
Total		389	12,44,372.00	14,38,398.28	15.59	154	3,61,825.75	6,17,056.02	70.54

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	4	67,120.00	69,728.00	36 - 93
2	COAL	12	56,404.18	56,404.98	0.00	3	8,192.43	8,192.43	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	7	42,646.34	42,288.34	4 - 63
5	PETROLEUM	47	1,78,185.04	1,81,452.12	1.83	14	47,963.68	51,060.48	5 - 74
6	POWER	62	3,07,590.01	3,73,501.06	21.43	41	2,19,616.34	2,64,779.59	3 - 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
8	RAILWAYS	128	2,64,554.84	3,63,562.17	37.42	24	37,255.36	1,07,979.60	12 - 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	14	19,309.70	21,421.44	2 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	57 - 57
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	5	80,071.14	80,443.93	5 - 29
Total		389	12,44,372.00	14,38,398.28	15.59	113	5,35,508.99	6,70,557.81	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	83,610.97	87,179.24	4.27	4	7,142.33	8,011.81	2 - 144
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	2	3,070.89	7,517.72	56 - 106
3	ASSAM	7	15,057.54	23,024.26	52.91	3	8,340.50	15,978.89	66 - 122
4	BIHAR	14	39,632.94	54,365.80	37.17	3	27,010.57	36,824.93	13 - 123
5	GUJARAT	11	27,846.79	30,914.56	11.02	1	11,459.00	11,459.00	54 - 54
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	1	3,919.59	8,398.75	135 - 135
8	JAMMU AND KASHMIR	10	25,238.37	51,229.67	102.98	4	14,387.53	40,378.83	12 - 193
9	KARNATAKA	18	59,444.23	68,301.46	14.90	5	45,051.08	47,605.80	2 - 30
10	KERALA	8	17,769.19	23,924.38	34.64	2	9,770.08	10,427.75	9 - 29
11	MADHYA PRADESH	16	39,844.82	46,658.20	17.10	3	13,338.65	14,908.82	21 - 96
12	MAHARASHTRA	45	1,46,268.44	1,57,645.05	7.78	14	50,173.15	54,199.74	3 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	25	57,615.98	65,411.17	13.53	6	22,764.71	24,991.64	10 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	2	13,149.74	13,463.70	48 - 57
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	7	55,604.64	59,383.19	9 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	31	84,597.70	85,907.82	1.55	3	20,622.72	20,622.72	4 - 26
24	WEST BENGAL	21	39,584.38	50,926.64	28.65	6	17,252.96	18,674.45	9 - 57
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
26	DELHI	5	48,156.73	48,383.52	0.47	3	41,198.73	41,571.52	5 - 25
27	CHHATISGARH	11	72,931.21	74,996.99	2.83	4	47,640.00	48,533.82	13 - 63
28	JHARKHAND	11	34,343.41	37,734.40	9.87	5	18,685.09	19,708.40	11 - 99
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	3	7,127.06	12,037.81	58 - 93
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	11,865.58	11,865.58	3 - 21
31	MULTI STATE	70	2,57,222.41	2,54,414.61	-1.09	23	74,390.59	1,11,068.94	5 - 261
Total		389	12,44,372.00	14,38,398.28	15.59	113	5,35,508.99	6,70,557.81	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	4	69,305.00	69,728.00	36 - 93
2	COAL	12	56,404.18	56,404.98	0.00	2	2,285.32	2,285.32	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,466.31	48,150.68	-0.65	6	27,121.34	26,763.34	4 - 63
5	PETROLEUM	47	1,82,442.82	1,81,452.12	-0.54	2	3,922.37	3,922.37	57 - 66
6	POWER	62	3,37,041.53	3,73,501.06	10.82	15	67,619.10	83,366.84	3 - 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
8	RAILWAYS	128	2,77,169.45	3,63,562.17	31.17	26	40,032.45	1,10,484.92	0 - 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	14	19,309.70	21,421.44	2 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	0	0.00	0.00	-
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	4	71,391.14	71,763.93	5 - 29
Total		389	12,93,183.00	14,38,398.28	11.23	73	3,00,986.42	3,89,736.16	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns[^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	7.45
2	COAL	12	56,404.18	56,404.98	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,466.31	48,150.68	-0.65	1	1,070.97	1,113.34	3.96
5	PETROLEUM	47	1,82,442.82	1,81,452.12	-0.54	3	5,055.04	6,140.19	21.47
6	POWER	62	3,37,041.53	3,73,501.06	10.82	20	1,34,963.55	1,71,423.08	27.01
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	128	2,77,169.45	3,63,562.17	31.17	76	80,122.90	2,23,399.08	178.82
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	14	16,427.80	21,649.27	31.78
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	2	15,819.21	20,650.00	30.54
Total		389	12,93,183.00	14,38,398.28	11.23	120	2,91,425.47	4,96,204.06	70.27

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns[^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	93- 93
2	COAL	12	56,404.18	56,404.98	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,466.31	48,150.68	-0.65	0	0.00	0.00	0- 0
5	PETROLEUM	47	1,82,442.82	1,81,452.12	-0.54	0	0.00	0.00	0- 0
6	POWER	62	3,37,041.53	3,73,501.06	10.82	8	35,411.46	51,159.20	12- 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
8	RAILWAYS	128	2,77,169.45	3,63,562.17	31.17	19	24,110.38	93,548.09	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	4	3,974.36	6,086.10	2- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	1	1,219.21	1,592.00	5- 5
Total		389	12,93,183.00	14,38,398.28	11.23	33	70,392.41	1,58,485.39	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	93- 93
2	COAL	12	56,404.18	56,404.98	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROLEUM	47	1,78,185.04	1,81,452.12	1.83	6	20,416.53	24,897.08	9- 66
6	POWER	62	3,07,590.01	3,73,501.06	21.43	26	1,45,520.98	1,90,684.23	10- 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
8	RAILWAYS	128	2,64,554.84	3,63,562.17	37.42	20	24,605.82	95,330.07	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	4	3,974.36	6,086.10	2- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	57- 57
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	1	1,219.21	1,592.00	5- 5
Total		389	12,44,372.00	14,38,398.28	15.59	59	2,12,562.90	3,49,353.48	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	83,610.97	87,179.24	4.27	2	1,784.62	3,012.10	2 - 144
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	2	3,070.89	7,517.72	56 - 106
3	ASSAM	7	15,057.54	23,024.26	52.91	2	5,875.35	13,600.00	81 - 122
4	BIHAR	14	39,632.94	54,365.80	37.17	3	27,010.57	36,824.93	13 - 123
5	GUJARAT	11	27,846.79	30,914.56	11.02	0	0.00	0.00	-
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	1	3,919.59	8,398.75	135 - 135
8	JAMMU AND KASHMIR	10	25,238.37	51,229.67	102.98	2	4,288.41	30,279.71	12 - 193
9	KARNATAKA	18	59,444.23	68,301.46	14.90	3	16,990.93	19,545.65	2 - 14
10	KERALA	8	17,769.19	23,924.38	34.64	1	4,588.29	5,245.96	9 - 9
11	MADHYA PRADESH	16	39,844.82	46,658.20	17.10	2	12,325.75	13,895.92	21 - 96
12	MAHARASHTRA	45	1,46,268.44	1,57,645.05	7.78	5	14,423.33	19,503.64	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	25	57,615.98	65,411.17	13.53	2	12,715.67	14,942.60	10 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	1	829.74	1,143.70	57 - 57
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	3	7,211.42	10,989.97	48 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	31	84,597.70	85,907.82	1.55	0	0.00	0.00	-
24	WEST BENGAL	21	39,584.38	50,926.64	28.65	2	7,027.98	8,449.48	9 - 57
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
26	DELHI	5	48,156.73	48,383.52	0.47	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	11	72,931.21	74,996.99	2.83	1	11,846.00	12,739.82	24 - 24
28	JHARKHAND	11	34,343.41	37,734.40	9.87	2	15,266.63	16,289.94	20 - 99
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	3	7,127.06	12,037.81	58 - 93
30	TELANGANA	6	14,904.53	16,572.01	11.19	0	0.00	0.00	-
31	MULTI STATE	70	2,57,222.41	2,54,414.61	-1.09	15	49,583.74	86,262.09	12 - 261
Total		389	12,44,372.00	14,38,398.28	15.59	59	2,12,562.90	3,49,353.48	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	NEW 250 TMTPA LPG PLANT AT PANAGARH	08/2014	190.45	09/2017	190.45	03/2018	130.15
	<u>POWER</u>						
2	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	04/2010	4,404.57	01/2015	5,135.01	03/2018	3,700.95
3	SYSTEM STRENGTHENING XII OF SR	02/2010	232.34	06/2012	340.77	03/2018	246.99
4	KISHANGANGA HEP (3X110 MW)	01/2009	3,642.04	01/2016	5,882.01	03/2018	5,301.63
5	50 MW SOLAR POWER PROJECT	06/2017	287.48	03/2018	273.68	03/2018	187.57
6	NORTH EASTERN REGION STRENGTHENING SCHEME IV	05/2016	409.19	05/2018	409.19	05/2018	212.50
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	11/2011	723.63	11/2014	882.13	03/2018	736.62
8	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM	01/2016	162.11	05/2018	162.11	03/2018	125.00

TABLE-26

List of projects added Rs. 150 Crore and above					(March 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>FERTILISERS</u>					
1	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	426.72	4/2020	426.72	4/2020
	<u>PETROLEUM</u>					
2	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	315.00	12/2021	315.00	12/2021
3	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	1,342.00	8/2020	1,342.00	8/2020
4	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	3,380.00	9/2019	3,380.00	9/2019
5	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH	12/2016	300.00	4/2021	300.00	4/2021
6	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	255.00	11/2020	255.00	11/2020
7	PUNE POL STORAGE DEPOT	8/2016	282.64	8/2020	282.64	8/2020
8	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1,112.00	6/2019	1,112.00	6/2019
	<u>POWER</u>					
9	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	198.49	9/2019	198.49	9/2019
10	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	358.83	5/2020	358.83	5/2020
11	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPPT AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	193.14	6/2019	193.14	6/2019
	<u>RAILWAYS</u>					
12	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	737.72	12/2018	737.72	12/2018
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
13	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	274.31	5/2018	274.31	5/2018
14	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM)	2/2018	391.00	10/2018	391.00	10/2018
15	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	234.27	10/2018	234.27	10/2018
16	CONSTRUCTION OF MAJOR BRIDGE OVER	3/2015	277.17	4/2017	277.17	4/2017

List of projects added Rs. 150 Crore and above					(March 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C					
17	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	403.36	6/2018	403.36	6/2018
18	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	417.24	5/2018	417.24	5/2018
19	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	409.85	12/2017	409.85	12/2017
20	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	262.97	10/2018	262.97	10/2018
	URBAN DEVELOPMENT					
21	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	422.00	/	422.00	-

TABLE-27

Milestones (Cumulative due & achieved) Rs.150 Crore and above

Total	3960
Achieved up to month	2225

TABLE-28

List of projects reporting additional delayed Rs. 150 Crore and above							(March 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 NPCIL	11,459.00	11,459.00	12/2015	11/2019	06/2020	7
	<u>COAL</u>						
2	NEYVELI SOLAR POWER PROJECT 130 MW NLC	687.28	767.00	06/2017	02/2018	04/2018	2
3	KANIHA OCP, MCL, (10.0 MTY) MCL	457.77	457.77	03/2013	11/2018	03/2019	4
4	ANANTA OC EXPANSION PH-III (15.0 MTY) MCL	207.28	207.28	03/2012	03/2019	03/2020	12
5	RAJRAPPA RCE OCP (3.0 MTY) CCL	510.85	510.85	03/2016	03/2018	03/2019	12
6	BAROUD OC EXPANSION (RCE)- 3MTY SECL	258.56	258.56	03/2016	03/2018	03/2019	12
7	RFR OF MANUGURU OC PROJECT SCCL	430.45	415.37	03/2016	03/2018	03/2019	12
8	BHUBANESWARI OCP, MCL (20.0 MTY) MCL	490.10	490.10	03/2017	05/2018	03/2020	22
	<u>STEEL</u>						
9	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	02/2018	06/2018	4
	<u>PETROLEUM</u>						
10	INTEGRATED DEVELOPMENT OF B-127 FIELDS ONGC	2,059.63	2,665.65	03/2015	03/2018	12/2019	21
	<u>POWER</u>						
11	PARE HYDRO ELECTRIC PROJECT NEEPCO	573.99	1,337.76	08/2013	03/2018	04/2018	1
12	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) PGCIL Central Sector Projects	2,525.00	2,525.00	11/2017	03/2018	04/2018	1
13	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B PGCIL Central Sector Projects	2,225.00	2,225.00	01/2018	03/2018	04/2018	1
14	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A PGCIL	1,479.30	1,479.30	04/2017	03/2018	05/2018	2
15	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) SJVN	330.00	330.00	11/2017	03/2018	05/2018	2


List of projects reporting additional delayed Rs. 150 Crore and above							(March 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION PGCIL	198.63	198.63	09/2014	03/2018	06/2018	3
17	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I PGCIL	374.63	374.63	04/2016	03/2018	06/2018	3
18	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX PGCIL	539.82	539.82	06/2016	06/2018	09/2018	3
19	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP PGCIL	268.80	340.88	03/2018	06/2018	09/2018	3
20	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO PGCIL	197.40	197.40	03/2018	03/2018	06/2018	3
21	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A PGCIL Central Sector Projects	955.00	1,364.00	12/2015	03/2018	06/2018	3
22	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) CVPPPL	8,112.12	8,112.12	04/2020	06/2023	10/2023	4
23	EASTERN REGION STRENGTHENING SCHEME -IX PGCIL	196.58	225.28	02/2016	04/2018	09/2018	5
24	EASTERN REGION STRENGTHENING SCHEME-III PGCIL	1,272.80	1,731.10	11/2012	03/2018	09/2018	6
25	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	534.02	08/2014	03/2018	09/2018	6
26	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,891.41	04/2016	06/2018	12/2018	6
27	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B PGCIL	155.57	206.42	03/2016	03/2018	09/2018	6
28	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII PGCIL	203.28	260.03	07/2017	12/2018	06/2019	6
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	6,179.96	12/2009	03/2018	10/2018	7
30	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) PGCIL	871.62	871.62	10/2017	10/2018	09/2019	11
31	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	550.18	11/2016	06/2018	06/2019	12
32	TALAIPALLI COAL MINING PROJECT NTPC	3,004.00	3,004.00	11/2019	12/2019	12/2020	12
33	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	13,762.80	08/2013	03/2018	03/2022	48

List of projects reporting additional delayed Rs. 150 Crore and above							(March 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>RAILWAYS</u>						
34	RANI-MARWAR JN. PATCH DOUBLING NWR	288.97	346.35	N.A.	10/2018	11/2018	1
35	MAHARAJGANJ-MASRAKH (NL) - NER NER	218.19	412.05	N.A.	04/2018	06/2018	2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
36	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 NHAI PPP (BOT)	1,266.60	1,266.60	09/2016	03/2018	06/2018	3
37	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) NHAI	709.00	709.00	09/2017	03/2018	09/2018	6
	<u>SHIPPING AND PORTS</u>						
38	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT KPL	600.00	257.90	12/2017	08/2019	05/2020	9
	<u>TELECOMMUNICATIONS</u>						
39	GUJARAT ACCESS (LOT 1) BSNL Central Sector Projects	171.54	171.54	05/2018	04/2018	05/2018	1
40	NETWORK FOR SPECTRUM DOT	13,334.00	24,664.00	07/2015	06/2019	04/2020	10
	<u>URBAN DEVELOPMENT</u>						
41	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD	332.72	321.00	09/2016	04/2018	05/2018	1
42	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN CPWD Central Sector Projects	350.02	479.87	03/2015	03/2018	04/2018	1
43	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN CPWD	884.30	884.30	12/2015	03/2018	05/2018	2
44	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB CPWD	388.00	388.00	05/2017	06/2018	08/2018	2


TABLE-29

Sector wise analysis of projects Rs.150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	69,728.00	28,425.34
CIVIL AVIATION	2	624.07	6,24.07	994.86	549.39
COAL	92	89,695.08	884,91.95	89,199.09	23,882.46
FERTILISERS	6	1,781.92	17,93.57	1,793.57	574.82
MINES	4	6,912.00	69,12.00	6,912.00	408.41
STEEL	30	54,971.33	553,52.30	55,185.01	40,748.78
PETROLEUM	124	2,10,560.21	2,143,23.69	2,12,573.46	64,610.38
POWER	117	3,28,395.59	3,590,20.91	3,95,733.97	2,33,023.13
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	14	3,897.21	38,97.21	3,919.69	1,507.40
RAILWAYS	334	3,41,529.69	3,572,93.76	4,62,504.09	1,30,501.41
ROAD TRANSPORT AND HIGHWAYS	530	3,51,472.35	3,521,13.14	3,57,629.96	62,776.84
SHIPPING AND PORTS	7	4,262.08	43,44.09	4,807.68	2,239.31
TELECOMMUNICATIONS	9	16,959.40	169,59.40	28,189.40	8,068.20
URBAN DEVELOPMENT	39	1,42,902.14	1,430,54.99	1,47,933.23	63,910.25
DEFENCE PRODUCTION	2	453.64	4,54.00	469.04	111.65
Grand total	1315	16,23,254.71	16,75,658.08	18,41,400.35	6,63,626.77

Graphical Presentation of All Projects w.r.t. Original Schedule

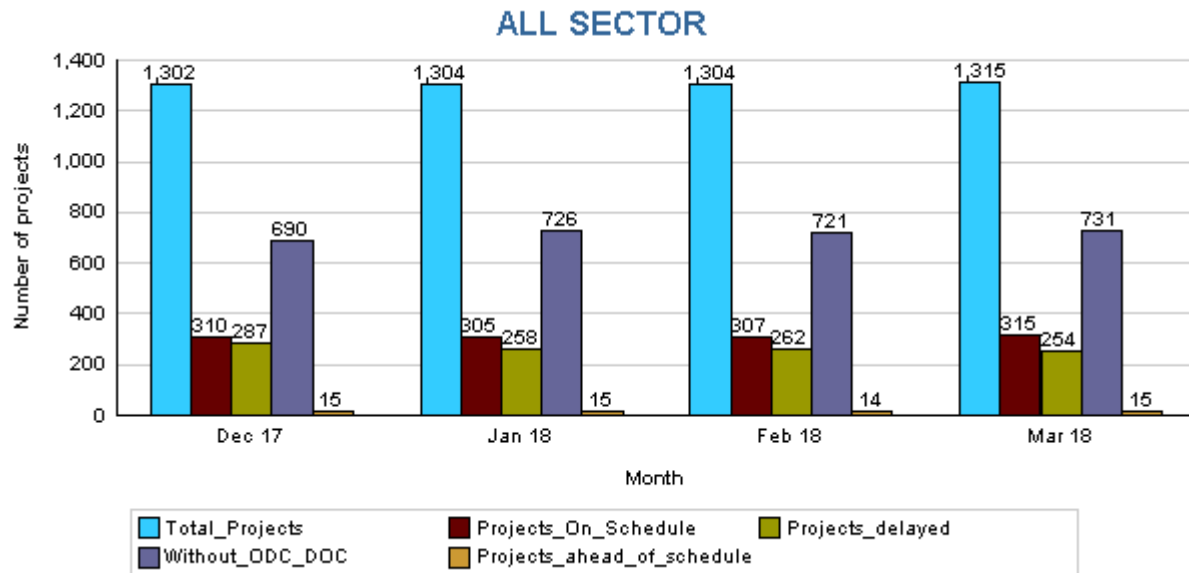


Break-up of 259 Delayed projects in March 2018

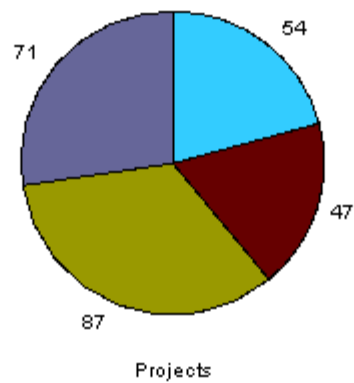


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

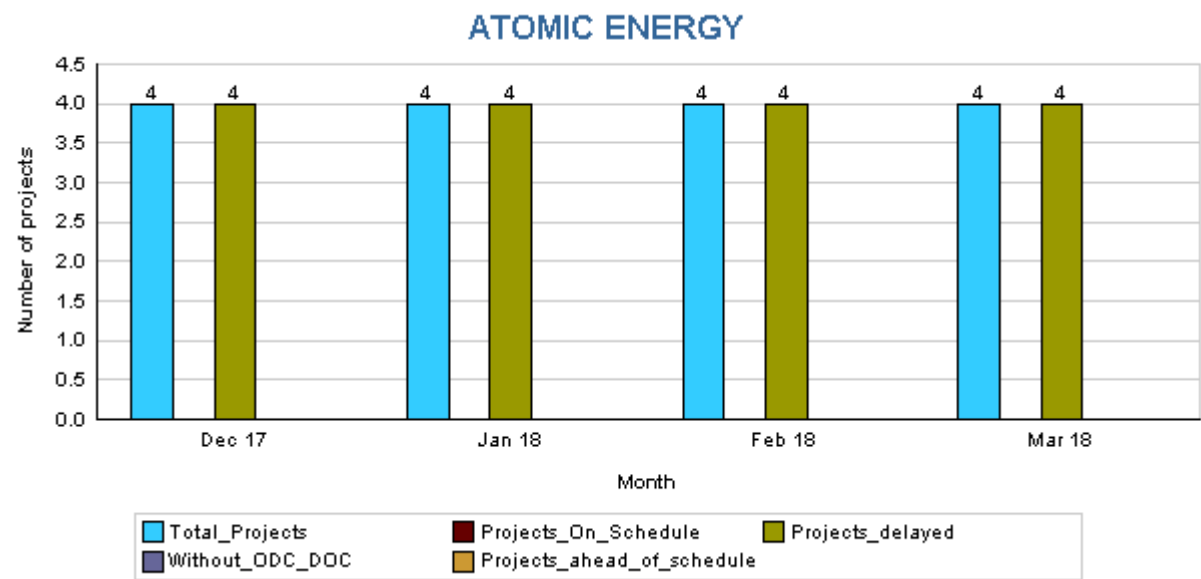


Break-up of 4 Delayed projects in March 2018

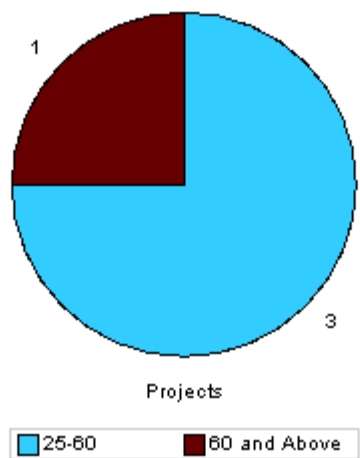


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

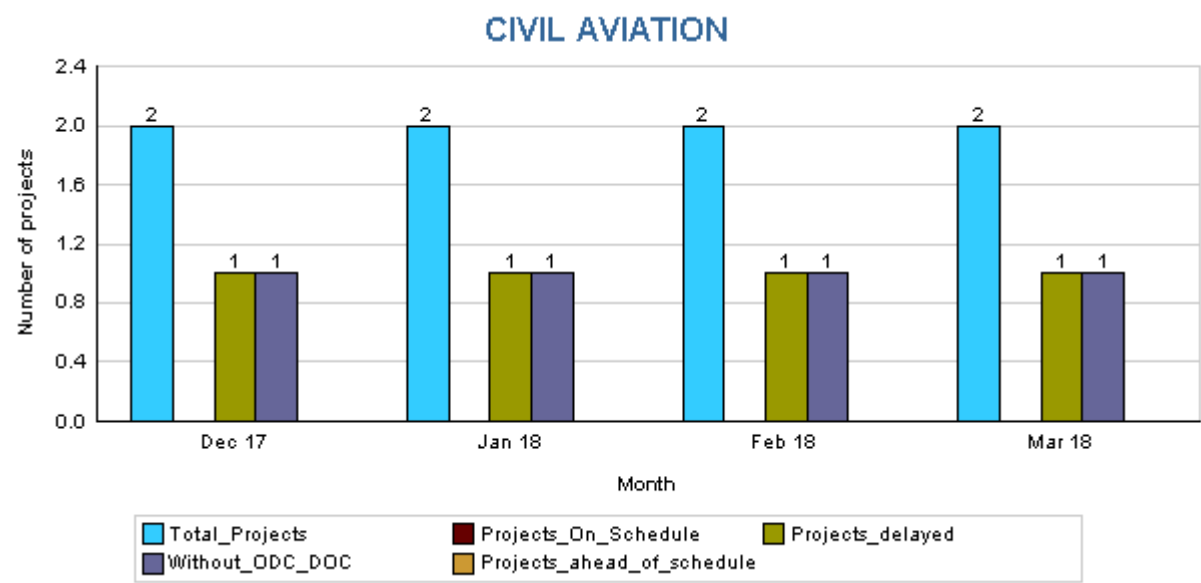


Break-up of 1 Delayed projects in March 2018




Delay in Months

13-24

Graphical Presentation of All Projects w.r.t. Original Schedule

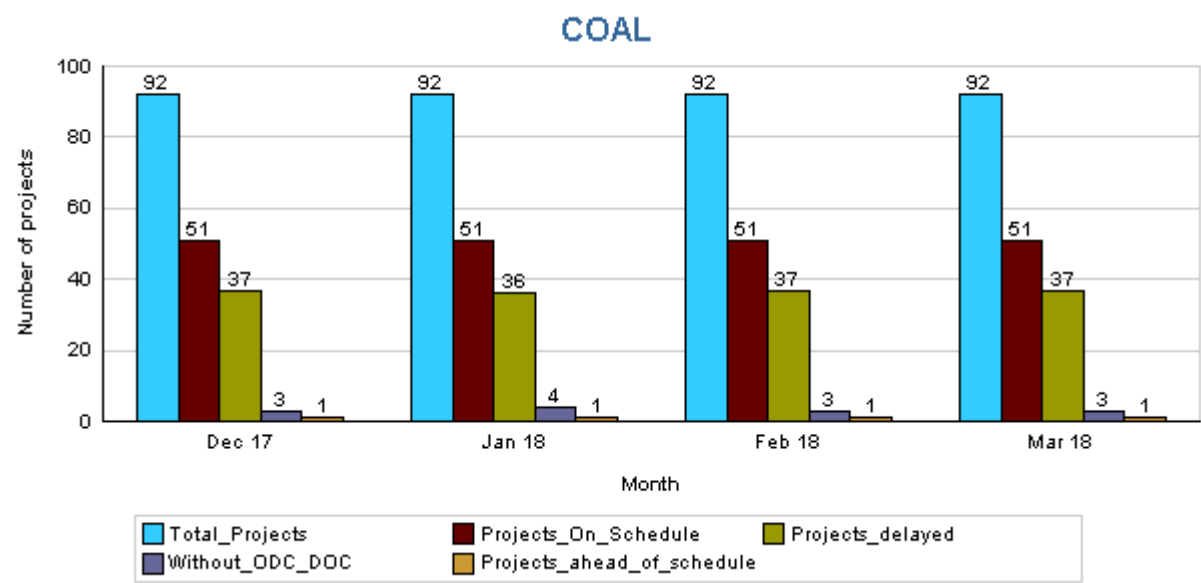

Break-up of 37 Delayed projects in March 2018

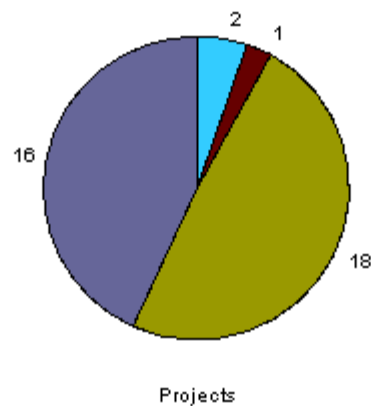

Delay in Months


1-12

13-24


25-60

60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

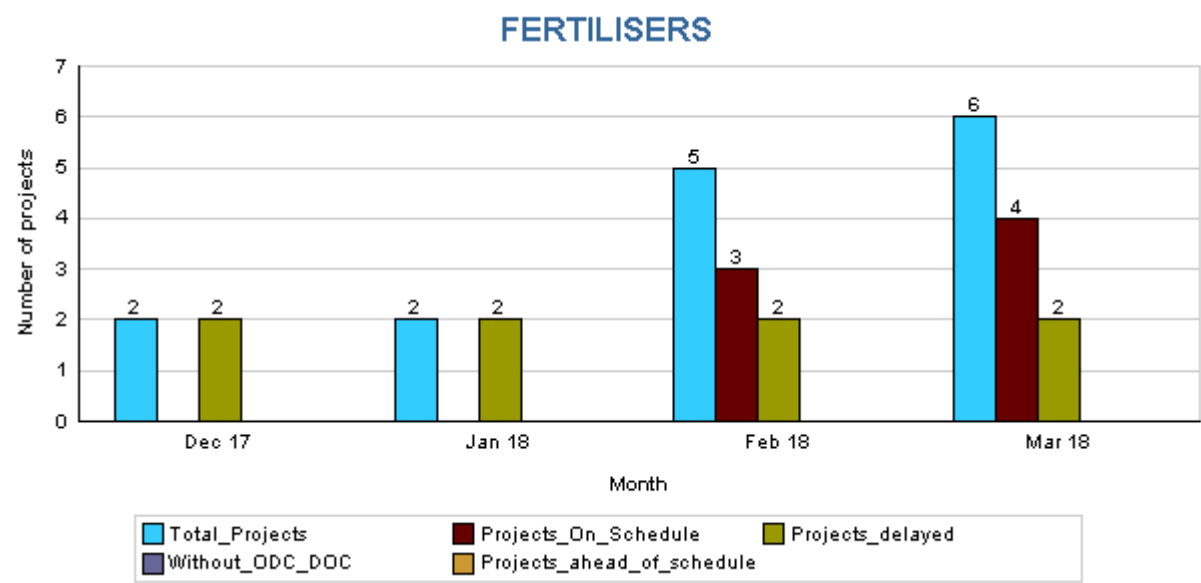


Break-up of 2 Delayed projects in March 2018

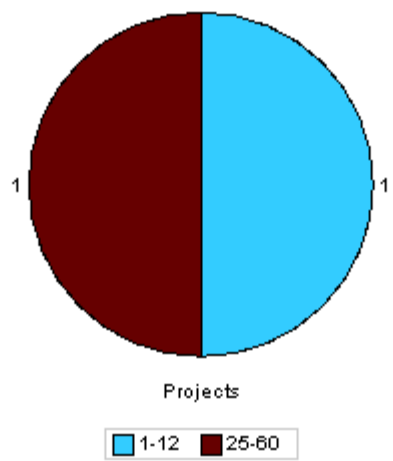


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

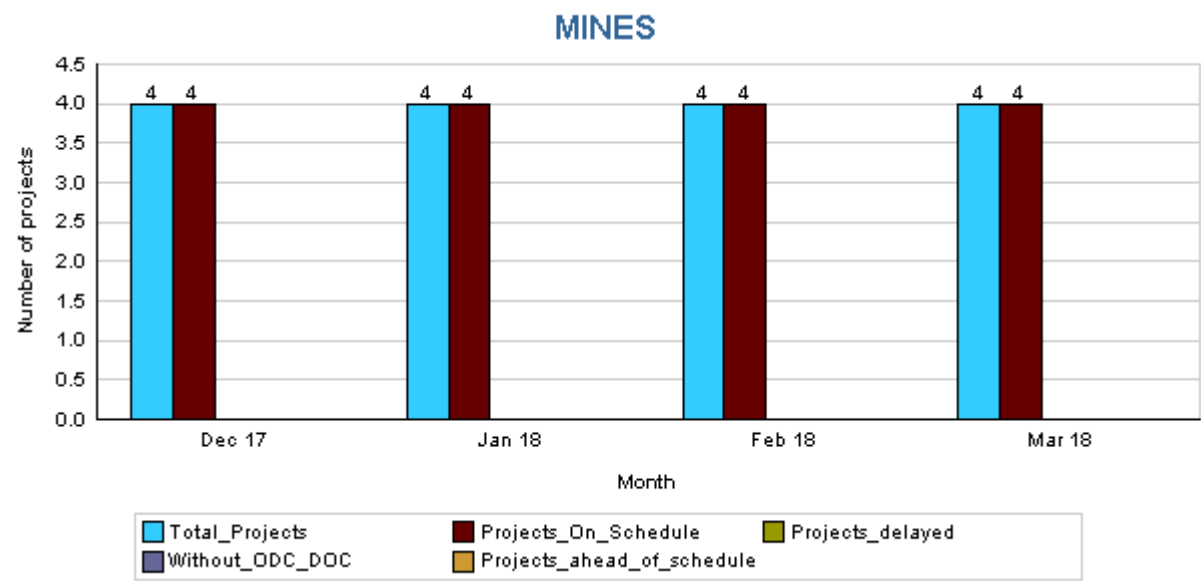


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

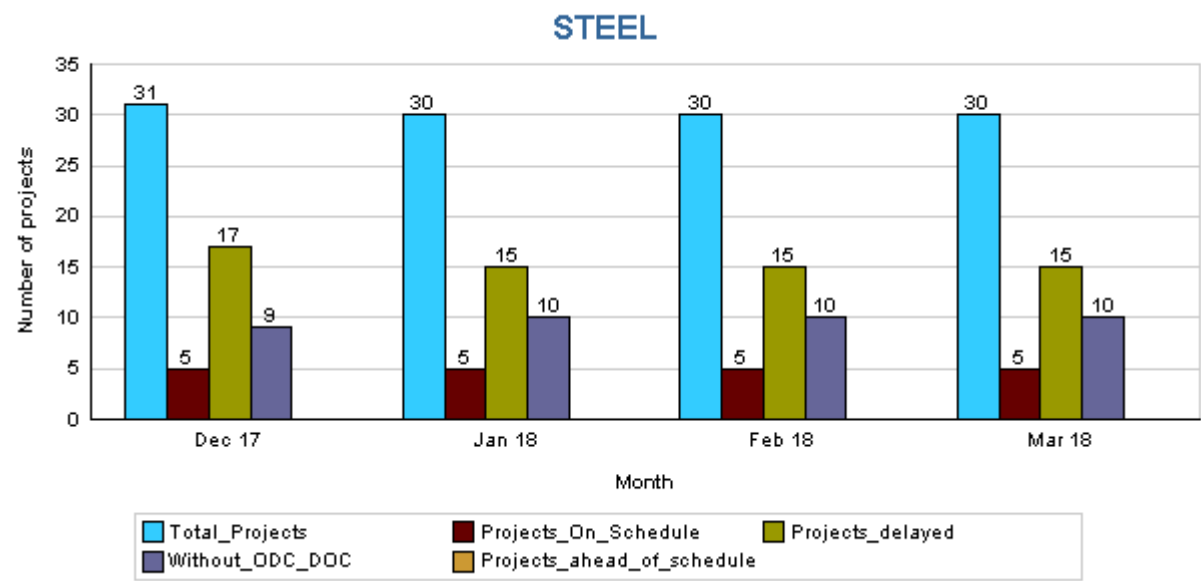

Break-up of 15 Delayed projects in March 2018

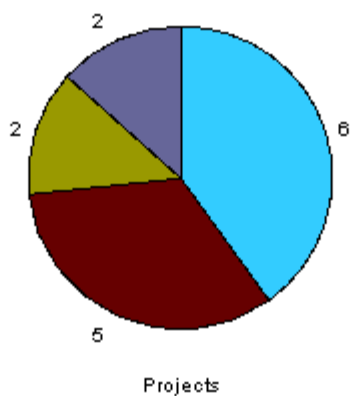

Delay in Months


1-12

13-24


25-60

60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

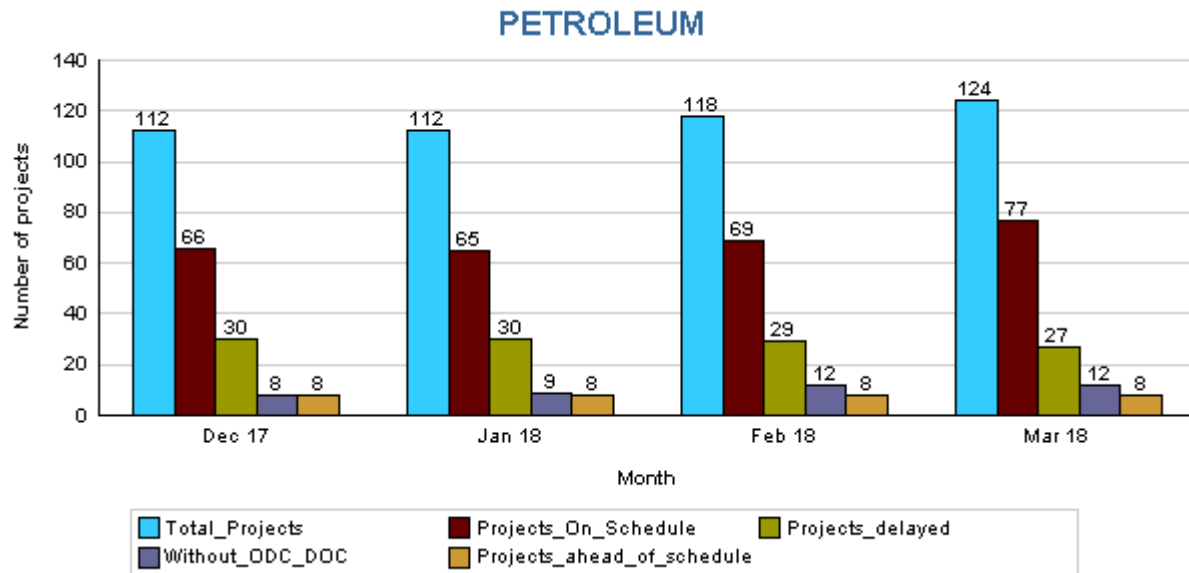


Break-up of 27 Delayed projects in March 2018

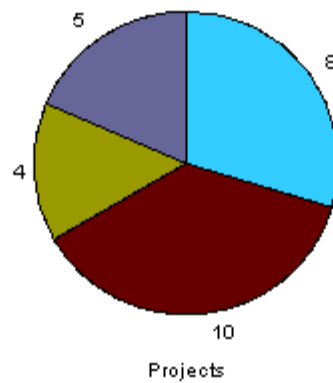


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

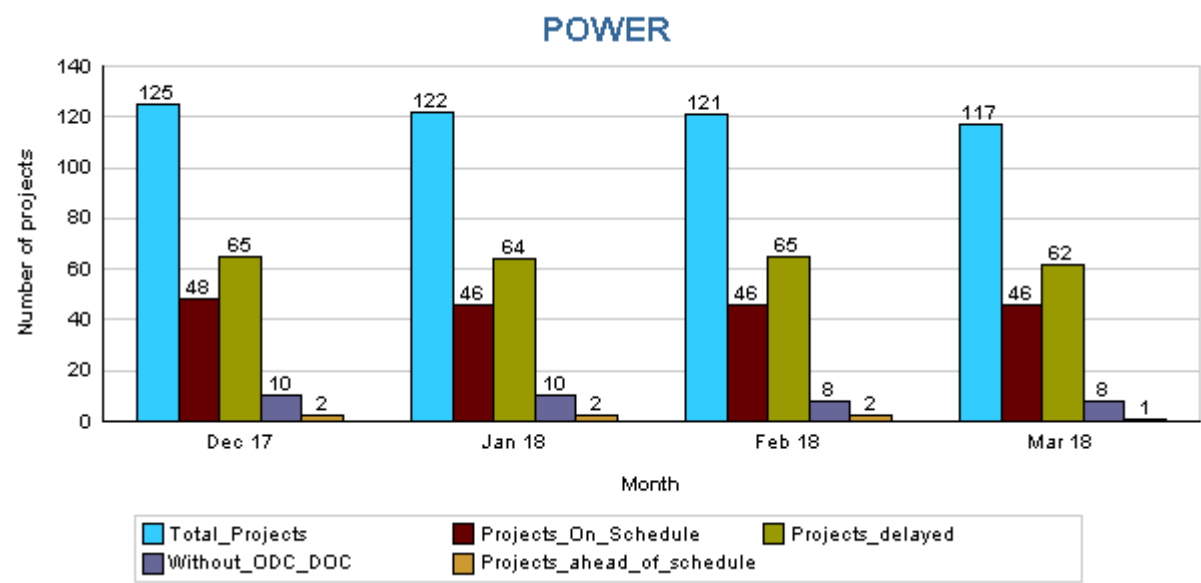


Break-up of 62 Delayed projects in March 2018

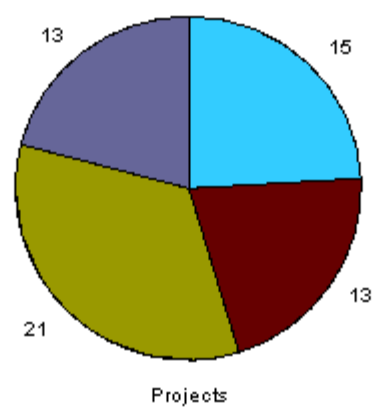

Delay in Months


Delay in Months	1-12	13-24	25-60	60 and Above
Projects	15	13	21	13

Graphical Presentation of All Projects w.r.t. Original Schedule

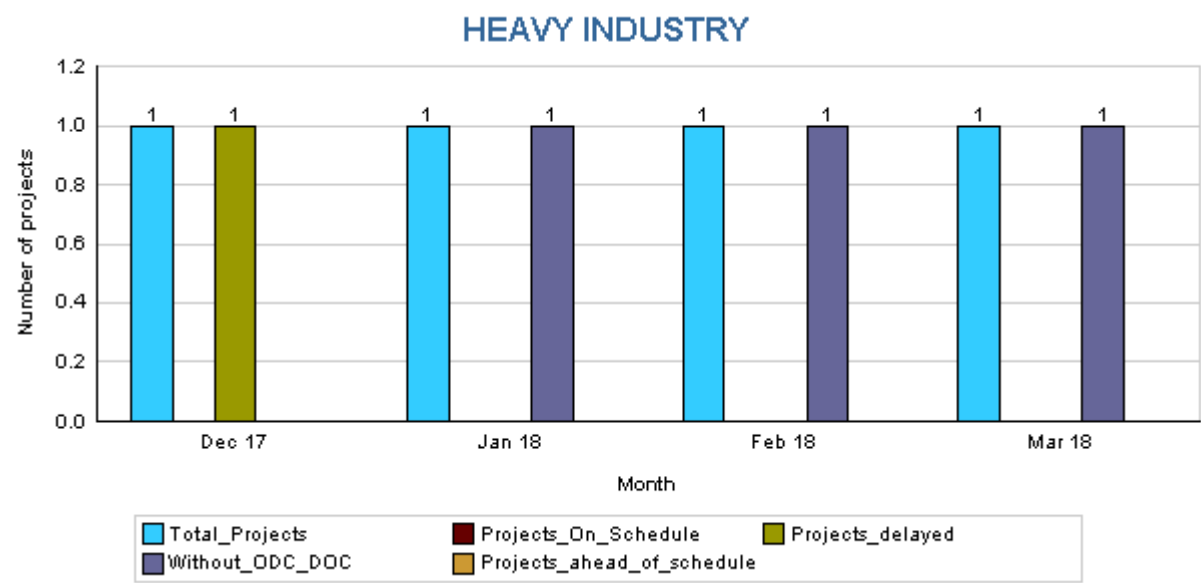


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

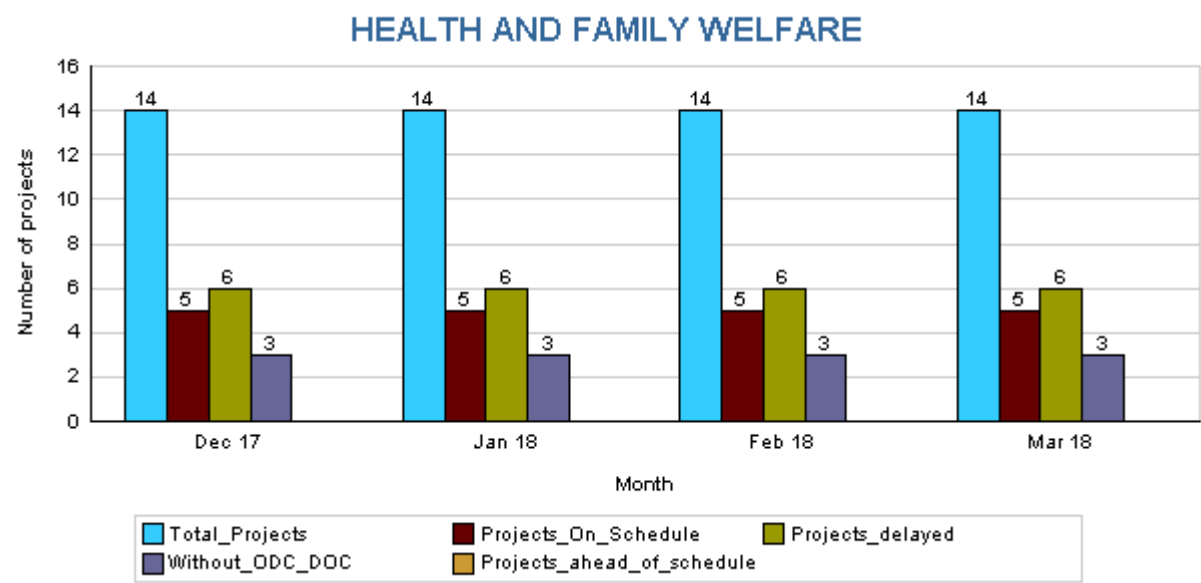


Break-up of 6 Delayed projects in March 2018

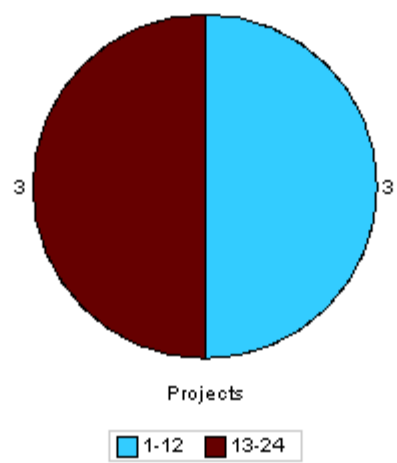


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

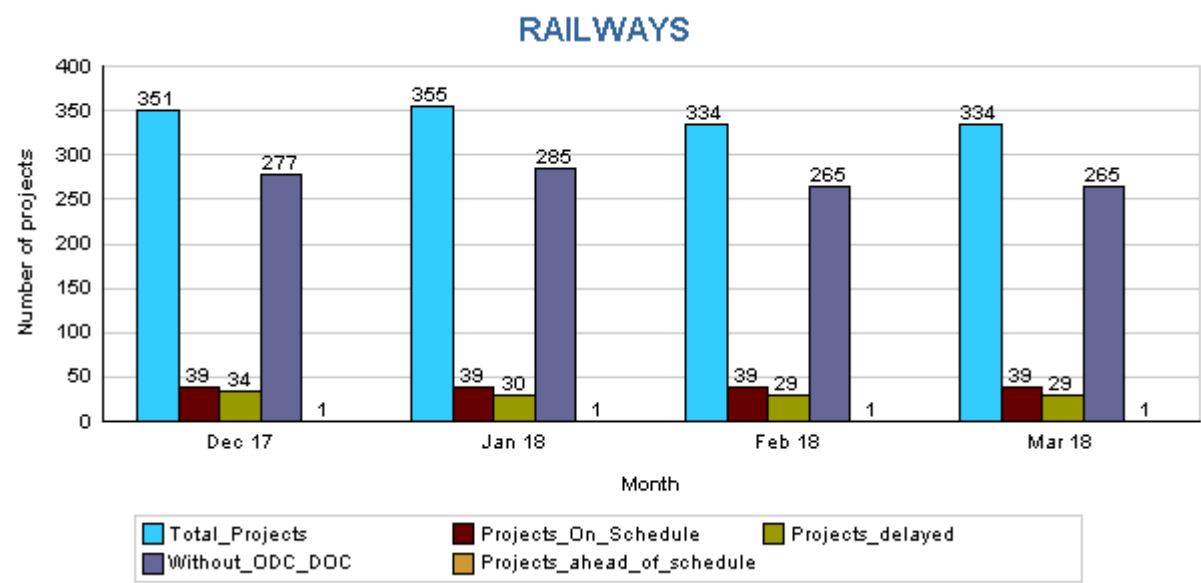


Break-up of 34 Delayed projects in March 2018

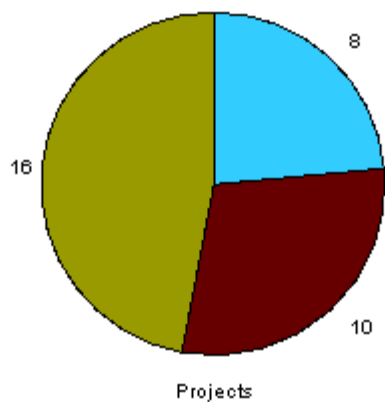


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

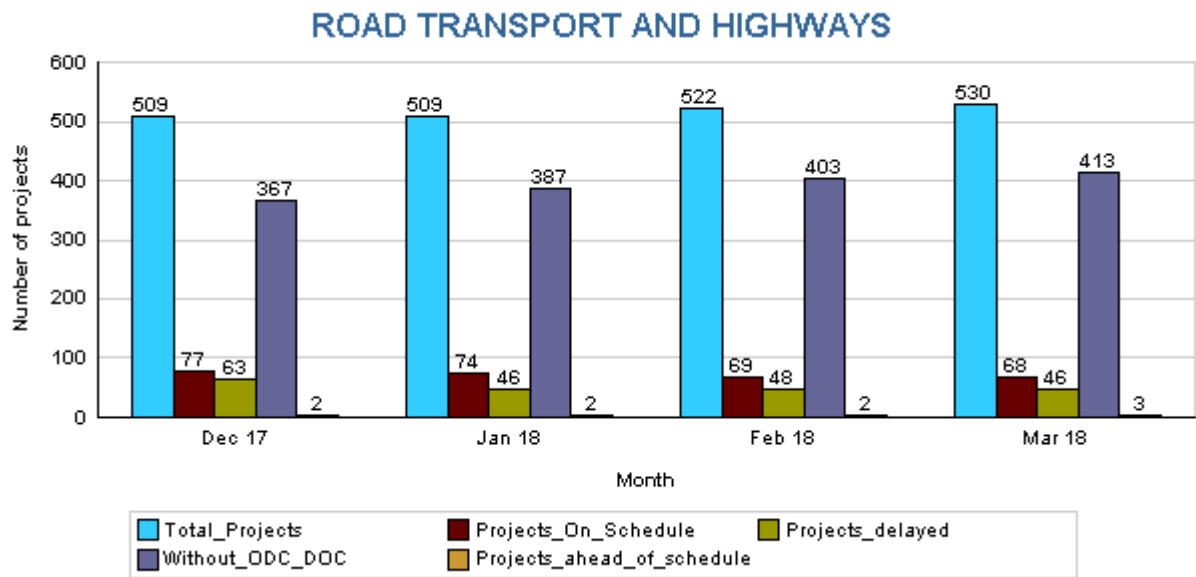


Break-up of 46 Delayed projects in March 2018

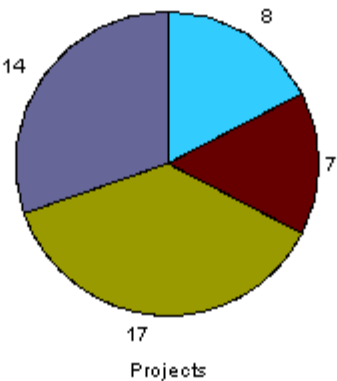


Delay in Months 1-12 13-24 25-60 60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

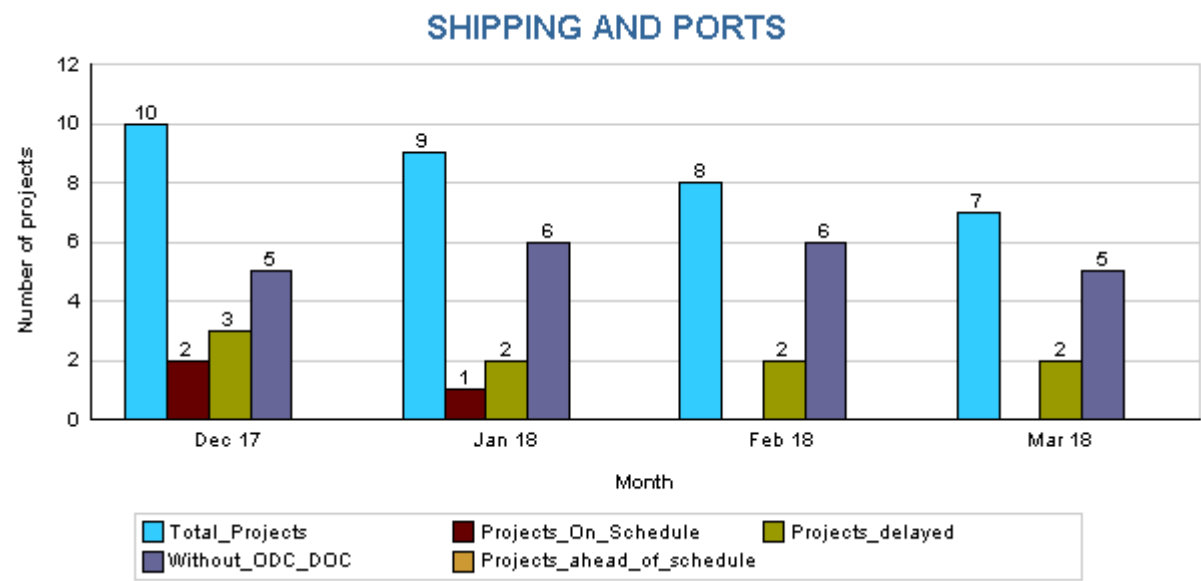


Break-up of 2 Delayed projects in March 2018

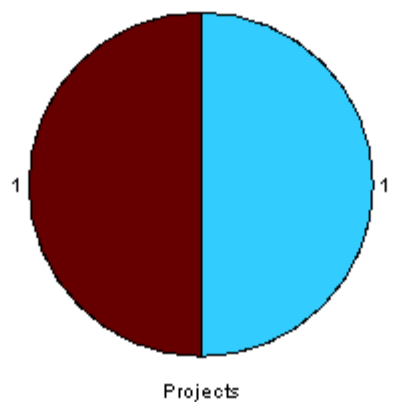


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

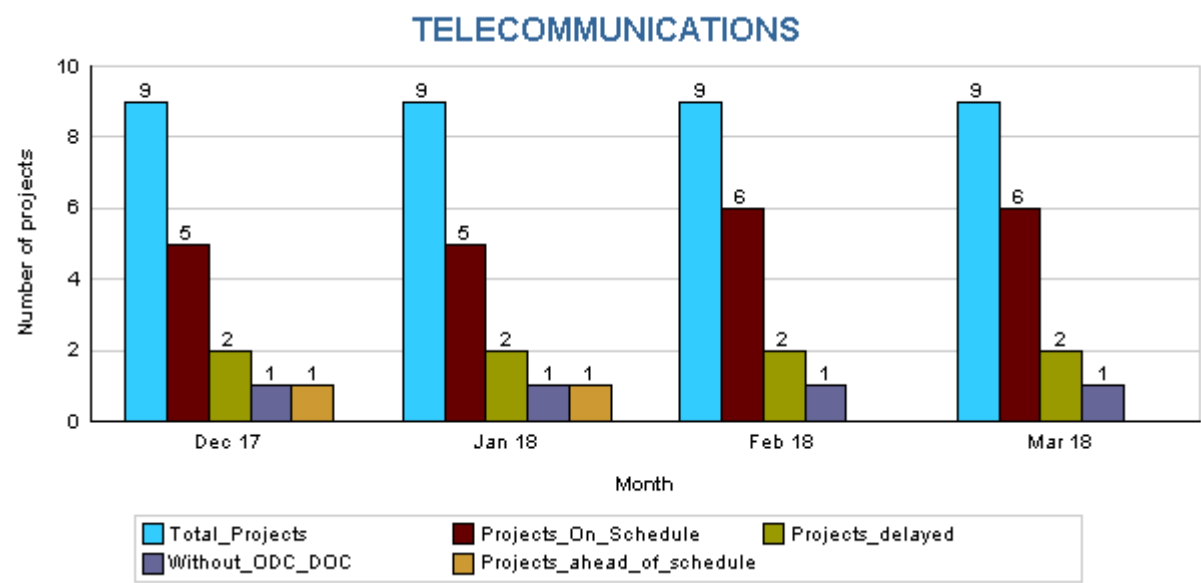


Break-up of 2 Delayed projects in March 2018

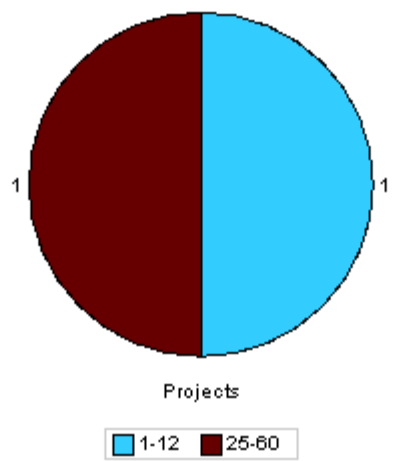


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

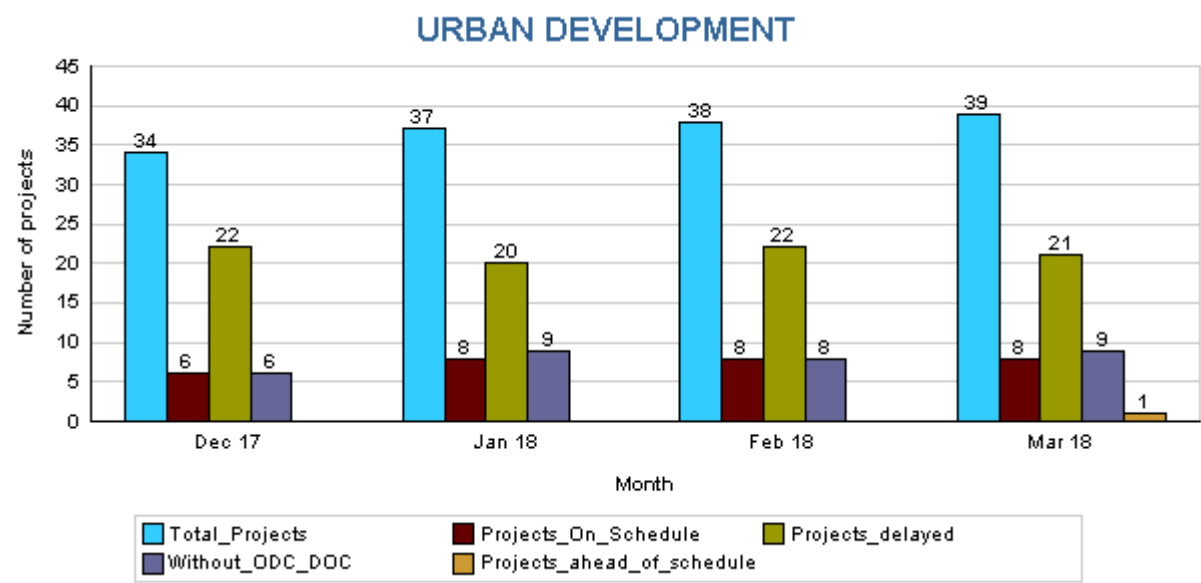


Break-up of 21 Delayed projects in March 2018

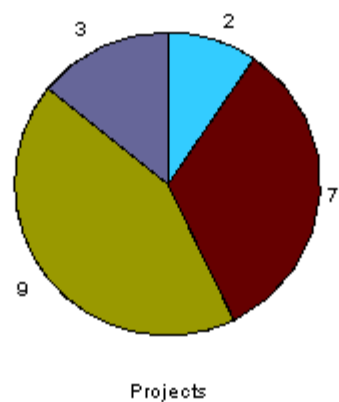

Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

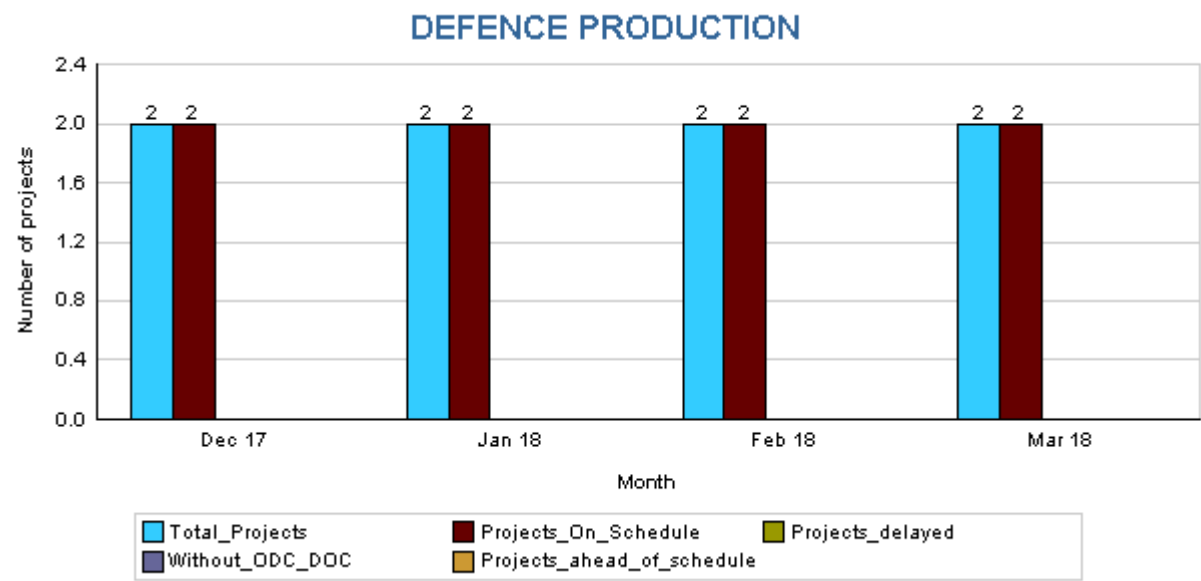

Delay in Months

TABLE-30

Detail of ongoing Projects Costing Rs. 150 Crore and above.								(All Cost/ Expenditure in Rs. Crore)	
						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	11,459.00	11,554.00	12/2015 11/2016	06/2020	54(O) 43(R)	47/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	9,147.00	12/2016 03/2017	12/2020	48(O) 45(R)	35/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,100.00	5,591.34	09/2010 09/2016	06/2018	93(O) 21(R)	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT- 3&4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36(O) -	0/0
	Total		67,120.00 -	69,728.00	28,425.34				165/225
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS ,	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	553.53	522.95	01/2011 -	-	-	0/0
	Total		624.07 -	994.86	549.39				0/0
	COAL								
7	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,668.79	03/2023 -	03/2023	0(O) -	14/17
8	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	1,698.30	03/2023 -	03/2023	0(O) -	4/19
9	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	5.79	03/2023 -	03/2023	0(O) -	1/11
10	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	137.98	03/2015 03/2020	03/2020	60(O) 0(R)	3/8
11	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	1/7
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	200.64	03/2014 -	03/2020	72(O) -	0/3
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36(O) -	7/8
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	153.81	03/2016 -	03/2019	36(O) -	4/7
15	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	31.90	03/2022 -	03/2022	0(O) -	2/8

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL, CHHATISGARH ,	05/2014	164.49 -	164.49	51.22	03/2020 -	03/2020	0(O) -	3/7
17	AMERA OC RCE - [N06000123]SECL, CHHATISGARH ,	02/2015	335.97 -	335.97	50.54	03/2018 -	03/2018	0(O) -	1/6
18	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH ,	07/2015	316.10 -	316.10	44.19	03/2020 -	03/2020	0(O) -	0/5
19	DURGAPUR OPENCAST PROJECT - [N06000136]SECL, CHHATISGARH ,	02/2015	916.24 -	916.24	.99	03/2023 -	03/2023	0(O) -	1/9
20	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL, CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/3
21	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL, CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/0
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND ,	08/2008	706.40 -	706.40	125.99	07/2012 -	03/2021	104(O) -	3/4
23	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND ,	09/2009	153.82 -	153.82	131.07	03/2014 -	-	-	6/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND ,	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108(O) -	3/4
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND ,	12/2007	179.87 -	179.87	98.15	03/2012 -	03/2019	84(O) -	3/4
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND ,	08/2008	264.68 -	264.68	154.03	03/2012 -	03/2019	84(O) -	3/4
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND ,	12/2009	510.85 -	510.85	350.19	03/2016 -	03/2019	36(O) -	3/4
28	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND ,	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	60(O) -	3/4
29	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
30	MOONDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND ,	08/2011	1,230.27 -	1,230.27	280.30	04/2015 -	04/2019	48(O) -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]CCL, JHARKHAND ,	02/2012	858.11 -	858.11	223.12	03/2020 -	03/2020	0(O) -	5/5
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL, JHARKHAND ,	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0(O) -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL, JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND ,	08/2010	289.45 -	289.45	174.74	05/2014 -	04/2018	47(O) -	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND ,	10/2012	269.82 -	269.82	169.31	04/2014 -	04/2018	48(O) -	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL, JHARKHAND ,	10/2015	359.69 -	359.69	42.26	03/2022 -	03/2022	0(O) -	1/21
37	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH ,	10/2007	259.40 -	486.57	410.19	03/2012 -	03/2018	72(O) -	1/3
38	BATURA OCP (2.0 MTY) - [N06000049]SECL, MADHYA PRADESH ,	08/2015	1,186.64 203.82	203.82	77.18	03/2023 03/2021	03/2021	-24(O) 0(R)	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL, MADHYA PRADESH ,	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	1/8
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL, MADHYA PRADESH ,	12/2014	357.80 -	357.80	114.47	03/2021 -	03/2021	0(O) -	2/8

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	35.61	03/2021 -	03/2021	0(O) -	1/7
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	1/6
43	MALACHUA OPENCASE PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	1.18	03/2023 -	03/2023	0(O) -	0/4
44	AMADAND OPENCASE EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	111.56	03/2021 -	03/2021	0(O) -	2/3
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	15.30	03/2022 -	03/2022	0(O) -	0/0
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	77.75	03/2021 -	03/2021	0(O) -	0/0
47	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	178.26	03/2020 -	03/2020	0(O) -	7/11
48	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	383.42	03/2020 -	03/2020	0(O) -	2/8
49	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	139.76	03/2021 -	03/2021	0(O) -	11/12
50	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	206.04	03/2018 -	03/2018	0(O) -	7/7
51	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	86.10	03/2023 02/2017	03/2023	0(O) 73(R)	7/11
52	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	88.13	03/2019 -	03/2019	0(O) -	10/13
53	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	96.81	03/2020 -	03/2020	0(O) -	5/10
54	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	77.21	03/2021 -	03/2021	0(O) -	2/6
55	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	232.10	03/2025 -	03/2025	0(O) -	3/13
56	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
57	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	277.65	17.31	03/2021 -	03/2021	0(O) -	3/6
58	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	51.12	03/2020 -	03/2020	0(O) -	2/6
59	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	39.89	03/2019 -	03/2019	0(O) -	2/9
60	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	126.93	03/2019 -	03/2019	0(O) -	2/8
61	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	239.83	03/2020 -	03/2020	0(O) -	0/0
62	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	.04	03/2022 -	03/2022	0(O) -	0/3
63	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	.13	03/2022 -	03/2022	0(O) -	0/12
64	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	87.11	03/2021 -	03/2021	0(O) -	1/6
65	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	334.77	03/2010 -	03/2018	96(O) -	9/10

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
66	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	313.25	03/2017 -	03/2020	36(O) -	11/12
67	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	565.86	03/2013 -	03/2019	72(O) -	8/9
68	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	260.71	03/2010 -	03/2019	108(O) -	3/4
69	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	219.29	03/2012 -	03/2020	96(O) -	4/5
70	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	242.14	03/2013 -	03/2019	72(O) -	6/8
71	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	105.89	03/2019 -	03/2019	0(O) -	2/9
72	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	682.70	03/2026 -	03/2026	0(O) -	5/15
73	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	32.84	03/2019 -	03/2019	0(O) -	3/6
74	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	3/5
75	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	374.32	03/2021 -	03/2021	0(O) -	4/9
76	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	6.22	09/2019 -	09/2019	0(O) -	0/0
77	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	168.58	12/2019 -	12/2019	0(O) -	0/0
78	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	5,229.45	12/2015 04/2018	04/2018	28(O) 0(R)	22/35
79	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	349.99	06/2015 09/2019	09/2019	51(O) 0(R)	5/7
80	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU ,	05/2016	687.28 -	767.00	756.08	06/2017 12/2017	04/2018	10(O) 4(R)	0/0
81	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	186.19	03/2012 -	03/2019	84(O) -	32/42
82	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
83	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	48.57	03/2012 -	03/2023	132(O) -	0/2
84	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	154.52	03/2015 -	03/2018	36(O) -	29/31
85	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72(O) -	5/6
86	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	.37	03/2015 -	03/2020	60(O) -	0/5
87	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60(O) -	4/29
88	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	437.51	316.06	03/2015 -	03/2021	72(O) -	5/13
89	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	125.24	06/2015 -	03/2018	33(O) -	27/36
90	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	417.33	137.69	07/2016 -	03/2020	44(O) -	19/28
91	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	154.69	03/2016 -	03/2019	36(O) -	33/39

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	78.04	03/2019 -	03/2019	0(O) -	6/18
93	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12(O) -	0/9
94	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	1/17
95	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 -	1,131.28	447.32	03/2018 -	03/2018	0(O) -	6/10
96	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	1,493.82	11/2021 -	11/2021	0(O) -	0/0
97	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL, WEST BENGAL ,	11/2015	602.86 -	602.86	293.94	03/2022 -	03/2022	0(O) -	7/12
98	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	343.50	03/2018 -	03/2020	24(O) -	10/16
	Total		89,695.08 -	89,199.09	23,882.46				435/901
	FERTILISERS								
99	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	17.26	11/2019 -	11/2019	0(O) -	0/1
100	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	106.14	11/2016 04/2019	04/2019	29(O) 0(R)	1/13
101	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 482.85	482.85	413.01	12/2017 04/2018	04/2018	4(O) 0(R)	0/1
102	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	1.32	04/2020 -	04/2020	0(O) -	0/0
103	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	17.53	11/2019 -	11/2019	0(O) -	0/2
104	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	19.56	11/2019 -	11/2019	0(O) -	0/2
	Total		1,781.92 -	1,793.57	574.82				1/19
	MINES								
105	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	89.75	04/2021 04/2021	04/2021	0(O) 0(R)	2/2
106	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	290.88	01/2020 01/2020	01/2020	0(O) 0(R)	1/2
107	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 355.00	355.00	27.78	11/2020 11/2020	11/2020	0(O) 0(R)	1/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N1000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	-	04/2021 04/2021	04/2021	0(O) 0(R)	0/0
	Total		6,912.00 -	6,912.00	408.41				4/5
	STEEL								
109	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	237.11	10/2016 -	03/2019	29(O) -	1/2
110	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
111	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	827.45	12/2017 -	10/2018	10(O) -	2/6
112	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	37.80	08/2018 -	10/2018	2(O) -	1/4
113	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	124.00	07/2018 -	09/2018	2(O) -	0/4
114	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
115	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH ,	08/2010	17,265.00 -	17,265.00	18,549.96	03/2013 -	06/2018	63(O) -	35/38
116	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	119.94	04/2015 -	-	-	4/5
117	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	13,876.24	05/2015 10/2018	10/2018	41(O) 0(R)	58/86
118	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	28.81	06/2020 -	06/2020	0(O) -	4/12
119	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
120	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND ,	03/2015	255.19 -	255.19	177.21	03/2018 -	03/2018	0(O) -	2/2
121	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	216.70	10/2017 -	12/2018	14(O) -	0/2
122	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	659.52	12/2017 -	11/2018	11(O) -	1/2
123	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	83.68	09/2017 -	-	-	0/0
124	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21(O) -	0/0
125	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
126	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
127	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
128	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	38.95	06/2019 -	06/2019	0(O) -	0/1
129	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
130	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
131	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0
132	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,089.04	04/2018 -	02/2019	10(O) -	2/3
133	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17(O) -	0/0
134	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
135	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
136	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
137	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	276.10	09/2018 -	01/2019	4(O) -	3/5
138	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
	Total		54,971.33 -	55,185.01	40,748.78				113/172
	PETROLEUM								
139	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020	0(O) -	0/1
140	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	95.26	09/2019 -	09/2019	0(O) -	19/27
141	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	262.74	06/2020 06/2020	06/2020	0(O) 0(R)	0/0
142	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	-	03/2021 -	03/2021	0(O) -	0/0
143	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	-	03/2021 -	03/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
144	FIELD DEVELOPMENT OF NBP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 207.80	207.80	-	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
145	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	14.08	04/2021 -	04/2021	0(O) -	0/0
146	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	130.07	02/2019 -	12/2018	-2(O) -	3/10
147	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.89	2,073.06	03/2013 09/2018	09/2018	66(O) 0(R)	5/15
148	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	330.35	13.34	01/2014 11/2019	11/2019	70(O) 0(R)	2/2
149	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM ,	03/2009	228.64 -	256.41	147.21	12/2016 -	05/2018	17(O) -	0/0
150	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	305.91	01/2018 -	-	-	46/61
151	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	112.81	08/2019 -	08/2019	0(O) -	2/13
152	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	480.79	11/2019 -	11/2019	0(O) -	7/17
153	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 249.85	244.70	24.69	05/2020 05/2020	05/2020	0(O) 0(R)	0/0
154	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	1.03	01/2019 -	09/2019	8(O) -	0/0
155	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	961.00	03/2015 -	11/2017	-	0/5
156	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	529.80	11/2018 -	11/2018	0(O) -	5/8
157	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	240.69	12/2020 -	02/2020	-10(O) -	2/2
158	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	55.39	06/2020 -	06/2020	0(O) -	2/2
159	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 -	300.00	-	04/2021 -	04/2021	0(O) -	0/0
160	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	2,765.06	05/2019 10/2019	10/2019	5(O) 0(R)	0/0
161	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT ,	09/2011	202.25 202.25	160.16	118.02	07/2016 06/2018	06/2018	23(O) 0(R)	6/12
162	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 567.22	567.22	414.94	11/2019 12/2018	12/2018	-11(O) 0(R)	0/0
163	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	168.01	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
164	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	154.37	03/2018 -	03/2018	0(O) -	20/22
165	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	80.23	04/2018 -	07/2018	3(O) -	17/20

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL, GUJARAT ,	02/2016	931.00 -	931.00	621.84	07/2017 -	02/2018	-	7/7
167	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC, GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	230.90	03/2026 03/2026	03/2026	0(O) 0(R)	0/0
168	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL, GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	41.89	07/2020 -	07/2020	0(O) -	0/0
169	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL, GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018	0(O) -	0/0
170	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL, GUJARAT ,	08/2017	1,342.00 -	1,342.00	-	08/2020 -	08/2020	0(O) -	0/0
171	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL, GUJARAT ,	03/2018	3,380.00 -	3,380.00	597.50	09/2019 -	09/2019	0(O) -	0/0
172	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL, HARYANA ,	11/2017	255.00 -	255.00	-	11/2020 -	11/2020	0(O) -	0/0
173	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL, HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	125.91	05/2019 -	12/2018	-5(O) -	3/13
174	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL, HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	41.00	09/2019 -	09/2019	0(O) -	2/2
175	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 -	-	-	8/12
176	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC, JHARKHAND ,	12/2015	658.62 910.23	910.23	9.35	03/2023 03/2022	03/2022	-12(O) 0(R)	0/0
177	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR, KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
178	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	606.89	02/2020 -	02/2020	0(O) -	0/0
179	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN, KARNATAKA ,	05/2015	224.00 207.00	207.25	92.97	04/2019 -	04/2019	0(O) -	5/8
180	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN, KARNATAKA ,	10/2015	135.00 170.70	170.70	104.65	03/2019 -	03/2019	0(O) -	4/11
181	BSVI UPGRADATION - [N16000257]MANGALORE REFIN, KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	108.81	12/2019 -	12/2019	0(O) -	7/9
182	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA ,	10/2015	607.06 -	714.25	325.27	10/2017 -	03/2019	17(O) -	38/52
183	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	1,290.71	08/2018 05/2019	05/2019	9(O) 0(R)	0/20
184	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA ,	02/2016	3,313.00 -	3,313.00	118.35	02/2020 -	02/2020	0(O) -	0/0
185	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL, KERALA ,	05/2015	337.06 -	337.06	93.74	08/2018 -	08/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
186	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019	0(O) -	0/0
187	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 181.02	181.02	168.93	01/2017 05/2018	05/2018	16(O) 0(R)	0/0
188	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	-	06/2020 -	06/2020	0(O) -	0/0
189	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,256.72	1,256.72	1,188.94	05/2013 03/2018	11/2018	66(O) 8(R)	1/5
190	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,729.04	03/2015 03/2018	12/2019	57(O) 21(R)	0/17
191	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA ,	03/2012	2,592.17 -	2,592.17	2,041.21	05/2014 05/2018	05/2018	48(O) 0(R)	0/21
192	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA ,	06/2014	5,706.47 5,813.25	5,813.25	5,558.19	05/2017 05/2018	05/2018	12(O) 0(R)	16/16
193	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,400.56	04/2019 03/2019	03/2019	-1(O) 0(R)	0/0
194	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA ,	02/2015	2,899.93 -	2,504.61	1,317.83	05/2017 05/2018	05/2018	12(O) 0(R)	0/0
195	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	1,027.52	03/2019 05/2020	05/2020	14(O) 0(R)	0/0
196	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 4,619.94	3,961.54	3,816.11	12/2017 03/2019	03/2019	15(O) 0(R)	0/0
197	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	1,526.01	04/2018 04/2018	04/2018	0(O) 0(R)	0/0
198	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	282.69	08/2021 -	08/2021	0(O) -	2/2
199	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	66.77	02/2020 -	02/2020	0(O) -	0/0
200	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	99.46	12/2019 -	12/2019	0(O) -	0/0
201	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA ,	05/2015	193.40 -	193.40	40.41	01/2019 -	01/2019	0(O) -	0/0
202	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	.08	01/2021 -	01/2021	0(O) -	0/0
203	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	.05	01/2021 -	01/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
204	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	.05	01/2021 -	01/2021	0(O) -	0/0
205	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	0/0
206	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	161.29	05/2019 05/2019	05/2019	0(O) 0(R)	0/0
207	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	-	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
208	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	-	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
209	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 968.61	968.61	-	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
210	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,006.83	4,006.83	184.01	05/2021 -	05/2021	0(O) -	0/0
211	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	33.23	08/2020 -	08/2020	0(O) -	0/0
212	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,561.00	3,397.00	1,961.00	12/2018 -	12/2018	0(O) -	31/39
213	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	542.96	09/2011 06/2019	06/2019	93(O) 0(R)	0/0
214	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 -	-	-	8/8
215	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	1,200.16	06/2018 -	06/2018	0(O) -	1/1
216	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	492.24	10/2014 03/2018	02/2019	52(O) 11(R)	31/40
217	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	146.36	03/2017 -	11/2018	20(O) -	0/0
218	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE ,	05/2013	4,124.35 5,725.50	5,725.50	5,130.40	04/2016 03/2018	03/2018	23(O) 0(R)	3/3
219	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	270.94	12/2020 -	12/2020	0(O) -	0/0
220	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	76.00	12/2020 -	08/2020	-4(O) -	2/2
221	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	336.86	10/2019 -	10/2019	0(O) -	3/3
222	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	135.02	07/2018 10/2020	10/2020	27(O) 0(R)	18/36
223	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	570.10	06/2020 -	06/2020	0(O) -	10/24

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
224	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	48.37	02/2019 -	02/2019	0(O) -	7/13
225	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	1.58	10/2020 -	10/2020	0(O) -	0/0
226	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	7.30	12/2019 -	12/2019	0(O) -	0/0
227	LAYING OF VIJAI PUR-AURAIYA PIPELINE SECTION OF VIJAI PUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,881.40	142.49	12/2019 12/2020	12/2019	0(O) -12(R)	14/24
228	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	40.20	12/2020 -	12/2020	0(O) -	13/24
229	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	71.07	12/2020 -	12/2020	0(O) -	13/24
230	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	2,915.00	1,645.33	12/2012 02/2019	02/2019	74(O) 0(R)	10/42
231	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	9.75	03/2021 -	03/2021	0(O) -	0/26
232	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	-	06/2017 -	-	-	0/0
233	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	1,817.34	09/2017 12/2018	12/2018	15(O) 0(R)	5/6
234	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA ,	03/2014	238.50 -	238.50	201.28	03/2017 10/2017	10/2017	-	6/6
235	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	213.63	12/2020 -	12/2020	0(O) -	14/24
236	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	133.17	01/2019 -	01/2019	0(O) -	2/6
237	LPG BP PROJECT KHANDA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	31.07	12/2019 -	12/2019	0(O) -	7/26
238	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 243.53	243.53	11.79	07/2022 -	07/2022	0(O) -	0/0
239	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	2.12	12/2021 -	12/2021	0(O) -	0/0
240	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
241	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
242	RESID UPGRADEATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.42	11/2015 -	-	-	52/52
243	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU ,	05/2015	257.87 -	257.87	202.35	11/2016 -	06/2018	19(O) -	19/22
244	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU ,	08/2014	393.00 -	393.00	281.45	04/2018 -	04/2018	0(O) -	0/10
245	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.08	02/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
246	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 390.52	390.52	95.40	03/2019 -	04/2019	1(O) -	0/0
247	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	4,497.00	93.11	12/2018 -	12/2018	0(O) -	2/2
248	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	.13	06/2020 -	06/2020	0(O) -	2/2
249	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	186.78	12/2019 -	12/2019	0(O) -	0/0
250	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	1.31	08/2020 -	08/2020	0(O) -	0/0
251	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	1.18	10/2020 -	10/2020	0(O) -	0/0
252	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA ,	05/2016	215.38 -	215.38	186.58	06/2017 -	01/2018	-	0/0
253	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	750.00	534.34	12/2018 -	12/2018	0(O) -	14/20
254	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	48.24	04/2022 -	04/2022	0(O) -	0/0
255	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	-	08/2021 -	08/2021	0(O) -	0/0
256	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	100.02	09/2019 -	09/2019	0(O) -	0/0
257	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	23.99	02/2020 -	02/2020	0(O) -	12/26
258	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL ,	03/2014	3,076.00 4,190.00	4,190.00	2,548.03	09/2017 06/2018	06/2018	9(O) 0(R)	6/7
259	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 -	694.00	315.57	10/2018 -	10/2018	0(O) -	0/0
260	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	5.73	12/2020 -	12/2020	0(O) -	0/0
261	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	9.30	12/2020 -	12/2020	0(O) -	9/24
262	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	28.93	04/2020 -	04/2020	0(O) -	0/0
	Total		2,10,560.21 -	2,12,573.46	64,610.38				543/978
	POWER								
263	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH ,	01/2016	207.88 -	207.88	111.50	07/2018 -	03/2018	-4(O) -	0/0
264	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	17,435.15	9,979.37	09/2010 -	-	-	0/0
265	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	6,424.41	12/2009 10/2018	10/2018	106(O) 0(R)	28/30

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
266	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH ,	12/2008	573.99 1,337.76	1,337.76	1,621.16	08/2013 04/2018	04/2018	56(O) 0(R)	37/38
267	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM ,	01/2008	4,375.35 8,150.00	8,150.00	7,057.00	09/2011 06/2018	06/2018	81(O) 0(R)	32/37
268	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	14,520.00	01/2011 04/2021	04/2021	123(O) 0(R)	26/47
269	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR ,	01/2007	5,353.00 -	7,998.00	6,974.42	05/2014 03/2017	02/2019	57(O) 23(R)	2/18
270	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	02/2019	13(O) -	27/31
271	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN, BIHAR ,	05/2015	436.68 -	602.44	485.63	12/2016 -	12/2018	24(O) -	10/16
272	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL, BIHAR ,	04/2016	790.13 -	790.30	368.70	06/2019 -	06/2019	0(O) -	0/0
273	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	9,555.00	06/2017 06/2019	06/2019	24(O) 0(R)	34/40
274	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,075.69	11/2019 -	12/2020	13(O) -	0/0
275	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL, DELHI ,	03/2015	1,394.52 -	1,394.52	86.60	05/2017 06/2019	06/2019	25(O) 0(R)	4/9
276	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI ,	05/2015	780.33 -	780.33	147.50	10/2018 -	10/2018	0(O) -	0/0
277	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL, GUJARAT ,	07/2016	300.94 -	300.94	112.80	12/2018 -	12/2018	0(O) -	0/0
278	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN, GUJARAT ,	11/2016	330.00 -	330.00	200.08	11/2017 -	05/2018	6(O) -	1/4
279	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	17.10	09/2018 -	09/2018	0(O) -	0/0
280	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT ,	12/2017	193.14 -	193.14	-	06/2019 -	06/2019	0(O) -	0/0
281	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75	6,684.84	09/2009 -	12/2020	135(O) -	2/3
282	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	895.22	04/2020 -	10/2023	42(O) -	0/0
283	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR ,	01/2014	1,788.41 -	2,333.71	1,223.54	09/2017 -	09/2018	12(O) -	0/0
284	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND ,	02/2014	14,366.58 -	15,164.05	6,924.00	02/2019 10/2020	10/2020	20(O) 0(R)	20/23
285	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND ,	08/2006	2,313.00 4,139.00	4,366.64	3,484.00	12/2011 -	-	-	14/14
286	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	2,657.86	10/2017 -	12/2016	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
287	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 03/2018	03/2018	14(O) 0(R)	48/48
288	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	81.90	02/2019 -	02/2019	0(O) -	0/0
289	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	8,980.00	09/2017 06/2019	06/2019	21(O) 0(R)	32/41
290	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	5,115.00	09/2019 -	09/2019	0(O) -	25/25
291	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	171.50	03/2017 09/2018	09/2018	18(O) 0(R)	0/0
292	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	99.50	06/2018 -	06/2018	0(O) -	0/0
293	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	40.16	09/2020 -	09/2020	0(O) -	9/16
294	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects	02/2015	1,750.00 -	1,750.00	867.00	06/2018 -	06/2018	0(O) -	0/0
295	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	660.59	09/2010 12/2018	12/2018	99(O) 0(R)	5/8
296	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
297	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	8,488.00	11/2016 03/2019	03/2019	28(O) 0(R)	34/38
298	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA , Central Sector Projects	04/2015	2,225.00 2,225.00	2,225.00	1,346.00	01/2018 -	04/2018	3(O) -	0/0
299	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,514.68	10/2012 12/2018	12/2018	74(O) 0(R)	8/11
300	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,639.60	08/2013 03/2022	03/2022	103(O) 0(R)	23/26
301	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,617.80	12/2012 06/2018	06/2018	66(O) 0(R)	16/23
302	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,440.03	11/2012 09/2018	09/2018	70(O) 0(R)	12/13
303	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	487.82	06/2014 12/2018	12/2018	54(O) 0(R)	10/12
304	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 534.02	534.02	386.87	08/2014 09/2018	09/2018	49(O) 0(R)	8/10
305	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE ,	03/2012	198.63 -	198.63	137.93	09/2014 09/2017	06/2018	45(O) 9(R)	0/0
306	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE ,	03/2013	514.20 703.10	703.10	598.00	06/2015 05/2018	05/2018	35(O) 0(R)	7/10

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
307	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 3,190.27	3,190.27	2,178.75	12/2015 06/2018	06/2018	30(O) 0(R)	15/18
308	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,184.14	04/2016 12/2018	12/2018	32(O) 0(R)	8/12
309	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	156.50	04/2016 12/2017	06/2018	26(O) 6(R)	0/0
310	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	400.50	06/2016 09/2018	09/2018	27(O) 0(R)	9/11
311	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 550.18	550.18	394.40	11/2016 06/2019	06/2019	31(O) 0(R)	8/12
312	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 206.42	206.42	143.20	03/2016 09/2018	09/2018	30(O) 0(R)	4/6
313	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	1,979.40	03/2018 03/2019	03/2019	12(O) 0(R)	9/12
314	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE ,	08/2014	288.49 -	376.09	234.30	02/2017 06/2018	06/2018	16(O) 0(R)	7/12
315	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 225.28	225.28	143.00	02/2016 09/2018	09/2018	31(O) 0(R)	16/17
316	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE ,	12/2014	6,517.36 -	6,517.36	3,772.80	04/2018 -	04/2018	0(O) -	12/12
317	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	190.10	03/2018 09/2018	09/2018	6(O) 0(R)	1/3
318	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	160.59	10/2017 09/2019	09/2019	23(O) 0(R)	0/5
319	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	178.70	07/2017 06/2019	06/2019	23(O) 0(R)	3/5
320	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	64.90	03/2018 -	06/2018	3(O) -	0/0
321	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	547.00	09/2017 09/2018	09/2018	12(O) 0(R)	0/0
322	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	2,392.90	04/2018 09/2018	09/2018	5(O) 0(R)	5/9
323	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE ,	04/2015	1,479.30 -	1,479.30	848.40	04/2017 03/2018	05/2018	13(O) 2(R)	8/8
324	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	1,149.70	07/2018 -	07/2018	0(O) -	0/0
325	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	907.80	07/2018 -	07/2018	0(O) -	0/0
326	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	272.70	01/2018 03/2019	03/2019	14(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
327	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	193.60	11/2018 -	11/2018	0(0) -	0/0
328	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	1,113.30	05/2019 -	05/2019	0(0) -	0/0
329	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	1,313.70	11/2019 -	11/2019	0(0) -	0/0
330	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE ,	04/2016	810.48 -	810.48	470.10	12/2018 -	12/2018	0(0) -	0/0
331	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	63.90	11/2018 -	11/2018	0(0) -	0/0
332	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	74.10	07/2018 -	07/2018	0(0) -	0/0
333	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	220.50	03/2019 -	03/2019	0(0) -	0/0
334	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	81.90	02/2019 -	02/2019	0(0) -	0/0
335	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	45.50	02/2019 -	02/2019	0(0) -	0/0
336	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	18.60	03/2019 -	03/2019	0(0) -	0/0
337	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	12.00	06/2019 -	06/2019	0(0) -	0/0
338	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE ,	10/2016	167.75 -	167.75	62.40	04/2019 -	04/2019	0(0) -	0/0
339	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	7.71	11/2019 -	11/2019	0(0) -	0/0
340	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	70.81	01/2019 -	01/2019	0(0) -	0/0
341	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	132.80	04/2019 -	04/2019	0(0) -	0/0
342	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	-	02/2020 -	02/2020	0(0) -	0/0
343	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	21.70	02/2019 -	02/2019	0(0) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
344	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 -	162.31	11.90	03/2019 -	03/2019	0(O) -	0/0
345	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	8.00	06/2019 -	06/2019	0(O) -	0/0
346	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	19.70	12/2019 -	12/2019	0(O) -	0/0
347	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 -	204.12	10.30	09/2019 -	09/2019	0(O) -	0/0
348	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	323.07	04/2020 -	04/2020	0(O) -	0/0
349	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	6.00	06/2019 -	06/2019	0(O) -	0/0
350	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,141.97	668.80	12/2018 -	12/2019	12(O) -	0/0
351	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	5,111.33	474.57	12/2018 -	12/2019	12(O) -	0/0
352	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 1,161.00	1,364.00	1,125.00	12/2015 -	06/2018	30(O) -	0/0
353	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE , Central Sector Projects	04/2015	2,525.00 -	2,525.00	1,783.00	11/2017 -	04/2018	5(O) -	0/0
354	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	1,532.00	04/2019 -	04/2019	0(O) -	0/0
355	EASTERN REGION STRENGTHENING SCHEME-XXVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	151.00	07/2020 -	07/2020	0(O) -	0/0
356	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	29.20	02/2020 -	02/2020	0(O) -	0/0
357	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	-	09/2019 -	09/2019	0(O) -	0/0
358	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	-	05/2020 -	05/2020	0(O) -	0/0
359	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	7,588.00	08/2018 06/2019	06/2019	10(O) 0(R)	27/37
360	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	207.90	04/2019 -	04/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
361	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN ,	07/2015	307.18 -	307.18	179.10	11/2017 10/2018	10/2018	11(O) 0(R)	0/0
362	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJASTHAN - [N18000227]PGCIL, RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	353.90	01/2019 -	01/2019	0(O) -	0/0
363	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	2,000.25	11/2008 09/2018	09/2018	118(O) 0(R)	20/22
364	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU ,	09/2011	1,940.13 2,702.65	2,702.65	2,420.46	09/2014 09/2018	09/2018	48(O) 0(R)	11/13
365	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	13.60	07/2019 -	07/2019	0(O) -	0/0
366	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC, TELANGANA ,	01/2016	10,598.98 -	10,598.98	1,849.00	07/2020 10/2020	10/2020	3(O) 0(R)	16/18
367	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA ,	07/2009	421.01 -	1,078.31	963.23	07/2013 -	-	-	26/26
368	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC, UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
369	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	4,333.00	03/2019 09/2019	09/2019	6(O) 0(R)	19/30
370	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	162.82	02/2014 02/2018	03/2019	61(O) 13(R)	4/8
371	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26(O) -	30/34
372	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL, UTTARAKHAND ,	07/2006	1,657.00 2,978.86	4,401.90	2,540.27	02/2016 09/2019	12/2020	58(O) 15(R)	16/30
373	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,521.00	03/2013 12/2020	12/2020	93(O) 0(R)	3/15
374	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND ,	08/2008	2,491.58 -	3,789.61	1,393.67	06/2013 -	11/2020	89(O) -	9/13
375	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	-	08/2017 -	-	-	0/15
376	NAITWAR MORI HEP - [N18000265]SJVN, UTTARAKHAND ,	10/2017	648.33 -	648.33	100.37	12/2021 -	12/2021	0(O) -	0/0
377	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	322.00	09/2019 02/2022	02/2022	29(O) 0(R)	5/9
378	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL ,	04/2007	4,122.00 8,781.00	9,142.58	8,300.00	02/2011 -	-	-	26/26
379	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL ,	04/2016	454.11 -	454.11	198.70	04/2018 -	04/2018	0(O) -	0/0
	Total		3,28,395.59 -	3,95,733.97	2,33,023.13				860/1098
	HEAVY INDUSTRY								
380	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS, MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	-	-	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	HEALTH AND FAMILY WELFARE								
381	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	24.38	03/2019 -	03/2019	0(O) -	0/0
382	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
383	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
384	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13(O) -	0/2
385	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16(O) -	0/5
386	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6(O) -	0/2
387	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	312.99	149.00	08/2018 -	08/2018	0(O) -	0/1
388	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	29.68	03/2019 -	03/2019	0(O) -	0/0
389	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	21.00	05/2018 -	08/2019	15(O) -	0/0
390	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6(O) -	0/1
391	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH ,	10/2013	159.50 -	159.50	158.65	11/2013 -	-	-	0/8
392	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10(O) -	0/3
393	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	77.50	09/2018 -	09/2018	0(O) -	0/0
394	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	21.79	03/2019 -	03/2019	0(O) -	0/0
	Total		3,897.21 -	3,919.69	1,507.40				0/22
	RAILWAYS								
395	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	155.74 164.36	966.43	975.05	02/2009 -	-	-	0/0
396	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	330.00 -	2,120.16	249.90	- -	03/2021	- -	0/0
397	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	743.00 -	1,825.00	1,667.23	03/2008 06/2008	03/2020	144(O) 141(R)	0/0
398	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	283.54 -	761.37	.51	- -	-	-	0/0
399	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	- -	-	-	0/1
400	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	1,313.48 -	2,288.70	257.84	- -	-	-	0/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
401	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	641.47	- -	03/2020	- -	0/0
402	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.07	- -	-	-	0/0
403	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	4,000.00 -	3,631.00	51.21	- -	-	-	0/0
404	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	52.05	- -	-	-	0/0
405	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	2,499.71	82.55	03/2021 -	03/2022	12(O) -	0/0
406	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	385.63	03/2018 -	03/2018	0(O) -	0/0
407	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	234.50	.39	03/2019 -	03/2019	0(O) -	0/0
408	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM ,	09/1997	1,500.00 -	5,450.00	5,040.11	04/2008 12/2011	06/2018	122(O) 78(R)	0/0
409	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM ,	09/2006	200.00 -	780.00	466.47	- -	03/2020	- -	0/0
410	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	312.12 -	535.00	569.93	- -	03/2019	- -	0/0
411	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	172.40	- -	03/2019	- -	0/0
412	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,232.00	143.70	- -	03/2022	- -	0/0
413	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	871.00	74.06	- -	03/2021	- -	0/0
414	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR ,	04/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-	-	0/0
415	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	492.98 -	1,320.00	921.03	12/2010 -	-	-	0/0
416	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	541.00	183.72	- -	-	-	0/0
417	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	324.66	330.82	- -	-	-	0/0
418	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR ,	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
419	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
420	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	412.05	350.14	- -	06/2018	- -	0/0
421	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	332.92 283.95	477.88	495.40	03/2012 -	-	-	0/0
422	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR ,	09/2006	300.00 -	2,135.00	922.41	- -	03/2020	- -	0/0
423	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR ,	04/2008	282.92 -	360.00	3.13	- -	03/2020	- -	0/0
424	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	490.80 -	490.80	.39	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
425	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	-	- -	-	-	0/0
426	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,	04/2008	445.25 -	445.25	-	- -	-	-	0/0
427	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
428	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	175.69 -	325.00	253.10	- -	-	-	0/0
429	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	285.07 -	378.56	111.71	- -	-	-	0/0
430	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
431	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
432	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
433	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
434	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	304.41 -	304.41	.19	- -	-	-	0/0
435	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	- -	-	-	0/0
436	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	- -	-	-	0/0
437	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	355.81	283.44	- -	-	-	0/0
438	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
439	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
440	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	-	- -	-	-	0/0
441	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020	0(O) -	0/1
442	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020	0(O) -	1/1
443	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
444	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	304.00 -	1,141.70	560.21	12/2012 -	-	-	0/0
445	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	324.90 -	555.00	517.35	03/2010 -	12/2017	-	0/3
446	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	826.57 1,160.83	1,160.83	516.08	- -	03/2020	- -	0/1
447	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	758.09 -	758.09	730.03	03/2020 -	03/2020	0(O) -	0/0
448	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	152.90	03/2018 -	03/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
449	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	- -	-	-	0/0
450	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
451	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	394.14 416.86	385.60	343.13	03/2013 -	03/2020	84(O) -	0/0
452	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 2,446.85	2,446.85	2,046.34	03/2014 -	-	-	0/0
453	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	82.24	03/2012 -	03/2019	84(O) -	0/0
454	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
455	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	567.18 -	975.62	431.74	- -	03/2020	- -	0/0
456	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	376.59 -	644.38	49.88	- -	12/2020	- -	0/0
457	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	439.88 -	844.10	16.24	- -	-	-	0/0
458	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.12	858.96	548.93	- -	03/2019	- -	0/0
459	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,266.89 -	1,548.66	506.55	- -	12/2020	- -	0/0
460	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT ,	04/2010	279.40 384.32	355.00	-	- -	-	-	0/0
461	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	155.78	- -	03/2021	- -	0/0
462	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	272.61	03/2019 -	03/2019	0(O) -	0/0
463	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	-	- -	-	-	0/0
464	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	-	- -	-	-	0/0
465	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	-	- -	-	-	0/0
466	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
467	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	- -	-	-	0/0
468	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	-	- -	-	-	0/0
469	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	233.95	03/2019 -	03/2019	0(O) -	0/0
470	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	4,500.00	125.20	- -	03/2019	- -	0/0
471	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	27,946.00	16,131.46	11/2002 -	12/2018	193(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
472	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND ,	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99(O) 111(R)	0/0
473	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND ,	04/1997	194.07 583.02	583.02	568.02	06/2004 -	-	-	0/0
474	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	- -	-	-	0/0
475	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	388.00	360.26	02/2006 -	12/2019	166(O) -	0/1
476	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 -	167.73	207.11	03/2012 -	-	-	0/0
477	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	583.00	436.96	12/2015 -	-	-	0/0
478	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	143.14	- -	-	-	0/0
479	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	209.00	133.82	12/2016 -	-	-	0/0
480	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	184.26	03/2021 -	03/2021	0(O) -	0/0
481	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA ,	04/1997	227.00 -	2,135.00	133.91	- -	-	-	0/0
482	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	138.00 1,382.78	1,382.78	6.24	- -	-	-	0/0
483	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	913.00 -	1,801.01	3.59	- -	-	-	0/0
484	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 -	1,350.91	832.60	- -	-	-	0/1
485	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	377.93 986.30	986.30	279.58	- -	-	-	0/1
486	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	-	- -	-	-	0/0
487	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	562.74 -	832.47	.94	- -	-	-	0/0
488	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 -	348.85	.35	- -	-	-	0/0
489	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	955.10	- -	03/2019	- -	0/1
490	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	-	-	0/0
491	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	1,117.00 1,922.00	1,922.00	15.78	- -	-	-	0/0
492	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.34	- -	-	-	0/0
493	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	285.57 279.54	279.54	3.95	01/1999 -	-	-	0/0
494	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,900.00 1,141.00	1,141.00	546.05	- 03/2020	-	-	0/5
495	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	960.00 578.00	578.00	365.36	- 11/2015	03/2020	- 52(R)	0/2
496	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	550.00 -	2,815.62	240.68	- -	-	-	0/0
497	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	7.74	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
498	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	342.85	378.76	-	-	-	0/0
499	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.28	-	-	-	0/0
500	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	900.00 -	4,131.90	-	-	-	-	0/0
501	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,000.00	-	-	-	-	0/0
502	RAMGANJUNDI-BHOPAL (NL).WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	470.92 727.13	2,713.09	632.05	-	03/2021	-	0/0
503	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	-	-	-	0/0
504	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH ,	09/2007	687.20 -	1,030.00	1,029.45	03/2010 -	03/2018	96(O) -	0/0
505	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	603.04 2,473.40	1,030.29	937.37	03/2012 -	-	-	0/0
506	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(O) -	1/1
507	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.65 -	1,485.85	752.76	12/2020 -	12/2020	0(O) -	0/0
508	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022	0(O) -	0/1
509	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	582.13	-	03/2020 -	03/2020	0(O) -	0/1
510	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	132.66	03/2019 -	03/2019	0(O) -	0/0
511	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	737.72 -	737.72	104.10	12/2018 -	12/2018	0(O) -	0/0
512	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.97	707.51	06/1999 -	-	-	0/0
513	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	812.12	03/2004 -	03/2020	192(O) -	0/0
514	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	514.68 2,271.50	2,271.50	1,479.39	-	03/2021	-	0/0
515	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60(O) -	0/0
516	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
517	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	499.30 3,168.29	3,168.29	832.15	-	03/2023	-	0/0
518	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	277.70 792.89	792.89	230.61	-	03/2021	-	0/0
519	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	199.12	167.49	-	03/2019	-	0/0
520	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	297.85 540.02	540.02	134.52	-	03/2022	-	0/0
521	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	8,857.98	-	-	03/2024	-	0/0
522	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	-	-	03/2024	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
523	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	-	- -	03/2024	- -	0/0
524	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	630.00 1,272.19	1,272.19	67.30	- -	03/2022	- -	0/0
525	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,326.00 2,449.91	2,449.91	42.53	- -	03/2023	- -	0/0
526	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	4,670.00 3,627.47	3,627.47	32.57	- -	03/2024	- -	0/0
527	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	.13	- -	03/2023	- -	0/0
528	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	854.00 1,035.16	1,035.16	4.63	- -	03/2023	- -	0/0
529	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	912.00 637.95	637.95	8.97	- -	03/2022	- -	0/0
530	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,750.00	1,388.35	03/2020 -	03/2020	0(O) -	0/0
531	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.16	12/2025 -	12/2025	0(O) -	0/0
532	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021	0(O) -	0/0
533	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	249.12	03/2019 -	03/2019	0(O) -	0/0
534	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	-	- -	-	-	0/0
535	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	-	- -	-	-	0/0
536	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	727.56 -	9,658.00	7,387.18	03/2011 -	03/2020	108(O) -	0/0
537	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	4,083.02 -	6,000.00	257.31	- -	03/2021	-	0/0
538	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM ,	04/2008	619.34 -	4,600.00	1,951.73	04/2014 -	03/2020	71(O) -	0/0
539	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
540	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	- -	-	-	0/0
541	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE ,	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261(O) -	0/0
542	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
543	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE ,	04/1997	218.24 236.41	525.00	687.24	- -	03/2019	-	0/0
544	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
545	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 744.71	1,126.79	761.70	- -	-	-	1/1
546	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
547	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.61	- -	-	-	0/6
548	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE ,	04/2000	733.00 -	3,040.00	2,879.89	12/2008 -	03/2019	123(O) -	0/0
549	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE ,	04/1998	92.63 -	350.00	320.46	02/2011 -	-	-	0/0
550	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	973.33	613.71	12/2012 12/2012	-	-	0/0
551	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	718.54	272.98	- -	05/2019	- -	0/0
552	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	268.78	94.42	- -	08/2018	- -	0/0
553	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	149.76	- -	10/2018	- -	0/0
554	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	532.41	- -	-	-	0/0
555	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	464.09	- -	03/2022	- -	0/0
556	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,562.27	181.66	- -	-	-	0/1
557	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
558	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46(O) -	0/0
559	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	553.63 -	1,009.00	7.93	- -	-	-	0/0
560	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
561	NEW BONGAIGAON-RANGIA-KAMAGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	- -	0/0
562	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	- -	-	-	0/0
563	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE ,	04/2008	822.39 -	1,810.00	1,711.51	- -	03/2018	- -	0/1
564	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	346.15	253.87	- -	-	-	0/0
565	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	53.96	- -	03/2020	- -	0/0
566	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	148.33	- -	-	-	0/0
567	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	165.82 -	450.00	122.97	- -	03/2020	- -	0/0
568	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	523.17 -	1,871.00	1,081.98	- -	03/2018	- -	0/0
569	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	601.43 -	1,800.00	77.17	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
570	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	319.58	141.88	- -	-	-	0/0
571	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	290.85	9.31	- -	-	-	0/0
572	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.60	6.42	- -	-	-	0/0
573	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	1,130.13	.30	- -	-	-	0/0
574	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07 -	234.41	161.17	03/2015 -	-	-	0/0
575	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	51.31	- -	-	-	0/0
576	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	87.22	- -	-	-	0/0
577	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	923.52	227.50	- -	-	-	0/0
578	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.91 -	595.91	103.62	- -	-	-	0/0
579	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	160.97	56.25	- -	-	-	0/0
580	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.00	92.93	- -	-	-	0/0
581	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	296.44 -	198.88	15.83	- -	-	-	0/0
582	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	47.63	- -	11/2018	- -	0/0
583	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	251.05	15.66	- -	-	-	0/0
584	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	365.67	1.37	- -	-	-	0/0
585	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	267.09 -	350.78	98.15	- -	-	-	0/0
586	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE ,	04/2011	193.44 -	186.64	150.28	- -	-	-	0/0
587	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	173.91	18.54	- -	-	-	0/0
588	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.11	03/2017 -	-	-	0/0
589	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	369.69	31.99	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
590	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	153.02	52.01	- -	-	-	0/0
591	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	186.89	62.73	- -	-	-	0/0
592	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	493.96 -	681.68	135.79	- -	-	-	0/0
593	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE ,	04/2010	423.66 -	720.59	456.58	03/2017 -	-	-	0/0
594	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
595	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	-	-	0/0
596	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,054.35 1,693.00	2,200.00	204.51	- -	-	-	0/0
597	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	923.23	2.40	- -	-	-	0/1
598	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
599	DEOBAND (MUZAFFARNAGAR) - ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
600	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	-	- -	-	-	0/0
601	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 -	1,714.49	660.95	- -	-	-	0/2
602	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	337.49 -	704.31	69.69	- -	-	-	0/1
603	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,050.00 -	2,132.77	316.84	- -	-	-	0/1
604	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
605	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
606	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	-	- -	-	-	0/0
607	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
608	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	8.43	- -	-	-	0/0
609	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE ,	04/2007	313.24 -	607.70	568.60	01/1999 -	-	-	0/0
610	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	750.00	-	01/1999 -	-	-	0/0
611	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	3.05	- -	03/2020	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
612	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	119.50	- -	-	-	0/0
613	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	860.43	386.47	- -	03/2020	- -	0/0
614	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,618.00 1,614.59	1,614.59	555.23	- -	-	-	0/0
615	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	720.00 -	678.54	-	- -	12/2018	- -	0/38
616	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	- -	-	-	0/0
617	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	202.11	- -	03/2021	- -	0/0
618	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	-	- -	-	-	0/0
619	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	850.00 -	3,000.00	431.96	03/2015 -	03/2020	60(O) -	0/0
620	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	- -	0/0
621	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	470.21 -	3,004.90	1,004.23	- -	06/2021	- -	0/0
622	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	301.64 -	1,185.99	1,130.35	- 09/2009	03/2019	- 114(R)	0/0
623	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	183.23 -	1,202.07	523.88	02/2015 -	12/2019	58(O) -	0/0
624	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	343.00	364.71	03/2009 03/2009	12/2017	-	1/1
625	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	491.88	- -	12/2022	- -	0/0
626	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
627	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	679.27 1,111.99	1,579.27	655.18	- -	03/2021	- -	0/0
628	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	858.67 843.04	843.04	54.62	- -	03/2021	- -	0/0
629	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	162.11	- -	03/2020	- -	0/0
630	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA ,	03/2011	165.16 -	234.71	226.35	03/2015 07/2015	07/2015	-	0/0
631	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	117.43	03/2021 -	03/2021	0(O) -	0/0
632	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	43.73	03/2021 -	03/2022	12(O) -	0/0
633	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	65.98	03/2021 -	03/2021	0(O) -	0/0
634	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	148.59	03/2021 -	03/2020	-12(O) -	0/0
635	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	969.83	268.65	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
636	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	183.99	12/2021 -	12/2021	0(O) -	0/0
637	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.67	85.34	- -	12/2024	- -	0/0
638	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	960.18 -	960.18	769.00	03/2020 -	03/2020	0(O) -	0/0
639	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	850.22	03/2019 -	03/2019	0(O) -	0/0
640	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]JECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0
641	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
642	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
643	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	795.01	392.08	- 02/1997	02/2019	- 264(R)	0/0
644	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,143.70	568.36	03/2015 -	12/2019	57(O) -	0/0
645	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 -	895.00	694.56	03/2014 -	06/2019	63(O) -	0/0
646	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	69.50	- -	03/2019	- -	0/0
647	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	118.82	- -	10/2018	- -	0/0
648	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	822.00	-	- -	-	-	0/1
649	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	323.00	-	- -	-	-	0/0
650	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	456.00 295.02	420.08	38.50	- -	-	-	0/0
651	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 218.39	244.02	141.37	- -	02/2019	- -	0/0
652	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 -	346.35	228.38	- -	11/2018	- -	0/0
653	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	349.00	148.53	- -	03/2019	- -	0/0
654	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	873.71	-	- -	-	-	0/0
655	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	396.47	03/2018 -	03/2018	0(O) -	0/0
656	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0
657	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.94	- -	-	-	0/0
658	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 495.74	732.89	390.56	06/2013 -	03/2017	-	1/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
659	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	404.19 -	2,072.50	1,048.37	- -	-	-	0/0
660	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,049.68	- -	-	-	0/0
661	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	456.00 582.83	2,300.00	231.40	- 07/2008	-	-	0/0
662	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	446.87 527.37	1,105.00	3.34	- 01/2011	-	-	0/0
663	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
664	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	468.18	- -	-	-	0/0
665	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
666	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	36.26	- -	-	-	0/0
667	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU ,	04/2011	190.10 -	350.00	320.41	- -	03/2018	- -	0/0
668	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,	12/1994	124.43 -	1,010.00	1,013.26	- -	-	-	0/0
669	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	125.00 -	458.26	3.69	07/2008 -	-	-	0/0
670	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	378.56 -	1,160.47	18.25	- -	03/2022	- -	0/1
671	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	523.33	03/2016 -	12/2017	-	0/0
672	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	1,112.00	.92	- -	-	-	0/1
673	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	616.08 -	616.08	-	- -	-	-	0/1
674	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
675	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	728.10 -	728.10	120.70	12/2024 -	12/2024	0(O) -	0/0
676	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	-	03/2022 -	03/2022	0(O) -	0/0
677	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA ,	04/2008	813.34 -	3,451.00	2,589.60	03/2014 -	03/2020	72(O) -	0/0
678	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 -	1,857.00	1,529.91	03/2007 -	04/2016	-	0/0
679	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	252.00 -	580.00	-	- -	07/2019	- -	2/3
680	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
681	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
682	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	325.00 -	1,581.53	618.19	03/2010 -	-	-	0/0
683	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
684	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	308.00	-	- -	-	-	0/0
685	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	474.30	430.32	- -	03/2018	-	0/0
686	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	227.00	241.05	- -	08/2018	-	0/0
687	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	-	- -	-	-	0/0
688	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
689	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	-	- -	-	-	0/0
690	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
691	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	-	- -	-	-	0/0
692	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,750.00 -	1,295.42	52.27	03/2022 -	03/2022	0(O) -	0/0
693	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	524.00 668.00	668.00	-	03/2020 -	03/2020	0(O) -	0/6
694	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	750.55 -	750.56	45.50	12/2024 -	12/2024	0(O) -	0/0
695	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	977.00	863.23	03/2019 -	03/2019	0(O) -	0/0
696	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.90 -	1,765.92	95.72	12/2025 -	12/2025	0(O) -	0/0
697	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.30	797.44	12/2020 -	12/2020	0(O) -	0/0
698	RAMNA - SINGRAULI DOUBLING - [N22000417]JECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	166.13	03/2020 -	03/2020	0(O) -	0/0
699	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12(O) -	0/0
700	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
701	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0
702	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	4,295.30 -	16,216.00	761.30	12/2026 -	12/2026	0(O) -	0/0
703	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL ,	04/1983	36.80 274.41	614.00	262.63	- -	03/2020	-	0/0
704	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.48	03/2007 03/2007	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
705	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
706	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL ,	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	- 111(R)	0/0
707	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	1,106.62 -	1,106.62	355.85	12/2010 -	-	-	3/7
708	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL ,	03/1984	293.97 -	749.69	-	06/2005 -	-	-	0/0
709	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
710	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,070.00	40.16	03/2014 -	-	-	0/0
711	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	1,635.74	03/2016 -	12/2020	57(O) -	0/0
712	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINAY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	2,913.50	750.71	03/2016 -	12/2018	33(O) -	0/0
713	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL ,	04/2009	533.38 -	533.38	127.10	12/2011 -	-	-	0/0
714	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL ,	04/2009	611.03 -	611.03	146.31	12/2011 -	-	-	0/0
715	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL ,	04/2004	293.74 -	229.33	140.60	12/2010 -	-	-	0/0
716	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL ,	04/1999	207.52 -	334.87	293.47	12/2012 -	-	-	0/0
717	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
718	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	434.00	40.77	- -	-	-	0/0
719	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL ,	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
720	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	97.41	- -	03/2020	- -	0/0
721	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL ,	04/2011	209.77 -	630.00	620.04	- -	03/2018	- -	0/0
722	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL ,	04/2012	283.55 -	450.00	361.54	- -	03/2019	- -	0/0
723	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
724	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	.64	- -	-	-	0/0
725	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL ,	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
726	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	556.31 -	612.00	-	- -	03/2020	- -	0/0
727	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL ,	01/1991	763.18 -	1,428.00	484.47	12/2021 -	12/2021	0(O) -	0/0
728	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	484.33	03/2003 -	-	-	0/0
	Total		3,41,529.69 -	4,62,504.09	1,30,501.41				13/106
	ROAD TRANSPORT AND HIGHWAYS								
729	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL, A & N ISLANDS ,	03/2015	262.97 -	262.97	-	10/2018 -	10/2018	0(O) -	0/0
730	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS ,	03/2017	409.85 -	409.85	-	12/2017 -	12/2017	-	0/0
731	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL, A & N ISLANDS ,	03/2015	277.17 -	277.17	-	04/2017 -	04/2017	-	0/0
732	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS ,	02/2018	391.00 -	391.00	-	10/2018 -	10/2018	0(O) -	0/0
733	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL, A & N ISLANDS ,	03/2018	234.27 -	234.27	-	10/2018 -	10/2018	0(O) -	0/0
734	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	-	05/2013 -	12/2017	-	0/0
735	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62(O) -	0/0
736	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	-	05/2014 -	06/2017	-	0/0
737	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH, ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
738	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD, ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	02/2017	-	0/1
739	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
740	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 -	207.40	44.08	07/2014 -	-	-	0/1
741	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	-	0/1
742	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/1
743	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	- -	-	-	0/1
744	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	- -	-	-	0/4
745	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(BRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	- -	-	-	0/0
746	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	-	0/2
747	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	-	0/4
748	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	-	0/4
749	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
750	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	-	2/4
751	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	-	0/4
752	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	-	0/0
753	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
754	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	-	0/2
755	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
756	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0
757	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	-	- -	11/2018	- -	0/0
758	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	02/2017	-	0/0
759	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	15.10	03/2020 -	03/2020	0(0) -	0/0
760	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	-	03/2020 -	05/2020	2(0) -	0/0
761	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	-	06/2017 -	-	-	0/0
762	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	-	- -	-	-	0/0
763	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	-	- -	-	-	0/0
764	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	-	- -	-	-	0/0
765	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
766	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0
767	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
768	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	05/2018	0(0) -	1/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
769	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
770	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0(O) -	1/4
771	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/3
772	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
773	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	09/2010	-	0/0
774	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	09/2010	-	0/0
775	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	05/2018	0(O) -	1/4
776	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	-	11/2016 -	11/2016	-	0/0
777	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	-	06/2016 -	06/2016	-	0/4
778	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	-	- -	-	-	0/0
779	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	-	10/2016 -	10/2016	-	0/4
780	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	-	- -	-	-	0/0
781	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36(O) -	0/0
782	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	-	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
783	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	-	04/2017 -	-	-	0/0
784	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	-	04/2017 -	-	-	0/0
785	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	-	04/2017 -	-	-	0/0
786	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	-	04/2017 -	-	-	0/0
787	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	-	04/2017 -	-	-	0/0
788	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	-	04/2017 -	-	-	0/0
789	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	-	04/2017 -	-	-	0/0
790	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	-	04/2017 -	-	-	0/0
791	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	-	04/2017 -	-	-	0/0
792	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	-	02/2009 -	05/2018	111(O) -	0/0
793	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	-	04/2009 -	12/2017	-	0/0
794	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	-	11/2008 -	09/2018	118(O) -	0/0
795	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112(O) -	0/0
796	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	-	04/2009 -	10/2018	114(O) -	0/0
797	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	-	03/2008 -	11/2017	-	0/0
798	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	-	06/2008 -	03/2018	117(O) -	0/0
799	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	208.00	-	04/2008 -	03/2018	119(O) -	0/0
800	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00	-	05/2008 -	02/2018	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
801	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHA, ASSAM ,	12/2003	196.00 -	331.23	-	07/2009 -	03/2018	104(O) -	0/0
802	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHA, ASSAM ,	12/2003	217.61 -	309.56	-	04/2010 -	04/2018	96(O) -	0/0
803	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	05/2018	0(O) -	0/4
804	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	06/2018	0(O) -	0/4
805	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	06/2018	0(O) -	0/4
806	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL, ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
807	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
808	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O) -	0/4
809	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD, ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	-	0/0
810	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD, ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	02/2011	-	0/0
811	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD, ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	-	0/0
812	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD, ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	-	0/0
813	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL, ASSAM , EPC	12/2015	225.02 -	159.20	-	12/2018 -	12/2018	0(O) -	0/4
814	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
815	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM , EPC	01/1991	520.01 -	520.01	-	-	-	-	0/0
816	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
817	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
818	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM , EPC	01/2016	252.00 -	252.00	-	01/2016 -	01/2016	-	0/4
819	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64(O) -	0/0
820	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	-	0/0
821	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
822	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	-	03/2014 -	09/2017	-	0/0
823	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR ,	10/2011	375.09 -	375.09	-	04/2014 -	-	-	0/0
824	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56(O) -	0/0
825	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	-	0/0
826	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH, BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
827	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH, BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	08/2016	-	0/0
828	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH, BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	10/2016	-	0/0
829	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR ,	08/2015	556.07 -	556.07	-	- -	-	-	0/0
830	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR ,	12/2015	1,041.10 -	1,041.10	-	- -	04/2019	- -	0/0
831	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR ,	08/2015	814.04 -	814.04	-	- -	-	-	0/0
832	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR ,	08/2015	322.09 -	322.09	-	- -	04/2018	- -	0/0
833	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR ,	01/1991	642.41 -	642.41	-	- -	-	-	0/0
834	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR ,	12/2015	1,167.45 -	1,167.45	-	- -	-	-	0/0
835	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR ,	08/2015	399.54 -	399.54	-	- -	04/2019	- -	0/0
836	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH, BIHAR ,	01/1991	478.35 -	478.35	-	- -	-	-	0/0
837	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR ,	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
838	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZZAFFARPUR - [N24000522]NHAI, BIHAR ,	08/2015	516.13 -	516.13	-	- -	04/2018	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
839	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	-	-	-	0/0
840	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	-	-	-	0/0
841	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	-	03/2014 -	-	-	0/0
842	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	-	08/2014 -	08/2014	-	0/0
843	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	-	08/2014 -	-	-	0/0
844	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	-	07/2016 -	-	-	0/0
845	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	-	07/2016 -	-	-	0/0
846	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	-	05/2016 -	-	-	0/0
847	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	-	06/2016 -	06/2016	-	0/0
848	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	-	05/2016 -	-	-	0/0
849	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	-	10/2016 -	-	-	0/0
850	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	-	07/2016 -	10/2016	-	0/0
851	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	-	11/2015 -	-	-	0/0
852	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	-	05/2017 -	-	-	0/0
853	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	-	12/2016 -	12/2016	-	0/0
854	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	0(0) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
855	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	-	03/2020 -	03/2020	0(0) -	0/0
856	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	-	08/2017 -	-	-	0/0
857	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	-	- -	-	-	0/0
858	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	-	- -	-	-	0/0
859	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	-	- -	-	-	0/0
860	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	03/2015	-	0/0
861	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	03/2015	-	0/0
862	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	-	-	0/0
863	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
864	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
865	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0
866	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
867	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
868	FOUR LANING OF ORISSACHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH ,	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	-	0/0
869	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	-	- -	05/2018	-	0/0
870	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	-	- -	04/2018	-	0/0
871	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	-	- -	04/2018	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
872	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	771.18	-	- -	03/2018	- -	0/0
873	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	- -	04/2018	- -	0/1
874	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
875	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
876	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
877	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	- -	-	-	0/0
878	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	- -	-	-	0/0
879	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	- -	-	-	0/0
880	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	-	2/3
881	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	-	07/2013 -	-	-	0/0
882	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	-	12/2015 -	07/2017	-	0/3
883	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	-	08/2016 -	-	-	0/0
884	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	-	- -	-	-	0/0
885	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	-	- -	-	-	0/0
886	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	-	- -	-	-	0/0
887	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	-	- -	-	-	0/0
888	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	-	- -	-	-	0/0
889	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	364.56	-	- -	-	-	0/0
890	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
891	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	-	-	-	-	0/0
892	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	-	-	-	-	0/0
893	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020	0(O) -	0/0
894	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	-	10/2017 -	-	-	0/0
895	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	-	05/2010 -	08/2017	-	0/0
896	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76(O) -	0/0
897	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	-	11/2013 -	08/2017	-	0/0
898	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	-	02/2018 -	02/2018	-	0/0
899	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI, HARYANA ,	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
900	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
901	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
902	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	-	04/2019	-	0/0
903	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	-	-	01/2018	-	0/0
904	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA ,	11/2015	867.66 -	867.66	-	-	05/2018	-	0/0
905	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI, HARYANA ,	05/2015	600.85 -	600.85	-	-	05/2018	-	0/0
906	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA ,	08/2016	248.97 -	248.97	-	-	05/2019	-	0/0
907	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	1,004.67	-	-	05/2019	-	0/0
908	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA ,	03/2017	639.79 -	552.90	-	03/2020 -	03/2020	0(O) -	0/0
909	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	-	11/2016 -	02/2018	-	0/0
910	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI, HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	-	03/2018 -	03/2018	0(O) -	0/0
911	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	-	-	02/2019	-	0/0
912	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI, HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
913	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	-	-	-	-	0/0
914	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	-	-	-	-	0/0
915	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020	0(O) -	0/0
916	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44(O) -	0/0
917	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
918	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	-	07/2013 -	11/2017	-	0/0
919	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	-	0/0
920	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
921	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
922	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	-	-	-	-	0/0
923	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	881.08	06/2015 -	12/2017	-	0/0
924	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	329.10	-	03/2019	-	0/0
925	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	-	-	-	-	0/0
926	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	37.20	-	08/2018	-	0/0
927	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	-	03/2020 -	03/2020	0(O) -	0/0
928	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	-	03/2020 -	03/2020	0(O) -	0/0
929	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	-	-	-	-	0/0
930	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	-	-	-	-	0/0
931	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	-	06/2018	-	3/3

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
932	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	-	0/0
933	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	-	0/0
934	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	293.12	09/2017 -	09/2018	12(O) -	0/0
935	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	-	0/0
936	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,484.71	08/2016 -	02/2019	30(O) -	0/0
937	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	654.13	- -	08/2018	- -	0/0
938	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	5.78	- -	03/2019	- -	0/0
939	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	4.03	- -	03/2019	- -	0/0
940	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	- -	-	-	0/0
941	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	89.91	- -	04/2020	- -	0/0
942	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	118.34	- -	03/2019	- -	0/0
943	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	100.33	- -	08/2019	- -	0/0
944	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	10.50	03/2020 -	06/2020	3(O) -	0/0
945	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	67.09	03/2020 -	05/2020	2(O) -	0/0
946	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	-	0/0
947	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017	-	0/0
948	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	.02	11/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
949	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	-	- -	11/2017	-	0/0
950	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0
951	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	-	09/2017 -	-	-	0/0
952	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	-	04/2013 -	09/2017	-	0/0
953	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	-	05/2013 -	07/2017	-	0/0
954	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	07/2017	-	0/0
955	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	09/2016	-	0/0
956	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
957	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	-	-	0/0
958	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	02/2016	-	0/0
959	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	-	0/0
960	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	05/2017	-	0/0
961	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
962	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	08/2016	-	0/0
963	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	-	0/0
964	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	04/2015	-	0/0
965	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	02/2015	-	0/0
966	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	-	- -	-	-	0/0
967	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	-	- -	-	-	0/0
968	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	05/2017	-	0/0
969	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(0) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
970	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018	0(O) -	0/0
971	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
972	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	-	11/2015 -	09/2017	-	0/0
973	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36(O) -	0/0
974	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
975	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	-	- -	-	-	0/0
976	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	- -	01/2019	-	0/0
977	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	-	0/0
978	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	-	- -	01/2019	-	0/0
979	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	-	10/2017 -	-	-	0/0
980	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	-	09/2017 -	-	-	0/0
981	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	-	09/2017 -	-	-	0/0
982	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	-	- -	-	-	0/0
983	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	-	- -	-	-	0/0
984	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	-	- -	-	-	0/0
985	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
986	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,091.65	03/2013 -	12/2017	-	0/0
987	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	437.90	06/2014 -	03/2018	45(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
988	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49(O) -	2/2
989	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	11/2016	-	0/2
990	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	- -	10/2017	-	0/4
991	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	07/2016	-	0/12
992	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	- -	06/2017	-	0/4
993	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	11/2016	-	0/4
994	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	- -	-	-	0/0
995	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	65.16	- -	-	-	0/0
996	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	205.97	- -	11/2014	-	0/0
997	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
998	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	-	0/0
999	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	157.92	- -	05/2018	-	0/0
1000	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	- -	05/2018	-	0/0
1001	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	-	0/0
1002	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	45.11	- -	05/2018	-	0/0
1003	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	31.47	- -	03/2019	-	0/0
1004	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	161.13	- -	05/2018	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1005	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,479.56	07/2017 -	01/2018	-	0/0
1006	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	535.52	11/2016 -	11/2017	-	0/0
1007	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
1008	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,881.81	01/2018 -	01/2018	-	0/0
1009	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,263.02	06/2012 -	03/2018	69(O) -	0/0
1010	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	11/2014	-	0/0
1011	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	-	- -	07/2018	- -	0/0
1012	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	-	- -	07/2019	- -	0/0
1013	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	-	- -	07/2019	- -	0/0
1014	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	-	- -	07/2018	- -	0/0
1015	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	-	- -	-	-	0/0
1016	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	-	- -	-	-	0/0
1017	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	-	- -	-	-	0/0
1018	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	-	- -	-	-	0/0
1019	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	-	- -	03/2019	- -	0/0
1020	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	-	- -	03/2019	- -	0/0
1021	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	-	- -	-	-	0/0
1022	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	43.29	- -	05/2019	- -	0/0
1023	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	6.00	02/2020 -	02/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1024	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	-	03/2020 -	03/2020	0(O) -	0/0
1025	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	-	03/2020 -	03/2020	0(O) -	0/0
1026	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020	0(O) -	0/0
1027	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	-	03/2020 -	03/2020	0(O) -	0/0
1028	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	-	03/2017 -	-	-	0/0
1029	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	86.42	03/2020 -	05/2019	-10(O) -	0/0
1030	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020	0(O) -	0/0
1031	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	-	- -	-	-	0/0
1032	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	-	- -	-	-	0/0
1033	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	-	- -	-	-	0/0
1034	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50(O) -	0/0
1035	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	02/2011	-	0/0
1036	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	-	- -	05/2018	-	0/0
1037	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
1038	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0
1039	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	10/2010	-	0/0
1040	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1041	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	09/2017	-	2/2
1042	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	-	0/0
1043	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49(O) -	0/0
1044	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,167.15	03/2013 -	11/2017	-	0/0
1045	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	-	04/2015 -	12/2017	-	0/0
1046	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	-	-	-	0/0
1047	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
1048	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	-	-	-	-	0/0
1049	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
1050	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36(O) -	0/0
1051	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36(O) -	0/0
1052	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36(O) -	0/0
1053	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	-	04/2017 -	-	-	0/0
1054	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42(O) -	0/0
1055	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	-	06/2014 -	12/2017	-	0/0
1056	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	10/2017	-	0/0
1057	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	-	0/0
1058	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	05/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1059	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	-	0/0
1060	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	-	- -	-	-	0/0
1061	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	-	- -	-	-	0/0
1062	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	-	0/0
1063	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
1064	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	-	- -	-	-	0/0
1065	DEVELOPMENT OF FOUR LANNING OF ANGUL -SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	-	- -	08/2019	- -	0/0
1066	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	-	- -	-	-	0/0
1067	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	-	0/0
1068	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	-	04/2018 -	04/2018	0(O) -	0/0
1069	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	-	10/2017 -	10/2017	-	0/0
1070	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	-	10/2017 -	10/2017	-	0/0
1071	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	-	05/2016 -	03/2017	-	0/0
1072	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	-	01/2017 -	-	-	0/0
1073	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	-	06/2016 -	-	-	0/0
1074	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5(O) -	0/0
1075	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	-	05/2016 -	03/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1076	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2018	-24(O) -	0/0
1077	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	-	07/2017 -	-	-	0/0
1078	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	-	- -	-	-	0/0
1079	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	-	- -	-	-	0/0
1080	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	-	- -	-	-	0/0
1081	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	-	- -	-	-	0/0
1082	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	-	- -	-	-	0/0
1083	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	-	- -	-	-	0/0
1084	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	-	- -	-	-	0/0
1085	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	-	- -	-	-	0/0
1086	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	-	- -	-	-	0/0
1087	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	-	- -	-	-	0/0
1088	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	-	- -	-	-	0/0
1089	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1090	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1091	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1092	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1093	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	-	01/2016 -	12/2017	-	0/0
1094	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1095	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1096	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1097	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1098	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1099	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1100	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1101	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1102	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1103	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	-	- -	11/2017	-	0/0
1104	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	-	- -	12/2017	-	0/0
1105	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB ,	12/2015	239.23 -	239.23	-	12/2017 -	12/2017	-	0/0
1106	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16(O) -	0/0
1107	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1108	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1109	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1110	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	-	-	-	-	0/0
1111	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	-	03/2020 -	03/2020	0(0) -	0/0
1112	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN ,	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
1113	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	-	0/0
1114	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN ,	03/2014	240.10 -	240.10	-	03/2016 -	-	-	0/0
1115	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1116	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1117	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
1118	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
1119	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1120	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(0) -	0/0
1121	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN ,	08/2015	538.08 -	538.08	-	02/2018 -	02/2018	-	0/0
1122	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	-	09/2016 -	09/2017	-	0/0
1123	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN ,	08/2015	482.27 -	482.27	-	02/2018 -	02/2018	-	0/0
1124	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN ,	07/2015	455.60 -	455.60	-	07/2017 -	07/2017	-	0/0
1125	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14 -	279.14	-	05/2017 -	-	-	0/0
1126	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN ,	10/2014	264.72 -	264.72	-	04/2017 -	-	-	0/0
1127	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	-	03/2018 -	03/2018	0(0) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1128	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	10/2016	-	0/0
1129	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	206.78	05/2016 -	05/2016	-	0/0
1130	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6(O) -	0/0
1131	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	-	08/2016 -	-	-	0/0
1132	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	-	04/2018 -	04/2018	0(O) -	0/0
1133	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1134	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1135	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	-	10/2011 -	12/2017	-	0/0
1136	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	-	- -	02/2018	-	0/0
1137	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019 -	-	-	0/0
1138	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019 -	06/2019	0(O) -	0/0
1139	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	-	06/2019 -	06/2019	0(O) -	0/0
1140	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	-	- -	-	-	0/0
1141	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	-	- -	10/2018	- -	0/0
1142	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	-	- -	01/2019	- -	0/0
1143	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1144	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	-	-	-	-	0/0
1145	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	-	-	-	-	0/0
1146	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	-	04/2020 -	04/2020	0(O) -	0/0
1147	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	-	10/2017 -	-	-	0/0
1148	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	-	-	-	-	0/0
1149	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	-	08/2013 -	-	-	0/0
1150	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
1151	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1152	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	-	10/2017 -	10/2017	-	0/0
1153	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60(O) -	0/0
1154	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	319.76	06/2013 -	-	-	0/0
1155	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67(O) -	0/0
1156	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64(O) -	0/0
1157	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1158	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	-	08/2015 -	-	-	0/0
1159	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	-	07/2015 -	-	-	0/0
1160	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	08/2015	-	0/0
1161	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	769.28	11/2017 -	08/2018	9(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1162	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12(O) -	0/0
1163	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1164	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19(O) -	0/0
1165	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0
1166	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	129.75	- -	08/2018	- -	0/0
1167	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	74.13	- -	07/2018	- -	0/0
1168	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	-	03/2020 -	03/2020	0(O) -	0/0
1169	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	173.62	07/2016 -	07/2018	24(O) -	0/0
1170	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	-	08/2017 -	-	-	0/0
1171	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	-	09/2017 -	-	-	0/0
1172	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	-	09/2017 -	-	-	0/0
1173	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	-	- -	-	-	0/0
1174	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	1,375.60	09/2016 -	06/2018	21(O) -	0/0
1175	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1176	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1177	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1178	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
1179	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1180	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	-	0/4
1181	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	-	0/1
1182	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	-	0/0
1183	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1184	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	-	- -	11/2018	- -	0/0
1185	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018	0(O) -	0/4
1186	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	04/2017	-	0/4
1187	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,667.96	06/2013 -	09/2017	-	0/0
1188	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,986.56	08/2013 -	08/2017	-	0/0
1189	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	693.46	09/2013 -	10/2017	-	0/0
1190	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	347.49	01/2014 -	12/2017	-	0/0
1191	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	-	0/0
1192	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
1193	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	03/2016	-	0/0
1194	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	-	0/0
1195	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	86.28	05/2017 -	06/2018	13(O) -	0/0
1196	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	409.92	01/2016 -	11/2017	-	0/0
1197	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	-	09/2016 -	09/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1198	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	147.92	01/2016 -	-	-	0/0
1199	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	566.34	01/2016 -	11/2017	-	0/0
1200	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	-	0/0
1201	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	-	0/0
1202	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	-	0/0
1203	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(0) -	0/0
1204	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	03/2017	-	0/0
1205	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	-	0/0
1206	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	-	0/0
1207	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH ,	09/2015	768.56 -	768.56	699.98	03/2018 -	03/2018	0(0) -	0/0
1208	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH ,	09/2015	664.53 -	664.53	590.82	03/2018 -	03/2018	0(0) -	0/0
1209	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH ,	09/2015	789.31 -	789.31	814.19	03/2018 -	03/2018	0(0) -	0/0
1210	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	796.52	03/2018 -	03/2018	0(0) -	0/0
1211	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	545.00	-	01/2019	-	0/0
1212	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	383.55	06/2016 -	06/2018	24(0) -	0/0
1213	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	141.16	06/2018 -	06/2018	0(0) -	0/0
1214	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	228.89	06/2018 -	06/2018	0(0) -	0/0
1215	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	195.03	07/2018 -	06/2018	-1(0) -	0/0
1216	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	247.71	06/2018 -	06/2018	0(0) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1217	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	08/2015	-	0/0
1218	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1219	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1220	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	.45	- -	-	-	0/0
1221	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0
1222	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
1223	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	115.21	- -	04/2019	-	0/0
1224	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	28.08	- -	-	-	0/0
1225	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	13.55	- -	-	-	0/0
1226	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	24.95	- -	04/2019	-	0/0
1227	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	-	- -	04/2019	-	0/0
1228	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	-	- -	-	-	0/0
1229	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	-	- -	-	-	0/0
1230	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	-	- -	-	-	0/0
1231	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	-	- -	04/2019	-	0/0
1232	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	49.05	- -	-	-	0/0
1233	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	165.66	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1234	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020	0(O) -	0/0
1235	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020	0(O) -	0/0
1236	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020	0(O) -	0/0
1237	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	23.48	03/2020 -	03/2020	0(O) -	0/0
1238	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	-	- -	-	-	0/0
1239	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	-	- -	-	-	0/0
1240	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	-	- -	-	-	0/0
1241	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	-	- -	-	-	0/0
1242	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	-	10/2013 -	12/2017	-	0/0
1243	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	-	- -	-	-	0/0
1244	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	-	- -	-	-	0/0
1245	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	578.25	- -	07/2018	-	0/0
1246	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	-	05/2018 -	05/2018	0(O) -	0/0
1247	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	-	06/2018 -	06/2018	0(O) -	0/0
1248	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	-	05/2018 -	05/2018	0(O) -	0/0
1249	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,436.15	08/2013 -	12/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1250	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,952.35	08/2013 -	03/2018	55(O) -	0/0
1251	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,811.29	09/2014 -	12/2017	-	0/0
1252	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	564.39	07/2014 -	03/2018	44(O) -	0/0
1253	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	03/2018	0(O) -	0/0
1254	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	-	-	01/2018	-	0/0
1255	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	184.92	06/2018 -	06/2018	0(O) -	0/0
1256	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	2,313.68	-	12/2017	-	0/0
1257	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	35.17	-	11/2018	-	0/0
1258	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	123.13	-	08/2018	-	0/0
	Total		3,51,472.35 -	3,57,629.96	62,776.84				23/182
	SHIPPING AND PORTS								
1259	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 669.46	669.46	413.91	12/2010 -	12/2018	96(O) -	0/0
1260	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1261	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
1262	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL, TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 247.00	255.00	255.02	06/2017 -	-	-	1/1
1263	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL, TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.33	275.98	275.98	12/2017 03/2018	-	-	1/1
1264	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL, TAMIL NADU ,	12/2014	274.85 334.00	321.94	321.94	04/2017 12/2017	-	-	1/1
1265	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU ,	03/2016	600.00 257.90	257.90	1.45	12/2017 05/2020	05/2020	29(O) 0(R)	0/0
	Total		4,262.08 -	4,807.68	2,239.31				3/3
	TELECOMMUNICATIONS								

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1266	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9(O) -	0/0
1267	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT , Central Sector Projects	09/2017	171.54 -	171.54	-	05/2018 -	05/2018	0(O) -	0/0
1268	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	159.30 -	159.30	-	04/2018 -	04/2018	0(O) -	0/0
1269	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	167.68 -	167.68	-	04/2018 -	04/2018	0(O) -	0/0
1270	MAHARASHTRA ACCESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	212.70 -	212.70	-	05/2018 -	05/2018	0(O) -	0/0
1271	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30 -	215.30	-	05/2018 -	05/2018	0(O) -	0/0
1272	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	7,642.00	07/2015 04/2020	04/2020	57(O) 0(R)	0/0
1273	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]TI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
1274	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH ,	11/2017	169.45 -	169.45	-	08/2018 -	08/2018	0(O) -	0/0
	Total		16,959.40 -	28,189.40	8,068.20				0/70
	URBAN DEVELOPMENT								
1275	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	120.56	03/2017 -	-	-	3/5
1276	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	-	-	-	-	0/0
1277	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	-	03/2019 -	03/2019	0(O) -	0/7
1278	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	-	06/2017 -	06/2020	36(O) -	0/0
1279	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI ,	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24(O) -	0/0
1280	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	210.53	10/2019 -	03/2020	5(O) -	0/7
1281	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	582.84	12/2015 -	05/2018	29(O) -	0/0
1282	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,118.00	3,245.00	11/2019 -	11/2019	0(O) -	1/7

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1283	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	4.91	- -	04/2019	- -	0/2
1284	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	-	- -	-	-	0/0
1285	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 2.00	238.56	-	05/2020 -	05/2020	0(O) -	0/0
1286	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	-	06/2019 -	06/2019	0(O) -	0/0
1287	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	-	- -	-	-	0/0
1288	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	142.67	11/2014 -	10/2018	47(O) -	0/8
1289	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	40.05	03/2016 -	12/2018	33(O) -	1/6
1290	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1291	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	1.66	02/2020 -	02/2020	0(O) -	0/0
1292	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	25.91	10/2012 -	03/2018	65(O) -	0/1
1293	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29(O) -	0/0
1294	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA ,	07/2015	154.00 -	154.00	90.76	11/2015 05/2018	05/2018	30(O) 0(R)	0/0
1295	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC	05/2016	164.00 -	164.00	85.46	11/2018 05/2018	05/2018	-6(O) 0(R)	7/11
1296	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33 349.33	349.33	307.50	03/2016 12/2017	04/2018	25(O) 4(R)	0/13
1297	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	170.62	149.22	03/2012 -	06/2018	75(O) -	15/20
1298	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 8,680.00	8,680.00	3,480.63	03/2018 12/2019	12/2019	21(O) 0(R)	0/0
1299	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	-	01/2015 -	-	-	0/0
1300	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44(O) -	0/10
1301	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	337.03	05/2017 02/2018	08/2018	15(O) 6(R)	7/12
1302	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	75.91	04/2019 06/2019	06/2019	2(O) 0(R)	3/8

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(March 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1303	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN , Central Sector Projects	08/2014	350.02 479.87	479.87	452.35	03/2015 12/2017	04/2018	37(O) 4(R)	0/0
1304	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU ,	04/2014	332.72 -	321.00	305.18	09/2016 03/2018	05/2018	20(O) 2(R)	0/0
1305	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	14,784.59	12/2015 -	-	-	11/24
1306	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD, TAMIL NADU ,	12/2015	209.00 -	209.00	26.00	- -	10/2019	- -	0/6
1307	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL, TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018	0(O) -	0/0
1308	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD, TAMIL NADU ,	11/2017	348.77 -	348.77	-	- -	-	-	0/0
1309	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD, TELANGANA ,	10/2016	209.84 -	209.84	1.65	03/2020 -	03/2020	0(O) -	0/5
1310	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1311	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND ,	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70(O) -	0/0
1312	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL ,	02/2014	156.57 -	156.57	133.20	08/2016 -	06/2018	22(O) -	8/13
1313	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	56.09	04/2018 -	05/2019	13(O) -	2/6
	Total		1,42,902.14 -	1,47,933.23	63,910.25				58/171
	DEFENCE PRODUCTION								
1314	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA ,	12/2016	167.69 168.00	172.99	62.51	05/2018 -	05/2018	0(O) -	4/5
1315	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL, GOA ,	12/2016	285.95 286.00	296.05	49.14	08/2020 -	08/2020	0(O) -	3/3
	Total		453.64 -	469.04	111.65				7/8
	Grand Total		16,23,254.71	18,41,400.35	6,63,626.77				2225/3960


Summary of projects in the Flash Report for the month of March, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1304
Number of Projects completed/dropped/frozen in Current Month	8
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	21
Number of Projects in Current Month	1315

Brief Analysis


Project Status with respect to Original Schedule: Out of 1315 projects, 15 projects are ahead of schedule, 315 projects are on schedule 254 projects are delayed. 593 projects do not have fixed dates of commissioning. 138 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

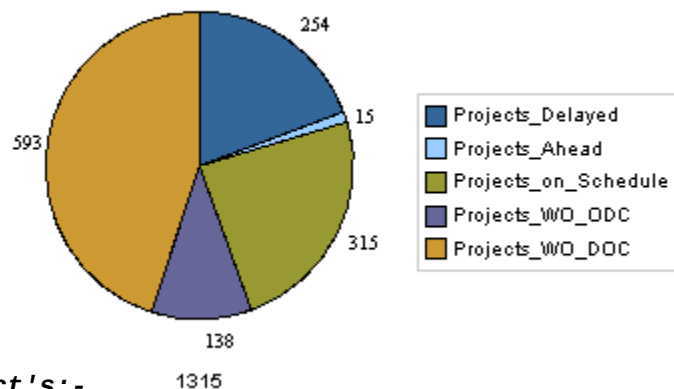

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1315 projects when sanctioned, was of the order of Rs. 1623254.71 crore but this was subsequently revised to Rs. 1841400.35 crore implying a cost overrun of 13.4%. The expenditure incurred on these projects till March, 2018 is Rs. 663626.77 crore, which is 36% of the anticipated cost of the projects.

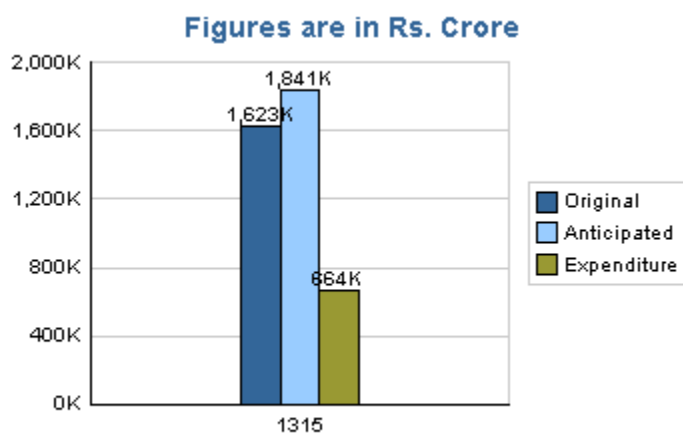

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

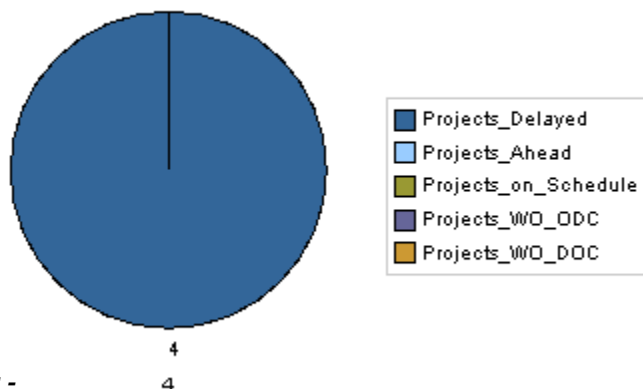


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 69728 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till March, 2018 is Rs. 28425.34 crore, which is 40.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

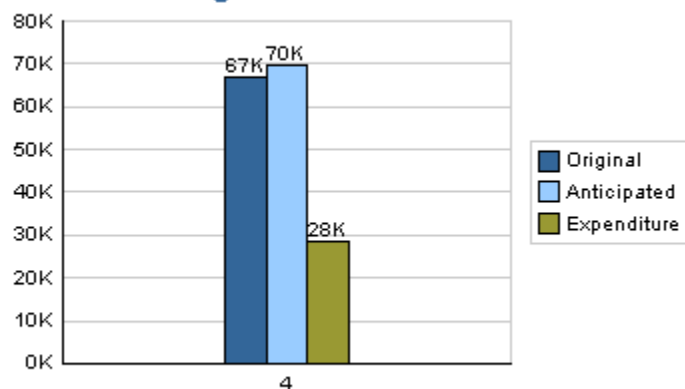

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

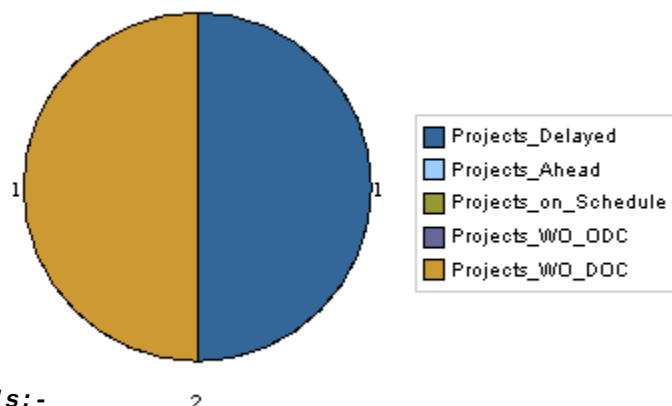


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 624.07 crore but this was subsequently anticipated to Rs. 994.86 crore implying a cost overrun of 59.4%. The expenditure incurred on these projects till March, 2018 is Rs. 549.39 crore, which is 55.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

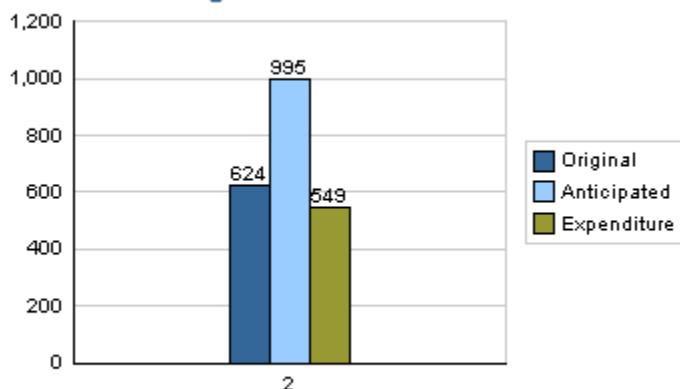

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	92
Number of Projects On Schedule	51
Number of Projects Delayed	37
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 92 projects, 1 project is ahead of schedule, 51 projects are on schedule 37 projects are delayed. 3 projects do not have fixed dates of commissioning.

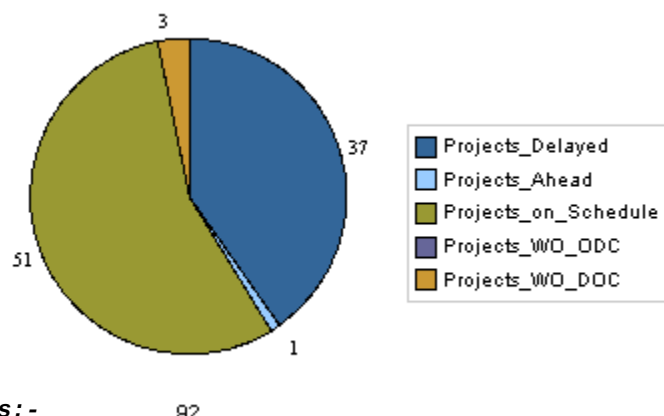


Total No Of Project's:-

92

Investment Scenario

Total original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 89695.08 crore but this was subsequently anticipated to Rs. 89199.09 cr The expenditure incurred on these projects till March, 2018 is Rs. 23882.46 crore, which is 26.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

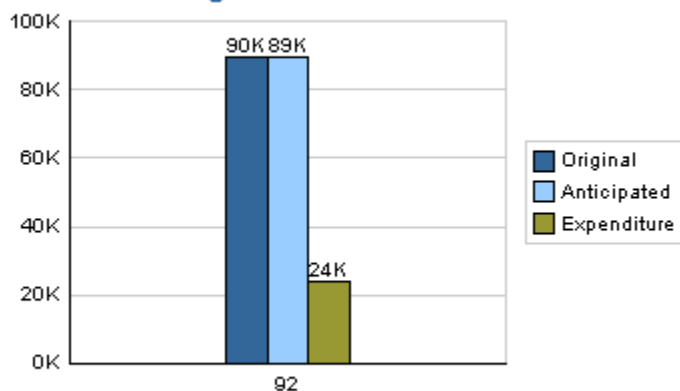

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule 2 projects are delayed.

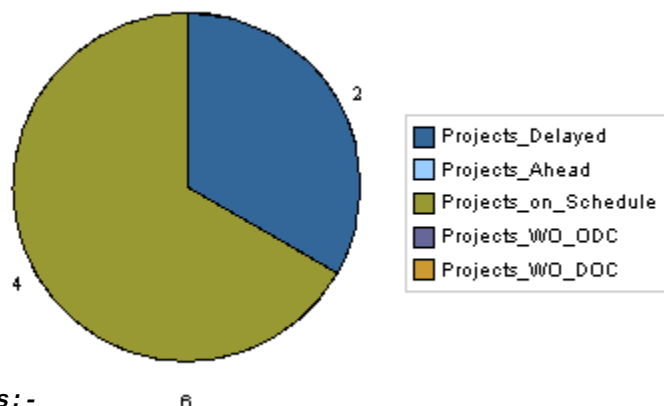


Total No Of Project's:-

6

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 1781.92 crore but this was subsequently anticipated to Rs. 1793.57 crore implying a cost overrun of .7%. The expenditure incurred on these projects till March, 2018 is Rs. 574.82 crore, which is 32% of the anticipated cost of the projects.

Figures are in Rs. Crore

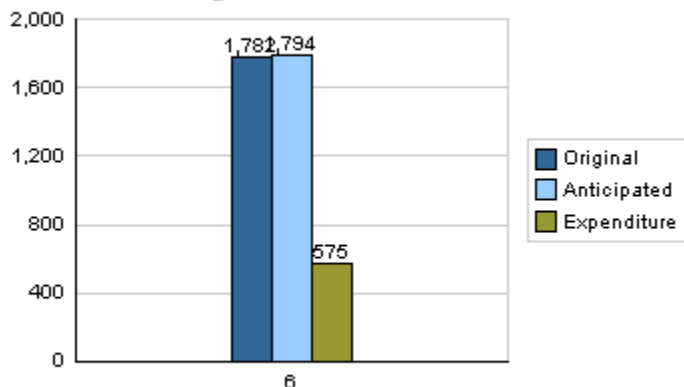

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	4
Number of Projects On Schedule	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are on schedule

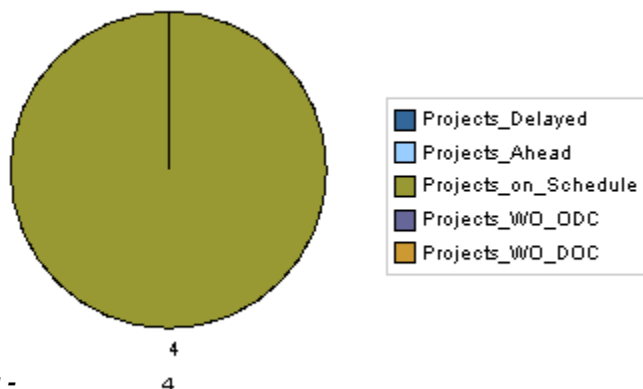


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6912 crore but this was subsequently anticipated to Rs. 6912 crore. The expenditure incurred on these projects till March, 2018 is Rs. 408.41 crore, which is 5.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

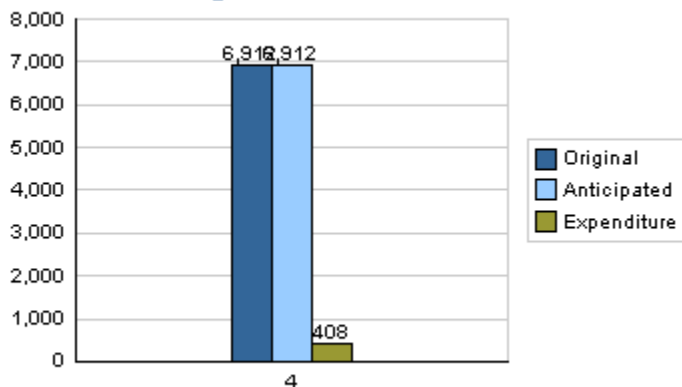

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	30
Number of Projects On Schedule	5
Number of Projects Delayed	15

Number of Projects Without Date Of Commissioning 10

Brief Analysis

Project Status with respect to Original Schedule: Out of 30 projects, 5 projects are on schedule 15 projects are delayed. 10 projects do not have fixed dates of commissioning.

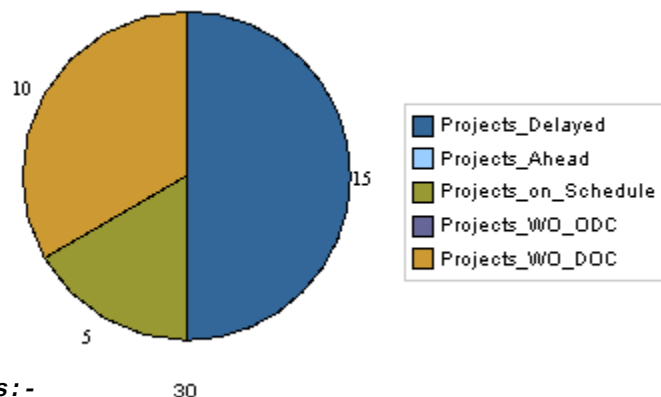


Total No Of Project's:-

30

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 54971.33 crore but this was subsequently anticipated to Rs. 55185.01 crore implying a cost overrun of .4%. The expenditure incurred on these projects till March, 2018 is Rs. 40748.78 crore, which is 73.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

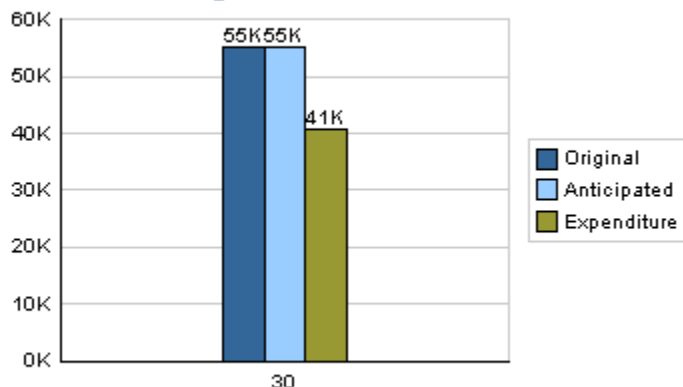

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	124
Number of Projects On Schedule	77
Number of Projects Delayed	27
Number of Projects Ahead	8
Number of Projects Without Date Of Commissioning	12

Brief Analysis

Project Status with respect to Original Schedule: Out of 124 projects, 8 projects are ahead of schedule, 77 projects are on schedule 27 projects are delayed. 12 projects do not have fixed dates of commissioning.

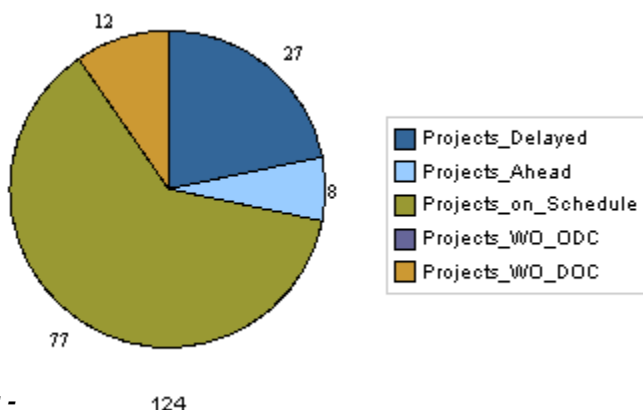


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 124 projects when sanctioned, was of the order of Rs. 210560.21 crore but this was subsequently anticipated to Rs. 212573.46 crore implying a cost overrun of 1%. The expenditure incurred on these projects till March, 2018 is Rs. 64610.38 crore, which is 30.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

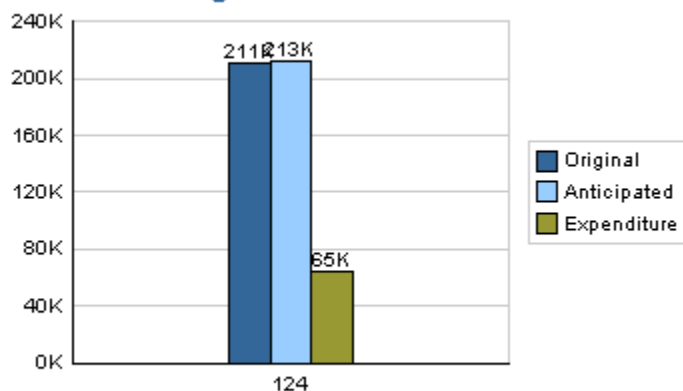

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	117
Number of Projects On Schedule	46
Number of Projects Delayed	62
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 117 projects, 1 project is ahead of schedule, 46 projects are on schedule 62 projects are delayed. 8 projects do not have fixed dates of commissioning.

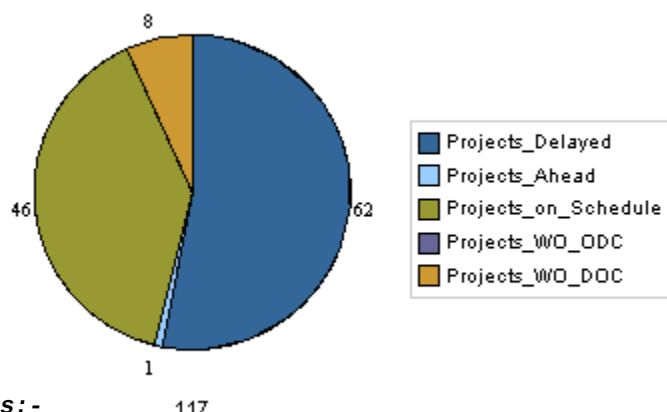


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 117 projects when sanctioned, was of the order of Rs. 328395.59 crore but this was subsequently anticipated to Rs. 395733.97 crore implying a cost overrun of 20.5%. The expenditure incurred on these projects till March, 2018 is Rs. 233023.13 crore, which is 58.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

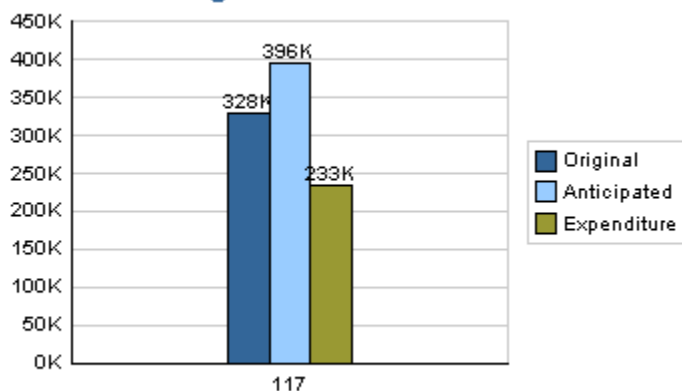

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

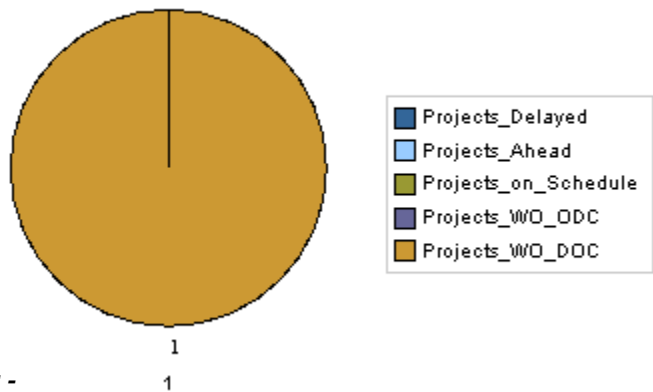


Total No Of Project's:- 1

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till March, 2018 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

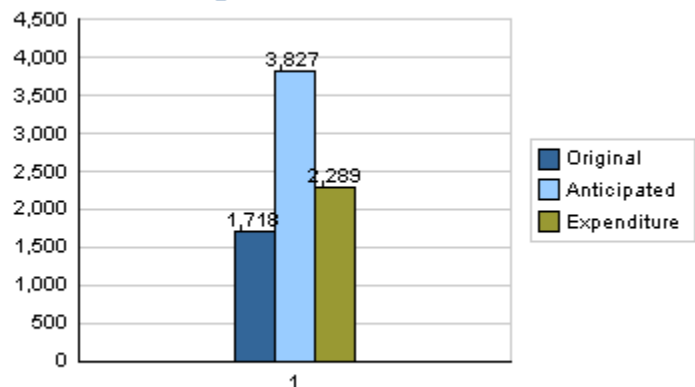

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	14
Number of Projects On Schedule	5
Number of Projects Delayed	6

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 14 projects, 5 projects are on schedule 6 projects are delayed. 3 projects do not have fixed dates of commissioning.

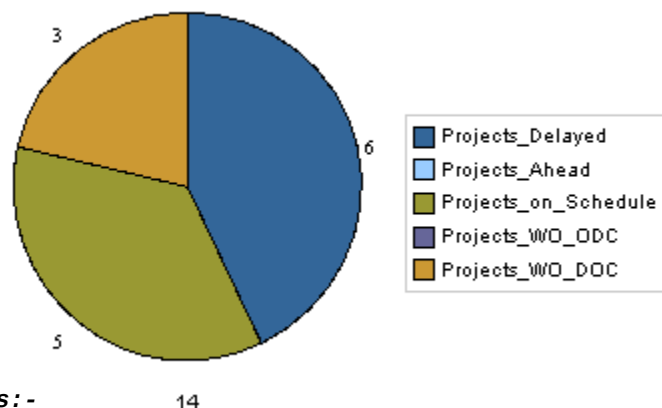


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 3897.21 crore but this was subsequently anticipated to Rs. 3919.69 crore implying a cost overrun of .6%. The expenditure incurred on these projects till March, 2018 is Rs. 1507.4 crore, which is 38.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

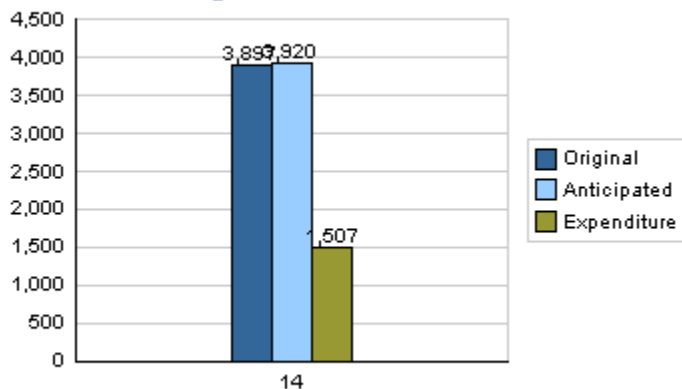

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	334
Number of Projects On Schedule	39
Number of Projects Delayed	29
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	76
Number of Projects Without Date Of Commissioning	189

Brief Analysis

Project Status with respect to Original Schedule: Out of 334 projects, 1 project is ahead of schedule, 39 projects are on schedule 29 projects are delayed. 189 projects do not have fixed dates of commissioning. 76 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

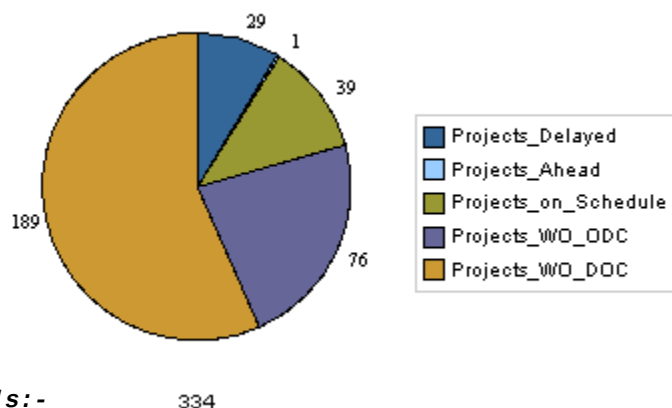


Total No Of Project's:-

334

Investment Scenario

Total original cost of implementation of 334 projects when sanctioned, was of the order of Rs. 341529.69 crore but this was subsequently anticipated to Rs. 462504.09 crore implying a cost overrun of 35.4%. The expenditure incurred on these projects till March, 2018 is Rs. 130501.41 crore, which is 28.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

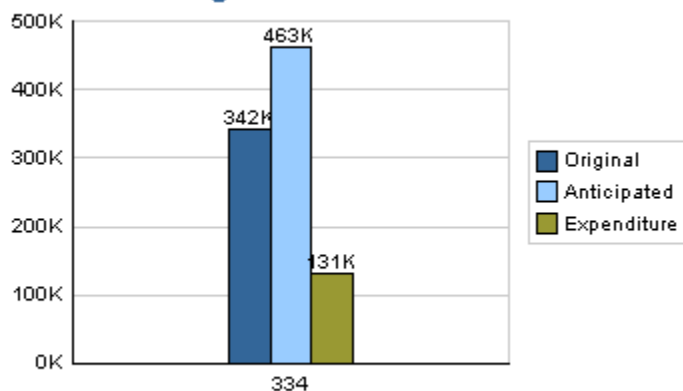

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	530
Number of Projects On Schedule	68
Number of Projects Delayed	46
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	60
Number of Projects Without Date Of Commissioning	353

Brief Analysis

Project Status with respect to Original Schedule: Out of 530 projects, 3 projects are ahead of schedule, 68 projects are on schedule 46 projects are delayed. 353 projects do not have fixed dates of commissioning. 60 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

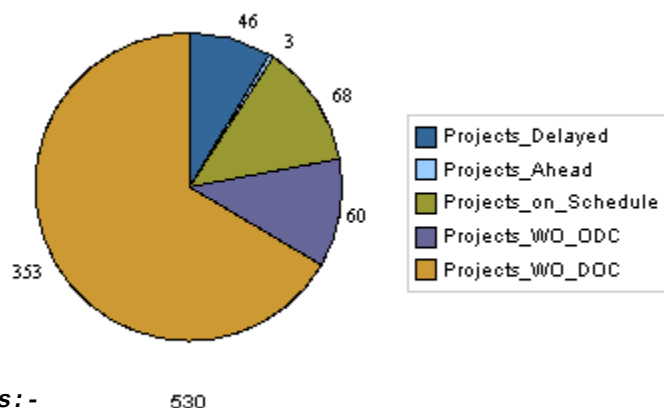


Total No Of Project's:-

530

Investment Scenario

Total original cost of implementation of 530 projects when sanctioned, was of the order of Rs. 351472.35 crore but this was subsequently anticipated to Rs. 357629.96 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till March, 2018 is Rs. 62776.84 crore, which is 17.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

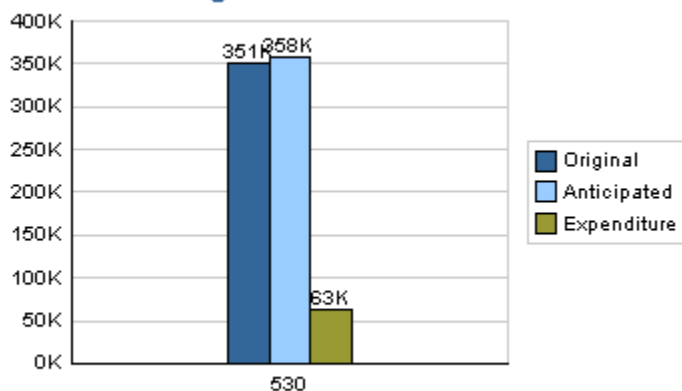

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects 7

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 5

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 2 projects are delayed. 5 projects do not have fixed dates of commissioning.

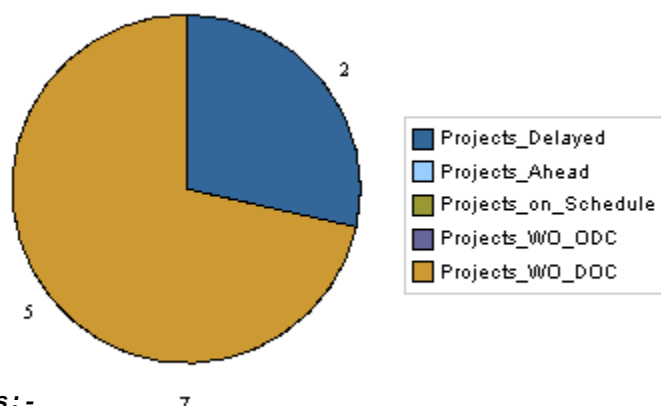


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 4262.08 crore but this was subsequently anticipated to Rs. 4807.68 crore implying a cost overrun of 12.8%. The expenditure incurred on these projects till March, 2018 is Rs. 2239.31 crore, which is 46.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

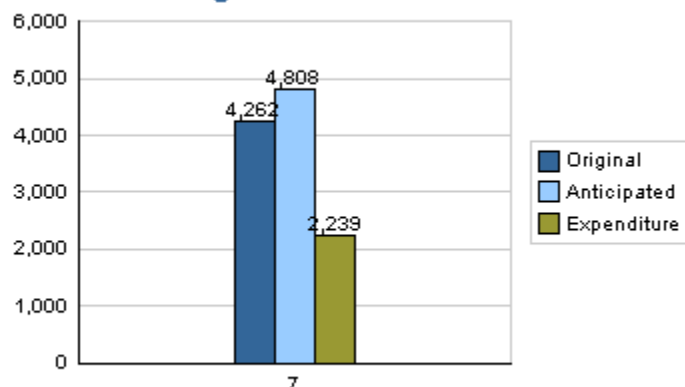

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	9
Number of Projects On Schedule	6
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 6 projects are on schedule 2 projects are delayed. 1 project does not have fixed dates of commissioning.

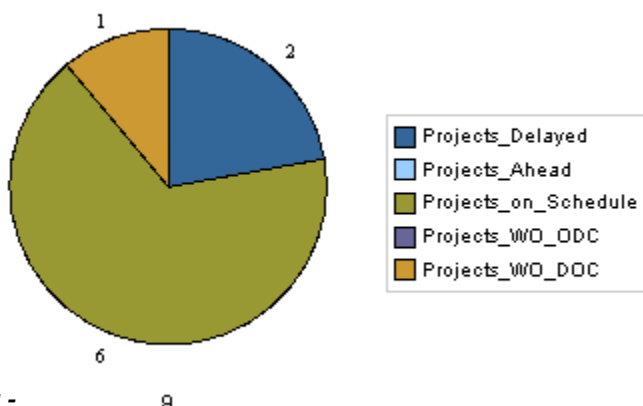


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 16959.4 crore but this was subsequently anticipated to Rs. 28189.4 crore implying a cost overrun of 66.2%. The expenditure incurred on these projects till March, 2018 is Rs. 8068.2 crore, which is 28.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

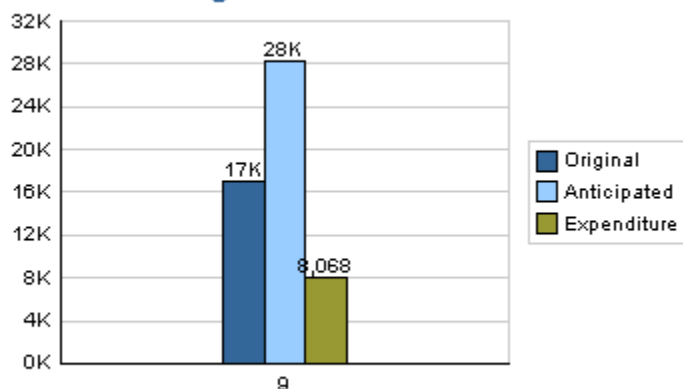

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	39
Number of Projects On Schedule	8
Number of Projects Delayed	21
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 39 projects, 1 project is ahead of schedule, 8 projects are on schedule 21 projects are delayed. 7 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

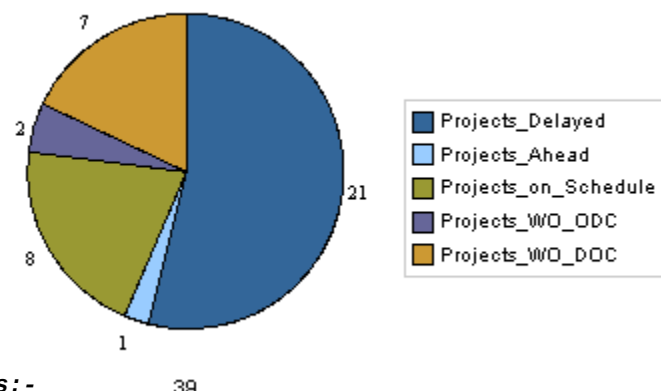


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 39 projects when sanctioned, was of the order of Rs. 142902.14 crore but this was subsequently anticipated to Rs. 147933.23 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till March, 2018 is Rs. 63910.25 crore, which is 43.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

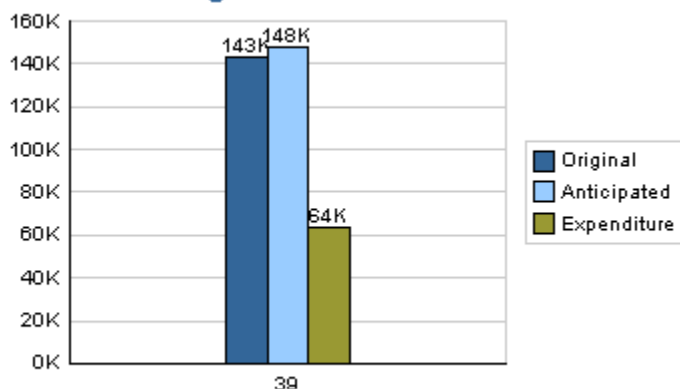

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule

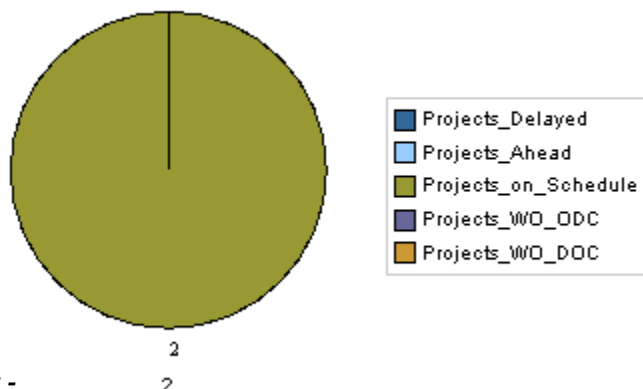


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 469.04 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till March, 2018 is Rs. 111.65 crore, which is 23.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

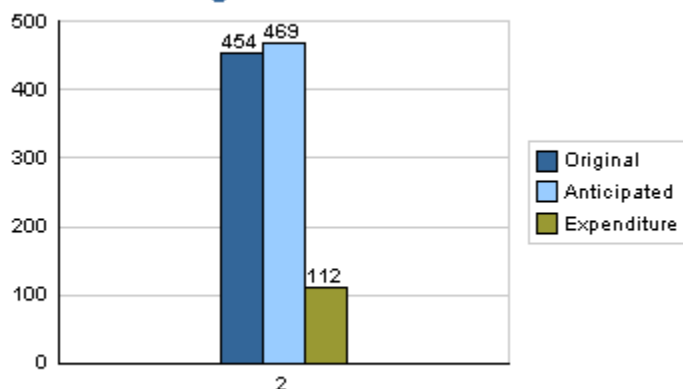

Annexure

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (MARCH 2018)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	5	1,575.26	1,575.26	0
2	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	26.44
3	ANDHRA PRADESH	61	97,970.05	1,02,492.35	7,493.68
4	ARUNACHAL PRADESH	31	16,602.41	32,431.5	18,413.06
5	ASSAM	44	26,450.2	36,075.5	17,967.56
6	BIHAR	81	69,841.31	86,662.38	40,040.8
7	CHHATISGARH	39	84,327.14	86,930.08	50,999.22
8	D & N HAVELI	1	6,086.08	5,842.31	2,765.06
9	DELHI	18	53,421.22	53,688.53	39,283.2
10	GOA	9	4,043.51	4,058.91	192.86
11	GUJARAT	48	44,056.76	47,616.96	19,169.29
12	HARYANA	22	14,152.14	16,038.37	1,384.24
13	HIMACHAL PRADESH	12	14,659.32	22,591.6	7,119.62
14	JAMMU AND KASHMIR	10	25,238.37	51,229.67	22,237.04
15	JHARKHAND	47	47,354.89	51,956.21	21,639.55
16	KARNATAKA	41	70,570.56	80,140.31	28,540.39
17	KERALA	20	22,456.58	29,047.66	2,687.03
18	MADHYA PRADESH	62	64,865.15	70,922.08	22,150.68
19	MAHARASHTRA	128	1,79,962.13	1,93,009.07	69,202.62
20	MANIPUR	2	944.25	9,874.69	7,439.18
21	MEGHALAYA	6	7,108.02	9,025	285.46
22	MIZORAM	4	1,632.48	5,613.14	2,082.55
23	MULTI STATE	176	2,99,041.56	3,01,840.01	97,803.3
24	NAGALAND	7	8,126.79	10,276.79	431.96
25	ODISHA	80	81,553.38	90,298.41	23,072.64
26	PUNJAB	30	16,014.41	16,020.14	2,636.78
27	RAJASTHAN	58	43,665.58	45,121.88	13,813.78
28	SIKKIM	6	2,537.08	5,585.45	931.23
29	TAMIL NADU	62	1,08,723.72	1,24,637.01	48,743.84
30	TELANGANA	36	24,952.57	27,652.97	6,970.47
31	TRIPURA	10	3,991.45	8,658.23	5,896.57
32	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	37,423.84
33	UTTARAKHAND	17	18,576.59	36,046.09	8,957.33
34	WEST BENGAL	52	51,062.35	64,821.5	35,825.5
TOTAL		1,315	16,23,254.71	18,41,400.35	6,63,626.77

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs.150 Crore and above						(March 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	ATOMIC ENERGY						
	Nuclear Power Corporation Of India Limited						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	11,459.00	11,554.00	12/2015 11/2016	06/2020
	Total		11,459.00 -	11,459.00	11,554.00		
	CIVIL AVIATION						
	Airport Authority Of India Limited						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	1/2009	309.46 -	553.53	522.95	01/2011 -	-
	Total		309.46 -	553.53	522.95		
	COAL						
	Mahanadi Coal Fields Limited						
3	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]	1/2005	302.96 -	302.96	334.77	03/2010 -	03/2018
4	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]	12/2007	457.77 -	457.77	565.86	03/2013 -	03/2019
5	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	219.29	03/2012 -	03/2020
6	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	260.71	03/2010 -	03/2019
	Neyveli Lignite Corporation						
7	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	5/2016	687.28 -	767.00	756.08	06/2017 12/2017	04/2018
	Northern Coal Fields Limited						
8	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	410.19	03/2012 -	03/2018
	Total		2,086.77 -	2,393.66	2,546.90		
	HEAVY INDUSTRY						
	Natrip Implementation Society						
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	4/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	-
	Total		1,718.00 -	3,827.30	2,289.00		
	PETROLEUM						
	Indian Strategic Petroleum Reserves Ltd						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs.150 Crore and above						(March 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	<u>Oil India Limited</u>						
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	1,200.00	961.00	03/2015 -	11/2017
	Total		1,864.35 -	2,893.00	2,510.85		
	POWER						
	<u>National Hydro-Electric Power Corporation</u>						
12	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	8,398.75	6,684.84	09/2009 -	12/2020
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	17,435.15	9,979.37	09/2010 -	-
	<u>National Thermal Power Corporation</u>						
14	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,521.00	03/2013 12/2020	12/2020
15	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	16,934.65	15,364.00	01/2017 03/2018	03/2018
16	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	1/2007	5,353.00 -	7,998.00	6,974.42	05/2014 03/2017	02/2019
	<u>North East Electric Power Corporation</u>						
17	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,424.41	12/2009 10/2018	10/2018
18	TRIPURA GAS BASED POWER PROJECT - [N18000071]	7/2009	421.01 -	1,078.31	963.23	07/2013 -	-
19	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,621.16	08/2013 04/2018	04/2018
	<u>Satluj Jal Vidyut Nigam Limited</u>						
20	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	602.44	485.63	12/2016 -	12/2018
	Total		37,631.17 -	63,811.32	52,018.06		
	RAILWAYS						
	<u>Central Railways</u>						
21	AMRAVATI-NARKHER NL(CR) - [220100118]	6/1994	663.01 175.30	858.97	707.51	06/1999 -	-
	<u>East Central Railways</u>						
22	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	4/1996	332.92 283.95	477.88	495.40	03/2012 -	-
23	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	559.91	538.21	07/2014 -	-
24	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs.150 Crore and above						(March 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
25	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	4/1997	162.87 -	541.00	183.72	- -	-
	<u>East Coast Railway</u>						
26	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	470.21 -	3,004.90	1,004.23	- -	06/2021
27	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	162.11	- -	03/2020
28	SAKRI-HASANPUR ROAD (NL) - [N22000171]	4/1999	175.69 -	325.00	253.10	- -	-
29	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	226.35	03/2015 07/2015	07/2015
	<u>Eastern Railways</u>						
30	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	4/2000	607.09 -	973.33	613.71	12/2012 12/2012	-
31	TINPAHAR - SAHIBGANJ (ER) - [N22000115]	4/2008	167.73 -	167.73	207.11	03/2012 -	-
32	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	4/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020
33	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]	4/1999	207.52 -	334.87	293.47	12/2012 -	-
34	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR- KATWA GC - [N22000245]	4/2010	423.66 -	720.59	456.58	03/2017 -	-
	<u>Metropolitan Rapid Transport Projects</u>						
35	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-
	<u>North Central Railway</u>						
36	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	4/1986	158.77 274.56	634.48	629.43	03/1994 -	-
37	ETAWAH-MAINPURI (NL),NCR - [220100318]	4/1997	120.00 -	245.39	210.67	12/2008 -	-
38	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	4/1999	108.00 -	432.72	446.52	12/2009 -	-
	<u>North East Frontier Railway</u>						
39	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	9/2001	492.98 -	1,320.00	921.03	12/2010 -	-
40	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	813.34 -	3,451.00	2,589.60	03/2014 -	03/2020
41	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	312.12 -	535.00	569.93	- -	03/2019
42	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	523.17 -	1,871.00	1,081.98	- -	03/2018
43	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	450.00	361.54	- -	03/2019
44	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	4/2011	209.77 -	630.00	620.04	- -	03/2018
45	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	4/1999	895.00 -	1,857.00	1,529.91	03/2007 -	04/2016

List of Projects in which Expenditure is More than Approved Cost

Costing Rs.150 Crore and above						(March 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
46	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	9/2006	300.00 -	2,135.00	922.41	- -	03/2020
47	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	200.00 -	780.00	466.47	- -	03/2020
48	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	619.34 -	4,600.00	1,951.73	04/2014 -	03/2020
49	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	9/1997	1,500.00 -	5,450.00	5,040.11	04/2008 12/2011	06/2018
50	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	727.56 -	9,658.00	7,387.18	03/2011 -	03/2020
51	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	4/2000	733.00 -	3,040.00	2,879.89	12/2008 -	03/2019
North Eastern Railway							
52	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	4/2003	218.19 -	412.05	350.14	- -	06/2018
53	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	718.54	272.98	- -	05/2019
54	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	3/2012	199.75 -	227.00	241.05	- -	08/2018
55	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	3/2008	195.64 -	474.30	430.32	- -	03/2018
56	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	4/1999	744.71 -	1,126.79	761.70	- -	-
North Western Railway							
57	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	895.00	694.56	03/2014 -	06/2019
Northern Railway							
58	JIND-SONEPAT (NL),NR - [220100280]	1/2004	238.56 -	740.00	722.65	03/2012 -	-
59	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,100.00	484.14	07/2012 -	-
60	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	27,946.00	16,131.46	11/2002 -	12/2018
61	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	3/2002	625.30 408.76	876.10	841.57	06/2007 -	-
62	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,581.53	618.19	03/2010 -	-
Rail Vikas Nigam Ltd.							
63	HARIDASPUR-PARADEEP(NL) - [220100285]	4/1996	301.64 -	1,185.99	1,130.35	- 09/2009	03/2019
64	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	343.00	364.71	03/2009 03/2009	12/2017
65	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	1,202.07	523.88	02/2015 -	12/2019
66	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	3/1997	261.70 -	388.00	360.26	02/2006 -	12/2019
67	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	9/2007	687.20 -	1,030.00	1,029.45	03/2010 -	03/2018

List of Projects in which Expenditure is More than Approved Cost

Costing Rs.150 Crore and above						(March 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
68	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	7/2006	743.00 -	1,825.00	1,667.23	03/2008 06/2008	03/2020
69	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	4/2008	822.39 -	1,810.00	1,711.51	- -	03/2018
70	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	4/2011	190.10 -	350.00	320.41	- -	03/2018
71	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	9/2006	324.90 -	555.00	517.35	03/2010 -	12/2017
72	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	4/1995	304.00 -	1,141.70	560.21	12/2012 -	-
<u>South Central Railway</u>							
73	GADWAL - RAICHUR (NL), SCR - [220100270]	4/1998	92.63 -	350.00	320.46	02/2011 -	-
74	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	3/1996	155.74 164.36	966.43	975.05	02/2009 -	-
75	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	1,013.26	- -	-
76	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	4/1997	218.24 236.41	525.00	687.24	- -	03/2019
77	JAGGAYYAPET - MELLACHERUVU - [N22000304]	4/2007	313.24 -	607.70	568.60	01/1999 -	-
<u>South East Central Railway</u>							
78	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019
<u>South Eastern Railway</u>							
79	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	583.00	436.96	12/2015 -	-
<u>South Western Railway</u>							
80	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	4/2007	179.65 -	1,350.91	832.60	- -	-
<u>Southern Railway</u>							
81	CALICUT-MANGALORE (DL) (SR) - [220100151]	2/1996	240.00 -	579.37	537.30	- -	-
82	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	9/2007	404.19 -	2,072.50	1,048.37	- -	-
83	CHENGANNUR-CHINGAVANAM - [N22000203]	4/2006	191.72 -	342.85	378.76	- -	-
84	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	4/1998	271.24 -	520.00	468.18	- -	-
85	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	9/2006	343.17 -	1,065.00	1,049.68	- -	-
86	KARUR-SALEM(NL),SR - [220100191]	2/1997	155.55 -	920.00	856.94	- -	-
87	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	3/1998	280.00 -	1,122.00	834.61	- -	-
<u>West Central Railway</u>							
88	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023

List of Projects in which Expenditure is More than Approved Cost

Costing Rs.150 Crore and above						(March 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Western Railway</u>						
89	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	4/2006	117.36 196.95	203.00	202.29	03/2011 -	-
	Total		28,674.35 -	1,18,116.83	80,036.92		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
90	TALEGAON-AMRAVATI - [N24000140]	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-
91	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,091.65	03/2013 -	12/2017
92	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	1,375.60	09/2016 -	06/2018
93	NAGPUR - KONDHALI - [N24000472]	9/2005	168.00 -	168.00	279.92	06/2006 -	-
94	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,479.56	07/2017 -	01/2018
95	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	796.52	03/2018 -	03/2018
96	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	814.19	03/2018 -	03/2018
97	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	495.78	566.34	01/2016 -	11/2017
98	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	351.34	409.92	01/2016 -	11/2017
99	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017
100	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	347.49	01/2014 -	12/2017
101	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,811.29	09/2014 -	12/2017
102	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	761.19	07/2008 -	-
103	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	1,665.00	2,313.68	- -	12/2017
104	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]	4/2010	1,170.52 -	1,170.52	2,263.02	06/2012 -	03/2018
105	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	2,881.81	01/2018 -	01/2018
106	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,952.35	08/2013 -	03/2018
107	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,436.15	08/2013 -	12/2017
108	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,167.15	03/2013 -	11/2017

List of Projects in which Expenditure is More than Approved Cost

Costing Rs.150 Crore and above						(March 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
109	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.52	10/2013 -	12/2018
110	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018
111	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,986.56	08/2013 -	08/2017
112	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-
113	MURADABAD-BAREILY - [N24000154]	4/2010	1,267.00 -	1,267.00	2,667.96	06/2013 -	09/2017
114	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018
	Total		26,172.09 -	26,172.09	39,999.84		
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
115	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	255.00	255.02	06/2017 -	-
116	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	275.98	275.98	12/2017 03/2018	-
	Total		443.44 -	530.98	531.00		
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
117	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
118	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	175.94	178.65	12/2015 -	-
	<u>Steel Authority Of India Limited (Sail)</u>						
119	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	8/2010	17,265.00 -	17,265.00	18,549.96	03/2013 -	06/2018
	Total		18,183.61 -	18,554.28	19,814.25		
	<u>URBAN DEVELOPMENT</u>						
	<u>Chennai Metro Rail Ltd</u>						
120	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	19,058.00	14,784.59	12/2015 -	-
	Total		14,600.00 -	19,058.00	14,784.59		
	Grand Total		1,43,142.24	2,67,369.99	2,26,608.36		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	PETROLEUM						
	Gas Authority Of India Limited						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	142.49	12/2019 12/2020	12/2019
	Hindustan Petroleum Corporation Limited						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00	4,199.00	194.97	03/2020 -	07/2019
	Indian Oil Corporation Limited						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	76.00	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	130.07	02/2019 -	12/2018
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	240.69	12/2020 -	02/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	125.91	05/2019 -	12/2018
	Total		10,668.92 -	10,668.92	910.13		
	POWER						
	Power Grid Corporation Of India Limited						
7	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	111.50	07/2018 -	03/2018
	Total		207.88 -	207.88	111.50		
	RAILWAYS						
	East Coast Railway						
8	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	148.59	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	148.59		
	ROAD TRANSPORT AND HIGHWAYS						
	National Highways Authority Of India						
9	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	195.03	07/2018 -	06/2018
10	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	86.42	03/2020 -	05/2019
11	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2018
	Total		2,251.26 -	2,341.00	281.45		

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		14,300.98	14,390.72	1,451.67		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	COAL						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	223.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	293.94	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.26	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	374.32	03/2021 -	03/2021
6	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	105.89	03/2019 -	03/2019
7	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.70	03/2026 -	03/2026
8	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
9	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	32.84	03/2019 -	03/2019
	<u>Neyveli Lignite Corporation</u>						
10	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,493.82	11/2021 -	11/2021
11	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	6.22	09/2019 -	09/2019
12	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	168.58	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
13	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	447.32	03/2018 -	03/2018
14	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	77.75	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
15	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
16	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	78.04	03/2019 -	03/2019
	<u>South-Eastern Coal Fields Limited</u>						
17	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
18	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	44.19	03/2020 -	03/2020
19	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	0.99	03/2023 -	03/2023
20	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
21	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,668.79	03/2023 -	03/2023
22	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.79	03/2023 -	03/2023
23	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	51.22	03/2020 -	03/2020
24	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	31.90	03/2022 -	03/2022
25	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
26	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
27	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.18	03/2023 -	03/2023
28	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
29	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,698.30	03/2023 -	03/2023
30	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.47	03/2021 -	03/2021
31	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	50.54	03/2018 -	03/2018
32	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	35.61	03/2021 -	03/2021
	Western Coal Fields Limited						
33	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
34	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	17.31	03/2021 -	03/2021
35	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	86.10	03/2023 02/2017	03/2023
36	GOKUL - [N06000120]	11/2014	267.67 -	267.67	206.04	03/2018 -	03/2018
37	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	77.21	03/2021 -	03/2021
38	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	139.76	03/2021 -	03/2021
39	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	0.04	03/2022 -	03/2022
40	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	51.12	03/2020 -	03/2020
41	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	96.81	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	178.26	03/2020 -	03/2020
43	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	87.11	03/2021 -	03/2021
44	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	383.42	03/2020 -	03/2020
45	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	239.83	03/2020 -	03/2020
46	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
47	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
48	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	15.30	03/2022 -	03/2022
49	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	0.13	03/2022 -	03/2022
50	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	126.93	03/2019 -	03/2019
51	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	232.10	03/2025 -	03/2025
	Total		66,658.54 -	66,926.41	10,987.36		
	DEFENCE PRODUCTION						
	Goa Shipyard Limited						
52	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	49.14	08/2020 -	08/2020
53	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	62.51	05/2018 -	05/2018
	Total		453.64 -	469.04	111.65		
	FERTILISERS						
	National Fertiliser Limited						
54	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	19.56	11/2019 -	11/2019
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	17.53	11/2019 -	11/2019
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	17.26	11/2019 -	11/2019
	Rashtriya Chemical & Fertiliser Limited						
57	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	1.32	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	55.67		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	HEALTH AND FAMILY WELFARE						
	Hospital Services Consultancy Corporation						
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	24.38	03/2019 -	03/2019
	Hospital Services Consultancy Corporation Ltd						
59	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	149.00	08/2018 -	08/2018
60	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	29.68	03/2019 -	03/2019
61	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	21.79	03/2019 -	03/2019
62	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	77.50	09/2018 -	09/2018
	Total		1,458.52 -	1,458.52	302.35		
	MINES						
	National Aluminum Company Limited (Nalco)						
63	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	290.88	01/2020 01/2020	01/2020
64	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	27.78	11/2020 11/2020	11/2020
65	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
66	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	89.75	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	408.41		
	PETROLEUM						
	Bharat Petroleum Corporation Limited						
67	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	40.41	01/2019 -	01/2019
68	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	281.45	04/2018 -	04/2018
69	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	93.74	08/2018 -	08/2018
70	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	118.35	02/2020 -	02/2020
71	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
72	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	66.77	02/2020 -	02/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
73	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	33.23	08/2020 -	08/2020
74	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	99.46	12/2019 -	12/2019
75	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	315.57	10/2018 -	10/2018
	Chennai Petroleum Corporation Limited						
76	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	186.78	12/2019 -	12/2019
77	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	1.31	08/2020 -	08/2020
	Gas Authority Of India Limited						
78	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	142.49	12/2019 12/2020	12/2019
79	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	40.20	12/2020 -	12/2020
80	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	71.07	12/2020 -	12/2020
81	PHULPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	1,961.00	12/2018 -	12/2018
82	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	11.79	07/2022 -	07/2022
83	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	48.24	04/2022 -	04/2022
84	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	606.89	02/2020 -	02/2020
85	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	9.30	12/2020 -	12/2020
86	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	213.63	12/2020 -	12/2020
87	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	154.37	03/2018 -	03/2018
88	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	750.00	534.34	12/2018 -	12/2018
	Hindustan Petroleum Corporation Limited						
89	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB, HARYANA) - [N16000242]	11/2016	230.00 -	230.00	48.37	02/2019 -	02/2019
90	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	-	11/2020 -	11/2020
91	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	95.26	09/2019 -	09/2019
92	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	570.10	06/2020 -	06/2020
93	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
94	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
95	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	9.75	03/2021 -	03/2021
	Indian Oil Corporation Limited						
96	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	336.86	10/2019 -	10/2019
97	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	597.50	09/2019 -	09/2019
98	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	2.12	12/2021 -	12/2021
99	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	133.17	01/2019 -	01/2019
100	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	100.02	09/2019 -	09/2019
101	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	14.08	04/2021 -	04/2021
102	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	41.00	09/2019 -	09/2019
103	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]	12/2017	466.43 -	466.43	1.18	10/2020 -	10/2020
104	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	112.81	08/2019 -	08/2019
105	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	0.08	01/2021 -	01/2021
106	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
107	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	93.11	12/2018 -	12/2018
108	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	529.80	11/2018 -	11/2018
109	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	0.05	01/2021 -	01/2021
110	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	-	08/2020 -	08/2020
111	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
112	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	0.13	06/2020 -	06/2020
113	ADDITIONAL FACILITIES AT VIJAYAWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
114	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	55.39	06/2020 -	06/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
115	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268	5/2016	348.00 -	348.00	0.05	01/2021 -	01/2021
116	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
117	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251	4/2016	1,021.00 -	1,021.00	5.73	12/2020 -	12/2020
118	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	1,330.00	1,200.16	06/2018 -	06/2018
119	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243	2/2016	2,582.00 -	2,582.00	480.79	11/2019 -	11/2019
120	SITARGANJ LPG PROJECT - [N16000282	2/2017	160.10 -	160.10	23.99	02/2020 -	02/2020
121	LPG BP PROJECT KHORDHA - [N16000283	12/2016	161.59 -	161.59	31.07	12/2019 -	12/2019
122	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284	9/2016	208.35 -	208.35	41.89	07/2020 -	07/2020
123	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
124	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	1,823.00	270.94	12/2020 -	12/2020
125	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249	5/2016	1,945.00 -	1,945.00	282.69	08/2021 -	08/2021
126	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
127	KHARAGPUR LPG BOTTLING PLANT - [N16000300	4/2017	163.02 -	163.02	28.93	04/2020 -	04/2020
	Mangalore Refinery And Petrochemicals Limited						
128	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256	10/2015	135.00 171.00	170.70	104.65	03/2019 -	03/2019
129	BSVI UPGRADEATION - [N16000257	9/2016	1,810.00 1,810.00	1,810.00	108.81	12/2019 -	12/2019
130	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255	5/2015	224.00 207.00	207.25	92.97	04/2019 -	04/2019
	Oil & Natural Gas Corporation Limited						
131	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	7/2016	249.85 250.00	244.70	24.69	05/2020 05/2020	05/2020
132	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297	2/2017	4,006.83 -	4,006.83	184.01	05/2021 -	05/2021
133	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280	4/2017	420.76 -	207.80	-	09/2018 09/2018	09/2018
134	REDEVELOPMENT OF SANTHAL FIELD - [N16000279	2/2017	1,162.56 -	1,162.56	230.90	03/2026 03/2026	03/2026
135	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290	1/2017	474.15 -	474.15	161.29	05/2019 05/2019	05/2019
136	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211	11/2014	195.63 -	187.10	168.01	09/2018 09/2018	09/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
137	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 11/2019	11/2019
138	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 11/2019	11/2019
139	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	1,526.01	04/2018 04/2018	04/2018
140	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 11/2019	11/2019
141	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	262.74	06/2020 06/2020	06/2020
	Oil India Limited						
142	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	7.30	12/2019 -	12/2019
143	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	1.58	10/2020 -	10/2020
	Total		1,30,709.35 -	1,29,734.22	13,870.82		
	POWER						
	National Thermal Power Corporation						
144	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	5,115.00	09/2019 -	09/2019
	Power Grid Corporation Of India Limited						
145	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
146	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	193.60	11/2018 -	11/2018
147	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.00	06/2019 -	06/2019
148	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	21.70	02/2019 -	02/2019
149	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	8.00	06/2019 -	06/2019
150	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	63.90	11/2018 -	11/2018
151	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	62.40	04/2019 -	04/2019
152	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	323.07	04/2020 -	04/2020
153	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	207.90	04/2019 -	04/2019
154	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	74.10	07/2018 -	07/2018
155	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	3,772.80	04/2018 -	04/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
156	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	1,313.70	11/2019 -	11/2019
157	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263	5/2017	445.89 -	445.89	81.90	02/2019 -	02/2019
158	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	8/2017	1,931.39 -	1,931.39	29.20	02/2020 -	02/2020
159	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262	5/2017	186.17 -	186.17	13.60	07/2019 -	07/2019
160	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261	5/2017	175.64 -	175.64	17.10	09/2018 -	09/2018
161	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257	12/2015	3,654.00 -	3,654.00	1,532.00	04/2019 -	04/2019
162	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	3/2017	3,500.00 3,500.00	3,500.00	151.00	07/2020 -	07/2020
163	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256	2/2015	1,750.00 -	1,750.00	867.00	06/2018 -	06/2018
164	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231	8/2016	431.89 -	431.89	81.90	02/2019 -	02/2019
165	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236	3/2017	251.60 -	251.60	12.00	06/2019 -	06/2019
166	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
167	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232	8/2016	177.52 -	177.52	45.50	02/2019 -	02/2019
168	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233	9/2016	562.25 -	562.25	18.60	03/2019 -	03/2019
169	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227	7/2016	1,429.38 -	1,429.38	353.90	01/2019 -	01/2019
170	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214	4/2016	454.11 -	454.11	198.70	04/2018 -	04/2018
171	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267	9/2017	198.49 -	198.49	-	09/2019 -	09/2019
172	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221	4/2016	287.99 -	287.99	99.50	06/2018 -	06/2018
173	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246	2/2017	204.12 -	204.12	10.30	09/2019 -	09/2019
174	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222	4/2016	790.13 -	790.30	368.70	06/2019 -	06/2019
175	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195	5/2015	780.33 -	780.33	147.50	10/2018 -	10/2018
176	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPF AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269	12/2017	193.14 -	193.14	-	06/2019 -	06/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
177	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	470.10	12/2018 -	12/2018
178	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
179	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	1,113.30	05/2019 -	05/2019
180	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	112.80	12/2018 -	12/2018
181	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	11.90	03/2019 -	03/2019
182	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	70.81	01/2019 -	01/2019
183	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	1,149.70	07/2018 -	07/2018
184	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	132.80	04/2019 -	04/2019
185	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.70	12/2019 -	12/2019
186	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	220.50	03/2019 -	03/2019
187	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	907.80	07/2018 -	07/2018
	Satluj Jal Vidyut Nigam Limited						
188	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	100.37	12/2021 -	12/2021
	Thdc India Limited						
189	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	40.16	09/2020 -	09/2020
	Total		70,403.71 -	71,682.23	19,548.22		
	RAILWAYS						
	Container Corporation Of India						
190	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	396.47	03/2018 -	03/2018
191	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	385.63	03/2018 -	03/2018
192	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	0.39	03/2019 -	03/2019
193	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	152.90	03/2018 -	03/2018
194	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	132.66	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
195	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	249.12	03/2019 -	03/2019
196	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	272.61	03/2019 -	03/2019
197	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	233.95	03/2019 -	03/2019
	East Central Railways						
198	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	166.13	03/2020 -	03/2020
199	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
200	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
	East Coast Railway						
201	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
202	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	65.98	03/2021 -	03/2021
203	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	117.43	03/2021 -	03/2021
	North Central Railway						
204	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
	North Eastern Railway						
205	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	52.27	03/2022 -	03/2022
	Rail India Technical And Economic Service						
206	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	Rail Vikas Nigam Ltd.						
207	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.92	95.72	12/2025 -	12/2025
208	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	45.50	12/2024 -	12/2024
209	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.30	797.44	12/2020 -	12/2020
210	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	730.03	03/2020 -	03/2020
211	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	769.00	03/2020 -	03/2020
212	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,388.35	03/2020 -	03/2020
213	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	850.22	03/2019 -	03/2019
214	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	863.23	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
215	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	120.70	12/2024 -	12/2024
216	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	752.76	12/2020 -	12/2020
217	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.16	12/2025 -	12/2025
218	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	16,216.00	761.30	12/2026 -	12/2026
	South Central Railway						
219	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	South East Central Railway						
220	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	737.72 -	737.72	104.10	12/2018 -	12/2018
221	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
	South Eastern Railway						
222	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.99	12/2021 -	12/2021
223	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	184.26	03/2021 -	03/2021
224	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	268.65	03/2020 -	03/2020
225	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	484.47	12/2021 -	12/2021
	West Central Railway						
226	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
227	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
228	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
	Total		44,948.54 -	58,686.20	10,794.58		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways						
229	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
231	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
232	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
	National Highways And Infrastructure Development Corporation Ltd.						
233	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742	3/2018	403.36 -	403.36	-	06/2018 -	06/2018
234	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741	3/2018	274.31 -	274.31	-	05/2018 -	05/2018
235	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743	3/2018	417.24 -	417.24	-	05/2018 -	05/2018
236	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748	2/2018	391.00 -	391.00	-	10/2018 -	10/2018
237	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
238	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
239	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
240	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
241	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
242	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
243	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
244	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
245	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
246	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
247	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
248	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
249	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
250	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
251	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
252	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744	3/2015	262.97 -	262.97	-	10/2018 -	10/2018
253	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749	3/2018	234.27 -	234.27	-	10/2018 -	10/2018
National Highways Authority Of India							
254	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
255	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	247.71	06/2018 -	06/2018
256	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
257	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
258	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
259	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
260	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
261	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651	2/2017	904.16 -	904.16	6.00	02/2020 -	02/2020
262	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	141.16	06/2018 -	06/2018
263	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
264	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	228.89	06/2018 -	06/2018
265	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
266	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	184.92	06/2018 -	06/2018
267	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
268	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	796.52	03/2018 -	03/2018
269	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	814.19	03/2018 -	03/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
270	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
271	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
272	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
273	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
274	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
275	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
276	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
277	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	590.82	03/2018 -	03/2018
278	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
279	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
280	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	699.98	03/2018 -	03/2018
281	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
282	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
283	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
284	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
285	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
286	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
287	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
288	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
289	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
290	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
291	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
292	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
293	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	23.48	03/2020 -	03/2020
National Highways Development Project							
294	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
295	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
296	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
	Total		49,630.08 -	50,200.26	4,235.03		
STEEL							
Hindustan Steelwork Construction Limited							
297	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
298	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
National Mineral Development Corporation (Nmcd)							
299	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	28.81	06/2020 -	06/2020
Steel Authority Of India Limited (Sail)							
300	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	177.21	03/2018 -	03/2018
301	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	38.95	06/2019 -	06/2019
	Total		1,706.06 -	1,706.06	465.03		
TELECOMMUNICATIONS							
Bharat Sanchar Nigam Limited							
302	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	169.45 -	169.45	-	08/2018 -	08/2018
303	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	167.68 -	167.68	-	04/2018 -	04/2018
304	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	159.30 -	159.30	-	04/2018 -	04/2018
305	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	212.70 -	212.70	-	05/2018 -	05/2018
306	GUJARAT ACCESS (LOT 1) - [N26000111]	9/2017	171.54 -	171.54	-	05/2018 -	05/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
307	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	215.30	-	05/2018 -	05/2018
	Total		1,095.97 -	1,095.97	.00		
	URBAN DEVELOPMENT						
	Central Public Works Department						
308	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]	1/2018	206.58 -	206.58	-	03/2019 -	03/2019
309	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	-	05/2020 -	05/2020
310	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	-	06/2019 -	06/2019
311	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	1.66	02/2020 -	02/2020
312	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	1.65	03/2020 -	03/2020
	Chennai Metro Rail Ltd						
313	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
	Lucknow Metro Rail Corporation Limited						
314	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	National Building Construcion Corporation Ltd						
315	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	3,245.00	11/2019 -	11/2019
	Total		16,051.29 -	15,905.29	5,785.08		
	Grand Total		3,91,128.98	4,05,877.48	66,564.20		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	ATOMIC ENERGY						
	Bhavini Limited						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00 -	09/2010 -	06/2018	74.69
	Total		3,492.00 -	6,100.00 -			
	CIVIL AVIATION						
	Airport Authority Of India Limited						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53 -	01/2011 -	-	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33 -	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86 -			
	COAL						
	Neyveli Lignite Corporation						
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00 -	06/2017 -	04/2018	11.60
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80 -	11/2021 -	11/2021	.00
	Northern Coal Fields Limited						
6	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57 -	03/2012 -	03/2018	87.58
	Singareni Colliers Company Limited						
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62 -	03/2012 -	03/2023	16.86
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86 -	03/2012 -	03/2019	80.24
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42 -	03/2019 -	03/2019	11.42
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28 -	03/2015 -	03/2020	114.60
	South-Eastern Coal Fields Limited						
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49 -	03/2015 -	03/2020	201.44
	Western Coal Fields Limited						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
12	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
	Total		19,751.90 -	21,090.72			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
13	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	3.16
14	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.53
	Total		453.64 -	469.04			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
16	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.38	05/2017 -	-	13.31
	Total		168.90 -	191.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
17	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
18	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33
	<u>Hindustan Petroleum Corporation Limited</u>						
19	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
20	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
21	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
22	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
23	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	06/2018	45.67
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
25	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	<u>Oil & Natural Gas Corporation Limited</u>						
26	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,725.50	04/2016 -	03/2018	38.82
27	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87
28	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
29	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	11/2018	45.83
30	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
31	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
32	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
	<u>Oil India Limited</u>						
33	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47
34	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64 -	256.41	12/2016 -	05/2018	12.15
35	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2017	37.72
	Total		29,189.20 -	36,281.45			
	POWER						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Damodar Valley Corporation</u>						
36	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	-	88.79
37	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	-	121.80
	<u>National Hydro-Electric Power Corporation</u>						
38	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28
39	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
	<u>National Thermal Power Corporation</u>						
40	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
41	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
42	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	06/2018	86.27
43	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
44	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
45	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41
46	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	02/2019	5.91
47	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65
48	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	03/2018	11.66
49	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
51	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
52	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	12/2016	7.41
	<u>North East Electric Power Corporation</u>						
53	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	10/2018	147.51
54	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	04/2018	133.06
55	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
56	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59
57	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2018	5.14
58	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65
59	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2018	36.79
60	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	12/2018	38.61
61	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	06/2019	5.34
62	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	09/2018	32.69
63	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	08/2014	288.49 -	376.09	02/2017 -	06/2018	30.37
64	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	09/2018	14.60
65	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	09/2018	26.82
66	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92
67	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	09/2018	36.01
68	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	09/2018	39.30
69	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2018	31.17
70	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	09/2018	79.61
71	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93
72	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	05/2018	36.74
73	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	06/2018	26.86
74	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
75	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
76	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42	9,141.97	12/2018	12/2019	92.28
77	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00	1,364.00	12/2015	06/2018	42.83
	Satluj Jal Vidyut Nigam Limited						
78	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68	602.44	12/2016	12/2018	37.96
	Thdc India Limited						
79	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42	294.60	02/2014	03/2019	50.75
80	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	3,789.61	06/2013	11/2020	52.10
81	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	4,401.90	02/2016	12/2020	165.65
	Total		1,79,131.74	2,46,470.12			
	RAILWAYS						
	Central Railways						
82	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30	3,168.29	-	03/2023	534.55
83	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70	792.89	-	03/2021	185.52
84	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06	199.12	-	03/2019	8.18
85	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85	540.02	-	03/2022	81.31
86	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68	2,271.50	-	03/2021	341.34
87	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01	858.97	06/1999	-	29.56
88	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00	5,341.68	-	03/2024	120.28
89	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00	3,438.51	-	03/2024	25.04
90	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00	1,272.19	-	03/2022	101.93
91	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00	2,449.91	-	03/2023	5.33
92	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00	2,081.27	-	03/2023	10.94
93	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00	1,035.16	-	03/2023	21.21

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	East Central Railways						
94	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
95	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
96	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
97	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
98	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
99	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
100	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
101	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
	East Coast Railway						
102	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	- -	12/2022	137.80
103	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
104	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
105	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	- -	03/2020	40.44
106	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	- -	03/2020	52.77
107	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
108	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
109	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
110	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
111	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
	Eastern Railways						
112	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
113	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
114	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
115	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
116	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
117	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
118	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
119	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
120	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
121	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
122	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
123	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
124	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
<u>Metropolitan Rapid Transport Projects</u>							
125	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
126	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
127	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	732.89	06/2013 -	03/2017	47.84
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
<u>North Central Railway</u>							
129	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
130	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
131	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
132	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
133	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
134	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	North East Frontier Railway						
135	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	03/2020	1,568.48
136	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
137	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
138	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
139	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
140	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2020	290.00
142	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	2,135.00	- -	03/2020	611.67
143	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
144	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
145	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	03/2020	27.24
146	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
147	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
148	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
149	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16
150	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00	- -	03/2018	200.33
151	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00	- -	03/2019	58.70
152	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
153	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	03/2020	94.45
154	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
155	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2020	171.38

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
156	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
157	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00	- -	03/2019	71.41
158	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
159	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	- -	03/2021	.00
160	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	- -	03/2020	10.01
<u>North Eastern Railway</u>							
161	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	- -	06/2018	88.85
162	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
163	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	- -	05/2019	212.37
164	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
165	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
166	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	- -	-	.33
167	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	- -	08/2018	10.26
168	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	- -	03/2018	142.44
169	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	227.00	- -	08/2018	13.64
170	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	- -	10/2018	61.80
171	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
<u>North Western Railway</u>							
172	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02
173	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	- -	02/2019	93.87
174	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	- -	03/2020	14.33
175	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84
176	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	- -	03/2019	41.64

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
177	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
178	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	- -	10/2018	24.47
179	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	- -	02/2019	14.35
180	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	- -	11/2018	19.86
181	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	- -	03/2019	44.16
	<u>Northern Railway</u>						
182	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
183	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
184	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
185	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
186	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
187	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
189	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
190	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
	<u>Rail Vikas Nigam Ltd.</u>						
191	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.99	- 09/2009	03/2019	293.18
192	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04
193	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	343.00	03/2009 03/2009	12/2017	157.10
194	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26
195	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88
196	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
197	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	03/2019	329.85
198	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
199	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00	1,141.70	12/2012	-	275.56
200	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90	555.00	03/2010	12/2017	70.82
201	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98	4,259.48	03/2016	12/2020	7.78
202	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322	04/2011	190.10	350.00	-	03/2018	84.11
203	AHMEDABAD-BOTAD (GC) - [N22000140	04/2012	567.18	975.62	-	03/2020	72.01
204	DHASA-JETALSAR (GC) - [N22000141	04/2012	376.59	644.38	-	12/2020	71.11
205	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,266.89	1,548.66	-	12/2020	22.24
206	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	04/2008	822.39	1,810.00	-	03/2018	120.09
207	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68	816.55	03/2016	12/2017	29.06
208	VIJAYAWADA-GUDUR - [N22000369	04/2015	3,246.26	3,548.67	-	-	9.32
209	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	750.55	750.56	12/2024	12/2024	.00
210	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01	977.00	03/2019	03/2019	5.39
211	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405	04/2015	1,765.90	1,765.92	12/2025	12/2025	.00
212	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	4,295.30	16,216.00	12/2026	12/2026	277.53
213	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	1,514.45	1,750.00	03/2020	03/2020	15.55
214	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	03/2012	1,183.25	1,183.30	12/2020	12/2020	.00
215	BINA - KOTA DOUBLING WITH RE - [N22000414	04/2011	1,485.65	1,485.85	12/2020	12/2020	.01
	Railway Electrification						
216	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10	275.08	03/2012	-	60.77
	South Central Railway						
217	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00	2,120.16	-	03/2021	542.47
218	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63	350.00	02/2011	-	277.85
219	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56	1,160.47	-	03/2022	206.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
220	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
221	GUDUR-DURGARA JAPATNAM - [N22000265]	04/2011	283.54 -	761.37	- -	-	168.52
222	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	1,313.48 -	2,288.70	- -	-	74.25
223	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	704.31	- -	-	108.69
224	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,050.00 -	2,132.77	- -	-	4.04
225	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	607.70	01/1999 -	-	94.00
226	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.43	02/2009 -	-	520.54
227	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
228	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	458.26	07/2008 -	-	266.61
229	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
230	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
South East Central Railway							
231	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
232	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
233	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88
South Eastern Railway							
234	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
235	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
236	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
237	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
238	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	583.02	06/2004 -	-	200.42
239	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
240	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
241	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
242	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
243	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
244	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
245	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	-	41.36
246	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
247	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
248	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
<u>South Western Railway</u>							
249	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
250	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
251	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
252	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
253	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
254	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
255	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
256	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
257	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
258	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
259	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
260	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
<u>Southern Railway</u>							
261	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
262	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	920.00	- -	-	491.45
263	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
264	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079	09/2007	404.19 -	2,072.50	- -	-	412.75
265	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	1,065.00	- -	-	210.34
266	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	2,300.00	- -	-	404.39
267	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	2,815.62	- -	-	411.93
268	ATTIPPATTU PUTTUR - [N22000184	04/2008	446.87 -	1,105.00	- -	-	147.28
269	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	2,350.00	- -	-	348.88
270	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
271	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188	04/1998	271.24 -	520.00	- -	-	91.71
272	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	346.15	- -	-	28.14
273	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	- -	-	295.05
274	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	-	173.71
275	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	342.85	- -	-	78.83
276	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	1,800.00	- -	-	199.29
277	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399	02/2015	900.00 -	4,131.90	- -	-	359.10
<u>West Central Railway</u>							
278	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	2,713.09	- -	03/2021	476.13
279	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
<u>Western Railway</u>							
280	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
281	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
282	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	04/2008	1,389.62	2,446.85	03/2014	-	76.08
283	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24	321.62	03/2012	03/2019	1.06
284	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88	844.10	-	-	91.89
285	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66	858.96	-	03/2019	167.87
286	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40	355.00	-	-	27.06
	Total		1,27,689.43	3,09,134.30			
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways						
287	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97	268.92	08/2015	-	3.84
288	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015	-	3.07
289	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016	-	.26
290	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018	04/2018	.11
291	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017	-	.04
292	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016	-	.06
293	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016	-	.02
294	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016	-	.30
	National Highways And Infrastructure Development Corporation Ltd.						
295	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017	01/2020	11.57
296	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00	447.37	10/2017	-	15.30
	National Highways Authority Of India						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
297	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2018	28.93
298	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75
299	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
300	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2018	68.99
301	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
302	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	04/2018	42.25
303	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
304	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
305	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
306	FOUR LANNING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
307	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
308	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
309	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
310	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
311	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
312	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
313	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
314	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
315	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
316	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
317	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2018	10.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
318	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
319	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
320	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39
	Public Works Dept Of State						
321	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
322	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
323	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
324	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
325	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24
326	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	31.78
327	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	-	10.82
328	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		24,613.28 -	31,456.93			
	SHIPPING AND PORTS						
	Kamarajar Port Limited						
329	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	255.00	06/2017 -	-	28.18
330	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88
331	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	321.94	04/2017 -	-	17.13
	Mumbai Port Trust						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
332	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
333	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		1,234.68 -	2,122.38			
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
334	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
335	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
336	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
337	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Rastriya Ispat Nigam Limited</u>						
338	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	Total		1,639.71 -	2,211.39			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
339	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	04/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
340	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	04/2018	44.75
341	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
342	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]	08/2014	350.02 -	479.87	03/2015 -	04/2018	37.10

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
343	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57
344	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	Chennai Metro Rail Ltd						
345	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	Total		17,021.00 -	22,244.19			
	Grand Total		4,20,259.34	7,07,467.50			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	ATOMIC ENERGY									
	Bhavini Limited									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,591.34	09/2010 09/2016	06/2018	93	74.68	Although all construction activities, total equipment erection & installation have been completed in PFBR, time schedules for first approach to criticality (FAC) followed by subsequent power operation got shifted initially from September 2014 to September 2016. This is primarily owing to augmentation of certain additional assessments & checks on the installed equipment prior to commencement of their commissioning, which have essentially emanated owing to both increased regulatory requirements and
	Nuclear Power Corporation Of India Limited									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	11,554.00	12/2015 11/2016	06/2020	54	0	. Equipment supply/erection delays by various vendors and contractors. . Various vendors / contractors facing cash flow / liquidity problems. . Teething troubles/learning experience being first pair of 700 MW indigenous reactors.
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,147.00	12/2016 03/2017	12/2020	48	0	. Equipment supply/erection delays by various vendors and contractors. . Delay in civil works by Main Plant civil contractor . Various vendors / contractors facing cash flow / liquidity problems
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	69,728.00	28,425.34					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	CIVIL AVIATION									
	Airport Authority Of India Limited									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	40.28	
	Total		314.61 -	441.33	26.44					
	COAL									
	Bharat Coking Coal Limited									
6	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	174.74	05/2014 -	04/2018	47	0	Implementation of Project delayed due to late of issue of 'Consent to Establishment
7	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	169.31	04/2014 -	04/2018	48	0	Implementation of Project delayed due to late settlement of land dispute i.e. on 18/08/2014 after the Issue of 'consent to establish' on 11/12/2012 and delay in implementing project by BOM Operator, M/s MIEL.
8	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	due to grant of EC clearance from MOEF work suspension by contractors on payment issue
9	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	280.30	04/2015 -	04/2019	48	0	Project implementation delayed by about 48 months mainly due to delay in acquisition of land for handing over the site.
	Central Coal Fields Limited									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	98.15	03/2012 -	03/2019	84	0	Mainly delayed due to acquisition of land,Forest land handover & completion of the Railway siding. Land Authentication.--Paper examination related to 63.546Ha completed. Decision on tenancy right is required from District Adm. Hazaribagh. Railway Siding-- DPR for construction of North Urimari Railway siding approved by East Central Railway.
11	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	154.03	03/2012 -	03/2019	84	0	delay in FC & forest land diversion.
12	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	350.19	03/2016 -	03/2019	36	0	completion is mainly delayed due to delay in possession of Non forest land as well as delay in permission for Forest land diversion.
13	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	60	0	Out of 122.62 Ha, authentication of 39.66 Ha land is completed in Karma village. Balance 82.96 Ha GM land in Karma & Sugia village is to be authenticated. For authentication of balance land matter is being pursued with CO Mandu for early authentication.
14	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	0	There was delay in FC, and handover of forest land of 312.76Ha. Stage II was granted on 12.10.2010 and the letter of site handover was issued on 29.03.2016 by DFO.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	125.99	07/2012 -	03/2021	104	0	Project is delayed mainly due to delay in construction of TORI-SHIVPUR Railway line upto Bukru. Construction of Railway line has been further delayed i.e. May 2018 upto Bukru and June 2018 upto Shivpur as per meeting held by MOC with railways on 19.04.2018. The Project will be able to achieve its rated capacity only after doubling of Tori-Shivpur Railway line. Tori balumath rail line section (19.3 KM) single line has been inaugurated on 9th March 2018.
	Eastern Coal Fields Limited									
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	343.50	03/2018 -	03/2020	24	0	Rehabilitation of PAFs- Process of P&P activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
	Mahanadi Coal Fields Limited									
17	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	334.77	03/2010 -	03/2018	96	0	Coal Evacuation Problem. Delay in completion of Jharsuguda – Barpali - Sardega Railway line by S.E. Railway.
18	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	565.86	03/2013 -	03/2019	72	0	delay in diversion of forest land
19	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	260.71	03/2010 -	03/2019	108	0	
20	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	242.14	03/2013 -	03/2019	72	0	
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	313.25	03/2017 -	03/2020	36	0	
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	219.29	03/2012 -	03/2020	96	0	
	Neyveli Lignite Corporation									
23	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	5,229.45	12/2015 04/2018	04/2018	28	0	delay in sequential supply of Materials by the package contractors, M/s BHEL & M/s EPIL

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
24	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU	05/2016	687.28 -	767.00	756.08	06/2017 12/2017	04/2018	10	11.6	The milestones could not be achieved due to delay in submission of Drawings and approval, due to delay in supply of equipment and delay in mobilization and erection by the package contractors - M/s Jakson Engineers Ltd., Noida and M/s BHEL.
25	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	709.06	349.99	06/2015 09/2019	09/2019	51	-51.37	Though the project was sanctioned on 30.04.2013 (Zero Date), Environment clearance for the project was obtained only on 02.09.2015. Accordingly, the milestones were re-scheduled.
	<u>Northern Coal Fields Limited</u>									
26	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	486.57	410.19	03/2012 -	03/2018	72	87.58	
	<u>Singareni Colliers Company Limited</u>									
27	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	154.52	03/2015 -	03/2018	36	0	Delay due to forest land diversion.
28	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72	0	Delay due to forest land diversion.
29	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	125.24	06/2015 -	03/2018	33	0	Delay due to diversion of Jallaram vagu.
30	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	186.19	03/2012 -	03/2019	84	80.24	Thickness of seam where LW was envisaged, is having inconsistent thickness and geologically disturbed.
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	154.69	03/2016 -	03/2019	36	-3.5	
32	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
33	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	.37	03/2015 -	03/2020	60	-32.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
34	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60	114.6	Delay due to acquisition of private land and strong opposition from villagers towards upcoming opencast project.
35	KALYANIKHANI OPENCAS T PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	137.69	07/2016 -	03/2020	44	0	Delay due to acquisition of non-forest land.
36	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	316.06	03/2015 -	03/2021	72	-2.14	Delay due to diversion of forest land and acquisition of non-forest land.
37	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	48.57	03/2012 -	03/2023	132	16.86	Delay due to Land acquisition and diversion of L-6 canal.
	South-Eastern Coal Fields Limited									
38	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	0	Project delayed due delay in availability of Consent To Operate (CTO) for 1.5 MTY coal production and issue of Stage II FC for 166.92 Ha forest land)
39	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	153.81	03/2016 -	03/2019	36	0	delay in possession of land
40	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	137.98	03/2015 03/2020	03/2020	60	201.44	
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	Land issues
42	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	200.64	03/2014 -	03/2020	72	0	delay in obtaining EC, delay in obtaining permission for forest land
	Total		20,254.10 -	20,473.06	12,519.68					
	FERTILISERS									
	Rashtriya Chemical & Fertiliser Limited									
43	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA	02/2016	482.85 482.85	482.85	413.01	12/2017 04/2018	04/2018	4	0	
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	106.14	11/2016 04/2019	04/2019	29	5.89	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		680.64 -	692.29	519.15					
	STEEL									
	Hindustan Steelwork Construction Limited									
45	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	0	Awaiting for approval for the cost
46	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	0	the concept plan and DPR is under the process of approval by the department of Medical education
47	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	Delay in the clearance by the central government. The plan is under approval process
48	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	Awaiting for approval for cost
49	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	the matter of funding for the project and administrative mechanism are still pending
	National Mineral Development Corporation (Nmhc)									
50	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	13,876.24	05/2015 10/2018	10/2018	41	0	
	Rastriya Ispat Nigam Limited									
51	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]JINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	124.00	07/2018 -	09/2018	2	0	No
52	COKE OVEN BATTERY-5 - [N12000117]JINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	827.45	12/2017 -	10/2018	10	-12.53	No
53	CENTRAL DISPATCH YARD - [N12000119]JINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	37.80	08/2018 -	10/2018	2	0	No

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
54	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	276.10	09/2018 -	01/2019	4	0	No
55	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	237.11	10/2016 -	03/2019	29	42.39	No
	Steel Authority Of India Limited (SAIL)									
56	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,549.96	03/2013 -	06/2018	63	0	
57	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	659.52	12/2017 -	11/2018	11	0	
58	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	216.70	10/2017 -	12/2018	14	0	Slow submission of design Engineering drawing by the contractor
59	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,089.04	04/2018 -	02/2019	10	0	envioronmental clearance awaited
	Total		46,113.39 -	45,900.79	38,031.55					
	PETROLEUM									
	Bharat Petroleum Corporation Limited									
60	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	1,290.71	08/2018 05/2019	05/2019	9	14.33	
	Chennai Petroleum Corporation Limited									
61	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	202.35	11/2016 -	06/2018	19	0	Reason of Delay Delay due to poor response to purchase & works tender, leading to repeated extension of bid submission dates including revision of PQC for works tender. Import restriction of pipes due to revision in Govt. guidelines.
	Gas Authority Of India Limited									
62	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	80.23	04/2018 -	07/2018	3	-38.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
63	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	2,915.00	1,645.33	12/2012 02/2019	02/2019	74	0	
	<u>Hindustan Petroleum Corporation Limited</u>									
64	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	492.24	10/2014 03/2018	02/2019	52	133.5	Reasons for Time and Cost Overrun -Delay in getting Forest approval.
	<u>Indian Oil Corporation Limited</u>									
65	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 4,190.00	4,190.00	2,548.03	09/2017 06/2018	06/2018	9	36.22	
66	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	1,817.34	09/2017 12/2018	12/2018	15	0	
67	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	325.27	10/2017 -	03/2019	17	17.66	Delay due to local agitation.
68	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	135.02	07/2018 10/2020	10/2020	27	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
69	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 5,725.50	5,725.50	5,130.40	04/2016 03/2018	03/2018	23	38.82	Reasons of Delay: Intrruption of Site works by villagers .
70	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	2,041.21	05/2014 05/2018	05/2018	48	0	Delay is due to slow work and also due to contractor having financial issues.
71	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	5,558.19	05/2017 05/2018	05/2018	12	1.87	
72	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,504.61	1,317.83	05/2017 05/2018	05/2018	12	-13.63	
73	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 181.02	181.02	168.93	01/2017 05/2018	05/2018	16	0	Delay in Procurement by contractor.
74	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 202.25	160.16	118.02	07/2016 06/2018	06/2018	23	-20.81	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
75	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	2,073.06	03/2013 09/2018	09/2018	66	-3.5	Reasons for Delay: -Substantial time taken for mobilization by survey and other agency. -ROU acquisition and issue related to payment -Delay in forest clearance. -Inadequate manpower at working sites affected the construction progress. -Local problem and court cases by tea gardener. -Slow progress in engineering and procurement.
76	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,188.94	05/2013 03/2018	11/2018	66	45.83	Reasons of Delay: Increase in scope of work post-award of contract due to legs of Sagar Samrat failing in in-place analysis as per ABS Guidelines necessitating replacement of all the 4 legs. $\therefore$ Delay in procurement of steel and fabrication of legs by the contractor. $\therefore$ Slow progress in fabrication
77	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 4,619.94	3,961.54	3,816.11	12/2017 03/2019	03/2019	15	-14.25	
78	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	95.40	03/2019 -	04/2019	1	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
79	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	571.47	542.96	09/2011 06/2019	06/2019	93	-22.42	Reasons for delay : -Delay in preparation of drawing and additional model testing of Hull form in Austria . - Shortage of skilled manpower at contractor's end. - Inadequate ancillary/sub-contractors at the location -Lack of planning to match resources to work targets. - Change in delivery location. -Delay in procurement of steel by PSL. -Delay in take over of Pipavav defence co. by Reliance group.
80	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	2,765.06	05/2019 10/2019	10/2019	5	-4.01	
81	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	13.34	01/2014 11/2019	11/2019	70	62.78	Reasons of Delay: Due to poor progress, contract terminated. Project is under tendering. Termination of contract once due to poor performance of the contractor. Cancellation of tendering process twice: Once submitted bids not Techno-Commercially acceptable & once quoted price of L-1 bidder too high. -Slow progress in engineering and procurement resulting in termination of contract. -Formulation of revised execution methodology for fresh tender and execution.
82	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,729.04	03/2015 03/2018	12/2019	57	29.42	Delay in conversion of Rig Sagar Laxmi to MOPU due to financial issues and non-performance of the contractor.
83	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	1,027.52	03/2019 05/2020	05/2020	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Oil India Limited									
84	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	256.41	147.21	12/2016 -	05/2018	17	12.15	
85	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	438.84	146.36	03/2017 -	11/2018	20	24.47	Reasons of Delay -land litigation -Original plan for construction at Naoholia had to be changed because site came under dispute/sub-judice. -Original EPMC contract lapsed.
86	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM	07/2011	350.00 -	350.00	1.03	01/2019 -	09/2019	8	0	
	Total		52,800.78 -	56,324.77	36,417.13					
	POWER									
	Chenab Valley Power Projects [P] Limited									
87	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	895.22	04/2020 -	10/2023	42	0	Flash flood, Contractual dispute
	National Hydro-Electric Power Corporation									
88	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,684.84	09/2009 -	12/2020	135	114.28	Cash Crunch, Slow progress of TBM
	National Thermal Power Corporation									
89	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 03/2018	03/2018	14	11.66	Agitation, delay in supply of generator
90	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 8,150.00	8,150.00	7,057.00	09/2011 06/2018	06/2018	81	86.27	Inadequate deployment of man power
91	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	7,998.00	6,974.42	05/2014 03/2017	02/2019	57	49.41	
92	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	02/2019	13	5.91	
93	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
94	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,488.00	11/2016 03/2019	03/2019	28	0	delay in Engg and BGR
95	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH	12/2012	11,846.00 -	12,739.82	9,555.00	06/2017 06/2019	06/2019	24	7.55	Delay in supplies of Generator Transformer
96	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC, MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	8,980.00	09/2017 06/2019	06/2019	21	10.55	Agitation of villagers
97	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC, ODISHA	02/2014	12,532.44 -	13,740.53	7,588.00	08/2018 06/2019	06/2019	10	9.64	Aquisition of balance land
98	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	4,333.00	03/2019 09/2019	09/2019	6	0	Delay in physical possession of land
99	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND	02/2014	14,366.58 -	15,164.05	6,924.00	02/2019 10/2020	10/2020	20	5.55	Delay in award of critical packages (Like ACC) by BHEL
100	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC, TELANGANA	01/2016	10,598.98 -	10,598.98	1,849.00	07/2020 10/2020	10/2020	3	0	
101	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,521.00	03/2013 12/2020	12/2020	93	29.14	Flash Flood
102	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00 -	3,004.00	1,075.69	11/2019 -	12/2020	13	0	
103	BARH STPP (3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	14,520.00	01/2011 04/2021	04/2021	123	73.65	Non Performance of Russian Agency M/s TPE and M/s PM
104	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	322.00	09/2019 02/2022	02/2022	29	0	delay in agreement in Power Purchase
	North East Electric Power Corporation									
105	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH	12/2008	573.99 1,337.76	1,337.76	1,621.16	08/2013 04/2018	04/2018	56	133.06	Flash flood, frequent law and order problem, bad road condition
106	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	6,424.41	12/2009 10/2018	10/2018	106	147.51	contractual problems, Land slide, flash flood, poor geological condition
	Power Grid Corporation Of India Limited									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
107	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,783.00	11/2017 -	04/2018	5	0	
108	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	2,225.00	1,346.00	01/2018 -	04/2018	3	0	
109	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	598.00	06/2015 05/2018	05/2018	35	36.74	765KV Bay commissioned in Jan'17 matching with associated line. ICT's ready. Commissioning matching with Srikakulam – Garivadi line (under TBCB route).
110	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	848.40	04/2017 03/2018	05/2018	13	0	All element completed except both ICTs at Tirunelveli Sub station.
111	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,617.80	12/2012 06/2018	06/2018	66	36.79	Implementation of balance lines affected due to local disturbances & geographical constraints. 01 line in Arunachal Pradesh (Tezu-Namsai line) affected due to compensation issues & land ownership disputes and further their commissioning linked to readiness of down stream system (being implemented under NER comprehensive scheme). Mizoram (Silcher-Melriat line) is affected due to tree cutting. Issue getting resolved with support of state/Distt. Admn.
112	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	137.93	09/2014 09/2017	06/2018	45	0	
113	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 3,190.27	3,190.27	2,178.75	12/2015 06/2018	06/2018	30	26.86	Generation project delayed/uncertain. Implementation also affected due to severe ROW problem mostly at Angul end & huge forest involvement. Working permission for Chattisgarh portion issued in Nov'17.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	156.50	04/2016 12/2017	06/2018	26	0	Substation PMUs has been supplied for which installation is under progress. PDC in control centre has been commissioned for WRDLC, GETCO, MPPTCL, Chattisgarh, Kamataka and Tamilnadu, Kerala, Delhi, HP, Punjab, UP & Rajasthan.
115	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	234.30	02/2017 06/2018	06/2018	16	30.37	08 out of 13 elements completed. Implementation affected due to delay in Transformer supply (failure in testing). Transformer supply out sourced, mfg./supply under progress.
116	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	64.90	03/2018 -	06/2018	3	0	
117	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,125.00	12/2015 -	06/2018	30	42.83	
118	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,000.25	11/2008 09/2018	09/2018	118	22.93	Implementation of balance 01 line (Edamon-Muvattupuzha line) is affected due to severe ROW problem (long pending). Problem being addressed progressively as per latest Revised G.O. of 30.07.15 (compensation to be done on land value, to be finalised by concerned DC with the support of State Govt.). Site is getting police protection as per requirement from State admn. Work affected due to non-availability of aggregate. Matter has been taken up Secy. level.
119	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,440.03	11/2012 09/2018	09/2018	70	36.01	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
120	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,420.46	09/2014 09/2018	09/2018	48	39.3	02 out of 03 line completed. Balance line affected due to severe ROW problem being faced in Karnataka on Salem PS – Madhugiri line. Obstruction are being removed progressively with the help of Police protection.
121	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 534.02	534.02	386.87	08/2014 09/2018	09/2018	49	79.61	Implementation affected due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Compensation order issued by State in line with Govt. guidance. Work under progress with the help of Police protection.
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	400.50	06/2016 09/2018	09/2018	27	0	01 out of 02 completed. Implementation affected due to severe ROW problem at singrauli end. Work also affected due to poor performance by executing agency, being expedited with support from Powergrid.
123	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	143.20	03/2016 09/2018	09/2018	30	32.69	Implementation of balance affected due to delay in equipment supply(Off-shore) & non-readiness of down stream line by State Govt. at Hamirpur.
124	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	143.00	02/2016 09/2018	09/2018	31	14.6	
125	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	190.10	03/2018 09/2018	09/2018	6	26.82	01 out of 02 line completed. Work badly affected due to disturbance in Kashmir and delay in finalisation of compensation by PNC. To resolve compensation issue matter taken up with State Govt. State/MoP help required. All efforts being made to complete earlier.
126	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	547.00	09/2017 09/2018	09/2018	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
127	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,392.90	04/2018 09/2018	09/2018	5	0	01 out of 03 line completed. Implementation affected due to forest clearance (awaited). Work slowed-down to the extent possible to match Generation.
128	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	171.50	03/2017 09/2018	09/2018	18	0	Completion matching with Generation.
129	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,223.54	09/2017 -	09/2018	12	30.49	Khalsti & Leh S/Stn. and 220LV Leh – Khalsti line were charged on 31 Oct'17. Implementation affected due to delay in land acquisition of Kargil S/s. Land handed over by DM in Dec'16. ROW clearance of 06 locs. to be expedited. Increased BE-18-19 allocation from 500 Cr. to 883 Cr. Required.
130	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	179.10	11/2017 10/2018	10/2018	11	0	Generation project ant. in March 2020. Work slowed-down to extent possible to match the generation. Forest clearance also awaited.
131	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	660.59	09/2010 12/2018	12/2018	99	54.59	02/03 line line completed). Balance portion (02 Kms) of line being executed using under ground cable. Work affected due to water logging. Severe ROW problem being encountered at Navi Mumbai end, miscreants have burnt and damaged part of laid cable. Matter critical. Commissioning linked to availability of State down stream system at Navi Mumbai . Critical.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
132	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,514.68	10/2012 12/2018	12/2018	74	5.14	8 out of 9 lines completed progressively by Dec'16). Balance 400kV Wardha – Aurangabad (on 1200KV tower) affected due to delay in implementation arising out of complexities involved (1200KV tower) & poor performance by executing agency necessitating termination & re-awarding fresh contracts. Work under progress after re-award. Severe ROW problem being encountered.
133	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	487.82	06/2014 12/2018	12/2018	54	31.17	01 out of 02 line completed. Balance 400KV Madugiri-Yelhanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the existing contractor has expressed inability to continue the balance work. Balance work re-award in Dec'17. Work under progress.
134	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,184.14	04/2016 12/2018	12/2018	32	38.61	Implementation affected due to severe ROW problem at Rajarhat end as well as in Jharkhand area. Work in Rajarhat S/stn. area almost standstill since last 9-10 months due to protest/agitation by locals who not allowing to enter in S/s. Work resumed in Oct'17 again stopped due to protest w.e.f 01.12.17. Matter being followed up at all levels for early resolution & efforts being made for resumption of work complete at the earliest.
135	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	1,979.40	03/2018 03/2019	03/2019	12	0	01 out of 03 element completed. Implementation affected due to delay in land acquisition & likely delay in off-shore supplies.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
136	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	272.70	01/2018 03/2019	03/2019	14	0	Implementation affected due to forest (Tiger reserve) clearance. Line passing through buffer zone of Tiger reserve area. Wildlife clearance proposal submitted. SBWL meeting yet to be held. Proposal forwarded to NBWL. Clearance awaited. Alternate arrangements made for evacuation (contingency through Punatsanghu ATS, ready). Generation project delayed (ant.by Nov'18).
137	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	394.40	11/2016 06/2019	06/2019	31	5.34	Implementation affected due to delay in supply of transformers due to testing issues and other transportation constraints.
138	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	178.70	07/2017 06/2019	06/2019	23	27.92	03 elements out of 04 elements complete. Project commissioned except Bus Reactor at Yelankha As per MoM of 40th SCSPSR held on 19.11.16. Procurement being taken up after resolution of ROW issue of LILO line at Yelahanka. Now, ROW issues for LILO resolved. Procurement process for Bus Reactor at Yelankha is under progress. NIT & OBD done, award under progress.
139	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	86.60	05/2017 06/2019	06/2019	25	0	Implementation affected due to delayed in land acquisition (land hand over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16). Rajghat sub station annulled. Additional bay at Maharanibagh in place of Rajghat S/stn. However, only 400KV line bays are being made at Maharanibagh. Award placed in Jan'18. Work under progress.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
140	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	160.59	10/2017 09/2019	09/2019	23	0	Gen. project delayed. Project re-scheduled due to match with Generation (now ant. by Sep'19).
141	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	668.80	12/2018 -	12/2019	12	92.28	33 packages out of 44 packages award. Balance award under progress). Award have been delayed due to poor response & high prices quoted by bidders. Out of 116 Sub stations land for only 56 nos land available. Non-availability of 22 nos. land for awarded Sub-station. Critical. Approval of new elements proposed by Govt. of Arunachal Pradesh
142	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	474.57	12/2018 -	12/2019	12	0	51 packages out of 55 packages award. Balance award under progress. Award have delayed due to poor response & high prices quoted by bidders. Increased BE 18-19 allocation from Rs. 282.5 Cr. to 1500 Cr. required.
143	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,639.60	08/2013 03/2022	03/2022	103	23.65	06/08 line completed. Balance lines (linked to Gen. Proj.) to be completed matching with Gen. Proj. Lower Subhansiri HEP is schedule uncertain. Works presently stand-still on a/c of local disturbance/ agitation against big dams.
	<u>Satluj Jal Vidyut Nigam Limited</u>									
144	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	200.08	11/2017 -	05/2018	6	0	
145	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	485.63	12/2016 -	12/2018	24	37.96	
	<u>Thdc India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
146	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	162.82	02/2014 02/2018	03/2019	61	50.75	IIInd stage forest clearance for Power Evacuation Arrangement.
147	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,789.61	1,393.67	06/2013 -	11/2020	89	52.1	Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Now the works at various fronts are in progress with intermittent hindrances by villagers. Regular support of Distt. Administration is required.
148	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,540.27	02/2016 09/2019	12/2020	58	165.65	Law and order problem: Dharna at Asena Crusher Plant since 10.02.18 is persistent till date, despite regular follow up with Distt. Administration
	Total		2,27,593.11 -	2,74,183.52	1,80,432.95					
	HEALTH AND FAMILY WELFARE									
	Hospital Services Consultancy Corporation Ltd									
149	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10	13.31	
150	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13	0	
151	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC, PUNJAB	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6	0	
152	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16	0	
153	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6	0	
154	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	21.00	05/2018 -	08/2019	15	0	
	Total		1,689.51 -	1,711.99	791.90					
	RAILWAYS									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	East Central Railways									
155	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12	0	
	East Coast Railway									
156	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	82.55	03/2021 -	03/2022	12	0	
157	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	43.73	03/2021 -	03/2022	12	0	
	Eastern Railways									
158	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	25.09	
	Metropolitan Rapid Transport Projects									
159	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	
160	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	50.68	
161	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	812.12	03/2004 -	03/2020	192	259.68	
	North Central Railway									
162	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	
163	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	226.23	
	North East Frontier Railway									
164	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,450.00	5,040.11	04/2008 12/2011	06/2018	122	263.33	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
165	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,040.00	2,879.89	12/2008 -	03/2019	123	314.73	Forest land aquisition
166	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	9,658.00	7,387.18	03/2011 -	03/2020	108	1227.45	frequently threatning and firing and kidnapping of site engineers. Poor condition of NH 37, Poor condition of rail bridge,
167	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	3,451.00	2,589.60	03/2014 -	03/2020	72	324.3	Land aquisition and clearance from supreme court in "In principle approval"
168	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 -	4,600.00	1,951.73	04/2014 -	03/2020	71	642.73	
169	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	204.95	
170	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	3,000.00	431.96	03/2015 -	03/2020	60	252.94	Local agitation and land compensation
North Western Railway										
171	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	895.00	694.56	03/2014 -	06/2019	63	37.02	
172	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,143.70	568.36	03/2015 -	12/2019	57	37.84	
Northern Railway										
173	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	27,946.00	16,131.46	11/2002 -	12/2018	193	1017.84	
Rail Vikas Nigam Ltd.										
174	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	1,030.00	1,029.45	03/2010 -	03/2018	96	49.88	
175	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	750.71	03/2016 -	12/2018	33	0	
176	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.07	523.88	02/2015 -	12/2019	58	556.04	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
177	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	388.00	360.26	02/2006 -	12/2019	166	48.26	
178	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,667.23	03/2008 06/2008	03/2020	144	145.63	
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,635.74	03/2016 -	12/2020	57	7.78	
	South East Central Railway									
180	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	359.96	
	West Central Railway									
181	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	Western Railway									
182	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	82.24	03/2012 -	03/2019	84	1.06	
183	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 416.86	385.60	343.13	03/2013 -	03/2020	84	-2.17	
	Total		39,411.20 -	1,10,498.39	52,629.65					
	ROAD TRANSPORT AND HIGHWAYS									
	Ministry Of Road Transport And Highways									
184	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-1.19	
	National Highways And Infrastructure Development Corporation Ltd.									
185	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
186	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	
187	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	
188	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	National Highways Authority Of India									
189	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112	80.68	
190	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 -	03/2018	117	0	
191	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	03/2018	119	0	
192	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	03/2018	104	68.99	
193	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76	106.5	
194	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	0	
195	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	0	
196	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42	0	
197	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,952.35	08/2013 -	03/2018	55	0	
198	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	564.39	07/2014 -	03/2018	44	0	
199	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	437.90	06/2014 -	03/2018	45	0	
200	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
201	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,263.02	06/2012 -	03/2018	69	0	
202	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	04/2018	96	42.25	
203	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	0	
204	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	0	
205	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	05/2018	111	28.93	
206	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	0	
207	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	1,375.60	09/2016 -	06/2018	21	0	
208	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	261.09	86.28	05/2017 -	06/2018	13	0	
209	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19	0	
210	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
211	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	383.55	06/2016 -	06/2018	24	0	
212	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	173.62	07/2016 -	07/2018	24	0	
213	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	1,387.11	769.28	11/2017 -	08/2018	9	0	
214	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	09/2018	118	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
215	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	293.12	09/2017 -	09/2018	12	0	
216	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	10/2018	114	0	
217	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	0	
218	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	0	
219	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	0	
220	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	0	
221	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12	0	
222	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,484.71	08/2016 -	02/2019	30	0	
223	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	0	
224	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	0	
225	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	0	
226	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	-	03/2020 -	05/2020	2	13.97	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(March 2018)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
227	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	67.09	03/2020 -	05/2020	2	44.39	
228	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	10.50	03/2020 -	06/2020	3	41.54	
	Public Works Dept Of State									
229	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	
	Total		33,499.34 -	36,060.12	14,492.21					
	SHIPPING AND PORTS									
	Kamarajar Port Limited									
230	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 257.90	257.90	1.45	12/2017 05/2020	05/2020	29	-57.02	
	Mumbai Port Trust									
231	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	413.91	12/2010 -	12/2018	96	82.72	Nil
	Total		966.39 -	927.36	415.36					
	TELECOMMUNICATIONS									
	Department Of Telecommunication									
232	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	7,642.00	07/2015 04/2020	04/2020	57	84.97	
	Mahanagar Telephone Nigam Limited									
233	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9	0	
	Total		13,752.26 -	25,082.26	7,814.30					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	URBAN DEVELOPMENT									
	Bangalore Metro Rail Corporation Limited									
234	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	
	Central Public Works Department									
235	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 -	03/2018	65	0	
236	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	307.50	03/2016 12/2017	04/2018	25	44.75	
237	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	452.35	03/2015 12/2017	04/2018	37	37.1	
238	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	321.00	305.18	09/2016 03/2018	05/2018	20	-3.52	
239	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	582.84	12/2015 -	05/2018	29	0	
240	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	90.76	11/2015 05/2018	05/2018	30	0	
241	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	133.20	08/2016 -	06/2018	22	0	
242	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	170.62	149.22	03/2012 -	06/2018	75	-16.77	
243	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	337.03	05/2017 02/2018	08/2018	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
244	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	142.67	11/2014 -	10/2018	47	0	
245	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	0	
246	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	40.05	03/2016 -	12/2018	33	0	
247	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	56.09	04/2018 -	05/2019	13	0	
248	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	75.91	04/2019 06/2019	06/2019	2	0	
249	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
250	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	210.53	10/2019 -	03/2020	5	30.58	
251	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	-	06/2017 -	06/2020	36	.57	
	Delhi Metro Rail Corporation Ltd									
252	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24	0	Delay due to Land acquisition.
	Kochi Metro Rail Corporation Ltd									
253	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
	Nagpur Metro Rail Corporation Ltd									
254	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 8,680.00	8,680.00	3,480.63	03/2018 12/2019	12/2019	21	0	
	Total		84,675.01 -	85,394.10	43,103.65					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (March 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Grand Total		5,88,870.34	7,27,417.98	4,15,619.31					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(March 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	ATOMIC ENERGY							
	Bhavini Limited							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	06/2018	74.69	93
	Total		3,492.00 -	6,100.00				
	CIVIL AVIATION							
	Airport Authority Of India Limited							
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	COAL							
	Neyveli Lignite Corporation							
3	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00	06/2017 -	04/2018	11.60	10
	Northern Coal Fields Limited							
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58	72
	Singareni Colliers Company Limited							
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60	60
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24	84
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	South-Eastern Coal Fields Limited							
8	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	Total		1,929.87 -	3,000.82				
	FERTILISERS							
	Rashtriya Chemical & Fertiliser Limited							
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		197.79 -	209.44				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
10	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33	9
	<u>Hindustan Petroleum Corporation Limited</u>							
11	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50	52
	<u>Indian Oil Corporation Limited</u>							
12	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
13	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22	9
	<u>Oil & Natural Gas Corporation Limited</u>							
14	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78	70
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,256.72	05/2013 -	11/2018	45.83	66
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42	57
17	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	05/2013	4,124.35 -	5,725.50	04/2016 -	03/2018	38.82	23
18	MH NORTH REDEVELOPMENT PHASE III - [N16000188	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87	12
	<u>Oil India Limited</u>							
19	TWENTY NOS. FEEDER GAS LINES - [N16000192	03/2009	228.64 -	256.41	12/2016 -	05/2018	12.15	17
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47	20
	Total		22,117.54 -	27,360.33				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
21	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28	135
	<u>National Thermal Power Corporation</u>							
22	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14	93

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
23	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41	57
24	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	06/2018	86.27	81
25	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55	24
26	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55	21
27	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	02/2019	5.91	13
28	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64	10
29	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65	123
30	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55	20
31	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	03/2018	11.66	14
<u>North East Electric Power Corporation</u>								
32	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	04/2018	133.06	56
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	10/2018	147.51	106
<u>Power Grid Corporation Of India Limited</u>								
34	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	09/2018	32.69	30
35	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	09/2018	14.60	31
36	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92	23
37	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	09/2018	26.82	6
38	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	06/2018	30.37	16
39	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	09/2018	79.61	49
40	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	06/2019	5.34	31
41	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2018	31.17	54
42	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	05/2018	36.74	35

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
43	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59	99
44	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	06/2018	42.83	30
45	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	09/2018	36.01	70
46	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	12/2018	38.61	32
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93	118
48	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49	12
49	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	09/2018	39.30	48
50	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2018	36.79	66
51	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	06/2018	26.86	30
52	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2018	5.14	74
53	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28	12
54	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65	103
	Satluj Jal Vidyut Nigam Limited							
55	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96	24
	Thdc India Limited							
56	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75	61
57	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,789.61	06/2013 -	11/2020	52.10	89
58	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	12/2020	165.65	58
	Total		1,49,564.80 -	1,96,155.21				
	RAILWAYS							
	Eastern Railways							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
	Metropolitan Rapid Transport Projects							
60	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
61	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	North Central Railway							
62	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
63	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
	North East Frontier Railway							
64	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94	60
65	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73	123
66	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72
67	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
68	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
69	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33	122
70	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45	108
	North Western Railway							
71	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02	63
72	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84	57
	Northern Railway							
73	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84	193
	Rail Vikas Nigam Ltd.							
74	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26	166
75	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88	96
76	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04	58
77	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63	144

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
78	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98	4,259.48	03/2016	12/2020	7.78	57
	<u>South East Central Railway</u>							
79	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30	1,776.81	03/1998	12/2019	359.96	261
	<u>West Central Railway</u>							
80	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66	6,093.31	05/2008	03/2023	2,360.35	178
	<u>Western Railway</u>							
81	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24	321.62	03/2012	03/2019	1.06	84
	Total		25,838.95	96,934.69				
	ROAD TRANSPORT AND HIGHWAYS							
	National Highways And Infrastructure Development Corporation Ltd.							
82	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93	155.00	01/2017	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
83	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	280.13	11/2008	03/2018	80.68	112
84	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61	309.56	04/2010	04/2018	42.25	96
85	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	331.23	07/2009	03/2018	68.99	104
86	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	361.00	02/2009	05/2018	28.93	111
87	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58	1,177.00	03/2020	06/2020	41.54	3
88	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62	1,187.10	03/2020	05/2020	13.97	2
89	SIX LANNING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]	03/2017	993.16	1,434.00	03/2020	05/2020	44.39	2
90	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	03/2018	106.50	76
	Total		4,961.94	7,523.02				
	SHIPPING AND PORTS							
	Mumbai Port Trust							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
91	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		366.39 -	669.46				
	STEEL							
	Rastriya Ispat Nigam Limited							
92	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39	29
	Total		343.00 -	488.40				
	TELECOMMUNICATIONS							
	Department Of Telecommunication							
93	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	04/2020	84.97	57
	Total		13,334.00 -	24,664.00				
	URBAN DEVELOPMENT							
	Central Public Works Department							
94	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
95	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	04/2018	44.75	25
96	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]	08/2014	350.02 -	479.87	03/2015 -	04/2018	37.10	37
97	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36
98	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
	Total		2,421.00 -	3,186.19				
	Grand Total		2,24,881.89	3,66,732.89				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	CIVIL AVIATION				
	Airport Authority Of India Limited				
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 -	-
	Total		309.46 -		
	COAL				
	Bharat Coking Coal Limited				
2	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	Eastern Coal Fields Limited				
3	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	-
	Singareni Colliers Company Limited				
4	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
	Total		1,595.80 -		
	STEEL				
	Hindustan Steelwork Construction Limited				
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
6	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
7	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
8	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
9	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
10	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
11	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
12	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	Steel Authority Of India Limited (Sail)				
13	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL, JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		7,151.88 -		
	PETROLEUM				
	<u>Bharat Petroleum Corporation Limited</u>				
15	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	<u>Chennai Petroleum Corporation Limited</u>				
16	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
17	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				
18	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA	03/2014	238.50 -	03/2017 10/2017	10/2017
19	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL, GUJARAT	02/2016	931.00 -	07/2017 -	02/2018
20	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	12/2016 -	-
21	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	05/2015 -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Numaligarh Refinery Limited</u>				
23	DIESEL HYDROTREATOR - [N16000207]NRL, ASSAM	07/2015	1,031.37 -	01/2018 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
24	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC, TRIPURA	05/2016	215.38 -	06/2017 -	01/2018
	<u>Oil India Limited</u>				
25	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	03/2015 -	11/2017
26	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL, MULTI STATE	11/2015	500.00 -	06/2017 -	-
	Total		10,863.92 -		
	POWER				
	<u>Damodar Valley Corporation</u>				
27	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,139.00	12/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
28	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.00	02/2011 -	-
	<u>National Hydro-Electric Power Corporation</u>				
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
30	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016
31	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
32	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
33	FGUTPP, UNCHAHAIR STAGE-IV (1X500 MW) - [N18000174]NTPC, UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
	<u>North East Electric Power Corporation</u>				
34	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 -	07/2013 -	-
	Total		30,190.89 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
35	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS, MULTI STATE	04/2011	1,718.00 -	09/2011 -	-
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
36	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	-
37	AIIMS-RAE BAREILLY HOUSING - [N21000006]HSCC, UTTAR PRADESH	10/2013	159.50 -	11/2013 -	-
38	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-
	Total		749.18 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
39	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
40	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	81,459.00 -	- -	-
	<u>East Central Railways</u>				
41	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	501.69 335.77	03/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
42	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
43	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
44	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
45	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
46	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
47	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-
48	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
49	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
50	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
51	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
52	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
53	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
54	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
55	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
56	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
57	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
58	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
59	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
60	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
East Coast Railway					
61	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 07/2015	07/2015
62	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
63	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
64	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
65	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
66	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Eastern Railways				
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
68	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
69	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	-
70	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
71	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-
72	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
73	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-
74	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	- -	-
75	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	450.00 -	- -	-
76	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	- -	-
77	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	- -	-
78	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	-
79	BANDEL-BOINCHI 3RD LINE - [N22000221]ER, MULTI STATE	04/2011	288.35 -	- -	-
80	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	- -	-
81	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	923.52 -	- -	-
82	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.91 -	- -	-
83	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER, MULTI STATE	04/2010	174.56 -	- -	-
84	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 -	- -	-
85	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	296.44 -	- -	-
86	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55 -	- -	-
87	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17 -	- -	-
88	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	267.09 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
89	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
90	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
91	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
92	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
93	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
94	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
95	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
96	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-
97	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
98	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
99	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
100	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
101	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
102	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 495.74	06/2013 -	03/2017
103	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
104	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
105	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
106	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
107	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
108	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>North East Frontier Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016
110	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
111	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
	North Eastern Railway				
112	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	- -	-
113	KICHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
114	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
115	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
116	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
	North Western Railway				
117	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
118	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
119	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
120	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
121	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 295.02	- -	-
	Northern Railway				
122	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
123	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
124	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
125	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-
126	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
127	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
128	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
129	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
130	DELHI-SOHNANU-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
131	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
132	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
133	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
134	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
135	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
136	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
137	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
138	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
139	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
140	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
141	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
142	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
143	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	12/2017
144	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	12/2017
145	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017
146	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
148	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	- -	-
149	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
	<u>Railway Electrification</u>				
150	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
151	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-
152	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	-
153	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
154	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-
155	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
156	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 1,693.00	- -	-
157	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
158	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
159	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
160	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
161	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
162	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
163	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
164	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
165	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
166	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-
	<u>South East Central Railway</u>				
167	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
	<u>South Eastern Railway</u>				
168	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
169	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 583.02	06/2004 -	-
170	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
171	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
172	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
173	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
174	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
175	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-
176	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	-
177	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
178	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
179	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
180	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-
181	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-
	South Western Railway				
182	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
183	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
184	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
185	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
186	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
187	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
188	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
189	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
190	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
191	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
192	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
193	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
194	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
195	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
196	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
	Southern Railway				
197	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
198	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
199	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	-
200	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
201	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
202	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
203	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-
204	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-
205	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
206	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
207	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
208	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
209	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
210	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
211	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
212	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
213	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
214	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
215	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
216	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
	Western Railway				
217	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 2,473.40	03/2012 -	-
218	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 -	-
219	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
220	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
221	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
222	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-
223	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
224	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
225	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
226	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
227	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		1,80,551.56 -		
	ROAD TRANSPORT AND HIGHWAYS				
	Dept Of Road Transport & Highways				
228	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
229	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
230	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
231	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	Ministry Of Road Transport And Highways				
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018
233	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016
234	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017
235	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017
236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	05/2016
237	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016
238	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017
239	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
240	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
241	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016
243	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016
246	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	10/2017
248	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017
249	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017
250	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	11/2014
251	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017
252	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017
253	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016
254	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
255	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
256	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
257	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
259	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
260	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
261	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
262	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
263	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
264	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
265	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
266	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
267	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
268	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
269	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
270	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
271	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
272	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
273	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
274	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
275	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
276	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
277	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
278	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
279	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
280	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
281	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
282	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
283	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
284	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
285	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
286	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
287	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	04/2017
288	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	04/2017
289	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	06/2016
290	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2016
291	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017
292	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
293	2 LANE WITH HARD SHOULDER, REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS	03/2017	409.85 -	12/2017 -	12/2017
294	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	-
295	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
296	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
297	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
298	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
299	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
300	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
301	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL, ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
302	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
303	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
304	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
305	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
306	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL, NAGALAND	02/2017	507.68 -	04/2017 -	-
307	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
National Highways Authority Of India					
308	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	12/2017
309	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017
310	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017
311	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
312	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	07/2017
313	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017
314	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017
315	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017
316	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017
317	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	09/2017
318	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017
319	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017
320	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017
321	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017
322	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017
323	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017
324	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017
325	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017
326	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017
327	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017
328	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017
329	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017
330	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017
331	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017
332	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017
333	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017
334	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	-	11/2017
335	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	-	11/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
336	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	12/2017
337	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	12/2017
338	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2017
339	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2017
340	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017
341	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017
342	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017
343	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017
344	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2017
345	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	12/2017
346	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2017
347	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2017
348	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017
349	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017
350	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017
351	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	12/2017
352	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017
353	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	12/2017
354	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	12/2017
355	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017
356	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	12/2017
357	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	12/2017
358	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018
359	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018
360	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
361	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018
362	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	02/2018
363	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018
364	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018
365	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018
366	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018
367	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	-	02/2018
368	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
369	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
370	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
371	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
372	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
373	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
374	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
375	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
376	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
377	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-
378	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-
379	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-
380	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
381	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
382	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-
383	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	-	-
384	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	-	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
385	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
386	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
387	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
388	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
389	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
390	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
391	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
392	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
393	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
394	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
395	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
396	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
397	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
398	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
399	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
400	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
401	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
402	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
403	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
404	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
405	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
406	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
407	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
408	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
409	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	-
410	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
411	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
412	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
413	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
414	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
415	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
416	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
417	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
418	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-
419	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
420	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
421	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-
422	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-
423	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
424	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
425	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
426	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
427	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-
428	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
429	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
430	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
431	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
432	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-
433	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-
434	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
435	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-
436	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
437	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
438	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
439	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-
440	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
441	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
442	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
443	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-
444	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
445	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
446	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
447	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
448	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-
449	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
450	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
451	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
452	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-
453	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
454	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
455	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
456	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
457	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
458	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
459	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
460	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
461	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
462	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
463	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
464	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-
465	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
466	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
467	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
468	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
469	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-
470	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
471	REHABILITATION AND UPGRADE OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
472	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
473	REHABILITATION AND UPGRADE OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
474	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
475	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
476	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
National Highways Development Project					
477	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
478	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016
479	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017
480	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017
481	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017
482	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015
483	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017
484	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017
485	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
486	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	06/2017
487	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017
488	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016
489	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016
490	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	10/2017
491	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016
492	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016
493	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017
494	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
495	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
496	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
	Public Works Dept Of State				
497	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017
498	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017
499	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
500	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011
501	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017
502	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	02/2017
503	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017
504	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
505	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018
506	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018
507	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015
508	REHABILITATION AND UPGADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
509	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017
510	REHABILITATION AND UPGADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
511	REHABILITATION AND UPGADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	05/2017
512	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017
513	REHABILITATION AND UPGADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
514	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
515	REHABILITATION AND UPGADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
516	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016
517	REHABILITATION AND UPGADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	08/2017
518	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017
519	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010
520	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010
521	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016
522	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017
523	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
524	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
525	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
526	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016
527	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017
528	REHABILITATION AND AUGMENTATION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014
529	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015
530	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2016
531	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	11/2016
532	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017
533	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016
534	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	12/2016
535	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016
536	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
537	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
538	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
539	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
540	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
541	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
542	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-
543	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
544	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
545	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
546	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
547	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
548	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
549	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
550	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
551	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
552	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
553	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
554	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
555	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
556	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
557	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
558	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
559	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
560	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
561	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
562	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
563	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
564	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
565	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
566	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
567	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
568	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
569	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
570	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
571	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
572	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
573	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
574	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
575	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
576	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
577	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
578	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(March 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
579	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
580	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
	Total		2,15,466.66 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
581	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU	10/2013	198.94 247.00	06/2017 -	-
582	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.33	12/2017 03/2018	-
583	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU	12/2014	274.85 334.00	04/2017 12/2017	-
	<u>Port Trust</u>				
584	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
585	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
	Total		3,295.69 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
586	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	Total		2,111.17 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
587	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
588	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-
589	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-
	<u>Chennai Metro Rail Ltd</u>				
590	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
591	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Mumbai Metro Rail Corporation Ltd</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(March 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
592	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
	<u>National Building Construcion Corporation Ltd</u>				
593	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		41,605.51 -		
	Grand Total		4,95,609.72		

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>ATOMIC ENERGY</u>					
	<u>Nuclear Power Corporation Of India Limited</u>					
1	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	11/2020 -	11/2023	0/0
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 -	-	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 -	06/2017 12/2017	04/2018	0/0
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Northern Coal Fields Limited</u>					
8	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	03/2021 -	03/2021	0/0
	<u>South-Eastern Coal Fields Limited</u>					
9	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH	05/2017	976.95 -	03/2026 -	03/2026	0/0
	<u>Western Coal Fields Limited</u>					
10	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
11	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>FERTILISERS</u>					
	<u>Rashtriya Chemical & Fertiliser Limited</u>					
12	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72 -	04/2020 -	04/2020	0/0
	<u>MINES</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	National Aluminum Company Limited (Nalco)					
13	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N1000013]NALCO,ODISHA	11/2017	483.00 483.00	04/2021 04/2021	04/2021	0/0
	STEEL					
	Hindustan Steelwork Construction Limited					
14	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	03/2018	0/0
15	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
16	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
17	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	08/2018	0/0
18	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
19	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
20	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
21	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
22	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
23	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
24	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
25	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
26	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
27	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
28	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	Steel Authority Of India Limited (Sail)					
29	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	PETROLEUM					
	Bharat Petroleum Corporation Limited					
30	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA	05/2015	337.06 -	08/2018 -	08/2018	0/0
31	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
32	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA	05/2015	193.40 -	01/2019 -	01/2019	0/0
33	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	06/2019 -	06/2019	0/0
34	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
35	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA	02/2016	554.00 -	02/2020 -	02/2020	0/0
36	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	02/2020 -	02/2020	0/0
37	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA	08/2016	282.64 -	08/2020 -	08/2020	0/0
38	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
Chennai Petroleum Corporation Limited						
39	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
40	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
Gas Authority Of India Limited						
41	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
42	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH	04/2017	287.49 -	04/2022 -	04/2022	0/0
43	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 243.53	07/2022 -	07/2022	0/0
Hindustan Petroleum Corporation Limited						
44	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
45	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA	11/2017	255.00 -	11/2020 -	11/2020	0/0
46	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	04/2021	0/0
Indian Oil Corporation Limited						
47	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	08/2018	0/0
48	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH	01/2018	666.64 -	09/2019 -	09/2019	0/0
49	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT	03/2018	3,380.00 -	09/2019 -	09/2019	0/0
50	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	04/2020 -	04/2020	0/0
51	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
52	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
53	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT	09/2016	208.35 -	07/2020 -	07/2020	0/0
54	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT	08/2017	1,342.00 -	08/2020 -	08/2020	0/0
55	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	10/2020	0/0
56	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
57	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
58	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
59	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
60	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
61	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
62	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
63	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2021	0/0
64	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	08/2021	0/0
65	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	12/2021 -	12/2021	0/0
Indian Strategic Petroleum Reserves Ltd						
66	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRIL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
Oil & Natural Gas Corporation Limited						
67	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	06/2017 -	01/2018	0/0
68	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 04/2018	04/2018	0/0
69	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	05/2017 05/2018	05/2018	0/0
70	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 181.02	01/2017 05/2018	05/2018	0/0
71	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0
72	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 207.80	09/2018 09/2018	09/2018	0/0
73	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 567.22	11/2019 12/2018	12/2018	0/0
74	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 6,068.80	04/2019 03/2019	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
75	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC, MAHARASHTRA	01/2015	4,619.94 4,619.94	12/2017 03/2019	03/2019	0/0
76	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU	11/2015	390.52 390.52	03/2019 -	04/2019	0/0
77	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC, MAHARASHTRA	01/2017	474.15 474.15	05/2019 05/2019	05/2019	0/0
78	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	09/2011 06/2019	06/2019	0/0
79	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 5,842.31	05/2019 10/2019	10/2019	0/0
80	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC, MAHARASHTRA	02/2017	546.15 546.15	11/2019 11/2019	11/2019	0/0
81	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC, MAHARASHTRA	02/2017	511.30 511.30	11/2019 11/2019	11/2019	0/0
82	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC, MAHARASHTRA	02/2017	968.61 968.61	11/2019 11/2019	11/2019	0/0
83	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
84	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC, ASSAM	07/2016	249.85 249.85	05/2020 05/2020	05/2020	0/0
85	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC, ANDHRA PRADESH	03/2016	34,012.00 -	06/2020 06/2020	06/2020	0/0
86	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC, MAHARASHTRA	02/2017	4,006.83 4,006.83	05/2021 -	05/2021	0/0
87	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC, JHARKHAND	12/2015	658.62 910.23	03/2023 03/2022	03/2022	0/0
88	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC, GUJARAT	02/2017	1,162.56 1,162.56	03/2026 03/2026	03/2026	0/0
<u>Oil India Limited</u>						
89	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	12/2016 -	05/2018	0/0
90	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	03/2017 -	11/2018	0/0
91	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
92	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL, MULTI STATE	09/2016	571.66 -	12/2019 -	12/2019	0/0
93	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL, MULTI STATE	05/2016	406.00 -	10/2020 -	10/2020	0/0
94	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL, MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
<u>POWER</u>						
<u>Chenab Valley Power Projects [P] Limited</u>						
95	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	10/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>National Hydro-Electric Power Corporation</u>					
96	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>National Thermal Power Corporation</u>					
97	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016	0/0
98	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00 -	11/2019 -	12/2020	0/0
	<u>Power Grid Corporation Of India Limited</u>					
99	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL, ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	03/2018	0/0
100	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 -	04/2018	0/0
101	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL, MULTI STATE	04/2015	2,525.00 -	11/2017 -	04/2018	0/0
102	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL, MAHARASHTRA	04/2015	2,225.00 2,225.00	01/2018 -	04/2018	0/0
103	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	09/2014 09/2017	06/2018	0/0
104	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 12/2017	06/2018	0/0
105	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	03/2018 -	06/2018	0/0
106	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL, MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
107	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL, MULTI STATE	03/2015	955.00 1,161.00	12/2015 -	06/2018	0/0
108	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL, MADHYA PRADESH	02/2015	1,750.00 -	06/2018 -	06/2018	0/0
109	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL, MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
110	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
111	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL, MULTI STATE	07/2016	150.99 -	07/2018 -	07/2018	0/0
112	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE	03/2015	1,071.24 -	09/2017 09/2018	09/2018	0/0
113	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH	01/2016	305.04 -	03/2017 09/2018	09/2018	0/0
114	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
115	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 -	09/2018	0/0
116	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	10/2018 -	10/2018	0/0
117	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	11/2017 10/2018	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
118	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
119	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
120	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
121	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
122	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
123	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	01/2019	0/0
124	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
125	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
126	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
127	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	02/2019	0/0
128	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 03/2019	03/2019	0/0
129	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
130	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
131	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
132	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
133	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE	10/2016	167.75 -	04/2019 -	04/2019	0/0
134	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
135	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
136	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
137	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
138	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALLAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
139	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
140	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0
141	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
142	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	07/2019	0/0
143	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
144	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	09/2019	0/0
145	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
146	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
147	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
148	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
149	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
150	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
151	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
152	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
153	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
154	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
	Satluj Jal Vidyut Nigam Limited					
155	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	12/2021 -	12/2021	0/0
	HEAVY INDUSTRY					
	Natrip Implementation Society					
156	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	-	0/0
	HEALTH AND FAMILY WELFARE					
	Hospital Services Consultancy Corporation					
157	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2019	0/0
	Hospital Services Consultancy Corporation Ltd					
158	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0
159	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2019	0/0
160	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
161	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	08/2019	0/0
162	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-	0/0
163	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
	RAILWAYS					
	Central Railways					
164	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- -	03/2019	0/0
165	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- -	03/2021	0/0
166	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- -	03/2021	0/0
167	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	03/2022	0/0
168	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- -	03/2022	0/0
169	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	- -	03/2022	0/0
170	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 3,168.29	- -	03/2023	0/0
171	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	- -	03/2023	0/0
172	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	- -	03/2023	0/0
173	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 1,035.16	- -	03/2023	0/0
174	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	03/2024	0/0
175	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	03/2024	0/0
176	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	03/2024	0/0
177	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	- -	03/2024	0/0
178	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
	Container Corporation Of India					
179	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2018	0/0
180	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2018	0/0
181	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
182	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
183	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
184	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	03/2019	0/0
185	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
186	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019	0/0
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
187	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
<u>East Central Railways</u>						
188	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0
189	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0
190	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
191	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
192	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
193	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
194	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
195	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
196	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-	0/0
197	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
198	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
199	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
200	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
201	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
202	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
203	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
204	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
205	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
206	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
207	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
208	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
209	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
East Coast Railway						
210	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 07/2015	07/2015	0/0
211	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	03/2020	0/0
212	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2020	0/0
213	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
214	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	- -	03/2021	0/0
215	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 843.04	- -	03/2021	0/0
216	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2021 -	03/2021	0/0
217	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
218	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	06/2021	0/0
219	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2021 -	03/2022	0/0
220	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2021 -	03/2022	0/0
221	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	- -	12/2022	0/0
222	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
223	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
224	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
225	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
226	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	Eastern Railways					
227	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	11/2018	0/0
228	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	03/2019	0/0
229	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	03/2020	0/0
230	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
231	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
232	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
233	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
234	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
235	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0
236	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
237	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
238	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
239	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
240	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-	0/0
241	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
242	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
243	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
244	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
245	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
246	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
247	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
248	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
249	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
250	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
251	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
252	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
253	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
254	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
255	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
256	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
257	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
258	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-	0/0
259	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
260	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
261	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
262	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
Kochi Metro Rail Corporation Ltd						
263	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
Metropolitan Rapid Transport Projects						
264	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
265	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
266	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
267	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
268	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-	0/0
269	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
North Central Railway						
270	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
271	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
272	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
273	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
274	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
North East Frontier Railway						
275	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016	0/0
276	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
277	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
278	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2018	0/0
279	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
280	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
281	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	- -	03/2019	0/0
282	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	- -	03/2019	0/0
283	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	- -	03/2019	0/0
284	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2020	0/0
285	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	03/2011 -	03/2020	0/0
286	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	- -	03/2020	0/0
287	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	- -	03/2020	0/0
288	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
289	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	04/2014 -	03/2020	0/0
290	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	03/2020	0/0
291	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
292	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
293	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	03/2020	0/0
294	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
295	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	03/2020	0/0
296	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	- -	03/2020	0/0
297	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	- -	03/2020	0/0
298	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- -	03/2021	0/0
299	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	03/2021	0/0
300	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	03/2022	0/0
301	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
302	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
North Eastern Railway						
303	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
304	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	06/2018	0/0
305	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	08/2018	0/0
306	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	08/2018	0/0
307	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	10/2018	0/0
308	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	05/2019	0/0
309	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
310	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
311	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
312	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
313	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
North Western Railway						
314	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	10/2018	0/0
315	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	11/2018	0/0
316	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	- 02/1997	02/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
317	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 218.39	- -	02/2019	0/0
318	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	03/2019	0/0
319	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	03/2019	0/0
320	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	06/2019	0/0
321	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	12/2019	0/0
322	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	03/2020	0/0
323	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
324	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
325	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 295.02	- -	-	0/0
Northern Railway						
326	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2018	0/0
327	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
328	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
329	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
330	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-	0/0
331	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
332	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
333	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
334	FAIZABAD-LALGANJ VIA KARBAGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
335	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
336	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
337	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
338	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
339	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
340	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
341	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
342	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
343	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
344	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
345	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
346	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
<u>Rail India Technical And Economic Service</u>						
347	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
<u>Rail Vikas Nigam Ltd.</u>						
348	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
349	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	03/2018	0/0
350	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	- -	03/2018	0/0
351	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
352	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	03/2019	0/0
353	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	03/2019	0/0
354	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
355	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
356	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	12/2019	0/0
357	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
358	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
359	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
360	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
361	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
362	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
363	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
364	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	376.59 -	- -	12/2020	0/0
365	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
366	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0
367	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
368	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
369	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
370	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	- -	12/2024	0/0
371	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
372	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
373	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
374	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
375	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
376	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
Railway Electrification						
377	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
South Central Railway						
378	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2019	0/0
379	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 -	- -	03/2021	0/0
380	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	- -	03/2021	0/0
381	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
382	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	- -	-	0/0
383	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
384	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-	0/0
385	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-	0/0
386	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 1,693.00	- -	-	0/0
387	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
388	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
389	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
390	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-	0/0
<u>South East Central Railway</u>						
391	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	737.72 -	12/2018 -	12/2018	0/0
392	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
393	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
394	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
<u>South Eastern Railway</u>						
395	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
396	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
397	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	763.18 -	12/2021 -	12/2021	0/0
398	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2021	0/0
399	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
400	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 583.02	06/2004 -	-	0/0
401	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
402	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
403	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-	0/0
404	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
405	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
406	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-	0/0
407	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	-	0/0
408	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
409	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
410	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
411	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-	0/0
412	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-	0/0
South Western Railway						
413	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	03/2020	0/0
414	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
415	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
416	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
417	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
418	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
419	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
420	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
421	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
422	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
423	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
424	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
425	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
426	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
Southern Railway						
427	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
428	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
429	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	-	0/0
430	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
431	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
432	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-	0/0
433	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-	0/0
434	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
435	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
436	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
437	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
438	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
439	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
440	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
441	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
442	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
443	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
444	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
445	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
West Central Railway						
446	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2021	0/0
Western Railway						
447	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
448	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	- -	03/2019	0/0
449	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 416.86	03/2013 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
450	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0
451	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	03/2022	0/0
452	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 2,473.40	03/2012 -	-	0/0
453	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 -	-	0/0
454	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
455	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
456	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
457	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-	0/0
458	GANDHINAGAR REDEVELOPMENT OF STATION ALOGLWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
459	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
460	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
461	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
462	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	ROAD TRANSPORT AND HIGHWAYS					
	Ministry Of Road Transport And Highways					
463	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
464	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
465	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017	0/0
466	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017	0/0
467	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
468	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	05/2016	0/0
469	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016	0/0
470	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017	0/0
471	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
472	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
473	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015	0/0
474	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
475	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
476	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
477	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
478	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016	0/0
479	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	10/2017	0/0
480	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017	0/0
481	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017	0/0
482	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	11/2014	0/0
483	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
484	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
485	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016	0/0
486	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	04/2018	0/0
487	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	05/2018	0/0
488	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
489	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
490	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
491	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
492	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
493	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
494	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
495	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
496	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
497	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
498	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
499	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
500	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
501	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
502	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
503	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
504	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
505	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
506	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
507	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
508	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
509	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
510	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
511	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
512	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
513	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
514	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
515	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
516	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
517	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
518	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
519	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
520	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
	National Highways And Infrastructure Development Corporation Ltd.					
521	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	04/2017	0/0
522	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017	0/0
523	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016	0/0
524	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	12/2017	0/0
525	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	05/2018	0/0
526	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	05/2018	0/0
527	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
528	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	06/2018	0/0
529	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	10/2018	0/0
530	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	10/2018	0/0
531	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	10/2018	0/0
532	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
533	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
534	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
535	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
536	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
537	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
538	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
539	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
540	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
541	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
542	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
543	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
544	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
545	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
546	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
547	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
548	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
549	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
550	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
National Highways Authority Of India						
551	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	12/2017	0/0
552	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017	0/0
553	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017	0/0
554	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017	0/0
555	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
556	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	08/2017	0/0
557	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	11/2013 -	08/2017	0/0
558	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017	0/0
559	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017	0/0
560	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017	0/0
561	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	09/2017	0/0
562	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
563	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
564	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017	0/0
565	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017	0/0
566	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017	0/0
567	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017	0/0
568	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017	0/0
569	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017	0/0
570	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017	0/0
571	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017	0/0
572	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017	0/0
573	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017	0/0
574	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017	0/0
575	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	-	11/2017	0/0
576	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	-	11/2017	0/0
577	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	12/2017	0/0
578	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2017	0/0
579	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2017	0/0
580	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017	0/0
581	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017	0/0
582	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017	0/0
583	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017	0/0
584	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2017	0/0
585	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	12/2017	0/0
586	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
587	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2017	0/0
588	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017	0/0
589	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017	0/0
590	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017	0/0
591	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	12/2017	0/0
592	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017	0/0
593	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	12/2017	0/0
594	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	12/2017	0/0
595	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
596	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0
597	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	12/2017	0/0
598	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0
599	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
600	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
601	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
602	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	02/2018	0/0
603	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018	0/0
604	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
605	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
606	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
607	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	02/2018	0/0
608	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	03/2018	0/0
609	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	03/2018	0/0
610	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
611	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00	07/2009	03/2018	0/0
612	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00	11/2011	03/2018	0/0
613	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00	01/2014	03/2018	0/0
614	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00	07/2013	03/2018	0/0
615	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	09/2014	03/2018	0/0
616	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79	08/2013	03/2018	0/0
617	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16	07/2014	03/2018	0/0
618	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69	06/2014	03/2018	0/0
619	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51	03/2018	03/2018	0/0
620	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56	03/2018	03/2018	0/0
621	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53	03/2018	03/2018	0/0
622	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31	03/2018	03/2018	0/0
623	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51	03/2018	03/2018	0/0
624	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78	03/2018	03/2018	0/0
625	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46	03/2018	03/2018	0/0
626	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52	06/2012	03/2018	0/0
627	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18	-	03/2018	0/0
628	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07	03/2020	03/2018	0/0
629	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61	04/2010	04/2018	0/0
630	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00	03/2014	04/2018	0/0
631	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34	04/2018	04/2018	0/0
632	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00	10/2017	04/2018	0/0
633	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90	04/2018	04/2018	0/0
634	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09	-	04/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
635	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	- -	04/2018	0/0
636	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	- -	04/2018	0/0
637	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	- -	04/2018	0/0
638	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	02/2009 -	05/2018	0/0
639	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	- -	05/2018	0/0
640	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	- -	05/2018	0/0
641	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	- -	05/2018	0/0
642	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	- -	05/2018	0/0
643	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	- -	05/2018	0/0
644	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	- -	05/2018	0/0
645	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	- -	05/2018	0/0
646	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI, HARYANA	05/2015	600.85 -	- -	05/2018	0/0
647	PATNA-MUZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	06/2018	0/0
648	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	06/2018	0/0
649	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	06/2018	0/0
650	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	06/2018	0/0
651	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
652	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
653	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
654	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
655	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
656	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	06/2018	0/0
657	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
658	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	- -	06/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
659	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
660	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
661	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	07/2018	0/0
662	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0
663	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	- -	07/2018	0/0
664	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	- -	07/2018	0/0
665	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	07/2018	0/0
666	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	08/2018	0/0
667	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	- -	08/2018	0/0
668	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0
669	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	08/2018	0/0
670	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	- -	08/2018	0/0
671	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	09/2018	0/0
672	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2018	0/0
673	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	10/2018	0/0
674	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	- -	10/2018	0/0
675	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	- -	11/2018	0/0
676	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	11/2018	0/0
677	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
678	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018	0/0
679	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2018	0/0
680	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018	0/0
681	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2018	0/0
682	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
683	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
684	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
685	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	01/2019	0/0
686	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	01/2019	0/0
687	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	- -	01/2019	0/0
688	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	02/2019	0/0
689	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	02/2019	0/0
690	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
691	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	03/2019	0/0
692	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
693	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	03/2019	0/0
694	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	03/2019	0/0
695	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	03/2019	0/0
696	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	03/2019	0/0
697	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	- -	03/2019	0/0
698	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	- -	03/2019	0/0
699	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	04/2019	0/0
700	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	04/2019	0/0
701	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
702	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	04/2019	0/0
703	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	04/2019	0/0
704	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	04/2019	0/0
705	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	04/2019	0/0
706	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
707	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	05/2019	0/0
708	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	05/2019	0/0
709	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	05/2019	0/0
710	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	05/2019	0/0
711	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	- -	05/2019	0/0
712	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	- -	05/2019	0/0
713	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
714	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
715	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	06/2019	0/0
716	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
717	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
718	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	- -	07/2019	0/0
719	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	- -	07/2019	0/0
720	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	08/2019	0/0
721	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	08/2019	0/0
722	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	09/2019	0/0
723	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	02/2020	0/0
724	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
725	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	03/2020	0/0
726	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
727	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
728	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
729	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	03/2020	0/0
730	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
731	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	03/2020	0/0
732	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	03/2020	0/0
733	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	03/2020	0/0
734	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
735	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
736	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
737	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
738	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
739	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
740	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
741	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	-	04/2020	0/0
742	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0
743	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
744	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	05/2020	0/0
745	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2020	0/0
746	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
747	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	06/2020	0/0
748	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
749	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
750	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
751	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
752	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
753	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
754	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
755	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
756	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
757	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	03/2016 -	-	0/0
758	PADI - DAHOD - [N24000353]NHAI, RAJASTHAN	11/2014	279.14 -	05/2017 -	-	0/0
759	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN	10/2014	264.72 -	04/2017 -	-	0/0
760	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
761	2-LANING WITH PS SITARGANJ BAREILLY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
762	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	-	0/0
763	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-	0/0
764	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
765	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
766	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
767	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-	0/0
768	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	- -	-	0/0
769	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	- -	-	0/0
770	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
771	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-	0/0
772	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-	0/0
773	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
774	MEERUT-BULANDSHAHR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
775	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
776	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
777	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-	0/0
778	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
779	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
780	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
781	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
782	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
783	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0
784	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
785	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
786	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0
787	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
788	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
789	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	-	0/0
790	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
791	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
792	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
793	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
794	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
795	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
796	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
797	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
798	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
799	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
800	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
801	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
802	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
803	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
804	REHABILITATION AND UPGRADATION TO FOUR LANNING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
805	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
806	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-	0/0
807	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
808	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
809	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
810	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
811	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
812	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-	0/0
813	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-	0/0
814	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-	0/0
815	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-	0/0
816	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
817	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-	0/0
818	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
819	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-	0/0
820	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
821	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
822	4-LANNING OF OTTANCHATRAMP BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
823	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-	0/0
824	BALANCE WORK FOR FOUR LANNING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
825	SIX LANNING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-	0/0
826	FOUR LANNING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
827	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
828	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-	0/0
829	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
830	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-	0/0
831	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
832	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-	0/0
833	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
834	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
835	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
836	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
837	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
838	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
839	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
840	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
841	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
842	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-	0/0
843	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
844	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-	0/0
845	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-	0/0
846	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-	0/0
847	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
848	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
849	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
850	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-	0/0
851	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
852	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
853	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
854	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
855	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
856	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
National Highways Development Project						
857	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015	0/0
858	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
859	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
860	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
861	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
862	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
863	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
864	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015	0/0
865	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
866	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
867	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
868	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
869	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
870	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
871	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
872	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
873	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
874	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
875	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
Public Works Dept Of State						
876	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
877	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
878	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
879	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
880	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
881	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
882	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
883	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015	0/0
884	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015	0/0
885	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
886	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
887	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
888	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
889	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
890	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
891	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0
892	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
893	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
894	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
895	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
896	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
897	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
898	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
899	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
900	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
901	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
902	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
903	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
904	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-	0/0
905	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
906	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
907	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
908	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
909	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
910	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
911	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
912	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
913	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
914	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
915	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
916	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
917	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
918	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
919	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
920	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
921	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
922	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
923	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
924	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
925	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
926	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
927	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
928	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
929	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
930	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
931	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
932	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
933	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
934	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
935	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
936	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
937	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
938	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
939	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
	SHIPPING AND PORTS					
	Kamarajar Port Limited					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
940	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU	03/2016	600.00 257.90	12/2017 05/2020	05/2020	0/0
	Mumbai Port Trust					
941	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	12/2010 -	12/2018	0/0
	Port Trust					
942	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
943	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
	TELECOMMUNICATIONS					
	Bharat Sanchar Nigam Limited					
944	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL, MAHARASHTRA	08/2017	159.30 -	04/2018 -	04/2018	0/0
945	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL, MAHARASHTRA	08/2017	167.68 -	04/2018 -	04/2018	0/0
946	MAHARASHTRA ACCESS (LOT 1) - [N26000109]BSNL, MAHARASHTRA	08/2017	212.70 -	05/2018 -	05/2018	0/0
947	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL, MAHARASHTRA	08/2017	215.30 -	05/2018 -	05/2018	0/0
948	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL, GUJARAT	09/2017	171.54 -	05/2018 -	05/2018	0/0
949	UP (EAST) ACCESS LOT1 - [N26000112]BSNL, UTTAR PRADESH	11/2017	169.45 -	08/2018 -	08/2018	0/0
	Department Of Telecommunication					
950	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 04/2020	04/2020	0/0
	Mahanagar Telephone Nigam Limited					
951	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL, DELHI	06/2016	418.26 -	06/2017 -	03/2018	0/0
	URBAN DEVELOPMENT					
	Bangalore Metro Rail Corporation Limited					
952	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	Central Public Works Department					
953	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02 479.87	03/2015 12/2017	04/2018	0/0
954	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	09/2016 03/2018	05/2018	0/0
955	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	12/2015 -	05/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (March 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
956	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	11/2015 05/2018	05/2018	0/0
957	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	06/2019	0/0
958	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
959	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 -	02/2020	0/0
960	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 2.00	05/2020 -	05/2020	0/0
961	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	06/2020	0/0
962	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-	0/0
963	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-	0/0
Chennai Metro Rail Ltd						
964	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	03/2018	0/0
Delhi Metro Rail Corporation Ltd						
965	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	03/2018	0/0
Jawahar Lal Nehru National Urban Renewal Mission						
966	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
Kochi Metro Rail Corporation Ltd						
967	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
Lucknow Metro Rail Corporation Limited						
968	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
Mumbai Metro Rail Corporation Ltd						
969	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-	0/0
Nagpur Metro Rail Corporation Ltd						
970	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 8,680.00	03/2018 12/2019	12/2019	0/0
National Building Construcion Corporation Ltd						
971	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
Total			10,53,176.42 -			0/0
Grand Total			10,53,176.42			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	PETROLEUM						
	Gas Authority Of India Limited						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271	7/2015	2,881.40 -	2,881.40	142.49	12/2019 12/2020	12/2019
	Hindustan Petroleum Corporation Limited						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	9/2015	4,199.00	4,199.00	194.97	03/2020 -	07/2019
	Indian Oil Corporation Limited						
3	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 -	2,321.00	76.00	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216	1/2016	247.52 -	247.52	130.07	02/2019 -	12/2018
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	5/2016	664.00 -	664.00	240.69	12/2020 -	02/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226	2/2016	356.00 -	356.00	125.91	05/2019 -	12/2018
	Total		10,668.92 -	10,668.92	910.13		
	POWER						
	Power Grid Corporation Of India Limited						
7	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210	1/2016	207.88 -	207.88	111.50	07/2018 -	03/2018
	Total		207.88 -	207.88	111.50		
	RAILWAYS						
	East Coast Railway						
8	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	148.59	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	148.59		
	ROAD TRANSPORT AND HIGHWAYS						
	National Highways Authority Of India						
9	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	195.03	07/2018 -	06/2018
10	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	86.42	03/2020 -	05/2019

Costing Rs. 150 Crore and above
(March 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2018
	Total		2,251.26 -	2,341.00	281.45		
	Grand Total		14,300.98	14,390.72	1,451.67		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	COAL						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	223.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	293.94	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.26	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
5	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	105.89	03/2019 -	03/2019
6	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
7	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.70	03/2026 -	03/2026
8	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	32.84	03/2019 -	03/2019
9	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	374.32	03/2021 -	03/2021
	<u>Neyveli Lignite Corporation</u>						
10	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	349.99	06/2015 09/2019	09/2019
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,493.82	11/2021 -	11/2021
12	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	168.58	12/2019 -	12/2019
13	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	6.22	09/2019 -	09/2019
14	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	5,229.45	12/2015 04/2018	04/2018
	<u>Northern Coal Fields Limited</u>						
15	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	447.32	03/2018 -	03/2018
16	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	77.75	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
17	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	78.04	03/2019 -	03/2019
18	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
South-Eastern Coal Fields Limited							
19	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	137.98	03/2015 03/2020	03/2020
20	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.79	03/2023 -	03/2023
21	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	77.18	03/2023 03/2021	03/2021
22	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	31.90	03/2022 -	03/2022
23	MALACHUA OPENCAS-2 PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.18	03/2023 -	03/2023
24	MADANNAGAR OPENCAS-2 PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
25	VIJAY WEST OPENCAS-2 PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
26	AMADAND OPENCAS-2 EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021
27	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,668.79	03/2023 -	03/2023
28	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,698.30	03/2023 -	03/2023
29	DURGAPUR OPENCAS-2 PROJECT - [N06000136]	2/2015	916.24 -	916.24	.99	03/2023 -	03/2023
30	AMGAON OPENCAS-2 PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	44.19	03/2020 -	03/2020
31	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
32	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	35.61	03/2021 -	03/2021
33	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.47	03/2021 -	03/2021
34	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	50.54	03/2018 -	03/2018
35	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
36	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	51.22	03/2020 -	03/2020
Western Coal Fields Limited							
37	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	17.31	03/2021 -	03/2021
38	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	139.76	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
39	GOKUL - [N06000120]	11/2014	267.67 -	267.67	206.04	03/2018 -	03/2018
40	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	383.42	03/2020 -	03/2020
41	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	51.12	03/2020 -	03/2020
42	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	239.83	03/2020 -	03/2020
43	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	87.11	03/2021 -	03/2021
44	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	.13	03/2022 -	03/2022
45	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	.04	03/2022 -	03/2022
46	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	15.30	03/2022 -	03/2022
47	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	126.93	03/2019 -	03/2019
48	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
49	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	178.26	03/2020 -	03/2020
50	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
51	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	232.10	03/2025 -	03/2025
52	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	77.21	03/2021 -	03/2021
53	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	96.81	03/2020 -	03/2020
54	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
	Total		75,174.95 -	73,796.21	16,695.86		
	DEFENCE PRODUCTION						
	Goa Shipyard Limited						
55	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	62.51	05/2018 -	05/2018
56	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	49.14	08/2020 -	08/2020
	Total		453.64 -	469.04	111.65		
	FERTILISERS						
	National Fertiliser Limited						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	17.26	11/2019 -	11/2019
58	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	19.56	11/2019 -	11/2019
59	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	17.53	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
60	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	106.14	11/2016 04/2019	04/2019
61	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	413.01	12/2017 04/2018	04/2018
62	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	1.32	04/2020 -	04/2020
	Total		1,781.92 -	1,793.57	574.82		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation</u>						
63	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	24.38	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
64	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	149.00	08/2018 -	08/2018
65	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	77.50	09/2018 -	09/2018
66	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	29.68	03/2019 -	03/2019
67	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	21.79	03/2019 -	03/2019
	Total		1,458.52 -	1,458.52	302.35		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
68	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	89.75	04/2021 04/2021	04/2021
69	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	290.88	01/2020 01/2020	01/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
70	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
71	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	27.78	11/2020 11/2020	11/2020
	Total		6,912.00 -	6,912.00	408.41		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
72	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	315.57	10/2018 -	10/2018
73	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	66.77	02/2020 -	02/2020
74	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	99.46	12/2019 -	12/2019
75	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY [N16000263]	2/2016	3,313.00 -	3,313.00	118.35	02/2020 -	02/2020
76	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	33.23	08/2020 -	08/2020
77	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
78	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	93.74	08/2018 -	08/2018
79	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	40.41	01/2019 -	01/2019
80	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	1,290.71	08/2018 05/2019	05/2019
81	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	281.45	04/2018 -	04/2018
	<u>Chennai Petroleum Corporation Limited</u>						
82	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	186.78	12/2019 -	12/2019
83	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	1.31	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
84	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	1,961.00	12/2018 -	12/2018
85	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	11.79	07/2022 -	07/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
86	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	48.24	04/2022 -	04/2022
87	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	2,915.00	1,645.33	12/2012 02/2019	02/2019
88	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	9.30	12/2020 -	12/2020
89	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	71.07	12/2020 -	12/2020
90	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	40.20	12/2020 -	12/2020
91	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	213.63	12/2020 -	12/2020
92	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	750.00	534.34	12/2018 -	12/2018
93	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	154.37	03/2018 -	03/2018
94	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	606.89	02/2020 -	02/2020
Hindustan Petroleum Corporation Limited							
95	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
96	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	9.75	03/2021 -	03/2021
97	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	-	11/2020 -	11/2020
98	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT - JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
99	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	95.26	09/2019 -	09/2019
100	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	48.37	02/2019 -	02/2019
101	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	570.10	06/2020 -	06/2020
Indian Oil Corporation Limited							
102	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
103	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	597.50	09/2019 -	09/2019
104	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	-	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	2.12	12/2021 -	12/2021
106	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	100.02	09/2019 -	09/2019
107	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]	12/2017	466.43 -	466.43	1.18	10/2020 -	10/2020
108	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
109	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
110	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	14.08	04/2021 -	04/2021
111	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	28.93	04/2020 -	04/2020
112	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	55.39	06/2020 -	06/2020
113	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	93.11	12/2018 -	12/2018
114	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	5.73	12/2020 -	12/2020
115	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	41.00	09/2019 -	09/2019
116	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	282.69	08/2021 -	08/2021
117	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	529.80	11/2018 -	11/2018
118	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	480.79	11/2019 -	11/2019
119	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	112.81	08/2019 -	08/2019
120	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	1,200.16	06/2018 -	06/2018
121	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
122	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	.13	06/2020 -	06/2020
123	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	41.89	07/2020 -	07/2020
124	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	31.07	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
125	SITARGANJ LPG PROJECT - [N16000282	2/2017	160.10 -	160.10	23.99	02/2020 -	02/2020
126	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY [N16000277	5/2016	429.00 -	429.00	133.17	01/2019 -	01/2019
127	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276	5/2016	261.00 -	261.00	.05	01/2021 -	01/2021
128	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
129	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
130	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268	5/2016	348.00 -	348.00	.05	01/2021 -	01/2021
131	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR- SOLAPUR PIPELINE - [N16000267	5/2016	212.00 -	212.00	.08	01/2021 -	01/2021
132	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY [N16000175	3/2014	3,076.00 -	4,190.00	2,548.03	09/2017 06/2018	06/2018
133	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179	3/2014	3,150.00 -	3,150.00	1,817.34	09/2017 12/2018	12/2018
134	PARADIP LPG IMPORT FACILITY - [N16000196	1/2015	690.00 -	690.00	135.02	07/2018 10/2020	10/2020
135	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195	2/2015	890.00 -	887.00	336.86	10/2019 -	10/2019
136	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	1,823.00	270.94	12/2020 -	12/2020
<u>Mangalore Refinery And Petrochemicals Limited</u>							
137	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255	5/2015	224.00 207.00	207.25	92.97	04/2019 -	04/2019
138	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256	10/2015	135.00 171.00	170.70	104.65	03/2019 -	03/2019
139	BSVI UPGRADATION - [N16000257	9/2016	1,810.00 1,810.00	1,810.00	108.81	12/2019 -	12/2019
<u>Oil & Natural Gas Corporation Limited</u>							
140	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061	3/2009	2,465.15 -	2,378.89	2,073.06	03/2013 09/2018	09/2018
141	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084	6/2007	736.65 -	571.47	542.96	09/2011 06/2019	06/2019
142	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159	9/2011	202.25 -	160.16	118.02	07/2016 06/2018	06/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
143	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	184.01	05/2021 -	05/2021
144	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 11/2019	11/2019
145	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 11/2019	11/2019
146	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 11/2019	11/2019
147	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	161.29	05/2019 05/2019	05/2019
148	FIELD DEVELOPMENT OF NBP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	207.80	-	09/2018 09/2018	09/2018
149	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	230.90	03/2026 03/2026	03/2026
150	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	24.69	05/2020 05/2020	05/2020
151	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	1,526.01	04/2018 04/2018	04/2018
152	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	3,961.54	3,816.11	12/2017 03/2019	03/2019
153	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	168.01	09/2018 09/2018	09/2018
154	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	2,041.21	05/2014 05/2018	05/2018
155	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	13.34	01/2014 11/2019	11/2019
156	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	1,027.52	03/2019 05/2020	05/2020
157	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,504.61	1,317.83	05/2017 05/2018	05/2018
158	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	567.22	414.94	11/2019 12/2018	12/2018
159	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	2,765.06	05/2019 10/2019	10/2019
160	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	262.74	06/2020 06/2020	06/2020
161	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	9.35	03/2023 03/2022	03/2022
162	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	181.02	168.93	01/2017 05/2018	05/2018
163	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,400.56	04/2019 03/2019	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
164	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	5,558.19	05/2017 05/2018	05/2018
165	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	5,725.50	5,130.40	04/2016 03/2018	03/2018
	Oil India Limited						
166	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	1.58	10/2020 -	10/2020
167	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI- BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	7.30	12/2019 -	12/2019
	Total		1,83,281.71 -	1,82,698.31	50,562.24		
	POWER						
	National Thermal Power Corporation						
168	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	8,980.00	09/2017 06/2019	06/2019
169	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	1/2008	4,375.35 -	8,150.00	7,057.00	09/2011 06/2018	06/2018
170	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,521.00	03/2013 12/2020	12/2020
171	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	4,333.00	03/2019 09/2019	09/2019
172	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	6,924.00	02/2019 10/2020	10/2020
173	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	1,849.00	07/2020 10/2020	10/2020
174	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	5,115.00	09/2019 -	09/2019
175	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	9,555.00	06/2017 06/2019	06/2019
176	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	8,488.00	11/2016 03/2019	03/2019
177	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	16,934.65	15,364.00	01/2017 03/2018	03/2018
178	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	14,520.00	01/2011 04/2021	04/2021
179	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	322.00	09/2019 02/2022	02/2022
180	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	7,588.00	08/2018 06/2019	06/2019
	North East Electric Power Corporation						
181	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,424.41	12/2009 10/2018	10/2018
182	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,621.16	08/2013 04/2018	04/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Power Grid Corporation Of India Limited						
183	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	660.59	09/2010 12/2018	12/2018
184	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. [N18000080]	2/2010	2,144.00 -	2,932.88	2,617.80	12/2012 06/2018	06/2018
185	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,184.14	04/2016 12/2018	12/2018
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX [N18000158]	2/2014	539.82 -	539.82	400.50	06/2016 09/2018	09/2018
187	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,639.60	08/2013 03/2022	03/2022
188	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	4,514.68	10/2012 12/2018	12/2018
189	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	-	06/2019 -	06/2019
190	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
191	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) [N18000267]	9/2017	198.49 -	198.49	-	09/2019 -	09/2019
192	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	29.20	02/2020 -	02/2020
193	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE- II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	81.90	02/2019 -	02/2019
194	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	13.60	07/2019 -	07/2019
195	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	17.10	09/2018 -	09/2018
196	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	151.00	07/2020 -	07/2020
197	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI [N18000257]	12/2015	3,654.00 -	3,654.00	1,532.00	04/2019 -	04/2019
198	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]	2/2015	1,750.00 -	1,750.00	867.00	06/2018 -	06/2018
199	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.00	06/2019 -	06/2019
200	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	323.07	04/2020 -	04/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
201	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246	2/2017	204.12 -	204.12	10.30	09/2019 -	09/2019
202	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII [N18000245	3/2017	379.95 -	379.95	19.70	12/2019 -	12/2019
203	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244	2/2017	235.53 -	235.53	8.00	06/2019 -	06/2019
204	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243	3/2017	162.31 -	162.31	11.90	03/2019 -	03/2019
205	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242	2/2017	322.30 -	322.30	21.70	02/2019 -	02/2019
206	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
207	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240	10/2016	608.24 -	608.24	132.80	04/2019 -	04/2019
208	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239	10/2016	408.46 -	408.46	70.81	01/2019 -	01/2019
209	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
210	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION [N18000237	10/2016	167.75 -	167.75	62.40	04/2019 -	04/2019
211	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236	3/2017	251.60 -	251.60	12.00	06/2019 -	06/2019
212	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233	9/2016	562.25 -	562.25	18.60	03/2019 -	03/2019
213	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232	8/2016	177.52 -	177.52	45.50	02/2019 -	02/2019
214	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231	8/2016	431.89 -	431.89	81.90	02/2019 -	02/2019
215	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230	7/2016	333.17 -	333.17	220.50	03/2019 -	03/2019
216	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229	7/2016	150.99 -	150.99	74.10	07/2018 -	07/2018
217	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228	7/2016	300.94 -	300.94	112.80	12/2018 -	12/2018
218	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227	7/2016	1,429.38 -	1,429.38	353.90	01/2019 -	01/2019
219	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224	5/2016	167.01 -	167.01	63.90	11/2018 -	11/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
220	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	207.90	04/2019 -	04/2019
221	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	368.70	06/2019 -	06/2019
222	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	99.50	06/2018 -	06/2018
223	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	470.10	12/2018 -	12/2018
224	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	1,313.70	11/2019 -	11/2019
225	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	1,113.30	05/2019 -	05/2019
226	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	193.60	11/2018 -	11/2018
227	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	198.70	04/2018 -	04/2018
228	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	272.70	01/2018 03/2019	03/2019
229	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	907.80	07/2018 -	07/2018
230	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	171.50	03/2017 09/2018	09/2018
231	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	2,392.90	04/2018 09/2018	09/2018
232	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	147.50	10/2018 -	10/2018
233	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	86.60	05/2017 06/2019	06/2019
234	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	547.00	09/2017 09/2018	09/2018
235	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	7/2010	1,272.80 -	1,731.10	1,440.03	11/2012 09/2018	09/2018
236	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	260.03	178.70	07/2017 06/2019	06/2019
237	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	160.59	10/2017 09/2019	09/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
238	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	1/2015	268.80 -	340.88	190.10	03/2018 09/2018	09/2018
239	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	3,772.80	04/2018 -	04/2018
240	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	225.28	143.00	02/2016 09/2018	09/2018
241	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	8/2014	288.49 -	376.09	234.30	02/2017 06/2018	06/2018
242	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	1,979.40	03/2018 03/2019	03/2019
243	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B [N18000165]	3/2014	155.57 -	206.42	143.20	03/2016 09/2018	09/2018
244	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	3,190.27	2,178.75	12/2015 06/2018	06/2018
245	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	703.10	598.00	06/2015 05/2018	05/2018
246	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 -	2,187.32	2,000.25	11/2008 09/2018	09/2018
247	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	386.87	08/2014 09/2018	09/2018
248	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	487.82	06/2014 12/2018	12/2018
249	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	9/2011	1,940.13 -	2,702.65	2,420.46	09/2014 09/2018	09/2018
250	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	179.10	11/2017 10/2018	10/2018
251	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	1,149.70	07/2018 -	07/2018
252	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	550.18	394.40	11/2016 06/2019	06/2019
Satluj Jal Vidyut Nigam Limited							
253	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	100.37	12/2021 -	12/2021
Thdc India Limited							
254	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	40.16	09/2020 -	09/2020
Total			2,30,172.82 -	2,60,501.21	1,54,697.77		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Container Corporation Of India</u>						
255	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	396.47	03/2018 -	03/2018
256	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	249.12	03/2019 -	03/2019
257	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	132.66	03/2019 -	03/2019
258	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	.39	03/2019 -	03/2019
259	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	272.61	03/2019 -	03/2019
260	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	233.95	03/2019 -	03/2019
261	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	152.90	03/2018 -	03/2018
262	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	385.63	03/2018 -	03/2018
	<u>East Central Railways</u>						
263	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
264	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	166.13	03/2020 -	03/2020
265	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
	<u>East Coast Railway</u>						
266	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	117.43	03/2021 -	03/2021
267	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	65.98	03/2021 -	03/2021
268	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
	<u>North Central Railway</u>						
269	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
270	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	52.27	03/2022 -	03/2022
	<u>Rail India Technical And Economic Service</u>						
271	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
272	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	45.50	12/2024 -	12/2024
273	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	120.70	12/2024 -	12/2024
274	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	16,216.00	761.30	12/2026 -	12/2026
275	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.92	95.72	12/2025 -	12/2025
276	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	863.23	03/2019 -	03/2019
277	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.16	12/2025 -	12/2025
278	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	769.00	03/2020 -	03/2020
279	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	850.22	03/2019 -	03/2019
280	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	752.76	12/2020 -	12/2020
281	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.30	797.44	12/2020 -	12/2020
282	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	730.03	03/2020 -	03/2020
283	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,388.35	03/2020 -	03/2020
South Central Railway							
284	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
South East Central Railway							
285	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
286	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	737.72 -	737.72	104.10	12/2018 -	12/2018
South Eastern Railway							
287	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	268.65	03/2020 -	03/2020
288	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	484.47	12/2021 -	12/2021
289	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.99	12/2021 -	12/2021
290	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	184.26	03/2021 -	03/2021
West Central Railway							

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
291	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
292	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
293	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
	Total		44,948.54 -	58,686.20	10,794.58		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways						
294	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
295	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
296	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
297	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
	National Highways And Infrastructure Development Corporation Ltd.						
298	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
299	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
300	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
301	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
302	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
303	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
304	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]	3/2018	234.27 -	234.27	-	10/2018 -	10/2018
305	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]	2/2018	391.00 -	391.00	-	10/2018 -	10/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
306	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744	3/2015	262.97 -	262.97	-	10/2018 -	10/2018
307	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743	3/2018	417.24 -	417.24	-	05/2018 -	05/2018
308	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742	3/2018	403.36 -	403.36	-	06/2018 -	06/2018
309	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741	3/2018	274.31 -	274.31	-	05/2018 -	05/2018
310	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
311	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
312	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
313	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
314	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
315	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
316	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
317	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
318	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
National Highways Authority Of India							
319	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
320	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	590.82	03/2018 -	03/2018
321	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
322	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
323	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	184.92	06/2018 -	06/2018
324	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
325	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	141.16	06/2018 -	06/2018
326	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
327	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
328	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	23.48	03/2020 -	03/2020
329	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
330	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
331	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
332	CONSTRUCTION OF ROAD APPROACHES TO RAIL- CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
333	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
334	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
335	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
336	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
337	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
338	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
339	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
340	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
341	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
342	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
343	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
344	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
345	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
346	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]	2/2017	904.16 -	904.16	6.00	02/2020 -	02/2020
347	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
348	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
349	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
350	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	247.71	06/2018 -	06/2018
351	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53 -	1,027.53	228.89	06/2018 -	06/2018
352	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
353	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
354	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	796.52	03/2018 -	03/2018
355	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
356	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	814.19	03/2018 -	03/2018
357	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	-	03/2018 -	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
358	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	699.98	03/2018 -	03/2018
	National Highways Development Project						
359	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
360	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
361	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
	Total		49,630.08 -	50,200.26	4,235.03		
	SHIPPING AND PORTS						
	Kamarajar Port Limited						
362	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]	3/2016	600.00 258.00	257.90	1.45	12/2017 05/2020	05/2020
	Total		600.00 -	257.90	1.45		
	STEEL						
	Hindustan Steelwork Construction Limited						
363	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
364	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
	National Mineral Development Corporation (Nmhc)						
365	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	13,876.24	05/2015 10/2018	10/2018
366	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	28.81	06/2020 -	06/2020
	Steel Authority Of India Limited (SAIL)						
367	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	177.21	03/2018 -	03/2018
368	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	38.95	06/2019 -	06/2019
	Total		17,231.06 -	17,231.06	14,341.27		
	TELECOMMUNICATIONS						
	Bharat Sanchar Nigam Limited						
369	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	159.30 -	159.30	-	04/2018 -	04/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
370	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	212.70 -	212.70	-	05/2018 -	05/2018
371	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	167.68 -	167.68	-	04/2018 -	04/2018
372	GUJARAT ACCESS (LOT 1) - [N26000111]	9/2017	171.54 -	171.54	-	05/2018 -	05/2018
373	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	169.45 -	169.45	-	08/2018 -	08/2018
374	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	215.30	-	05/2018 -	05/2018
	Department Of Telecommunication						
375	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	24,664.00	7,642.00	07/2015 04/2020	04/2020
	Total		14,429.97 -	25,759.97	7,642.00		
	URBAN DEVELOPMENT						
	Central Public Works Department						
376	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]	7/2015	154.00 -	154.00	90.76	11/2015 05/2018	05/2018
377	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	1.65	03/2020 -	03/2020
378	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]	1/2018	206.58 -	206.58	-	03/2019 -	03/2019
379	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	-	06/2019 -	06/2019
380	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	-	05/2020 -	05/2020
381	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	5/2016	164.00 -	164.00	85.46	11/2018 05/2018	05/2018
382	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	8/2016	294.00 -	294.00	75.91	04/2019 06/2019	06/2019
383	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	1.66	02/2020 -	02/2020
	Chennai Metro Rail Ltd						
384	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
	Lucknow Metro Rail Corporation Limited						
385	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Nagpur Metro Rail Corporation Ltd</u>						
386	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	3,480.63	03/2018 12/2019	12/2019
	<u>National Building Construcion Corporation Ltd</u>						
387	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,118.00	3,245.00	11/2019 -	11/2019
	Total		25,343.29 -	25,197.29	9,517.84		
	Grand Total		6,51,418.50	7,04,961.54	2,69,885.27		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	ATOMIC ENERGY						
	Bhavini Limited						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00 -	09/2010 -	06/2018	74.69
	Total		3,492.00 -	6,100.00 -			
	CIVIL AVIATION						
	Airport Authority Of India Limited						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53 -	01/2011 -	-	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33 -	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86 -			
	COAL						
	Neyveli Lignite Corporation						
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00 -	06/2017 -	04/2018	11.60
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80 -	11/2021 -	11/2021	.00
	Northern Coal Fields Limited						
6	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57 -	03/2012 -	03/2018	87.58
	Singareni Colliers Company Limited						
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62 -	03/2012 -	03/2023	16.86
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86 -	03/2012 -	03/2019	80.24
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42 -	03/2019 -	03/2019	11.42
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28 -	03/2015 -	03/2020	114.60
	Total		19,411.53 -	20,221.55 -			
	DEFENCE PRODUCTION						
	Goa Shipyard Limited						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
11	CONSTRUCTION WORKS PHASE 4 - [N39000001	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	2.97
12	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.51
	Total		453.64 -	469.04			
	HEALTH AND FAMILY WELFARE						
	Hospital Services Consultancy Corporation Ltd						
13	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	-	13.31
	Total		168.90 -	191.38			
	HEAVY INDUSTRY						
	Natrip Implementation Society						
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	PETROLEUM						
	Hindustan Petroleum Corporation Limited						
15	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	Indian Oil Corporation Limited						
16	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
	Indian Strategic Petroleum Reserves Ltd						
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	Mangalore Refinery And Petrochemicals Limited						
18	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU [N16000255	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	Oil & Natural Gas Corporation Limited						
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
	Oil India Limited						
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
21	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64 -	256.41	12/2016 -	05/2018	12.15
22	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2017	37.72
	Total		6,777.30 -	8,126.94			
	POWER						
	<u>Damodar Valley Corporation</u>						
23	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	-	5.50
24	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	-	4.12
	<u>National Hydro-Electric Power Corporation</u>						
25	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
	<u>National Thermal Power Corporation</u>						
27	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
28	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
29	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
30	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
31	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41
32	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	02/2019	5.91
33	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	03/2018	11.66
34	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
35	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
36	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
	<u>North East Electric Power Corporation</u>						
37	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
38	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	06/2018	30.37
39	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
40	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
41	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28
42	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	06/2018	42.83
Satluj Jal Vidyut Nigam Limited							
43	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
Thdc India Limited							
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,789.61	06/2013 -	11/2020	52.10
45	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	12/2020	165.65
	Total		1,28,465.99 -	1,73,191.91			
RAILWAYS							
Central Railways							
46	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	390.00
47	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	- -	03/2024	120.28
48	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	- -	03/2024	25.04
East Central Railways							
49	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
50	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
51	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
52	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
53	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
54	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	-	252.66
55	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	-	-	72.37
56	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
	East Coast Railway						
57	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	-	06/2021	539.05
58	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,579.27	-	03/2021	132.50
59	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	-	03/2020	52.77
60	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
61	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	-	-	32.26
62	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	-	-	84.98
63	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	-	-	32.80
64	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
	Eastern Railways						
65	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
66	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
67	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	-	-	.14
68	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	-	-	31.33
69	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	-	-	38.00
70	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
71	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	-	-	3.31
72	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	-	-	6.48
73	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
74	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
75	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
76	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
77	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
Metropolitan Rapid Transport Projects							
78	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
79	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	732.89	06/2013 -	03/2017	47.84
80	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
North Central Railway							
81	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
82	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
83	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
84	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
85	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
North East Frontier Railway							
86	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	03/2020	123.75
87	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
88	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
89	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
90	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
91	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
92	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2020	290.00

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
93	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,135.00 -	- -	03/2020	611.67
94	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00 -	03/2015 -	03/2020	252.94
95	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00 -	03/2014 -	03/2020	324.30
96	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00 -	- -	03/2020	27.24
97	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69 -	12/2015 -	03/2020	204.95
98	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00 -	- -	03/2020	71.62
99	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00 -	03/2007 -	04/2016	107.49
100	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00 -	- -	07/2019	130.16
101	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00 -	- -	03/2018	200.33
102	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00 -	- -	03/2019	58.70
103	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00 -	- -	03/2021	46.95
104	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00 -	- -	03/2020	94.45
105	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28 -	- -	-	63.25
106	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00 -	- -	03/2020	171.38
107	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00 -	- -	03/2018	257.63
108	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00 -	- -	03/2019	71.41
109	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93 -	- -	03/2019	62.12
110	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00 -	- -	03/2021	.00
111	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	556.31 -	612.00 -	- -	03/2020	10.01
North Eastern Railway							
112	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05 -	- -	06/2018	88.85
113	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40 -	- -	-	60.34

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
114	HATHUA-BHATNI (N L) (NER) - [N220100319]	04/2005	230.03 -	718.54	-	05/2019	212.37
115	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [N220100256]	04/1999	744.71 -	1,126.79	-	-	51.31
116	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	-	8.10
117	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	-	-	.33
118	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	-	08/2018	10.26
119	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	-	03/2018	142.44
120	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	227.00	-	08/2018	13.64
121	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	-	10/2018	61.80
122	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16
North Western Railway							
123	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	895.00	03/2014	06/2019	37.02
124	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	02/1997	410.08 -	795.01	-	02/2019	93.87
125	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	-	03/2020	14.33
126	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	04/2008	829.74 -	1,143.70	03/2015	12/2019	37.84
127	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	-	03/2019	41.64
128	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	-	-	23.02
129	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	-	10/2018	24.47
130	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	420.08	-	-	-7.88
131	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	-	02/2019	14.35
132	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	-	11/2018	19.86
133	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	-	03/2019	44.16
Northern Railway							
134	JIND-SONEPAT (NL),NR - [N220100280]	01/2004	238.56 -	740.00	03/2012	-	210.19

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
135	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	-	-	25.87
136	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	-	-	117.77
137	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	-	-	57.68
138	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	-	-	369.31
139	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
140	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
141	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
142	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
	Rail Vikas Nigam Ltd.						
143	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.99	- 09/2009	03/2019	293.18
144	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04
145	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	343.00	03/2009 03/2009	12/2017	65.70
146	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26
147	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88
148	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
149	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	03/2019	329.85
150	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
151	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,141.70	12/2012 -	-	275.56
152	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2017	70.82
153	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78
154	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	350.00	- -	03/2018	84.11
155	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
156	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
157	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66 -	- -	12/2020	22.24
158	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,810.00 -	- -	03/2018	120.09
159	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55 -	03/2016 -	12/2017	29.06
160	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67 -	- -	-	9.32
161	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56 -	12/2024 -	12/2024	.00
162	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00 -	03/2019 -	03/2019	5.39
163	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	04/2015	1,765.90 -	1,765.92 -	12/2025 -	12/2025	.00
164	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	4,295.30 -	16,216.00 -	12/2026 -	12/2026	277.53
165	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00 -	03/2020 -	03/2020	15.55
166	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,183.30 -	12/2020 -	12/2020	.00
167	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85 -	12/2020 -	12/2020	.01
	Railway Electrification						
168	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08 -	03/2012 -	-	60.77
	South Central Railway						
169	KOTLALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,120.16 -	- -	03/2021	542.47
170	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00 -	02/2011 -	-	277.85
171	MANOHARABAD-KOTHPALLI NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47 -	- -	03/2022	206.55
172	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00 -	- -	-	108.66
173	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	761.37 -	- -	-	168.52
174	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	1,313.48 -	2,288.70 -	- -	-	74.25
175	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	704.31 -	- -	-	108.69
176	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,050.00 -	2,132.77 -	- -	-	4.04
177	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	607.70 -	01/1999 -	-	94.00

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
178	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.43	02/2009 -	-	488.00
179	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
180	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	458.26	07/2008 -	-	266.61
181	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
	South East Central Railway						
182	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
183	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
	South Eastern Railway						
184	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
185	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
186	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
187	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
188	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
189	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
190	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
191	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
192	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
193	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
194	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	-	41.36
195	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
196	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
197	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	South Western Railway						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
198	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	-	-	97.26
199	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	-	-	651.97
200	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	-	57.65
201	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	-	-	47.93
202	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	-	-	2.29
203	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	-	-	14.14
204	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	-	-	840.53
	Southern Railway						
205	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	-	-	141.40
206	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	-	-	491.45
207	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	-	-	300.71
208	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50	-	-	412.75
209	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	-	-	210.34
210	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	-	-	404.39
211	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	2,815.62	-	-	411.93
212	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	1,105.00	-	-	147.28
213	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	-	-	348.88
214	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	-	-	78.78
215	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	-	-	91.71
216	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	-	-	28.14
217	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	-	-	295.05
218	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	-	-	173.71

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
219	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	-	-	78.83
220	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,800.00	-	-	199.29
221	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	4,131.90	-	-	359.10
	West Central Railway						
222	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	-	03/2021	273.12
223	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
	Western Railway						
224	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
225	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
226	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	844.10	-	-	91.89
	Total		1,11,331.35 -	2,77,486.78			
	ROAD TRANSPORT AND HIGHWAYS						
	Dept Of Road Transport & Highways						
227	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
	Ministry Of Road Transport And Highways						
228	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
	National Highways And Infrastructure Development Corporation Ltd.						
229	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	National Highways Authority Of India						
230	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2018	28.93
231	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75
232	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
233	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2018	68.99
234	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
235	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	04/2018	42.25
236	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
237	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
238	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
239	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
240	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
241	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
242	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
243	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
244	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
245	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
246	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
247	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
248	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
249	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
250	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2018	10.24
251	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
252	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
253	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39
	Public Works Dept Of State						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
254	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
255	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
256	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	.12
257	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	.01
258	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		22,077.61 -	28,716.05			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
259	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	255.00	06/2017 -	-	28.18
260	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	6.97
	<u>Port Trust</u>						
261	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		593.44 -	1,130.98			
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
262	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
263	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Rastriya Ispat Nigam Limited</u>						
264	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	Total		1,261.61 -	1,777.68			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(March 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
265	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	04/2020	84.97
	Total		13,334.00 -	24,664.00			
	URBAN DEVELOPMENT						
	Central Public Works Department						
266	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
267	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.60
268	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	05/2020 -	05/2020	.00
	Chennai Metro Rail Ltd						
269	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	Total		16,553.95 -	21,387.55			
	Grand Total		3,26,263.39	5,68,286.02			

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(March 2018)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
	Bhavini Limited								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,591.34	09/2010 09/2016	06/2018	93	21
	Nuclear Power Corporation Of India Limited								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	11,554.00	12/2015 11/2016	06/2020	54	43
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,147.00	12/2016 03/2017	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	69,728.00	28,425.34				
	CIVIL AVIATION								
	Airport Authority Of India Limited								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	26.44				
	COAL								
	Bharat Coking Coal Limited								
6	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	174.74	05/2014 -	04/2018	47	-
7	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	169.31	04/2014 -	04/2018	48	-
8	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
9	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	280.30	04/2015 -	04/2019	48	-
	Central Coal Fields Limited								
10	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	98.15	03/2012 -	03/2019	84	-
11	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	154.03	03/2012 -	03/2019	84	-
12	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	350.19	03/2016 -	03/2019	36	-
13	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	60	-
14	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	-
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	125.99	07/2012 -	03/2021	104	-

Costing Rs. 150 Crore and above
(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Eastern Coal Fields Limited</u>								
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	343.50	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
17	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	334.77	03/2010 -	03/2018	96	-
18	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	565.86	03/2013 -	03/2019	72	-
19	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	260.71	03/2010 -	03/2019	108	-
20	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	242.14	03/2013 -	03/2019	72	-
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	313.25	03/2017 -	03/2020	36	-
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	219.29	03/2012 -	03/2020	96	-
	<u>Neyveli Lignite Corporation</u>								
23	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU	05/2016	687.28 -	767.00	756.08	06/2017 12/2017	04/2018	10	4
	<u>Northern Coal Fields Limited</u>								
24	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	486.57	410.19	03/2012 -	03/2018	72	-
	<u>Singareni Colliers Company Limited</u>								
25	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	154.52	03/2015 -	03/2018	36	-
26	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72	-
27	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	125.24	06/2015 -	03/2018	33	-
28	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	186.19	03/2012 -	03/2019	84	-
29	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	154.69	03/2016 -	03/2019	36	-
30	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
31	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	.37	03/2015 -	03/2020	60	-
32	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60	-
33	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	137.69	07/2016 -	03/2020	44	-
34	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	437.51	316.06	03/2015 -	03/2021	72	-
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	48.57	03/2012 -	03/2023	132	-
	<u>South-Eastern Coal Fields Limited</u>								
36	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	-
37	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	153.81	03/2016 -	03/2019	36	-

Costing Rs. 150 Crore and above

(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
38	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
39	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	200.64	03/2014 -	03/2020	72	-
	Western Coal Fields Limited								
40	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 409.68	409.68	86.10	03/2023 02/2017	03/2023	0	73
	Total		12,924.33 -	13,807.08	6,888.36				
	STEEL								
	Hindustan Steelwork Construction Limited								
41	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	-
42	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	-
43	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
44	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
45	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	Rastriya Ispat Nigam Limited								
46	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	124.00	07/2018 -	09/2018	2	-
47	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	827.45	12/2017 -	10/2018	10	-
48	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	37.80	08/2018 -	10/2018	2	-
49	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	276.10	09/2018 -	01/2019	4	-
50	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	237.11	10/2016 -	03/2019	29	-
	Steel Authority Of India Limited (Sail)								
51	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,549.96	03/2013 -	06/2018	63	-
52	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	659.52	12/2017 -	11/2018	11	-
53	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	216.70	10/2017 -	12/2018	14	-
54	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,089.04	04/2018 -	02/2019	10	-
	Total		30,588.39 -	30,375.79	24,155.31				

Costing Rs. 150 Crore and above

(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	PETROLEUM								
	Chennai Petroleum Corporation Limited								
55	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	202.35	11/2016 -	06/2018	19	-
	Gas Authority Of India Limited								
56	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	80.23	04/2018 -	07/2018	3	-
	Hindustan Petroleum Corporation Limited								
57	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	492.24	10/2014 03/2018	02/2019	52	11
	Indian Oil Corporation Limited								
58	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	325.27	10/2017 -	03/2019	17	-
	Oil & Natural Gas Corporation Limited								
59	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,188.94	05/2013 03/2018	11/2018	66	8
60	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	95.40	03/2019 -	04/2019	1	-
61	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,729.04	03/2015 03/2018	12/2019	57	21
	Oil India Limited								
62	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	256.41	147.21	12/2016 -	05/2018	17	-
63	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	146.36	03/2017 -	11/2018	20	-
64	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	1.03	01/2019 -	09/2019	8	-
	Total		5,745.66 -	7,253.66	4,408.07				
	POWER								
	Chenab Valley Power Projects [P] Limited								
65	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	895.22	04/2020 -	10/2023	42	-
	National Hydro-Electric Power Corporation								
66	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,684.84	09/2009 -	12/2020	135	-
	National Thermal Power Corporation								
67	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	6,974.42	05/2014 03/2017	02/2019	57	23
68	NPGL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	02/2019	13	-
69	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	-
70	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	3,004.00	1,075.69	11/2019 -	12/2020	13	-

Costing Rs. 150 Crore and above

(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Power Grid Corporation Of India Limited								
71	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,783.00	11/2017 -	04/2018	5	-
72	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	2,225.00	1,346.00	01/2018 -	04/2018	3	-
73	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	848.40	04/2017 03/2018	05/2018	13	2
74	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	137.93	09/2014 09/2017	06/2018	45	9
75	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	156.50	04/2016 12/2017	06/2018	26	6
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	64.90	03/2018 -	06/2018	3	-
77	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,125.00	12/2015 -	06/2018	30	-
78	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,223.54	09/2017 -	09/2018	12	-
79	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	668.80	12/2018 -	12/2019	12	-
80	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	474.57	12/2018 -	12/2019	12	-
	Satluj Jal Vidyut Nigam Limited								
81	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	200.08	11/2017 -	05/2018	6	-
82	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	485.63	12/2016 -	12/2018	24	-
	Thdc India Limited								
83	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	162.82	02/2014 02/2018	03/2019	61	13
84	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,789.61	1,393.67	06/2013 -	11/2020	89	-
85	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,540.27	02/2016 09/2019	12/2020	58	15
	Total		67,824.00 -	85,364.54	45,283.40				
	HEALTH AND FAMILY WELFARE								
	Hospital Services Consultancy Corporation Ltd								

Costing Rs. 150 Crore and above
(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
86	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10	-
87	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13	-
88	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC, PUNJAB	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6	-
89	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16	-
90	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6	-
91	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	21.00	05/2018 -	08/2019	15	-
	Total		1,689.51 -	1,711.99	791.90				
	RAILWAYS								
	East Central Railways								
92	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12	-
	East Coast Railway								
93	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	82.55	03/2021 -	03/2022	12	-
94	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 2,361.74	2,361.74	43.73	03/2021 -	03/2022	12	-
	Eastern Railways								
95	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	-	111
96	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	111
	Metropolitan Rapid Transport Projects								
97	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
98	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
99	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	812.12	03/2004 -	03/2020	192	-
	North Central Railway								
100	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
101	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	-
	North East Frontier Railway								
102	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	5,450.00	5,040.11	04/2008 12/2011	06/2018	122	78

Costing Rs. 150 Crore and above

(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
103	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,040.00	2,879.89	12/2008 -	03/2019	123	-
104	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	9,658.00	7,387.18	03/2011 -	03/2020	108	-
105	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	2,589.60	03/2014 -	03/2020	72	-
106	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	1,951.73	04/2014 -	03/2020	71	-
107	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
108	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	431.96	03/2015 -	03/2020	60	-
	North Western Railway								
109	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	795.01	392.08	- 02/1997	02/2019	-	264
110	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	895.00	694.56	03/2014 -	06/2019	63	-
111	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,143.70	568.36	03/2015 -	12/2019	57	-
	Northern Railway								
112	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	27,946.00	16,131.46	11/2002 -	12/2018	193	-
	Rail Vikas Nigam Ltd.								
113	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	1,030.00	1,029.45	03/2010 -	03/2018	96	-
114	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.50	750.71	03/2016 -	12/2018	33	-
115	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.99	1,130.35	- 09/2009	03/2019	-	114
116	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	1,202.07	523.88	02/2015 -	12/2019	58	-
117	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	388.00	360.26	02/2006 -	12/2019	166	-
118	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,667.23	03/2008 06/2008	03/2020	144	141
119	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,635.74	03/2016 -	12/2020	57	-
	South East Central Railway								
120	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	-
	South Western Railway								
121	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	365.36	- 11/2015	03/2020	-	52
	West Central Railway								

Costing Rs. 150 Crore and above

(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
122	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	<u>Western Railway</u>								
123	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	82.24	03/2012 -	03/2019	84	-
124	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 416.86	385.60	343.13	03/2013 -	03/2020	84	-
	Total		42,271.83 -	1,14,376.72	55,274.67				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
125	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
126	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
127	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
128	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
129	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	<u>National Highways Authority Of India</u>								
130	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112	-
131	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 -	03/2018	117	-
132	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	03/2018	119	-
133	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	03/2018	104	-
134	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76	-
135	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	-
136	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	-
137	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42	-
138	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,952.35	08/2013 -	03/2018	55	-

Costing Rs. 150 Crore and above
(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
139	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	564.39	07/2014 -	03/2018	44	-
140	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	437.90	06/2014 -	03/2018	45	-
141	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49	-
142	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,263.02	06/2012 -	03/2018	69	-
143	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	04/2018	96	-
144	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	-
145	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	-
146	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	05/2018	111	-
147	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	-
148	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	1,375.60	09/2016 -	06/2018	21	-
149	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	261.09	86.28	05/2017 -	06/2018	13	-
150	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19	-
151	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
152	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	383.55	06/2016 -	06/2018	24	-
153	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	173.62	07/2016 -	07/2018	24	-
154	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	1,387.11	769.28	11/2017 -	08/2018	9	-
155	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	09/2018	118	-
156	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	709.00	293.12	09/2017 -	09/2018	12	-
157	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	10/2018	114	-
158	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	-

Costing Rs. 150 Crore and above
(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
159	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	-
160	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	-
161	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	-
162	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12	-
163	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,484.71	08/2016 -	02/2019	30	-
164	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	-
165	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	-
166	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	-
167	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	-	03/2020 -	05/2020	2	-
168	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	67.09	03/2020 -	05/2020	2	-
169	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	10.50	03/2020 -	06/2020	3	-
Public Works Dept Of State									
170	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
Total			33,499.34 -	36,060.12	14,492.21				
SHIPPING AND PORTS									
Mumbai Port Trust									
171	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	413.91	12/2010 -	12/2018	96	-
Total			366.39 -	669.46	413.91				
TELECOMMUNICATIONS									
Mahanagar Telephone Nigam Limited									
172	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9	-

Costing Rs. 150 Crore and above
(March 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		418.26 -	418.26	172.30				
	URBAN DEVELOPMENT								
	Bangalore Metro Rail Corporation Limited								
173	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-
	Central Public Works Department								
174	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 -	03/2018	65	-
175	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	307.50	03/2016 12/2017	04/2018	25	4
176	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	452.35	03/2015 12/2017	04/2018	37	4
177	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	321.00	305.18	09/2016 03/2018	05/2018	20	2
178	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	582.84	12/2015 -	05/2018	29	-
179	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	133.20	08/2016 -	06/2018	22	-
180	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	170.62	149.22	03/2012 -	06/2018	75	-
181	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	337.03	05/2017 02/2018	08/2018	15	6
182	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	142.67	11/2014 -	10/2018	47	-
183	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	-
184	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	40.05	03/2016 -	12/2018	33	-
185	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	56.09	04/2018 -	05/2019	13	-
186	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
187	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	210.53	10/2019 -	03/2020	5	-
188	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	-	06/2017 -	06/2020	36	-

Costing Rs. 150 Crore and above

(March 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Delhi Metro Rail Corporation Ltd</u>								
189	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
190	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
	Total		75,547.01 -	76,266.10	39,456.35				
	Grand Total		3,38,309.33	4,36,473.05	2,19,788.26				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	06/2018	3492	93
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	06/2017	04/2018	687.28	10
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2019	430.45	36
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2018	365.01	33
9	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
10	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2019	258.56	36
11	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
12	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
13	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	04/2018	269.82	48
14	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2018	302.96	96
15	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2019	510.85	36
16	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2019	457.77	72
17	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2020	321.5	72
18	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
19	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2020	207.28	96
20	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2018	209.78	36
22	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	84
23	KISTARAM OCP	SCCL	11/2010	03/2015	03/2020	242.29	60
24	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
25	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2019	198.59	36
26	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2018	181.19	72
27	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
28	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
29	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	04/2018	289.45	47
30	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54
31	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
32	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.4	72
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
37	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
38	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
39	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
40	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
42	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
45	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	03/2018	09/2018	505.58	6
46	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	03/2018	168.9	10
47	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	08/2018	152.95	6
48	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	09/2018	293.65	16
49	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	06/2018	204.44	13

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
51	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9
52	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
53	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
54	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	05/2018	2899.93	12
55	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
56	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
57	SIX PIPELINE REPLACEMENT PROJECT	ONGC	03/2009	01/2017	05/2018	181.02	16
58	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2019	2915	74
59	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	09/2018	2465.15	66
60	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	23
61	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2019	736.65	93
62	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT	OIL	07/2011	03/2017	11/2018	352.56	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AT MADHUBAN						
63	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
64	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	23
65	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076	9
66	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
67	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	12
68	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	05/2018	228.64	17
69	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	06/2018	257.87	19
70	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
71	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	11/2018	861.79	66
72	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2018	2592.17	48
73	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	52

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
74	TALAIPALLI COAL MINING PROJECT	NTPC	09/2015	11/2019	12/2020	3004	13
75	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
76	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12
77	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2018	198.63	45
78	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	03/2018	15166.19	14
79	SOLAPUR STPP	NTPC	03/2012	11/2016	03/2019	9395.18	28
80	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	11846	24
81	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	05/2018	514.2	35
82	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2018	2514.88	30
83	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	09/2018	305.04	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
84	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
85	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	11/2017	05/2018	330	6
86	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	10/2023	8112.12	42
87	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	6
88	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	12532.44	10
89	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	14366.58	20
90	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
91	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	PGCIL	01/2015	03/2018	09/2018	268.8	6
92	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
93	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	06/2019	203.28	23
94	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	09/2018	1272.8	70
95	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	06/2019	522.29	31
96	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	09/2018	155.57	30
97	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
98	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2018	4375.35	81
99	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPSPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	03/2019	5151.37	12
100	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	06/2018	288.49	16
101	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	09/2018	196.58	31
102	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	09/2018	1071.24	12
103	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
104	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	61
105	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353	57
106	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
107	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	05/2018	1479.3	13
108	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	10/2018	307.18	11
109	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	89
110	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	06/2018	955	30
111	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	02/2019	12964.6	13
112	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	02/2019	9750.89	26
113	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2020	3919.59	135
114	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	99
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2018	4824.12	74
116	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	11638.55	21
117	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
118	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2018	2144	66
119	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	32
120	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	06/2018	374.63	26
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	09/2018	539.82	27
122	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2018	2496.9	106
123	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	09/2018	1940.13	48
124	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657	58
125	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	54
126	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	04/2018	573.99	56
127	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	09/2018	297.33	49
128	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	118
129	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	123

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
130	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
131	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
132	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
133	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2021	03/2022	2361.74	12
134	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
135	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
136	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
137	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
138	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	63
139	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
140	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	99
141	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500	122
142	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
143	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733	123
144	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
145	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
146	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
147	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	58
148	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.7	166
149	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.2	96
150	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
151	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINROY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
153	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
155	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
156	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	57
157	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
158	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
159	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2021	03/2022	2499.71	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
160	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
161	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	03/2018	1348.2	49
162	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2018	1266.6	21
163	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2018	1250	60
164	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2018	571	62
165	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2018	2848	49
166	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	03/2018	1410	42
167	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	55
168	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	02/2019	1655.01	30
169	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	04/2018	217.61	96
170	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	07/2018	641.17	24
171	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
172	QUAZIGUND-BANIHAL KM.220.00 TO	NHAI	07/2010	07/2015	03/2019	1987	44

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM.188.00						
173	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2018	671.3	64
174	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2018	374	67
175	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2018	485	64
176	JORBAT - BARAPANI	NHAI	01/2011	01/2014	03/2018	536	50
177	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2018	575	56
178	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	03/2018	702.16	44
179	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108	76
180	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2018	208	119
181	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	03/2018	225	117
182	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2018	942.69	45
183	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	09/2018	709	12
184	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	08/2018	1387.11	9
185	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	12/2018	563.92	12
186	FOUR LANING OF VARANASI BYPASS	NHAI	05/2015	05/2017	06/2018	261.09	13
187	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	06/2018	563.92	19
188	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	05/2018	280	111
189	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	09/2018	167.64	118
190	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	112
191	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	10/2018	200	114
192	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2018	196	104
193	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2018	597	6
194	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
195	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
196	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
197	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
198	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
199	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
200	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
201	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
202	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29
203	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
204	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2018	2858	10
205	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343	29
206	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	06/2018	17265	63
207	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	HSCL	12/2007	06/2016	03/2018	253.92	21
208	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HSCL	05/2015	03/2017	08/2018	189	17
209	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	12/2018	151.33	15
210	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
211	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSCL	02/2014	12/2016	12/2018	787.29	24
212	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	10/2018	15525	41
213	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2018	1154.18	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
214	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2018	1034.01	14
215	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.3	10

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
216	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	MTNL	06/2016	06/2017	03/2018	418.26	9
217	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	04/2020	13334	57

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
218	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
219	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER	CPWD	07/2015	11/2015	05/2018	154	30
220	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
221	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2018	165.23	65
222	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	04/2018	241.33	25
223	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2018	270.83	47
224	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	05/2018	332.72	20
225	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	04/2018	350.02	37
226	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2018	216.69	44
227	NSG AT KOLKATA	CPWD	10/2014	04/2018	05/2019	162.88	13
228	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
229	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	08/2018	388	15
230	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	06/2018	156.57	22
231	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2018	171.86	33
232	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	06/2018	205	75
233	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT	CPWD	07/2012	12/2015	05/2018	884.3	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	LAND ADJOINING PRAGATI MAIDAN						
234	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
235	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	03/2018	38585	24
236	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(MARCH 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6100	2608

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
5	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
8	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
13	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
19	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
21	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
22	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	5725.5	1601.15
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
23	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
24	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
25	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	17435.15	11149.82
26	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
28	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
29	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	534.02	236.69
30	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1337.76	763.77
31	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
32	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4401.9	2744.9
33	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
35	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3789.61	1298.03
36	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
37	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
38	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	14366.58	15164.05	797.47
40	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	12532.44	13740.53	1208.09
41	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8150	3774.65
42	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
43	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
44	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
45	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	514.2	703.1	188.9
46	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
47	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	11846	12739.82	893.82
48	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	15166.19	16934.65	1768.46
49	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
50	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
51	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9142.58	5020.58
52	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4366.64	2053.64
53	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
54	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
55	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9141.97	4387.55
56	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
57	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2333.71	545.3
58	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	9870.51	11148.86	1278.35
59	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	2514.88	3190.27	675.39
60	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	11638.55	12865.92	1227.37

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
62	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	N.A.	36.8	614	577.2
63	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
64	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	920	764.45
65	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02
66	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
67	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2120.16	1790.16
68	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	261.7	388	126.3
69	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	810.78	1928.07	1117.29
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	343	209.59
71	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.07	1018.84
72	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
73	HATHUA-BHATNI (N L) (NER)	NER	04/2005	N.A.	230.03	718.54	488.51
74	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
75	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	412.05	193.86
76	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	470.92	2713.09	2242.17
77	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	4500	3453.12
78	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
79	GUDUR-DURGARAJAPATNAM	SCR	04/2011	N.A.	283.54	761.37	477.83
80	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
81	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
82	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
83	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
85	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1825	1082
86	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
87	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5450	3950
88	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	900.05	1125.89	225.84
89	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
90	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
91	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
92	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	750	283.52
93	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	607.7	294.46
94	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
95	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
96	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	1514.45	1750	235.55
97	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2026	4295.3	16216	11920.7
98	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
99	TRIVANDRUM-KANYAKUMARI DOUBLING	SR	02/2015	N.A.	900	4131.9	3231.9
100	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
101	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
102	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	03/2021	701.61	810.02	108.41
103	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
104	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
105	VIJAYAWADA-GUDUR	RVNL	04/2015	N.A.	3246.26	3548.67	302.41
106	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	854	1035.16	181.16

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	1876	2081.27	205.27
108	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	2326	2449.91	123.91
109	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
110	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	N.A.	2750	3438.51	688.51
111	PUNE-NASIK (265 KM)	CR	02/2016	N.A.	2425	5341.68	2916.68
112	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
113	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	1800	1198.57
114	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
115	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	398.93	152.86
116	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	535	222.88
117	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	523.17	1871	1347.83
118	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
119	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
120	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
121	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
122	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
123	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
124	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
125	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	283.55	450	166.45
126	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	630	420.23
127	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	580	328
128	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1857	962
129	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1810	987.61
131	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
132	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
133	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
134	ATTIPPATTU PUTTUR	SR	04/2008	N.A.	446.87	1105	658.13
135	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
136	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
137	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
138	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
139	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
140	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
141	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
142	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
143	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
144	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
145	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
146	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	N.A.	242.09	349	106.91
147	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
148	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2562.27	479.52
149	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	N.A.	1266.89	1548.66	281.77
150	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	858.96	538.3
151	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	844.1	404.22
152	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
154	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	246.08	348.55	102.47
155	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	477.31	182.31
156	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	474.3	278.66
157	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	450	2100	1650
158	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	N.A.	410.08	795.01	384.93
159	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
160	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
161	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
162	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
163	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
164	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
165	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	2135	1835
166	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	2815.62	2265.62
167	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.97	195.96
168	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
169	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1143.7	313.96
170	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1579.27	900
171	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	1389.62	2446.85	1057.23
172	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
173	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	227	2135	1908
174	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	194.07	583.02	388.95
175	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
176	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
177	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
178	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	458.26	333.26
179	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	350	159.9
180	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
181	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	525	306.76
182	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	155.74	966.43	810.69
183	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
184	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	555	230.1
185	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	1141.7	837.7
186	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
187	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27946	25446
189	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	780	580
190	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	732.89	237.15
191	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44
192	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
193	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	3040	2307
194	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
195	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
196	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
197	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
198	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
199	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	704.31	366.82
200	NADIKUDE-SRI KALAHASTI	SCR	04/2011	N.A.	1313.48	2288.7	975.22
201	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
202	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
203	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
204	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
205	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
206	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
207	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
208	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
209	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	2300	1844
210	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
211	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
212	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	1030	342.8
213	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
214	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
215	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
216	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	3168.29	2668.99
217	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
218	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	895	241.81
219	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
220	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	350	257.37
221	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
222	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24
223	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
224	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.99	884.35
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
225	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
226	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
227	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
228	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
229	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
230	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
231	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
232	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
233	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
234	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
235	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
236	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
237	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
238	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
239	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
241	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	TERMINAL ON BOT BASIS IN MUMB						
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
242	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCCL	05/2005	02/2014	768.88	1113.34	344.46
243	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
244	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
245	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108
246	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
247	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
248	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	350.02	479.87	129.85
249	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	06/2018	3492.00	6100.00	2608	93

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	349.28	186.52	60
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.40	486.57	227.17	72
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	448.86	199.83	84

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	5245.96	657.67	9
8	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	723.40	413.59	52
9	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	11/2018	861.79	1256.72	394.93	66
10	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57
11	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076.00	4190.00	1114	9
12	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
13	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	5725.50	1601.15	23
14	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	106.78	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
16	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9141.97	4387.55	12
17	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL-KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2333.71	545.3	12
18	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2018	2514.88	3190.27	675.39	30
19	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	1,5095.67	6402.7	123
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	09/2018	297.33	534.02	236.69	49
21	BRBCL-NABINAGAR TPP- JV (4X250 Mw)	NTPC	01/2007	05/2014	02/2019	5353.00	7998.00	2645	57
22	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	602.44	165.76	24
23	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	3789.61	1298.03	89
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2018	2496.90	6179.96	3683.06	106
25	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	09/2018	1940.13	2702.65	762.52	48
26	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657.00	4401.90	2744.9	58
27	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	639.46	151.97	54
28	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	04/2018	573.99	1337.76	763.77	56
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	408.03	118
30	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	738.48	260.79	99

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2018	4824.12	5071.94	247.82	74
32	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	3846.30	867.82	93
33	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2018	4375.35	8150.00	3774.65	81
34	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	1,2532.44	1,3740.53	1208.09	10
35	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	1,4366.58	1,5164.05	797.47	20
36	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	09/2018	1272.80	1731.10	458.3	70
37	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	1,1846.00	1,2739.82	893.82	24
38	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	03/2018	1,5166.19	1,6934.65	1768.46	14
39	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	05/2018	514.20	703.10	188.9	35
40	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	06/2018	955.00	1364.00	409	30
41	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	02/2019	1,2964.60	1,3731.26	766.66	13
42	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2020	3919.59	8398.75	4479.16	135
43	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	1,1638.55	1,2865.92	1227.37	21
44	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,3762.80	2632.61	103
45	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2018	2144.00	2932.88	788.88	66
46	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	1891.41	526.89	32

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2018)

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
48	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	1143.70	313.96	57
49	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
50	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34
51	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	4259.48	307.5	57
52	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
53	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
54	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	8930.44	108
55	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
56	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1082	144
57	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	895.00	241.81	63
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
59	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
60	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5450.00	3950	122
61	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
62	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733.00	3040.00	2307	123
63	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	2150	60
64	SUKINDA ROAD - ANGUL	RVNL	04/1998	02/2015	12/2019	183.23	1202.07	1018.84	58

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	(NL)(ECOR)								
65	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.70	388.00	126.3	166
66	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.20	1030.00	342.8	96
67	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
68	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	2,7946.00	25446	193

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
69	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2018	196.00	331.23	135.23	104
70	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108.00	2288.00	1180	76
71	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	280.13	125.09	112

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
72	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
73	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343.00	488.40	145.4	29

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
74	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	04/2020	1,3334.00	2,4664.00	11330	57

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MARCH 2018)

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
75	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
76	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	04/2018	241.33	349.33	108	25
77	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	04/2018	350.02	479.87	129.85	37

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(March 2018)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	ROAD TRANSPORT AND HIGHWAYS							
	National Highways Authority Of India							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	12/2017	.00	47
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	07/2017	.00	50
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	10/2017	.00	53
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2018	.00	67
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2018	.00	64
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	08/2017	.00	87
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2017	.00	49
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	-	.00	0
10	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	03/2018	.00	50
11	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00 -	567.00	11/2013 -	-	.00	0
12	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2018	.00	62
13	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2017	.00	42
14	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	03/2018	.00	56
15	DEOLI KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	10/2017	.00	51
16	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
17	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2017	.00	64

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (March 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	-	.00	0
19	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR PPP (BOT) - [N24000586]	06/2016	637.18	637.18	06/2019	-	.00	0
20	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00	650.00	11/2013	08/2017	.00	45
21	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00	664.00	02/2014	-	.00	0
22	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	06/2018	.00	64
23	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16	702.16	07/2014	03/2018	.00	44
24	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	11/2017	.00	56
25	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	06/2019	.00	0
26	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	04/2018	.00	0
27	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36	830.36	07/2018	07/2018	.00	0
28	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	11/2017	.00	12
29	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	-	.00	0
30	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	01/2018	.00	6
31	4-LANING OF BRAHMAPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	03/2018	.00	55
32	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00	1,046.00	09/2013	10/2017	.00	49
33	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	12/2017	.00	42
34	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	12/2017	.00	52
35	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	12/2017	.00	42
36	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	08/2017	.00	48
37	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,206.10	04/2013	09/2017	2.65	53
38	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	12/2018	.00	60

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (March 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 (BOT) - [N24000233] - PPP	04/2014	1,266.60	1,266.60	09/2016	06/2018	.00	21
40	MURADABAD-BAREILY - PPP (BOT) - [N24000154]	04/2010	1,267.00	1,267.00	06/2013	09/2017	.00	51
41	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	03/2018	.00	49
42	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	-	08/2018	.00	0
43	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00	1,393.00	-	01/2018	.00	0
44	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	12/2017	.00	39
45	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	03/2018	.00	42
46	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	12/2017	.00	30
47	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	06/2017	.00	37
48	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	10/2017	.00	25
49	FOUR LANING OF BIAORA-DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	-	01/2019	.00	0
50	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00	1,585.00	05/2013	12/2017	.00	55
51	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	09/2017	51.83	22
52	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	02/2019	.00	30
53	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	-	01/2019	.00	0
54	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	-	.00	0
55	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	12/2017	.00	74
56	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	09/2017	.00	73
57	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	12/2017	.00	57
58	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	11/2017	.00	52
59	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	01/2018	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (March 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
60	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	02/2018	.00	15
61	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	1,928.22	04/2015 -	12/2017	.00	32
62	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	03/2019	.00	44
63	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	07/2017	.00	19
64	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	- -	04/2019	.00	0
65	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	-	.00	0
66	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50	76
67	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	- -	05/2019	.00	0
68	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	12/2017	.00	40
69	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	04/2018	.00	49
70	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56	63
	Total		81,844.48 -	85,331.12				
	SHIPPING AND PORTS							
	Kamarajar Port Limited							
71	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94 -	255.00	06/2017 -	-	28.18	0
72	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88	0
	Mumbai Port Trust							
73	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		809.83 -	1,200.44				
	Grand Total		82,654.31	86,531.56				

Details of Central Sector Projects Costing Rs.150 crore and above (as on					31.03.2018)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	A & N ISLANDS				
	Road Transport And Highways				
1	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [12/2017]	409.85 (-) [409.85]	0.00 (0.00) [0]
2	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [4/2017]	277.17 (-) [277.17]	0.00 (0.00) [0]
3	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [10/2018]	262.97 (-) [262.97]	0.00 (0.00) [0]
4	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [10/2018]	391.00 (-) [391.00]	0.00 (0.00) [0]
5	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [10/2018]	234.27 (-) [234.27]	0.00 (0.00) [0]
	ANDAMAN & NICOBAR ISLANDS				
	Civil Aviation				
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	26.44 (126.72) [21]
	ANDHRA PRADESH				
	Health And Family Welfare				
7	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2019]	272.19 (-) [272.19]	24.38 (0.00) [0]
	Petroleum				
8	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
9	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2021]	384.58 (-) [384.58]	14.08 (0.00) [0]
10	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (9/2018) [9/2018]	420.76 (207.80) [207.80]	0.00 (-212.96) [0]
11	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (6/2020) [6/2020]	34,012.00 (-) [34,012.00]	262.74 (0.00) [0]
12	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
13	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	540.49 (0.00) [0]
14	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	95.26 (0.00) [0]

			[9/2019]	[407.00]	[0]
	Power				
15	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS	1/2016	7/2018 (-) [3/2018]	207.88 (-) [207.88]	111.50 (0.00) [-4]
	Railways				
16	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [829.00]	0.94 (0.00) [0]
17	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.07 (0.00) [0]
18	GUDUR-DURGARAJPATNAM	4/2011	/ (-) [0/0]	283.54 (-) [761.37]	0.51 (477.83) [0]
19	GUNTUR-GUNTAKAL	4/2016	/ (-) [0/0]	4,000.00 (-) [3,631.00]	51.21 (-369.00) [0]
20	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	/ (-) [3/2021]	330.00 (-) [2,120.16]	249.90 (1,790.16) [-]
21	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2021 (-) [3/2022]	2,499.71 (2,499.71) [2,499.71]	82.55 (0.00) [12]
22	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [3/2019]	234.50 (-) [234.50]	0.39 (0.00) [0]
23	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [3/2018]	387.70 (-) [387.70]	385.63 (0.00) [0]
24	NADIKUDE-SRI KALAHASTI	4/2011	/ (-) [0/0]	1,313.48 (-) [2,288.70]	257.84 (975.22) [0]
25	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	155.74 (164.36) [966.43]	975.05 (810.69) [0]
26	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	7/2006	3/2008 (6/2008) [3/2020]	743.00 (-) [1,825.00]	1,667.23 (1,082.00) [144]
27	VIJAYAWADA-GUDUR	4/2015	/ (-) [0/0]	3,246.26 (-) [3,548.67]	52.05 (302.41) [0]
28	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	/ (-) [3/2020]	1,503.71 (-) [1,503.71]	641.47 (0.00) [-]
	Road Transport And Highways				
29	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	0.00 (0.00) [0]
30	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
31	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	5/2013 (-) [12/2017]	1,585.00 (-) [1,585.00]	0.00 (0.00) [0]
32	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [11/2015]	333.21 (-) [333.21]	0.00 (0.00) [0]
33	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [12/2016]	333.21 (333.21) [333.21]	0.00 (0.00) [0]

34	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [12/2016]	333.21 (-) [333.21]	0.00 (0.00) [0]
35	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [0/0]	648.33 (-) [648.33]	0.00 (0.00) [0]
36	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	/ (-) [11/2018]	1,134.97 (-) [1,134.97]	0.00 (0.00) [-]
37	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	10/2015	/ (-) [0/0]	480.21 (-) [480.21]	0.00 (0.00) [0]
38	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR	7/2015	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
39	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A	12/2014	2/2015 (-) [0/0]	201.12 (201.00) [201.12]	0.00 (0.00) [0]
40	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC	1/2014	7/2014 (-) [0/0]	361.30 (-) [207.40]	44.08 (-153.90) [0]
41	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	2/2015	5/2015 (-) [5/2017]	224.83 (-) [224.83]	0.00 (0.00) [0]
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [11/2016]	195.45 (-) [195.45]	0.00 (0.00) [0]
43	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	2/2014	11/2014 (-) [11/2016]	170.21 (-) [170.21]	5.65 (0.00) [0]
44	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	3/2015	/ (-) [0/0]	175.03 (-) [175.00]	0.00 (-0.03) [0]
45	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION)	2/2015	2/2017 (-) [2/2017]	241.61 (-) [241.61]	7.71 (0.00) [0]
46	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	2/2015	4/2015 (-) [5/2016]	224.83 (-) [224.83]	0.00 (0.00) [0]
47	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (-) [10/2017]	271.45 (-) [271.45]	0.00 (0.00) [0]
48	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [3/2020]	648.32 (-) [503.10]	15.10 (-145.22) [0]
49	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	2/2015	/ (-) [0/0]	266.00 (-) [266.00]	0.00 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	3/2015	9/2015 (-) [8/2017]	309.01 (-) [309.01]	0.00 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	2/2014	7/2014 (-) [7/2016]	258.99 (-) [258.99]	16.54 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	2/2014	6/2014 (-) [6/2016]	417.61 (-) [417.61]	0.00 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	11/2014	2/2017 (-) [2/2017]	297.78 (330.00) [330.00]	0.00 (32.22) [0]
54	REHABILITATION UPGRADATION OF NH-67 FROM KM	7/2014	2/2015	251.55	7.74

	641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC		(-) [2/2017]	(-) [251.55]	(0.00) [0]
55	SIX LANNING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/	1,323.15	0.00
			(-) [0/0]	(-) [1,323.15]	(0.00) [0]
56	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014	1,535.00	0.00
			(-) [6/2017]	(-) [1,535.00]	(0.00) [0]
57	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020	1,041.62	0.00
			(-) [5/2020]	(-) [1,187.10]	(145.48) [2]
58	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013	571.00	582.52
			(-) [12/2018]	(-) [571.00]	(0.00) [62]
59	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017	1,684.00	54.13
			(-) [2/2017]	(-) [1,684.00]	(0.00) [0]
	Steel				
60	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	7/2015	7/2018	465.85	124.00
			(-) [9/2018]	(-) [465.85]	(0.00) [2]
61	CENTRAL DISPATCH YARD	8/2015	8/2018	320.66	37.80
			(-) [10/2018]	(-) [320.66]	(0.00) [2]
62	COKE OVEN BATTERY-5	12/2011	12/2017	2,858.00	827.45
			(-) [10/2018]	(-) [2,500.00]	(-358.00) [10]
63	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	1/1999	232.00	0.00
			(-) [0/0]	(-) [232.00]	(0.00) [0]
64	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	343.00	237.11
			(-) [3/2019]	(-) [488.40]	(145.40) [29]
	Urban Development				
65	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019	206.58	0.00
			(-) [3/2019]	(-) [206.58]	(0.00) [0]
66	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017	157.84	120.56
			(-) [0/0]	(-) [157.84]	(0.00) [0]
67	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/	246.90	0.00
			(-) [0/0]	(-) [246.90]	(0.00) [0]
	ARUNACHAL PRADESH				
	Petroleum				
68	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019	247.52	130.07
			(-) [12/2018]	(-) [247.52]	(0.00) [-2]
	Power				
69	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	2,496.90	6,424.41
			(10/2018) [10/2018]	(6,179.96) [6,179.96]	(3,683.06) [106]
70	PARE HYDRO ELECTRIC PROJECT	12/2008	8/2013	573.99	1,621.16
			(4/2018) [4/2018]	(1,337.76) [1,337.76]	(763.77) [56]
71	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010	6,285.33	9,979.37
			(-) [0/0]	(-) [17,435.15]	(11,149.82) [0]
	Road Transport And Highways				
72	2 LANNING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018	394.00	0.00
			(-)	(-)	(0.00)

			[6/2018]	[394.00]	[0]
73	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [5/2018]	235.08 (-) [235.08]	47.81 (0.00) [0]
74	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59)	3/2015	5/2018 (-) [5/2018]	194.11 (-) [194.11]	30.54 (0.00) [0]
75	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
76	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450)	1/2016	11/2016 (-) [11/2016]	183.65 (-) [183.65]	0.00 (0.00) [0]
77	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
78	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
79	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2016]	198.00 (-) [198.00]	0.00 (0.00) [0]
80	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	38.50 (0.00) [0]
81	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
82	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
83	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]
84	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
85	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [6/2016]	334.22 (-) [334.22]	0.00 (0.00) [0]
86	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]
87	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
88	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
89	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
90	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
91	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
92	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]

93	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [9/2010]	165.00 (-) [165.00]	0.00 (0.00) [0]
94	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
95	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
96	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
97	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
98	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [9/2010]	104.00 (-) [201.00]	0.00 (97.00) [0]
ASSAM					
Health And Family Welfare					
99	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
Petroleum					
100	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (9/2018) [9/2018]	2,465.15 (-) [2,378.89]	2,073.06 (-86.26) [66]
101	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	1.03 (0.00) [8]
102	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	13.34 (127.41) [70]
103	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	112.81 (0.00) [0]
104	DIESEL HYDROTREATOR	7/2015	1/2018 (-) [0/0]	1,031.37 (-) [1,031.37]	305.91 (0.00) [0]
105	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	480.79 (0.00) [0]
106	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	24.69 (-5.15) [0]
107	TWENTY NOS. FEEDER GAS LINES	3/2009	12/2016 (-) [5/2018]	228.64 (-) [256.41]	147.21 (27.77) [17]
108	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [11/2017]	871.35 (-) [1,200.00]	961.00 (328.65) [0]
Power					
109	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [6/2018]	4,375.35 (8,150.00) [8,150.00]	7,057.00 (3,774.65) [81]
Railways					
110	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	/ (-) [3/2019]	312.12 (-) [535.00]	569.93 (222.88) [-]
111	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	/ (-)	2,232.32 (-)	143.70 (-0.32)

			[3/2022]	[2,232.00]	[-]
112	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	9/1997	4/2008 (12/2011) [6/2018]	1,500.00 (-) [5,450.00]	5,040.11 (3,950.00) [122]
113	DIGARU-HOJAI (102 KM)	4/2015	/ (-) [3/2021]	870.96 (-) [871.00]	74.06 (0.04) [-]
114	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	/ (-) [3/2019]	246.07 (-) [398.93]	172.40 (152.86) [-]
115	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	/ (-) [3/2020]	200.00 (-) [780.00]	466.47 (580.00) [-]
Road Transport And Highways					
116	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [5/2017]	268.08 (-) [268.08]	0.00 (0.00) [0]
117	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [2/2011]	470.20 (-) [470.20]	0.00 (0.00) [0]
118	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [12/2018]	225.02 (-) [159.20]	0.00 (-65.82) [0]
119	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [6/2018]	223.30 (-) [223.30]	0.00 (0.00) [0]
120	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
121	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [11/2018]	588.95 (-) [588.95]	80.00 (0.00) [0]
122	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2018]	289.99 (-) [289.99]	0.00 (0.00) [0]
123	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [1/2016]	252.00 (-) [252.00]	0.00 (0.00) [0]
124	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [6/2018]	437.39 (-) [437.39]	21.86 (0.00) [0]
125	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [1/2016]	294.17 (-) [294.17]	0.00 (0.00) [0]
126	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [4/2018]	217.61 (-) [309.56]	0.00 (91.95) [96]
127	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [2/2018]	160.00 (-) [160.00]	0.00 (0.00) [0]
128	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
129	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2018]	168.39 (-) [168.39]	16.84 (0.00) [0]
130	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [6/2018]	463.49 (-) [463.49]	9.26 (0.00) [0]
131	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200	5/2015	5/2018 (-)	454.89 (-)	22.74 (0.00)

	TO KM		[5/2018]	[454.89]	[0]
132	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [5/2018]	280.00 (-) [361.00]	0.00 (81.00) [111]
133	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [3/2018]	196.00 (-) [331.23]	0.00 (135.23) [104]
134	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [3/2018]	155.04 (-) [280.13]	0.00 (125.09) [112]
135	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [12/2017]	199.81 (-) [385.13]	0.00 (185.32) [0]
136	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	0.00 (0.00) [118]
137	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	4/2009 (-) [10/2018]	200.00 (-) [200.00]	0.00 (0.00) [114]
138	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2018]	208.00 (-) [208.00]	0.00 (0.00) [119]
139	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [3/2018]	225.00 (-) [225.00]	0.00 (0.00) [117]
140	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [11/2017]	245.00 (-) [245.00]	0.00 (0.00) [0]
141	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [2/2018]	176.22 (-) [176.22]	0.00 (0.00) [0]
142	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [2/2018]	218.31 (-) [218.31]	0.00 (0.00) [0]
	BIHAR				
	Petroleum				
143	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	240.69 (0.00) [-10]
144	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [11/2018]	822.66 (-) [822.66]	529.80 (0.00) [0]
145	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [6/2020]	324.00 (-) [324.00]	55.39 (0.00) [0]
	Power				
146	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS	4/2016	6/2019 (-) [6/2019]	790.13 (-) [790.30]	368.70 (0.17) [0]
147	BARH STPP(3X660MW) NTPC	2/2005	1/2011 (4/2021) [4/2021]	8,692.97 (15,095.67) [15,095.67]	14,520.00 (6,402.70) [123]
148	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	5/2014 (3/2017) [2/2019]	5,353.00 (-) [7,998.00]	6,974.42 (2,645.00) [57]
149	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	1/2018 (-) [2/2019]	12,964.60 (-) [13,731.26]	10,084.21 (766.66) [13]
150	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	5/2015	12/2016 (-) [12/2018]	436.68 (-) [602.44]	485.63 (165.76) [24]

	Railways				
151	ARA-BHABHUA ROAD (NL)	4/2008	/	490.80	0.39
			(-)	(-)	(0.00)
			[0/0]	[490.80]	[0]
152	ARARIA-SUPAUL (NL)	4/2008	/	304.41	0.19
			(-)	(-)	(0.00)
			[0/0]	[304.41]	[0]
153	BIHTA-AURANGABAD (NL)	4/2008	/	326.20	1.68
			(-)	(-)	(0.00)
			[0/0]	[326.20]	[0]
154	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/	285.07	111.71
			(-)	(-)	(93.49)
			[0/0]	[378.56]	[0]
155	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/	406.92	200.00
			(-)	(-)	(-67.92)
			[0/0]	[339.00]	[0]
156	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-)	(-)	(0.00)
			[0/0]	[205.00]	[0]
157	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	0.00
			(-)	(-)	(0.00)
			[0/0]	[445.25]	[0]
158	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	13.00
			(-)	(-)	(154.16)
			[0/0]	[367.17]	[0]
159	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	330.82
			(-)	(-)	(-203.99)
			[0/0]	[324.66]	[0]
160	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	501.69	876.49
			(-)	(335.77)	(541.87)
			[0/0]	[1,043.56]	[0]
161	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	/	470.00	40.00
			(-)	(-)	(0.00)
			[0/0]	[470.00]	[0]
162	KATIHAR - JOGBANI (GC)(NEFR)	9/2001	12/2010	492.98	921.03
			(-)	(-)	(827.02)
			[0/0]	[1,320.00]	[0]
163	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	183.72
			(-)	(-)	(378.13)
			[0/0]	[541.00]	[0]
164	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	282.92	3.13
			(-)	(-)	(77.08)
			[3/2020]	[360.00]	[-]
165	KIUL - GAYA DOUBLING PROJECT	12/2015	12/2020	1,200.20	0.00
			(-)	(-)	(0.00)
			[12/2020]	[1,200.20]	[0]
166	KOSI BRIDGE (NL), ECR	4/2002	3/2012	322.95	320.39
			(-)	(-)	(18.46)
			[0/0]	[341.41]	[0]
167	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.38
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
168	MAHARAJGANJ-MASRAKH (NL) - NER	4/2003	/	218.19	350.14
			(-)	(-)	(193.86)
			[6/2018]	[412.05]	[-]
169	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	332.92	495.40
			(-)	(283.95)	(144.96)
			[0/0]	[477.88]	[0]
170	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	4.41
			(-)	(-)	(715.09)
			[0/0]	[926.09]	[0]

171	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.58
			(-)	(-)	(0.00)
			[0/0]	[281.30]	[0]
172	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.52
			(-)	(-)	(0.00)
			[0/0]	[228.05]	[0]
173	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	538.21
			(-)	(-)	(227.76)
			[0/0]	[559.91]	[0]
174	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.00
			(-)	(-)	(0.00)
			[0/0]	[620.57]	[0]
175	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	/	300.00	922.41
			(-)	(-)	(1,835.00)
			[3/2020]	[2,135.00]	[-]
176	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	12/2020	1,491.47	0.00
			(-)	(-)	(0.00)
			[12/2020]	[1,491.47]	[0]
177	SAKRI-HASANPUR ROAD (NL)	4/1999	/	175.69	253.10
			(-)	(-)	(149.31)
			[0/0]	[325.00]	[0]
178	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	283.44
			(-)	(-)	(-16.33)
			[0/0]	[355.81]	[0]
179	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[380.00]	[0]
180	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.17
			(-)	(-)	(1,714.61)
			[0/0]	[2,393.23]	[0]
	Road Transport And Highways				
181	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013	351.54	0.00
			(-)	(-)	(0.00)
			[10/2017]	[351.54]	[0]
182	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	0.00
			(-)	(-)	(0.00)
			[12/2017]	[511.54]	[0]
183	2-LANNING WITH PS KHAGARIA-PURNEA	5/2011	2/2014	664.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[664.00]	[0]
184	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	0.00
			(-)	(-)	(0.00)
			[0/0]	[375.09]	[0]
185	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	0.00
			(-)	(-)	(0.00)
			[3/2018]	[575.00]	[56]
186	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	0.00
			(-)	(-)	(0.00)
			[0/0]	[581.84]	[0]
187	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015	288.24	0.00
			(-)	(-)	(0.00)
			[0/0]	[288.24]	[0]
188	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,598.00]	[0]
189	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020	235.48	0.00
			(-)	(-)	(-7.71)
			[3/2020]	[227.77]	[0]
190	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016	683.83	0.00
			(-)	(-)	(0.00)
			[0/0]	[683.83]	[0]

191	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [553.30]	0.00 (0.00) [0]
192	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	0.00 (0.00) [0]
193	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [6/2016]	369.77 (-) [369.77]	0.00 (0.00) [0]
194	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [0/0]	1,167.45 (-) [1,167.45]	0.00 (0.00) [0]
195	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [0/0]	642.41 (-) [642.41]	0.00 (0.00) [0]
196	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	/ (-) [4/2018]	322.09 (-) [322.09]	0.00 (0.00) [-]
197	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	0.00 (0.00) [0]
198	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [0/0]	814.04 (-) [814.04]	0.00 (0.00) [0]
199	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
200	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	/ (-) [4/2019]	1,041.10 (-) [1,041.10]	0.00 (0.00) [-]
201	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [9/2017]	574.00 (-) [574.00]	0.00 (0.00) [0]
202	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [6/2018]	671.30 (-) [671.30]	0.00 (0.00) [64]
203	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [12/2016]	1,742.01 (-) [1,742.01]	0.00 (0.00) [0]
204	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
205	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2014	3/2014 (-) [0/0]	377.64 (-) [377.64]	0.00 (0.00) [0]
206	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [8/2014]	278.39 (-) [278.39]	0.00 (0.00) [0]
207	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
208	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [319.68]	0.00 (0.00) [0]
209	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
210	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [8/2016]	282.41 (-) [282.41]	67.52 (0.00) [0]
211	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE	1/2013	8/2014	322.01	0.00

	WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG		(-) [0/0]	(-) [322.01]	(0.00) [0]
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [10/2016]	358.22 (-) [358.22]	188.71 (0.00) [0]
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	0.00 (0.00) [0]
214	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
215	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
216	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [0/0]	950.64 (-) [950.64]	0.00 (0.00) [0]
217	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV	3/2015	7/2016 (-) [10/2016]	206.80 (-) [206.80]	0.00 (0.00) [0]
218	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	/ (-) [4/2019]	399.54 (-) [399.54]	0.00 (0.00) [-]
219	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [12/2017]	854.80 (-) [854.80]	0.00 (0.00) [0]
220	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	/ (-) [4/2018]	516.13 (-) [516.13]	0.00 (0.00) [-]
221	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
	Steel				
222	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	Urban Development				
223	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [6/2020]	496.18 (496.00) [498.99]	0.00 (2.81) [36]
	CHHATISGARH				
	Coal				
224	AMERA OC RCE	2/2015	3/2018 (-) [3/2018]	335.97 (-) [335.97]	50.54 (0.00) [0]
225	AMGAON OPENCASST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	44.19 (0.00) [0]
226	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016 (-) [3/2019]	198.59 (-) [198.59]	169.49 (0.00) [36]
227	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2019]	258.56 (-) [258.56]	153.81 (0.00) [36]
228	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	51.22 (0.00) [0]
229	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	31.90 (0.00) [0]
230	DURGAPUR OPENCASST PROJECT	2/2015	3/2023	916.24	0.99

			(-) [3/2023]	(-) [916.24]	(0.00) [0]
231	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,668.79 (0.00) [0]
232	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2020]	152.43 (459.49) [459.49]	137.98 (307.06) [60]
233	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	5.16 (0.00) [72]
234	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	1,698.30 (0.00) [0]
235	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
236	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2020]	321.50 (-) [321.50]	200.64 (0.00) [72]
237	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	5.79 (0.00) [0]
238	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
239	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	0.00 (0.00) [0]
	<u>Power</u>				
240	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	6/2017 (6/2019) [6/2019]	11,846.00 (-) [12,739.82]	9,555.00 (893.82) [24]
241	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [12/2020]	3,004.00 (-) [3,004.00]	1,075.69 (0.00) [13]
	<u>Railways</u>				
242	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL	4/1995	12/2012 (-) [0/0]	304.00 (-) [1,141.70]	560.21 (837.70) [0]
243	KIRANDUL - JAGDALPUR DOUBLING	12/2012	/ (-) [3/2020]	826.57 (1,160.83) [1,160.83]	516.08 (334.26) [-]
244	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [3/2018]	207.00 (-) [207.00]	152.90 (0.00) [0]
245	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [3/2020]	758.09 (-) [758.09]	730.03 (0.00) [0]
246	SALKA ROAD -ANUPNAGAR LINE DOUBLING	9/2006	3/2010 (-) [12/2017]	324.90 (-) [555.00]	517.35 (230.10) [0]
	<u>Road Transport And Highways</u>				
247	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700- 292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-	12/2010	12/2012 (-) [0/0]	169.26 (-) [169.26]	0.00 (0.00) [0]
248	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	/ (-) [4/2018]	726.67 (-) [726.67]	0.00 (0.00) [-]
249	FOUR LANING OF ORISSA/CHATTISGARH BORDER -	2/2013	8/2015	1,232.00	0.00

	AURANG SECTION		(-) [12/2017]	(-) [1,232.00]	(0.00) [0]
250	FOUR LANING OF SARAGAON - BILASPUR	12/2015	/	509.13	0.00
			(-) [4/2018]	(-) [509.13]	(0.00) [-]
251	FOUR LANING OF SIMGA - SARAGAON	12/2015	/	596.67	0.00
			(-) [5/2018]	(-) [596.67]	(0.00) [-]
252	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION.	10/2014	3/2015	213.47	0.00
			(-) [3/2015]	(-) [213.47]	(0.00) [0]
253	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/	291.05	0.00
			(-) [0/0]	(-) [291.05]	(0.00) [0]
254	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION.	12/2014	/	394.20	0.00
			(-) [0/0]	(-) [394.20]	(0.00) [0]
255	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015	485.44	0.00
			(-) [0/0]	(-) [485.44]	(0.00) [0]
256	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV	10/2014	3/2015	298.34	0.00
			(-) [3/2015]	(-) [298.34]	(0.00) [0]
257	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I	11/2014	3/2015	262.54	0.00
			(-) [0/0]	(-) [262.54]	(0.00) [0]
258	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	3/2015	/	422.34	22.25
			(-) [0/0]	(-) [422.34]	(0.00) [0]
	Steel				
259	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	6/2020	818.00	28.81
			(-) [6/2020]	(-) [818.00]	(0.00) [0]
260	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	4/2015	188.93	119.94
			(-) [0/0]	(-) [188.93]	(0.00) [0]
261	EXPANSION OF BHILAI STEEL PLANT	8/2010	3/2013	17,265.00	18,549.96
			(-) [6/2018]	(-) [17,265.00]	(0.00) [63]
262	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015	15,525.00	13,876.24
			(10/2018) [10/2018]	(-) [15,525.00]	(0.00) [41]
	D & N HAVELI				
	Petroleum				
263	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019	6,086.08	2,765.06
			(10/2019) [10/2019]	(5,842.31) [5,842.31]	(-243.77) [5]
	DELHI				
	Health And Family Welfare				
264	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017	204.44	147.30
			(-) [6/2018]	(-) [204.44]	(0.00) [13]
265	AIIMS - OPD(NEW)	8/2014	5/2017	293.65	217.60
			(-) [9/2018]	(-) [293.65]	(0.00) [16]
266	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013	414.11	141.00
			(-) [0/0]	(-) [414.11]	(0.00) [0]
	Power				
267	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017	1,394.52	86.60
			(6/2019)	(-)	(0.00)

			[6/2019]	[1,394.52]	[25]
268	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)	5/2015	10/2018 (-) [10/2018]	780.33 (-) [780.33]	147.50 (0.00) [0]
	Railways				
269	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [0/0]	295.68 (-) [295.68]	1.20 (0.00) [0]
270	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [0/0]	156.65 (-) [197.17]	56.10 (40.52) [0]
	Road Transport And Highways				
271	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/ (-) [3/2018]	771.18 (-) [771.18]	0.00 (0.00) [-]
	Telecommunications				
272	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [3/2018]	418.26 (-) [418.26]	172.30 (0.00) [9]
	Urban Development				
273	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	/ (-) [4/2019]	197.33 (-) [197.33]	4.91 (0.00) [-]
274	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [5/2018]	884.30 (-) [884.30]	582.84 (0.00) [29]
275	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [6/2019]	188.00 (-) [188.00]	0.00 (0.00) [0]
276	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [3/2018]	38,585.00 (-) [38,585.00]	34,270.32 (0.00) [24]
277	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2020]	1,219.21 (-) [1,592.00]	210.53 (372.79) [5]
278	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (2.00) [238.56]	0.00 (0.00) [0]
279	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [11/2019]	4,264.00 (-) [4,118.00]	3,245.00 (-146.00) [0]
280	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/ (-) [0/0]	422.00 (-) [422.00]	0.00 (0.00) [0]
281	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [0/0]	2,694.00 (-) [2,694.00]	0.00 (0.00) [0]
	GOA				
	Defence Production				
282	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020 (-) [8/2020]	285.95 (286.00) [296.05]	49.14 (10.10) [0]
283	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018 (-) [5/2018]	167.69 (168.00) [172.99]	62.51 (5.30) [0]
	Road Transport And Highways				
284	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [280.16]	16.06 (0.00) [0]
285	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-)	184.05 (-)	10.72 (0.00)

			[0/0]	[184.05]	[0]
286	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	0.00 (0.00) [0]
287	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	16.10 (0.00) [0]
288	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE	3/2015	/ (-) [4/2018]	297.00 (-) [297.00]	38.33 (0.00) [-]
289	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	0.00 (0.00) [0]
290	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	0.00 (0.00) [0]
	GUJARAT				
	Atomic Energy				
291	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (11/2016) [6/2020]	11,459.00 (-) [11,459.00]	11,554.00 (0.00) [54]
	Petroleum				
292	ANKLESHWAR BARODA PIPELINE PROJECT	7/2014	3/2018 (-) [3/2018]	199.95 (-) [199.95]	154.37 (0.00) [0]
293	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [9/2019]	3,380.00 (-) [3,380.00]	597.50 (0.00) [0]
294	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [7/2018]	327.78 (-) [200.00]	80.23 (-127.78) [3]
295	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	0.00 (0.00) [0]
296	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY	2/2016	7/2017 (-) [2/2018]	931.00 (-) [931.00]	621.84 (0.00) [0]
297	GAMJI REDEVELOPMENT PROJECT	5/2015	11/2019 (12/2018) [12/2018]	1,671.22 (567.22) [567.22]	414.94 (-1,104.00) [-11]
298	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	41.89 (0.00) [0]
299	NAWAGAM-KOYALI PIPELINE PROJECT	11/2014	9/2018 (9/2018) [9/2018]	195.63 (-) [187.10]	168.01 (-8.53) [0]
300	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	9/2011	7/2016 (6/2018) [6/2018]	202.25 (202.25) [160.16]	118.02 (-42.09) [23]
301	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (3/2026) [3/2026]	1,162.56 (1,162.56) [1,162.56]	230.90 (0.00) [0]
302	REPLACEMENT OF KV SECTION OF KSPL	10/2014	8/2018 (-) [8/2018]	279.00 (-) [279.00]	200.05 (0.00) [0]
	Power				
303	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [6/2019]	193.14 (-) [193.14]	0.00 (0.00) [0]
304	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA)	5/2017	9/2018 (-)	175.64 (-)	17.10 (0.00)

	GUJARAT		[9/2018]	[175.64]	[0]
305	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B)	7/2016	12/2018 (-) [12/2018]	300.94 (-) [300.94]	112.80 (0.00) [0]
306	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	11/2017 (-) [5/2018]	330.00 (-) [330.00]	200.08 (0.00) [6]
	Railways				
307	AHMEDABAD-BOTAD (GC)	4/2012	/ (-) [3/2020]	567.18 (-) [975.62]	431.74 (408.44) [-]
308	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2013 (-) [3/2020]	394.14 (416.86) [385.60]	343.13 (-8.54) [84]
309	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [203.00]	202.29 (85.64) [0]
310	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-) [3/2019]	318.24 (-) [321.62]	82.24 (3.38) [84]
311	DHASA-JETALSAR (GC)	4/2012	/ (-) [12/2020]	376.59 (-) [644.38]	49.88 (267.79) [-]
312	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
313	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (-) [0/0]	439.88 (-) [844.10]	16.24 (404.22) [0]
314	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [3/2019]	343.00 (-) [343.00]	272.61 (0.00) [0]
315	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
316	PALANPUR-SAMAKHAYALI (DL)	4/2013	/ (-) [12/2020]	1,266.89 (-) [1,548.66]	506.55 (281.77) [-]
317	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	/ (-) [3/2019]	320.66 (1,378.12) [858.96]	548.93 (538.30) [-]
318	SURENDRA NAGAR RAJKOT	4/2015	/ (-) [3/2021]	1,002.39 (-) [1,002.39]	155.78 (0.00) [-]
319	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	4/2008	3/2014 (-) [0/0]	1,389.62 (2,446.85) [2,446.85]	2,046.34 (1,057.23) [0]
320	VIRAMGAM-SURENDRANAGAR (DL)	4/2010	/ (-) [0/0]	279.40 (384.32) [355.00]	0.00 (75.60) [0]
321	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	Road Transport And Highways				
322	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	0.00 (0.00) [0]
323	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	0.00 (0.00) [0]
324	4-LANNING OF PORBANDAR DWARKA SECTION IN THE	6/2017	6/2020	1,958.88	0.00

	STATE OF GUJARAT		(-) [6/2020]	(-) [1,958.88]	(0.00) [0]
325	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [7/2017]	2,125.24 (-) [2,125.24]	0.00 (0.00) [0]
326	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [0/0]	364.56 (-) [364.56]	0.00 (0.00) [0]
327	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	0.00 (0.00) [0]
328	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	0.00 (0.00) [0]
329	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	0.00 (0.00) [0]
330	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	0.00 (0.00) [0]
331	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [12/2017]	1,509.10 (-) [3,237.87]	0.00 (1,728.77) [0]
332	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
333	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [0/0]	953.88 (-) [953.88]	0.00 (0.00) [0]
334	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,251.11]	0.00 (0.00) [0]
335	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
336	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	0.00 (0.00) [0]
	Steel				
337	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	Telecommunications				
338	GUJARAT ACCESS (LOT 1)	9/2017	5/2018 (-) [5/2018]	171.54 (-) [171.54]	0.00 (0.00) [0]
	HARYANA				
	Fertilisers				
339	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	17.26 (0.00) [0]
	Health And Family Welfare				
340	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2018]	505.58 (-) [505.58]	257.00 (0.00) [6]
341	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	7/2016	8/2018 (-) [8/2018]	312.99 (-) [312.99]	149.00 (0.00) [0]
	Petroleum				
342	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-)	255.00 (-)	0.00 (0.00)

			[11/2020]	[255.00]	[0]
	Railways				
343	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	4/2013	/	400.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[400.00]	[0]
344	JIND-SONEPAT (NL),NR	1/2004	3/2012	238.56	722.65
			(-)	(-)	(501.44)
			[0/0]	[740.00]	[0]
345	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019	346.32	233.95
			(-)	(-)	(-46.32)
			[3/2019]	[300.00]	[0]
346	ROHTAK-MEHAM HANSI	4/2012	/	287.00	4.38
			(-)	(-)	(338.00)
			[0/0]	[625.00]	[0]
	Road Transport And Highways				
347	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016	602.95	0.00
			(-)	(-)	(0.00)
			[6/2018]	[602.95]	[24]
348	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018	574.28	0.00
			(-)	(-)	(0.00)
			[7/2018]	[574.28]	[0]
349	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020	639.79	0.00
			(-)	(-)	(-86.89)
			[3/2020]	[552.90]	[0]
350	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	/	2,128.72	0.00
			(-)	(-)	(0.00)
			[4/2019]	[2,128.72]	[-]
351	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	/	248.97	0.00
			(-)	(-)	(0.00)
			[5/2019]	[248.97]	[-]
352	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	/	1,004.67	0.00
			(-)	(-)	(0.00)
			[5/2019]	[1,004.67]	[-]
353	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010	486.00	0.00
			(-)	(-)	(0.00)
			[8/2017]	[486.00]	[0]
354	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	/	867.66	0.00
			(-)	(-)	(0.00)
			[5/2018]	[867.66]	[-]
355	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018	723.54	0.00
			(-)	(-)	(0.00)
			[2/2018]	[723.54]	[0]
356	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	7/2015	/	1,393.00	0.00
			(-)	(-)	(0.00)
			[1/2018]	[1,393.00]	[0]
357	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011	1,108.00	0.00
			(-)	(-)	(1,180.00)
			[3/2018]	[2,288.00]	[76]
358	ROHTAK-BAWAL	5/2011	11/2013	650.00	0.00
			(-)	(-)	(0.00)
			[8/2017]	[650.00]	[0]
359	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA-BARWALA - PANCHKULA (PKG - 1)	5/2015	/	600.85	0.00
			(-)	(-)	(0.00)
			[5/2018]	[600.85]	[-]
360	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA-BARWALA - PANCHKULA(PKG - 2)	10/2015	4/2018	562.34	0.00
			(-)	(-)	(0.00)
			[4/2018]	[562.34]	[0]
	HIMACHAL PRADESH				
	Petroleum				
361	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019	151.00	41.00
			(-)	(-)	(0.00)

			[9/2019]	[151.00]	[0]
362	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP	2/2016	5/2019 (-) [12/2018]	356.00 (-) [356.00]	125.91 (0.00) [-5]
	Power				
363	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2020]	3,919.59 (-) [8,398.75]	6,684.84 (4,479.16) [135]
	Railways				
364	BHANUPALI-BILASPUR BERI NL	4/2008	/ (-) [3/2019]	1,046.88 (-) [4,500.00]	125.20 (3,453.12) [-]
	Road Transport And Highways				
365	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	/ (-) [2/2019]	273.20 (-) [273.20]	0.00 (0.00) [-]
366	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [6/2020]	2,485.93 (-) [2,485.93]	0.00 (0.00) [0]
367	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [2/2018]	1,916.79 (-) [1,916.79]	0.00 (0.00) [0]
368	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2018]	934.46 (-) [934.46]	0.00 (0.00) [0]
369	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	0.00 (0.00) [0]
370	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [0/0]	447.75 (-) [447.75]	0.00 (0.00) [0]
371	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	0.00 (0.00) [0]
	Urban Development				
372	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [10/2018]	270.83 (-) [270.83]	142.67 (0.00) [47]
	JAMMU AND KASHMIR				
	Power				
373	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [10/2023]	8,112.12 (-) [8,112.12]	895.22 (0.00) [42]
374	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT	1/2014	9/2017 (-) [9/2018]	1,788.41 (-) [2,333.71]	1,223.54 (545.30) [12]
	Railways				
375	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2018]	2,500.00 (-) [27,946.00]	16,131.46 (25,446.00) [193]
	Road Transport And Highways				
376	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [0/0]	1,471.75 (-) [1,471.75]	0.00 (0.00) [0]
377	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [6/2019]	2,168.66 (-) [2,168.66]	0.00 (0.00) [0]
378	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [12/2018]	2,136.97 (-) [2,136.97]	0.00 (0.00) [0]
379	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013	1,813.76	0.00

			(-) [11/2017]	(-) [1,813.76]	(0.00) [0]
380	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	3,986.82 (0.00) [0]
381	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [3/2019]	1,987.00 (-) [1,987.00]	0.00 (0.00) [44]
382	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [12/2017]	1,100.70 (-) [1,100.70]	0.00 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
383	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	223.12 (0.00) [0]
384	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2020]	163.51 (-) [163.51]	93.28 (0.00) [108]
385	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	42.26 (0.00) [0]
386	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
387	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2019]	162.46 (-) [162.46]	84.79 (0.00) [60]
388	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [4/2018]	289.45 (-) [289.45]	174.74 (0.00) [47]
389	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2021]	706.40 (-) [706.40]	125.99 (0.00) [104]
390	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [4/2019]	1,230.27 (-) [1,230.27]	280.30 (0.00) [48]
391	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2018]	339.88 (-) [339.88]	12.08 (0.00) [54]
392	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	4.57 (0.00) [0]
393	NORTH URIMARI OCP (3.0 MTY)	12/2007	3/2012 (-) [3/2019]	179.87 (-) [179.87]	98.15 (0.00) [84]
394	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2018]	269.82 (-) [269.82]	169.31 (0.00) [48]
395	RAJMAHAL OC EXP.	9/2009	3/2014 (-) [0/0]	153.82 (-) [153.82]	131.07 (0.00) [0]
396	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2019]	510.85 (-) [510.85]	350.19 (0.00) [36]
397	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2019]	264.68 (-) [264.68]	154.03 (0.00) [84]
	<u>Petroleum</u>				
398	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022)	658.62 (910.23)	9.35 (251.61)

			[3/2022]	[910.23]	[-12]
399	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	4/2011	5/2015 (-) [0/0]	191.96 (-) [191.96]	176.28 (0.00) [0]
	Power				
400	BOKARO THERMAL POWER STATION-A	8/2006	12/2011 (-) [0/0]	2,313.00 (4,139.00) [4,366.64]	3,484.00 (2,053.64) [0]
401	NORTH KARANPURA STPP (3X660 MW)	2/2014	2/2019 (10/2020) [10/2020]	14,366.58 (-) [15,164.05]	6,924.00 (797.47) [20]
402	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [12/2016]	4,237.96 (4,552.00) [4,552.00]	2,657.86 (314.04) [0]
	Railways				
403	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [3/2021]	1,724.20 (-) [1,724.20]	184.26 (0.00) [0]
404	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	4/2010	12/2015 (-) [0/0]	309.44 (-) [583.00]	436.96 (273.56) [0]
405	GOELKERA-MANOHARPUR,(LD)(SER)	3/1997	2/2006 (-) [12/2019]	261.70 (-) [388.00]	360.26 (126.30) [166]
406	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [0/0]	459.91 (-) [459.91]	221.54 (0.00) [0]
407	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	4/1995	12/2011 (12/2010) [3/2020]	900.05 (-) [1,125.89]	980.99 (225.84) [99]
408	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	/ (-) [0/0]	258.20 (-) [365.00]	143.14 (106.80) [0]
409	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (-) [0/0]	148.77 (-) [209.00]	133.82 (60.23) [0]
410	RANCHI-LOHARDAGA(GC),SER	4/1997	6/2004 (-) [0/0]	194.07 (583.02) [583.02]	568.02 (388.95) [0]
411	TINPAHAR - SAHIBGANJ (ER)	4/2008	3/2012 (-) [0/0]	167.73 (-) [167.73]	207.11 (0.00) [0]
	Road Transport And Highways				
412	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [3/2020]	239.68 (-) [235.90]	0.00 (-3.78) [0]
413	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [3/2020]	165.50 (-) [172.16]	0.00 (6.66) [0]
414	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	/ (-) [3/2019]	997.15 (-) [997.15]	329.10 (0.00) [-]
415	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
416	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	/ (-) [8/2018]	323.72 (-) [323.72]	37.20 (0.00) [-]
417	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [12/2017]	1,479.00 (-) [1,479.00]	881.08 (0.00) [0]

418	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
419	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [458.03]	0.00 (0.00) [0]
	Steel				
420	ALTERNATE GAS NETWORK AT BSL	3/2015	3/2018 (-) [3/2018]	255.19 (-) [255.19]	177.21 (0.00) [0]
421	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [3/2018]	200.00 (-) [200.00]	131.15 (0.00) [0]
422	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [4/2018]	170.00 (-) [170.00]	88.91 (0.00) [0]
423	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [12/2018]	787.29 (-) [787.29]	285.30 (0.00) [24]
424	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [3/2018]	253.92 (253.92) [253.92]	193.97 (0.00) [21]
425	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	2/2014	9/2017 (-) [0/0]	4,749.00 (-) [4,749.00]	83.68 (0.00) [0]
426	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (-) [11/2018]	1,154.18 (-) [1,154.18]	659.52 (0.00) [11]
427	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (-) [12/2018]	1,034.01 (-) [1,034.01]	216.70 (0.00) [14]
428	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (-) [6/2019]	262.87 (-) [262.87]	38.95 (0.00) [0]
	Urban Development				
429	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [12/2018]	171.86 (-) [171.86]	40.05 (0.00) [33]
	KARNATAKA				
	Petroleum				
430	BSVI UPGRADATION	9/2016	12/2019 (-) [12/2019]	1,810.00 (1,810.00) [1,810.00]	108.81 (0.00) [0]
431	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [4/2019]	224.00 (207.00) [207.25]	92.97 (-16.75) [0]
432	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [749.00]	606.89 (0.00) [0]
433	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (-) [3/2019]	135.00 (170.70) [170.70]	104.65 (35.70) [0]
434	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	Power				
435	KUDGI STPP STAGE 1	1/2012	1/2017 (3/2018) [3/2018]	15,166.19 (-) [16,934.65]	15,364.00 (1,768.46) [14]
436	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II	5/2017	2/2019 (-)	445.89 (-)	81.90 (0.00)

	(PART-B)		[2/2019]	[445.89]	[0]
	Railways				
437	ARSIKERE-TUMKUR	3/2015	/ (11/2015) [3/2020]	960.00 (578.00) [578.00]	365.36 (-382.00) [-]
438	BAGALKOT-KUDACHI NL	4/2010	/ (-) [0/0]	377.93 (986.30) [986.30]	279.58 (608.37) [0]
439	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	/ (-) [0/0]	138.00 (1,382.78) [1,382.78]	6.24 (1,244.78) [0]
440	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [0/0]	327.25 (367.77) [367.77]	0.34 (40.52) [0]
441	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [0/0]	558.00 (692.43) [692.43]	0.00 (134.43) [0]
442	GADAG-WADI NL	4/2013	/ (-) [0/0]	1,117.00 (1,922.00) [1,922.00]	15.78 (805.00) [0]
443	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	/ (-) [3/2019]	2,127.00 (-) [2,127.00]	955.10 (0.00) [-]
444	HUBLI- CHIKJAJUR	3/2015	/ (3/2020) [0/0]	1,900.00 (1,141.00) [1,141.00]	546.05 (-759.00) [0]
445	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [0/0]	227.00 (-) [2,135.00]	133.91 (1,908.00) [0]
446	MARIKUPPAM - KUPPAM	4/2012	1/1999 (-) [0/0]	285.57 (279.54) [279.54]	3.95 (-6.03) [0]
447	MUNIRABAD (GINGERA) -RAICHUR NL	4/2007	/ (-) [0/0]	179.65 (-) [1,350.91]	832.60 (1,171.26) [0]
448	SHIMOGA-HARIHAR NL	4/2011	/ (-) [0/0]	562.74 (-) [832.47]	0.94 (269.73) [0]
449	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [0/0]	146.75 (-) [167.50]	0.34 (20.75) [0]
450	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [0/0]	913.00 (-) [1,801.01]	3.59 (888.01) [0]
451	WHITE FIELD-KOLAR NL	4/2011	/ (-) [0/0]	341.05 (-) [348.85]	0.35 (7.80) [0]
	Road Transport And Highways				
452	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	/ (-) [3/2019]	1,167.42 (-) [1,167.42]	118.34 (0.00) [-]
453	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [2/2019]	1,655.01 (-) [1,655.01]	1,484.71 (0.00) [30]
454	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/ (-) [0/0]	720.69 (-) [720.69]	99.03 (0.00) [0]
455	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	/ (-) [3/2019]	701.40 (-) [701.40]	5.78 (0.00) [-]
456	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE	3/2016	/	870.00	4.03

	TO BANTAWAL		(-) [3/2019]	(-) [870.00]	(0.00) [-]
457	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	/	1,388.00	654.13
			(-) [8/2018]	(-) [1,388.00]	(0.00) [-]
458	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	/	1,664.20	89.91
			(-) [4/2020]	(-) [1,664.20]	(0.00) [-]
459	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	/	946.00	818.53
			(-) [6/2018]	(-) [946.00]	(0.00) [-]
460	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018	219.40	0.00
			(-) [1/2018]	(-) [219.40]	(0.00) [0]
461	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020	993.16	67.09
			(-) [5/2020]	(-) [1,434.00]	(440.84) [2]
462	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020	831.58	10.50
			(-) [6/2020]	(-) [1,177.00]	(345.42) [3]
463	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015	165.67	0.00
			(-) [11/2017]	(-) [165.67]	(0.00) [0]
464	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015	159.12	0.00
			(-) [11/2017]	(-) [159.12]	(0.00) [0]
465	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017	709.00	293.12
			(-) [9/2018]	(-) [709.00]	(0.00) [12]
466	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	/	950.69	100.33
			(-) [8/2019]	(-) [950.69]	(0.00) [-]
	Steel				
467	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014	768.88	1,085.64
			(-) [0/0]	(1,070.97) [1,113.34]	(344.46) [0]
468	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015	324.87	262.93
			(-) [0/0]	(324.87) [324.87]	(0.00) [0]
	Urban Development				
469	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019	26,405.14	2,391.46
			(-) [3/2020]	(-) [26,405.14]	(0.00) [13]
470	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020	246.31	1.66
			(-) [2/2020]	(-) [246.31]	(0.00) [0]
	KERALA				
	Petroleum				
471	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019	1,112.00	108.79
			(-) [6/2019]	(-) [1,112.00]	(0.00) [0]
472	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY	5/2015	8/2018	337.06	93.74
			(-) [8/2018]	(-) [337.06]	(0.00) [0]
473	LPG TERMINAL AT KOCHI	10/2015	10/2017	607.06	325.27
			(-) [3/2019]	(-) [714.25]	(107.19) [17]
474	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020	3,313.00	118.35
			(-) [2/2020]	(-) [3,313.00]	(0.00) [0]
475	PROPYLENE DERIVATIVES PETROCHEMICAL	11/2014	8/2018	4,588.29	1,290.71

	PROJECT(PDPP) AT KOCHI REFINERY		(5/2019) [5/2019]	(5,245.96) [5,245.96]	(657.67) [9]
	Railways				
476	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/	550.00	240.68
			(-)	(-)	(2,265.62)
			[0/0]	[2,815.62]	[0]
477	CHENGANNUR-CHINGAVANAM	4/2006	/	191.72	378.76
			(-)	(-)	(151.13)
			[0/0]	[342.85]	[0]
478	ERNAKULAM-KUMBALAM	4/2010	/	189.24	6.28
			(-)	(-)	(0.00)
			[0/0]	[189.24]	[0]
479	KUMBALAM-TURAVUR	4/2011	/	252.96	7.74
			(-)	(-)	(0.00)
			[0/0]	[252.96]	[0]
480	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/	900.00	0.00
			(-)	(-)	(3,231.90)
			[0/0]	[4,131.90]	[0]
481	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/	1,000.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,000.00]	[0]
	Road Transport And Highways				
482	4 LANNING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/	845.24	0.00
			(-)	(-)	(0.00)
			[11/2017]	[845.24]	[0]
483	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	/	804.97	0.00
			(-)	(-)	(0.00)
			[6/2018]	[804.97]	[-]
484	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017	1,124.11	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,124.11]	[0]
485	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	1/2014	11/2017	267.16	0.02
			(-)	(352.00)	(84.89)
			[0/0]	[352.05]	[0]
486	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017	255.75	0.02
			(-)	(348.00)	(92.68)
			[9/2017]	[348.43]	[0]
487	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012	617.00	0.00
			(-)	(-)	(0.00)
			[12/2017]	[617.00]	[0]
	Urban Development				
488	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER	7/2015	11/2015	154.00	90.76
			(5/2018)	(-)	(0.00)
			[5/2018]	[154.00]	[30]
489	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012	165.23	25.91
			(-)	(-)	(0.00)
			[3/2018]	[165.23]	[65]
490	KOCHI METRO RAIL PROJECT	7/2012	7/2017	5,181.79	0.00
			(-)	(-)	(0.00)
			[12/2019]	[5,181.79]	[29]
	MADHYA PRADESH				
	Coal				
491	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021	869.44	111.56
			(-)	(-)	(0.00)
			[3/2021]	[869.44]	[0]
492	AMRITDHARA OC PROJECT	2/2015	3/2023	481.60	0.00
			(-)	(-)	(0.00)
			[3/2023]	[481.60]	[0]
493	BATURA HIGHWALL PROJECT	7/2015	3/2022	231.92	0.00
			(-)	(-)	(0.00)
			[3/2022]	[231.92]	[0]

494	BATURA OCP (2.0 MTY)	8/2015	3/2023 (3/2021) [3/2021]	1,186.64 (203.82) [203.82]	77.18 (-982.82) [-24]
495	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	15.30 (0.00) [0]
496	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	77.75 (0.00) [0]
497	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	35.61 (0.00) [0]
498	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	1.18 (0.00) [0]
499	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	3/2012 (-) [3/2018]	259.40 (-) [486.57]	410.19 (227.17) [72]
500	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	114.47 (0.00) [0]
	Petroleum				
501	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [6/2020]	236.00 (-) [236.00]	0.00 (0.00) [0]
502	SIX PIPELINE REPLACEMENT PROJECT	3/2009	1/2017 (5/2018) [5/2018]	181.02 (181.02) [181.02]	168.93 (0.00) [16]
	Power				
503	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [2,104.21]	40.16 (0.00) [0]
504	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	9/2017 (6/2019) [6/2019]	11,638.55 (-) [12,865.92]	8,980.00 (1,227.37) [21]
505	KHARGONE STPP STAGE I (1320 MW)	3/2015	9/2019 (-) [9/2019]	9,870.51 (-) [11,148.86]	5,115.00 (1,278.35) [0]
506	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	4/2016	6/2018 (-) [6/2018]	287.99 (-) [287.99]	99.50 (0.00) [0]
507	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	1/2016	3/2017 (9/2018) [9/2018]	305.04 (-) [305.04]	171.50 (0.00) [18]
508	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V	2/2015	6/2018 (-) [6/2018]	1,750.00 (-) [1,750.00]	867.00 (0.00) [0]
	Railways				
509	BHOPAL BINA 3D LINE DOUBLING	9/2007	3/2010 (-) [3/2018]	687.20 (-) [1,030.00]	1,029.45 (342.80) [96]
510	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.65 (-) [1,485.85]	752.76 (0.20) [0]
511	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,101.16]	194.91 (717.37) [0]
512	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	12/2018 (-) [12/2018]	737.72 (-) [737.72]	104.10 (0.00) [0]
513	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	12/2020	1,762.94	0.00

			(-) [12/2020]	(-) [1,762.94]	(0.00) [0]
514	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2020 (-) [3/2020]	582.13 (-) [582.13]	0.00 (0.00) [0]
515	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2022]	2,478.23 (-) [2,478.23]	0.00 (0.00) [0]
516	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [3/2019]	174.00 (-) [174.00]	132.66 (0.00) [0]
517	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	/ (-) [3/2021]	470.92 (727.13) [2,713.09]	632.05 (2,242.17) [-]
518	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2012 (-) [0/0]	603.04 (2,473.40) [1,030.29]	937.37 (427.25) [0]
	Road Transport And Highways				
519	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	0.00 (0.00) [0]
520	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	/ (-) [1/2019]	227.49 (-) [227.49]	0.00 (0.00) [-]
521	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]
522	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [0/0]	990.61 (-) [990.61]	0.00 (0.00) [0]
523	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
524	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [0/0]	390.51 (-) [390.51]	43.25 (0.00) [0]
525	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	11/2011	2/2015 (-) [2/2015]	670.82 (-) [670.82]	590.00 (0.00) [0]
526	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	5/2015 (-) [0/0]	704.26 (-) [704.26]	0.00 (0.00) [0]
527	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	3/2013	2/2016 (-) [2/2016]	257.80 (-) [257.80]	59.30 (0.00) [0]
528	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	/ (-) [1/2019]	1,583.79 (-) [1,583.79]	0.00 (0.00) [-]
529	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [0/0]	960.24 (-) [960.24]	0.00 (0.00) [0]
530	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [3/2019]	1,012.90 (-) [1,012.90]	0.00 (0.00) [36]
531	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [9/2017]	1,055.00 (-) [1,601.77]	0.00 (546.77) [0]
532	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [12/2017]	928.83 (-) [928.83]	0.00 (0.00) [0]
533	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE	3/2015	/	794.30	0.00

	-I		(-) [0/0]	(-) [794.30]	(0.00) [0]
534	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/	795.76	0.00
			(-) [0/0]	(-) [795.76]	(0.00) [0]
535	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/	810.22	0.00
			(-) [0/0]	(-) [810.22]	(0.00) [0]
536	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I	1/2016	7/2018	830.36	0.00
			(-) [7/2018]	(-) [830.36]	(0.00) [0]
537	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017	639.97	0.00
			(-) [0/0]	(-) [639.97]	(0.00) [0]
538	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/	770.73	0.00
			(-) [0/0]	(-) [770.73]	(0.00) [0]
539	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	6/2018	927.54	29.17
			(-) [6/2018]	(-) [927.54]	(0.00) [0]
540	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017	497.05	0.00
			(-) [5/2017]	(-) [497.05]	(0.00) [0]
541	INDORE-DEWAS(NH-3)	11/2010	5/2013	325.00	0.00
			(-) [7/2017]	(-) [325.00]	(0.00) [0]
542	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013	1,175.00	0.00
			(-) [9/2017]	(-) [1,206.10]	(31.10) [0]
543	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	3/2018	628.45	20.74
			(-) [3/2018]	(-) [628.45]	(0.00) [0]
544	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	2/2015	5/2017	327.32	142.73
			(-) [5/2017]	(-) [327.32]	(0.00) [0]
545	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	2/2015	7/2017	377.83	57.42
			(-) [7/2017]	(-) [377.83]	(0.00) [0]
546	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	6/2015	12/2017	641.02	89.88
			(-) [12/2017]	(-) [641.02]	(0.00) [0]
547	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015	381.86	252.03
			(-) [4/2015]	(-) [381.86]	(0.00) [0]
548	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015	320.48	189.49
			(-) [9/2016]	(-) [320.48]	(0.00) [0]
549	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	6/2015	5/2017	532.49	137.08
			(-) [5/2017]	(-) [532.49]	(0.00) [0]
550	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015	871.15	332.25
			(-) [8/2016]	(-) [871.15]	(0.00) [0]
551	UMARIYA TO SHAHNOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017	511.83	40.87
			(-) [8/2017]	(-) [511.83]	(0.00) [0]
	Urban Development				
552	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY	5/2016	11/2018	164.00	85.46
			(5/2018)	(-)	(0.00)
			[5/2018]	[164.00]	[-6]
	MAHARASHTRA				

	Coal				
553	ADASA UG TO OC	8/2015	3/2023 (-) [3/2023]	288.90 (-) [288.90]	0.00 (0.00) [0]
554	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2019]	198.68 (-) [198.68]	39.89 (0.00) [0]
555	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	77.21 (0.00) [0]
556	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	232.10 (0.00) [0]
557	BHANEKAON OC	2/2015	3/2023 (2/2017) [3/2023]	187.94 (409.68) [409.68]	86.10 (221.74) [0]
558	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2019]	304.52 (-) [304.52]	126.93 (0.00) [0]
559	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	383.42 (0.00) [0]
560	GOKUL	11/2014	3/2018 (-) [3/2018]	267.67 (-) [267.67]	206.04 (0.00) [0]
561	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2021]	277.65 (-) [277.65]	17.31 (0.00) [0]
562	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	239.83 (0.00) [0]
563	MAKARDHOKRA I OC	9/2014	3/2021 (-) [3/2021]	266.23 (-) [266.23]	139.76 (0.00) [0]
564	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	51.12 (0.00) [0]
565	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2019]	295.56 (-) [295.56]	88.13 (0.00) [0]
566	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	178.26 (0.00) [0]
567	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	96.81 (0.00) [0]
	Fertilisers				
568	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	1.32 (0.00) [0]
569	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	2/2016	12/2017 (4/2018) [4/2018]	482.85 (482.85) [482.85]	413.01 (0.00) [4]
570	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (4/2019) [4/2019]	197.79 (209.44) [209.44]	106.14 (11.65) [29]
	Health And Family Welfare				
571	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [3/2019]	274.19 (-) [274.19]	29.68 (0.00) [0]
	Petroleum				

572	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (11/2019) [11/2019]	968.61 (968.61) [968.61]	0.00 (0.00) [0]
573	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	0.05 (0.00) [0]
574	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	212.00 (-) [212.00]	0.08 (0.00) [0]
575	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	348.00 (-) [348.00]	0.05 (0.00) [0]
576	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (3/2018) [11/2018]	861.79 (1,256.72) [1,256.72]	1,188.94 (394.93) [66]
577	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (11/2019) [11/2019]	546.15 (546.15) [546.15]	0.00 (0.00) [0]
578	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (11/2019) [11/2019]	511.30 (511.30) [511.30]	0.00 (0.00) [0]
579	DEVELOPMENT OF C-26 CLUSTER FIELDS	3/2012	5/2014 (5/2018) [5/2018]	2,592.17 (-) [2,592.17]	2,041.21 (0.00) [48]
580	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (-) [5/2021]	4,006.83 (4,006.83) [4,006.83]	184.01 (0.00) [0]
581	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2019) [3/2019]	4,619.94 (4,619.94) [3,961.54]	3,816.11 (-658.40) [15]
582	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	66.77 (0.00) [0]
583	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (3/2018) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,729.04 (606.02) [57]
584	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	282.69 (0.00) [0]
585	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY	5/2015	1/2019 (-) [1/2019]	193.40 (-) [193.40]	40.41 (0.00) [0]
586	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (4/2018) [4/2018]	3,190.69 (-) [3,247.19]	1,526.01 (56.50) [0]
587	MH NORTH REDEVELOPMENT PHASE III	6/2014	5/2017 (5/2018) [5/2018]	5,706.47 (5,813.25) [5,813.25]	5,558.19 (106.78) [12]
588	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	99.46 (0.00) [0]
589	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (3/2019) [3/2019]	6,068.80 (6,068.80) [5,296.93]	4,400.56 (-771.87) [-1]
590	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [7/2019]	4,199.00 (-) [4,199.00]	194.97 (0.00) [-8]
591	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	1,027.52 (0.00) [14]
592	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION	1/2017	5/2019	474.15	161.29

	OF MUKTA PAY		(5/2019) [5/2019]	(474.15) [474.15]	(0.00) [0]
593	PIPELINE REPLACEMENT PROJECT -4	2/2015	5/2017 (5/2018) [5/2018]	2,899.93 (-) [2,504.61]	1,317.83 (-395.32) [12]
594	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	33.23 (0.00) [0]
	Power				
595	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
596	SOLAPUR STPP	3/2012	11/2016 (3/2019) [3/2019]	9,395.18 (-) [9,395.18]	8,488.00 (0.00) [28]
597	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B	4/2015	1/2018 (-) [4/2018]	2,225.00 (2,225.00) [2,225.00]	1,346.00 (0.00) [3]
598	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	9/2010 (12/2018) [12/2018]	477.69 (738.48) [738.48]	660.59 (260.79) [99]
	Railways				
599	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	/ (-) [3/2019]	184.06 (199.12) [199.12]	167.49 (15.06) [-]
600	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	/ (-) [3/2021]	514.68 (2,271.50) [2,271.50]	1,479.39 (1,756.82) [-]
601	AMRAVATI-NARKHER NL(CR)	6/1994	6/1999 (-) [0/0]	663.01 (668.34) [858.97]	707.51 (195.96) [0]
602	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2020]	495.44 (1,781.98) [1,781.98]	812.12 (1,286.54) [192]
603	DAUND - MANMAD (236 KM)	2/2016	/ (-) [3/2023]	1,876.00 (2,081.27) [2,081.27]	0.13 (205.27) [-]
604	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	1,514.45 (-) [1,750.00]	1,388.35 (235.55) [0]
605	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [12/2025]	723.78 (-) [723.78]	0.16 (0.00) [0]
606	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	/ (-) [3/2024]	9,968.00 (-) [8,857.98]	0.00 (-1,110.02) [-]
607	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	/ (-) [3/2023]	2,326.00 (2,449.91) [2,449.91]	42.53 (123.91) [-]
608	KALYAN-KASARA 3RD LINE	4/2011	/ (-) [3/2021]	277.70 (792.89) [792.89]	230.61 (515.19) [-]
609	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	/ (-) [3/2023]	854.00 (1,035.16) [1,035.16]	4.63 (181.16) [-]
610	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [3/2019]	305.00 (-) [305.00]	249.12 (0.00) [0]
611	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]

612	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2019]	5,300.00 (-) [7,986.04]	2,423.55 (2,686.04) [60]
613	PUNE-MIRAJ-LONDA (467 KM)	2/2015	/ (-) [3/2024]	4,670.00 (3,627.47) [3,627.47]	32.57 (-1,042.53) [-]
614	PUNE-NASIK (265 KM)	2/2016	/ (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [-]
615	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	12/2021 (-) [12/2021]	1,273.00 (1,908.00) [1,908.00]	0.00 (635.00) [0]
616	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
617	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	/ (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [-]
618	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
619	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	/ (-) [3/2022]	912.00 (637.95) [637.95]	8.97 (-274.05) [-]
620	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	/ (-) [3/2022]	630.00 (1,272.19) [1,272.19]	67.30 (642.19) [-]
621	WARDHA-NANDED MAHARASHTRA	4/2008	/ (-) [3/2023]	499.30 (3,168.29) [3,168.29]	832.15 (2,668.99) [-]
622	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	/ (-) [3/2022]	297.85 (540.02) [540.02]	134.52 (242.17) [-]
Road Transport And Highways					
623	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	/ (-) [5/2019]	2,288.18 (-) [2,288.18]	0.00 (0.00) [-]
624	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	/ (-) [5/2019]	1,885.74 (-) [1,885.74]	0.00 (0.00) [-]
625	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [1/2018]	972.50 (-) [972.50]	1,479.56 (0.00) [0]
626	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [0/0]	607.00 (-) [607.00]	0.00 (0.00) [0]
627	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	0.00 (0.00) [0]
628	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [11/2017]	923.04 (-) [923.04]	535.52 (0.00) [0]
629	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
630	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [0/0]	1,071.61 (-) [1,071.61]	0.00 (0.00) [0]
631	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	/ (-) [3/2019]	446.17 (-) [446.17]	0.00 (0.00) [-]

632	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [3/2020]	1,098.06 (-) [1,160.64]	0.00 (62.58) [0]
633	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	0.00 (0.00) [0]
634	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	0.00 (0.00) [0]
635	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	/ (-) [3/2019]	400.25 (-) [400.25]	0.00 (0.00) [-]
636	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [0/0]	1,064.88 (-) [1,064.88]	0.00 (0.00) [0]
637	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [0/0]	1,059.73 (-) [1,071.00]	0.00 (11.27) [0]
638	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [3/2020]	1,030.44 (-) [1,065.51]	0.00 (35.07) [0]
639	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [3/2020]	988.34 (-) [1,043.28]	0.00 (54.94) [0]
640	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	/ (-) [5/2018]	505.00 (-) [505.00]	161.13 (0.00) [-]
641	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	/ (-) [7/2018]	197.69 (-) [197.69]	0.00 (0.00) [-]
642	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60	3/2016	/ (-) [7/2018]	244.00 (-) [244.00]	0.00 (0.00) [-]
643	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	/ (-) [3/2019]	649.50 (-) [649.50]	31.47 (0.00) [-]
644	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	/ (-) [5/2019]	244.90 (-) [244.90]	43.29 (0.00) [-]
645	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	/ (-) [5/2018]	593.26 (-) [593.26]	45.11 (0.00) [-]
646	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [156.26]	65.16 (0.00) [0]
647	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	3/2011	/ (-) [11/2014]	185.82 (292.00) [185.82]	205.97 (0.00) [0]
648	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	/ (-) [5/2018]	531.13 (-) [531.13]	163.10 (0.00) [-]
649	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [10/2017]	168.30 (-) [168.30]	13.43 (0.00) [0]
650	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [7/2016]	187.79 (-) [187.79]	57.60 (0.00) [0]
651	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [3/2020]	247.02 (-) [157.49]	0.00 (-89.53) [0]
652	CONSTRUCTION OF NH-4B FROM KM.21.200 TO	9/2015	/	414.51	157.92

	KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D		(-) [5/2018]	(-) [414.00]	(-0.51) [-]
653	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [5/2019]	296.19 (-) [254.00]	86.42 (-42.19) [-10]
654	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [3/2018]	1,170.52 (-) [1,170.52]	2,263.02 (0.00) [69]
655	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [1/2018]	1,871.34 (-) [1,871.34]	2,881.81 (0.00) [0]
656	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [2/2020]	904.16 (-) [904.16]	6.00 (0.00) [0]
657	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	279.92 (0.00) [0]
658	NAGPUR RING ROAD PACKAGE-1	3/2016	/ (-) [7/2019]	546.00 (-) [546.00]	0.00 (0.00) [-]
659	NAGPUR RING ROAD PACKAGE-2	3/2016	/ (-) [7/2019]	591.66 (-) [591.66]	0.00 (0.00) [-]
660	PANVEL-INDAPUR	12/2011	6/2014 (-) [3/2018]	942.69 (-) [942.69]	437.90 (0.00) [45]
661	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [12/2017]	1,724.55 (-) [1,724.55]	2,091.65 (0.00) [0]
662	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00	12/2013	11/2016 (-) [11/2016]	220.72 (-) [220.72]	95.02 (0.00) [0]
663	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337	6/2014	11/2016 (-) [11/2016]	260.39 (-) [260.39]	87.43 (0.00) [0]
664	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [6/2017]	446.77 (-) [446.77]	87.62 (0.00) [0]
665	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	1/2014	11/2014 (-) [11/2014]	292.98 (-) [292.98]	95.60 (0.00) [0]
666	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	6.50 (0.00) [0]
667	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [0/0]	404.94 (-) [404.94]	0.00 (0.00) [0]
668	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [0/0]	290.73 (-) [290.73]	0.00 (0.00) [0]
669	TALEGAON-AMRAVATI	11/2009	11/2013 (-) [0/0]	567.00 (-) [567.00]	1,055.94 (0.00) [0]
670	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	0.00 (0.00) [0]
671	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [3/2018]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [49]
Shipping And Ports					
672	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS	1/2007	12/2010	366.39	413.91

	AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB		(-) [12/2018]	(669.46) [669.46]	(303.07) [96]
	Telecommunications				
673	MADHYA PRADESH ACCESS (LOT1)	8/2017	5/2018 (-) [5/2018]	215.30 (-) [215.30]	0.00 (0.00) [0]
674	MAHARASHTRA ACESS (LOT 1)	8/2017	5/2018 (-) [5/2018]	212.70 (-) [212.70]	0.00 (0.00) [0]
675	MAHARASHTRA CORE (LOT1)	8/2017	4/2018 (-) [4/2018]	167.68 (-) [167.68]	0.00 (0.00) [0]
676	MAHARASHTRA NODAL (LOT 1)	8/2017	4/2018 (-) [4/2018]	159.30 (-) [159.30]	0.00 (0.00) [0]
	Urban Development				
677	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [0/0]	23,136.00 (-) [23,136.00]	0.00 (0.00) [0]
678	NAGPUR METRO RAIL	8/2014	3/2018 (12/2019) [12/2019]	8,680.00 (8,680.00) [8,680.00]	3,480.63 (0.00) [21]
679	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	2/2011	3/2016 (12/2017) [4/2018]	241.33 (349.33) [349.33]	307.50 (108.00) [25]
680	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	6/2010	3/2012 (-) [6/2018]	205.00 (-) [170.62]	149.22 (-34.38) [75]
	MANIPUR				
	Railways				
681	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	727.56 (-) [9,658.00]	7,387.18 (8,930.44) [108]
	Urban Development				
682	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [11/2018]	216.69 (-) [216.69]	52.00 (0.00) [44]
	MEGHALAYA				
	Health And Family Welfare				
683	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [8/2019]	363.99 (-) [363.99]	21.00 (0.00) [15]
	Railways				
684	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	/ (-) [3/2021]	4,083.02 (-) [6,000.00]	257.31 (1,916.98) [-]
	Road Transport And Highways				
685	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [2/2011]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
686	JORBAT - BARAPANI	1/2011	1/2014 (-) [3/2018]	536.00 (-) [536.00]	0.00 (0.00) [50]
687	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	/ (-) [5/2018]	479.20 (-) [479.20]	0.00 (0.00) [-]
	Steel				
688	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [12/2018]	151.33 (-) [151.33]	7.15 (0.00) [15]
	MIZORAM				

	<u>Railways</u>				
689	BHAIRABI SAIRONG, NL, NEFR	4/2008	4/2014 (-) [3/2020]	619.34 (-) [4,600.00]	1,951.73 (3,980.66) [71]
	<u>Road Transport And Highways</u>				
690	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [10/2010]	195.04 (-) [195.04]	130.82 (0.00) [0]
691	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
692	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
693	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	0.13 (0.00) [0]
694	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	87.11 (0.00) [0]
695	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	0.04 (0.00) [0]
	<u>Heavy Industry</u>				
696	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	4/2011	9/2011 (-) [0/0]	1,718.00 (-) [3,827.30]	2,289.00 (2,109.30) [0]
	<u>Petroleum</u>				
697	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
698	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (-) [1,823.00]	270.94 (0.00) [0]
699	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	7.30 (0.00) [0]
700	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	71.07 (0.00) [0]
701	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	6/2007	9/2011 (6/2019) [6/2019]	736.65 (-) [571.47]	542.96 (-165.18) [93]
702	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	40.20 (0.00) [0]
703	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	9.75 (0.00) [0]
704	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	5/2013	4/2016 (3/2018) [3/2018]	4,124.35 (5,725.50) [5,725.50]	5,130.40 (1,601.15) [23]
705	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [10/2019]	890.00 (-) [887.00]	336.86 (-3.00) [0]
706	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2019) [2/2019]	2,915.00 (2,915.00) [2,915.00]	1,645.33 (0.00) [74]
707	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF	7/2015	12/2019	2,881.40	142.49

	VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT		(12/2020) [12/2019]	(-) [2,881.40]	(0.00) [0]
708	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	570.10 (0.00) [0]
709	PARADIP HALDIA DURGAPUR LPG PIPELINE	2/2011	6/2018 (-) [6/2018]	913.00 (1,330.00) [1,330.00]	1,200.16 (417.00) [0]
710	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (-) [2,321.00]	76.00 (0.00) [-4]
711	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (10/2020) [10/2020]	690.00 (-) [690.00]	135.02 (0.00) [27]
712	PARADIP-RAIPUR- RANCHI PIPELINE	8/2009	12/2016 (-) [0/0]	1,793.00 (-) [1,793.00]	1,788.86 (0.00) [0]
713	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	3/2015	12/2018 (-) [12/2018]	3,957.00 (3,561.00) [3,397.00]	1,961.00 (-560.00) [0]
714	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	1.58 (0.00) [0]
715	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)	11/2016	2/2019 (-) [2/2019]	230.00 (-) [230.00]	48.37 (0.00) [0]
716	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [11/2018]	352.56 (-) [438.84]	146.36 (86.28) [20]
717	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (3/2018) [2/2019]	309.81 (723.40) [723.40]	492.24 (413.59) [52]
	Power				
718	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [9/2019]	198.49 (-) [198.49]	0.00 (0.00) [0]
719	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION	10/2016	4/2019 (-) [4/2019]	167.75 (-) [167.75]	62.40 (0.00) [0]
720	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	3/2014	3/2016 (9/2018) [9/2018]	155.57 (206.42) [206.42]	143.20 (50.85) [30]
721	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	3/2013	12/2015 (6/2018) [6/2018]	2,514.88 (3,190.27) [3,190.27]	2,178.75 (675.39) [30]
722	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	3/2013	6/2015 (5/2018) [5/2018]	514.20 (703.10) [703.10]	598.00 (188.90) [35]
723	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2019]	4,754.42 (-) [9,141.97]	668.80 (4,387.55) [12]
724	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	0.00 (0.00) [0]
725	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (9/2018) [9/2018]	196.58 (225.28) [225.28]	143.00 (28.70) [31]
726	EASTERN REGION STRENGTHENING SCHEME XI	5/2016	11/2018 (-) [11/2018]	766.21 (-) [766.21]	193.60 (0.00) [0]
727	EASTERN REGION STRENGTHENING SCHEME XIV	5/2016	11/2018	167.01	63.90

			(-) [11/2018]	(-) [167.01]	(0.00) [0]
728	EASTERN REGION STRENGTHENING SCHEME-III	7/2010	11/2012 (9/2018) [9/2018]	1,272.80 (1,731.10) [1,731.10]	1,440.03 (458.30) [70]
729	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (12/2018) [12/2018]	1,364.52 (1,891.41) [1,891.41]	1,184.14 (526.89) [32]
730	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2019) [6/2019]	522.29 (550.18) [550.18]	394.40 (27.89) [31]
731	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	151.00 (0.00) [0]
732	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [6/2019]	235.53 (-) [235.53]	8.00 (0.00) [0]
733	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [2/2019]	322.30 (-) [322.30]	21.70 (0.00) [0]
734	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	3/2012	9/2014 (9/2017) [6/2018]	198.63 (-) [198.63]	137.93 (0.00) [45]
735	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [6/2018]	197.40 (-) [197.40]	64.90 (0.00) [3]
736	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [5/2019]	3,519.59 (-) [3,519.59]	1,113.30 (0.00) [0]
737	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	4/2015	4/2017 (3/2018) [5/2018]	1,479.30 (-) [1,479.30]	848.40 (0.00) [13]
738	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	4/2015	4/2018 (9/2018) [9/2018]	3,705.61 (-) [3,705.61]	2,392.90 (0.00) [5]
739	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C	7/2015	7/2018 (-) [7/2018]	2,247.37 (-) [2,247.37]	1,149.70 (0.00) [0]
740	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	323.07 (0.00) [0]
741	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	1,313.70 (0.00) [0]
742	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	29.20 (0.00) [0]
743	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	12.00 (0.00) [0]
744	INSTALLATION OF STATCOMS IN WESTERN REGION	3/2015	9/2017 (9/2018) [9/2018]	1,071.24 (-) [1,071.24]	547.00 (0.00) [12]
745	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B)	12/2014	4/2018 (-) [4/2018]	6,517.36 (-) [6,517.36]	3,772.80 (0.00) [0]
746	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2019]	5,111.33 (-) [5,111.33]	474.57 (0.00) [12]
747	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022)	11,130.19 (13,762.80)	12,639.60 (2,632.61)

			[3/2022]	[13,762.80]	[103]
748	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	2/2014	6/2016 (9/2018) [9/2018]	539.82 (-) [539.82]	400.50 (0.00) [27]
749	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA	3/2017	3/2019 (-) [3/2019]	162.31 (-) [162.31]	11.90 (0.00) [0]
750	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN	7/2016	3/2019 (-) [3/2019]	333.17 (-) [333.17]	220.50 (0.00) [0]
751	PROVISION OF SERIES REACTORS IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	177.52 (-) [177.52]	45.50 (0.00) [0]
752	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	431.89 (-) [431.89]	81.90 (0.00) [0]
753	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	7.71 (0.00) [0]
754	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (-) [3/2019]	562.25 (-) [562.25]	18.60 (0.00) [0]
755	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [4/2019]	3,654.00 (-) [3,654.00]	1,532.00 (0.00) [0]
756	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [4/2019]	608.24 (-) [608.24]	132.80 (0.00) [0]
757	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	8/2014	2/2017 (6/2018) [6/2018]	288.49 (-) [376.09]	234.30 (87.60) [16]
758	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [6/2019]	203.28 (260.03) [260.03]	178.70 (56.75) [23]
759	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [12/2019]	379.95 (-) [379.95]	19.70 (0.00) [0]
760	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-) [6/2019]	337.75 (-) [337.75]	6.00 (0.00) [0]
761	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION	1/2016	7/2018 (-) [7/2018]	1,455.47 (-) [1,455.47]	907.80 (0.00) [0]
762	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	8/2014 (9/2018) [9/2018]	297.33 (534.02) [534.02]	386.87 (236.69) [49]
763	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (12/2018) [12/2018]	487.49 (639.46) [639.46]	487.82 (151.97) [54]
764	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2018) [12/2018]	4,824.12 (5,071.94) [5,071.94]	4,514.68 (247.82) [74]
765	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A)	4/2015	11/2017 (-) [4/2018]	2,525.00 (-) [2,525.00]	1,783.00 (0.00) [5]
766	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	3/2015	12/2015 (-) [6/2018]	955.00 (1,161.00) [1,364.00]	1,125.00 (409.00) [30]
767	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	3/2018 (9/2018) [9/2018]	268.80 (340.88) [340.88]	190.10 (72.08) [6]

768	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	2/2010	12/2012 (6/2018) [6/2018]	2,144.00 (2,932.88) [2,932.88]	2,617.80 (788.88) [66]
769	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [9/2019]	871.62 (-) [871.62]	160.59 (0.00) [23]
770	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (-) [1/2019]	408.46 (-) [408.46]	70.81 (0.00) [0]
771	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I	4/2016	12/2018 (-) [12/2018]	810.48 (-) [810.48]	470.10 (0.00) [0]
772	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (3/2019) [3/2019]	5,151.37 (-) [5,151.37]	1,979.40 (0.00) [12]
773	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (3/2019) [3/2019]	808.63 (-) [808.63]	272.70 (0.00) [14]
774	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [6/2018]	374.63 (-) [374.63]	156.50 (0.00) [26]
775	WESTERN REGION STRENGTHENING SCHEME-XVI	7/2016	7/2018 (-) [7/2018]	150.99 (-) [150.99]	74.10 (0.00) [0]
776	WESTERN REGION STRENGTHENING SCHEME XVII	2/2017	9/2019 (-) [9/2019]	204.12 (-) [204.12]	10.30 (0.00) [0]
777	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (-) [2/2020]	195.05 (-) [195.05]	0.00 (0.00) [0]
	Railways				
778	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH	4/2010	/ (-) [0/0]	338.54 (-) [338.54]	212.64 (0.00) [0]
779	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [0/0]	288.35 (-) [238.36]	51.31 (-49.99) [0]
780	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [0/0]	450.55 (-) [251.05]	15.66 (-199.50) [0]
781	BHADRACHALAM ROAD-SATTUPALLI	4/2010	/ (-) [0/0]	337.49 (-) [704.31]	69.69 (366.82) [0]
782	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [923.23]	2.40 (0.00) [0]
783	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [0/0]	175.80 (-) [173.91]	18.54 (-1.89) [0]
784	CALICUT-MANGALORE (DL) (SR)	2/1996	/ (-) [0/0]	240.00 (-) [579.37]	537.30 (339.37) [0]
785	CHANDIGARH-BADDI NL	4/2007	/ (-) [0/0]	328.14 (-) [1,540.00]	45.20 (1,211.86) [0]
786	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [0/0]	337.96 (-) [186.89]	62.73 (-151.07) [0]
787	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,350.00]	2.27 (1,826.48) [0]

788	CHHAPRA-BALLIA UP	3/2013	/	295.00	149.76
			(-)	(-)	(182.31)
			[10/2018]	[477.31]	[-]
789	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	/	243.78	94.42
			(-)	(-)	(25.00)
			[8/2018]	[268.78]	[-]
790	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	/	595.91	103.62
			(-)	(-)	(0.00)
			[0/0]	[595.91]	[0]
791	CHOTTAUDEPUR-DHAR(NL)	4/2007	/	1,347.26	532.41
			(-)	(-)	(0.00)
			[0/0]	[1,347.26]	[0]
792	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	/	1,640.04	464.09
			(-)	(-)	(0.00)
			[3/2022]	[1,640.04]	[-]
793	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	/	296.44	15.83
			(-)	(-)	(-97.56)
			[0/0]	[198.88]	[0]
794	DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/	81,459.00	0.00
			(-)	(-)	(-53,278.00)
			[0/0]	[28,181.00]	[0]
795	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR	4/2013	/	1,239.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,239.00]	[0]
796	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/	336.91	143.18
			(-)	(-)	(0.00)
			[0/0]	[336.91]	[0]
797	DEOGHAR - SULTANGANJ (INL), ER	4/2000	12/2012	607.09	613.71
			(12/2012)	(-)	(366.24)
			[0/0]	[973.33]	[0]
798	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	2/2019	622.41	10.34
			(-)	(-)	(1,408.09)
			[12/2022]	[2,030.50]	[46]
799	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	/	553.63	7.93
			(-)	(-)	(455.37)
			[0/0]	[1,009.00]	[0]
800	GADWAL - RAICHUR (NL), SCR	4/1998	2/2011	92.63	320.46
			(-)	(-)	(257.37)
			[0/0]	[350.00]	[0]
801	GAYA-CHATRA (NL)	4/2008	/	415.67	14.62
			(-)	(-)	(134.08)
			[0/0]	[549.75]	[0]
802	GONDIA-JABALPUR(GC),(SECR)	2/1997	3/1998	386.30	967.96
			(-)	(-)	(1,390.51)
			[12/2019]	[1,776.81]	[261]
803	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/	636.38	0.00
			(-)	(-)	(0.00)
			[0/0]	[636.38]	[0]
804	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	4/1986	3/1994	158.77	629.43
			(-)	(274.56)	(475.71)
			[0/0]	[634.48]	[0]
805	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	2/2020	1,176.09	1.92
			(-)	(-)	(2,669.51)
			[12/2022]	[3,845.60]	[34]
806	HAJIPUR - BACHAWARA	5/2015	/	720.00	0.00
			(-)	(-)	(-41.46)
			[12/2018]	[678.54]	[-]
807	HANSDIHA-GODDA NL	4/2011	/	267.09	98.15
			(-)	(-)	(83.69)
			[0/0]	[350.78]	[0]
808	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/	172.03	6.42

			(-) [0/0]	(-) [260.60]	(88.57) [0]
809	HATHUA-BHATNI (N L) (NER)	4/2005	/	230.03	272.98
			(-) [5/2019]	(-) [718.54]	(488.51) [-]
810	HOTGI-KUDGI-GADAG	3/2015	/	1,618.00	555.23
			(-) [0/0]	(1,614.59) [1,614.59]	(-3.41) [0]
811	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	/	157.94	47.63
			(-) [11/2018]	(-) [157.94]	(0.00) [-]
812	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	0.02
			(-) [0/0]	(-) [166.89]	(0.00) [0]
813	JAGGAYYAPET - MELLACHERUVU	4/2007	1/1999	313.24	568.60
			(-) [0/0]	(-) [607.70]	(294.46) [0]
814	JAKHAL-MANSA DOUBLING ON SPR SECTION	4/2008	/	162.96	153.31
			(-) [0/0]	(-) [162.96]	(0.00) [0]
815	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	3/2002	6/2007	625.30	841.57
			(-) [0/0]	(408.76) [876.10]	(250.80) [0]
816	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	/	2,050.00	316.84
			(-) [0/0]	(-) [2,132.77]	(82.77) [0]
817	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	/	923.52	227.50
			(-) [0/0]	(-) [923.52]	(0.00) [0]
818	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/	174.56	56.25
			(-) [0/0]	(-) [160.97]	(-13.59) [0]
819	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	4/1999	/	744.71	761.70
			(-) [0/0]	(744.71) [1,126.79]	(382.08) [0]
820	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	4/2010	3/2017	423.66	456.58
			(-) [0/0]	(-) [720.59]	(296.93) [0]
821	KAZIPET-BALHRSHA	4/2015	/	2,063.03	202.11
			(-) [3/2021]	(-) [2,063.03]	(0.00) [-]
822	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	/	1,054.35	204.51
			(-) [0/0]	(1,693.00) [2,200.00]	(1,145.65) [0]
823	KURUPPANTHARA-CHINGAVANAM	4/2007	/	270.14	253.87
			(-) [0/0]	(-) [346.15]	(76.01) [0]
824	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	/	406.99	141.88
			(-) [0/0]	(-) [319.58]	(-87.41) [0]
825	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008	247.66	972.82
			(-) [3/2023]	(-) [6,093.31]	(5,845.65) [178]
826	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	/	601.43	77.17
			(-) [0/0]	(-) [1,800.00]	(1,198.57) [0]
827	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	/	493.96	135.79
			(-) [0/0]	(-) [681.68]	(187.72) [0]
828	MIRAJ-LONDA	3/2015	/	1,830.00	119.50
			(-)	(1,190.92)	(-639.08)

			[0/0]	[1,190.92]	[0]
829	MM FROM BURAMARA-CHAKULIA	4/2008	1/1999 (-) [0/0]	466.48 (-) [750.00]	0.00 (283.52) [0]
830	MONIGRAM- NIMITTA	4/2012	/ (-) [0/0]	250.93 (-) [259.23]	8.43 (8.30) [0]
831	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	/ (-) [3/2019]	218.24 (236.41) [525.00]	687.24 (306.76) [-]
832	MURKONGSELEK-PASIGHAT NL	4/2011	/ (-) [3/2020]	165.82 (-) [450.00]	122.97 (284.18) [-]
833	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [0/0]	450.00 (-) [2,100.00]	484.14 (1,650.00) [0]
834	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	/ (-) [0/0]	494.54 (-) [369.69]	31.99 (-124.85) [0]
835	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	/ (-) [3/2020]	242.22 (-) [471.00]	53.96 (228.78) [-]
836	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [0/0]	241.52 (-) [394.28]	148.33 (152.76) [0]
837	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	/ (-) [3/2019]	1,798.00 (-) [1,798.00]	0.00 (0.00) [-]
838	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [3/2018]	523.17 (-) [1,871.00]	1,081.98 (1,347.83) [-]
839	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2019]	733.00 (-) [3,040.00]	2,879.89 (2,307.00) [123]
840	PHULERA - DIGANA DOUBLING	5/2015	/ (-) [3/2020]	600.00 (-) [685.99]	3.05 (85.99) [-]
841	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [0/0]	261.38 (-) [332.14]	87.22 (70.76) [0]
842	PIRPAINTI-JASIDIH	4/2013	/ (-) [0/0]	915.98 (-) [1,130.13]	0.30 (214.15) [0]
843	PLASSEY-JIAGANJ DOUBLING	4/2011	3/2015 (-) [0/0]	248.07 (-) [234.41]	161.17 (-13.66) [0]
844	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [0/0]	299.60 (-) [269.60]	1.11 (-30.00) [0]
845	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	3/1998	/ (-) [0/0]	280.00 (-) [1,122.00]	834.61 (842.00) [0]
846	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [2,562.27]	181.66 (479.52) [0]
847	RAYADURGA-TUMKUR NL	4/2007	/ (-) [0/0]	970.34 (-) [1,714.49]	660.95 (744.15) [0]
848	SAINTHIA-TARAPITH 3RD LINE	4/2011	/ (-) [0/0]	193.44 (-) [186.64]	150.28 (-6.80) [0]

849	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE	4/2010	/	268.52	78.81
			(-)	(-)	(0.00)
			[0/0]	[268.52]	[0]
850	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/	297.47	52.01
			(-)	(-)	(-144.45)
			[0/0]	[153.02]	[0]
851	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	/	277.28	92.93
			(-)	(-)	(-11.28)
			[0/0]	[266.00]	[0]
852	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/	296.00	0.00
			(-)	(-)	(170.65)
			[0/0]	[466.65]	[0]
853	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/	450.00	9.31
			(-)	(-)	(-159.15)
			[0/0]	[290.85]	[0]
854	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/	365.17	1.37
			(-)	(-)	(0.50)
			[0/0]	[365.67]	[0]
855	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	4/2008	/	822.39	1,711.51
			(-)	(-)	(987.61)
			[3/2018]	[1,810.00]	[-]
856	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	4/2013	/	876.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[876.00]	[0]
857	YELAHANKA-PENUKONDA	5/2015	/	860.43	386.47
			(-)	(-)	(0.00)
			[3/2020]	[860.43]	[-]
Road Transport And Highways					
858	4 LANING OF NAGPUR-BETUL	2/2011	8/2014	2,498.76	0.00
			(-)	(-)	(0.00)
			[12/2017]	[2,498.76]	[0]
859	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015	1,928.22	0.00
			(-)	(-)	(0.00)
			[12/2017]	[1,928.22]	[0]
860	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018	788.51	0.00
			(-)	(-)	(0.00)
			[3/2018]	[788.51]	[0]
861	GWALIOR-JHANSI, NH-75	12/2003	12/2009	604.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[604.00]	[0]
862	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013	754.00	1,167.15
			(-)	(-)	(0.00)
			[11/2017]	[754.00]	[0]
863	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/	1,244.10	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,244.10]	[0]
864	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011	1,693.75	0.00
			(-)	(-)	(0.00)
			[9/2017]	[1,693.75]	[0]
865	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014	2,848.00	0.00
			(-)	(-)	(0.00)
			[4/2018]	[2,848.00]	[49]
866	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	3/2015	/	789.83	109.77
			(-)	(-)	(0.00)
			[0/0]	[789.83]	[0]
Telecommunications					
867	NETWORK FOR SPECTRUM	3/2012	7/2015	13,334.00	7,642.00
			(4/2020)	(-)	(11,330.00)
			[4/2020]	[24,664.00]	[57]
868	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014	2,111.17	253.90
			(-)	(-)	(-100.00)

			[0/0]	[2,011.17]	[0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
869	DIMAPUR-TIZIT NL	4/2013	/ (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [-]
870	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2020]	850.00 (-) [3,000.00]	431.96 (2,150.00) [60]
	<u>Road Transport And Highways</u>				
871	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
872	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
873	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
874	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
875	WIDENING OF 2(TWO) LANING OF LONGLENG- CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
876	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2020]	207.28 (-) [207.28]	219.29 (0.00) [96]
877	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2019]	172.08 (-) [172.08]	260.71 (0.00) [108]
878	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2019]	479.15 (-) [479.15]	105.89 (0.00) [0]
879	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	313.25 (0.00) [36]
880	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	374.32 (0.00) [0]
881	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2019]	479.53 (-) [479.53]	242.14 (0.00) [72]
882	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2019]	337.66 (-) [337.66]	32.84 (0.00) [0]
883	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2019]	457.77 (-) [457.77]	565.86 (0.00) [72]
884	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2018]	289.03 (-) [289.03]	0.00 (0.00) [0]
885	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2018]	302.96 (-) [302.96]	334.77 (0.00) [96]
886	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	682.70 (0.00) [0]
	<u>Mines</u>				

887	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	89.75 (0.00) [0]
888	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (11/2020) [11/2020]	355.00 (355.00) [355.00]	27.78 (0.00) [0]
889	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.00 (0.00) [0]
890	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	290.88 (0.00) [0]
	Petroleum				
891	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	2.12 (0.00) [0]
892	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (243.53) [243.53]	11.79 (0.00) [0]
893	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	213.63 (0.00) [0]
894	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [1/2019]	429.00 (-) [429.00]	133.17 (0.00) [0]
895	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	31.07 (0.00) [0]
896	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY	3/2014	3/2017 (10/2017) [10/2017]	238.50 (-) [238.50]	201.28 (0.00) [0]
897	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (12/2018) [12/2018]	3,150.00 (-) [3,150.00]	1,817.34 (0.00) [15]
	Power				
898	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	8/2018 (6/2019) [6/2019]	12,532.44 (-) [13,740.53]	7,588.00 (1,208.09) [10]
899	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (-) [4/2019]	844.64 (-) [844.64]	207.90 (0.00) [0]
	Railways				
900	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2019]	942.95 (-) [942.95]	850.22 (0.00) [0]
901	BHADRAK - NERGUNDI 3RD LINE	3/2013	/ (-) [3/2021]	858.67 (843.04) [843.04]	54.62 (-15.63) [-]
902	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	3/2021 (-) [3/2020]	1,172.92 (-) [1,172.92]	148.59 (0.00) [-12]
903	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
904	DELANG-PURI DOUBLING	3/2011	3/2015 (7/2015) [7/2015]	165.16 (-) [234.71]	226.35 (69.55) [0]
905	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2020]	5,200.00 (-) [5,200.00]	0.00 (0.00) [0]
906	HARIDASPUR-PARADEEP(NL)	4/1996	/	301.64	1,130.35

			(9/2009) [3/2019]	(-) [1,185.99]	(884.35) [-]
907	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2021 (-) [3/2021]	1,547.38 (1,547.38) [1,547.38]	117.43 (0.00) [0]
908	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	3/2021 (-) [3/2021]	701.61 (-) [810.02]	65.98 (108.41) [0]
909	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2017]	133.41 (207.00) [343.00]	364.71 (209.59) [0]
910	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	/ (-) [6/2021]	470.21 (-) [3,004.90]	1,004.23 (2,534.69) [-]
911	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2021 (-) [3/2022]	2,361.74 (2,361.74) [2,361.74]	43.73 (0.00) [12]
912	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [3/2020]	969.83 (-) [969.83]	268.65 (0.00) [0]
913	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	4/1995	12/2021 (-) [12/2021]	524.43 (-) [939.00]	183.99 (414.57) [0]
914	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	/ (-) [3/2020]	155.81 (-) [238.03]	162.11 (82.22) [-]
915	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2020]	960.18 (-) [960.18]	769.00 (0.00) [0]
916	SAMBALPUR-TALCHER DOUBLING	3/2011	/ (-) [3/2021]	679.27 (1,111.99) [1,579.27]	655.18 (900.00) [-]
917	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2019]	183.23 (-) [1,202.07]	523.88 (1,018.84) [58]
918	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	/ (-) [12/2022]	810.78 (1,928.07) [1,928.07]	491.88 (1,117.29) [-]
919	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	/ (-) [12/2024]	2,335.67 (-) [2,335.67]	85.34 (0.00) [-]
Road Transport And Highways					
920	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [0/0]	1,282.94 (-) [1,282.94]	0.00 (0.00) [0]
921	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	/ (-) [8/2019]	2,510.04 (-) [2,510.04]	0.00 (0.00) [-]
922	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [0/0]	752.28 (-) [752.28]	0.00 (0.00) [0]
923	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016 (-) [3/2017]	319.80 (320.00) [320.00]	0.00 (0.20) [0]
924	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016 (-) [10/2016]	319.80 (-) [319.80]	0.00 (0.00) [0]
925	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [0/0]	1,069.65 (-) [1,069.65]	0.00 (0.00) [0]
926	PANIKHOLI-RIMOLI	3/2012	9/2014	1,410.00	0.00

			(-) [3/2018]	(-) [1,410.00]	(0.00) [42]
927	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/	1,008.96	0.00
			(-) [0/0]	(-) [1,008.96]	(0.00) [0]
928	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPASS	1/2018	/	564.66	0.00
			(-) [0/0]	(-) [564.66]	(0.00) [0]
929	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017	476.56	0.00
			(-) [0/0]	(-) [476.56]	(0.00) [0]
930	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/	633.68	0.00
			(-) [0/0]	(-) [633.68]	(0.00) [0]
931	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/	953.09	0.00
			(-) [0/0]	(-) [953.09]	(0.00) [0]
932	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/	668.86	0.00
			(-) [0/0]	(-) [668.86]	(0.00) [0]
933	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/	614.48	0.00
			(-) [0/0]	(-) [614.48]	(0.00) [0]
934	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017	342.05	0.00
			(-) [1/2017]	(-) [342.05]	(0.00) [0]
935	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/	1,522.00	0.00
			(-) [0/0]	(-) [1,522.00]	(0.00) [0]
936	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/	503.88	0.00
			(-) [0/0]	(-) [503.88]	(0.00) [0]
937	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020	1,288.07	0.00
			(-) [3/2018]	(-) [1,420.00]	(131.93) [-24]
938	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/	686.65	0.00
			(-) [0/0]	(-) [686.65]	(0.00) [0]
939	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/	686.65	0.00
			(-) [0/0]	(-) [686.65]	(0.00) [0]
940	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/	417.51	0.00
			(-) [0/0]	(-) [417.51]	(0.00) [0]
941	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017	342.05	0.00
			(-) [0/0]	(342.00) [342.00]	(-0.05) [0]
942	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/	999.00	0.00
			(-) [0/0]	(-) [999.00]	(0.00) [0]
943	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016	171.96	0.00
			(-) [0/0]	(172.00) [172.00]	(0.04) [0]
944	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017	218.63	29.27
			(-) [10/2017]	(-) [218.63]	(0.00) [0]
945	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018	229.41	6.65
			(-) [5/2018]	(-) [229.41]	(0.00) [0]
946	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014	1,047.00	0.00
			(-)	(-)	(0.00)

			[12/2017]	[1,047.00]	[0]
947	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	3/2014	5/2016 (-) [3/2017]	162.51 (163.00) [163.00]	0.00 (0.49) [0]
948	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [6/2017]	191.50 (192.00) [192.00]	0.00 (0.50) [0]
949	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [10/2017]	239.91 (240.00) [240.00]	0.00 (0.09) [0]
950	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY	1/2015	4/2018 (-) [4/2018]	326.63 (327.00) [327.00]	0.00 (0.37) [0]
951	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [11/2018]	157.30 (157.00) [157.00]	0.00 (-0.30) [5]
952	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [11/2017]	159.39 (-) [159.39]	0.00 (0.00) [0]
953	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [3/2018]	191.08 (-) [191.08]	0.00 (0.00) [31]
954	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	3/2015	10/2017 (-) [10/2017]	226.31 (226.00) [226.00]	0.00 (-0.31) [0]
	Steel				
955	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (-) [2/2019]	3,127.30 (-) [3,127.30]	2,089.04 (0.00) [10]
	PUNJAB				
	Fertilisers				
956	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	17.53 (0.00) [0]
957	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	19.56 (0.00) [0]
	Health And Family Welfare				
958	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [8/2018]	152.95 (-) [152.95]	39.00 (0.00) [6]
	Railways				
959	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	4/2009	/ (-) [0/0]	396.04 (-) [369.00]	186.27 (-27.04) [0]
960	QADIAN-BEAS	4/2011	/ (-) [0/0]	205.22 (-) [205.22]	1.59 (0.00) [0]
	Road Transport And Highways				
961	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	/ (-) [0/0]	573.96 (605.00) [605.00]	209.74 (31.04) [0]
962	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	2/2015	/ (-) [0/0]	486.74 (-) [486.74]	189.39 (0.00) [0]
963	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (-) [1,169.61]	0.00 (0.00) [0]
964	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	11/2014	/ (-) [0/0]	463.65 (546.00) [463.65]	280.16 (0.00) [0]

965	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	2/2015	/ (-) [0/0]	483.38 (-) [483.38]	65.76 (0.00) [0]
966	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	2/2015	/ (-) [0/0]	616.36 (-) [616.36]	68.58 (0.00) [0]
967	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	299.81 (0.00) [0]
968	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [889.24]	389.64 (0.00) [0]
969	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	/ (-) [9/2019]	1,388.34 (-) [1,388.34]	0.00 (0.00) [-]
970	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	3/2015	/ (-) [0/0]	312.79 (-) [312.79]	17.57 (0.00) [0]
971	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K	7/2014	/ (-) [0/0]	319.80 (-) [319.80]	102.55 (0.00) [0]
972	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [3/2020]	754.54 (-) [756.27]	0.00 (1.73) [0]
973	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (-) [0/0]	766.36 (-) [766.36]	99.86 (0.00) [0]
974	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	12/2015	/ (-) [0/0]	578.38 (-) [578.38]	128.53 (0.00) [0]
975	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-) [4/2019]	447.29 (-) [447.29]	0.00 (0.00) [16]
976	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21	12/2015	12/2017 (-) [12/2017]	239.23 (-) [239.23]	0.00 (0.00) [0]
977	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [12/2017]	479.00 (-) [479.00]	0.00 (0.00) [0]
978	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	9/2015	/ (-) [11/2017]	273.06 (-) [273.06]	0.00 (0.00) [0]
979	JALANDHAR - AMRITSAR	1/2014	1/2016 (-) [12/2017]	523.85 (-) [523.85]	0.00 (0.00) [0]
980	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	3/2015	/ (-) [0/0]	435.90 (-) [435.90]	31.02 (0.00) [0]
981	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	1/2015	/ (-) [0/0]	279.68 (-) [279.68]	25.28 (0.00) [0]
982	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	6/2015	/ (-) [0/0]	899.21 (-) [899.21]	25.08 (0.00) [0]
983	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	26.92 (0.00) [0]
Urban Development					
984	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (2/2018) [8/2018]	388.00 (-) [388.00]	337.03 (0.00) [15]

985	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (6/2019) [6/2019]	294.00 (-) [294.00]	75.91 (0.00) [2]
	RAJASTHAN				
	Atomic Energy				
986	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (3/2017) [12/2020]	12,320.00 (-) [12,320.00]	9,147.00 (0.00) [48]
	Coal				
987	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	168.58 (0.00) [0]
988	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	6.22 (0.00) [0]
	Petroleum				
989	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
	Power				
990	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (-) [1/2019]	1,429.38 (-) [1,429.38]	353.90 (0.00) [0]
991	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	7/2015	11/2017 (10/2018) [10/2018]	307.18 (-) [307.18]	179.10 (0.00) [11]
	Railways				
992	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [873.71]	0.00 (0.00) [0]
993	AJMER-BANGURGRAM	4/2011	/ (-) [2/2019]	213.39 (218.39) [244.02]	141.37 (30.63) [-]
994	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [822.00]	0.00 (0.00) [0]
995	ALWAR-BANDIKUI DOUBLING	4/2013	/ (-) [3/2019]	242.09 (-) [349.00]	148.53 (106.91) [-]
996	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	/ (-) [3/2019]	246.08 (-) [348.55]	69.50 (102.47) [-]
997	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	/ (2/1997) [2/2019]	410.08 (780.98) [795.01]	392.08 (384.93) [-]
998	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	4/2008	3/2015 (-) [12/2019]	829.74 (-) [1,143.70]	568.36 (313.96) [57]
999	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	4/2008	3/2014 (-) [6/2019]	653.19 (-) [895.00]	694.56 (241.81) [63]
1000	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	/ (-) [0/0]	456.00 (295.02) [420.08]	38.50 (-35.92) [0]
1001	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2018]	493.17 (-) [493.17]	396.47 (0.00) [0]
1002	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [323.00]	0.00 (0.00) [0]
1003	RANI-MARWAR JN. PATCH DOUBLING	4/2012	/	288.97	228.38

			(-) [11/2018]	(-) [346.35]	(57.38) [-]
1004	THIYAT HAMIRA-SANU	4/2013	/	236.93	118.82
			(-) [10/2018]	(-) [294.90]	(57.97) [-]
	Road Transport And Highways				
1005	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [4/2018]	597.00 (-) [597.00]	0.00 (0.00) [6]
1006	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	/	320.30	0.00
			(-) [1/2019]	(-) [320.30]	(0.00) [-]
1007	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [0/0]	530.07 (-) [530.07]	0.00 (0.00) [0]
1008	2-LANING WITH PS BHILWARA-LODPURA SECTION	3/2014	3/2016 (-) [0/0]	240.10 (-) [240.10]	0.00 (0.00) [0]
1009	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/	688.70	0.00
			(-) [0/0]	(-) [688.70]	(0.00) [0]
1010	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/	1,031.95	0.00
			(-) [0/0]	(-) [1,031.95]	(0.00) [0]
1011	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [4/2018]	822.90 (-) [822.90]	0.00 (0.00) [0]
1012	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	2/2010 (-) [0/0]	275.00 (-) [281.31]	0.00 (6.31) [0]
1013	DEOLI KOTA	1/2011	7/2013 (-) [10/2017]	593.00 (-) [593.00]	0.00 (0.00) [0]
1014	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO	12/2017	/	1,308.73	0.00
			(-) [0/0]	(-) [1,308.73]	(0.00) [0]
1015	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [6/2019]	763.23 (-) [763.23]	0.00 (0.00) [0]
1016	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [6/2019]	649.00 (-) [649.00]	0.00 (0.00) [0]
1017	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	0.00 (0.00) [0]
1018	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [12/2017]	1,673.70 (-) [1,673.70]	0.00 (0.00) [0]
1019	JAISALMER - BARMER	8/2015	2/2018 (-) [2/2018]	482.27 (-) [482.27]	0.00 (0.00) [0]
1020	JODHPUR - BARMER SECTION OF PACKAGE -I	10/2014	4/2017 (-) [0/0]	264.72 (-) [264.72]	0.00 (0.00) [0]
1021	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [10/2013]	511.00 (-) [511.00]	0.00 (0.00) [0]
1022	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [10/2013]	511.00 (-) [511.00]	0.00 (0.00) [0]
1023	PADI - DAHOD	11/2014	5/2017	279.14	0.00

			(-) [0/0]	(-) [279.14]	(0.00) [0]
1024	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	9/2015	3/2018 (-) [3/2018]	567.51 (-) [567.51]	0.00 (0.00) [0]
1025	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1026	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	1/1991	5/2016 (-) [5/2016]	208.87 (-) [208.87]	206.78 (0.00) [0]
1027	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	1/1991	10/2016 (-) [10/2016]	269.26 (-) [269.26]	212.72 (0.00) [0]
1028	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1029	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [0/0]	1,100.19 (-) [1,100.19]	0.00 (0.00) [0]
1030	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [0/0]	1,239.82 (-) [1,239.82]	0.00 (0.00) [0]
1031	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [4/2020]	894.00 (-) [894.00]	0.00 (0.00) [0]
1032	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50)	7/2015	7/2017 (-) [7/2017]	455.60 (-) [455.60]	0.00 (0.00) [0]
1033	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N	8/2015	2/2018 (-) [2/2018]	538.08 (-) [538.08]	0.00 (0.00) [0]
1034	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (-) [9/2017]	425.19 (-) [425.19]	0.00 (0.00) [0]
1035	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [2/2018]	275.90 (-) [275.90]	0.00 (0.00) [0]
1036	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	/ (-) [10/2018]	331.46 (-) [331.46]	0.00 (0.00) [-]
1037	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR	6/2016	6/2019 (-) [0/0]	637.18 (-) [637.18]	0.00 (0.00) [0]
1038	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.80 (0.00) [0]
1039	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	224.68 (0.00) [0]
1040	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1041	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [6/2018]	621.43 (-) [621.43]	0.00 (0.00) [0]
	Steel				
1042	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [8/2018]	189.00 (-) [189.00]	0.00 (0.00) [17]
	Urban Development				

1043	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN	8/2014	3/2015 (12/2017) [4/2018]	350.02 (479.87) [479.87]	452.35 (129.85) [37]
	SIKKIM				
	Civil Aviation				
1044	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	1/2009	1/2011 (-) [0/0]	309.46 (-) [553.53]	522.95 (244.07) [0]
	Railways				
1045	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	Road Transport And Highways				
1046	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
1047	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
1048	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
1049	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [10/2017]	388.00 (-) [447.37]	0.00 (59.37) [0]
	TAMIL NADU				
	Atomic Energy				
1050	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	2,133.00 (0.00) [36]
1051	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [6/2018]	3,492.00 (5,677.00) [6,100.00]	5,591.34 (2,608.00) [93]
	Coal				
1052	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (9/2019) [9/2019]	1,458.17 (709.06) [709.06]	349.99 (-749.11) [51]
1053	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (4/2018) [4/2018]	5,907.11 (-) [5,907.11]	5,229.45 (0.00) [28]
1054	NEYVELI SOLAR POWER PROJECT 130 MW	5/2016	6/2017 (12/2017) [4/2018]	687.28 (-) [767.00]	756.08 (79.72) [10]
	Petroleum				
1055	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	0.13 (0.00) [0]
1056	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	186.78 (0.00) [0]
1057	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [10/2020]	466.43 (-) [466.43]	1.18 (0.00) [0]
1058	ENNORE TERMINAL	8/2014	4/2018 (-) [4/2018]	393.00 (-) [393.00]	281.45 (0.00) [0]
1059	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [12/2018]	4,497.00 (-) [4,497.00]	93.11 (0.00) [0]
1060	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-)	711.00 (-)	11.12 (0.00)

			[6/2020]	[711.00]	[0]
1061	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (-) [4/2019]	390.52 (390.52) [390.52]	95.40 (0.00) [1]
1062	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [0/0]	678.00 (-) [678.00]	5.08 (0.00) [0]
1063	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	5/2015	11/2016 (-) [6/2018]	257.87 (-) [257.87]	202.35 (0.00) [19]
1064	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	1.31 (0.00) [0]
1065	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.42 (0.00) [0]
	Power				
1066	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	9/2011	9/2014 (9/2018) [9/2018]	1,940.13 (2,702.65) [2,702.65]	2,420.46 (762.52) [48]
1067	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (9/2018) [9/2018]	1,779.29 (2,187.32) [2,187.32]	2,000.25 (408.03) [118]
1068	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [7/2019]	186.17 (-) [186.17]	13.60 (0.00) [0]
	Railways				
1069	ATTIPPATTU PUTTUR	4/2008	/ (1/2011) [0/0]	446.87 (527.37) [1,105.00]	3.34 (658.13) [0]
1070	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	4/1998	/ (-) [0/0]	271.24 (-) [520.00]	468.18 (248.76) [0]
1071	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	9/2006	/ (-) [0/0]	343.17 (-) [1,065.00]	1,049.68 (721.83) [0]
1072	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1073	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [3/2017]	495.74 (495.74) [732.89]	390.56 (237.15) [0]
1074	KARUR-SALEM(NL),SR	2/1997	/ (-) [0/0]	155.55 (-) [920.00]	856.94 (764.45) [0]
1075	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [0/0]	164.41 (-) [450.00]	36.26 (285.59) [0]
1076	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	/ (-) [0/0]	404.19 (-) [2,072.50]	1,048.37 (1,668.31) [0]
1077	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.61 (661.00) [0]
1078	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	4/2011	/ (-) [3/2018]	190.10 (-) [350.00]	320.41 (159.90) [-]
1079	TIDIVANAM-NAGARI (NL)	9/2006	/ (7/2008) [0/0]	456.00 (582.83) [2,300.00]	231.40 (1,844.00) [0]
	Road Transport And Highways				

1080	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [12/2018]	485.00 (-) [485.00]	406.68 (0.00) [64]
1081	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1082	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	0.00 (0.00) [0]
1083	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [0/0]	1,227.87 (-) [1,227.87]	0.00 (0.00) [0]
1084	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1085	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [8/2015]	154.14 (-) [154.14]	0.00 (0.00) [0]
1086	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [0/0]	600.00 (-) [600.00]	319.76 (0.00) [0]
1087	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [8/2018]	1,387.11 (-) [1,387.11]	769.28 (0.00) [9]
1088	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [7/2018]	641.17 (-) [641.17]	173.62 (0.00) [24]
1089	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [0/0]	1,176.37 (-) [1,176.37]	0.00 (0.00) [0]
1090	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	/ (-) [8/2018]	707.82 (-) [707.82]	129.75 (0.00) [-]
1091	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	0.00 (0.00) [0]
1092	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	/ (-) [7/2018]	641.17 (-) [641.17]	74.13 (0.00) [-]
1093	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1094	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [0/0]	379.90 (-) [379.90]	0.00 (0.00) [0]
1095	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [12/2018]	1,250.00 (-) [1,250.00]	1,329.31 (0.00) [60]
1096	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	11/2014	11/2016 (-) [6/2018]	563.92 (-) [563.92]	186.50 (0.00) [19]
1097	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1098	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	761.19 (0.00) [0]
1099	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [12/2018]	374.00 (-) [374.00]	237.00 (0.00) [67]
1100	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017	563.92	95.89

			(-) [12/2018]	(-) [563.92]	(0.00) [12]
	Shipping And Ports				
1101	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED	12/2014	4/2017 (12/2017) [0/0]	274.85 (334.00) [321.94]	321.94 (47.09) [0]
1102	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017 (5/2020) [5/2020]	600.00 (257.90) [257.90]	1.45 (-342.10) [29]
1103	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	6/2017 (-) [0/0]	198.94 (247.00) [255.00]	255.02 (56.06) [0]
1104	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017 (3/2018) [0/0]	244.50 (258.33) [275.98]	275.98 (31.48) [0]
1105	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006 (-) [0/0]	150.00 (-) [600.00]	139.80 (450.00) [0]
1106	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008 (-) [0/0]	2,427.40 (-) [2,427.40]	831.21 (0.00) [0]
	Urban Development				
1107	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	/ (-) [10/2019]	209.00 (-) [209.00]	26.00 (0.00) [-]
1108	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [3/2018]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1109	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	14,784.59 (4,458.00) [0]
1110	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [0/0]	348.77 (-) [348.77]	0.00 (0.00) [0]
1111	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	4/2014	9/2016 (3/2018) [5/2018]	332.72 (-) [321.00]	305.18 (-11.72) [20]
	TELANGANA				
	Coal				
1112	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	0.00 (0.00) [0]
1113	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2019]	426.79 (-) [426.79]	0.00 (0.00) [12]
1114	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2021]	447.06 (-) [437.51]	316.06 (-9.55) [72]
1115	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1116	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2019]	397.09 (-) [442.42]	78.04 (45.33) [0]
1117	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [417.33]	137.69 (0.00) [44]
1118	KISTARAM OCP	11/2010	3/2015 (-) [3/2020]	242.29 (-) [164.04]	0.37 (-78.25) [60]
1119	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012	181.19	159.87

			(-) [3/2018]	(-) [181.19]	(0.00) [72]
1120	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	48.57 (70.65) [132]
1121	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2020]	162.76 (-) [349.28]	1.31 (186.52) [60]
1122	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2019]	430.45 (-) [415.37]	154.69 (-15.08) [36]
1123	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [3/2018]	365.01 (-) [365.01]	125.24 (0.00) [33]
1124	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2018]	209.78 (-) [209.78]	154.52 (0.00) [36]
1125	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2019]	249.03 (-) [448.86]	186.19 (199.83) [84]
	Power				
1126	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	7/2020 (10/2020) [10/2020]	10,598.98 (-) [10,598.98]	1,849.00 (0.00) [3]
	Railways				
1127	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2017]	632.68 (-) [816.55]	523.33 (183.87) [0]
1128	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	169.16 (0.00) [0]
1129	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	616.08 (-) [616.08]	0.00 (0.00) [0]
1130	MACHERLA-NALGONDA(NL)(SCR)	7/1998	7/2008 (-) [0/0]	125.00 (-) [458.26]	3.69 (333.26) [0]
1131	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	0.00 (65.24) [0]
1132	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	/ (-) [3/2022]	378.56 (-) [1,160.47]	18.25 (781.91) [-]
1133	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [1,112.00]	0.92 (0.00) [0]
1134	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	/ (-) [0/0]	124.43 (-) [1,010.00]	1,013.26 (885.57) [0]
1135	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	728.10 (-) [728.10]	120.70 (0.00) [0]
	Road Transport And Highways				
1136	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	1/2014	3/2016 (-) [0/0]	340.00 (-) [340.00]	0.00 (0.00) [0]
1137	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [6/2018]	1,266.60 (-) [1,266.60]	1,375.60 (0.00) [21]
1138	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-	3/2011	12/2015 (-)	218.31 (-)	208.28 (121.51)

	202 UNDER LWE S		[0/0]	[339.82]	[0]
1139	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [1/2017]	153.21 (-) [153.21]	0.00 (0.00) [0]
1140	FOUR LANING OF YADGIRI - WARANGAL	12/2015	/ (-) [11/2018]	1,423.96 (-) [1,423.96]	0.00 (0.00) [-]
1141	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO	12/2013	3/2016 (-) [0/0]	158.65 (-) [158.65]	103.50 (0.00) [0]
1142	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S	12/2013	3/2016 (-) [0/0]	177.18 (-) [177.18]	40.51 (0.00) [0]
1143	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1144	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [2/2017]	295.47 (-) [313.27]	0.00 (17.80) [0]
1145	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	10/2014	12/2016 (-) [12/2016]	244.30 (-) [156.09]	0.00 (-88.21) [0]
1146	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW	12/2013	3/2016 (-) [0/0]	244.08 (-) [244.08]	38.32 (0.00) [0]
	Urban Development				
1147	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [3/2020]	209.84 (-) [209.84]	1.65 (0.00) [0]
	TRIPURA				
	Petroleum				
1148	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A	5/2016	6/2017 (-) [1/2018]	215.38 (-) [215.38]	186.58 (0.00) [0]
	Power				
1149	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	Railways				
1150	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (-) [3/2020]	813.34 (-) [3,451.00]	2,589.60 (2,637.66) [72]
1151	AGARTALA-AKHAURA NL	4/2012	/ (-) [7/2019]	252.00 (-) [580.00]	0.00 (328.00) [-]
1152	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (-) [1,857.00]	1,529.91 (962.00) [0]
	Road Transport And Highways				
1153	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [3/2018]	369.00 (-) [369.00]	36.90 (0.00) [0]
1154	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [4/2017]	497.89 (-) [497.89]	70.47 (0.00) [0]
	Steel				
1155	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1156	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-)	202.61 (227.00)	199.95 (24.39)

			[0/0]	[227.00]	[0]
1157	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	UTTAR PRADESH				
	Coal				
1158	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	6/2011	3/2018 (-) [3/2018]	1,131.28 (-) [1,131.28]	447.32 (0.00) [0]
1159	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	1,493.82 (0.80) [0]
	Health And Family Welfare				
1160	AIIMS-RAE BARELI-HOUSING	10/2013	11/2013 (-) [0/0]	159.50 (-) [159.50]	158.65 (0.00) [0]
	Petroleum				
1161	AURAIYA PHULPUR PIPELINE PROJECT	7/2015	12/2018 (-) [12/2018]	1,427.94 (-) [750.00]	534.34 (-677.94) [0]
1162	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	100.02 (0.00) [0]
1163	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	48.24 (0.00) [0]
1164	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [8/2021]	318.80 (-) [318.80]	0.00 (0.00) [0]
	Power				
1165	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (2/2018) [3/2019]	195.42 (294.60) [294.60]	162.82 (99.18) [61]
1166	FGUTPP, UNCHAHAHAR STAGE-IV (1X500 MW)	7/2013	12/2016 (-) [0/0]	3,363.12 (-) [3,363.12]	2,244.00 (0.00) [0]
1167	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	12/2016 (-) [2/2019]	9,750.89 (-) [9,750.89]	6,957.91 (0.00) [26]
1168	TANDA TPP STAGE-II (2X660 MW)	9/2014	3/2019 (9/2019) [9/2019]	9,188.98 (-) [9,188.98]	4,333.00 (0.00) [6]
	Railways				
1169	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	4/1999	12/2009 (-) [0/0]	108.00 (-) [432.72]	446.52 (324.72) [0]
1170	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [308.00]	0.00 (1.00) [0]
1171	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	3/2012	/ (-) [8/2018]	199.75 (-) [227.00]	241.05 (27.25) [-]
1172	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2020]	1,183.25 (-) [1,183.30]	797.44 (0.05) [0]
1173	BHOJIPUR TANAKPUR VIA PILIBHIT	3/2008	/ (-) [3/2018]	195.64 (-) [474.30]	430.32 (278.66) [-]
1174	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]

1175	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [245.39]	210.67 (125.39) [0]
1176	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	4/2013	/ (-) [0/0]	654.00 (-) [654.00]	0.00 (0.00) [0]
1177	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1178	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1179	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2018 (-) [3/2019]	528.57 (-) [528.57]	0.61 (0.00) [12]
1180	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2019]	927.01 (-) [977.00]	863.23 (49.99) [0]
1181	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [3/2020]	524.00 (668.00) [668.00]	0.00 (144.00) [0]
1182	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	12/2025 (-) [12/2025]	1,765.90 (-) [1,765.92]	95.72 (0.02) [0]
1183	MEERUT-MUZAFARNAGAR PATCH DL	4/2012	/ (-) [0/0]	377.44 (-) [377.44]	182.85 (0.00) [0]
1184	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2020]	2,436.21 (-) [2,436.21]	166.13 (0.00) [0]
1185	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,750.00 (-) [1,295.42]	52.27 (-454.58) [0]
1186	UNCHAHAR-AMETHI	4/2012	/ (-) [0/0]	380.00 (-) [380.00]	4.12 (0.00) [0]
1187	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	4/2006	3/2010 (-) [0/0]	325.00 (-) [1,581.53]	618.19 (1,256.53) [0]
1188	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	12/2024 (-) [12/2024]	750.55 (-) [750.56]	45.50 (0.01) [0]
Road Transport And Highways					
1189	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [9/2017]	368.73 (-) [368.73]	0.00 (0.00) [0]
1190	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [3/2017]	305.49 (-) [305.49]	0.00 (0.00) [0]
1191	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [11/2017]	351.34 (-) [351.34]	409.92 (0.00) [0]
1192	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [11/2017]	495.78 (-) [495.78]	566.34 (0.00) [0]
1193	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [12/2017]	291.36 (-) [291.36]	347.49 (0.00) [0]
1194	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	147.92 (0.00) [0]

1195	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	/ (-) [4/2019]	2,016.00 (-) [2,016.00]	0.00 (0.00) [-]
1196	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [0/0]	1,668.00 (-) [1,668.00]	0.00 (0.00) [0]
1197	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [6/2018]	611.65 (-) [611.65]	383.55 (0.00) [24]
1198	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [0/0]	1,408.00 (-) [1,408.00]	0.00 (0.00) [0]
1199	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [0/0]	1,737.00 (-) [1,737.00]	0.00 (0.00) [0]
1200	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	28.08 (0.00) [0]
1201	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	/ (-) [4/2019]	1,587.49 (-) [1,587.49]	24.95 (0.00) [-]
1202	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	13.55 (0.00) [0]
1203	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	/ (-) [1/2019]	1,657.20 (-) [1,657.20]	545.00 (0.00) [-]
1204	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [3/2020]	2,064.99 (-) [2,447.00]	23.48 (382.01) [0]
1205	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1206	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	/ (-) [4/2019]	676.73 (-) [676.73]	115.21 (0.00) [-]
1207	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	6/2015	3/2018 (-) [3/2018]	774.57 (-) [774.57]	0.00 (0.00) [0]
1208	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150	1/2014	10/2016 (-) [10/2016]	397.04 (-) [397.04]	0.00 (0.00) [0]
1209	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43	10/2013	3/2017 (-) [3/2017]	317.76 (-) [317.76]	15.47 (0.00) [0]
1210	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [10/2017]	1,046.00 (-) [1,046.00]	693.46 (0.00) [0]
1211	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	3/2015	/ (-) [0/0]	629.74 (-) [629.74]	0.00 (0.00) [0]
1212	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [534.55]	49.05 (0.00) [0]
1213	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1214	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	165.66 (0.00) [0]
1215	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY	1/2014	3/2016	282.41	0.00

	(PHASE -I) ON EASTERN SIDE OF NH 24B		(-) [3/2016]	(-) [282.41]	(0.00) [0]
1216	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	1/2016	/	701.12	0.00
			(-) [5/2019]	(-) [701.12]	(0.00) [-]
1217	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	/	1,081.57	0.00
			(-) [6/2019]	(-) [1,081.57]	(0.00) [-]
1218	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/	1,232.21	0.00
			(-) [0/0]	(-) [1,232.21]	(0.00) [0]
1219	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020	1,989.00	0.00
			(-) [3/2020]	(-) [1,989.00]	(0.00) [0]
1220	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018	785.78	796.52
			(-) [3/2018]	(-) [785.78]	(0.00) [0]
1221	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV)	9/2015	3/2018	789.31	814.19
			(-) [3/2018]	(-) [789.31]	(0.00) [0]
1222	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V)	9/2015	3/2018	664.53	590.82
			(-) [3/2018]	(-) [664.53]	(0.00) [0]
1223	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI)	9/2015	3/2018	768.56	699.98
			(-) [3/2018]	(-) [768.56]	(0.00) [0]
1224	ETAWAH CHAKERI	3/2013	9/2015	1,573.00	1,850.00
			(-) [10/2017]	(-) [1,573.00]	(0.00) [0]
1225	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018	667.00	247.71
			(-) [6/2018]	(-) [667.00]	(0.00) [0]
1226	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018	667.00	195.03
			(-) [6/2018]	(-) [667.00]	(0.00) [-1]
1227	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018	1,027.53	228.89
			(-) [6/2018]	(-) [1,027.53]	(0.00) [0]
1228	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018	815.28	141.16
			(-) [6/2018]	(-) [815.28]	(0.00) [0]
1229	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017	261.09	86.28
			(-) [6/2018]	(-) [261.09]	(0.00) [13]
1230	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020	1,373.28	0.00
			(-) [3/2020]	(-) [1,373.28]	(0.00) [0]
1231	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020	1,184.71	0.00
			(-) [3/2020]	(-) [1,310.00]	(125.29) [0]
1232	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	/	899.00	0.00
			(-) [4/2019]	(-) [899.00]	(0.00) [-]
1233	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013	1,141.00	1,986.56
			(-) [8/2017]	(-) [1,141.00]	(0.00) [0]
1234	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	10/2013	10/2016	283.45	0.00
			(-) [10/2016]	(-) [283.45]	(0.00) [0]
1235	MEERUT-BULANDSHAHAH	1/2016	/	683.24	0.45
			(-)	(-)	(0.00)

			[0/0]	[683.24]	[0]
1236	MURADABAD-BAREILY	4/2010	6/2013 (-) [9/2017]	1,267.00 (-) [1,267.00]	2,667.96 (0.00) [0]
1237	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [3/2017]	445.89 (-) [445.89]	0.00 (0.00) [0]
1238	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	10/2013	3/2017 (-) [3/2017]	493.94 (-) [493.94]	0.00 (0.00) [0]
1239	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	10/2014	10/2016 (-) [10/2016]	227.74 (-) [227.74]	0.00 (0.00) [0]
1240	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1241	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1242	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1243	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [8/2015]	164.54 (-) [164.54]	0.00 (0.00) [0]
	Steel				
1244	FORGED WHEEL PLANT	4/2014	9/2018 (-) [1/2019]	1,682.85 (-) [1,682.85]	276.10 (0.00) [4]
	Telecommunications				
1245	UP (EAST) ACCESS LOT1	11/2017	8/2018 (-) [8/2018]	169.45 (-) [169.45]	0.00 (0.00) [0]
	Urban Development				
1246	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	UTTARAKHAND				
	Petroleum				
1247	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [2/2020]	160.10 (-) [160.10]	23.99 (0.00) [0]
	Power				
1248	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	0.00 (274.07) [0]
1249	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	100.37 (0.00) [0]
1250	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (-) [3,846.30]	3,521.00 (867.82) [93]
1251	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (9/2019) [12/2020]	1,657.00 (2,978.86) [4,401.90]	2,540.27 (2,744.90) [58]
1252	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [11/2020]	2,491.58 (-) [3,789.61]	1,393.67 (1,298.03) [89]
	Railways				
1253	HARIDWAR-LAKSAR	4/2012	/ (-)	219.83 (-)	38.33 (126.80)

			[0/0]	[346.63]	[0]
1254	KICHHA-KHATIMA (NL) - NER	4/2003	/	142.45	0.15
			(-)	(-)	(85.95)
			[0/0]	[228.40]	[0]
1255	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2026	4,295.30	761.30
			(-)	(-)	(11,920.70)
			[12/2026]	[16,216.00]	[0]
	Road Transport And Highways				
1256	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018	403.36	0.00
			(-)	(-)	(0.00)
			[6/2018]	[403.36]	[0]
1257	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018	417.24	0.00
			(-)	(-)	(0.00)
			[5/2018]	[417.24]	[0]
1258	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	/	605.84	578.25
			(-)	(-)	(0.00)
			[7/2018]	[605.84]	[-]
1259	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/	1,443.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,443.00]	[0]
1260	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018	274.31	0.00
			(-)	(-)	(0.00)
			[5/2018]	[274.31]	[0]
1261	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/	720.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[720.00]	[0]
1262	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013	478.51	0.00
			(-)	(-)	(-0.51)
			[12/2017]	[478.00]	[0]
	Urban Development				
1263	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	114.26	0.00
			(-)	(266.00)	(151.74)
			[10/2019]	[266.00]	[70]
	WEST BENGAL				
	Coal				
1264	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022	602.86	293.94
			(-)	(-)	(0.00)
			[3/2022]	[602.86]	[0]
1265	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018	1,055.05	343.50
			(-)	(-)	(0.00)
			[3/2020]	[1,055.05]	[24]
	Health And Family Welfare				
1266	CNCI KOLKATA WEST BENGAL	8/2016	9/2018	244.00	77.50
			(-)	(-)	(0.00)
			[9/2018]	[244.00]	[0]
1267	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017	168.90	110.00
			(-)	(-)	(22.48)
			[3/2018]	[191.38]	[10]
1268	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019	355.15	21.79
			(-)	(-)	(0.00)
			[3/2019]	[355.15]	[0]
	Petroleum				
1269	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	3/2014	9/2017	3,076.00	2,548.03
			(6/2018)	(4,190.00)	(1,114.00)
			[6/2018]	[4,190.00]	[9]
1270	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020	1,740.00	9.30
			(-)	(-)	(0.00)
			[12/2020]	[1,740.00]	[0]
1271	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020	1,021.00	5.73
			(-)	(-)	(0.00)
			[12/2020]	[1,021.00]	[0]

1272	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (-) [10/2018]	694.00 (-) [694.00]	315.57 (0.00) [0]
1273	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [4/2020]	163.02 (-) [163.02]	28.93 (0.00) [0]
	Power				
1274	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (-) [4/2018]	454.11 (-) [454.11]	198.70 (0.00) [0]
1275	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	4/2007	2/2011 (-) [0/0]	4,122.00 (8,781.00) [9,142.58]	8,300.00 (5,020.58) [0]
1276	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,381.84]	322.00 (0.00) [29]
	Railways				
1277	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	4/1999	12/2012 (-) [0/0]	207.52 (-) [334.87]	293.47 (127.35) [0]
1278	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [0/0]	1,027.40 (-) [2,373.00]	484.33 (1,345.60) [0]
1279	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [0/0]	1,106.62 (-) [1,106.62]	355.85 (0.00) [0]
1280	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [0/0]	255.64 (-) [272.20]	0.64 (16.56) [0]
1281	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	4/2011	/ (-) [0/0]	289.64 (-) [760.00]	0.13 (470.36) [0]
1282	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [0/0]	267.37 (-) [434.00]	40.77 (166.63) [0]
1283	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [0/0]	573.78 (-) [268.52]	0.67 (-305.26) [0]
1284	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	4/2009	12/2011 (-) [0/0]	533.38 (-) [533.38]	127.10 (0.00) [0]
1285	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2018]	4,874.58 (-) [4,874.58]	1,881.65 (0.00) [27]
1286	GHUTIASARIF-CANNING (ER)	4/2009	12/2011 (-) [0/0]	611.03 (-) [611.03]	146.31 (0.00) [0]
1287	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.48 (632.54) [0]
1288	MM FROM PANSKURA-GHATAL NL	4/2011	1/1999 (-) [0/0]	276.69 (-) [426.00]	0.00 (149.31) [0]
1289	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [3/2020]	221.42 (-) [380.00]	97.41 (158.58) [-]
1290	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	/ (-) [3/2020]	36.80 (274.41) [614.00]	262.63 (577.20) [-]
1291	NEW COOCHBEHAR TO SAMUKTALA	4/2011	/ (-)	209.77 (-)	620.04 (420.23)

			[3/2018]	[630.00]	[-]
1292	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	4/2012	/ (-) [3/2019]	283.55 (-) [450.00]	361.54 (166.45) [-]
1293	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	/ (-) [3/2020]	556.31 (-) [612.00]	0.00 (55.69) [-]
1294	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [0/0]	2,298.42 (-) [2,070.00]	40.16 (-228.42) [0]
1295	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [12/2018]	2,913.51 (-) [2,913.50]	750.71 (-0.01) [33]
1296	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1297	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [12/2020]	3,951.98 (-) [4,259.48]	1,635.74 (307.50) [57]
1298	PANDABESWAR-CHINPAI DOUBLING (ER)	4/2004	12/2010 (-) [0/0]	293.74 (-) [229.33]	140.60 (-64.41) [0]
1299	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	1/1991	12/2021 (-) [12/2021]	763.18 (-) [1,428.00]	484.47 (664.82) [0]
1300	TAMLUK DIGHA, LINE DOUBLING (SER)	3/1984	6/2005 (-) [0/0]	293.97 (-) [749.69]	0.00 (455.72) [0]
1301	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	/ (12/2009) [3/2019]	1,188.91 (-) [1,319.33]	757.23 (130.42) [-]
1302	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,544.30 (2,355.23) [0]
Road Transport And Highways					
1303	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [6/2018]	1,083.00 (-) [1,083.00]	184.92 (0.00) [0]
1304	4-LANING OF BRAHAMPUR-FARAKA	2/2011	8/2013 (-) [3/2018]	998.79 (-) [998.79]	1,952.35 (0.00) [55]
1305	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [12/2017]	1,078.84 (-) [1,078.84]	2,436.15 (0.00) [0]
1306	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [12/2017]	1,396.18 (-) [1,396.18]	2,811.29 (0.00) [0]
1307	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2018]	361.15 (-) [361.15]	0.00 (0.00) [0]
1308	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	/ (-) [11/2018]	229.37 (-) [229.37]	35.17 (0.00) [-]
1309	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	/ (-) [8/2018]	767.03 (-) [767.03]	123.13 (0.00) [-]
1310	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [3/2018]	702.16 (-) [702.16]	564.39 (0.00) [44]
1311	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	3/2018 (-)	322.00 (-)	56.41 (0.00)

	BANKUARA- PURUL		[3/2018]	[322.00]	[0]
1312	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/	1,665.00	2,313.68
			(-)	(-)	(0.00)
			[12/2017]	[1,665.00]	[0]
	Steel				
1313	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016	185.37	178.30
			(-)	(-)	(0.00)
			[0/0]	[185.37]	[0]
	Urban Development				
1314	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016	156.57	133.20
			(-)	(-)	(0.00)
			[6/2018]	[156.57]	[22]
1315	NSG AT KOLKATA	10/2014	4/2018	162.88	56.09
			(-)	(-)	(0.00)
			[5/2019]	[162.88]	[13]
	Total			16,23,254.71 (2,63,059.32) [18,41,400.35]	6,63,626.77 (2,18,145.64)

Sector wise of On-Going Projects having Expenditure (as on 30.03.2018)

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
ATOMIC ENERGY											
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	06/2018	3492.00	6100.00	5392.16	174.63	24.55	5591.34
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459.00	11459.00	9891.00	1394.00	269.00	11554.00
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320.00	12320.00	7615.00	1272.00	260.00	9147.00
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4	NPCIL	03/2013	11/2020	11/2023	39849.00	39849.00	0.00	2133.00	0.00	2133.00
CIVIL AVIATION											
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	N.A.	309.46	553.53	480.57	42.38	0.00	522.95
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	24.13	2.31	0.00	26.44
COAL											
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	BCCL	02/2014	03/2021	03/2021	555.52	555.52	4.57	0.00	0.00	4.57
8	KAPURIA UG(PSLW)	BCCL	08/2011	04/2017	N.A.	988.35	988.35	45.26	0.00	0.00	45.26
9	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	04/2018	289.45	289.45	145.88	15.50	13.36	174.74
10	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	04/2018	269.82	269.82	134.69	29.26	5.36	169.31
11	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	339.88	12.08	0.00	0.00	12.08
12	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	1230.27	170.61	102.64	7.05	280.30
13	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.40	706.40	116.58	4.19	5.22	125.99
14	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	163.51	92.97	0.31	0.00	93.28
15	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	179.87	95.73	2.42	0.00	98.15
16	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	264.68	152.82	1.21	0.00	154.03
17	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	162.46	80.51	4.28	0.00	84.79
18	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2019	510.85	510.85	334.70	13.26	2.23	350.19
19	AMRAPALI OC(12MTY)	CCL	02/2012	03/2020	03/2020	858.11	858.11	174.35	7.67	41.10	223.12
20	JHANJRA COMBINED PR(3.50 MTY)	ECL	11/2015	03/2022	03/2022	602.86	602.86	259.61	28.39	5.94	293.94
21	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	N.A.	153.82	153.82	118.59	12.48	0.00	131.07
22	HURA - C OC (3 MTY)	ECL	10/2015	03/2022	03/2022	359.69	359.69	0.81	40.99	0.46	42.26
23	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	1055.05	305.58	30.60	7.32	343.50

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
24	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2019	479.15	479.15	82.24	5.28	18.37	105.89
25	SIARMAL OCP (40.00MTY)	MCL	05/2014	03/2026	03/2026	3756.36	3756.36	661.44	21.03	0.23	682.70
26	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2019	337.66	337.66	24.58	5.54	2.72	32.84
27	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2018	289.03	289.03	0.00	0.00	0.00	0.00
28	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2021	1375.38	1375.38	351.43	19.76	3.13	374.32
29	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2018	302.96	302.96	328.96	2.12	3.69	334.77
30	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2019	457.77	457.77	401.22	76.90	87.74	565.86
31	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.10	490.10	223.47	76.14	13.64	313.25
32	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2020	207.28	207.28	91.79	117.27	10.23	219.29
33	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	479.53	200.59	22.02	19.53	242.14
34	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	172.08	185.93	15.25	59.53	260.71
35	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.40	486.57	266.38	132.63	11.18	410.19
36	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	NCL	06/2011	03/2018	03/2018	1131.28	1131.28	402.75	31.61	12.96	447.32
37	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2021	1783.09	1783.09	0.00	28.21	49.54	77.75
38	EXPANSION OF MINE-I (LEASE AREA) AND MINE- I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	709.06	209.55	131.16	9.28	349.99
39	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	5907.11	4256.43	914.35	58.67	5229.45
40	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	NLC	03/2015	09/2019	09/2019	522.45	522.45	4.49	1.73	0.00	6.22
41	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	NLC	03/2015	12/2019	12/2019	513.63	513.63	164.88	3.70	0.00	168.58
42	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	06/2017	04/2018	687.28	767.00	425.37	323.88	6.83	756.08
43	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	11/2021	17237.00	17237.80	957.32	351.88	184.62	1493.82
44	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	489.62	477.74	-429.17	0.00	48.57
45	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	448.86	157.64	28.55	0.00	186.19
46	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	N.A.	453.63	453.63	121.91	0.00	0.00	121.91
47	KISTARAM OCP	SCCL	11/2010	03/2015	03/2020	242.29	164.04	0.09	0.28	0.00	0.37
48	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2018	181.19	181.19	176.64	-16.77	0.00	159.87
49	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2019	397.09	442.42	8.94	69.10	0.00	78.04
50	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2018	209.78	209.78	112.94	41.58	0.00	154.52
51	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	437.51	224.87	91.19	0.00	316.06
52	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	349.28	1.31	0.00	0.00	1.31

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
53	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2018	365.01	365.01	56.16	69.08	0.00	125.24
54	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	417.33	31.49	106.20	0.00	137.69
55	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2019	430.45	415.37	153.44	1.25	0.00	154.69
56	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	426.79	0.00	0.00	0.00	0.00
57	KALYANIKHANI 6 INCLINE PROJECT	SCCL	12/2015	03/2020	03/2020	477.65	477.65	0.00	0.00	0.00	0.00
58	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	72.61	62.99	2.38	137.98
59	BATURA OCP (2.0 MTY)	SECL	08/2015	03/2023	03/2021	1186.64	203.82	40.78	36.40	0.00	77.18
60	PELMA OCP(15.00MTY)	SECL	11/2014	03/2023	03/2023	1624.59	1624.59	5.73	0.06	0.00	5.79
61	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	178.44	5.01	0.15	0.00	5.16
62	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2019	198.59	198.59	169.24	0.25	0.00	169.49
63	CHHAL OC SEAM -III (6.00 MTY)	SECL	12/2013	03/2022	03/2022	610.63	610.63	28.80	0.57	2.53	31.90
64	MALACHUA OPENCAST PROJECT	SECL	10/2015	03/2023	03/2023	488.33	488.33	1.06	0.12	0.00	1.18
65	MADANNAGAR OPENCAST PROJECT	SECL	10/2015	03/2024	03/2024	1875.32	1875.32	0.00	0.00	0.00	0.00
66	BIJARI OC RCE (1.50 MTY)	SECL	05/2014	03/2020	03/2020	164.49	164.49	44.20	6.92	0.10	51.22
67	AMRITDHARA OC PROJECT	SECL	02/2015	03/2023	03/2023	481.60	481.60	0.00	0.00	0.00	0.00
68	AMERA OC RCE	SECL	02/2015	03/2018	03/2018	335.97	335.97	47.76	2.78	0.00	50.54
69	RAJNAGAR OCP RPR (1.70 MTY)	SECL	12/2014	03/2021	03/2021	357.80	357.80	114.16	0.31	0.00	114.47
70	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2021	371.04	371.04	34.02	1.59	0.00	35.61
71	BATURA HIGHWALL PROJECT	SECL	07/2015	03/2022	03/2022	231.92	231.92	0.00	0.00	0.00	0.00
72	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2020	316.10	316.10	24.80	19.39	0.00	44.19
73	DURGAPUR OPENCAST PROJECT	SECL	02/2015	03/2023	03/2023	916.24	916.24	0.45	0.54	0.00	0.99
74	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	SECL	08/2013	03/2023	03/2023	7612.33	7612.33	1172.51	496.71	29.08	1698.30
75	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2020	321.50	321.50	197.26	3.38	0.00	200.64
76	GEVRA EXPANSION OCP (SECL) (35-70) MTY	SECL	06/2010	03/2023	03/2023	11816.40	11816.40	2196.83	438.14	33.82	2668.79
77	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2019	258.56	258.56	144.56	9.25	0.00	153.81
78	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2021	869.44	869.44	108.64	2.92	0.00	111.56
79	VIJAY WEST OPENCAST PROJECT	SECL	05/2017	03/2026	03/2026	976.95	976.95	75.96	0.00	0.00	75.96
80	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2021	277.65	277.65	16.38	0.93	0.00	17.31
81	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	WCL	11/2015	03/2020	03/2020	498.42	498.42	27.79	19.12	4.21	51.12
82	DINESH OCP	WCL	11/2014	03/2020	03/2020	611.16	611.16	344.44	26.75	12.23	383.42
83	MAKARDHOKRA I OC	WCL	09/2014	03/2021	03/2021	266.23	266.23	135.96	3.80	0.00	139.76
84	GOKUL	WCL	11/2014	03/2018	03/2018	267.67	267.67	197.40	8.64	0.00	206.04
85	BHANEGAON OC	WCL	02/2015	03/2023	03/2023	187.94	409.68	85.19	0.84	0.07	86.10

[illegible]

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
107	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	N.A.	414.11	414.11	141.00	0.00	0.00	141.00
108	AIIMS-RAE BARELI-HOUSING	HSCC	10/2013	11/2013	N.A.	159.50	159.50	142.00	16.65	0.00	158.65
109	LGBRIMH-TEZPUR, ASSAM	HSCC	07/2012	12/2014	N.A.	175.57	175.57	113.50	0.00	0.00	113.50
110	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	06/2018	204.44	204.44	114.00	33.30	0.00	147.30
111	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	09/2018	293.65	293.65	174.00	43.60	0.00	217.60
112	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	03/2018	168.90	191.38	54.00	56.00	0.00	110.00
113	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	03/2018	09/2018	505.58	505.58	156.00	101.00	0.00	257.00
114	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	08/2018	152.95	152.95	15.04	23.96	0.00	39.00
115	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	363.99	0.00	21.00	0.00	21.00
116	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	HSCC	07/2016	08/2018	08/2018	312.99	312.99	62.00	87.00	0.00	149.00
117	CNCI KOLKATA WEST BENGAL	HSCC	08/2016	09/2018	09/2018	244.00	244.00	37.38	40.12	0.00	77.50
118	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	03/2019	274.19	274.19	0.00	29.68	0.00	29.68
119	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	03/2019	272.19	272.19	0.00	24.38	0.00	24.38
120	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	03/2019	355.15	355.15	0.00	21.79	0.00	21.79
HEAVY INDUSTRY											
121	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	N.A.	1718.00	3827.30	0.00	2289.00	0.00	2289.00
MINES											
122	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	04/2021	5540.00	5540.00	2.20	58.87	28.68	89.75
123	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	01/2020	534.00	534.00	175.88	111.69	3.31	290.88
124	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	11/2020	355.00	355.00	0.00	27.78	0.00	27.78
125	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	04/2021	483.00	483.00	0.00	0.00	0.00	0.00
PETROLEUM											
126	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	10/2018	694.00	694.00	113.52	140.08	61.97	315.57
127	ENNORE TERMINAL	BPCL	08/2014	04/2018	04/2018	393.00	393.00	159.56	99.61	22.28	281.45

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
128	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	5245.96	734.78	411.19	144.74	1290.71
129	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	N.A.	678.00	678.00	5.06	0.02	0.00	5.08
130	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	BPCL	02/2016	02/2020	02/2020	554.00	554.00	10.82	34.30	21.65	66.77
131	MMPL PIPELINE REROUTING PROJECT	BPCL	04/2013	12/2019	12/2019	449.58	449.58	86.94	12.32	0.20	99.46
132	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY	BPCL	05/2015	01/2019	01/2019	193.40	193.40	3.25	17.83	19.33	40.41
133	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	02/2020	3313.00	3313.00	32.61	74.57	11.17	118.35
134	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY	BPCL	05/2015	08/2018	08/2018	337.06	337.06	5.88	59.99	27.87	93.74
135	PUNE POL STORAGE DEPOT	BPCL	08/2016	08/2020	08/2020	282.64	282.64	0.00	0.00	33.23	33.23
136	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	06/2019	1112.00	1112.00	0.00	0.00	108.79	108.79
137	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	N.A.	3110.36	3110.36	2544.81	370.61	0.00	2915.42
138	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	06/2018	257.87	257.87	93.78	108.57	0.00	202.35
139	BS-VI PROJECTS	CPCL	09/2017	12/2019	12/2019	1858.00	1858.00	36.33	107.93	42.52	186.78
140	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	08/2020	421.00	421.00	0.00	1.15	0.16	1.31
141	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	03/2015	12/2018	12/2018	3957.00	3397.00	132.56	1639.09	189.35	1961.00
142	GAIL GAS LTD BENGALURU CGD PROJECT	GAIL	02/2015	02/2020	02/2020	749.00	749.00	342.33	222.65	41.91	606.89
143	AURAIYA PHULPUR PIPELINE PROJECT	GAIL	07/2015	12/2018	12/2018	1427.94	750.00	0.00	514.17	20.17	534.34
144	ANKLESHWAR BARODA PIPELINE PROJECT	GAIL	07/2014	03/2018	03/2018	199.95	199.95	56.00	88.58	9.79	154.37
145	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	07/2018	327.78	200.00	0.00	47.80	32.43	80.23
146	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	GAIL	07/2015	12/2019	12/2019	2881.40	2881.40	4.85	9.23	128.41	142.49
147	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2020	1933.00	1933.00	0.00	60.27	153.36	213.63
148	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2020	2433.00	2433.00	0.00	42.30	-2.10	40.20
149	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2020	3437.00	3437.00	0.00	11.32	59.75	71.07
150	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2020	1740.00	1740.00	0.00	5.73	3.57	9.30
151	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2019	2915.00	2915.00	1224.00	397.62	23.71	1645.33

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
152	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	GAIL	04/2017	04/2022	04/2022	287.49	287.49	0.00	39.40	8.84	48.24
153	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	GAIL	07/2017	07/2022	07/2022	243.53	243.53	0.00	7.80	3.99	11.79
154	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	723.40	330.18	119.50	42.56	492.24
155	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	HPCL	11/2011	03/2013	N.A.	310.00	370.00	17.84	0.00	0.00	17.84
156	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2020	20928.00	20928.00	347.88	192.61	0.00	540.49
157	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	HPCL	09/2016	09/2019	09/2019	407.00	407.00	10.35	41.84	43.07	95.26
158	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	HPCL	09/2016	06/2020	06/2020	1879.00	1879.00	21.79	390.29	158.02	570.10
159	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)	HPCL	11/2016	02/2019	02/2019	230.00	230.00	1.61	26.29	20.47	48.37
160	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	07/2019	4199.00	4199.00	110.71	84.26	0.00	194.97
161	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	03/2021	03/2021	2677.00	2677.00	0.00	5.87	3.88	9.75
162	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH	HPCL	12/2016	04/2021	04/2021	300.00	300.00	0.00	0.00	0.00	0.00
163	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	HPCL	11/2017	11/2020	11/2020	255.00	255.00	0.00	0.00	0.00	0.00
164	ENNORE-TRICHY-MADURAI LPG PIPELINE	IOCL	05/2013	06/2020	06/2020	711.00	711.00	11.12	0.00	0.00	11.12
165	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	239.60	85.67	0.00	325.27
166	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076.00	4190.00	1224.67	1280.96	42.40	2548.03
167	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150.00	3150.00	868.17	791.39	157.78	1817.34
168	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	N.A.	191.96	191.96	137.65	38.63	0.00	176.28
169	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	12/2020	1823.00	1823.00	11.40	184.91	74.63	270.94
170	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	08/2020	2321.00	2321.00	37.10	35.56	3.34	76.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
171	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	IOCL	02/2015	10/2019	10/2019	890.00	887.00	27.08	268.97	40.81	336.86
172	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690.00	690.00	98.28	35.97	0.77	135.02
173	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY	IOCL	03/2014	03/2017	10/2017	238.50	238.50	146.84	52.75	1.69	201.28
174	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	12/2016	N.A.	1793.00	1793.00	1735.43	53.43	0.00	1788.86
175	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	06/2018	913.00	1330.00	777.29	326.53	96.34	1200.16
176	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	IOCL	01/2016	02/2019	12/2018	247.52	247.52	43.82	45.15	41.10	130.07
177	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP	IOCL	02/2016	05/2019	12/2018	356.00	356.00	39.26	70.25	16.40	125.91
178	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	IOCL	06/2016	08/2019	08/2019	423.00	423.00	24.24	48.06	40.51	112.81
179	INDMAX PROJECT AT BONGAIGAON REFINERY	IOCL	02/2016	11/2019	11/2019	2582.00	2582.00	52.92	392.99	34.88	480.79
180	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY	IOCL	02/2016	07/2017	02/2018	931.00	931.00	290.78	305.50	25.56	621.84
181	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	IOCL	07/2015	11/2018	11/2018	822.66	822.66	214.87	251.73	63.20	529.80
182	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	08/2021	08/2021	1945.00	1945.00	6.60	275.55	0.54	282.69
183	BRANCH PIPELINE OF PAJPL TO UNA	IOCL	02/2016	09/2019	09/2019	151.00	151.00	3.76	30.99	6.25	41.00
184	HALDIA BARAUNI PRODUCT PIPELINE	IOCL	04/2016	12/2020	12/2020	1021.00	1021.00	4.45	1.28	0.00	5.73
185	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	IOCL	05/2016	12/2020	02/2020	664.00	664.00	23.64	216.51	0.54	240.69
186	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	12/2018	4497.00	4497.00	12.08	61.95	19.08	93.11
187	MOTIHARI AMLEKHGANJ PIPELINE	IOCL	09/2015	06/2020	06/2020	324.00	324.00	0.49	31.98	22.92	55.39
188	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	01/2021	212.00	212.00	0.00	0.08	0.00	0.08
189	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	01/2021	348.00	348.00	0.00	0.05	0.00	0.05

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
190	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	IOCL	01/2015	03/2021	03/2021	342.00	342.00	0.00	0.00	0.00	0.00
191	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	IOCL	07/2014	03/2021	03/2021	247.00	247.00	0.00	0.00	0.00	0.00
192	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	01/2021	261.00	261.00	0.00	0.05	0.00	0.05
193	INSTALLATION OF ADDITIONAL CRUDE TANKS (NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	01/2019	429.00	429.00	12.01	121.16	0.00	133.17
194	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	02/2020	160.10	160.10	0.00	23.16	0.83	23.99
195	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	12/2019	161.59	161.59	28.80	2.27	0.00	31.07
196	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	IOCL	09/2016	07/2020	07/2020	208.35	208.35	16.93	9.26	15.70	41.89
197	AUGMENTATION OF CTMPL	IOCL	12/2016	06/2020	06/2020	228.00	228.00	0.00	0.00	0.13	0.13
198	REPLACEMENT OF KV SECTION OF KSPL	IOCL	10/2014	08/2018	08/2018	279.00	279.00	142.16	57.89	0.00	200.05
199	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	04/2020	163.02	163.02	0.00	28.93	0.00	28.93
200	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	IOCL	08/2017	04/2021	04/2021	384.58	384.58	0.81	5.21	8.06	14.08
201	REVAMPING OF EXISTING FACILITIES/AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	IOCL	08/2017	08/2021	08/2021	318.80	318.80	0.00	0.00	0.00	0.00
202	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	IOCL	08/2017	06/2020	06/2020	236.00	236.00	0.00	0.00	0.00	0.00
203	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	10/2020	466.43	466.43	0.25	0.59	0.34	1.18
204	BS-VI PROJECT AT MATHURA REFINERY	IOCL	01/2018	09/2019	09/2019	666.64	666.64	19.61	73.48	6.93	100.02
205	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	IOCL	08/2017	12/2021	12/2021	315.00	315.00	0.00	2.12	0.00	2.12
206	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	IOCL	08/2017	08/2020	08/2020	1342.00	1342.00	0.00	0.00	0.00	0.00
207	BS-VI PROJECT AT GUJARAT REFINERY	IOCL	03/2018	09/2019	09/2019	3380.00	3380.00	581.88	15.62	0.00	597.50
208	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	N.A.	993.00	1693.00	1398.50	151.35	0.00	1549.85

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
209	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	MANGALORE REFIN	05/2015	04/2019	04/2019	224.00	207.25	28.42	47.69	16.86	92.97
210	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	MANGALORE REFIN	10/2015	03/2019	03/2019	135.00	170.70	33.34	63.04	8.27	104.65
211	BSVI UPGRADATION	MANGALORE REFIN	09/2016	12/2019	12/2019	1810.00	1810.00	13.31	67.14	28.36	108.81
212	DIESEL HYDROTREATOR	NRL	07/2015	01/2018	N.A.	1031.37	1031.37	41.49	264.42	0.00	305.91
213	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	11/2018	352.56	438.84	70.40	75.96	0.00	146.36
214	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	05/2018	228.64	256.41	136.22	10.99	0.00	147.21
215	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	11/2017	871.35	1200.00	565.63	395.37	0.00	961.00
216	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	OIL	05/2016	10/2020	10/2020	406.00	406.00	0.00	1.50	0.08	1.58
217	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	12/2019	571.66	571.66	0.00	7.30	0.00	7.30
218	50MW WIND ENERGY POWER PROJECT	OIL	11/2015	06/2017	N.A.	500.00	500.00	0.00	368.24	0.00	0.00
219	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350.00	350.00	0.00	1.03	0.00	1.03
220	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	09/2018	2465.15	2378.89	1931.23	136.06	5.77	2073.06
221	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	160.16	103.54	11.82	2.66	118.02
222	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2019	736.65	571.47	534.32	8.60	0.04	542.96
223	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	5725.50	2798.79	1492.15	839.46	5130.40
224	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	3567.76	1990.43	0.00	5558.19
225	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	03/2019	6068.80	5296.93	3358.54	957.70	84.32	4400.56
226	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	10/2019	6086.08	5842.31	1935.54	541.67	287.85	2765.06
227	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	12/2018	1671.22	567.22	307.48	77.10	30.36	414.94
228	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	05/2018	2899.93	2504.61	1237.43	0.00	80.40	1317.83

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
250	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	10/2023	8112.12	8112.12	807.22	86.29	1.71	895.22
251	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	N.A.	2313.00	4366.64	3484.00	0.00	0.00	3484.00
252	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	N.A.	4122.00	9142.58	8300.00	0.00	0.00	8300.00
253	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2018	2496.90	6179.96	5563.86	612.43	248.12	6424.41
254	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	04/2018	573.99	1337.76	1362.81	205.01	53.34	1621.16
255	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	N.A.	421.01	1078.31	963.23	0.00	0.00	963.23
256	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2020	3919.59	8398.75	6176.84	475.81	32.19	6684.84
257	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	N.A.	6285.33	17435.15	9158.79	679.64	140.94	9979.37
258	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	11638.55	12865.92	7423.00	1299.00	258.00	8980.00
259	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	3846.30	3133.00	313.00	75.00	3521.00
260	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2018	4375.35	8150.00	6550.00	434.00	73.00	7057.00
261	FGUTPP, UNCHAHAHAR STAGE-IV (1X500 MW)	NTPC	07/2013	12/2016	N.A.	3363.12	3363.12	2098.00	146.00	0.00	2244.00
262	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	9188.98	2662.00	1256.00	415.00	4333.00
263	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	12532.44	13740.53	5488.00	1541.00	559.00	7588.00
264	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	14366.58	15164.05	4882.00	1390.00	652.00	6924.00
265	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	1381.84	260.00	46.00	16.00	322.00
266	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353.00	7998.00	6422.94	551.48	0.00	6974.42
267	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	02/2019	12964.60	13731.26	9072.44	1011.77	0.00	10084.21
268	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	02/2019	9750.89	9750.89	6557.22	400.69	0.00	6957.91
269	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	15095.67	13125.00	1158.00	237.00	14520.00
270	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	03/2018	15166.19	16934.65	13267.00	2097.00	0.00	15364.00
271	MOUDA STPP STAGE 2	NTPC	03/2012	09/2016	N.A.	7921.47	7921.47	5302.00	0.00	0.00	5302.00
272	SOLAPUR STPP	NTPC	03/2012	11/2016	03/2019	9395.18	9395.18	7563.00	888.00	37.00	8488.00
273	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	11846.00	12739.82	8043.00	1298.00	214.00	9555.00
274	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	N.A.	1527.00	1801.07	146.00	2.00	0.00	0.00
275	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	09/2019	9870.51	11148.86	2676.00	1757.00	682.00	5115.00
276	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	07/2020	10/2020	10598.98	10598.98	813.00	586.00	450.00	1849.00
277	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	12/2016	4237.96	4552.00	1984.86	542.00	131.00	2657.86
278	TALAIPELLI COAL MINING PROJECT	NTPC	09/2015	11/2019	12/2020	3004.00	3004.00	721.51	192.18	162.00	1075.69

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
279	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	738.48	640.99	19.60	0.00	660.59
280	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2018	4824.12	5071.94	4453.08	61.60	0.00	4514.68
281	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	13762.80	12371.70	267.90	0.00	12639.60
282	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2018	2144.00	2932.88	2504.50	113.30	0.00	2617.80
283	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	1891.41	1110.64	73.50	0.00	1184.14
284	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	06/2018	374.63	374.63	64.00	92.50	0.00	156.50
285	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	09/2018	539.82	539.82	377.20	23.30	0.00	400.50
286	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	06/2019	522.29	550.18	336.70	57.70	0.00	394.40
287	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	09/2018	155.57	206.42	112.40	30.80	0.00	143.20
288	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	03/2019	5151.37	5151.37	1139.40	840.00	0.00	1979.40
289	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	06/2018	288.49	376.09	185.60	48.70	0.00	234.30
290	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	09/2018	196.58	225.28	93.00	50.00	0.00	143.00
291	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B)	PGCIL	12/2014	04/2018	04/2018	6517.36	6517.36	2779.40	993.40	0.00	3772.80
292	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP	PGCIL	01/2015	03/2018	09/2018	268.80	340.88	122.30	67.80	0.00	190.10
293	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	871.62	112.10	48.49	0.00	160.59
294	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	06/2019	203.28	260.03	139.80	38.90	0.00	178.70
295	EASTERN REGION STRENGTHENING SCHEME-II	PGCIL	07/2010	11/2012	09/2018	1272.80	1731.10	1381.93	58.10	0.00	1440.03
296	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	06/2018	197.40	197.40	38.70	26.20	0.00	64.90

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
297	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	09/2018	1071.24	1071.24	247.40	299.60	0.00	547.00
298	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	1394.52	1.90	84.70	0.00	86.60
299	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)	PGCIL	05/2015	10/2018	10/2018	780.33	780.33	8.20	139.30	0.00	147.50
300	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	PGCIL	04/2015	04/2018	09/2018	3705.61	3705.61	1564.40	828.50	0.00	2392.90
301	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	05/2018	1479.30	1479.30	525.10	323.30	0.00	848.40
302	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C	PGCIL	07/2015	07/2018	07/2018	2247.37	2247.37	263.20	886.50	0.00	1149.70
303	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	10/2018	307.18	307.18	111.10	68.00	0.00	179.10
304	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND INDBARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	09/2018	1940.13	2702.65	2307.46	113.00	0.00	2420.46
305	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	639.46	481.42	6.40	0.00	487.82
306	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	09/2018	297.33	534.02	352.47	34.40	0.00	386.87
307	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	1939.45	60.80	0.00	2000.25
308	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2018	198.63	198.63	127.63	10.30	0.00	137.93
309	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	05/2018	514.20	703.10	545.90	52.10	0.00	598.00
310	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2018	2514.88	3190.27	1865.05	313.70	0.00	2178.75
311	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	09/2018	305.04	305.04	84.80	86.70	0.00	171.50
312	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION	PGCIL	01/2016	07/2018	07/2018	1455.47	1455.47	216.00	691.80	0.00	907.80
313	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS	PGCIL	01/2016	07/2018	03/2018	207.88	207.88	28.80	82.70	0.00	111.50

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
314	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	808.63	95.30	177.40	0.00	272.70
315	EASTERN REGION STRENGTHENING SCHEME XV	PGCIL	04/2016	04/2018	04/2018	454.11	454.11	28.50	170.20	0.00	198.70
316	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2333.71	946.50	277.04	0.00	1223.54
317	EASTERN REGION STRENGTHENING SCHEME X	PGCIL	05/2016	11/2018	11/2018	766.21	766.21	0.30	193.30	0.00	193.60
318	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	PGCIL	05/2016	05/2019	05/2019	3519.59	3519.59	229.80	883.50	0.00	1113.30
319	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	PGCIL	05/2016	11/2019	11/2019	14733.37	14733.37	499.30	814.40	0.00	1313.70
320	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I	PGCIL	04/2016	12/2018	12/2018	810.48	810.48	157.50	312.60	0.00	470.10
321	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	PGCIL	04/2016	06/2018	06/2018	287.99	287.99	38.10	61.40	0.00	99.50
322	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS	PGCIL	04/2016	06/2019	06/2019	790.13	790.30	129.40	239.30	0.00	368.70
323	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	PGCIL	04/2016	04/2019	04/2019	844.64	844.64	44.80	163.10	0.00	207.90
324	EASTERN REGION STRENGTHENING SCHEME XIV	PGCIL	05/2016	11/2018	11/2018	167.01	167.01	8.00	55.90	0.00	63.90
325	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	PGCIL	07/2016	01/2019	01/2019	1429.38	1429.38	66.00	287.90	0.00	353.90
326	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B)	PGCIL	07/2016	12/2018	12/2018	300.94	300.94	7.40	105.40	0.00	112.80
327	WESTERN REGION STRENGTHENING SCHEME-XVI	PGCIL	07/2016	07/2018	07/2018	150.99	150.99	1.10	73.00	0.00	74.10
328	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN	PGCIL	07/2016	03/2019	03/2019	333.17	333.17	8.30	212.20	0.00	220.50
329	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION	PGCIL	08/2016	02/2019	02/2019	431.89	431.89	0.40	81.50	0.00	81.90

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
330	PROVISION OF SERIES REACTORS IN NORTHERN REGION	PGCIL	08/2016	02/2019	02/2019	177.52	177.52	0.00	45.50	0.00	45.50
331	SOUTHERN REGION STRENGTHENING SCHEME XXI	PGCIL	09/2016	03/2019	03/2019	562.25	562.25	0.00	18.60	0.00	18.60
332	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	PGCIL	03/2017	06/2019	06/2019	251.60	251.60	0.00	12.00	0.00	12.00
333	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION	PGCIL	10/2016	04/2019	04/2019	167.75	167.75	0.00	62.40	0.00	62.40
334	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	PGCIL	03/2017	11/2019	11/2019	283.72	283.72	1.20	6.51	0.00	7.71
335	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	01/2019	408.46	408.46	20.20	50.61	0.00	70.81
336	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	10/2016	04/2019	04/2019	608.24	608.24	0.00	132.80	0.00	132.80
337	WESTERN REGION STRENGTHENING SCHEME XVIII	PGCIL	02/2017	02/2020	02/2020	195.05	195.05	0.00	0.00	0.00	0.00
338	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	02/2019	322.30	322.30	0.20	21.50	0.00	21.70
339	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA	PGCIL	03/2017	03/2019	03/2019	162.31	162.31	0.00	11.90	0.00	11.90
340	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	06/2019	235.53	235.53	0.00	8.00	0.00	8.00
341	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	12/2019	379.95	379.95	19.60	0.10	0.00	19.70
342	WESTERN REGION STRENGTHENING SCHEME XVII	PGCIL	02/2017	09/2019	09/2019	204.12	204.12	0.00	10.30	0.00	10.30
343	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	PGCIL	02/2017	04/2020	04/2020	5070.13	5070.13	0.00	323.07	0.00	323.07
344	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	PGCIL	03/2017	06/2019	06/2019	337.75	337.75	0.00	6.00	0.00	6.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
345	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9141.97	256.56	412.24	0.00	668.80
346	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	5111.33	223.86	250.71	0.00	474.57
347	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	06/2018	955.00	1364.00	1001.00	124.00	0.00	1125.00
348	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART-A)	PGCIL	04/2015	11/2017	04/2018	2525.00	2525.00	701.00	1082.00	0.00	1783.00
349	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B	PGCIL	04/2015	01/2018	04/2018	2225.00	2225.00	445.00	901.00	0.00	1346.00
350	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V	PGCIL	02/2015	06/2018	06/2018	1750.00	1750.00	204.00	663.00	0.00	867.00
351	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	12/2015	04/2019	04/2019	3654.00	3654.00	343.00	1189.00	0.00	1532.00
352	EASTERN REGION STRENGTHENING SCHEME- XVIII	PGCIL	03/2017	07/2020	07/2020	3500.00	3500.00	0.00	151.00	0.00	151.00
353	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	09/2018	175.64	175.64	0.00	17.10	0.00	17.10
354	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	07/2019	186.17	186.17	0.00	13.60	0.00	13.60
355	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	02/2019	445.89	445.89	0.00	81.90	0.00	81.90
356	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	02/2020	1931.39	1931.39	0.00	29.20	0.00	29.20
357	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	PGCIL	09/2017	09/2019	09/2019	198.49	198.49	0.00	0.00	0.00	0.00
358	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	05/2020	358.83	358.83	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
359	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPF AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	12/2017	06/2019	06/2019	193.14	193.14	0.00	0.00	0.00	0.00
360	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	602.44	463.90	17.33	4.40	485.63
361	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	11/2017	05/2018	330.00	330.00	110.38	86.69	3.01	200.08
362	NAITWAR MORI HEP	SJVN	10/2017	12/2021	12/2021	648.33	648.33	65.76	19.96	14.65	100.37
363	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	294.60	112.60	46.09	4.13	162.82
364	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	3789.61	1148.27	196.26	49.14	1393.67
365	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657.00	4401.90	2189.76	269.20	81.31	2540.27
366	AMELIA COAL MINE	THDCIL	01/2017	09/2020	09/2020	2104.21	2104.21	36.28	3.51	0.37	40.16
	RAILWAYS										
367	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2018	493.17	493.17	376.00	9.61	10.86	396.47
368	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	03/2019	305.00	305.00	217.84	23.21	8.07	249.12
369	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	CCOI	01/2013	03/2018	03/2018	387.70	387.70	323.91	51.46	10.26	385.63
370	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	CCOI	05/2014	03/2018	03/2018	207.00	207.00	135.51	13.64	3.75	152.90
371	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2019	346.32	300.00	180.03	37.50	16.42	233.95
372	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	03/2019	174.00	174.00	74.22	47.49	10.95	132.66
373	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	03/2019	343.00	343.00	222.83	34.45	15.33	272.61
374	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	03/2019	234.50	234.50	0.14	0.25	0.00	0.39
375	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	03/2023	499.30	3168.29	532.82	270.73	28.60	832.15
376	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	03/2021	277.70	792.89	177.52	43.19	9.90	230.61
377	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	N.A.	03/2019	184.06	199.12	126.50	25.81	15.18	167.49
378	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	03/2022	297.85	540.02	98.02	27.54	8.96	134.52
379	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	03/2021	514.68	2271.50	1164.05	291.49	23.85	1479.39
380	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	N.A.	663.01	858.97	688.04	22.27	-2.80	707.51
381	INDORE - MANMAD VIA MALEGAON (368 KM)	CR	02/2016	N.A.	03/2024	9968.00	8857.98	0.00	0.00	0.00	0.00
382	PUNE-NASIK (265 KM)	CR	02/2016	N.A.	03/2024	2425.00	5341.68	0.00	0.00	0.00	0.00
383	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	N.A.	03/2024	2750.00	3438.51	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
384	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	03/2022	630.00	1272.19	19.48	43.11	4.71	67.30
385	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	03/2023	2326.00	2449.91	0.63	33.91	7.99	42.53
386	PUNE-MIRAJ-LONDA (467 KM)	CR	02/2015	N.A.	03/2024	4670.00	3627.47	0.33	17.19	15.05	32.57
387	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	03/2023	1876.00	2081.27	0.00	0.14	-0.01	0.13
388	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	03/2023	854.00	1035.16	0.00	4.00	0.63	4.63
389	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	N.A.	03/2022	912.00	637.95	0.35	6.93	1.69	8.97
390	DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	N.A.	81459.00	28181.00	0.00	0.00	0.00	0.00
391	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	12/2022	810.78	1928.07	435.40	50.65	5.83	491.88
392	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	06/2021	470.21	3004.90	845.66	135.28	23.29	1004.23
393	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	03/2021	679.27	1579.27	467.16	177.19	10.83	655.18
394	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	N.A.	03/2021	858.67	843.04	19.40	35.22	0.00	54.62
395	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	03/2020	826.57	1160.83	388.26	108.84	18.98	516.08
396	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	N.A.	03/2020	155.81	238.03	139.75	16.36	6.00	162.11
397	DELANG-PURI DOUBLING	ECOR	03/2011	03/2015	07/2015	165.16	234.71	223.96	1.91	0.48	226.35
398	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	ECOR	04/2008	N.A.	N.A.	445.25	445.25	0.00	0.00	0.00	0.00
399	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	N.A.	415.67	549.75	14.62	0.00	0.00	14.62
400	BIHTA-AURANGABAD (NL)	ECOR	04/2008	N.A.	N.A.	326.20	326.20	1.68	0.00	0.00	1.68
401	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	N.A.	175.69	325.00	253.10	0.00	0.00	253.10
402	CHHAPRA-MUZAFFARPUR (NL)	ECOR	04/2006	N.A.	N.A.	285.07	378.56	111.71	0.00	0.00	111.71
403	JAGDALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2021	03/2021	1547.38	1547.38	18.59	84.53	14.31	117.43
404	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2021	03/2022	2499.71	2499.71	10.65	49.35	22.55	82.55
405	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2021	03/2022	2361.74	2361.74	9.93	25.05	8.75	43.73
406	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	03/2021	03/2021	701.61	810.02	19.92	42.34	3.72	65.98
407	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	03/2021	03/2020	1172.92	1172.92	37.97	110.62	0.00	148.59
408	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	ECOR	04/2016	03/2020	03/2020	5200.00	5200.00	0.00	0.00	0.00	0.00
409	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	N.A.	528.65	324.66	330.82	0.00	0.00	330.82
410	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	N.A.	332.92	477.88	495.40	0.00	0.00	495.40
411	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC).ECR	ECR	04/1997	03/2012	N.A.	501.69	1043.56	876.49	0.00	0.00	876.49
412	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	N.A.	162.87	541.00	183.72	0.00	0.00	183.72

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
413	KOSI BRIDGE (NL), ECR	ECR	04/2002	03/2012	N.A.	322.95	341.41	320.39	0.00	0.00	320.39
414	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	N.A.	380.00	380.00	0.00	0.00	0.00	0.00
415	HAJIPUR - BACHAWARA	ECR	05/2015	N.A.	12/2018	720.00	678.54	0.00	0.00	0.00	0.00
416	DANIAWAN-BIHARSARIF (NL), ECR	ECR	04/2001	N.A.	N.A.	406.92	339.00	200.00	0.00	0.00	200.00
417	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	N.A.	459.91	459.91	221.54	0.00	0.00	221.54
418	NAWADA-LAXMIPUR (NL)	ECR	04/2008	N.A.	N.A.	620.57	620.57	0.00	0.00	0.00	0.00
419	DARBANGHA-KUSHESHWARSTHAN (NL)	ECR	04/2005	N.A.	N.A.	205.00	205.00	5.21	0.00	0.00	5.21
420	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	N.A.	211.00	926.09	4.41	0.00	0.00	4.41
421	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	N.A.	678.62	2393.23	17.17	0.00	0.00	17.17
422	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	ECR	04/2008	N.A.	N.A.	228.05	228.05	1.52	0.00	0.00	1.52
423	ARARIA-SUPAUL (NL)	ECR	04/2008	N.A.	N.A.	304.41	304.41	0.19	0.00	0.00	0.19
424	KURSELA-BIHARIGANJ (NL)	ECR	04/2008	N.A.	N.A.	192.56	192.56	0.38	0.00	0.00	0.38
425	MUZAFFARPUR-DARBANGHA (NL)	ECR	04/2008	N.A.	N.A.	281.30	281.30	0.58	0.00	0.00	0.58
426	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	N.A.	372.14	355.81	283.44	0.00	0.00	283.44
427	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	N.A.	N.A.	470.00	470.00	40.00	0.00	0.00	40.00
428	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	N.A.	213.01	367.17	13.00	0.00	0.00	13.00
429	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	12/2020	12/2020	1200.20	1200.20	0.00	0.00	0.00	0.00
430	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	12/2020	12/2020	1491.47	1491.47	0.00	0.00	0.00	0.00
431	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	N.A.	332.15	559.91	538.21	0.00	0.00	538.21
432	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2020	2436.21	2436.21	22.62	96.50	47.01	166.13
433	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	528.57	0.61	0.00	0.00	0.61
434	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	03/2019	1188.91	1319.33	757.23	0.00	0.00	757.23
435	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	N.A.	607.09	973.33	613.71	0.00	0.00	613.71
436	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	N.A.	1106.62	1106.62	355.85	0.00	0.00	355.85
437	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	03/2012	N.A.	167.73	167.73	207.11	0.00	0.00	207.11
438	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	ER	04/2009	12/2011	N.A.	533.38	533.38	127.10	0.00	0.00	127.10
439	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	N.A.	N.A.	277.28	266.00	92.93	0.00	0.00	92.93

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
440	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	N.A.	N.A.	296.44	198.88	15.83	0.00	0.00	15.83
441	HOWRAH DIVISION- PLATFORM SHELTER (40 CATEGORY STATIONS)	ER	04/2010	N.A.	11/2018	157.94	157.94	47.63	0.00	0.00	47.63
442	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT	ER	04/2007	N.A.	N.A.	450.55	251.05	15.66	0.00	0.00	15.66
443	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	N.A.	365.17	365.67	1.37	0.00	0.00	1.37
444	HANSDIHA-GODDA NL	ER	04/2011	N.A.	N.A.	267.09	350.78	98.15	0.00	0.00	98.15
445	SAINTHIA-TARAPITH 3RD LINE	ER	04/2011	N.A.	N.A.	193.44	186.64	150.28	0.00	0.00	150.28
446	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	N.A.	175.80	173.91	18.54	0.00	0.00	18.54
447	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	N.A.	299.60	269.60	1.11	0.00	0.00	1.11
448	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	N.A.	N.A.	494.54	369.69	31.99	0.00	0.00	31.99
449	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	ER	04/2000	N.A.	N.A.	297.47	153.02	52.01	0.00	0.00	52.01
450	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	ER	04/2003	N.A.	N.A.	337.96	186.89	62.73	0.00	0.00	62.73
451	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	N.A.	493.96	681.68	135.79	0.00	0.00	135.79
452	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	N.A.	423.66	720.59	456.58	0.00	0.00	456.58
453	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE	ER	04/2010	N.A.	N.A.	268.52	268.52	78.81	0.00	0.00	78.81
454	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES	ER	04/2011	N.A.	N.A.	166.89	166.89	0.02	0.00	0.00	0.02
455	MONIGRAM- NIMTITA	ER	04/2012	N.A.	N.A.	250.93	259.23	8.43	0.00	0.00	8.43
456	BAZAR SAU -AZIMGANJ JN. DOUBLING	ER	04/2012	N.A.	N.A.	255.64	272.20	0.64	0.00	0.00	0.64
457	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	980.99	0.00	0.00	980.99
458	GHUTIASHARIF-CANNING (ER)	ER	04/2009	12/2011	N.A.	611.03	611.03	146.31	0.00	0.00	146.31

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
459	PANDABESWAR-CHINPAI DOUBLING (ER)	ER	04/2004	12/2010	N.A.	293.74	229.33	140.60	0.00	0.00	140.60
460	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	N.A.	207.52	334.87	293.47	0.00	0.00	293.47
461	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	N.A.	N.A.	406.99	319.58	141.88	0.00	0.00	141.88
462	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	N.A.	450.00	290.85	9.31	0.00	0.00	9.31
463	HANSNABAD-HINGALGANJ NEW BG LINE	ER	04/2010	N.A.	N.A.	172.03	260.60	6.42	0.00	0.00	6.42
464	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	N.A.	915.98	1130.13	0.30	0.00	0.00	0.30
465	PLASSEY-JIAGANJ DOUBLING	ER	04/2011	03/2015	N.A.	248.07	234.41	161.17	0.00	0.00	161.17
466	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	N.A.	288.35	238.36	51.31	0.00	0.00	51.31
467	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	N.A.	261.38	332.14	87.22	0.00	0.00	87.22
468	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	N.A.	N.A.	923.52	923.52	227.50	0.00	0.00	227.50
469	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTISURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	N.A.	N.A.	595.91	595.91	103.62	0.00	0.00	103.62
470	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	ER	04/2010	N.A.	N.A.	174.56	160.97	56.25	0.00	0.00	56.25
471	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	KMRCL	04/2010	03/2016	N.A.	2397.72	2397.72	197.20	0.00	0.00	197.20
472	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	N.A.	1049.69	3404.92	3544.30	0.00	0.00	3544.30
473	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	623.78	177.81	10.53	812.12
474	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2017	495.74	732.89	386.03	4.53	0.00	390.56
475	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2423.55	0.00	0.00	2423.55
476	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	4874.58	1881.65	0.00	0.00	1881.65

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
477	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR	M RTP	04/2009	N.A.	N.A.	573.78	268.52	0.67	0.00	0.00	0.67
478	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	N.A.	714.10	714.10	65.20	0.00	0.00	65.20
479	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	N.A.	158.77	634.48	629.43	0.00	0.00	629.43
480	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	N.A.	120.00	245.39	210.67	0.00	0.00	210.67
481	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	N.A.	108.00	432.72	446.52	0.00	0.00	446.52
482	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	1.92	0.00	0.00	1.92
483	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	10.34	0.00	0.00	10.34
484	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	03/2020	524.00	668.00	0.00	0.00	0.00	0.00
485	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	06/2018	218.19	412.05	315.40	34.26	0.48	350.14
486	KICHHA-KHATIMA (NL) - NER	NER	04/2003	N.A.	N.A.	142.45	228.40	0.15	0.00	0.00	0.15
487	HATHUA-BHATNI (N L) (NER)	NER	04/2005	N.A.	05/2019	230.03	718.54	263.23	9.23	0.52	272.98
488	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	N.A.	744.71	1126.79	751.05	10.65	0.00	761.70
489	GHAZIPUR - AUNRIHAR (40 KM)	NER	04/2014	N.A.	N.A.	182.92	197.73	0.00	0.00	0.00	0.00
490	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	N.A.	307.00	308.00	0.00	0.00	0.00	0.00
491	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	N.A.	08/2018	243.78	268.78	87.44	6.24	0.74	94.42
492	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	03/2018	195.64	474.30	349.40	75.36	5.56	430.32
493	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	N.A.	08/2018	199.75	227.00	198.70	0.00	42.35	241.05
494	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	10/2018	295.00	477.31	63.74	82.74	3.28	149.76
495	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	NER	03/2013	N.A.	N.A.	643.00	644.00	0.00	0.00	0.00	0.00
496	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	03/2022	1750.00	1295.42	16.40	34.46	1.41	52.27
497	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	N.A.	03/2020	36.80	614.00	258.91	3.72	0.00	262.63
498	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	N.A.	492.98	1320.00	911.22	8.10	1.71	921.03
499	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	1282.50	655.61	13.62	1951.73

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
500	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5450.00	4572.44	393.01	74.66	5040.11
501	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733.00	3040.00	2527.95	314.57	37.37	2879.89
502	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	6316.91	894.21	176.06	7387.18
503	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	03/2020	200.00	780.00	403.35	47.15	15.97	466.47
504	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	03/2020	300.00	2135.00	918.83	3.45	0.13	922.41
505	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	337.16	91.21	3.59	431.96
506	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2117.13	433.11	39.36	2589.60
507	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	03/2020	282.92	360.00	3.13	0.00	0.00	3.13
508	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	383.92	0.00	0.00	383.92
509	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	N.A.	03/2019	1798.00	1798.00	0.00	0.00	0.00	0.00
510	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	03/2020	221.42	380.00	26.08	71.33	0.00	97.41
511	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	04/2016	895.00	1857.00	1416.08	88.43	25.40	1529.91
512	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	07/2019	252.00	580.00	0.00	0.00	0.00	0.00
513	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	03/2020	4274.00	4274.00	0.00	0.00	0.00	0.00
514	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	03/2018	209.77	630.00	490.22	122.79	7.03	620.04
515	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	03/2019	283.55	450.00	213.47	132.17	15.90	361.54
516	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	03/2021	4083.02	6000.00	238.74	18.48	0.09	257.31
517	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	03/2020	242.22	471.00	46.22	6.92	0.82	53.96
518	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	N.A.	241.52	394.28	148.33	0.00	0.00	148.33
519	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	03/2020	165.82	450.00	113.49	9.31	0.17	122.97
520	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	03/2018	523.17	1871.00	1081.96	0.02	0.00	1081.98
521	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	03/2019	312.12	535.00	415.46	116.96	37.51	569.93
522	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	03/2019	246.07	398.93	75.22	53.55	43.63	172.40

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
523	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	N.A.	03/2022	2232.32	2232.00	43.15	50.01	50.54	143.70
524	DIGARU-HOJAI (102 KM)	NFR	04/2015	N.A.	03/2021	870.96	871.00	12.99	18.54	42.53	74.06
525	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	N.A.	03/2020	556.31	612.00	0.00	0.00	0.00	0.00
526	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	N.A.	238.56	740.00	722.65	0.00	0.00	722.65
527	MEERUT-MUZAFARNAGAR PATCH DL	NR	04/2012	N.A.	N.A.	377.44	377.44	182.85	0.00	0.00	182.85
528	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	NR	04/2009	N.A.	N.A.	396.04	369.00	186.27	0.00	0.00	186.27
529	GRADE SEPARATOR AT DAYABASTI	NR	04/1999	N.A.	N.A.	156.65	197.17	56.10	0.00	0.00	56.10
530	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	NR	04/2013	N.A.	N.A.	654.00	654.00	0.00	0.00	0.00	0.00
531	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR	NR	04/2013	N.A.	N.A.	1239.00	1239.00	0.00	0.00	0.00	0.00
532	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	N.A.	287.00	625.00	4.38	0.00	0.00	4.38
533	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	N.A.	336.91	336.91	143.18	0.00	0.00	143.18
534	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	N.A.	295.68	295.68	1.20	0.00	0.00	1.20
535	HARIDWAR-LAKSAR	NR	04/2012	N.A.	N.A.	219.83	346.63	38.33	0.00	0.00	38.33
536	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH	NR	04/2010	N.A.	N.A.	338.54	338.54	212.64	0.00	0.00	212.64
537	JAKHAL-MANSA DOUBLING ON SPR SECTION	NR	04/2008	N.A.	N.A.	162.96	162.96	153.31	0.00	0.00	153.31
538	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	NR	04/2013	N.A.	N.A.	400.00	400.00	0.00	0.00	0.00	0.00
539	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	NR	04/2013	N.A.	N.A.	876.00	876.00	0.00	0.00	0.00	0.00
540	UNCHAHAH-AMETHI	NR	04/2012	N.A.	N.A.	380.00	380.00	4.12	0.00	0.00	4.12
541	QADIAN-BEAS	NR	04/2011	N.A.	N.A.	205.22	205.22	1.59	0.00	0.00	1.59
542	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	N.A.	328.14	1540.00	45.20	0.00	0.00	45.20
543	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	N.A.	450.00	2100.00	484.14	0.00	0.00	484.14
544	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2018	2500.00	27946.00	15131.46	1000.00	0.00	16131.46
545	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	03/2002	06/2007	N.A.	625.30	876.10	841.57	0.00	0.00	841.57
546	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	N.A.	325.00	1581.53	618.19	0.00	0.00	618.19

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
547	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARGUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	895.00	545.33	139.74	9.49	694.56
548	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	N.A.	02/2019	410.08	795.01	338.97	49.62	3.49	392.08
549	PHULERA - DIGANA DOUBLING	NWR	05/2015	N.A.	03/2020	600.00	685.99	0.05	3.00	0.00	3.05
550	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	N.A.	873.71	873.71	0.00	0.00	0.00	0.00
551	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	1143.70	313.60	240.45	14.31	568.36
552	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	03/2019	246.08	348.55	12.88	49.01	7.61	69.50
553	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	N.A.	2082.75	2562.27	176.92	3.81	0.93	181.66
554	THIYAT HAMIRA-SANU	NWR	04/2013	N.A.	10/2018	236.93	294.90	76.49	38.09	4.24	118.82
555	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	N.A.	822.00	822.00	0.00	0.00	0.00	0.00
556	PUSHKAR-MERTA	NWR	04/2013	N.A.	N.A.	323.00	323.00	0.00	0.00	0.00	0.00
557	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	N.A.	N.A.	456.00	420.08	22.00	14.19	2.31	38.50
558	AJMER-BANGURGRAM	NWR	04/2011	N.A.	02/2019	213.39	244.02	59.10	67.85	14.42	141.37
559	RANI-MARWAR JN. PATCH DOUBLING	NWR	04/2012	N.A.	11/2018	288.97	346.35	136.74	77.12	14.52	228.38
560	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	N.A.	03/2019	242.09	349.00	49.81	98.72	0.00	148.53
561	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	N.A.	171.10	275.08	141.55	0.00	0.00	141.55
562	GOOTY-DHARMAVARAM-BANGLORE	MITES	04/2015	N.A.	N.A.	636.38	636.38	0.00	0.00	0.00	0.00
563	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	MITES	03/2015	03/2021	03/2021	636.38	636.38	63.60	105.56	0.00	169.16
564	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	03/2019	301.64	1185.99	829.14	249.43	51.78	1130.35
565	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	1202.07	333.94	155.05	34.89	523.88
566	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2017	133.41	343.00	349.57	14.64	0.50	364.71
567	GOELKERA-MANOHARPUR,(LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.70	388.00	303.59	44.93	11.74	360.26
568	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.20	1030.00	982.74	44.62	2.09	1029.45
569	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1223.85	344.92	98.46	1667.23
570	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	2913.50	694.86	35.08	20.77	750.71
571	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	03/2019	1046.88	4500.00	8.08	115.90	1.22	125.20
572	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	N.A.	970.34	1714.49	556.76	96.97	7.22	660.95

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
573	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	N.A.	03/2019	2127.00	2127.00	722.53	187.10	45.47	955.10
574	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	RVNL	04/1995	12/2012	N.A.	304.00	1141.70	373.37	162.59	24.25	560.21
575	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.90	555.00	462.25	46.26	8.84	517.35
576	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	4259.48	1285.44	282.54	67.76	1635.74
577	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	N.A.	2298.42	2070.00	38.91	1.25	0.00	40.16
578	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	N.A.	03/2020	1503.71	1503.71	325.71	253.09	62.67	641.47
579	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	03/2018	190.10	350.00	255.00	53.90	11.51	320.41
580	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	03/2020	567.18	975.62	218.82	169.15	43.77	431.74
581	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	12/2020	376.59	644.38	10.84	33.96	5.08	49.88
582	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	N.A.	12/2020	1266.89	1548.66	235.00	234.04	37.51	506.55
583	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	03/2018	822.39	1810.00	1580.43	98.62	32.46	1711.51
584	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	816.55	386.47	114.06	22.80	523.33
585	VIJAYAWADA-GUDUR	RVNL	04/2015	N.A.	N.A.	3246.26	3548.67	34.61	8.94	8.50	52.05
586	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	12/2024	12/2024	750.55	750.56	0.00	22.91	22.59	45.50
587	SECUNDERABAD-MAHABUBNAGAR DOUBLING	RVNL	04/2015	12/2024	12/2024	728.10	728.10	0.34	45.45	74.91	120.70
588	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2019	927.01	977.00	645.03	185.03	33.17	863.23
589	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	12/2025	12/2025	1765.90	1765.92	5.28	27.09	63.35	95.72
590	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2026	12/2026	4295.30	16216.00	152.09	422.00	187.21	761.30
591	DIGHI PORT NEW LINE	RVNL	04/2015	12/2025	12/2025	723.78	723.78	0.14	0.02	0.00	0.16
592	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2020	1514.45	1750.00	1090.71	265.39	32.25	1388.35
593	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	N.A.	12/2024	2335.67	2335.67	0.05	62.22	23.07	85.34

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
594	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2020	960.18	960.18	597.93	150.15	20.92	769.00
595	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	03/2020	758.09	758.09	552.83	142.46	34.74	730.03
596	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2019	942.95	942.95	745.15	99.95	5.12	850.22
597	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2020	1183.25	1183.30	622.96	143.34	31.14	797.44
598	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2020	1485.65	1485.85	593.76	135.97	23.03	752.76
599	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	03/2021	330.00	2120.16	189.39	57.00	3.51	249.90
600	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	N.A.	92.63	350.00	319.43	1.03	0.00	320.46
601	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	03/2022	378.56	1160.47	4.26	13.99	0.00	18.25
602	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	N.A.	1112.00	1112.00	0.89	0.03	0.00	0.92
603	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	N.A.	1054.35	2200.00	175.67	28.84	0.00	204.51
604	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	N.A.	923.23	923.23	1.87	0.53	0.00	2.40
605	GUDUR-DURGARAJAPATNAM	SCR	04/2011	N.A.	N.A.	283.54	761.37	0.51	0.00	0.00	0.51
606	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	N.A.	829.00	829.00	0.72	0.22	0.00	0.94
607	NADIKUDE-SRI KALAHASTI	SCR	04/2011	N.A.	N.A.	1313.48	2288.70	81.15	148.55	28.14	257.84
608	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	N.A.	337.49	704.31	1.13	68.56	0.00	69.69
609	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	N.A.	N.A.	2050.00	2132.77	254.75	62.09	0.00	316.84
610	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	N.A.	313.24	607.70	507.71	60.89	0.00	568.60
611	NANDYAL-YERRAGUNTLA(NL),SCR	SCR	03/1996	02/2009	N.A.	155.74	966.43	934.30	34.87	5.88	975.05
612	MUNEERABAD-MAHABOBNAGAR(NL),SCR	SCR	04/1997	N.A.	03/2019	218.24	525.00	650.16	30.32	6.76	687.24
613	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	N.A.	125.00	458.26	3.69	0.00	0.00	3.69
614	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	N.A.	124.43	1010.00	992.25	21.01	0.00	1013.26
615	KONDAPALLI-KOTHAGUDEM	SCR	04/2013	N.A.	N.A.	616.08	616.08	0.00	0.00	0.00	0.00
616	DUVVADA-VIJAYAWADA	SCR	04/2015	N.A.	N.A.	3873.07	3873.07	0.07	0.00	0.00	0.07
617	GUNTUR-GUNTAKAL	SCR	04/2016	N.A.	N.A.	4000.00	3631.00	0.00	19.31	31.90	51.21
618	KAZIPET-BALHRSHA	SCR	04/2015	N.A.	03/2021	2063.03	2063.03	136.89	65.22	0.00	202.11
619	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	03/2022	119.73	184.97	0.00	0.00	0.00	0.00
620	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	N.A.	383.79	1101.16	194.91	0.00	0.00	194.91
621	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	967.96	0.00	0.00	967.96
622	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	12/2021	1273.00	1908.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
623	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	12/2018	12/2018	737.72	737.72	58.62	45.48	0.00	104.10
624	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	N.A.	466.48	750.00	0.00	0.00	0.00	0.00
625	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	N.A.	276.69	426.00	0.00	0.00	0.00	0.00
626	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	N.A.	393.46	1026.00	182.46	0.02	0.00	182.48
627	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	N.A.	293.97	749.69	0.00	0.00	0.00	0.00
628	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	N.A.	194.07	583.02	537.55	30.47	0.00	568.02
629	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	N.A.	148.77	209.00	81.44	48.25	4.13	133.82
630	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	N.A.	267.37	434.00	40.66	0.00	0.11	40.77
631	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	N.A.	553.63	1009.00	7.90	0.03	0.00	7.93
632	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	N.A.	289.64	760.00	0.13	0.00	0.00	0.13
633	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	N.A.	149.90	230.00	54.96	0.00	0.00	54.96
634	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	N.A.	309.44	583.00	380.90	46.89	9.17	436.96
635	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	N.A.	258.20	365.00	78.90	44.43	19.81	143.14
636	ARA-BHABHUA ROAD (NL)	SER	04/2008	N.A.	N.A.	490.80	490.80	0.39	0.00	0.00	0.39
637	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	03/2020	969.83	969.83	47.14	198.99	22.52	268.65
638	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	03/2021	1724.20	1724.20	110.03	56.77	17.46	184.26
639	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	12/2021	763.18	1428.00	480.45	2.82	1.20	484.47
640	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2021	524.43	939.00	183.99	0.00	0.00	183.99
641	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	N.A.	1027.40	2373.00	482.65	0.00	1.68	484.33
642	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	N.A.	240.00	579.37	535.00	2.30	0.00	537.30
643	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	N.A.	155.55	920.00	849.35	7.59	0.00	856.94
644	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	N.A.	280.00	1122.00	834.61	0.00	0.00	834.61
645	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	N.A.	404.19	2072.50	832.99	215.38	0.00	1048.37

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
646	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	N.A.	343.17	1065.00	1026.42	23.26	0.00	1049.68
647	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	N.A.	456.00	2300.00	209.66	21.74	0.00	231.40
648	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	N.A.	550.00	2815.62	235.08	5.60	0.00	240.68
649	ATTIPPATTU PUTTUR	SR	04/2008	N.A.	N.A.	446.87	1105.00	3.34	0.00	0.00	3.34
650	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	N.A.	523.52	2350.00	2.26	0.01	0.00	2.27
651	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	N.A.	839.00	1500.00	0.61	0.00	0.00	0.61
652	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	N.A.	271.24	520.00	464.30	3.88	0.00	468.18
653	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	N.A.	270.14	346.15	251.56	2.31	0.00	253.87
654	KUMBALAM-TURAVUR	SR	04/2011	N.A.	N.A.	252.96	252.96	7.16	0.58	0.00	7.74
655	ERODE-PALANI	SR	04/2008	N.A.	N.A.	288.57	1140.00	1.63	0.00	0.00	1.63
656	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	N.A.	164.41	450.00	29.78	6.48	0.00	36.26
657	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	N.A.	191.72	342.85	359.08	19.68	0.00	378.76
658	ERNAKULAM-KUMBALAM	SR	04/2010	N.A.	N.A.	189.24	189.24	6.17	0.11	0.00	6.28
659	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	N.A.	N.A.	601.43	1800.00	55.20	21.97	0.00	77.17
660	TRIVANDRUM-KANYAKUMARI DOUBLING	SR	02/2015	N.A.	N.A.	900.00	4131.90	0.00	0.00	0.00	0.00
661	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	N.A.	1000.00	1000.00	0.00	0.00	0.00	0.00
662	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	N.A.	913.00	1801.01	2.54	1.05	0.00	3.59
663	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	N.A.	179.65	1350.91	694.79	120.94	16.87	832.60
664	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	N.A.	377.93	986.30	258.97	19.27	1.34	279.58
665	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAIL NILAYAM NL	SWR	04/2013	N.A.	N.A.	558.00	692.43	0.00	0.00	0.00	0.00
666	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	N.A.	296.00	466.65	0.00	0.00	0.00	0.00
667	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	N.A.	562.74	832.47	0.94	0.00	0.00	0.94
668	WHITE FIELD-KOLAR NL	SWR	04/2011	N.A.	N.A.	341.05	348.85	0.35	0.00	0.00	0.35
669	TORANAGALLU-RANJITPURA DL	SWR	04/2011	N.A.	N.A.	146.75	167.50	0.32	0.02	0.00	0.34
670	GADAG-WADI NL	SWR	04/2013	N.A.	N.A.	1117.00	1922.00	2.88	5.47	7.43	15.78
671	CHIKBALLA-PUR-GOWRIBIDANUR NL	SWR	04/2013	N.A.	N.A.	327.25	367.77	0.00	0.31	0.03	0.34
672	MARIKUPPAM - KUPPAM	SWR	04/2012	01/1999	N.A.	285.57	279.54	1.51	2.44	0.00	3.95
673	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	N.A.	227.00	2135.00	133.71	0.20	0.00	133.91
674	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	N.A.	138.00	1382.78	5.59	0.53	0.12	6.24
675	HUBLI- CHIKJAJUR	SWR	03/2015	N.A.	N.A.	1900.00	1141.00	311.74	209.70	24.61	546.05

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
676	MIRAJ-LONDA	SWR	03/2015	N.A.	N.A.	1830.00	1190.92	16.77	102.73	0.00	119.50
677	YELAHANKA-PENUKONDA	SWR	05/2015	N.A.	03/2020	860.43	860.43	213.40	145.56	27.51	386.47
678	ARSIKERE-TUMKUR	SWR	03/2015	N.A.	03/2020	960.00	578.00	239.60	102.24	23.52	365.36
679	HOTGI-KUDGI-GADAG	SWR	03/2015	N.A.	N.A.	1618.00	1614.59	318.05	237.18	0.00	555.23
680	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	03/2021	470.92	2713.09	624.49	7.56	0.00	632.05
681	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	972.82	0.00	0.00	972.82
682	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	12/2020	12/2020	1762.94	1762.94	0.00	0.00	0.00	0.00
683	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2022	2478.23	2478.23	0.00	0.00	0.00	0.00
684	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2020	03/2020	582.13	582.13	0.00	0.00	0.00	0.00
685	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	N.A.	603.04	1030.29	754.84	169.46	13.07	937.37
686	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	03/2011	N.A.	117.36	203.00	202.29	0.00	0.00	202.29
687	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	N.A.	1389.62	2446.85	1767.90	251.43	27.01	2046.34
688	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	321.62	93.66	-11.70	0.28	82.24
689	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	385.60	205.45	126.90	10.78	343.13
690	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	N.A.	N.A.	1347.26	1347.26	397.75	136.51	-1.85	532.41
691	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	N.A.	03/2022	1640.04	1640.04	413.24	46.43	4.42	464.09
692	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	N.A.	439.88	844.10	0.86	15.03	0.35	16.24
693	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	03/2019	320.66	858.96	546.88	2.05	0.00	548.93
694	VIRAMGAM-SURENDRANAGAR (DL)	WR	04/2010	N.A.	N.A.	279.40	355.00	335.40	-7.36	0.00	0.00
695	SURENDRA NAGAR RAJKOT	WR	04/2015	N.A.	03/2021	1002.39	1002.39	93.30	50.90	11.58	155.78
696	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	WR	03/2017	N.A.	N.A.	243.60	243.60	0.00	0.00	0.00	0.00
697	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	WR	03/2010	N.A.	N.A.	265.88	265.88	0.00	0.00	0.00	0.00
698	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	WR	03/2012	N.A.	N.A.	217.38	217.38	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
699	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	WR	03/2012	N.A.	N.A.	248.26	248.26	0.00	0.00	0.00	0.00
700	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	WR	03/2012	N.A.	N.A.	153.83	153.83	0.00	0.00	0.00	0.00
ROAD TRANSPORT AND HIGHWAYS											
701	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	DORTH	03/2015	N.A.	N.A.	298.33	298.33	16.10	0.00	0.00	16.10
702	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	DORTH	03/2015	N.A.	N.A.	184.05	184.05	10.72	0.00	0.00	10.72
703	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	DORTH	03/2015	N.A.	N.A.	280.16	280.16	16.06	0.00	0.00	16.06
704	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A	DORTH	12/2014	02/2015	N.A.	201.12	201.12	0.00	0.00	0.00	0.00
705	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR	MORTH	07/2015	N.A.	N.A.	314.43	314.43	0.00	0.00	0.00	0.00
706	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	MORTH	10/2015	N.A.	N.A.	289.60	289.60	0.00	0.00	0.00	0.00
707	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	MORTH	12/2011	N.A.	N.A.	156.26	156.26	65.16	0.00	0.00	65.16
708	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	MORTH	03/2011	N.A.	11/2014	185.82	185.82	205.97	0.00	0.00	205.97
709	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	MORTH	03/2015	N.A.	N.A.	422.34	422.34	22.25	0.00	0.00	22.25
710	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	MORTH	10/2015	N.A.	N.A.	480.21	480.21	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
711	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	MORTH	10/2014	01/2015	N.A.	269.22	269.22	33.24	0.00	0.00	33.24
712	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	MORTH	10/2014	01/2015	N.A.	257.09	257.09	14.80	0.00	0.00	14.80
713	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	MORTH	10/2013	05/2014	N.A.	278.87	278.87	0.00	0.00	0.00	0.00
714	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF	MORTH	01/1991	04/2014	N.A.	376.52	376.52	0.00	0.00	0.00	0.00
715	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	MORTH	02/2015	03/2015	N.A.	383.40	383.40	224.68	0.00	0.00	224.68
716	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	MORTH	03/2015	08/2015	N.A.	258.97	268.92	0.00	0.00	0.00	0.00
717	REHABILITATION AND UPGRADATION OF NH 226 FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	MORTH	03/2015	07/2015	N.A.	157.18	162.00	0.00	0.00	0.00	0.00
718	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	MORTH	11/2015	08/2015	08/2015	154.14	154.14	0.00	0.00	0.00	0.00
719	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	MORTH	03/2015	N.A.	N.A.	629.74	629.74	0.00	0.00	0.00	0.00
720	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	MORTH	01/2014	03/2016	03/2016	282.41	282.41	0.00	0.00	0.00	0.00
721	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	MORTH	01/2015	N.A.	N.A.	225.81	225.81	6.50	0.00	0.00	6.50
722	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	MORTH	12/2015	06/2018	06/2018	621.43	621.43	0.00	0.00	0.00	0.00
723	STRENGTHENING AND WIDENING TO TWO LANES WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	165.67	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
724	STRENGTHENING AND WIDENING TO TWO LANES WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPUR	MORTH	03/2015	11/2015	11/2017	159.12	159.12	0.00	0.00	0.00	0.00
725	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	MORTH	10/2014	10/2016	10/2016	227.74	227.74	0.00	0.00	0.00	0.00
726	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	MORTH	01/1991	10/2016	10/2016	269.26	269.26	212.72	0.00	0.00	212.72
727	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	MORTH	01/1991	01/2018	01/2018	219.40	219.40	0.00	0.00	0.00	0.00
728	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	MORTH	01/1991	10/2017	10/2017	218.63	218.63	29.27	0.00	0.00	29.27
729	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	MORTH	01/1991	N.A.	N.A.	675.00	675.00	0.00	0.00	0.00	0.00
730	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	MORTH	01/1991	03/2018	03/2018	322.00	322.00	56.41	0.00	0.00	56.41
731	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	MORTH	01/1991	08/2016	08/2016	282.41	282.41	67.52	0.00	0.00	67.52
732	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	MORTH	01/1991	10/2016	10/2016	358.22	358.22	188.71	0.00	0.00	188.71
733	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI	MORTH	01/1991	05/2016	05/2016	208.87	208.87	206.78	0.00	0.00	206.78
734	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	MORTH	01/1991	05/2018	05/2018	229.41	229.41	6.65	0.00	0.00	6.65
735	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	MORTH	10/2015	N.A.	N.A.	936.40	936.40	0.00	0.00	0.00	0.00
736	WIDENING WITH PS AND STRONG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	08/2015	164.54	164.54	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
737	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	MORTH	12/2014	N.A.	N.A.	207.88	207.88	0.00	0.00	0.00	0.00
738	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	MORTH	12/2015	N.A.	N.A.	773.98	773.98	0.00	0.00	0.00	0.00
739	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	MORTH	12/2015	N.A.	N.A.	819.95	819.95	0.00	0.00	0.00	0.00
740	REHABILITATION AND UPGRADING TO 2 LANES- 2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	MORTH	01/1991	N.A.	N.A.	478.35	478.35	0.00	0.00	0.00	0.00
741	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	MORTH	12/2014	N.A.	N.A.	207.88	207.88	0.00	0.00	0.00	0.00
742	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	MORTH	10/2014	03/2014	N.A.	377.64	377.64	0.00	0.00	0.00	0.00
743	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	MORTH	10/2013	08/2014	08/2014	278.39	278.39	0.00	0.00	0.00	0.00
744	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	MORTH	01/2013	08/2014	N.A.	322.01	322.01	0.00	0.00	0.00	0.00
745	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	11/2013	07/2016	N.A.	683.83	683.83	0.00	0.00	0.00	0.00
746	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	MORTH	02/2014	07/2016	N.A.	665.50	665.50	0.00	0.00	0.00	0.00
747	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	02/2016	05/2016	N.A.	178.85	178.85	0.00	0.00	0.00	0.00
748	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	02/2016	06/2016	06/2016	369.77	369.77	0.00	0.00	0.00	0.00
749	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	02/2016	05/2016	N.A.	553.30	553.30	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
750	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MORTH	01/2014	10/2016	N.A.	1408.85	1408.85	0.00	0.00	0.00	0.00
751	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV	MORTH	03/2015	07/2016	10/2016	206.80	206.80	0.00	0.00	0.00	0.00
752	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	MORTH	08/2015	11/2015	N.A.	288.24	288.24	0.00	0.00	0.00	0.00
753	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	MORTH	08/2016	12/2016	12/2016	1742.01	1742.01	0.00	0.00	0.00	0.00
754	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	MORTH	03/2014	05/2016	06/2017	191.50	192.00	0.00	0.00	0.00	0.00
755	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W	MORTH	01/2015	04/2018	04/2018	326.63	327.00	0.00	0.00	0.00	0.00
756	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	MORTH	02/2015	10/2017	10/2017	239.91	240.00	0.00	0.00	0.00	0.00
757	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	MORTH	03/2015	10/2017	10/2017	226.31	226.00	0.00	0.00	0.00	0.00
758	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	MORTH	12/2013	05/2016	03/2017	319.80	320.00	0.00	0.00	0.00	0.00
759	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	MORTH	07/2014	01/2017	N.A.	342.05	342.00	0.00	0.00	0.00	0.00
760	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	MORTH	08/2013	06/2016	N.A.	171.96	172.00	0.00	0.00	0.00	0.00
761	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	MORTH	06/2016	06/2018	11/2018	157.30	157.00	0.00	0.00	0.00	0.00
762	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	MORTH	03/2014	05/2016	03/2017	162.51	163.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
763	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	05/2018	280.00	361.00	410.32	0.48	0.00	0.00
764	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2017	199.81	385.13	209.80	4.23	0.00	0.00
765	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	09/2018	167.64	167.64	268.94	9.17	0.00	0.00
766	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	280.13	195.35	0.00	0.00	0.00
767	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	10/2018	200.00	200.00	245.83	6.52	0.00	0.00
768	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	08/2017	486.00	486.00	475.57	6.30	0.00	0.00
769	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	02/2018	160.00	160.00	198.82	6.64	0.00	0.00
770	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2018	196.00	331.23	340.12	11.84	0.00	0.00
771	TALEGAON-AMRAVATI	NHAI	11/2009	11/2013	N.A.	567.00	567.00	1055.94	0.00	0.00	1055.94
772	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108.00	2288.00	3869.00	13.53	0.00	0.00
773	DEOLI KOTA	NHAI	01/2011	07/2013	10/2017	593.00	593.00	1036.26	0.00	0.00	0.00
774	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	03/2018	1348.20	1348.20	1593.87	199.03	0.00	1792.90
775	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2017	617.00	617.00	245.89	0.00	0.00	0.00
776	MURADABAD-BAREILY	NHAI	04/2010	06/2013	09/2017	1267.00	1267.00	2664.02	3.94	0.00	2667.96
777	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	12/2017	2498.76	2498.76	2489.54	0.00	0.00	0.00
778	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2017	1724.55	1724.55	1997.63	73.02	21.00	2091.65
779	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	07/2017	325.00	325.00	469.54	1.50	0.00	0.00
780	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	11/2017	245.00	245.00	214.88	1.74	0.00	0.00
781	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	04/2018	217.61	309.56	389.08	2.28	0.00	0.00
782	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2018	208.00	208.00	297.81	0.00	0.00	0.00
783	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	03/2018	225.00	225.00	312.79	1.72	0.00	0.00
784	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	N.A.	275.00	281.31	168.31	2.95	0.00	0.00
785	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	N.A.	604.00	604.00	423.83	0.00	0.00	0.00
786	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	12/2017	1585.00	1585.00	2159.63	213.97	0.00	0.00
787	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	NHAI	11/2013	11/2016	02/2018	1916.79	1916.79	1737.91	146.50	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
788	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2018	1266.60	1266.60	1163.00	212.60	0.00	1375.60
789	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.10	3237.87	3176.22	10.97	0.00	0.00
790	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	09/2017	1175.00	1206.10	1206.00	20.83	0.00	0.00
791	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	09/2017	1693.75	1693.75	2675.28	0.00	0.00	0.00
792	2-LANING WITH PS BHILWARA-LODPURA SECTION	NHAI	03/2014	03/2016	N.A.	240.10	240.10	151.72	2.00	0.00	0.00
793	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	N.A.	06/2018	946.00	946.00	818.53	0.00	0.00	818.53
794	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987.00	1987.00	1566.61	95.60	0.00	0.00
795	NASHRI- CHANANI	NHAI	05/2011	06/2015	N.A.	2159.00	2159.00	3986.82	0.00	0.00	3986.82
796	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	11/2017	1813.76	1813.76	2393.99	0.00	0.00	0.00
797	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2018	671.30	671.30	880.29	0.00	0.00	0.00
798	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	10/2017	351.54	351.54	351.23	0.00	0.00	0.00
799	ROHTAK-BAWAL	NHAI	05/2011	11/2013	08/2017	650.00	650.00	832.39	0.00	0.00	0.00
800	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	08/2017	1141.00	1141.00	1948.72	37.84	0.00	1986.56
801	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2018	1250.00	1250.00	1328.96	0.35	0.00	1329.31
802	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	N.A.	600.00	600.00	316.63	3.13	0.00	319.76
803	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	N.A.	953.88	953.88	974.73	0.39	0.00	0.00
804	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2018	374.00	374.00	237.00	0.00	0.00	237.00
805	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI	NHAI	09/2011	08/2013	12/2018	485.00	485.00	406.68	0.00	0.00	406.68
806	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2018	571.00	571.00	582.52	0.00	0.00	582.52
807	JORBAT - BARAPANI	NHAI	01/2011	01/2014	03/2018	536.00	536.00	671.62	1.10	0.00	0.00
808	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2018	2848.00	2848.00	574.74	45.69	0.00	0.00
809	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2017	1535.00	1535.00	2993.77	177.00	0.00	0.00
810	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	N.A.	664.00	664.00	654.59	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
811	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	09/2017	574.00	574.00	898.99	0.30	0.00	0.00
812	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	N.A.	375.09	375.09	494.33	0.00	0.00	0.00
813	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2018	575.00	575.00	604.61	0.00	0.00	0.00
814	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2017	511.54	511.54	545.27	0.00	0.00	0.00
815	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2017	1100.70	1100.70	1216.15	124.72	0.00	0.00
816	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	03/2018	1410.00	1410.00	1555.96	0.00	0.00	0.00
817	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	10/2017	1046.00	1046.00	541.42	138.31	13.73	693.46
818	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	11/2017	754.00	754.00	1077.66	77.65	11.84	1167.15
819	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2017	1078.84	1078.84	2302.79	123.50	9.86	2436.15
820	4-LANING OF BRAHAMPURE-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	998.79	1816.24	129.58	6.53	1952.35
821	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	12/2017	1047.00	1047.00	1613.62	16.21	0.00	0.00
822	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2017	1396.18	1396.18	2600.47	171.33	39.49	2811.29
823	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2017	291.36	291.36	320.46	6.00	21.03	347.49
824	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	03/2018	702.16	702.16	418.47	132.65	13.27	564.39
825	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2017	478.51	478.00	366.77	42.40	0.00	0.00
826	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	NHAI	04/2012	04/2014	N.A.	624.00	624.00	350.79	0.00	0.00	350.79
827	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2017	1479.00	1479.00	740.26	130.40	10.42	881.08
828	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2018	942.69	942.69	345.22	71.61	21.07	437.90
829	ETAWAH CHAKERI	NHAI	03/2013	09/2015	10/2017	1573.00	1573.00	1850.00	0.00	0.00	1850.00
830	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	07/2017	2125.24	2125.24	4659.71	0.00	0.00	0.00
831	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2017	1928.22	1928.22	2211.94	276.06	0.00	0.00
832	TWO LANING WITH PAVED SHOULDER BARMER SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N	NHAI	08/2015	02/2018	02/2018	538.08	538.08	30.08	22.07	0.00	0.00
833	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	09/2018	709.00	709.00	131.27	152.05	9.80	293.12
834	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	09/2017	425.19	425.19	217.87	0.00	0.00	0.00
835	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	NHAI	08/2015	02/2018	02/2018	723.54	723.54	530.94	31.29	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
836	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	08/2018	1387.11	1387.11	472.61	296.67	0.00	769.28
837	JAISALMER - BARMER	NHAI	08/2015	02/2018	02/2018	482.27	482.27	40.75	30.38	0.00	0.00
838	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	12/2017	523.85	523.85	170.68	79.40	0.00	0.00
839	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	12/2018	563.92	563.92	53.85	42.04	0.00	95.89
840	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50)	NHAI	07/2015	07/2017	07/2017	455.60	455.60	54.50	11.62	0.00	0.00
841	JODHPUR - BARMER SECTION OF PACKAGE -I	NHAI	10/2014	04/2017	N.A.	264.72	264.72	98.18	0.00	0.00	0.00
842	PADI - DAHOD	NHAI	11/2014	05/2017	N.A.	279.14	279.14	62.77	2.50	0.00	0.00
843	FOUR LANING OF VARANASI BYPASS	NHAI	05/2015	05/2017	06/2018	261.09	261.09	31.17	55.11	0.00	86.28
844	UP/HARYANA BORDER - YAMUNA NAGAR -SAHAWARWALA - PANCHKULA(PKG - 2)	NHAI	10/2015	04/2018	04/2018	562.34	562.34	109.07	183.87	0.00	0.00
845	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	NHAI	09/2015	03/2018	03/2018	567.51	567.51	42.79	0.00	0.00	0.00
846	THIRUMAYAM - MANAMADURAI SECTION	NHAI	07/2014	01/2017	N.A.	401.11	401.11	269.47	4.42	0.00	273.89
847	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	11/2017	351.34	351.34	318.65	91.27	0.00	409.92
848	VADODARA-SURAT SECTION	NHAI	03/2014	08/2016	N.A.	503.16	503.16	346.60	25.21	0.00	0.00
849	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	NHAI	09/2015	09/2016	09/2017	368.73	368.73	159.86	46.79	0.00	0.00
850	2-LANING WITH PS SITARGANJ BAREILLY SECTION	NHAI	06/2014	01/2016	N.A.	301.04	301.04	110.86	37.06	0.00	147.92
851	2-LANING WITH PAVED SHOULDERS OF TANDA RAEBARELI	NHAI	04/2014	01/2016	11/2017	495.78	495.78	445.83	110.69	9.82	566.34
852	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	06/2018	563.92	563.92	186.13	0.37	0.00	186.50
853	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2018	597.00	597.00	0.00	21.54	0.00	0.00
854	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	NHAI	07/2015	N.A.	05/2019	2288.18	2288.18	0.00	0.00	0.00	0.00
855	4 LANING OF BAHARAGORA - SINGHARA	NHAI	07/2015	N.A.	N.A.	1282.94	1282.94	0.00	0.00	0.00	0.00
856	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	N.A.	530.07	530.07	234.21	0.12	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
857	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	N.A.	05/2018	414.51	414.00	0.00	130.04	27.88	157.92
858	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI)	NHAI	09/2015	03/2018	03/2018	768.56	768.56	275.78	398.01	26.19	699.98
859	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	N.A.	05/2018	531.13	531.13	0.00	100.18	62.92	163.10
860	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V)	NHAI	09/2015	03/2018	03/2018	664.53	664.53	228.16	339.14	23.52	590.82
861	CONSTRUCTION OF ISLAMPUR BY PASS	NHAI	10/2015	N.A.	01/2018	361.15	361.15	0.00	0.00	0.00	0.00
862	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	NHAI	07/2015	N.A.	05/2019	1885.74	1885.74	0.00	0.00	0.00	0.00
863	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	N.A.	05/2018	593.26	593.26	0.00	20.02	25.09	45.11
864	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV)	NHAI	09/2015	03/2018	03/2018	789.31	789.31	372.34	370.92	70.93	814.19
865	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	N.A.	03/2019	649.50	649.50	0.00	31.47	0.00	31.47
866	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	602.95	54.89	211.88	0.00	0.00
867	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	04/2018	822.90	822.90	55.00	0.00	0.00	0.00
868	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	NHAI	09/2015	03/2018	03/2018	788.51	788.51	103.37	238.18	0.00	0.00
869	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	07/2018	574.28	574.28	51.47	152.82	0.00	0.00
870	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	N.A.	04/2019	2128.72	2128.72	106.57	142.58	0.00	0.00
871	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	NHAI	09/2015	03/2018	03/2018	785.78	785.78	324.20	449.75	22.57	796.52
872	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	N.A.	05/2018	505.00	505.00	0.00	136.04	25.09	161.13
873	6 LANING OF AGRA - ETAWAH BYPASS	NHAI	07/2015	N.A.	01/2019	1657.20	1657.20	0.00	505.00	40.00	545.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
874	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	01/2018	972.50	972.50	1302.04	177.10	0.42	1479.56
875	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	11/2017	923.04	923.04	422.83	102.19	10.50	535.52
876	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	NHAI	06/2015	N.A.	11/2017	845.24	845.24	47.56	16.94	0.00	0.00
877	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	611.65	47.83	292.54	43.18	383.55
878	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	02/2019	1655.01	1655.01	1194.00	282.75	7.96	1484.71
879	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	06/2018	1083.00	1083.00	26.64	153.28	5.00	184.92
880	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	NHAI	03/2015	N.A.	N.A.	795.76	795.76	92.24	87.23	0.00	0.00
881	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	NHAI	03/2015	N.A.	N.A.	794.30	794.30	63.42	48.41	0.00	0.00
882	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	06/2019	2168.66	2168.66	0.00	0.00	0.00	0.00
883	NAGPUR - KONDHALI	NHAI	09/2005	06/2006	N.A.	168.00	168.00	279.92	0.00	0.00	279.92
884	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	NHAI	09/2015	N.A.	11/2017	273.06	273.06	17.85	37.50	0.00	0.00
885	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	12/2017	1673.70	1673.70	3073.44	91.98	0.00	0.00
886	FOUR LANING OF PATNA TO KOILWAR	NHAI	08/2015	N.A.	N.A.	556.07	556.07	0.00	0.00	0.00	0.00
887	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	03/2018	934.46	934.46	104.98	72.11	0.00	0.00
888	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	NHAI	12/2015	N.A.	04/2019	1041.10	1041.10	0.00	0.00	0.00	0.00
889	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	12/2017	1232.00	1232.00	1090.17	0.00	0.00	0.00
890	FOUR LANING OF KOILWAR TO BHOJPUR	NHAI	08/2015	N.A.	N.A.	814.04	814.04	0.00	0.00	0.00	0.00
891	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	NHAI	09/2014	N.A.	12/2017	479.00	479.00	391.33	16.43	0.00	0.00
892	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21	NHAI	12/2015	12/2017	12/2017	239.23	239.23	123.47	44.69	0.00	0.00
893	FOUR LANING WITH PS TALEBANI -SMBALPUR	NHAI	12/2015	N.A.	N.A.	752.28	752.28	0.00	0.00	0.00	0.00
894	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	N.A.	11/2018	1423.96	1423.96	444.03	10.61	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
895	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	NHAI	07/2015	N.A.	01/2018	1393.00	1393.00	1917.27	344.81	0.00	0.00
896	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	12/2018	2136.97	2136.97	0.00	27.62	0.00	0.00
897	FOUR LANING OF JABALPUR - LAKHNADON	NHAI	03/2015	N.A.	12/2017	928.83	928.83	139.75	1114.62	0.00	0.00
898	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	N.A.	08/2018	1388.00	1388.00	363.58	271.68	18.87	654.13
899	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	06/2018	815.28	815.28	34.04	96.31	10.81	141.16
900	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	NHAI	11/2015	N.A.	05/2018	867.66	867.66	502.66	59.69	0.00	0.00
901	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	NHAI	01/2016	06/2018	06/2018	1027.53	1027.53	73.87	144.47	10.55	228.89
902	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	09/2017	1055.00	1601.77	1328.85	0.00	0.00	0.00
903	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	N.A.	05/2018	596.67	596.67	0.00	67.84	0.00	0.00
904	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.90	1012.90	429.04	159.22	0.00	0.00
905	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	06/2018	667.00	667.00	51.96	132.24	10.83	195.03
906	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	06/2018	667.00	667.00	78.95	143.10	25.66	247.71
907	FOUR LANING OF SHIVPURI - GUNA PACKAGE -	NHAI	01/2016	07/2018	07/2018	830.36	830.36	305.95	167.13	0.00	0.00
908	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	N.A.	04/2018	322.09	322.09	0.00	0.00	0.00	0.00
909	FOUR LANING OF SARAGAON - BILASPUR	NHAI	12/2015	N.A.	04/2018	509.13	509.13	0.00	202.90	0.00	0.00
910	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	447.29	4.88	46.87	0.00	0.00
911	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	NHAI	03/2015	N.A.	N.A.	810.22	810.22	63.60	82.49	0.00	0.00
912	FOUR LANING OF BIAORA DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	NHAI	06/2015	N.A.	01/2019	1583.79	1583.79	357.53	202.67	0.00	0.00
913	FOUR LANING OF BHOJPUR TO BUXAR	NHAI	01/1991	N.A.	N.A.	642.41	642.41	0.00	0.00	0.00	0.00
914	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	NHAI	12/2015	N.A.	N.A.	1167.45	1167.45	0.00	0.00	0.00	0.00
915	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	01/2018	1871.34	1871.34	2169.89	678.42	33.50	2881.81
916	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	1170.52	2041.03	63.52	158.47	2263.02

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
917	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	N.A.	04/2018	726.67	726.67	0.00	18.03	0.00	0.00
918	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	12/2017	1665.00	1665.00	1738.47	575.21	0.00	2313.68
919	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	N.A.	05/2018	479.20	479.20	6.14	0.00	0.00	0.00
920	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	N.A.	04/2019	399.54	399.54	0.00	0.00	0.00	0.00
921	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	NHAI	08/2015	N.A.	02/2018	275.90	275.90	0.00	0.00	0.00	0.00
922	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ	NHAI	08/2015	N.A.	12/2017	854.80	854.80	0.00	0.00	0.00	0.00
923	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR	NHAI	08/2015	N.A.	04/2018	516.13	516.13	18.48	0.00	0.00	0.00
924	TRICHY - KARUR	NHAI	03/2007	07/2008	N.A.	516.00	516.00	761.19	0.00	0.00	761.19
925	MEERUT-BULANDSHAHAR	NHAI	01/2016	N.A.	N.A.	683.24	683.24	0.45	0.00	0.00	0.45
926	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	NHAI	01/2016	N.A.	05/2019	701.12	701.12	0.00	0.00	0.00	0.00
927	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	NHAI	01/2016	N.A.	06/2019	1081.57	1081.57	0.00	0.00	0.00	0.00
928	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62	NHAI	03/2016	N.A.	07/2018	197.69	197.69	0.00	0.00	0.00	0.00
929	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	NHAI	03/2016	N.A.	04/2019	676.73	676.73	0.00	115.21	0.00	115.21
930	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	NHAI	01/2016	N.A.	11/2018	1134.97	1134.97	16.31	251.79	0.00	0.00
931	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	NHAI	02/2016	N.A.	02/2019	273.20	273.20	0.00	21.43	0.00	0.00
932	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	NHAI	03/2016	N.A.	N.A.	1404.50	1404.50	0.00	9.62	18.46	28.08
933	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	NHAI	02/2016	N.A.	03/2019	997.15	997.15	0.00	329.10	0.00	329.10
934	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	NHAI	03/2016	N.A.	N.A.	1396.74	1396.74	0.00	4.10	9.45	13.55

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
935	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	NHAI	02/2016	N.A.	N.A.	1069.65	1069.65	0.00	0.00	0.00	0.00
936	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	N.A.	04/2019	1587.49	1587.49	0.00	24.95	0.00	24.95
937	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	N.A.	03/2019	701.40	701.40	0.00	5.78	0.00	5.78
938	CONSTRUCTION OF ROBFLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	N.A.	11/2018	229.37	229.37	6.39	28.78	0.00	35.17
939	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	N.A.	03/2019	870.00	870.00	1.45	2.58	0.00	4.03
940	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	N.A.	08/2018	707.82	707.82	129.75	0.00	0.00	129.75
941	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	N.A.	04/2019	899.00	899.00	0.00	0.00	0.00	0.00
942	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	N.A.	07/2018	641.17	641.17	27.95	46.18	0.00	74.13
943	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	N.A.	07/2019	546.00	546.00	0.00	0.00	0.00	0.00
944	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	NHAI	03/2016	N.A.	N.A.	720.00	720.00	0.00	0.00	0.00	0.00
945	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	N.A.	07/2019	591.66	591.66	0.00	0.00	0.00	0.00
946	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60	NHAI	03/2016	N.A.	07/2018	244.00	244.00	0.00	0.00	0.00	0.00
947	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	NHAI	03/2016	N.A.	N.A.	1443.00	1443.00	0.00	0.00	0.00	0.00
948	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	NHAI	03/2016	N.A.	N.A.	1668.00	1668.00	0.00	0.00	0.00	0.00
949	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	NHAI	03/2016	N.A.	N.A.	1408.00	1408.00	0.00	0.00	0.00	0.00
950	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	NHAI	03/2016	N.A.	N.A.	1737.00	1737.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
951	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	N.A.	06/2018	804.97	804.97	0.00	0.00	0.00	0.00
952	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	NHAI	05/2016	N.A.	N.A.	998.18	998.18	0.00	0.00	0.00	0.00
953	FOUR LANING OF TALAJA MAHUVA SECTION OF NH 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	NHAI	05/2016	N.A.	N.A.	834.64	834.64	0.00	0.00	0.00	0.00
954	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	NHAI	05/2016	N.A.	N.A.	723.64	723.64	0.00	0.00	0.00	0.00
955	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	NHAI	05/2016	N.A.	N.A.	763.08	763.08	0.00	0.00	0.00	0.00
956	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	NHAI	05/2016	N.A.	N.A.	425.60	425.60	0.00	0.00	0.00	0.00
957	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	NHAI	05/2016	N.A.	N.A.	364.56	364.56	0.00	0.00	0.00	0.00
958	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	NHAI	06/2016	06/2019	N.A.	637.18	637.18	0.00	0.00	0.00	0.00
959	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	NHAI	06/2016	06/2019	06/2019	763.23	763.23	0.00	0.00	0.00	0.00
960	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	NHAI	06/2016	06/2019	06/2019	649.00	649.00	0.00	0.00	0.00	0.00
961	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	NHAI	05/2015	05/2017	N.A.	581.84	581.84	77.43	0.00	0.00	0.00
962	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	NHAI	07/2016	N.A.	N.A.	688.70	688.70	0.00	0.00	0.00	0.00
963	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	NHAI	07/2016	N.A.	N.A.	829.97	829.97	0.00	0.00	0.00	0.00
964	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	NHAI	07/2016	N.A.	10/2018	331.46	331.46	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
965	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	NHAI	07/2016	N.A.	N.A.	458.03	458.03	0.00	0.00	0.00	0.00
966	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	N.A.	09/2019	1388.34	1388.34	0.00	0.00	0.00	0.00
967	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	N.A.	1169.61	1169.61	0.00	0.00	0.00	0.00
968	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	NHAI	08/2016	N.A.	04/2020	1664.20	1664.20	0.00	75.54	14.37	89.91
969	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	N.A.	08/2018	323.72	323.72	0.00	21.26	15.94	37.20
970	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	NHAI	08/2016	N.A.	N.A.	1583.18	1583.18	0.00	0.00	0.00	0.00
971	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	NHAI	08/2016	N.A.	01/2019	227.49	227.49	0.00	3.50	0.00	0.00
972	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	N.A.	03/2019	1167.42	1167.42	0.00	103.81	14.53	118.34
973	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	N.A.	04/2019	2016.00	2016.00	0.00	0.00	0.00	0.00
974	4-LANING OF HOSKOTE-DOBBASPET	NHAI	05/2014	N.A.	N.A.	720.69	720.69	98.89	0.14	0.00	99.03
975	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA BARWALA - PANCHKULA (PKG - 1)	NHAI	05/2015	N.A.	05/2018	600.85	600.85	99.84	164.69	0.00	0.00
976	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	NHAI	08/2016	N.A.	05/2019	248.97	248.97	0.00	0.00	0.00	0.00
977	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	NHAI	08/2016	N.A.	01/2019	320.30	320.30	0.00	0.00	0.00	0.00
978	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	03/2018	771.18	771.18	261.77	298.19	0.00	0.00
979	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	NHAI	09/2016	N.A.	N.A.	1273.71	1273.71	0.00	0.00	0.00	0.00
980	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	N.A.	08/2019	2510.04	2510.04	0.00	0.00	0.00	0.00
981	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	NHAI	09/2016	N.A.	08/2018	767.03	767.03	0.00	123.13	0.00	123.13

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
982	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	NHAI	09/2016	N.A.	N.A.	1239.82	1239.82	0.00	0.00	0.00	0.00
983	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	N.A.	08/2019	950.69	950.69	0.00	66.58	33.75	100.33
984	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	NHAI	09/2016	N.A.	N.A.	1100.19	1100.19	0.00	0.00	0.00	0.00
985	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	NHAI	09/2016	N.A.	N.A.	1244.10	1244.10	0.00	0.00	0.00	0.00
986	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	NHAI	09/2016	N.A.	05/2019	1004.67	1004.67	0.00	0.00	0.00	0.00
987	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	NHAI	11/2016	N.A.	N.A.	1071.61	1071.61	0.00	0.00	0.00	0.00
988	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	NHAI	11/2016	N.A.	N.A.	1064.88	1064.88	0.00	0.00	0.00	0.00
989	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	N.A.	03/2019	400.25	400.25	0.00	0.00	0.00	0.00
990	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	N.A.	03/2019	446.17	446.17	0.00	0.00	0.00	0.00
991	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	NHAI	11/2016	N.A.	N.A.	290.73	290.73	0.00	0.00	0.00	0.00
992	VIJAYAWADA-GUNDUGOLANU SECTION	NHAI	09/2014	02/2017	02/2017	1684.00	1684.00	54.13	0.00	0.00	54.13
993	REHABILITATION AND UPGRADATION TO FOUR LANNING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	NHAI	10/2016	N.A.	N.A.	1008.96	1008.96	0.00	0.00	0.00	0.00
994	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	NHAI	10/2016	N.A.	N.A.	447.75	447.75	0.00	0.00	0.00	0.00
995	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	NHAI	12/2016	N.A.	N.A.	417.19	417.19	0.00	0.00	0.00	0.00
996	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	NHAI	12/2016	N.A.	N.A.	1031.95	1031.95	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
997	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	NHAI	12/2016	N.A.	N.A.	534.55	534.55	0.00	47.57	1.48	49.05
998	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	N.A.	07/2018	605.84	605.84	546.24	32.01	0.00	578.25
999	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	NHAI	01/2017	N.A.	N.A.	450.68	450.68	0.00	102.97	62.69	165.66
1000	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	N.A.	N.A.	1251.11	1251.11	0.00	0.00	0.00	0.00
1001	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	NHAI	01/2017	N.A.	05/2019	244.90	244.90	0.00	43.29	0.00	43.29
1002	FOUR LANNING OF TULJAPUR-AUSA SECTION	NHAI	02/2017	02/2020	02/2020	904.16	904.16	0.00	6.00	0.00	6.00
1003	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	03/2020	848.45	848.45	0.00	0.00	0.00	0.00
1004	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	03/2020	1373.28	1373.28	0.00	0.00	0.00	0.00
1005	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	03/2020	1184.71	1310.00	0.00	0.00	0.00	0.00
1006	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	NHAI	03/2017	03/2020	03/2020	247.02	157.49	0.00	0.00	0.00	0.00
1007	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	03/2020	744.64	982.00	0.00	0.00	0.00	0.00
1008	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	NHAI	03/2017	03/2020	03/2020	1030.44	1065.51	0.00	0.00	0.00	0.00
1009	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	NHAI	03/2017	03/2020	03/2020	988.34	1043.28	0.00	0.00	0.00	0.00
1010	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	N.A.	1059.73	1071.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1011	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	NHAI	03/2017	03/2020	05/2019	296.19	254.00	0.00	23.87	62.55	86.42
1012	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	NHAI	03/2017	03/2020	03/2020	1098.06	1160.64	0.00	0.00	0.00	0.00
1013	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	03/2020	754.54	756.27	0.00	0.00	0.00	0.00
1014	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	NHAI	03/2017	03/2020	03/2020	1989.00	1989.00	0.00	0.00	0.00	0.00
1015	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	NHAI	03/2017	03/2020	03/2020	639.79	552.90	0.00	12.08	0.00	0.00
1016	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	03/2020	672.89	736.01	0.00	0.00	0.00	0.00
1017	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	03/2020	235.48	227.77	0.00	0.00	0.00	0.00
1018	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	NHAI	03/2017	03/2020	03/2020	648.32	503.10	0.00	15.10	0.00	15.10
1019	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	05/2020	1041.62	1187.10	0.00	0.00	0.00	0.00
1020	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	NHAI	03/2017	03/2020	03/2020	165.50	172.16	0.00	0.00	0.00	0.00
1021	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	NHAI	03/2017	03/2020	03/2020	239.68	235.90	0.00	0.00	0.00	0.00
1022	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2018	1288.07	1420.00	0.00	0.00	0.00	0.00
1023	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	03/2020	2064.99	2447.00	0.00	23.48	0.00	23.48

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1024	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	06/2020	831.58	1177.00	0.00	0.00	10.50	10.50
1025	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	05/2020	993.16	1434.00	0.00	0.00	67.09	67.09
1026	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	04/2020	894.00	894.00	0.00	0.00	0.00	0.00
1027	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	06/2020	2485.93	2485.93	0.00	0.00	0.00	0.00
1028	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	NHAI	06/2017	06/2020	06/2020	1958.88	1958.88	0.00	0.00	0.00	0.00
1029	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	07/2018	641.17	641.17	27.95	121.71	23.96	173.62
1030	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	N.A.	950.64	950.64	0.00	0.00	0.00	0.00
1031	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	N.A.	1176.37	1176.37	0.00	0.00	0.00	0.00
1032	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	N.A.	476.56	476.56	0.00	0.00	0.00	0.00
1033	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	N.A.	648.33	648.33	0.00	0.00	0.00	0.00
1034	JUNAGADH BYPASS	NHAI	10/2017	10/2017	N.A.	232.49	232.49	0.00	0.00	0.00	0.00
1035	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	N.A.	639.97	639.97	0.00	0.00	0.00	0.00
1036	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	N.A.	964.17	964.17	0.00	0.00	0.00	0.00
1037	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	N.A.	1124.11	1124.11	0.00	0.00	0.00	0.00
1038	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	NHAI	09/2017	09/2017	N.A.	374.40	374.40	0.00	0.00	0.00	0.00
1039	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	N.A.	990.61	990.61	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1040	4-LANNING OF OTTANCHATRAM BYPASS	NHAI	09/2017	09/2017	N.A.	244.27	244.27	0.00	0.00	0.00	0.00
1041	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	N.A.	1227.87	1227.87	0.00	0.00	0.00	0.00
1042	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	NHAI	12/2017	N.A.	N.A.	950.27	950.27	0.00	0.00	0.00	0.00
1043	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	NHAI	12/2017	N.A.	N.A.	379.90	379.90	0.00	0.00	0.00	0.00
1044	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	NHAI	12/2017	N.A.	N.A.	1308.73	1308.73	0.00	0.00	0.00	0.00
1045	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	NHAI	12/2017	N.A.	N.A.	1232.21	1232.21	0.00	0.00	0.00	0.00
1046	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	NHAI	12/2017	N.A.	N.A.	404.94	404.94	0.00	0.00	0.00	0.00
1047	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	NHAI	12/2017	N.A.	N.A.	2598.00	2598.00	0.00	0.00	0.00	0.00
1048	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	NHAI	12/2017	N.A.	N.A.	686.65	686.65	0.00	0.00	0.00	0.00
1049	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	NHAI	12/2017	N.A.	N.A.	417.51	417.51	0.00	0.00	0.00	0.00
1050	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	NHAI	12/2017	N.A.	N.A.	1471.75	1471.75	0.00	0.00	0.00	0.00
1051	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	NHAI	12/2017	N.A.	N.A.	328.67	328.67	0.00	0.00	0.00	0.00
1052	SIX LANING OF NARASANNAPETA RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	NHAI	12/2017	N.A.	N.A.	1323.15	1323.15	0.00	0.00	0.00	0.00
1053	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	NHAI	12/2017	N.A.	N.A.	357.00	357.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1054	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	NHAI	12/2017	N.A.	N.A.	207.00	207.00	0.00	0.00	0.00	0.00
1055	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	NHAI	12/2017	N.A.	N.A.	305.00	305.00	0.00	0.00	0.00	0.00
1056	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	NHAI	01/2018	N.A.	N.A.	573.70	573.70	0.00	0.00	0.00	0.00
1057	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	NHAI	01/2018	N.A.	N.A.	895.39	895.39	0.00	0.00	0.00	0.00
1058	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	NHAI	01/2018	N.A.	N.A.	273.46	273.46	0.00	0.00	0.00	0.00
1059	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	NHAI	01/2018	N.A.	N.A.	1155.16	1155.16	0.00	0.00	0.00	0.00
1060	FOUR LANING OF DELINKED STRETCH OF SEONI MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	NHAI	01/2018	N.A.	N.A.	960.24	960.24	0.00	0.00	0.00	0.00
1061	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	NHAI	01/2018	N.A.	N.A.	770.73	770.73	0.00	0.00	0.00	0.00
1062	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	NHAI	01/2018	N.A.	N.A.	607.00	607.00	0.00	0.00	0.00	0.00
1063	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	NHAI	01/2018	N.A.	N.A.	621.00	621.00	0.00	0.00	0.00	0.00
1064	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	NHAI	01/2018	N.A.	N.A.	953.09	953.09	0.00	0.00	0.00	0.00
1065	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	NHAI	01/2018	N.A.	N.A.	668.86	668.86	0.00	0.00	0.00	0.00
1066	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	NHAI	01/2018	N.A.	N.A.	633.68	633.68	0.00	0.00	0.00	0.00
1067	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	NHAI	01/2018	N.A.	N.A.	614.48	614.48	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1068	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	NHAI	01/2018	N.A.	N.A.	564.66	564.66	0.00	0.00	0.00	0.00
1069	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	NHAI	01/2018	N.A.	N.A.	686.65	686.65	0.00	0.00	0.00	0.00
1070	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	NHAI	01/2018	N.A.	N.A.	1522.00	1522.00	0.00	0.00	0.00	0.00
1071	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	NHAI	01/2018	N.A.	N.A.	999.00	999.00	0.00	0.00	0.00	0.00
1072	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	NHAI	01/2018	N.A.	N.A.	503.88	503.88	0.00	0.00	0.00	0.00
1073	VARANASI RING ROAD PKG - I	NHAI	01/2018	N.A.	N.A.	450.77	450.77	0.00	0.00	0.00	0.00
1074	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	NHDP	02/2015	07/2017	07/2017	377.83	377.83	57.42	0.00	0.00	57.42
1075	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337	NHDP	06/2014	11/2016	11/2016	260.39	260.39	87.43	0.00	0.00	87.43
1076	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	NHDP	03/2015	N.A.	04/2018	297.00	297.00	38.33	0.00	0.00	38.33
1077	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	NHDP	03/2015	N.A.	10/2017	168.30	168.30	13.43	0.00	0.00	13.43
1078	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	NHDP	01/2014	N.A.	06/2017	446.77	446.77	87.62	0.00	0.00	87.62
1079	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00	NHDP	12/2013	11/2016	11/2016	220.72	220.72	95.02	0.00	0.00	95.02
1080	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	03/2017	445.89	445.89	0.00	0.00	0.00	0.00
1081	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150	NHDP	01/2014	10/2016	10/2016	397.04	397.04	0.00	0.00	0.00	0.00
1082	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	NHDP	06/2015	N.A.	N.A.	390.51	390.51	43.25	0.00	0.00	43.25
1083	BHOPAL-BIORA (4L) OF NH-12 IN MP	NHDP	11/2011	05/2015	N.A.	704.26	704.26	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1084	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	NHDP	03/2013	02/2016	02/2016	257.80	257.80	59.30	0.00	0.00	59.30
1085	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2017	497.05	497.05	0.00	0.00	0.00	0.00
1086	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	NHDP	06/2015	05/2017	05/2017	532.49	532.49	137.08	0.00	0.00	137.08
1087	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	NHDP	06/2015	03/2018	03/2018	774.57	774.57	0.00	0.00	0.00	0.00
1088	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	NHDP	08/2015	N.A.	N.A.	257.80	257.00	12.38	0.00	0.00	12.38
1089	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43	NHDP	10/2013	03/2017	03/2017	317.76	317.76	15.47	0.00	0.00	15.47
1090	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	NHDP	10/2013	10/2016	10/2016	283.45	283.45	0.00	0.00	0.00	0.00
1091	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	NHDP	06/2015	12/2017	12/2017	641.02	641.02	89.88	0.00	0.00	89.88
1092	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	04/2015	381.86	381.86	252.03	0.00	0.00	252.03
1093	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	NHDP	10/2013	03/2017	03/2017	493.94	493.94	0.00	0.00	0.00	0.00
1094	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	NHDP	11/2011	02/2015	02/2015	670.82	670.82	590.00	0.00	0.00	590.00
1095	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	NHDP	02/2015	05/2017	05/2017	327.32	327.32	142.73	0.00	0.00	142.73
1096	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	NHDP	11/2015	03/2018	03/2018	628.45	628.45	20.74	0.00	0.00	20.74
1097	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	NHDP	12/2015	06/2018	06/2018	927.54	927.54	29.17	0.00	0.00	29.17
1098	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	05/2018	454.89	454.89	22.74	0.00	0.00	22.74

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1099	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	06/2018	437.39	437.39	21.86	0.00	0.00	21.86
1100	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	06/2018	463.49	463.49	9.26	0.00	0.00	9.26
1101	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	NHIDCL	06/2016	01/2019	01/2019	829.00	829.00	59.85	0.00	0.00	59.85
1102	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	NHIDCL	03/2015	11/2018	11/2018	168.39	168.39	16.84	0.00	0.00	16.84
1103	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	11/2018	588.95	588.95	80.00	0.00	0.00	80.00
1104	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	NHIDCL	03/2015	05/2018	05/2018	194.11	194.11	30.54	0.00	0.00	30.54
1105	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	NHIDCL	10/2015	01/2019	01/2019	179.82	179.82	8.99	0.00	0.00	8.99
1106	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	NHIDCL	07/2015	10/2018	10/2018	197.16	197.16	38.50	0.00	0.00	38.50
1107	2 LANING FROM LONGDING TO KANUBARI OF NH 52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	06/2018	394.00	394.00	0.00	0.00	0.00	0.00
1108	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	NHIDCL	10/2014	03/2018	03/2018	369.00	369.00	36.90	0.00	0.00	36.90
1109	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	NHIDCL	05/2014	04/2017	04/2017	497.89	497.89	70.47	0.00	0.00	70.47
1110	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	NHIDCL	03/2015	05/2018	05/2018	235.08	235.08	47.81	0.00	0.00	47.81
1111	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	NHIDCL	12/2015	12/2018	12/2018	225.02	159.20	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1112	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	NHIDCL	12/2015	06/2018	06/2018	223.30	223.30	0.00	0.00	0.00	0.00
1113	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	NHIDCL	01/1991	N.A.	N.A.	520.01	520.01	0.00	0.00	0.00	0.00
1114	4 LANING FROM RANGAGARA TO KALIABHORTINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	NHIDCL	12/2015	12/2018	12/2018	289.99	289.99	0.00	0.00	0.00	0.00
1115	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	NHIDCL	01/2016	01/2016	01/2016	294.17	294.17	0.00	0.00	0.00	0.00
1116	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	01/2016	252.00	252.00	0.00	0.00	0.00	0.00
1117	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450	NHIDCL	01/2016	11/2016	11/2016	183.65	183.65	0.00	0.00	0.00	0.00
1118	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	NHIDCL	01/2016	06/2016	06/2016	334.22	334.22	0.00	0.00	0.00	0.00
1119	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	NHIDCL	04/2016	N.A.	N.A.	245.79	245.79	0.00	0.00	0.00	0.00
1120	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	NHIDCL	04/2016	10/2016	10/2016	198.00	198.00	0.00	0.00	0.00	0.00
1121	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	NHIDCL	11/2015	N.A.	N.A.	434.06	434.06	0.00	0.00	0.00	0.00
1122	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	155.00	0.00	0.00	0.00	0.00
1123	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	N.A.	1253.10	1253.10	0.00	0.00	0.00	0.00
1124	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	N.A.	284.09	284.09	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1125	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	NHIDCL	02/2017	04/2017	N.A.	195.23	195.23	0.00	0.00	0.00	0.00
1126	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	NHIDCL	02/2017	04/2017	N.A.	203.36	203.36	0.00	0.00	0.00	0.00
1127	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	NHIDCL	01/2017	04/2017	N.A.	194.66	194.66	0.00	0.00	0.00	0.00
1128	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	N.A.	168.32	168.32	0.00	0.00	0.00	0.00
1129	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	N.A.	180.57	180.57	0.00	0.00	0.00	0.00
1130	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	N.A.	216.71	216.71	0.00	0.00	0.00	0.00
1131	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	N.A.	167.28	167.28	0.00	0.00	0.00	0.00
1132	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	373.07	0.00	0.00	0.00	0.00
1133	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	396.52	0.00	0.00	0.00	0.00
1134	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	429.52	0.00	0.00	0.00	0.00
1135	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	NHIDCL	02/2017	04/2017	N.A.	507.68	507.68	0.00	0.00	0.00	0.00
1136	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	NHIDCL	01/2017	04/2017	N.A.	198.22	198.22	0.00	0.00	0.00	0.00
1137	RHENOK-RORATHANG-PAKYONG ON NH 717A	NHIDCL	04/2017	10/2017	10/2017	388.00	447.37	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1138	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	NHIDCL	03/2018	05/2018	05/2018	274.31	274.31	0.00	0.00	0.00	0.00
1139	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	NHIDCL	03/2018	06/2018	06/2018	403.36	403.36	0.00	0.00	0.00	0.00
1140	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	NHIDCL	03/2018	05/2018	05/2018	417.24	417.24	0.00	0.00	0.00	0.00
1141	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	NHIDCL	03/2015	10/2018	10/2018	262.97	262.97	0.00	0.00	0.00	0.00
1142	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	NHIDCL	03/2017	12/2017	12/2017	409.85	409.85	0.00	0.00	0.00	0.00
1143	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	NHIDCL	03/2015	04/2017	04/2017	277.17	277.17	0.00	0.00	0.00	0.00
1144	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	NHIDCL	02/2018	10/2018	10/2018	391.00	391.00	0.00	0.00	0.00	0.00
1145	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	NHIDCL	03/2018	10/2018	10/2018	234.27	234.27	0.00	0.00	0.00	0.00
1146	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC	PWD	01/2014	07/2014	N.A.	361.30	207.40	44.08	0.00	0.00	44.08
1147	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION)	PWD	02/2014	07/2014	07/2016	258.99	258.99	16.54	0.00	0.00	16.54
1148	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	251.55	7.74	0.00	0.00	7.74
1149	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	PWD	03/2015	N.A.	N.A.	175.03	175.00	0.00	0.00	0.00	0.00
1150	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	PWD	02/2015	N.A.	N.A.	266.00	266.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1151	FOUR LANE OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	PWD	07/2015	12/2015	12/2016	333.21	333.21	0.00	0.00	0.00	0.00
1152	REHABILITATION AND UP GRADATION OF NH-4 FROM KM.81.500-KM 130.00 DHAMTARI-KANKER SECTION.	PWD	10/2014	03/2015	03/2015	213.47	213.47	0.00	0.00	0.00	0.00
1153	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV	PWD	10/2014	03/2015	03/2015	298.34	298.34	0.00	0.00	0.00	0.00
1154	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I	PWD	11/2014	03/2015	N.A.	262.54	262.54	0.00	0.00	0.00	0.00
1155	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	PWD	01/2014	11/2014	11/2016	195.45	195.45	0.00	0.00	0.00	0.00
1156	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI-KAWARDHA SECTION.	PWD	12/2015	N.A.	N.A.	291.05	291.05	0.00	0.00	0.00	0.00
1157	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-	PWD	12/2010	12/2012	N.A.	169.26	169.26	0.00	0.00	0.00	0.00
1158	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	PWD	02/2014	11/2014	11/2016	170.21	170.21	5.65	0.00	0.00	5.65
1159	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA-SIMGA SECTION.	PWD	12/2014	N.A.	N.A.	394.20	394.20	0.00	0.00	0.00	0.00
1160	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	PWD	11/2015	12/2015	N.A.	485.44	485.44	0.00	0.00	0.00	0.00
1161	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	PWD	03/2015	N.A.	N.A.	435.90	435.90	31.02	0.00	0.00	31.02
1162	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	PWD	01/2015	N.A.	N.A.	279.68	279.68	25.28	0.00	0.00	25.28
1163	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	PWD	11/2014	N.A.	N.A.	463.65	463.65	280.16	0.00	0.00	280.16

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1164	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	PWD	11/2014	N.A.	N.A.	573.96	605.00	209.74	0.00	0.00	209.74
1165	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	224.83	0.00	0.00	0.00	0.00
1166	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU	PWD	03/2015	09/2015	08/2017	309.01	309.01	0.00	0.00	0.00	0.00
1167	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	271.45	0.00	0.00	0.00	0.00
1168	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	12/2016	333.21	333.21	0.00	0.00	0.00	0.00
1169	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	PWD	02/2014	06/2014	06/2016	417.61	417.61	0.00	0.00	0.00	0.00
1170	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	N.A.	624.41	624.41	0.00	0.00	0.00	0.00
1171	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	N.A.	156.63	276.00	132.21	0.00	0.00	132.21
1172	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	PWD	11/2010	03/2011	N.A.	305.49	305.49	0.00	0.00	0.00	0.00
1173	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	N.A.	193.69	193.69	0.00	0.00	0.00	0.00
1174	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	PWD	03/2012	05/2012	N.A.	207.03	207.03	0.00	0.00	0.00	0.00
1175	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	PWD	04/2013	08/2013	N.A.	151.59	151.59	0.00	0.00	0.00	0.00
1176	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	PWD	04/2013	08/2013	N.A.	166.27	166.27	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1177	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	PWD	01/2013	02/2013	N.A.	182.28	182.00	24.36	0.00	0.00	24.36
1178	WIDENING OF 2(TWO) LANE OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROAD	PWD	12/2010	02/2011	N.A.	1296.00	1296.00	0.00	0.00	0.00	0.00
1179	REHABILITATION AND UPGRADATION OF NH - 365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S)	PWD	12/2013	03/2016	N.A.	177.18	177.18	40.51	0.00	0.00	40.51
1180	REHABILITATION AND UPGRADATION OF NH - 365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTION)	PWD	12/2013	03/2016	N.A.	158.65	158.65	103.50	0.00	0.00	103.50
1181	REHABILITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTON) TO T	PWD	12/2013	03/2016	N.A.	244.08	244.08	38.32	0.00	0.00	38.32
1182	REHABILITATION AND UPGRADATION OF NH - 765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	PWD	01/2014	03/2016	N.A.	340.00	340.00	0.00	0.00	0.00	0.00
1183	REHABILITATION AND UPGRADATION OF NH - 565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT)	PWD	01/2014	03/2016	N.A.	270.00	270.00	19.84	0.00	0.00	19.84
1184	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	PWD	10/2014	12/2016	12/2016	244.30	156.09	0.00	0.00	0.00	0.00
1185	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	PWD	10/2014	02/2017	02/2017	295.47	313.27	0.00	0.00	0.00	0.00
1186	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	PWD	03/2015	01/2017	01/2017	153.21	153.21	0.00	0.00	0.00	0.00
1187	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	N.A.	218.31	339.82	208.28	0.00	0.00	208.28
1188	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROADS IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	PWD	08/2014	07/2016	07/2016	187.79	187.79	57.60	0.00	0.00	57.60
1189	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	09/2017	255.75	348.43	0.02	0.00	0.00	0.02

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1190	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	PWD	01/2014	11/2017	N.A.	267.16	352.05	0.02	0.00	0.00	0.02
1191	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION)	PWD	02/2015	02/2017	02/2017	241.61	241.61	7.71	0.00	0.00	7.71
1192	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR NELLORE SECTION) IN	PWD	11/2014	02/2017	02/2017	297.78	330.00	0.00	0.00	0.00	0.00
1193	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	PWD	02/2015	N.A.	N.A.	483.38	483.38	65.76	0.00	0.00	65.76
1194	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	PWD	02/2015	N.A.	N.A.	616.36	616.36	68.58	0.00	0.00	68.58
1195	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	PWD	11/2010	03/2017	03/2017	305.49	305.49	0.00	0.00	0.00	0.00
1196	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	PWD	02/2015	N.A.	N.A.	486.74	486.74	189.39	0.00	0.00	189.39
1197	SATANA-BELA SECTION OF NH-75(4L) IN MP	PWD	01/2012	08/2015	09/2016	320.48	320.48	189.49	0.00	0.00	189.49
1198	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	PWD	03/2015	N.A.	N.A.	312.79	312.79	17.57	0.00	0.00	17.57
1199	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K	PWD	07/2014	N.A.	N.A.	319.80	319.80	102.55	0.00	0.00	102.55
1200	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	PWD	12/2015	N.A.	N.A.	766.36	766.36	99.86	0.00	0.00	99.86
1201	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	PWD	01/2011	N.A.	N.A.	264.16	264.16	0.00	0.00	0.00	0.00
1202	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	PWD	11/2015	N.A.	N.A.	847.02	847.02	299.81	0.00	0.00	299.81

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1203	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	PWD	11/2010	05/2017	05/2017	268.08	268.08	0.00	0.00	0.00	0.00
1204	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	PWD	11/2015	N.A.	N.A.	889.24	889.24	389.64	0.00	0.00	389.64
1205	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	PWD	11/2010	02/2011	02/2011	470.20	470.20	0.00	0.00	0.00	0.00
1206	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	08/2016	871.15	871.15	332.25	0.00	0.00	332.25
1207	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	PWD	12/2015	N.A.	N.A.	578.38	578.38	128.53	0.00	0.00	128.53
1208	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	PWD	03/2015	N.A.	N.A.	789.83	789.83	109.77	0.00	0.00	109.77
1209	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	PWD	10/2015	11/2015	11/2015	333.21	333.21	0.00	0.00	0.00	0.00
1210	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	PWD	05/2011	02/2018	02/2018	176.22	176.22	0.00	0.00	0.00	0.00
1211	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	PWD	11/2014	02/2018	02/2018	218.31	218.31	0.00	0.00	0.00	0.00
1212	IMPROVEMENT FROM KM 0/0 TO 68/0	PWD	12/2013	10/2016	10/2016	319.80	319.80	0.00	0.00	0.00	0.00
1213	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	10/2010	195.04	195.04	130.82	0.00	0.00	130.82
1214	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	PWD	02/2015	04/2015	05/2016	224.83	224.83	0.00	0.00	0.00	0.00
1215	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	PWD	07/2014	01/2017	01/2017	342.05	342.05	0.00	0.00	0.00	0.00
1216	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	PWD	12/2009	09/2010	09/2010	165.00	165.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1217	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	PWD	12/2009	09/2010	09/2010	104.00	201.00	0.00	0.00	0.00	0.00
1218	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	PWD	12/2010	02/2011	02/2011	1494.48	1494.48	0.00	0.00	0.00	0.00
1219	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	PWD	09/2012	10/2013	10/2013	511.00	511.00	0.00	0.00	0.00	0.00
1220	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	PWD	09/2012	10/2013	10/2013	511.00	511.00	0.00	0.00	0.00	0.00
1221	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	PWD	03/2015	08/2017	08/2017	511.83	511.83	40.87	0.00	0.00	40.87
1222	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	PWD	12/2011	11/2017	11/2017	159.39	159.39	0.00	0.00	0.00	0.00
1223	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	PWD	06/2015	N.A.	N.A.	892.17	892.17	26.92	0.00	0.00	26.92
1224	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	PWD	06/2015	N.A.	N.A.	899.21	899.21	25.08	0.00	0.00	25.08
1225	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	191.08	0.00	0.00	0.00	0.00
1226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40	PWD	01/1991	N.A.	N.A.	154.62	154.62	0.00	0.00	0.00	0.00
1227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	PWD	01/1991	N.A.	N.A.	319.68	319.68	0.00	0.00	0.00	0.00
1228	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	PWD	01/2014	11/2014	11/2014	292.98	292.98	95.60	0.00	0.00	95.60
1229	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	PWD	03/2016	N.A.	N.A.	1142.62	1142.62	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1230	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	PWD	03/2016	N.A.	N.A.	1101.58	1101.58	0.00	0.00	0.00	0.00
	SHIPPING AND PORTS										
1231	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	KPL	10/2013	06/2017	N.A.	198.94	255.00	212.27	36.17	6.58	255.02
1232	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	KPL	02/2015	12/2017	N.A.	244.50	275.98	189.00	74.42	12.56	275.98
1233	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED	KPL	12/2014	04/2017	N.A.	274.85	321.94	251.64	60.30	10.00	321.94
1234	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600.00	257.90	1.45	0.00	0.00	1.45
1235	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	411.12	2.79	0.00	413.91
1236	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	N.A.	150.00	600.00	139.80	0.00	0.00	139.80
1237	SETHUSAMUDRAM SHIP CHANNEL PROJECT	PORT TRUST	06/2005	10/2008	N.A.	2427.40	2427.40	831.21	0.00	0.00	831.21
	STEEL										
1238	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSCL	12/2007	12/2016	N.A.	202.61	227.00	199.95	0.00	0.00	199.95
1239	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	N.A.	175.49	206.71	141.28	0.00	0.00	141.28
1240	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	N.A.	768.88	1113.34	1085.64	0.00	0.00	1085.64
1241	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	HSCL	07/2011	12/2015	N.A.	324.87	324.87	262.93	0.00	0.00	262.93
1242	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	12/2018	151.33	151.33	7.15	0.00	0.00	7.15
1243	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	HSCL	07/2014	01/1999	N.A.	232.00	232.00	0.00	0.00	0.00	0.00
1244	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	HSCL	01/2013	N.A.	N.A.	175.00	175.00	1.83	0.00	0.00	1.83

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1245	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HSCL	05/2015	03/2017	08/2018	189.00	189.00	0.00	0.00	0.00	0.00
1246	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956.00	956.00	651.21	0.00	0.00	651.21
1247	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	HSCL	12/2007	06/2016	03/2018	253.92	253.92	193.97	0.00	0.00	193.97
1248	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	HSCL	12/2007	03/2018	03/2018	200.00	200.00	131.15	0.00	0.00	131.15
1249	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSCL	02/2014	12/2016	12/2018	787.29	787.29	285.30	0.00	0.00	285.30
1250	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	HSCL	04/2013	04/2018	04/2018	170.00	170.00	88.91	0.00	0.00	88.91
1251	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	N.A.	149.73	175.94	178.65	0.00	0.00	178.65
1252	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	HSCL	08/2012	03/2016	N.A.	185.37	185.37	178.30	0.00	0.00	178.30
1253	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	10/2018	15525.00	15525.00	12066.99	1231.65	577.60	13876.24
1254	2 MTPA PELLET PLANT AT NAGARNAR	NMDC	11/2015	06/2020	06/2020	818.00	818.00	25.32	2.81	0.68	28.81
1255	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343.00	488.40	167.19	69.13	0.79	237.11
1256	FORGED WHEEL PLANT	RINL	04/2014	09/2018	01/2019	1682.85	1682.85	40.73	137.37	98.00	276.10
1257	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2018	2858.00	2500.00	380.35	406.10	41.00	827.45
1258	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	10/2018	320.66	320.66	2.22	34.82	0.76	37.80
1259	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	RINL	07/2015	07/2018	09/2018	465.85	465.85	11.40	108.60	4.00	124.00
1260	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	06/2018	17265.00	17265.00	17366.70	1193.74	-10.48	18549.96
1261	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	SAIL	04/2014	04/2015	N.A.	188.93	188.93	109.16	10.78	0.00	119.94
1262	ALTERNATE GAS NETWORK AT BSL	SAIL	03/2015	03/2018	03/2018	255.19	255.19	133.83	34.19	9.19	177.21
1263	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.30	3127.30	576.35	1441.83	70.86	2089.04
1264	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2018	1034.01	1034.01	132.10	81.02	3.58	216.70
1265	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2018	1154.18	1154.18	259.62	355.34	44.56	659.52

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1266	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	SAIL	02/2014	09/2017	N.A.	4749.00	4749.00	59.66	23.84	0.18	83.68
1267	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2019	262.87	262.87	11.58	26.93	0.44	38.95
	TELECOMMUNICATIONS										
1268	MAHARASHTRA NODAL (LOT 1)	BSNL	08/2017	04/2018	04/2018	159.30	159.30	0.00	0.00	0.00	0.00
1269	MAHARASHTRA CORE (LOT1)	BSNL	08/2017	04/2018	04/2018	167.68	167.68	0.00	0.00	0.00	0.00
1270	MAHARASHTRA ACCESS (LOT 1)	BSNL	08/2017	05/2018	05/2018	212.70	212.70	0.00	0.00	0.00	0.00
1271	MADHYA PRADESH ACCESS (LOT1)	BSNL	08/2017	05/2018	05/2018	215.30	215.30	0.00	0.00	0.00	0.00
1272	GUJARAT ACCESS (LOT 1)	BSNL	09/2017	05/2018	05/2018	171.54	171.54	0.00	0.00	0.00	0.00
1273	UP (EAST) ACCESS LOT1	BSNL	11/2017	08/2018	08/2018	169.45	169.45	0.00	0.00	0.00	0.00
1274	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	04/2020	13334.00	24664.00	5160.00	2482.00	0.00	7642.00
1275	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	ITI	09/2014	09/2014	N.A.	2111.17	2011.17	253.90	0.00	0.00	253.90
1276	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	MTNL	06/2016	06/2017	03/2018	418.26	418.26	0.00	172.30	0.00	172.30
	URBAN DEVELOPMENT										
1277	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	26405.14	499.85	1891.61	0.00	2391.46
1278	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	N.A.	14600.00	19058.00	12472.32	2312.27	0.00	14784.59
1279	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	CMRL	06/2016	03/2018	03/2018	3770.00	3770.00	0.00	0.00	0.00	0.00
1280	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	N.A.	04/2019	197.33	197.33	2.76	1.40	0.75	4.91
1281	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	08/2018	388.00	388.00	208.67	108.13	20.23	337.03
1282	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD	12/2015	N.A.	10/2019	209.00	209.00	0.00	19.54	6.46	26.00
1283	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	05/2018	332.72	321.00	212.32	85.02	7.84	305.18
1284	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	06/2018	156.57	156.57	98.07	28.28	6.85	133.20

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1285	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2018	270.83	270.83	107.02	27.16	8.49	142.67
1286	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2018	171.86	171.86	35.36	4.55	0.14	40.05
1287	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	04/2018	241.33	349.33	193.00	103.50	11.00	307.50
1288	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2020	1219.21	1592.00	10.53	150.00	50.00	210.53
1289	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	06/2018	205.00	170.62	127.15	22.07	0.00	149.22
1290	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2018	165.23	165.23	25.91	0.00	0.00	25.91
1291	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	CPWD	06/2014	03/2017	N.A.	157.84	157.84	72.96	43.63	3.97	120.56
1292	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	05/2018	884.30	884.30	428.36	134.14	20.34	582.84
1293	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	04/2018	350.02	479.87	278.59	165.14	8.62	452.35
1294	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2018	216.69	216.69	52.00	0.00	0.00	52.00
1295	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER	CPWD	07/2015	11/2015	05/2018	154.00	154.00	49.80	32.38	8.58	90.76
1296	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY	CPWD	05/2016	11/2018	05/2018	164.00	164.00	19.31	59.94	6.21	85.46
1297	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	03/2020	209.84	209.84	0.12	1.43	0.10	1.65
1298	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	498.99	0.00	0.20	0.00	0.00
1299	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	0.00	0.00	0.00	0.00

SN	PROJECT	AGENCY	DATE OF APPROVAL (Month/Year)	ORIGINAL DATE COMMISSIONING (Month/Year)	ANTICIPATED DATE COMMISSIONING (Month/Year)	COST ORIGINAL (Rs.in crore)	COST ANTICIPATED (Rs.in crore)	CUMULATIVE EXPENDITURE PFYR (Rs.in crore)	CUMULATIVE EXPENDITURE CURRENT FYR (Rs.in crore)	EXPENDITURE IN MARCH 2018 (Rs.in crore)	CUMULATIVE EXPENDITURE UP TO MARCH 2018 (Rs.in crore)
1300	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	06/2019	294.00	294.00	0.00	67.24	8.67	75.91
1301	RESIDENTIAL QUATERS FOR HAL,BANGLORE	CPWD	12/2016	02/2020	02/2020	246.31	246.31	0.00	1.66	0.00	1.66
1302	NSG AT KOLKATA	CPWD	10/2014	04/2018	05/2019	162.88	162.88	7.50	39.79	8.80	56.09
1303	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	CPWD	11/2017	05/2020	05/2020	238.56	238.56	0.00	0.00	0.00	0.00
1304	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	CPWD	12/2017	06/2019	06/2019	188.00	188.00	0.00	0.00	0.00	0.00
1305	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	CPWD	01/2018	03/2019	03/2019	206.58	206.58	0.00	0.00	0.00	0.00
1306	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	CPWD	11/2017	N.A.	N.A.	348.77	348.77	0.00	0.00	0.00	0.00
1307	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	CPWD	10/2016	N.A.	N.A.	422.00	422.00	0.00	0.00	0.00	0.00
1308	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	03/2018	38585.00	38585.00	21825.61	12444.71	0.00	34270.32
1309	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	JNNURM	08/2007	N.A.	N.A.	246.90	246.90	0.00	0.00	0.00	0.00
1310	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	5181.79	0.00	0.00	0.00	0.00
1311	LUCKNOW METRO RAIL CORPORATION LTD	LMRCL	01/2016	03/2019	03/2019	6928.00	6928.00	1061.41	1475.36	0.00	2536.77
1312	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	N.A.	23136.00	23136.00	0.00	0.00	0.00	0.00
1313	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	11/2019	4264.00	4118.00	2465.00	602.00	178.00	3245.00
1314	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	NBCC	07/2016	N.A.	N.A.	2694.00	2694.00	0.00	0.00	0.00	0.00
1315	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680.00	8680.00	1578.88	1510.70	391.05	3480.63
TOTAL						1623254.71	1841400.35	585652.68	132285.67	15524.60	663626.77
