

**343rd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
May 2014**



NHPC - PARBATI H.E.P. STAGE -III



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-70
Sector wise Graph	71-81
ANNEXURE	82-82
Central Sector Projects	83-83
List of Projects Having Expenditure More than cost	84-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-106
List of On schedule Projects Original Schedule	107-113
List of Delayed Projects w.r.t Original Schedule	114-127
List of Projects Having Time and cost overrun w.r.t original	128-132
List of Projects Having cost overrun w.r.t original	133-144
List of Projects without Milestones	145-166
List of On schedule Projects w.r.t. Latest Schedule	167-174
List of Projects Ahead of Schedule w.r.t Latest Schedule	175-175
List of Delayed Projects w.r.t Latest Schedule	176-189

कार्यकारी सारांश

1. मई, 2014 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 735 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। मई, 2014 के दौरान 2 परियोजनाओं (प्रत्येक एक परियोजना विद्युत तथा कोयले में) के पूरा होने की सूचना नहीं दी गई है।

2. संदर्भाधीन माह के दौरान, 735 परियोजनाओं में से, 282 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 83 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 83 परियोजनाओं में से, 24 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	291	37	4	1
2.	सड़क परिवहन एवं राजमार्ग	138	89	56	12
3.	विद्युत	102	52	6	2
4.	पेट्रोलियम	80	47	11	6
5.	कोयला	55	30	2	0
6.	इस्पात	20	13	3	2
7.	पोत परिवहन एवं पत्तन	19	3	0	0
8.	दूरसंचार	11	4	0	0
9.	नागर विमानन	8	2	0	0
10.	शहरी विकास	5	1	0	0
11.	परमाणु ऊर्जा	4	4	1	1
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		735	282	83	24

3. 735 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ₹ 9,57,390.48 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 11,40,912.47 करोड़ रुपए होने की संभावना है जो ₹ 1,83,521.99 करोड़ (मूल लागत का 19.20%) की समग्र लागत वृद्धि को दर्शाता है। मई, 2014 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,70,976.01 करोड़ है जो परियोजनाओं की अनुमानित लागत का 50.00% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.05.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		लागत-वृद्धि (% में)
				मूल	अनुमानित	
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी-बलूरघाट से नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.18	1810.82
3	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1423.98	1172.55
4	अकोला-खण्डवा जीसी अकोला-अकोट	रेलवे	04/2008	184.26	2000.00	985.42
5	बंगलुरु सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	रेलवे	02/1999	138.00	1382.78	902.01

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (31.05.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	कुसमुण्डा एक्सपे. (ओसीपी) (एसईसीएल) (15-50) एमटीवाई	कोयला	06/2008	1188.31	7612.33	6424.02
3	जिरीबाम से इंफाल (टीयूपीयूआई) (एनईएफआर)	शहरी विकास	04/2003	727.56	5996.00	5268.44
4	बंगलौर मेट्रो रेल परियोजना	विद्युत	05/2006	6395.00	11609.00	5214.00
5	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 735 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 118 समय पर तथा 282 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 262 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 21 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 309 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 282 विलंबित परियोजनाओं में से, 55 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 73 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 85 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 69 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.05.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	09/2014	246
2	फ्रैट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	11/2002	12/2017	181
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141
5	अमरावती, नारखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	141

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, उपस्कर स्थापित करना, भूखनन की स्थिति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी

परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.05.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		संचयी व्यय (रु. करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	6.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी-बलूरघाट से नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रैट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	0.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	0.97	4.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.05.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	विरमगम-बिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	155.66	एन.आर.	200.42
2	शापुर-सरादिया और सोमनाथ-कोडिनार के लिए राजकोटवेरावल, वंशजालिया से जतलसर नए एमएम के साथ (जीसी)	रेलवे	04/1994	320.66	एन.आर.	462.18
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	688.63
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8805.00
5	दल्ली-रजहारा रौघट (दल्ली-रजहारा जगदलपुर के भाग), एनएल, आरवीएनएल	रेलवे	04/1995	304.00	एन.आर.	138.39

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.05.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

i) परमाणु ऊर्जा क्षेत्र में, सभी 4 परियोजनाएं विलंबित हैं । परियोजना 'कुडनकुलम एटोमिक पावर प्लांट, (एनपीसीआईएल)' (मेगा परियोजना) के संबंध में उपस्करों की आपूर्ति और स्थापन में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

ii) कोयला क्षेत्र में 55 परियोजनाओं में से 30 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'अशोक एक्सपें. ओसीपी-सीसीएल (10 एमटीवाई), सीसीएल' परियोजना के संबंध में वन संबंधी स्वीकृति में विलंब होने के कारण 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; और परियोजना 'कर्मा

ओसीपी (1.0 एमटीवाई), सीसीएल' के संबंध में 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

iii) इस्पात क्षेत्र में 20 परियोजनाओं में से 13 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 2-5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 बड़ी परियोजनाएं हैं । परियोजना 'बोकारो स्टील प्लांट के विस्तार, सेल' के संबंध में विद्युत के स्थिरीकरण तथा स्वचालन प्रणाली में विलंब होने के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'दुर्गापुर इस्पात संयंत्र का विस्तार, सेल' में कार्यक्षेत्र में परिवर्तन होने के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'आरएमएचपी, आरआईएनएल में लौह अयस्क भंडारण के संवर्धन के संबंध में निविदा को अंतिम रूप देने में देरी होने के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

iV) रेलवे क्षेत्र में 291 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 3-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 1 बड़ी परियोजना है । परियोजना 'गुना-इटावा वाया शिवपुरी- ग्वालियर-भिन्ड, एनएल, एनसीआर' तथा 'रांची-लोहरदगा (जीसी), एसईआर' में क्रमशः खंभों में दरार का उभरना तथा कानून और व्यवस्था की समस्याओं के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'आरवीएनएल दक्षिणेश्वर, (एमटीपी), तथा बारानगर से बराकपुर तक मेट्रो रेलवे के निर्माण के लिए नए काम के संबंध में वन संबंधी अनुमति में विलंब के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'तमलुक-बसुल्या-सुताहाट दोहरीकरण, एसईआर' के संबंध में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

v) विद्युत क्षेत्र में, 102 परियोजनाओं में से 52 परियोजनाएं विलंबित हैं । माह के दौरान 6 परियोजनाओं के संबंध में 9 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 परियोजनाएं मेगा परियोजनाएं हैं । परियोजनाएं 'उत्तर क्षेत्रीय ट्रांसमिशन सुदृढीकरण योजना,

पीजीसीआईएल' और 'ट्रांशमिशन सिस्टम फॉर कनेक्टिविटी ऑफ एस्सार पावर गुजरात लि., पीजीसीआईएल' में आरओडब्ल्यू समस्याओं के कारण से प्रत्येक में क्रमशः 1 तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'ट्रांशमिशन सिस्टम फॉर कनेक्टिविटी ऑफ एमबी पावर लि., पीजीसीआईएल' में वन संबंधी अनुमति तथा आरओडब्ल्यू समस्याओं के कारण से प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'सुबानसिरी लोअर, एच.ई.पी, एनएचपीसी' के संबंध में विभिन्न दबाव समूहों द्वारा आंदोलन के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'तीस्ता लो डैम एचईपी, चरण IV एनएचपीसी' के संबंध में निविदा की समाप्ति के कारण में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पश्चिम रेलवे और उत्तर रेलवे (लाईन बेस और रिएक्टर प्रोविजन) के सामान्य सुदृढीकरण प्रणाली, पीजीसीआईएल' के संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) पेट्रोलियम क्षेत्र में, 80 परियोजनाओं में से 47 परियोजनाएं विलंबित हैं । माह के दौरान 11 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 6 परियोजना मेगा परियोजना है । परियोजना '2000एचपी ड्रिलिंग रिग की 2 नगों की खरीद, ओआईएल' के संबंध में अदालती मामलों के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'विजयपुर और पाटा में पेट्रोकेमिकल कॉम्प्लेक्स-II, गेल' के संबंध में निर्माण गतिविधियों में धीमी प्रगति के कारण क्रमशः 2 और 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'गैस टरबाइन जेनरेशन सेट, ओआईएल' में उपस्करों के वितरण में देरी होने के कारण से 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'डेवलपमेंट ऑफ सी-सीरिज फील्ड्स, ओएनजीसी' के संबंध में प्लान किए गए कुओं की ड्रिलिंग में विलंब होने के कारण 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है परियोजना 'डेवलपमेंट ऑफ बी-193 क्लस्टर फील्ड्स, ओएनजीसी' तथा '12 ऑफशोर सप्लाई वेसेल्स (ओएसवी) का निर्माण, ओएनजीसी' के कार्यक्षेत्र में परिवर्तन तथा स्थल पर क्रमशः अपर्याप्त सहायक/उप ठेकेदार के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पारादीप में मार्केटिंग टर्मिनल, आईओसीएल' तथा 'विशाख में सामरिक कच्चे तेल भंडारण परियोजना, आईएसपीआरएल' में 3 तथा 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है परियोजना 'रिग सागर सम्राट को मोबाइल ऑफशोर उत्पादन इकाई (एमओपीएस) में बदलना, ओएनजीसी' तथा 'पाइपलाइन प्रतिस्थापन परियोजना-3, ओएनजीसी' में 9 तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) सड़क क्षेत्र में 138 परियोजनाओं में से 89 परियोजनाएं विलंबित हैं । माह के दौरान 56 परियोजनाओं के संबंध में 1-40 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 12 मेगा परियोजनाएं हैं । 56 परियोजनाओं में से 6 परियोजनाओं में से प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है और 4 परियोजनाओं में से प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 10 परियोजनाओं में से प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 3 परियोजनाओं में से प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 10 परियोजनाओं में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 3 परियोजनाओं में से प्रत्येक में 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 2 परियोजनाओं में से प्रत्येक में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 2 परियोजनाओं में क्रमशः 8 और 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 9 परियोजनाओं में से प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'भोपाल-सांची, एनएचआई' तथा कृष्णानगर-बरहामपुर, एनएचआई' में क्रमशः 14 और 17 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'इन्दौर-देवास (एनएच-3), एनएचआई' और 'बरही-हजारीबाग का 4 लेनिंग, एनएचआई' में क्रमशः 18 तथा 19 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'निरोली-रॉक्सी-राजमुंडा, एनएचआई' तथा 'बेलगम-खानपुर सेक्शन का 4 लेनिंग' तथा 'खानपुर-कर्नाटक/गोवा-बॉर्डर का 2 लेनिंग, एनएचआई' में क्रमशः 24 तथा 29 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पानीपत-जलंधर का 6 लेन, (96 कि.मी. से 387.1 कि.मी.), एनएचआई' में 40 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

10. दिनांक 31.05.2014 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for May 2014 contains information on the status of the 735 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During May 2014, 2 projects (1 project each is in Coal and Power Sector) have reported completion.

2. During the reference month, out of 735 projects, 282 projects are delayed with respect to original schedule and 83 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 83 projects, 24 are Mega Projects costing ₹ 1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	291	37	4	1
2.	ROAD TRANSPORT AND HIGHWAYS	138	89	56	12
3.	POWER	102	52	6	2
4.	PETROLEUM	80	47	11	6
5.	COAL	55	30	2	0
6.	STEEL	20	13	3	2
7.	SHIPPING AND PORTS	19	3	0	0
8.	TELECOMMUNICATIONS	11	4	0	0
9.	CIVIL AVIATION	8	2	0	0
10.	URBAN DEVELOPMENT	5	1	0	0
11.	ATOMIC ENERGY	4	4	1	1
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		735	282	83	24

3. Total original cost of implementation of the 735 projects was about ₹ 9,57,390.48 crore and their anticipated completion cost is likely to be ₹ 11,40,912.47 crore, which reflects an overall cost overruns of ₹ 1,83,521.99 crore (19.20 % of original cost). The expenditure incurred on these projects till May 2014 is ₹ 5,70,976.01 crore, which is 50.00 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as follows:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-05 -2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		COST OVERRUNS (in %)
				ORIGINAL	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	RAILWAYS	03/1981	37.68	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	RAILWAYS	04/1983	36.80	703.18	1810.82
3	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	111.90	1423.98	1172.55
4	AKOLA-KHANDWA GC AKOLA-AKOT	RAILWAYS	04/2008	184.26	2000.00	985.42
5	BANGLORE SATYAMANGALAM (NL)(SWR)	RAILWAYS	02/1999	138.00	1382.78	902.01

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-05-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	2500.00	20000.00	17500.00
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	COAL	06/2008	1188.31	7612.33	6424.02
3	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	5996.00	5268.44
4	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6395.00	11609.00	5214.00
5	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13171.00	17270.00	4099.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 735 projects, 5 projects are ahead of schedule, 118 are on schedule and 282 are delayed with respect to original schedule. However, the numbers of delayed projects further decrease to 262 if delay is calculated on the basis of latest schedule of completion. Further, 21 projects have been sanctioned without any commissioning schedule/date and for 309 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 282 delayed projects, 55 projects have overall delay in the range of 1 to 12 months, 73 projects have a delay in the range of 13 to 24 months, 85 projects have a delay in the range of 25 to 60 months and 69 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-05-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	RAILWAYS	04/1986	03/1994	09/2014	246
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	RAILWAYS	03/1984	03/1995	03/2015	240
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	11/2002	12/2017	181
4	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	03/2005	12/2016	141
5	AMRAVATI-NARKHER NL(CR)	RAILWAYS	06/1994	06/1999	03/2011	141

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipments, fund constraints, geological surprises, equipment erection, geo-mining condition, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issue, ROU/ROW problems, law and order situation, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as follows:-

List of 5 Earliest Projects without Milestones (as on 31-05-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as follows:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-05-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	VIRAMGAM-BHILDI(WR),GC	RAILWAYS	04/1990	155.66	N.R.	200.42
2	RAJKOTVERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	N.R.	462.18
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	688.63
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	2500.00	2500.00	8805.00
5	DALLI-RAJHARA-RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	RAILWAYS	04/1995	304.00	N.R.	138.39

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

N.R.: Not Reported.

The earliest initiated 5 projects in which project agencies are not reporting/providing or updating revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.05.2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Atomic Energy Sector**, all the 4 projects are delayed. The project 'Kudankulam Atomic Power Plant, (NPCIL)' (Mega Project) has reported additional delay of 9 months due to delay in supply and erection of equipments.

ii) In the **Coal Sector**, out of 55 projects, 30 projects are delayed. During the month, 2 projects have reported additional delay of 36 months each. The project 'Ashok Expn. OCP -CCL (10 Mty), CCL' has reported additional delay of 36 months due to delay in forest clearance; and the project 'Karma OCP (1.0 Mty), CCL' has reported additional delay of 36 months (however, no specific reasons have been reported by the project authority for the delay in this project).

iii) In the **Steel Sector**, out of 20 projects, 13 projects are delayed. During the month, 3 projects have reported additional delays in the range of 2-5 months, out of which 2 are Mega projects. The project 'Expansion of Bokaro Steel Plant, SAIL' has reported additional delay of 2 months due to delay in testing and stabilization of electrical & automation system ; the project 'Expansion of Durgapur Steel Plant, SAIL' has reported additional delay of 3 months due to change of scope of work; and the project 'Augmentation of Iron Ore Storage in RMHP, RINL' has reported additional delay of 5 months due to delay in finalization of tender.

iv) In the **Railway Sector**, out of 291 projects, 37 projects are delayed. During the month, 4 projects have reported additional delays in the range of 3-24 months, out of which 1 is Mega project. The projects 'Guna-Etawah via Shivpuri-Gwalior –Bhind, NL, NCR' and 'Ranchi-Lohardaga, (GC), SER' have reported additional delays of 3 months each due to occurrence of cracks in piers and law & order problems respectively; the project 'New Work for Construction of Metro Railway from Baranagar to Barrackpore and Dakshineshwar (MTP), RVNL' has reported additional delay of 24 months due to delay in forest clearance; and the project 'Tamluk-Basulya-Sutahat Doubling, SER' has reported additional delay of 6 months (however, no specific reasons have been reported by the project authority for the delay in this project).

v) In the **Power Sector**, out of 102 projects, 52 projects are delayed. During the month 6 projects have reported additional delays in the range of 1-9 months, out of which 2 are Mega projects. The projects 'Northern Region Transmission Strengthening Scheme, PGCIL' and 'Transmission System for Connectivity of Essar Power Gujarat Limited, PGCIL' have reported additional delays of 1 and 9 months respectively due to ROW problems; the project 'Transmission System for Connectivity of MB Power Limited, PGCIL' has reported additional delay of 2 months due to delay in forest clearance and ROW problems; the project 'Subansiri Lower H.E.P, NHPC' has reported additional delay of 3 months due to agitation by different pressure groups; the project 'Teesta Low Dam HEP, Stage-IV, NHPC' has reported additional delay of 6 months due to termination of contract; and the project 'System Strengthening Common for WR and NR (Line Bays and Reactor Provision), PGCIL' has reported additional delay of 2 months (however, no specific reason has been reported by the project authority for the delay in this project).

vi) In the **Petroleum Sector**, out of 80 projects, 47 projects are delayed. During the month 11 projects have reported additional delays in the range of 1-12 months, out of which 6 are Mega projects. The project 'Purchase of 2 Nos. of 2000 HP Drilling RIG, OIL' has reported additional delay of 1 month due to court case; the projects 'Petrochemical Complex-II at Vijaypur and Pata, GAIL' and 'MRPL Phase-III Expansion Mangalore Refinery' have reported additional delays of 2 and 3 months respectively due to slow progress in construction works; the project 'Gas Turbine Generation Set, OIL' has reported additional delay of 2 months due to delay in supply of equipments; the project 'Development of C-Series Fields ONGC' has reported additional delay of 8 months due to delay in drilling of planned wells; the projects 'Development of B-193 Cluster Fields, ONGC' and 'Construction of 12 Offshore Supply Vessels (OSV) ONGC' have reported additional delays of 12 months each due to change in scope of works and inadequate ancillary/sub-contractor at the location respectively; the projects 'Marketing Terminal at Paradeep, IOCL' and 'Strategic Crude Oil Storage Project at VIZAG, ISPRL' have reported additional delays of 3 and 5 months; and the projects 'Conversion of RIG Sagar Samrat to Mobile Offshore Production Unit (MOPS), ONGC' and 'Pipeline Replacement Project-3, ONGC' have reported additional delays of 9 and 12 months (however, no specific reasons have been reported by the project authorities for the delay in these projects).

vii) In the **Road Sector**, out of 138 projects, 89 projects are delayed. During the month 56 projects have reported additional delays in the range of 1-40 months, out of which 12 are Mega projects. Of these 56 projects, 6 projects have reported additional delays of 1 month each, 4 projects have reported additional delays of 2 months each, 10 projects have reported additional delays of 3 months each, 3 projects have reported additional delays of 4 months each, 10 projects have reported additional delays of 6 months each, 3 projects have reported additional delays of 7 months each, 2 projects have reported additional delays of 9 months each, 2 projects have reported additional delays of 8 and 11 months respectively, 9 projects have reported additional delays of 12 months each. The projects 'Bhopal-Sanchi, NHAI' and 'Krishnanagar-Berhampur, NHAI' have reported additional delays of 14 and 17 months respectively; the projects 'Indore-Dewas (NH-3), NHAI' and '4-Laning of Barhi-Hazaribagh, NHAI' have reported additional delays of 18 and 19 months respectively; the projects 'Niroli-Roxy-Rajamunda, NHAI' and '4 Lanning of Belgum-Khanpur Section and 2 Lanning of Khanpur-Karnataka/Goa Border, NHAI' have reported additional delays of 24 and 29 months respectively; and the project 'Panipat-Jalandhar 6 Lane (KM 96 to 387.1 KM), NHAI' has reported additional delay of 40 months (however, no specific reasons have been reported by the project authority for the delay in these project).


10. The status as on 31.05.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	291	4
2	ROAD TRANSPORT AND HIGHWAYS	138	56
3	POWER	102	6
4	PETROLEUM	80	11
5	COAL	55	2
6	STEEL	20	3
7	SHIPPING AND PORTS	19	0
8	TELECOMMUNICATIONS	11	0
9	CIVIL AVIATION	8	0
10	URBAN DEVELOPMENT	5	0
11	ATOMIC ENERGY	4	1
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	735	83

Sectoral break up of on-going infrastructure projects.

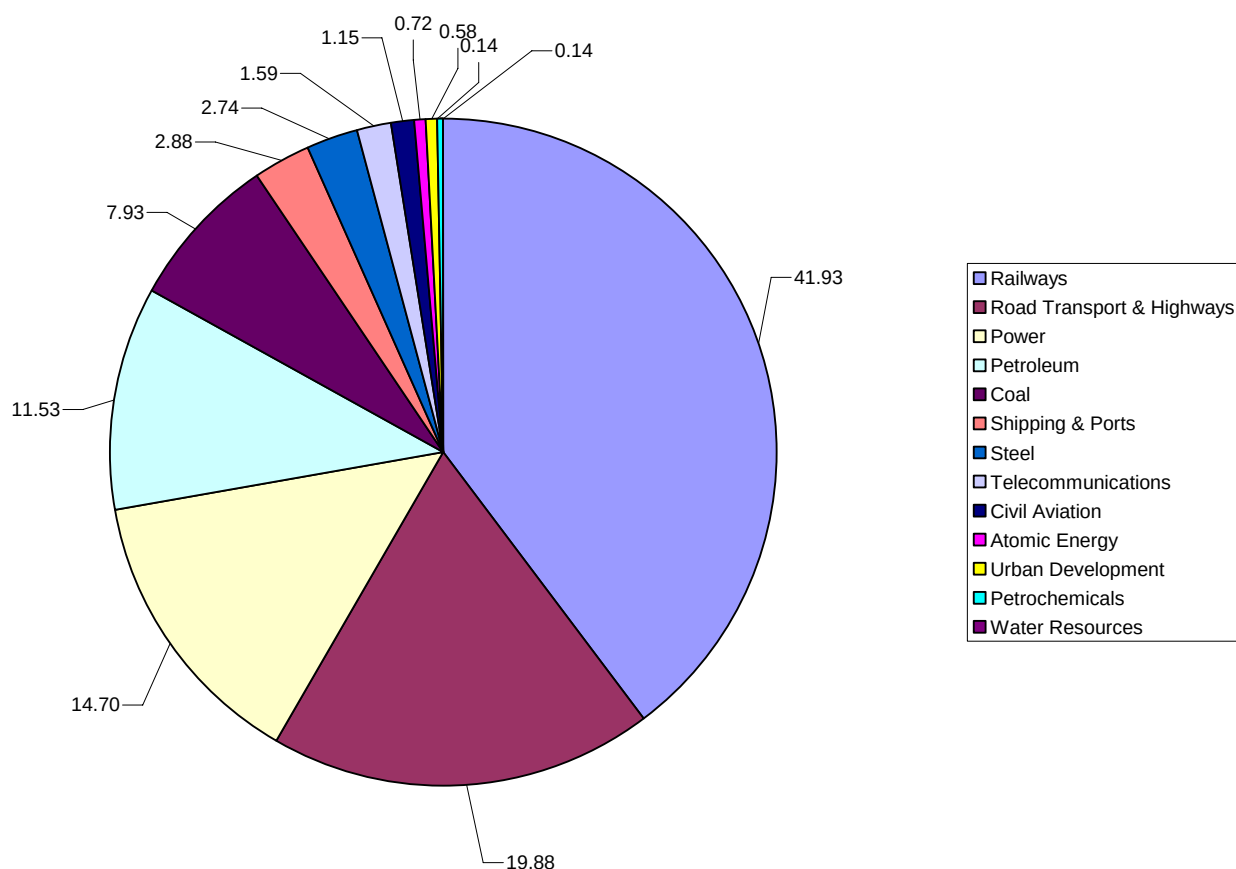

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2014			
	<u>COAL</u>			
1	BINA EXTN. PROJ(6.0 MTPA) (NORTHERN COAL FIELDS LIMITED) - [N06000019]	168.97	03/2014	67.53
	<u>POWER</u>			
2	PARBATI H.E.P. STAGE -III (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100250]	2,304.56	10/2010	2349.46


Summary of projects in the Flash Report for the month of May, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	727
Number of Projects completed/dropped/frozen in Current Month	5
Number of Projects Added in Current Month	13
Number of Projects in Current Month	735


Brief Analysis

Project Status with respect to Original Schedule: Out of 735 projects, 5 projects are ahead of schedule, 118 projects are on schedule and 282 projects are delayed. Of the balance, 309 projects do not have fixed dates of commissioning while 21 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

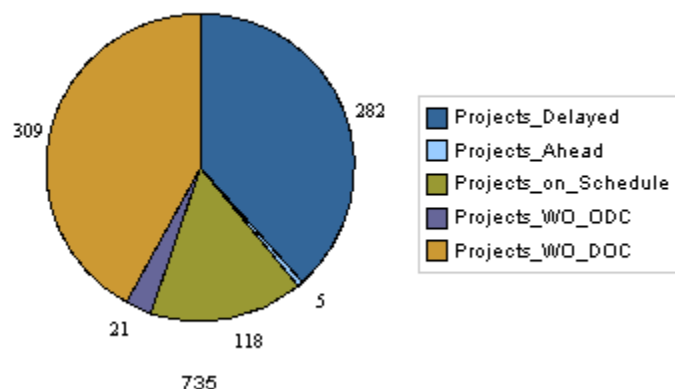

Investment Scenario

Total original cost of implementation of 735 projects when sanctioned, was of the order of Rs. 957390.48 crore but this was subsequently revised to Rs. 1140912.47 crore implying a cost overrun of 19.2%. The expenditure incurred on these projects till May, 2014 is Rs. 570976.01 crore, which is 50% of the revised cost of the projects.

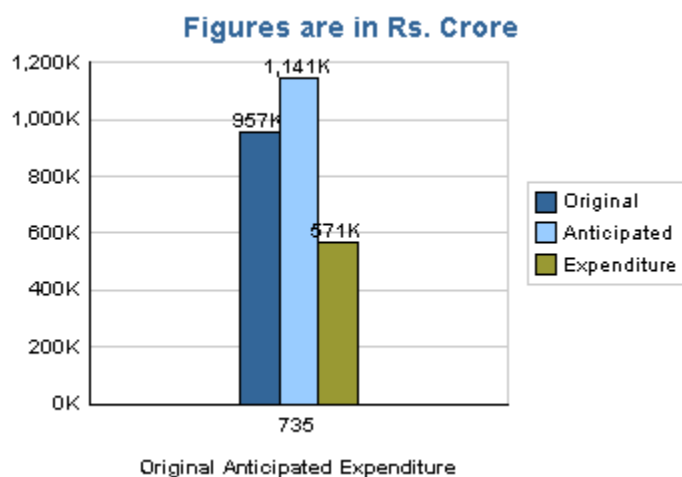

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	727
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects elevated to status of Major project during the current months	3
No of Projects added in Current Month	13
No of Projects in Current Month	735

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	282	5	118	21	309	735	38.37
Latest Approved (Date)	262	12	131	21	309	735	35.65

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	599	8,41,088.03	9,03,203.61	4,24,968.99	47.10	62,115.58	7.40
Project with Revision in Cost	136	1,81,415.80	2,37,708.86	1,46,007.02	61.40	56,293.06	31.00
Total	735	10,22,503.83	11,40,912.47	5,70,976.01	50.05	118408.64	11.58
Original Cost of All Projects							
Original Cost	735	9,57,390.48	11,40,912.47	5,70,976.01	50.00	1,83,521.99	19.20

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	282	488,921.85	588,819.20	393,336.59	66.80	99,897.35	20.40
Latest Approved (RCE)	262	506,187.84	566,142.30	384,551.35	67.90	59,954.46	11.80

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	84	107,135.91	116,083.41	106,667.41	91.90	8,947.50	8.40
Total	84	107,135.91	116,083.41	106,667.41	91.89	8947.5	8.35

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	4,086.1	4,996.7	22.3
3	COAL	55	38,568.4	48,390.6	25.5	8	9,767.8	20,187.6	106.7
4	STEEL	20	65,959.3	72,188.6	9.4	8	24,551.0	30,810.3	25.5
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	80	197,630.1	210,187.3	6.4	19	56,965.2	75,262.1	32.1
7	POWER	102	249,361.9	262,250.2	5.2	14	36,642.4	49,530.7	35.2
8	RAILWAYS	291	155,156.9	275,719.2	77.7	153	67,057.3	187,908.5	180.2
9	ROAD TRANSPORT AND HIGHWAYS	138	103,326.7	105,331.5	1.9	9	2,815.3	4,844.7	72.1
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	9	8,629.0	11,916.7	38.1
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	2	6,509.2	11,782.1	81.0
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		735	957,390.5	1,140,912.5	19.2	232	241,083.8	431,774.8	79.1

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	24,561.0	29,968.8	22.0	9	11,299.4	17,574.1	55.5
2	ARUNACHAL PRADESH	4	9,512.2	12,475.6	31.2	3	3,226.9	6,190.3	91.8
3	ASSAM	38	24,056.9	38,946.6	61.9	14	11,753.0	26,729.0	127.4
4	BIHAR	46	33,296.7	40,874.2	22.8	15	13,337.3	21,093.0	58.1
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	15.8
6	GUJARAT	32	37,940.0	39,011.9	2.8	7	3,021.0	4,413.4	46.1
7	HARYANA	10	4,709.7	6,907.4	46.7	3	1,585.8	3,783.5	138.6
8	HIMACHAL PRADESH	5	13,457.4	18,070.4	34.3	2	5,574.0	10,187.0	82.8
9	JAMMU AND KASHMIR	7	11,965.4	30,895.6	158.2	3	4,904.9	23,835.1	385.9
10	KARNATAKA	35	79,606.4	94,510.7	18.7	18	14,297.2	29,539.7	106.6
11	KERALA	12	22,610.7	25,135.4	11.2	5	5,480.4	8,005.2	46.1
12	MADHYA PRADESH	19	30,521.2	32,003.8	4.9	5	3,061.7	4,963.7	62.1
13	MAHARASHTRA	50	93,249.8	109,917.8	17.9	18	32,848.9	51,552.1	56.9
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	724.1
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	MIZORAM	2	988.1	3,307.1	234.7	2	988.1	3,307.1	234.7
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	187.8
18	ODISHA	34	61,113.8	68,023.3	11.3	12	33,469.7	40,379.2	20.6
19	PUNJAB	4	1,680.2	1,653.2	-1.6	0	0.0	0.0	0.0
20	RAJASTHAN	25	25,638.7	25,695.9	0.2	5	2,337.2	2,880.5	23.2
21	SIKKIM	2	1,648.9	3,684.9	123.5	1	1,339.5	3,375.4	152.0
22	TAMIL NADU	39	54,453.9	70,685.6	29.8	20	30,997.2	47,228.9	52.4
23	TRIPURA	6	2,966.3	4,737.3	59.7	3	2,129.4	3,934.7	84.8
24	UTTAR PRADESH	27	19,788.4	23,055.5	16.5	9	2,164.3	5,479.6	153.2
25	WEST BENGAL	37	53,725.7	63,984.3	19.1	14	19,809.6	30,068.3	51.8
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	DELHI	4	41,531.3	41,531.3	0.0	0	0.0	0.0	0.0
28	CHHATISGARH	24	57,805.7	65,314.3	13.0	6	2,585.1	10,093.7	290.5
29	JHARKHAND	27	16,118.8	20,383.6	26.5	8	2,534.9	6,971.4	175.0
30	UTTARAKHAND	7	9,501.0	13,063.9	37.5	5	7,496.0	11,058.9	47.5
31	TELANGANA	22	9,563.3	12,332.1	29.0	5	1,473.0	4,241.8	188.0
32	MULTI STATE	187	203,894.7	226,339.6	11.0	37	21,456.0	46,057.8	114.7
Total		735	957,390.5	1,140,912.5	19.2	232	241,083.8	431,774.8	79.1

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 75
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	2	653.7	653.7	7 - 71
3	COAL	55	38,568.4	48,390.6	25.5	30	25,613.7	35,855.4	24 - 120
4	STEEL	20	65,959.3	72,188.6	9.4	13	64,208.3	70,162.3	10 - 69
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	80	197,630.1	210,187.3	6.4	47	129,471.0	139,689.1	3 - 110
7	POWER	102	249,361.9	262,250.2	5.2	52	131,036.4	142,582.6	1 - 113
8	RAILWAYS	291	155,156.9	275,719.2	77.7	37	29,143.6	81,613.0	3 - 246
9	ROAD TRANSPORT AND HIGHWAYS	138	103,326.7	105,331.5	1.9	89	61,951.1	63,929.1	4 - 120
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	3	1,889.9	3,270.0	5 - 99
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	4	2,018.2	1,843.9	37 - 68
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		735	957,390.5	1,140,912.5	19.2	282	488,921.9	588,819.2	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	24,561.0	29,968.8	22.0	8	17,332.3	20,539.0	11 - 69
2	ARUNACHAL PRADESH	4	9,512.2	12,475.6	31.2	3	9,356.2	12,067.7	25 - 99
3	ASSAM	38	24,056.9	38,946.6	61.9	29	15,144.2	23,478.7	21 - 120
4	BIHAR	46	33,296.7	40,874.2	22.8	10	20,737.2	25,005.5	5 - 98
5	GOA	1	335.6	388.5	15.8	0	0.0	0.0	-
6	GUJARAT	32	37,940.0	39,011.9	2.8	12	24,832.9	24,854.4	6 - 27
7	HARYANA	10	4,709.7	6,907.4	46.7	3	1,875.1	3,055.1	40 - 55
8	HIMACHAL PRADESH	5	13,457.4	18,070.4	34.3	2	8,446.7	11,139.6	73 - 106
9	JAMMU AND KASHMIR	7	11,965.4	30,895.6	158.2	6	11,799.1	30,702.5	6 - 181
10	KARNATAKA	35	79,606.4	94,510.7	18.7	6	16,777.3	17,020.6	17 - 44
11	KERALA	12	22,610.7	25,135.4	11.2	5	17,074.0	17,774.0	5 - 58
12	MADHYA PRADESH	19	30,521.2	32,003.8	4.9	8	3,545.9	3,658.7	5 - 74
13	MAHARASHTRA	50	93,249.8	109,917.8	17.9	18	29,294.9	36,953.7	3 - 129
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	72 - 72
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	1	536.0	536.0	11 - 11
16	MIZORAM	2	988.1	3,307.1	234.7	2	988.1	3,307.1	35 - 113
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	24 - 24
18	ODISHA	34	61,113.8	68,023.3	11.3	18	52,335.8	55,568.3	4 - 84
19	PUNJAB	4	1,680.2	1,653.2	-1.6	1	705.0	705.0	21 - 21
20	RAJASTHAN	25	25,638.7	25,695.9	0.2	6	15,364.0	14,917.7	3 - 76
21	SIKKIM	2	1,648.9	3,684.9	123.5	2	1,648.9	3,684.9	15 - 71
22	TAMIL NADU	39	54,453.9	70,685.6	29.8	15	36,540.7	45,969.7	3 - 99
23	TRIPURA	6	2,966.3	4,737.3	59.7	4	2,417.4	4,188.4	16 - 120
24	UTTAR PRADESH	27	19,788.4	23,055.5	16.5	11	5,608.5	7,089.5	13 - 93
25	WEST BENGAL	37	53,725.7	63,984.3	19.1	14	30,490.2	34,623.8	3 - 141
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	-
27	DELHI	4	41,531.3	41,531.3	0.0	1	2,494.0	2,494.0	8 - 8
28	CHHATISGARH	24	57,805.7	65,314.3	13.0	14	41,280.9	48,016.3	4 - 120
29	JHARKHAND	27	16,118.8	20,383.6	26.5	13	9,861.5	10,449.7	3 - 132
30	UTTARAKHAND	7	9,501.0	13,063.9	37.5	5	7,754.2	11,207.0	26 - 79
31	TELANGANA	22	9,563.3	12,332.1	29.0	5	1,898.8	3,098.7	24 - 47
32	MULTI STATE	187	203,894.7	226,339.6	11.0	58	101,204.2	108,271.2	1 - 246
Total		735	957,390.5	1,140,912.5	19.2	282	488,921.9	588,819.2	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 75
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	2	653.7	653.7	7 - 71
3	COAL	55	38,568.4	48,390.6	25.5	29	24,425.4	28,243.1	24 - 84
4	STEEL	20	65,959.3	72,188.6	9.4	10	62,441.9	68,084.6	10 - 69
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	80	197,630.1	210,187.3	6.4	46	126,230.0	133,050.2	3 - 110
7	POWER	102	249,361.9	262,250.2	5.2	50	130,093.7	140,540.6	1 - 106
8	RAILWAYS	291	155,156.9	275,719.2	77.7	36	28,818.6	80,496.5	3 - 246
9	ROAD TRANSPORT AND HIGHWAYS	138	103,326.7	105,331.5	1.9	79	59,998.7	61,851.6	4 - 120
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	1	1,228.0	2,158.2	58 - 58
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	4	2,018.2	1,843.9	37 - 68
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		735	957,390.5	1,140,912.5	19.2	262	478,844.1	566,142.3	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,625.0	6,946.0	4.8	2	2,660.6	2,981.7	12.1
3	COAL	55	48,365.0	48,390.6	0.1	4	1,431.8	1,716.6	19.9
4	STEEL	20	70,209.4	72,188.6	2.8	3	14,993.1	17,002.3	13.4
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	80	210,325.3	210,187.3	-0.1	8	37,161.1	40,806.6	9.8
7	POWER	102	255,362.2	262,250.2	2.7	10	26,642.8	33,530.8	25.9
8	RAILWAYS	291	184,470.6	275,719.2	49.5	130	69,108.0	160,809.6	132.7
9	ROAD TRANSPORT AND HIGHWAYS	138	103,865.0	105,331.5	1.4	9	3,158.6	4,844.7	53.4
10	SHIPPING AND PORTS	19	17,488.0	18,600.6	6.4	6	4,617.6	5,941.7	28.7
11	TELECOMMUNICATIONS	11	5,295.8	5,199.5	-1.8	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	74,052.2	79,266.2	7.0	1	6,395.0	11,609.0	81.5
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		735	1,022,503.8	1,140,912.5	11.6	180	190,229.2	313,778.3	64.9

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	1	1,808.00	2,015.00	13- 13
3	COAL	55	38,568.41	48,390.55	25.47	1	1,188.31	7,612.33	120- 120
4	STEEL	20	65,959.26	72,188.55	9.44	5	9,557.89	13,808.07	37- 69
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	80	197,630.12	210,187.26	6.35	7	19,587.43	32,235.40	20- 110
7	POWER	102	249,361.87	262,250.17	5.17	1	1,657.00	2,978.86	79- 79
8	RAILWAYS	291	155,156.87	275,719.17	77.70	14	10,842.61	28,863.02	0- 141
9	ROAD TRANSPORT AND HIGHWAYS	138	103,326.71	105,331.49	1.94	3	580.65	705.74	59- 80
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	5	5,400.70	7,558.41	10- 99
11	TELECOMMUNICATIONS	11	5,295.83	5,199.48	-1.82	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		735	957390.48	1140912.47	19.17	37	50622.59	95776.83	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 75
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	0	0.00	0.00	0- 0
3	COAL	55	38,568.41	48,390.55	25.47	6	9,127.17	19,498.95	24- 120
4	STEEL	20	65,959.26	72,188.55	9.44	4	23,538.89	29,522.85	31- 69
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	80	197,630.12	210,187.26	6.35	15	48,287.85	62,770.03	12- 110
7	POWER	102	249,361.87	262,250.17	5.17	10	28,438.70	39,439.99	10- 87
8	RAILWAYS	291	155,156.87	275,719.17	77.70	33	23,744.20	76,213.63	3- 246
9	ROAD TRANSPORT AND HIGHWAYS	138	103,326.71	105,331.49	1.94	8	2,649.01	4,651.57	40- 93
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	2	1,378.00	2,758.16	58- 99
11	TELECOMMUNICATIONS	11	5,295.83	5,199.48	-1.82	1	149.15	158.72	60- 60
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		735	957390.48	1140912.47	19.17	81	153975.97	257960.9	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	BINA EXTN. PROJ(6.0 MTPA)	11/2006	168.97	03/2014	168.97	03/2014	67.53
	<u>POWER</u>						
2	PARBATI H.E.P. STAGE -III (NHPC)	10/2005	2,304.56	10/2010	2,716.00	08/2014	2,349.46

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	RESID UPGRADATION PROJECT	2/2011	3,110.36	11/2015	3,110.36	11/2015
	<u>POWER</u>					
2	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC	6/2014	400.47	/	400.47	-
3	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	5,151.37	/	5,151.37	-
	<u>RAILWAYS</u>					
4	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM)	3/2012	1,503.71	/	1,503.71	-
5	KAKINADA-PITHAPURAM	3/1999	215.06	/	215.06	-
6	SAMBALPUR-TALCHER DOUBLING	3/2011	679.27	/	1,111.99	-
7	BHADRAK - NERGUNDI 3RD LINE	3/2013	858.67	/	858.67	-
8	JHARSUGUDA-RENGALI DOUBLING	3/2006	201.00	/	201.00	-
9	KIRANDUL - JAGDALPUR DOUBLING	12/2012	826.57	/	826.57	-
10	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	155.81	/	155.81	-

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
11	DELANG-PURI DOUBLING	3/2011	165.16	3/2015	165.16	3/2015
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
12	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III	9/2013	606.00	/	606.00	-
13	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV	4/2014	1,123.17	/	1,123.17	-

Milestones (Cumulative due & achieved)		
Total	3460	
Achieved up to month	1421	

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	06/2014	03/2015	9
	<u>COAL</u>						
2	ASHOK EXPN.OCP -CCL (10 MTY) CCL	471.66	341.63	03/2011	03/2014	03/2017	36
3	KARMA OCP (1.0MTY) CCL	162.46	162.46	03/2014	03/2014	03/2017	36
	<u>STEEL</u>						
4	EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	05/2014	07/2014	2
5	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2014	03/2015	3
6	AUGMENTATION OF IRON ORE STORAGE IN RMHP RINL	480.00	450.00	09/2009	07/2014	12/2014	5
	<u>PETROLEUM</u>						
7	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG OIL	270.00	270.00	12/2014	10/2015	11/2015	1
8	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA GAIL	8,140.00	8,140.00	02/2014	06/2014	08/2014	2
9	GAS TURBINE GENERATION SET OIL	216.88	216.88	10/2011	06/2014	08/2014	2
10	MRPL PHASE-III EXPANSION MANGALORE REFIN	12,412.00	12,160.26	01/2012	06/2014	09/2014	3
11	MARKETING TERMINAL AT PARADEEP IOCL	199.75	199.75	06/2014	09/2014	12/2014	3
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG ISPRL	672.00	1,038.00	10/2011	09/2014	02/2015	5
13	DEVELOPMENT OF C-SERIES FIELDS ONGC	3,195.16	3,690.37	12/2008	09/2014	05/2015	8
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	761.68	05/2013	06/2014	03/2015	9
15	DEVELOPMENT OF B-193 CLUSTER FIELDS ONGC	3,248.78	6,000.00	08/2010	05/2014	05/2015	12
16	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2014	12/2015	12

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
17	PIPELINE REPLACEMENT PROJECT-3 ONGC	2,547.26	1,417.00	05/2014	05/2014	05/2015	12
	<u>POWER</u>						
18	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	05/2014	06/2014	1
19	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED PGCIL	425.51	425.51	10/2013	06/2014	08/2014	2
20	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	06/2014	08/2014	2
21	SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	6,285.33	09/2010	09/2018	12/2018	3
22	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,061.38	09/2009	09/2015	03/2016	6
23	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED PGCIL	552.44	552.44	02/2014	06/2014	03/2015	9
	<u>RAILWAYS</u>						
24	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) NCR	158.77	608.02	03/1994	06/2014	09/2014	3
25	RANCHI-LOHARDAGA(GC),SER SER	194.07	596.40	06/2004	03/2015	06/2015	3
26	TAMLUK-BASULYA-SUTAHATA DOUBLING SER	146.95	171.02	06/2013	06/2014	12/2014	6
27	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
28	KISHANGARH-AJMER-BEAWER NHAI	795.00	795.00	05/2012	06/2014	07/2014	1
29	CHITRADURGA-TUMKUR(NH-4) NHAI	839.00	839.00	N.A.	05/2014	06/2014	1
30	BELGAUM-DHARWAD(NH-4) NHAI	480.00	480.00	N.A.	06/2014	07/2014	1
31	UGRADATION OF HYDERABAD-BANGALORE SECTION NHAI	680.00	680.00	N.A.	05/2014	06/2014	1
32	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY NHAI	600.00	600.00	06/2013	05/2014	06/2014	1

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
33	KANDLA - MUNDRA PORT NHA	953.88	953.88	07/2013	10/2014	11/2014	1
34	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHA)	251.03	251.03	10/2008	10/2014	12/2014	2
35	AMRITSAR-PATHANKOT NHA	705.00	705.00	11/2012	06/2014	08/2014	2
36	DEOLI-KOTA NHA	593.00	593.00	07/2013	06/2014	08/2014	2
37	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 NHA	574.00	574.00	03/2014	06/2014	08/2014	2
38	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 NHA	199.81	385.13	04/2009	12/2014	03/2015	3
39	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 NHA	155.04	280.13	11/2008	06/2014	09/2014	3
40	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHA)	195.00	195.00	06/2008	12/2014	03/2015	3
41	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHA)	237.80	237.80	06/2008	12/2014	03/2015	3
42	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 NHA	212.00	386.10	09/2007	12/2014	03/2015	3
43	GHAZIABAD-ALIGARH NH-91 NHA	1,141.00	1,141.00	08/2013	06/2014	09/2014	3
44	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 NHA	535.00	535.00	12/2013	06/2014	09/2014	3
45	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 NHA	1,250.00	1,250.00	12/2013	06/2014	09/2014	3
46	4-LANNING OF CHAPRA-HAJIPUR NHA	575.00	575.00	07/2013	12/2014	03/2015	3
47	2 LANNING OF MUZAFFARPUR - SONBARSA NHA	511.54	511.54	11/2013	06/2014	09/2014	3
48	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION NHA	1,509.10	1,509.10	09/2012	08/2014	12/2014	4
49	INDORE-JHABUA-GUJRAT/MP NHA	1,175.00	1,175.00	04/2013	08/2014	12/2014	4
50	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER NHA	909.00	909.00	05/2014	05/2014	09/2014	4
51	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHA	155.00	201.66	09/2008	06/2014	12/2014	6
52	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C NHA	230.00	230.00	06/2005	12/2014	06/2015	6


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
53	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) NHAI	332.94	332.94	09/2008	06/2014	12/2014	6
54	DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	06/2014	12/2014	6
55	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM NHAI	1,585.00	1,585.00	05/2013	06/2014	12/2014	6
56	KUNDUPUR-SURATHKAL & MANGLORE NHAI	671.00	671.00	N.A.	12/2014	06/2015	6
57	JORBAT - BARAPANI NHAI	536.00	536.00	01/2014	06/2014	12/2014	6
58	SRINAGAR TO BANIHAL NHAI	1,100.70	1,100.70	06/2014	06/2014	12/2014	6
59	4-LANING OF FARAKA-RAIGANJ NHAI	1,078.84	1,078.84	08/2013	12/2014	06/2015	6
60	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 NHAI	828.00	828.00	09/2014	09/2014	03/2015	6
61	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	280.00	280.00	02/2009	05/2014	12/2014	7
62	PATNA-MUZZAFFARPUR NHAI	671.30	671.30	02/2013	05/2014	12/2014	7
63	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS NHAI	374.00	374.00	05/2013	05/2014	12/2014	7
64	HARANGAJO TO MAIBANG, NH-54 NHAI	196.00	363.74	07/2009	04/2014	12/2014	8
65	MURADABAD-BAREILLY NHAI	1,267.00	1,267.00	06/2013	06/2014	03/2015	9
66	VARANASI-AURANGABAD KM.786 TO KM.978.40 NHAI	2,848.00	2,848.00	03/2014	03/2015	12/2015	9
67	CHAMBAL BRIDGE, NH-76 (RJ-5) NHAI	275.00	281.31	02/2010	07/2015	06/2016	11
68	GWALIOR-JHANSI, NH-75 NHAI	604.00	604.00	12/2009	12/2014	12/2015	12
69	AGRA-BYPASS(NS-1/UP-1), NH-2,3 NHAI	348.16	465.50	09/2007	06/2014	06/2015	12
70	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) NHAI	572.30	572.30	10/2011	06/2014	06/2015	12
71	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) NHAI	617.00	617.00	08/2012	03/2015	03/2016	12
72	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 NHAI	1,535.00	1,535.00	05/2014	05/2014	05/2015	12


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
73	BAREILY-SITAPUR NHAI	1,046.00	1,046.00	09/2013	12/2014	12/2015	12
74	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) NHAI	478.00	478.00	10/2013	12/2014	12/2015	12
75	PANVEL-INDAPUR NHAI	942.69	942.69	06/2014	12/2014	12/2015	12
76	BARSAT-KRISHNANAGAR NHAI	867.00	867.00	02/2015	02/2015	02/2016	12
77	BHOPAL-SANCHI NHAI	209.00	209.00	01/2013	10/2014	12/2015	14
78	KRISHNANAGAR-BERHAMPUR NHAI	702.16	702.16	07/2014	07/2014	12/2015	17
79	INDORE-DEWAS(NH-3) NHAI	325.00	325.00	05/2013	06/2014	12/2015	18
80	4-LANING OF BARHI-HAZARIBAGH NHAI	398.00	398.00	02/2014	02/2014	09/2015	19
81	NIROLI-ROXY-RAJAMUNDA NHAI	586.00	586.00	01/2014	12/2014	12/2016	24
82	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER NHAI	359.00	359.00	09/2013	07/2014	12/2016	29
83	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) NHAI	1,108.00	2,288.00	11/2011	11/2011	03/2015	40

Graphical Presentation of All Projects w.r.t. Original Schedule

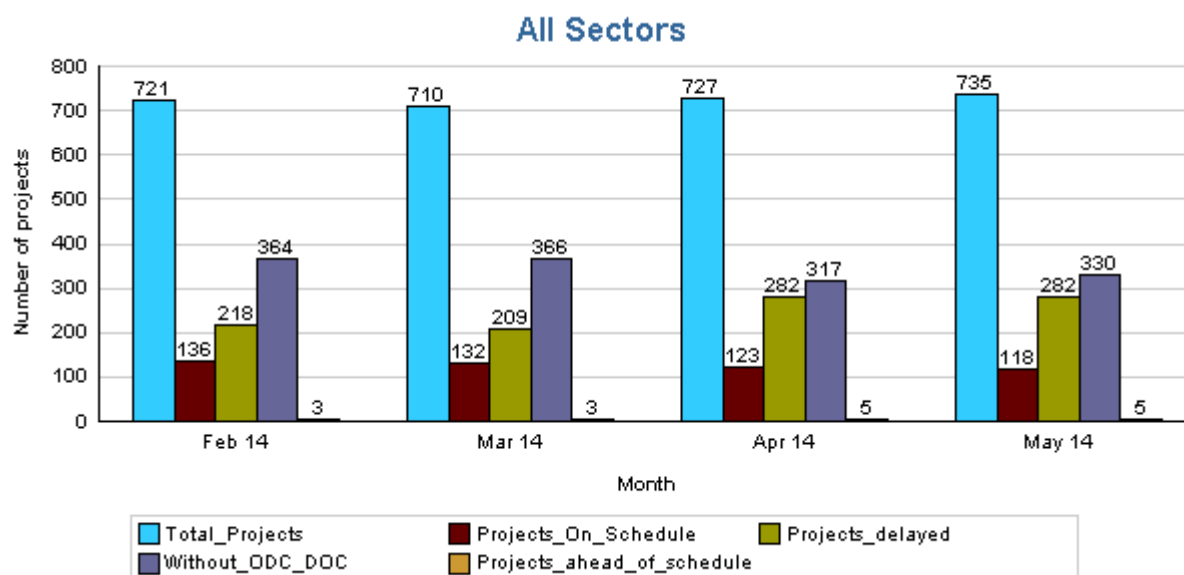

Break-up of 282 Delayed projects in May 2014

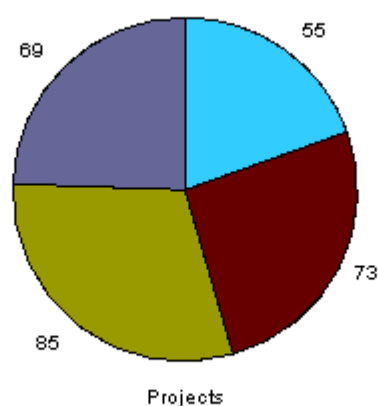


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of All Projects w.r.t. Revised Schedule

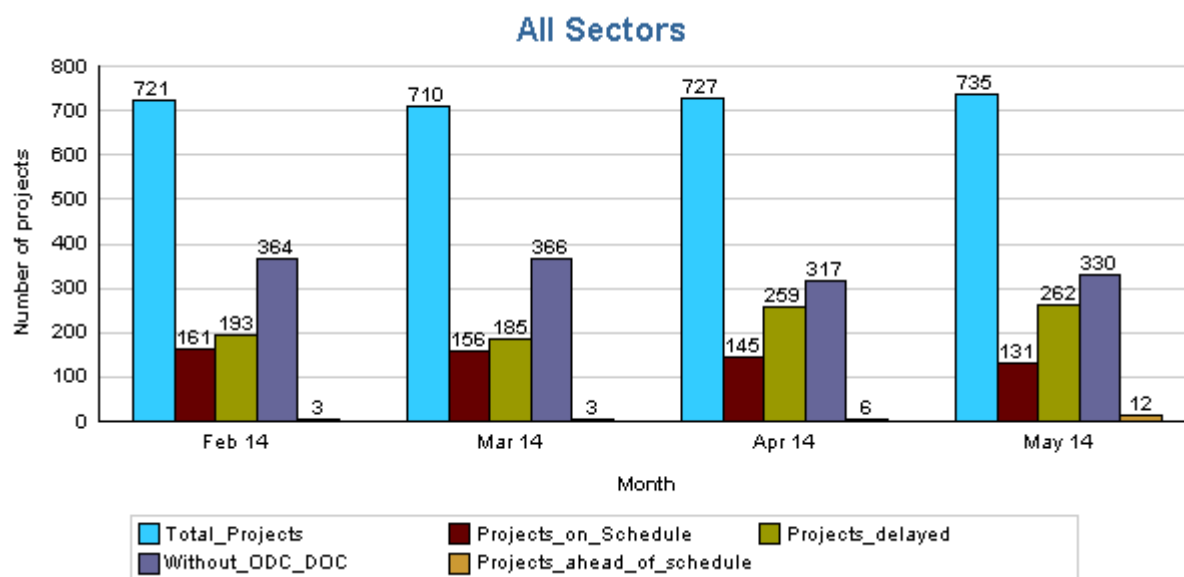


Break-up of 262 Delayed projects in May 2014

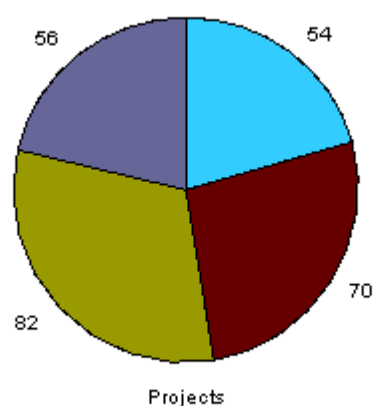


Delay in Months



Graphical Presentation of URBAN DEVELOPMENT Sector

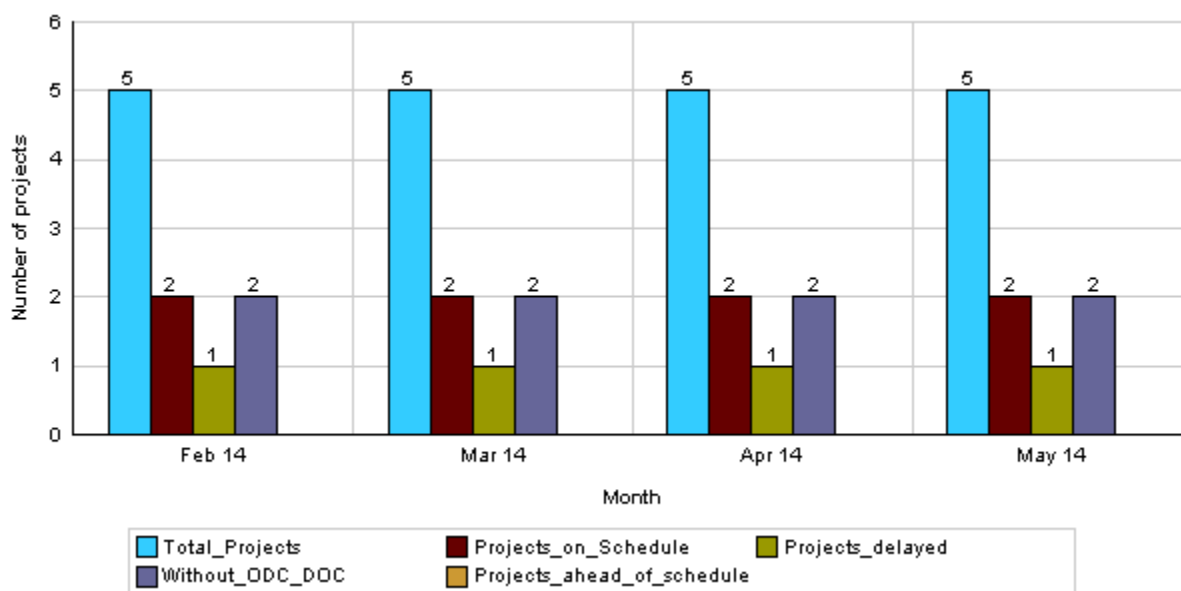


Break-up of 1 Delayed projects in May 2014




Delay in Months

Graphical Presentation of TELECOMMUNICATIONS Sector

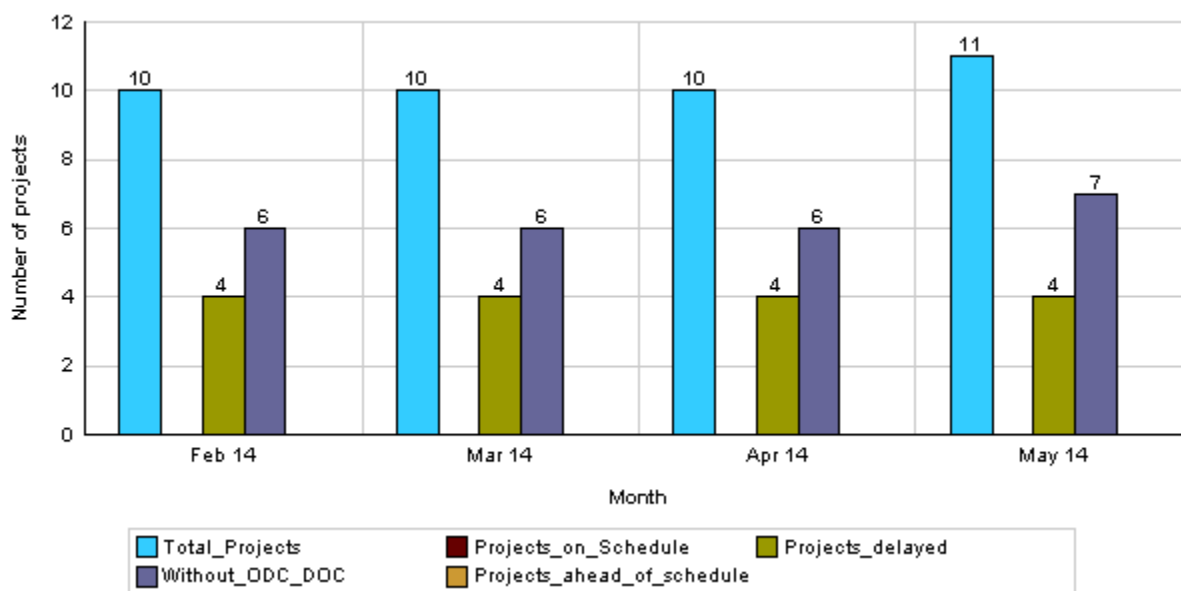


Break-up of 4 Delayed projects in May 2014

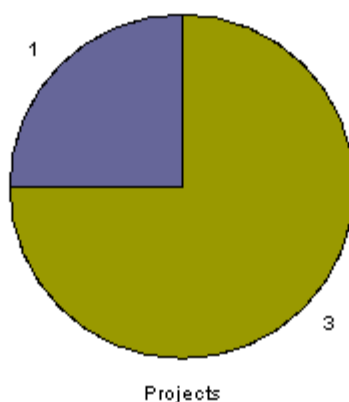


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	3	0	0	0
13-24	0	0	0	0
25-60	0	0	3	0
MORE THAN 60	0	0	0	1

Graphical Presentation of SHIPPING AND PORTS Sector

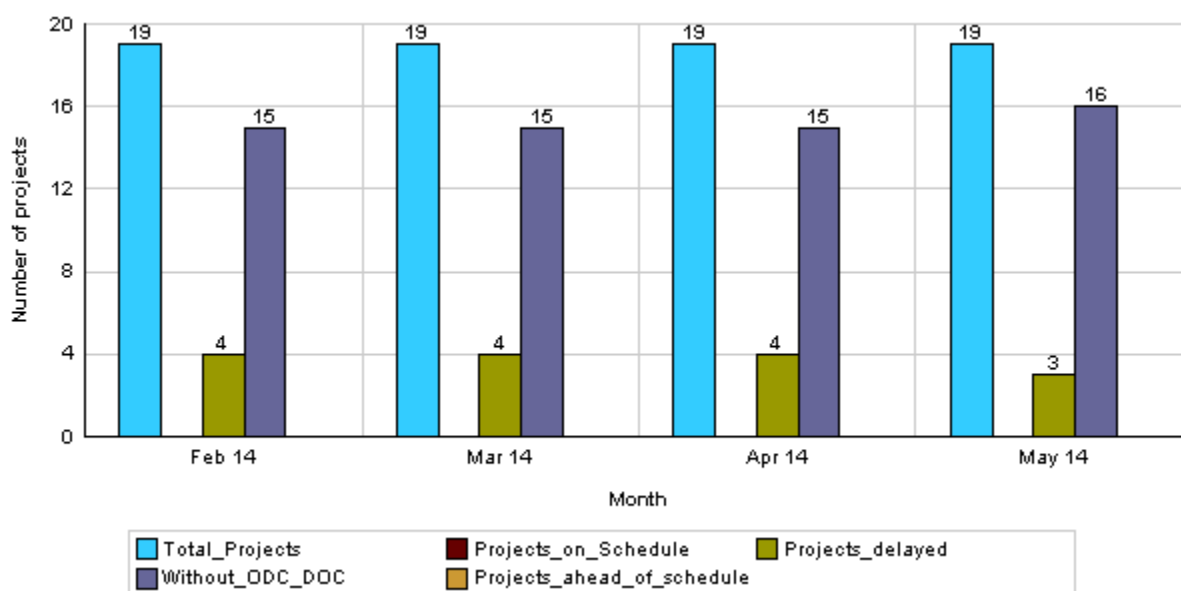


Break-up of 3 Delayed projects in May 2014

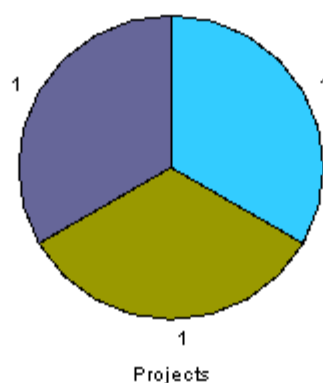


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

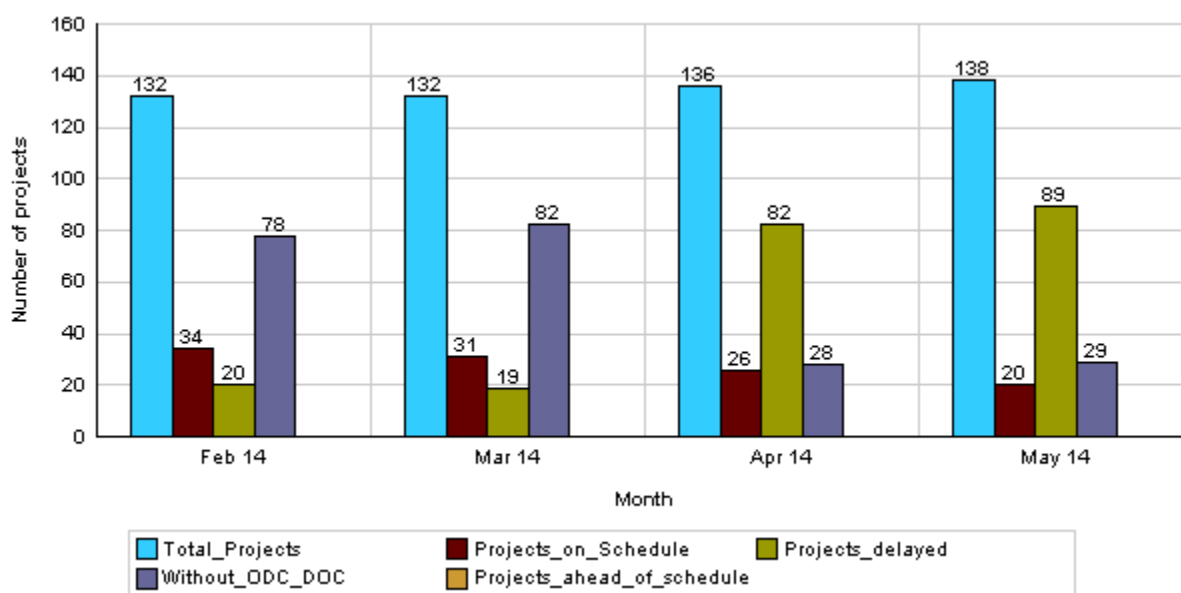


Break-up of 89 Delayed projects in May 2014

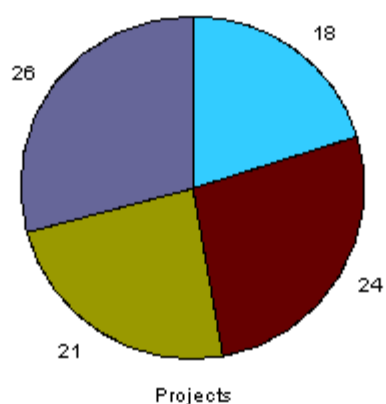


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	18	24	21	26

Graphical Presentation of RAILWAYS Sector

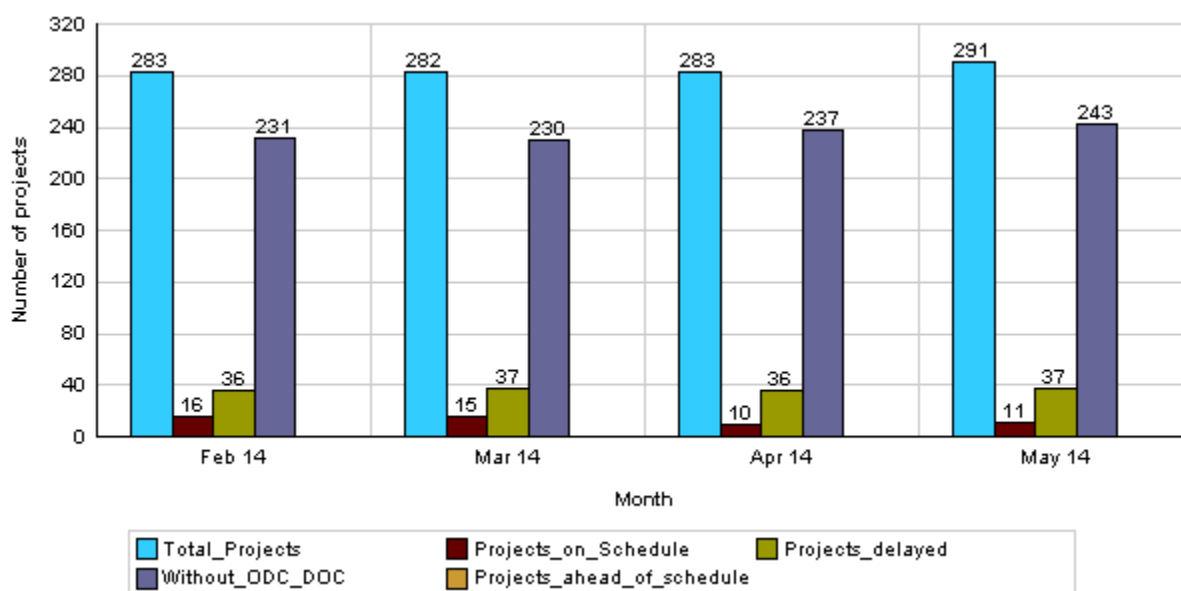


Break-up of 37 Delayed projects in May 2014

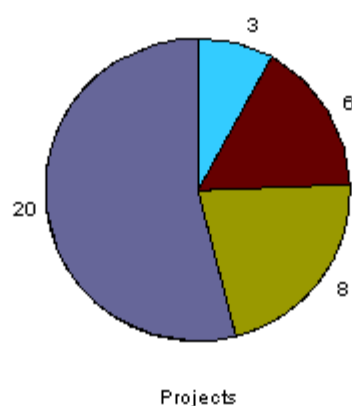


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

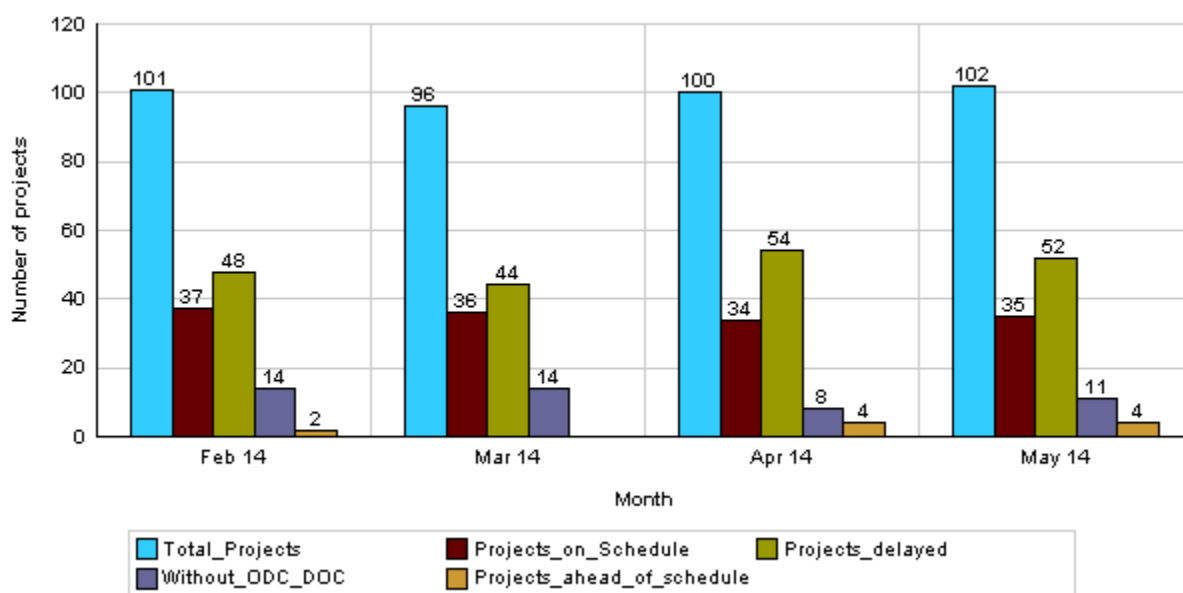


Break-up of 52 Delayed projects in May 2014

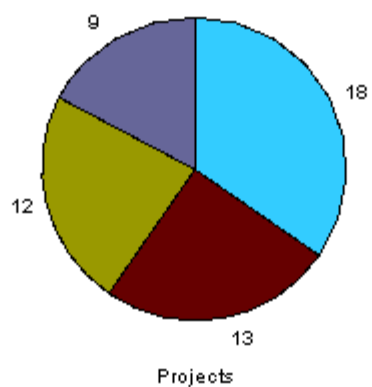


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	18	13	12	9

Graphical Presentation of PETROLEUM Sector

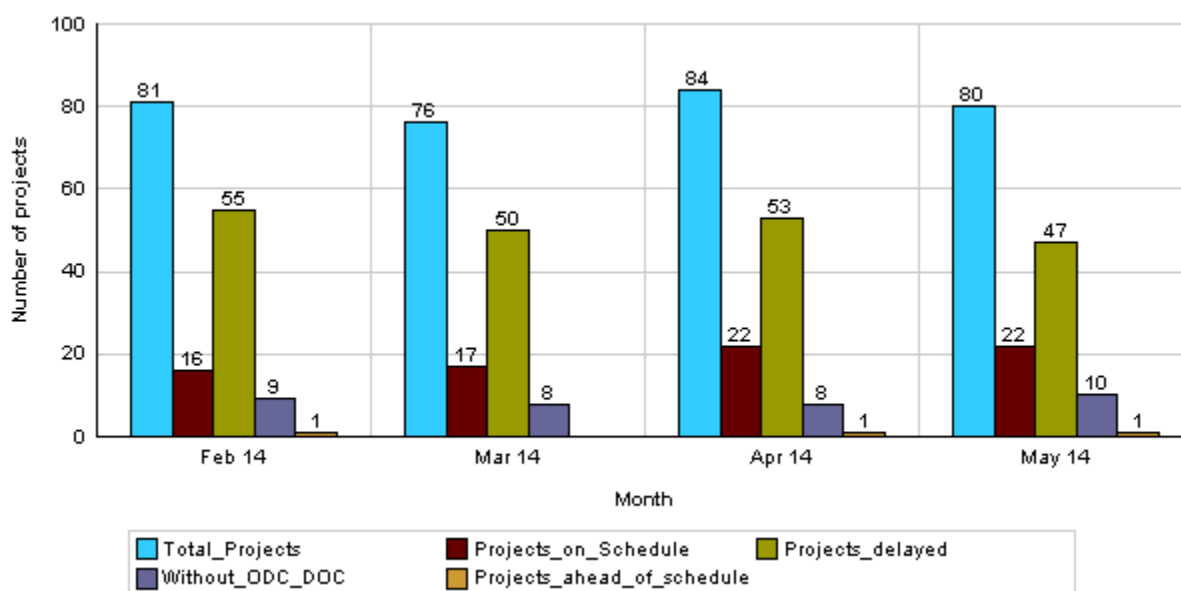


Break-up of 47 Delayed projects in May 2014

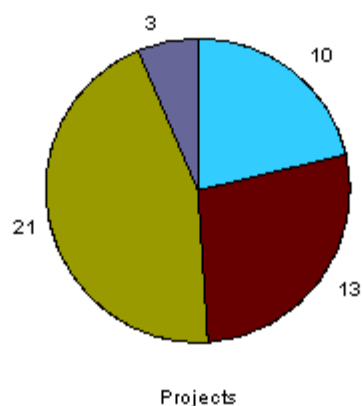


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
-----------------	------	-------	-------	--------------

Graphical Presentation of STEEL Sector

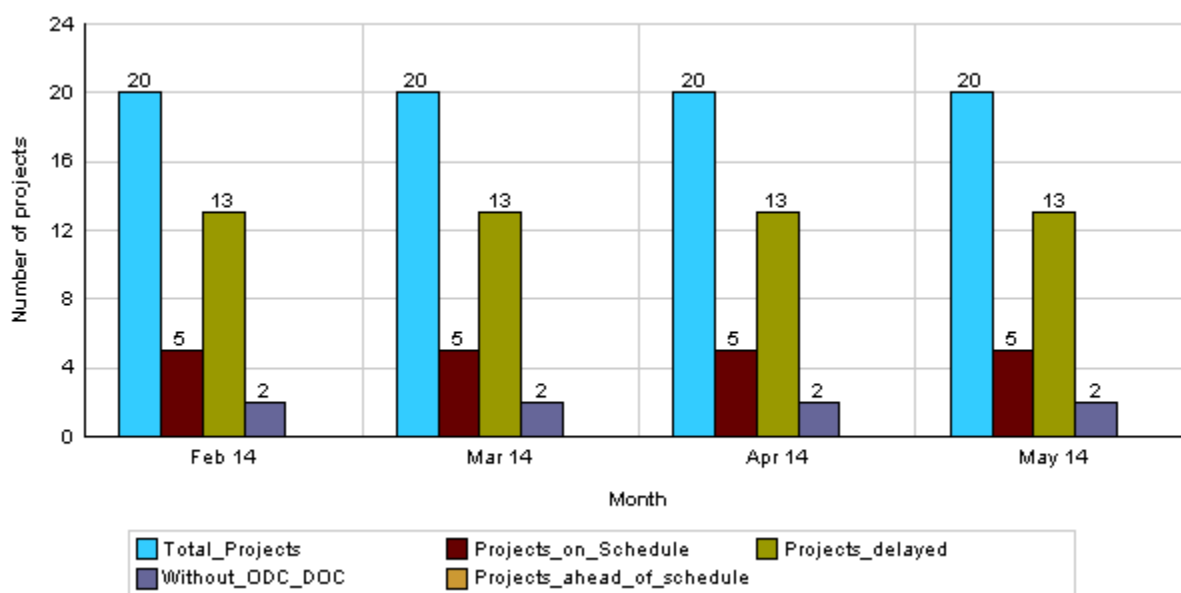


Break-up of 13 Delayed projects in May 2014

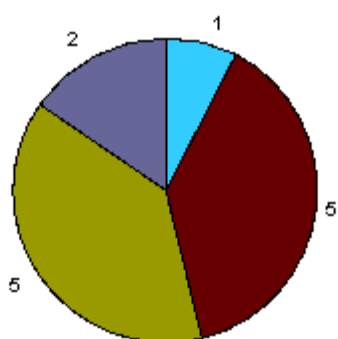


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	1	5	5	2

Graphical Presentation of COAL Sector

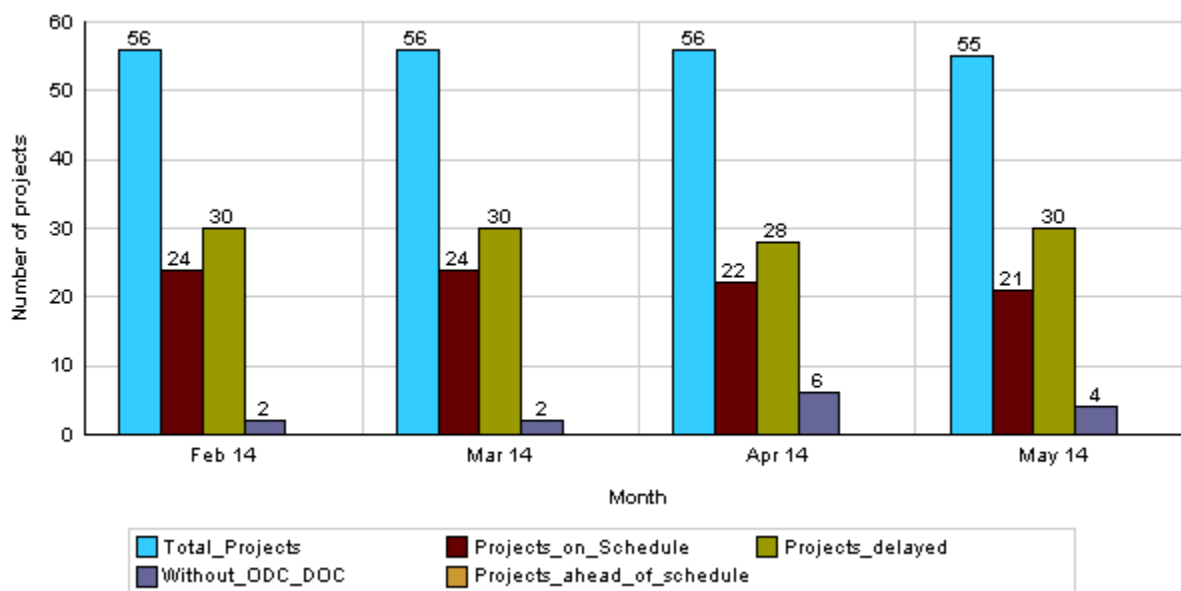


Break-up of 30 Delayed projects in May 2014

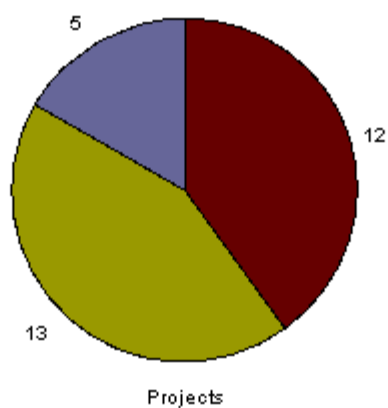


Delay in Months

Legend: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of CIVIL AVIATION Sector

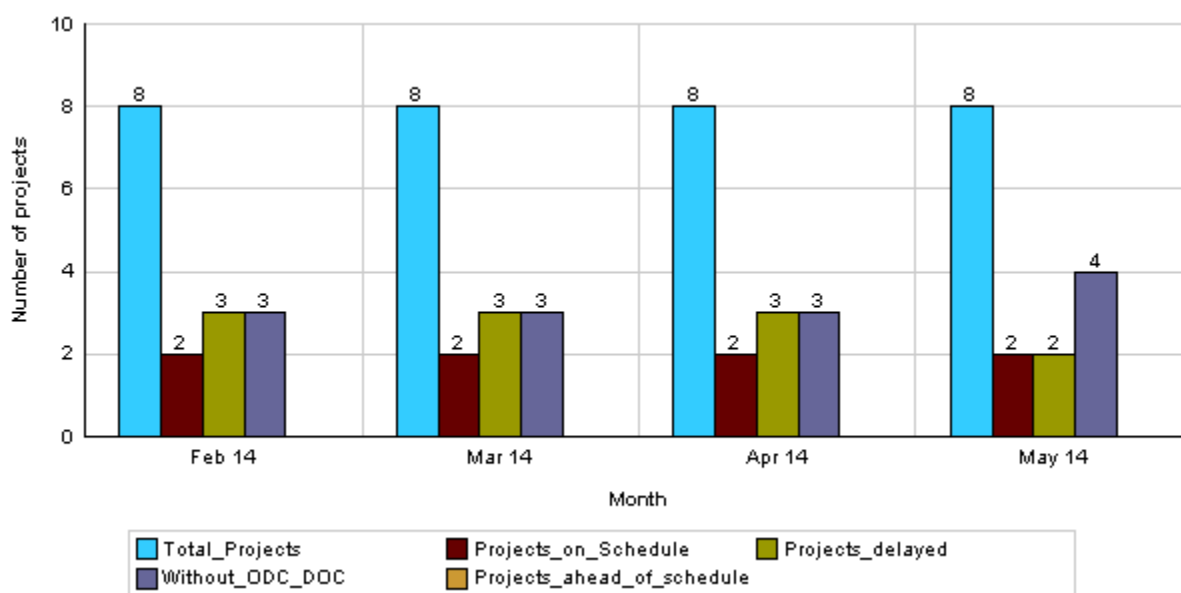


Break-up of 2 Delayed projects in May 2014

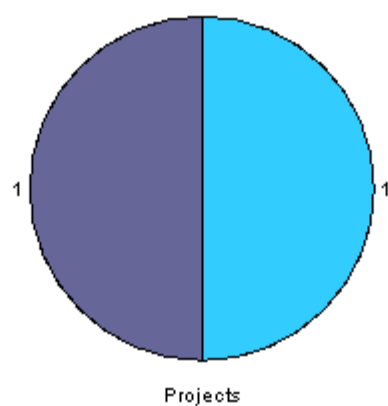


Delay in Months

Delay in Months	Count
1-12	1
13-24	0
25-60	0
MORE THAN 60	1

Graphical Presentation of ATOMIC ENERGY Sector

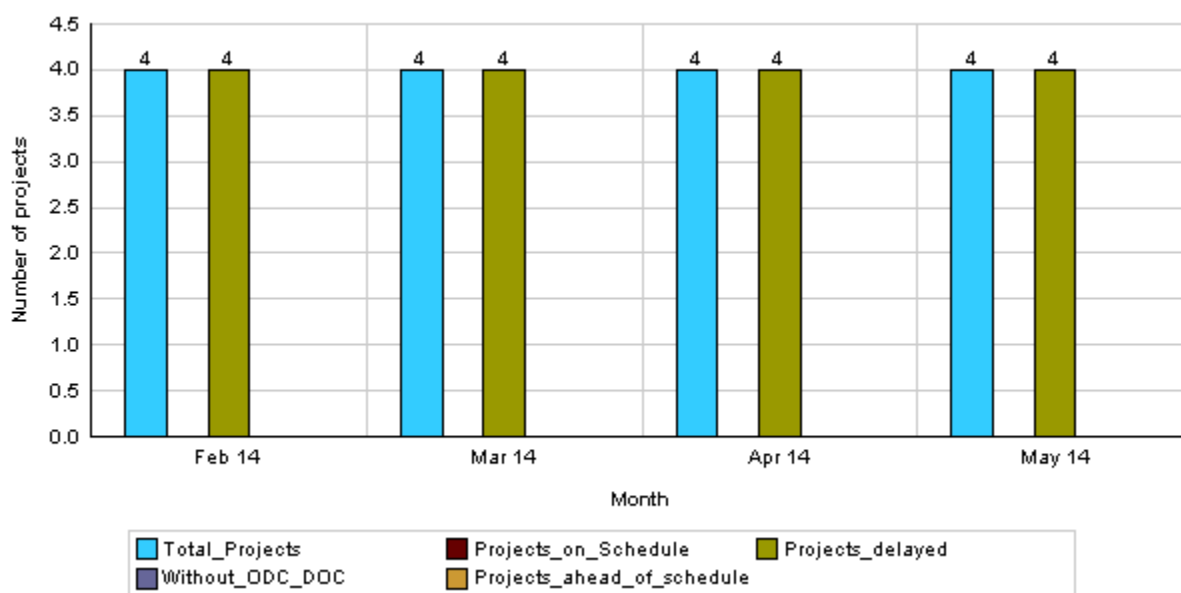

Break-up of 4 Delayed projects in May 2014

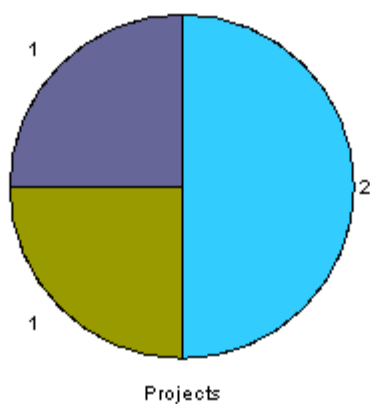

Delay in Months

Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	40,442.00	46,726.00	29,914.17
CIVIL AVIATION	8	6,035.46	6,624.95	6,946.00	5,810.66
COAL	55	38,568.41	48,364.96	48,390.55	18,101.08
STEEL	20	65,959.26	70,209.44	72,188.55	60,193.46
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	7,712.19
PETROLEUM	80	197,630.12	210,325.28	210,187.26	108,138.33
POWER	102	249,361.87	255,362.16	262,250.17	145,051.40
RAILWAYS	291	155,156.87	184,470.57	275,719.17	83,078.94
ROAD TRANSPORT AND HIGHWAYS	138	103,326.71	103,864.96	105,331.49	91,122.81
SHIPPING AND PORTS	19	15,617.12	17,487.95	18,600.58	8,395.88
TELECOMMUNICATIONS	11	5,295.83	5,295.83	5,199.48	1,769.33
URBAN DEVELOPMENT	5	73,993.32	74,052.22	79,266.22	11,652.27
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	735	957,390.48	1,022,503.83	1,140,912.47	570,976.01

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	4,723.00	12/2015 -	11/2016	11(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,626.00	12/2008 -	03/2015	75(O) -	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,564.17	09/2010 -	03/2015	54(O) -	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,001.00	12/2016 -	03/2017	3(O) -	4/69
	Total		40,442.00 -	46,726.00	29,914.17				60/329
	<u>CIVIL AVIATION</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	2,593.13	2,573.92	05/2011 -	03/2013	-	0/2
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	272.79	01/2011 04/2013	12/2016	71(O) 44(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	279.52	05/2012 -	04/2014	-	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	2,015.00	1,939.20	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	261.51	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	483.68	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,946.00	5,810.66				0/2
	<u>COAL</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.88	03/2013 09/2012	03/2015	24(O) 30(R)	19/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	87.18	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	619.15	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	95.88	03/2020 -	03/2020	0(O) -	0/3

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	126.88	03/2012 -	03/2016	48(O) -	4/5
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	99.00	03/2011 -	03/2017	72(O) -	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.41	03/2010 -	03/2016	72(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	57.77	03/2016 -	03/2016	0(O) -	0/6
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017	0(O) -	3/11
23	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	244.00	03/2015 -	03/2015	0(O) -	0/3
24	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	610.33	-	03/2022 -	03/2022	0(O) -	0/0
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	271.88	03/2014 -	03/2016	24(O) -	2/9
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,539.76	03/2014 -	03/2016	24(O) -	6/13
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,535.66	03/2014 -	03/2016	24(O) -	10/16
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.30	03/2015 -	03/2015	0(O) -	1/13
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	120.15	03/2013 -	03/2015	24(O) -	2/7
31	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2015	0(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	35.49	03/2011 -	03/2017	72(O) -	0/2
35	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	102.04	12/2012 -	03/2016	39(O) -	11/44
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.07	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	116.72	03/2013 -	03/2015	24(O) -	3/9
38	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	49.19	03/2014 -	03/2017	36(O) -	0/2
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
40	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	29.25	03/2018 -	03/2018	0(O) -	0/4
41	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	392.24	03/2013 -	03/2014	-	0/2
43	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	118.59	03/2010 -	03/2017	84(O) -	8/10
44	KUMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	754.00	03/2013 03/2023	03/2023	120(O) 0(R)	0/16
45	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44(O) -	0/3
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	209.19	03/2014 -	03/2016	24(O) -	1/6
47	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36(O) -	4/6
48	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
49	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	-	0/0
50	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	341.52	12/2015 -	04/2018	28(O) -	5/33
51	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36(O) -	0/2
52	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	59.49	03/2012 -	03/2017	60(O) -	0/2
53	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	0.46	03/2015 -	03/2015	0(O) -	1/1
54	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.50	03/2014 -	03/2016	24(O) -	0/1
55	PURNADIDH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	121.20	03/2013 -	03/2015	24(O) -	0/3
56	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	33.46	03/2014 -	03/2016	24(O) -	0/2
57	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	221.36	03/2016 -	03/2016	0(O) -	0/2
58	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	226.55	03/2012 -	03/2015	36(O) -	24/27
59	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
60	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.14 -	430.14	65.54	03/2016 -	03/2016	0(O) -	6/48
61	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	5.43	06/2015 -	06/2015	0(O) -	2/51
62	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	95.46	03/2015 -	03/2015	0(O) -	8/31
63	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	70.75	03/2012 -	-	-	24/42
64	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.14	03/2016 -	03/2016	0(O) -	0/12
65	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	139.29	03/2012 -	03/2016	48(O) -	0/2
66	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,991.89	06/2009 -	06/2014	60(O) -	19/23

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,264.42	03/2012 -	08/2014	29(O) -	19/38
	Total		38,568.41 -	48,390.55	18,101.08				207/781
	<u>STEEL</u>								
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	381.69	04/2013 09/2014	09/2014	17(O) 0(R)	17/18
69	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	10.55	05/2016 -	05/2016	0(O) -	0/3
70	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	349.64	260.53	12/2009 08/2010	06/2013	-	1/1
71	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	343.58	294.54	01/2010 02/2011	11/2013	-	3/3
72	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	295.38	05/2013 01/2015	01/2015	20(O) 0(R)	13/20
73	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	311.70	09/2009 05/2012	12/2014	63(O) 31(R)	1/1
74	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	372.46	12/2011 01/2015	01/2015	37(O) 0(R)	15/20
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.73	09/2008 12/2013	06/2014	69(O) 6(R)	3/4
76	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	104.96	08/2014 -	08/2014	0(O) -	1/4
77	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	109.87	11/2013 -	06/2015	19(O) -	1/4
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,803.22	03/2013 -	03/2015	24(O) -	28/35
79	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,673.10	12/2011 -	07/2014	31(O) -	18/24
80	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,191.19	12/2012 -	03/2015	27(O) -	14/20
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,945.82	12/2011 -	07/2014	31(O) -	22/29
82	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,855.72	10/2009 10/2012	09/2014	59(O) 23(R)	66/67
83	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	11,151.97	03/2013 -	09/2014	18(O) -	16/20
84	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	126.81	10/2013 -	08/2014	10(O) -	1/5
85	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014	0(O) -	0/2
86	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	339.35	87.72	06/2015 -	06/2015	0(O) -	1/3
87	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	254.90	36.64	12/2014 -	12/2014	0(O) -	0/2

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		65,959.26 -	72,188.55	60,193.46				221/285
	<u>PETROCHEMICALS</u>								
88	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 -	8,920.00	7,712.19	04/2012 -	-	-	22/29
	Total		5,460.61 -	8,920.00	7,712.19				22/29
	<u>PETROLEUM</u>								
89	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 -	678.02	113.00	06/2012 -	07/2014	25(O) -	0/3
90	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	2,182.31	06/2012 -	06/2014	24(O) -	0/0
91	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE	03/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018	0(O) -	0/0
92	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24(O) -	0/0
93	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24(O) -	0/0
94	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24(O) 12(R)	0/5
95	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL, MULTI STATE	08/2011	586.00 -	586.00	171.74	08/2015 -	08/2015	0(O) -	0/12
96	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, MULTI STATE	12/2009	540.92 -	540.92	338.32	07/2012 07/2012	-	-	6/7
97	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 -	204.29	151.39	06/2012 -	06/2014	24(O) -	0/0
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	449.94	09/2011 -	12/2015	51(O) -	0/0
99	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	169.76	08/2013 -	09/2014	13(O) -	0/5
100	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	302.26 -	240.95	102.80	09/2012 -	12/2014	27(O) -	0/0
101	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC, MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
102	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC, GUJARAT	03/2009	234.78 234.78	317.64	102.78	09/2012 -	12/2014	27(O) -	0/5
103	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 -	761.68	589.37	05/2013 06/2014	03/2015	22(O) 9(R)	0/5
104	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL, MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54(O) -	0/0
105	DE-BOTTLENECKING OF SMPL - [N16000089]OCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	901.48	- -	08/2015	- -	0/12
106	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,728.25	04/2006 06/2012	06/2015	110(O) 36(R)	0/0
107	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,855.00	08/2010 03/2012	05/2015	57(O) 38(R)	0/10

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
109	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,165.53	07/2010 05/2012	05/2014	46(O) 24(R)	0/0
110	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	282.02	05/2014 -	05/2015	12(O) -	0/9
111	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	3,068.29	12/2008 04/2013	05/2015	77(O) 25(R)	0/0
112	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
113	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 -	04/2015	0(O) -	0/0
114	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	248.39	12/2014 -	12/2014	0(O) -	0/8
115	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,011.64	01/2014 -	12/2015	23(O) -	0/9
116	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	10/2014	0(O) -	0/0
117	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,881.89	09/2011 05/2012	12/2014	39(O) 31(R)	6/76
118	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	07/2014	34(O) 28(R)	56/59
119	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	42.23	09/2017 -	09/2017	0(O) -	0/0
120	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	2.80	- -	-	-	0/0
121	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	08/2014	34(O) -	0/9
122	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	2,468.61	05/2015 -	05/2015	0(O) -	0/17
123	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	1.30	07/2016 -	07/2016	0(O) -	0/0
124	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	595.34	03/2015 -	03/2015	0(O) -	0/12
125	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0
126	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016	0(O) -	0/0
127	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	2,261.15	12/2015 -	05/2016	5(O) -	0/0
128	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	90.83	03/2014 -	03/2015	12(O) -	0/5
129	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0
130	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	312.00	286.76	01/2012 -	07/2013	-	0/1
132	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,400.03	12/2012 -	-	-	0/14
133	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.26	130.05	03/2015 -	03/2015	0(O) -	0/64
134	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	20.38	01/2016 -	12/2015	-1(O) -	0/0
135	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	11/2012	666.00 701.00	701.00	202.33	11/2015 -	11/2015	0(O) -	18/29
136	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	136.46	06/2014 -	12/2014	6(O) -	0/0
137	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23(O) -	0/0
138	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	74.55	12/2014 -	12/2014	0(O) -	0/0
139	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	11,398.28	01/2012 -	09/2014	32(O) -	0/108
140	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,719.76	09/2012 -	04/2014	-	0/0
141	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,920.81	05/2010 03/2013	04/2014	-	0/0
142	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
143	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	189.66	07/2015 -	12/2015	5(O) -	0/0
144	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	25,767.00	11/2012 11/2013	12/2014	25(O) 13(R)	72/100
145	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	983.27	09/2012 -	08/2015	35(O) -	6/7
146	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,603.47	02/2014 -	08/2014	6(O) -	0/0
147	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	256.97	04/2012 -	06/2014	26(O) -	0/0
148	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	33.26	07/2016 -	07/2016	0(O) -	0/5
149	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,151.22	05/2014 -	05/2015	12(O) -	0/5
150	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017	0(O) -	0/0
151	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	963.62	07/2012 -	06/2014	23(O) -	0/31
152	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	11/2015	11(O) -	0/0
153	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	686.58	72.73	04/2015 -	04/2015	0(O) -	0/0
154	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	560.47	12/2014 -	03/2015	3(O) -	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
155	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	-	02/2016 -	02/2016	0(O) -	0/0
156	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	-	11/2015 -	11/2015	0(O) -	0/0
157	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,910.30	-	05/2016 -	05/2016	0(O) -	0/0
158	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	551.29	11/2015 -	11/2015	0(O) -	13/25
159	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	648.92	04/2012 -	12/2013	-	0/0
160	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	856.67	10/2011 -	06/2015	44(O) -	0/0
161	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,242.78	01/2012 -	06/2015	41(O) -	0/0
162	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	963.51	10/2011 -	02/2015	40(O) -	0/0
163	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	-	04/2015	-	0/0
164	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	06/2014	22(O) -	0/5
165	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	14.98	03/2015 -	03/2015	0(O) -	0/5
166	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.83	10/2014 -	10/2015	12(O) -	0/0
167	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.55	03/2012 -	03/2015	36(O) -	13/20
168	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	531.34	12/2013 -	09/2015	21(O) -	0/0
	Total		197,630.12 -	210,187.26	108,138.33				190/697
	<u>POWER</u>								
169	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,344.56	08/2012 -	06/2014	22(O) -	0/11
170	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	187.77	-	-	-	1/17
171	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	03/2016	0(O) -	0/0
172	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	43.56	10/2014 -	10/2014	0(O) -	0/7
173	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	7,590.00	08/2013 -	03/2015	19(O) -	15/20
174	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	10,036.00	12/2009 -	03/2017	87(O) -	20/46
175	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,540.00	07/2011 -	08/2016	61(O) -	6/34

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
176	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	133.05	12/2015 -	12/2015	0(O) -	2/20
177	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,325.76	09/2014 -	12/2014	3(O) -	7/20
178	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	482.33	06/2015 -	06/2015	0(O) -	0/0
179	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	1,398.65	08/2014 -	08/2014	0(O) -	7/20
180	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.17	06/2014 -	06/2014	0(O) -	0/20
181	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
182	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	13.93	10/2014 -	10/2014	0(O) -	2/2
183	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	836.13	11/2012 -	06/2015	31(O) -	2/13
184	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	14.64	05/2016 -	04/2016	-1(O) -	0/0
185	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
186	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
187	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,434.25	05/2014 -	09/2014	4(O) -	2/8
188	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,243.00	09/2017 -	09/2017	0(O) -	10/39
189	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	648.10	08/2014 -	08/2014	0(O) -	1/15
190	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	-	07/2016 -	07/2016	0(O) -	0/0
191	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,380.35	12/2013 -	11/2014	11(O) -	2/7
192	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	53.87	11/2016 -	03/2016	-8(O) -	0/0
193	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	1,007.16	941.71	12/2007 12/2009	-	-	2/11

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
194	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,940.49	12/2009 06/2016	03/2017	87(O) 9(R)	11/27
195	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.04	3,403.83	01/2016 -	11/2016	10(O) -	1/6
196	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	5,915.00	04/2009 -	05/2015	73(O) -	2/9
197	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	4,381.00	12/2016 -	12/2016	0(O) -	14/23
198	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,877.65	09/2008 -	03/2013	-	15/23
199	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,644.00	05/2017 -	05/2017	0(O) -	6/37
200	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	128.00	08/2017 -	08/2017	0(O) -	0/9
201	MOUDA STPP - [N18000048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
202	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	2,588.00	09/2016 -	09/2016	0(O) -	18/23
203	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	8,436.00	08/2013 -	06/2015	22(O) -	0/16
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	383.12	07/2013 -	03/2015	20(O) -	2/11
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	282.27	02/2012 -	12/2013	-	1/13
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	400.96	11/2011 -	-	-	2/14
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	-	06/2016 -	06/2016	0(O) -	0/0
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,037.82	04/2013 -	12/2014	20(O) -	0/11
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	333.92	11/2014 -	11/2014	0(O) -	2/12
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	34.59	03/2016 -	03/2016	0(O) -	0/0
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	265.19	03/2015 -	03/2015	0(O) -	4/15
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	105.70	04/2015 -	05/2015	1(O) -	0/16
214	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	667.64	11/2012 -	06/2014	19(O) -	0/11
215	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	3,919.59	4,474.99	09/2009 -	07/2018	106(O) -	1/12
216	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	840.66	08/2013 09/2015	09/2015	25(O) 0(R)	19/37
217	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	3,134.02	01/2012 -	-	-	19/28
218	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	6,230.81	4,357.00	10/2012 -	10/2013	-	16/16

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
219	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	2,612.00	11/2016 -	11/2016	0(O) -	14/17
220	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	09/2016 -	09/2016	0(O) -	0/0
221	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	0/0
222	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,858.57	09/2010 -	12/2018	99(O) -	0/0
223	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	2,120.41	08/2012 -	09/2014	25(O) -	1/5
224	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	311.88	06/2016 -	12/2015	-6(O) -	0/20
225	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	185.19	06/2012 -	06/2014	24(O) -	0/3
226	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	716.98	12/2014 -	11/2014	-1(O) -	2/2
227	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	129.24	03/2014 -	08/2014	5(O) -	3/7
228	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	407.83	08/2014 -	05/2015	9(O) -	2/18
229	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	989.09	08/2012 -	12/2014	28(O) -	0/11
230	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	-	08/2014 -	08/2016	24(O) -	0/0
231	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	771.13	02/2015 -	02/2015	0(O) -	1/14
232	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	656.08	11/2014 -	11/2014	0(O) -	0/16
233	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	684.82	01/2015 -	01/2015	0(O) -	4/19
234	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	224.27	08/2014 -	08/2014	0(O) -	7/20
235	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	287.52	06/2014 -	09/2014	3(O) -	8/20
236	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,121.00	03/2013 -	03/2017	48(O) -	0/14
237	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,061.38	1,502.70	09/2009 -	03/2016	78(O) -	1/5
238	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	712.67	07/2010 02/2016	02/2017	79(O) 12(R)	1/15
239	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	160.62	01/2014 -	09/2014	8(O) -	3/15
240	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,026.16	08/2014 -	06/2015	10(O) -	2/19

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
241	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,543.91	10/2014 -	06/2015	8(O) -	3/18
242	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,888.78	10/2012 -	03/2015	29(O) -	0/11
243	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	31(O) -	0/4
244	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	- -	-	-	0/0
245	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,739.80	12/2012 -	06/2015	30(O) -	0/11
246	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	-	- -	-	-	0/0
247	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	489.75	01/2015 -	12/2015	11(O) -	2/20
248	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,MULTI STATE	02/2012	324.33 -	324.33	186.56	08/2014 -	08/2014	0(O) -	9/20
249	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	-	10/2016 -	10/2016	0(O) -	0/0
250	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,054.17	10/2014 -	10/2014	0(O) -	3/16
251	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	71.10	05/2016 -	05/2016	0(O) -	0/0
252	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	412.30	02/2014 -	03/2015	13(O) -	5/17
253	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	376.82	10/2013 -	08/2014	10(O) -	1/8
254	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	996.76	12/2013 -	06/2014	6(O) -	4/13
255	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	287.31	11/2013 -	03/2015	16(O) -	7/20
256	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,544.34	03/2013 -	09/2014	18(O) -	5/15
257	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,436.07	03/2014 -	12/2014	9(O) -	5/15
258	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,122.08	12/2013 -	12/2014	12(O) -	2/8
259	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	68.80	01/2013 -	06/2015	29(O) -	5/18

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
260	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,220.26	11/2013 -	06/2015	19(O) -	5/16
261	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,088.37	11/2012 -	03/2015	28(O) -	0/13
262	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,853.33	07/2014 -	12/2014	5(O) -	3/14
263	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	951.48	765.07	07/2013 -	11/2014	16(O) -	19/25
264	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	368.72 -	913.63	601.12	07/2006 12/2015	12/2015	113(O) 0(R)	2/14
265	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
266	VINDHYACHAL STTP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	1,013.00	08/2015 -	08/2015	0(O) -	2/18
267	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	0/15
268	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	485.66	07/2014 -	07/2018	48(O) -	1/1
269	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	483.89	09/2010 -	06/2014	45(O) -	0/5
270	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,902.59	06/2015 -	12/2015	6(O) -	3/27
	Total		249,361.87 -	262,250.17	145,051.40				363/1297
	<u>RAILWAYS</u>								
271	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	17.40	04/2012 -	03/2016	47(O) -	0/0
272	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	184.06	2.77	- -	-	-	0/0
273	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	609.11	03/2014 -	03/2017	36(O) -	0/0
274	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
275	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	403.29	12/2009 03/2011	12/2014	60(O) 45(R)	0/0
276	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	2.00	- -	-	-	0/0
277	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	62.06	03/2013 -	03/2013	-	0/0
278	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	308.52	- -	-	-	0/0
279	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	20.99	- -	-	-	0/0
280	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
281	AKKANAPET-MEDAK - [N22000285]SCOR,TELANGANA	04/2012	153.00 -	153.00	-	- -	-	-	0/0
282	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
283	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	485.00	417.14	03/2011 03/2011	03/2011	-	0/0
284	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
285	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	108.57	- -	-	-	0/0
286	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	82.60	- -	03/2016	- -	0/0
287	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	725.00	573.40	06/1999 03/2011	03/2011	-	0/0
288	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.78	- -	-	-	0/0
289	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
290	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
291	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
292	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
293	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.95	- -	-	-	0/0
294	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	199.75	50.21	- -	-	-	0/0
295	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	46.13	- -	-	-	0/0
296	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	7.52	- -	-	-	0/0
297	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	199.88	12/2012 -	12/2014	24(O) -	0/0
298	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	1,382.78	1.65	- -	-	-	0/0
299	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	1.76	- -	-	-	0/0
300	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	480.78	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
301	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	245.15 1,106.62	1,106.62	235.15	12/2010 03/2011	03/2011	-	0/0
302	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	11.72	- -	-	-	0/0
303	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
304	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.10	376.57	03/2004 12/2010	12/2014	129(O) 48(R)	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
305	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	337.50	0.21	- -	-	-	0/0
306	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	923.23	-	- -	-	-	0/0
307	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	858.67	0.66	- -	-	-	0/0
308	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
309	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	174.83	04/2014 -	03/2017	35(O) -	0/0
310	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.79	- -	-	-	0/0
311	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.27	03/2011 -	-	-	0/0
312	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	80.29	- -	-	-	0/0
313	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	795.45	03/2010 -	12/2015	69(O) -	0/0
314	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	484.61	2.12	03/2012 -	-	-	0/0
315	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
316	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.28	- -	-	-	0/0
317	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	267.37	34.02	- -	-	-	0/0
318	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	3,160.19	04/2008 03/2014	12/2017	116(O) 45(R)	0/0
319	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
320	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	58.81	03/2015 -	12/2015	9(O) -	0/0
321	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.17	- -	-	-	0/0
322	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	60.79	- -	-	-	0/0
323	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	562.37	- -	12/2014	- -	0/0
324	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0
325	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	462.05	- -	-	-	0/0
326	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.03	- -	-	-	0/0
327	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	494.92	3.62	- -	-	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
328	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]JECOR,BIHAR	04/2006	285.07 -	378.56	106.98	- -	-	-	0/0
329	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
330	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
331	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.13	- -	-	-	0/0
332	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	0.10	- -	-	-	0/0
333	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	0.10	- -	-	-	0/0
334	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]JER,MULTI STATE	04/2005	595.91 -	595.91	88.27	- -	-	-	0/0
335	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	149.26	- -	-	-	0/0
336	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
337	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	407.98	416.11	- -	03/2014	-	0/0
338	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	959.83	03/2007 -	03/2017	120(O) -	0/0
339	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	267.50	- -	-	-	0/0
340	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
341	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	163.16	- -	-	-	0/0
342	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]JER, WEST BENGAL	04/2009	259.51 533.38	533.38	110.70	12/2011 02/2012	02/2012	-	0/0
343	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	138.39	12/2012 -	-	-	0/0
344	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	388.67	83.91	12/2015 -	03/2016	3(O) -	0/0
345	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]JECR,BIHAR	04/2001	104.79 -	406.92	148.85	- -	-	-	0/0
346	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]JER,MULTI STATE	04/2010	296.44 -	296.44	3.92	- -	-	-	0/0
347	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]JECR,BIHAR	04/2005	366.73 -	205.00	5.20	- -	-	-	0/0
348	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	247.48	- -	03/2014	-	0/0
349	DELANG-PURI DOUBLING - [N22000320]JECOR,ODISHA	03/2011	165.16 -	165.16	79.06	03/2015 -	03/2015	0(O) -	0/0
350	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
351	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	142.99	- -	-	-	0/0
352	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	607.09	546.20	12/2012 12/2012	02/2013	-	0/0
353	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	2.00	- -	-	-	0/0
354	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	2.43	02/2019 -	02/2019	0(O) -	0/0
355	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	651.17	7.22	- -	-	-	0/0
356	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
357	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	914.98	766.03	- -	12/2012	-	0/0
358	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	100.00	03/2016 -	03/2016	0(O) -	0/0
359	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	10/2014	31(O) 10(R)	0/0
360	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
361	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
362	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	227.22	12/2008 -	09/2014	69(O) -	0/0
363	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	267.13	06/2013 06/2013	03/2015	21(O) 21(R)	0/0
364	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
365	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240(O) -	0/0
366	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	0.10	- -	-	-	0/0
367	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	294.43	02/2011 02/2011	03/2013	-	0/0
368	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.88	- -	-	-	0/0
369	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
370	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 -	611.03	138.80	12/2011 11/2013	11/2013	-	0/0
371	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 -	261.70	79.25	02/2006 -	-	-	0/0
372	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	863.23	823.02	- -	03/2012	-	0/0
373	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
374	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	52.17	- -	-	-	0/0
375	GUDUR-DURGARAJAPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0
376	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	459.37	- 05/2009	05/2009	-	0/0
377	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	586.81	03/1994 -	09/2014	246(O) -	0/0
378	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	9.29	- -	-	-	0/0
379	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.92	02/2020 -	02/2020	0(O) -	0/0
380	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
381	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	213.01	-	- -	-	-	0/0
382	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	324.66	197.39	- -	-	-	0/0
383	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.51	- -	-	-	0/0
384	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.80	- -	-	-	0/0
385	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	295.52	- 09/2009	-	-	0/0
386	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	-	- -	-	-	0/0
387	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
388	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	887.59	- -	01/2013	-	0/0
389	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	158.51	- -	03/2014	-	0/0
390	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	60.70	03/2015 -	03/2015	0(O) -	0/0
391	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
392	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	46.57	- -	-	-	0/0
393	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	41.67	- -	-	-	0/0
394	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	445.40	180.41	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
395	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
396	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	110.07	- -	-	-	0/0
397	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	185.24	01/1999 -	-	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
398	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	653.46	236.09	03/2014 -	03/2014	-	0/0
399	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	140.57	- -	-	-	0/0
400	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	838.17	06/2007 -	06/2007	-	0/0
401	JAYANAGAR-DARBHANGA-MARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	1,043.56	734.77	03/2012 08/2012	-	-	0/0
402	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	14.00	- -	-	-	0/0
403	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	201.00	-	- -	-	-	0/0
404	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	740.00	554.48	03/2012 03/2012	12/2012	-	0/0
405	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	2,216.69	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
406	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCOR,MULTI STATE	04/2008	2,050.00 -	2,050.00	178.72	- -	12/2014	- -	0/0
407	KAKINADA-PITHAPURAM - [N22000314]SECR,ANDHRA PRADESH	03/1999	215.06 -	215.06	0.01	- -	-	-	0/0
408	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	205.08	- -	-	-	0/0
409	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	53.59	- -	-	-	0/0
410	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	3.71	- -	-	-	0/0
411	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	1,708.41	1,576.77	- -	03/2015	- -	0/0
412	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
413	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	534.94	- -	03/2014	-	1/1
414	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	800.00	776.13	- -	10/2012	-	0/0
415	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	140.02	12/2012 -	03/2016	39(O) -	0/0
416	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	1,022.64	742.61	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
417	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	177.23	03/2017 -	03/2017	0(O) -	0/0
418	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	1,054.35	0.63	- -	-	-	0/0
419	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 162.87	162.87	127.64	- -	-	-	0/0
420	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	279.04	03/2009 03/2009	08/2014	65(O) 65(R)	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
421	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 470.21	1,995.25	307.01	- -	12/2014	- -	0/0
422	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	826.57	30.63	- -	-	-	0/0
423	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	2.22	- -	03/2015	- -	0/0
424	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	768.87	547.12	- 03/2010	03/2010	-	0/0
425	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	2,957.21	1,803.36	07/2005 -	-	-	0/0
426	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	418.17	224.29	- -	-	-	0/0
427	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
428	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	341.41	295.38	03/2012 03/2013	03/2013	-	0/0
429	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	1,045.20	0.03	- -	-	-	0/0
430	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
431	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
432	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
433	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	406.99	141.02	- -	-	-	0/0
434	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	925.00 -	1,630.97	434.20	05/2008 03/2011	-	-	0/0
435	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	68.98	03/2014 -	03/2014	-	0/0
436	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	364.06	0.30	- -	-	-	0/0
437	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,185.44	4,253.73	03/2009 -	03/2017	96(O) -	0/0
438	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	0.92	07/2008 -	07/2008	-	0/0
439	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	12.90	- -	-	-	0/0
440	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.52	- -	-	-	0/0
441	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	119.42	- -	-	-	0/0
442	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	472.00	194.49	- -	02/2013	-	0/0
443	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	900.05	820.52	12/2011 12/2011	03/2013	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
444	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 671.82	791.59	1.23	- -	-	-	0/0
445	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.35	- -	03/2016	- -	0/0
446	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	97.81	- -	-	-	0/0
447	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	477.88	454.47	03/2012 03/2013	03/2013	-	0/0
448	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
449	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	1.08	01/1999 -	-	-	0/0
450	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.65	- -	-	-	0/0
451	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	1,383.45	415.36	- -	-	-	0/0
452	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	0.84	- -	-	-	0/0
453	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
454	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	466.48	0.25	01/1999 -	-	-	0/0
455	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
456	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	-	- -	-	-	0/0
457	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
458	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	390.60	2.11	- -	-	-	0/0
459	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	7,952.58	1,739.04	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
460	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	284.45	- -	03/2014	-	0/0
461	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	259.46	- -	-	-	0/0
462	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	545.64	0.50	- -	-	-	0/0
463	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
464	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	0.02	- -	-	-	0/0
465	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	169.82	24.33	- -	-	-	0/0
466	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	1.02	- -	-	-	0/0
467	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	883.00	689.92	02/2009 -	03/2012	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
468	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	1,036.78	384.94	07/2012 -	-	-	0/0
469	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
470	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
471	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	532.87	48.93	- -	-	-	0/0
472	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	185.79	- -	03/2018	- -	0/0
473	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	242.22	36.18	- -	-	-	0/0
474	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	4,083.02	4.07	- -	-	-	0/0
475	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	230.67	- -	03/2014	-	0/0
476	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	03/2016	- -	0/0
477	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	221.42	22.39	- -	-	-	0/0
478	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.18	254.13	- -	03/2015	- -	0/0
479	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
480	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	45.90	- -	03/2017	- -	0/0
481	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	5.02	- -	03/2017	- -	0/0
482	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	1,418.21	1,039.78	- -	-	-	0/0
483	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	9.23	03/2015 -	03/2017	24(O) -	0/0
484	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,581.17	12/2008 -	03/2017	99(O) -	0/0
485	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	64.64	03/2014 -	03/2016	24(O) -	0/0
486	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.51	422.20	03/2016 -	03/2016	0(O) -	0/0
487	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	84.44	03/2016 -	06/2016	3(O) -	0/0

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
488	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,951.98	398.46	03/2016 -	03/2016	0(O) -	0/0
489	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	425.14	03/2008 06/2008	-	-	0/0
490	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
491	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	293.74	139.18	12/2010 12/2010	12/2010	-	0/0
492	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	191.00 -	260.16	222.52	- -	05/2014	- -	0/0
493	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 2,921.00	2,921.00	2,116.80	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
494	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 495.68	925.30	688.63	- -	02/2014	-	0/0
495	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	203.00 -	203.00	195.76	- -	03/2014	-	0/0
496	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	15.73	- -	-	-	0/0
497	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
498	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	16.58	03/2015 -	03/2015	0(O) -	0/0
499	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
500	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
501	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
502	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
503	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	1,122.00	840.85	- -	03/2013	-	0/6
504	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	279.63	12/2007 03/2010	-	-	0/0
505	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 2,363.00	2,363.00	1,371.16	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
506	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	307.18	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
507	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	913.48	462.18	- -	-	-	0/0
508	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	874.57	562.62	03/2013 -	03/2014	-	0/0
509	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	238.69	- -	-	-	0/0
510	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 194.07	596.40	378.37	06/2004 -	06/2015	132(O) -	0/0
511	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR, ASSAM	01/2004	915.70 915.70	3,019.17	2,791.02	- -	03/2015	- -	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.12	- -	-	-	0/0
513	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	788.27	- -	-	-	0/0
514	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	25.53	- -	-	-	0/0
515	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	398.78	03/2012 -	-	-	0/0
516	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	273.30	- -	-	-	0/0
517	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	755.54	2.83	- -	-	-	0/0
518	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	28.86	- 12/2017	12/2017	- 0(R)	0/0
519	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	17.98	- -	-	-	0/0
520	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	243.91	- -	-	-	0/0
521	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	340.57	- -	-	-	0/0
522	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	234.09	03/2010 -	-	-	0/0
523	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	14.00	- -	-	-	0/0
524	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	14.73	- -	-	-	0/0
525	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
526	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	85.23	12/2015 -	03/2017	15(O) -	0/0
527	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	1.06	- -	-	-	0/0
528	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.47	- -	-	-	0/0
529	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.81	- -	-	-	0/0
530	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	61.30	- -	-	-	0/0
531	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	0.10	- -	-	-	0/0
532	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	839.00	0.01	- -	-	-	0/0
533	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	114.40	02/2015 -	02/2015	0(O) -	0/0
534	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.47	- -	-	-	0/0

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
535	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	499.05	03/2014 -	03/2014	-	0/0
536	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	810.78	133.63	- -	-	-	0/0
537	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	457.17	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
538	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	141.84	06/2013 -	12/2014	18(O) -	0/0
539	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.30	- -	-	-	0/0
540	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	157.96 1,188.91	1,188.91	678.25	- 12/2009	02/2012	-	0/0
541	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	236.93	-	- -	-	-	0/0
542	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	820.00	190.83	- -	-	-	0/0
543	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	420.00	60.46	- -	-	-	0/0
544	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	90.18	03/2012 -	-	-	0/0
545	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	900.00	571.02	- -	-	-	0/0
546	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	3,176.10	3,503.29	12/2006 08/2010	08/2010	-	0/0
547	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	1.02	- -	-	-	0/0
548	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.27	- -	-	-	0/0
549	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181(O) -	0/0
550	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	767.25	03/2014 -	03/2014	-	0/0
551	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.29	- -	-	-	0/0
552	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,116.53	302.32	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
553	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]SCR,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	- -	-	-	0/0
554	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
555	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	200.42	- 03/2010	-	-	0/0
556	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	116.06	- -	-	-	0/0
557	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	198.28	- -	04/2014	-	0/0
558	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	2,501.05	70.75	- -	-	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
559	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	5.25	- -	-	-	0/0
560	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	1.05	- -	-	-	0/0
561	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		155,156.87 -	275,719.17	83,078.94				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
562	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	346.20	08/2013 -	02/2015	18(O) -	0/0
563	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
564	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	351.20	10/2014 -	10/2014	0(O) -	0/0
565	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	263.80	07/2014 -	07/2014	0(O) -	0/0
566	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.20	05/2013 -	05/2013	-	0/0
567	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,177.00	11/2013 -	09/2014	10(O) -	0/0
568	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	433.30	04/2014 -	09/2014	5(O) -	0/0
569	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,293.00	10/2014 -	10/2014	0(O) -	0/0
570	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	50.28	07/2014 -	07/2014	0(O) -	0/0
571	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	136.20	01/2014 -	12/2015	23(O) -	0/0
572	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
573	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	700.20	02/2014 -	02/2014	-	0/0
574	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	314.60	04/2014 -	03/2014	-	0/0
575	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	170.70	05/2014 -	05/2014	0(O) -	0/0
576	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	683.20	09/2014 -	03/2015	6(O) -	0/3
577	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,660.00	08/2014 -	07/2015	11(O) -	0/0
578	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,379.00	06/2013 -	06/2013	-	0/3
579	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	12/2016	39(O) -	0/0
580	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	929.60	08/2013 -	08/2013	-	0/3

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
581	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
582	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	457.60	02/2014 -	09/2015	19(O) -	0/0
583	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,524.00	08/2013 -	12/2014	16(O) -	0/0
584	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,611.00	08/2013 -	06/2015	22(O) -	0/0
585	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	325.10	08/2013 -	12/2015	28(O) -	0/0
586	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	190.00	10/2015 -	10/2015	0(O) -	0/0
587	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.60	07/2013 -	03/2015	20(O) -	0/0
588	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,660.00	09/2014 -	09/2014	0(O) -	0/0
589	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	282.50	09/2007 07/2011	06/2015	93(O) 47(R)	0/0
590	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	104.80	12/2015 -	12/2015	0(O) -	0/3
591	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,184.00	11/2012 -	08/2014	21(O) -	0/0
592	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
593	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	375.40	09/2013 -	12/2015	27(O) -	0/0
594	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12(O) -	0/0
595	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,097.00	06/2014 -	06/2014	0(O) -	0/0
596	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	656.70	- -	07/2014	- -	2/2
597	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35(O) -	0/0
598	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19(O) -	0/0
599	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	309.20	06/2008 -	03/2015	81(O) -	0/0
600	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	267.00	06/2008 -	03/2015	81(O) -	0/0
601	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.40	06/2005 -	06/2015	120(O) -	0/0
602	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	217.61	438.80	04/2010 01/2016	03/2015	59(O) -10(R)	0/0
603	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	06/2016	76(O) -	0/0
604	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	886.70	03/2013 -	12/2014	21(O) -	0/0
605	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38(O) -	0/0
606	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
607	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,KARNATAKA	03/2011	839.00 -	839.00	692.50	- -	06/2014	- -	0/1
608	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	12/2014	19(O) -	0/0
609	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
610	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	481.30	04/2015 -	04/2015	0(O) -	0/0
611	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.90	05/2010 -	12/2014	55(O) -	0/0
612	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	726.30	07/2013 -	08/2014	13(O) -	0/0
613	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	06/2014	12(O) -	0/0
614	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	775.10	- -	05/2013	-	1/1
615	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	268.70	06/2008 -	06/2014	72(O) -	0/0
616	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.20	05/2008 01/2015	10/2014	77(O) -3(R)	0/0
617	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	309.10	09/2010 -	08/2014	47(O) -	0/0
618	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	808.10	09/2015 -	09/2015	0(O) -	0/0
619	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	519.40	09/2008 -	12/2014	75(O) -	0/0
620	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	262.40	11/2016 -	11/2016	0(O) -	0/0
621	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	467.70	08/2015 -	08/2015	0(O) -	0/0
622	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	562.50	10/2013 -	11/2015	25(O) -	0/0
623	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	171.80	09/2008 -	12/2014	75(O) -	0/0
624	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	2,024.00	08/2013 06/2014	09/2014	13(O) 3(R)	0/0
625	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,398.00	09/2012 -	12/2014	27(O) -	2/3
626	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	318.50	04/2008 01/2015	10/2014	78(O) -3(R)	0/0
627	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	266.30	04/2008 01/2015	12/2014	80(O) -1(R)	0/0
628	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72(O) -	0/0
629	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	280.00	354.10	02/2009 -	12/2014	70(O) -	0/0
630	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	227.00	07/2009 -	12/2014	65(O) -	0/0

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
631	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 333.83	386.10	123.00	09/2007 -	03/2015	90(O) -	0/0
632	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	310.20	10/2013 -	12/2015	26(O) -	0/0
633	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	01/2013	-	0/0
634	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
635	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	598.40	05/2013 -	12/2015	31(O) -	0/0
636	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20(O) -	0/0
637	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	693.90	02/2013 -	02/2013	-	0/0
638	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,981.00	12/2012 -	12/2012	-	0/0
639	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,092.00	07/2013 -	06/2014	11(O) -	0/0
640	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	664.90	01/2014 -	12/2014	11(O) -	0/0
641	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	856.70	07/2013 -	11/2014	16(O) -	0/0
642	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	07/2014	26(O) -	0/0
643	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	284.10	10/2008 -	06/2014	68(O) -	0/0
644	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	682.00	07/2014 -	12/2015	17(O) -	0/0
645	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	1,111.00	- -	06/2015	- -	2/3
646	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	567.10	07/2012 -	07/2014	24(O) -	0/0
647	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 241.28	280.13	167.20	11/2008 12/2014	09/2014	70(O) -3(R)	0/0
648	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	127.10	04/2009 12/2014	03/2015	71(O) 3(R)	0/0
649	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 167.64	167.64	114.30	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
650	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 200.00	200.00	195.10	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
651	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,244.00	06/2013 -	03/2015	21(O) -	0/0
652	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	589.90	03/2013 -	12/2015	33(O) -	0/0
653	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	311.60	06/2008 -	06/2014	72(O) -	0/0
654	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	284.80	10/2014 -	10/2014	0(O) -	0/0
655	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	320.20	04/2008 01/2015	12/2014	80(O) -1(R)	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
656	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	275.60	06/2008 09/2014	09/2014	75(O) 0(R)	0/0
657	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
658	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	512.90	06/2015 -	05/2016	11(O) -	0/0
659	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	541.90	09/2013 -	09/2013	-	0/0
660	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,118.00	02/2010 -	12/2014	58(O) -	0/0
661	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O) -	0/0
662	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	701.80	09/2014 -	10/2015	13(O) -	0/0
663	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40(O) -	0/0
664	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	0(O) -	0/0
665	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	285.80	06/2014 -	12/2015	18(O) -	0/0
666	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	888.30	03/2014 -	08/2014	5(O) -	0/0
667	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	12/2014	22(O) -	0/0
668	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,341.00	07/2012 -	07/2012	-	0/0
669	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,207.00	03/2013 -	12/2014	21(O) -	0/0
670	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	471.40	01/2014 -	08/2014	7(O) -	0/0
671	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	03/2012	-	0/0
672	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,136.00	07/2015 -	06/2016	11(O) -	0/0
673	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	372.40	10/2008 -	12/2014	74(O) -	0/0
674	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	336.60	06/2015 -	06/2015	0(O) -	0/0
675	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	266.40	09/2014 -	09/2014	0(O) -	0/0
676	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,161.00	11/2013 -	11/2013	-	0/0
677	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	813.40	03/2013 -	12/2014	21(O) -	0/0
678	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	963.00	05/2014 -	09/2014	4(O) -	0/0
679	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	157.47	262.30	09/2007 03/2014	12/2014	87(O) 9(R)	0/0
680	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
681	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	268.50	06/2014 -	06/2014	0(O) -	0/0
682	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	09/2014	9(O) -	0/0
683	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,281.00	12/2013 -	09/2014	9(O) -	0/0
684	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.00	05/2014 -	05/2015	12(O) -	0/0
685	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	155.50	08/2012 -	03/2016	43(O) -	0/0
686	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	06/2014	75(O) -7(R)	0/0
687	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	12/2014	6(O) -	0/0
688	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	06/2014	34(O) -	2/2
689	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,376.00	11/2013 -	11/2013	-	0/0
690	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11(O) -	0/0
691	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	146.40	05/2013 -	12/2014	19(O) -	0/0
692	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	382.60	-	06/2014	-	2/2
693	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,042.00	03/2014 -	12/2015	21(O) -	0/0
694	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	193.10	200.40	03/2008 -	02/2008	-	0/0
695	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	-	-	-	0/0
696	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	63.78	11/2012 -	12/2014	25(O) -	0/0
697	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015	0(O) -	0/0
698	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	-	-	-	0/0
699	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		103,326.71 -	105,331.49	91,122.81				14/29
	<u>SHIPPING AND PORTS</u>								
700	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	211.30	04/2011 11/2011	11/2011	-	0/0

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
701	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
702	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	47.32	01/2013 06/2013	06/2013	-	0/0
703	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
704	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	81.40	12/2011 10/2012	10/2012	-	0/0
705	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 04/2014	04/2014	-	0/0
706	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0
707	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,005.88	12/2010 09/2012	10/2015	58(O) 37(R)	0/0
708	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
709	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
710	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
711	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
712	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99(O) 0(R)	0/0
713	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
714	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
715	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
716	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
717	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0
718	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	18,600.58	8,395.88				0/1

Sector Wise Details

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>TELECOMMUNICATIONS</u>								
719	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	09/2014	68(O) -	0/0
720	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2014	50(O) 33(R)	0/0
721	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	930.60	828.48	11/2010 12/2012	09/2013	-	0/0
722	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	336.84	-	10/2009 -	-	-	0/0
723	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.81	06/2009 -	06/2014	60(O) -	0/0
724	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
725	GSM EQUIPMENT OF 4,50,000 LINES (2G) HARYANA (PHASE V.2) TELECOM CIRCLE - [N26000080]BSNL,HARYANA	09/2008	216.54 -	216.54	-	09/2009 -	-	-	0/0
726	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
727	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEAPON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
728	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GPON EQUIPMENT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
729	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	37(O) -	0/0
	Total		5,295.83 -	5,199.48	1,769.33				0/0
	<u>URBAN DEVELOPMENT</u>								
730	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
731	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRC,L,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
732	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
733	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016	0(O) -	0/0
734	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8(O) -	0/0
	Total		73,993.32 -	79,266.22	11,652.27				3/3
	<u>WATER RESOURCES</u>								

Sector Wise Details									
(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
735	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		957,390.48	1,140,912.47	570,976.01				1081/3460

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDHRA PRADESH	22	24,560.99	29,968.77	20,275.39
2	ARUNACHAL PRADESH	4	9,512.22	12,475.64	11,055.83
3	ASSAM	38	24,056.86	38,946.64	31,031.01
4	BIHAR	46	33,296.66	40,874.24	32,593.65
5	CHANDIGARH	1	452	452	261.51
6	CHHATISGARH	24	57,805.7	65,314.32	27,468.37
7	DELHI	4	41,531.33	41,531.33	9,437.65
8	GOA	1	335.61	388.53	279.52
9	GUJARAT	32	37,940.02	39,011.92	17,630.55
10	HARYANA	10	4,709.67	6,907.4	7,250.06
11	HIMACHAL PRADESH	5	13,457.44	18,070.4	13,827.2
12	JAMMU AND KASHMIR	7	11,965.4	30,895.6	15,404.43
13	JHARKHAND	27	16,118.82	20,383.59	11,516.43
14	KARNATAKA	35	79,606.44	94,510.66	29,111.3
15	KERALA	12	22,610.65	25,135.43	9,657.38
16	MADHYA PRADESH	19	30,521.22	32,003.81	11,930.78
17	MAHARASHTRA	50	93,249.83	1,09,917.82	56,423.84
18	MANIPUR	1	727.56	5,996	2,216.69
19	MEGHALAYA	3	4,845.02	4,845.02	951.27
20	MIZORAM	2	988.06	3,307.11	775.95
21	MULTI STATE	187	2,03,894.71	2,26,339.64	93,754.51
22	NAGALAND	2	5,124	6,720.57	9.23
23	ODISHA	34	61,113.78	68,023.29	46,232.08
24	PUNJAB	4	1,680.2	1,653.16	2,510.93
25	RAJASTHAN	25	25,638.72	25,695.93	13,022.25
26	SIKKIM	2	1,648.94	3,684.88	358.02
27	TAMIL NADU	39	54,453.92	70,685.62	46,706.83
28	TELANGANA	22	9,563.31	12,332.13	3,235.77
29	TRIPURA	6	2,966.26	4,737.26	2,731.85
30	UTTAR PRADESH	27	19,788.44	23,055.49	15,609.39
31	UTTARAKHAND	7	9,501.04	13,063.93	3,842.34
32	WEST BENGAL	37	53,725.66	63,984.34	33,864
TOTAL		735	9,57,390.48	11,40,912.47	5,70,976.01

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	17,626
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	4,564.17
3	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,474.99
4	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,858.57
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	2,940.49
6	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	10,036
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,502.7
8	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	POWER	03/2005	596.45	-	941.71
9	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	200.42
10	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	688.63
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	2500	8,805
12	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
13	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	887.59
14	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	155	776.13

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	NANDYAL-YERRAGUNTLA(NL), SCR	RAILWAYS	03/1996	155.74	429.49	689.92
16	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,000	1500	3,160.19
17	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	194.07	378.37
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	233	501.69	734.77
19	KATIHAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	742.61
20	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	459.37
21	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	RAILWAYS	03/2002	625.3	408.76	838.17
22	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	100	571.02
23	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	840.85
24	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,581.17
25	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3156.32	3,503.29
26	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	294.43
27	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	190.81	238.56	554.48
28	RAJATGARH-BARANG(LD), ECOR	RAILWAYS	04/1999	166.16	-	307.18

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.53	2,216.69
30	DANIAWAN-BIHARSARIF (NL), ECR	RAILWAYS	04/2001	104.79	-	148.85
31	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	2,791.02
32	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	279.04
33	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	279.63
34	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	262.3
35	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	171.8
36	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	243.4
37	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	ROAD TRANSPORT AND HIGHWAYS	12/2003	166.27	-	200.4
38	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	267
39	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	309.2
40	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	519.4
41	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	284.1
42	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	372.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	CIVIL AVIATION	08/2008	1,942.51	2325	2,573.92
44	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	1,248.88
45	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	15,945.82
46	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,855
47	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	PETROLEUM	07/2009	238.68	-	286.76
48	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	7,712.19
49	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	PETROLEUM	08/2009	246.81	-	256.97
50	RAMPUR HEP(412 MW)	POWER	01/2007	2,047.03	-	3,134.02
51	WESTERN REGION STRENGTHENING SCHEME-V	POWER	12/2007	477.69	-	483.89
52	BONGAIGAON THERMAL POWER PROJECT	POWER	01/2008	4,375.35	-	4,540
53	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	-	840.66
54	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	7,590
55	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	623.44	765.07
56	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	POWER	01/2011	368.72	-	601.12

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	PETROLEUM	08/2008	144.02	-	151.39
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	114.01	332.92	454.47
59	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	795.45
60	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	404.19	415.36
61	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	343.17	766.03
62	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	170	417.14
63	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	RAILWAYS	09/1996	156	156	416.11
64	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	562.62
65	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.27
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	1676.31	4,253.73
67	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	462.18
68	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.65
69	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	788.27
70	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	243.91

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	267.5
72	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	462.05
73	NEW BG LINE FROM DUDHNOI-MENDIPATAR	RAILWAYS	04/1999	175.43	-	230.67
74	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	959.83
75	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	562.37
76	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	1,039.78
77	PANVEL PEN DOUBLING	RAILWAYS	04/2006	191	-	222.52
78	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	259.46
79	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2
80	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
81	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	266.3
82	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	311.6
83	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
84	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	318.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	275.6
86	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	320.2
87	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	211.2
88	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	268.7
89	BRAHMPUTRA BRIDGE, NH NO-31	ROAD TRANSPORT AND HIGHWAYS	12/2003	217.61	309.56	438.8
90	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,118
91	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	309.1
92	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	661.9
93	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,341
94	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,398
95	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826
96	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,128
97	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
98	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
100	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
101	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,981
102	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,376
103	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
104	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
105	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	886.7
106	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,111
107	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,184
108	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	726.3
109	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
110	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	775.1
111	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,244
112	4 LANING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,660

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	656.7
114	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	598.4
115	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.2
116	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,379
117	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	929.6
118	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,161
119	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	1141	2,024
120	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,281
121	SAMAIKHALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	813.4
122	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	664.9
123	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
124	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	700.2
125	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	888.3
126	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	824.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,177
128	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	457.6
129	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	622.1
130	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	963
131	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	693.9
132	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,611
133	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,524
134	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,660
135	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	351.2
136	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

List of Projects Ahead of Schedule w.r.t. Original Schedule

						(May 2014)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	311.88	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	311.88		
	<u>PETROLEUM</u>						
2	LPG TERMINAL AT KOCHI - [N16000171	12/2012	607.06 -	607.06	20.38	01/2016 -	12/2015
	Total		607.06 -	607.06	20.38		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	716.98	12/2014 -	11/2014
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154	10/2013	1,315.90 -	1,315.90	53.87	11/2016 -	03/2016
5	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,364.52	14.64	05/2016 -	04/2016
	Total		4,615.77 -	4,615.77	785.49		
	Grand Total		6,731.57	6,731.57	1,117.75		

List of Projects Without Original Date of Commissioning

(May 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	- -	04/2015	-	0/0
2	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	901.48	- -	08/2015	-	0/12
	Total		11,865.00 -	11,865.00	902.84				0/12
	<u>RAILWAYS</u>								
3	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	260.16	222.52	- -	05/2014	-	0/0
4	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 470.21	1,995.25	307.01	- -	12/2014	-	0/0
5	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	562.37	- -	12/2014	-	0/0
6	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCOR,MULTI STATE	04/2008	2,050.00 -	2,050.00	178.72	- -	12/2014	-	0/0
7	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.18	254.13	- -	03/2015	-	0/0
8	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	1,708.41	1,576.77	- -	03/2015	-	0/0
9	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 915.70	3,019.17	2,791.02	- -	03/2015	-	0/0
10	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	2.22	- -	03/2015	-	0/0
11	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.35	- -	03/2016	-	0/0
12	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	03/2016	-	0/0
13	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	82.60	- -	03/2016	-	0/0
14	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	45.90	- -	03/2017	-	0/0
15	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	5.02	- -	03/2017	-	0/0
16	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	28.86	- 12/2017		0(R3)	0/0

(May 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	430.33	185.79	- -	03/2018	-	0/0
	Total		6,807.89 -	13,496.86	6,392.61				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
18	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, KARNATAKA	03/2011	839.00 -	839.00	692.50	- -	06/2014	-	0/1
19	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	680.00	382.60	- -	06/2014	-	2/2
20	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	656.70	- -	07/2014	-	2/2
21	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	1,111.00	- -	06/2015	-	2/3
	Total		2,670.00 -	2,670.00	2,842.80				6/8
	Grand Total		21,342.89	28,031.86	10,138.25				6/20

List of Projects Without Date of Commissioning

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI, WEST BENGAL	08/2008	1,942.51 2,325.00	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	04/2014
	Total		4,712.12 -		
	<u>COAL</u>				
5	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	03/2013 -	03/2014
6	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
8	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		1,846.57 -		
	<u>STEEL</u>				
9	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	12/2009 08/2010	06/2013
10	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	01/2010 02/2011	11/2013
	Total		462.00 -		
	<u>PETROCHEMICALS</u>				
11	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
12	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	01/2012 -	07/2013
13	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	05/2010 03/2013	04/2014
15	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	09/2012 -	04/2014
16	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	07/2012 07/2012	-
17	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	-
18	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
19	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
	Total		18,467.42 -		
	<u>POWER</u>				
20	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
21	MOUDA STPP - [N18000048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	08/2012 -	03/2013
22	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	10/2012 -	03/2013
23	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	10/2012 -	10/2013
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	02/2012 -	12/2013
25	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	12/2007 12/2009	-
26	RAMPUR HEP(412 MW) - [N18000024]JSVNL,HIMACHAL PRADESH	01/2007	2,047.03 -	01/2012 -	-
27	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	11/2011 -	-
28	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	- -	-
29	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	- -	-
30	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	- -	-
	Total		28,796.52 -		
	<u>RAILWAYS</u>				
31	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	06/2007
32	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
33	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009
34	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
35	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 08/2010	08/2010
36	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010
37	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011
38	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011
39	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
40	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	- -	02/2012
41	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012
42	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012
43	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012
44	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012
45	HARNOUT - SET. UP OF W/S TO UND. POH OF UP TO 50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	- -	03/2012
46	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	- -	03/2012
47	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 155.00	- -	10/2012
48	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012
49	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 343.17	- -	12/2012
50	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	- -	01/2013
51	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013
52	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 218.19	- -	02/2013
53	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013
54	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	- -	03/2013
55	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013
56	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013
57	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013
58	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	03/2013
59	GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 -	12/2011 11/2013	11/2013

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
60	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013
61	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 495.68	- -	02/2014
62	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	03/2014
63	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	- -	03/2014
64	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	- -	03/2014
65	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	- -	03/2014
66	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	- -	03/2014
67	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	03/2014
68	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014
69	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	03/2014
70	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014
71	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2014
72	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
73	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014
74	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014
75	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
76	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
77	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
78	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
79	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]SCR,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
80	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
81	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
82	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
83	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
84	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-
86	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
87	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-
88	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-
89	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-
90	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
91	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 162.87	- -	-
92	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-
93	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-
94	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-
95	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
96	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-
97	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-
98	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-
99	RAMGANJMONDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-
100	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	- -	-
101	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
102	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 671.82	- -	-
103	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 -	02/2006 -	-
104	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
105	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
106	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-
107	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-
108	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-
109	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
110	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
111	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
112	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
113	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
114	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
115	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
116	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
117	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-
118	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-
119	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
120	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
121	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
122	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
123	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
124	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
125	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
126	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-
127	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
128	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
129	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-
130	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
131	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
132	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
133	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
134	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
135	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
136	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
137	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
138	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
139	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
140	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-
141	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
142	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
143	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-
144	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
145	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
146	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
147	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
148	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
149	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-
150	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
151	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
152	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
153	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
154	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
155	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
156	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
157	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
158	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
159	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
160	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
161	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
162	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
163	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
164	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
165	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
166	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
167	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR, WEST BENGAL	04/2010	221.42 -	- -	-
168	AGARTALA-AKHAURA NL - [N22000195]NEFR, TRIPURA	04/2012	252.00 -	- -	-
169	DIMAPUR-TIZIT NL - [N22000196]NEFR, NAGALAND	04/2013	4,274.00 -	- -	-
170	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
171	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
172	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
173	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
174	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR, MEGHALAYA	04/2010	4,083.02 -	- -	-
175	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-
176	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-
177	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
178	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR, ASSAM	04/2012	246.07 -	- -	-
179	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
180	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
181	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
182	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
183	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
185	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
186	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
187	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
188	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
189	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
190	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
191	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
192	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
193	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
194	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-
195	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
196	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
197	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
198	HANSIDIH-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
199	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
200	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
201	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
202	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
203	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
204	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
205	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
206	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
207	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
208	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
209	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
210	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
211	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
212	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
213	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	- -	-
214	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	- -	-
215	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	- -	-
216	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	- -	-
217	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	- -	-
218	GUDUR-DURGARAJAPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
219	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
220	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
221	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
222	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
223	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
224	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
225	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
226	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
227	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
228	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
229	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
230	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
232	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
233	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	- -	-
234	AKKANAPET-MEDAK - [N22000285]SCOR,TELANGANA	04/2012	153.00 -	- -	-
235	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
236	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	- -	-
237	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
238	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
239	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
240	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
241	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
242	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
243	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
244	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
245	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
246	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
247	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
248	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
249	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
250	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
251	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
252	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
253	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
254	KAKINADA-PITHAPURAM - [N22000314]SECR,ANDHRA PRADESH	03/1999	215.06 -	- -	-
255	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
256	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
257	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	-
258	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-
	Total		103,517.35 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
259	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	02/2008
260	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
261	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
262	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012
263	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013
264	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013
265	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	05/2013
266	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013
267	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
268	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013
269	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
270	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
271	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
272	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013
273	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
274	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
275	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014
276	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2014
277	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
278	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
279	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
280	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
281	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-
282	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
283	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		16,287.31 -		
	SHIPPING AND PORTS				
284	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010
285	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011
286	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
287	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
288	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012
289	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012
290	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
291	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013
292	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
293	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
294	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
295	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
296	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
297	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 04/2014	04/2014
298	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
299	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		13,727.25 -		
	<u>TELECOMMUNICATIONS</u>				
300	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012
301	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013
302	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013
303	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-
304	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEPOE EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-
305	GSM EQUIPMENT OF 4,50,000 LINES (2G) HARYANA (PHASE V.2) TELECOM CIRCLE - [N26000080]BSNL,HARYANA	09/2008	216.54 -	09/2009 -	-
306	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-
	Total		3,277.68 -		
	<u>URBAN DEVELOPMENT</u>				
307	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
308	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>WATER RESOURCES</u>				
309	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		203,606.91		

List of On Schedule Projects w.r.t. Original Schedule

						(May 2014)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	261.51	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		669.60 -	669.60	261.55		
	<u>COAL</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	244.00	03/2015 -	03/2015
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017
5	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	52.14	03/2016 -	03/2016
6	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
7	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	87.18	03/2016 -	03/2016
8	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
10	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
11	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	95.88	03/2020 -	03/2020
12	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	65.54	03/2016 -	03/2016
13	KALYANIKHANI OPENCASE PROJECT - [N06000101]	7/2012	417.33 -	417.33	2.07	07/2016 -	07/2016
14	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	5.43	06/2015 -	06/2015
15	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	57.77	03/2016 -	03/2016
16	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
17	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.03	03/2015 -	03/2015
18	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	29.25	03/2018 -	03/2018
19	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	221.36	03/2016 -	03/2016
20	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	95.46	03/2015 -	03/2015

(May 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015
22	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	76.30	03/2015 -	03/2015
23	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	619.15	03/2016 03/2016	03/2016
	Total		11,108.17 -	10,736.83	1,843.56		
	<u>PETROLEUM</u>						
24	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	595.34	03/2015 -	03/2015
25	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	33.26	07/2016 -	07/2016
26	RESID UPGRADE PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	-	11/2015 -	11/2015
27	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
28	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 -	10/2014
29	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS - [N16000181]	3/2013	2,913.10 -	2,910.30	-	05/2016 -	05/2016
30	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	1.30	07/2016 -	07/2016
31	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
32	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	-	02/2016 -	02/2016
33	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	42.23	09/2017 -	09/2017
34	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
35	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
36	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	130.05	03/2015 -	03/2015
37	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	72.73	04/2015 -	04/2015
38	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
39	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	14.98	03/2015 -	03/2015
40	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	74.55	12/2014 -	12/2014
41	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,468.61	05/2015 -	05/2015
42	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	551.29	11/2015 -	11/2015
43	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	202.33	11/2015 -	11/2015

(May 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	171.74	08/2015 -	08/2015
45	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	248.39	12/2014 -	12/2014
	Total		37,219.66 -	37,363.87	4,699.29		
	<u>POWER</u>						
46	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,398.65	08/2014 -	08/2014
47	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	43.17	06/2014 -	06/2014
48	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]	2/2014	378.71 -	378.71	-	10/2016 -	10/2016
49	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
50	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
51	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
52	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	09/2016 -	09/2016
53	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
55	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
56	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
57	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	43.56	10/2014 -	10/2014
58	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	265.19	03/2015 -	03/2015
59	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,013.00	08/2015 -	08/2015
60	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	2,612.00	11/2016 -	11/2016
61	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	2,588.00	09/2016 -	09/2016
62	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	4,381.00	12/2016 -	12/2016
63	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	656.08	11/2014 -	11/2014
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	333.92	11/2014 -	11/2014
65	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	648.10	08/2014 -	08/2014

(May 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
66	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	71.10	05/2016 -	05/2016
67	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	34.59	03/2016 -	03/2016
68	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	1,243.00	09/2017 -	09/2017
69	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	482.33	06/2015 -	06/2015
70	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	133.05	12/2015 -	12/2015
71	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
72	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	128.00	08/2017 -	08/2017
73	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,644.00	05/2017 -	05/2017
74	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	13.93	10/2014 -	10/2014
75	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
76	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	224.27	08/2014 -	08/2014
77	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	771.13	02/2015 -	02/2015
78	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	186.56	08/2014 -	08/2014
79	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	1,054.17	10/2014 -	10/2014
80	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	684.82	01/2015 -	01/2015
	Total		83,404.42 -	83,404.42	20,653.62		
	<u>RAILWAYS</u>						
81	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	114.40	02/2015 -	02/2015
82	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
83	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	165.16	79.06	03/2015 -	03/2015
84	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	177.23	03/2017 -	03/2017
85	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	16.58	03/2015 -	03/2015

(May 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	422.20	03/2016 -	03/2016
87	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	100.00	03/2016 -	03/2016
88	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
89	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	2.43	02/2019 -	02/2019
90	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	60.70	03/2015 -	03/2015
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	398.46	03/2016 -	03/2016
	Total		15,688.03 -	20,400.69	1,374.08		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
92	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
93	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	268.50	06/2014 -	06/2014
94	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	284.80	10/2014 -	10/2014
95	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	336.60	06/2015 -	06/2015
96	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	808.10	09/2015 -	09/2015
97	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	263.80	07/2014 -	07/2014
98	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	481.30	04/2015 -	04/2015
99	4 LANING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
100	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	262.40	11/2016 -	11/2016
101	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	190.00	10/2015 -	10/2015
102	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
103	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	266.40	09/2014 -	09/2014
104	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	1,293.00	10/2014 -	10/2014
105	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	104.80	12/2015 -	12/2015
106	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	351.20	10/2014 -	10/2014
107	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	467.70	08/2015 -	08/2015

(May 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211	7/2012	356.40 -	356.40	50.28	07/2014 -	07/2014
109	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,660.00	09/2014 -	09/2014
110	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190	12/2011	325.00 -	325.00	170.70	05/2014 -	05/2014
111	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	2,097.00	06/2014 -	06/2014
	Total		22,418.30 -	22,418.30	11,106.11		
	<u>STEEL</u>						
112	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078	7/2012	332.65 -	332.65	104.96	08/2014 -	08/2014
113	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079	6/2012	237.09 -	254.90	36.64	12/2014 -	12/2014
114	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080	11/2012	313.05 -	339.35	87.72	06/2015 -	06/2015
115	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014
116	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	10.55	05/2016 -	05/2016
	Total		1,288.94 -	1,333.05	258.73		
	<u>URBAN DEVELOPMENT</u>						
117	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
118	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	8,699.49		
	Grand Total		236,787.26	241,316.90	48,896.43		

List of Projects Without Milestones w.r.t. Original Schedule

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	04/2014	0/0
4	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	10/2014	0/0
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	03/2015	0/0
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015	0/0
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	12/2016	0/0
	Total		4,092.95 -			0/0
	<u>COAL</u>					
8	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014	0/0
9	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
10	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	03/2022 -	03/2022	0/0
	Total		2,180.48 -			0/0
	<u>PETROLEUM</u>					
11	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013	0/0
12	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	05/2010 03/2013	04/2014	0/0
13	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	09/2012 -	04/2014	0/0
14	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2014	0/0
15	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	06/2012 -	06/2014	0/0
16	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	04/2012 -	06/2014	0/0
17	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	06/2012 -	06/2014	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	08/2014	0/0
19	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	10/2014 -	10/2014	0/0
20	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	10/2010 -	12/2014	0/0
21	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	09/2012 -	12/2014	0/0
22	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	12/2014 -	12/2014	0/0
23	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	06/2014 -	12/2014	0/0
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPL,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	02/2015	0/0
25	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	12/2014 -	03/2015	0/0
26	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
27	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	- -	04/2015	0/0
28	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	04/2015 -	04/2015	0/0
29	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	12/2008 04/2013	05/2015	0/0
30	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	04/2006 06/2012	06/2015	0/0
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	06/2015	0/0
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KERALA	01/2006	993.00 1,693.00	01/2012 -	06/2015	0/0
33	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	12/2013 -	09/2015	0/0
34	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	10/2014 -	10/2015	0/0
35	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	12/2014 -	11/2015	0/0
36	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	11/2015 -	11/2015	0/0
37	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
38	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
39	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	12/2015	0/0
40	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	07/2015 -	12/2015	0/0
41	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	01/2016 -	12/2015	0/0
42	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	02/2016 -	02/2016	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
43	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	02/2016 -	02/2016	0/0
44	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	04/2016 -	04/2016	0/0
45	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
46	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	05/2016 -	05/2016	0/0
47	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0
48	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	07/2016 -	07/2016	0/0
49	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2016	0/0
50	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2016	0/0
51	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 -	03/2017	0/0
52	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	09/2012 -	03/2017	0/0
53	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	09/2017 -	09/2017	0/0
54	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
55	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	12/2018 -	12/2018	0/0
56	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
57	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
	Total		107,132.15 -			0/0
	<u>POWER</u>					
58	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	09/2014	0/0
59	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	06/2015 -	06/2015	0/0
60	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
61	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	12/2015 -	12/2015	0/0
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	03/2016 -	03/2016	0/0
63	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	11/2016 -	03/2016	0/0
64	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	03/2016 -	03/2016	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
65	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	05/2016 -	04/2016	0/0
66	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
67	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	05/2016 -	05/2016	0/0
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	06/2016 -	06/2016	0/0
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	06/2016 -	06/2016	0/0
70	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	07/2016 -	07/2016	0/0
71	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	08/2014 -	08/2016	0/0
72	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	09/2016 -	09/2016	0/0
73	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	10/2016 -	10/2016	0/0
74	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	11/2016	0/0
75	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	12/2018	0/0
76	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	- -	-	0/0
77	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	- -	-	0/0
	Total		23,818.73 -			0/0
	<u>RAILWAYS</u>					
78	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	06/2007	0/0
79	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
80	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
81	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
82	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 08/2010	08/2010	0/0
83	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
84	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011	0/0
85	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
86	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
87	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
88	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
89	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
90	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
91	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012	0/0
92	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
93	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
94	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	- -	10/2012	0/0
95	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
96	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	- -	12/2012	0/0
97	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	01/2013	0/0
98	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
99	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	- -	02/2013	0/0
100	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
101	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013	0/0
102	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
103	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
104	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2013	0/0
105	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 -	12/2011 11/2013	11/2013	0/0
106	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013	0/0
107	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 495.68	- -	02/2014	0/0
108	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	03/2014	0/0
109	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	- -	03/2014	0/0
110	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	- -	03/2014	0/0
111	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	- -	03/2014	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
112	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	03/2014	0/0
113	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
114	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	03/2014	0/0
115	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
116	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2014	0/0
117	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
118	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014	0/0
119	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014	0/0
120	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	- -	05/2014	0/0
121	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
122	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
123	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	09/2014	0/0
124	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	12/2008 -	09/2014	0/0
125	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	03/2012 12/2013	10/2014	0/0
126	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
127	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	12/2014	0/0
128	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 470.21	- -	12/2014	0/0
129	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
130	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	12/2012 -	12/2014	0/0
131	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	06/2013 -	12/2014	0/0
132	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	12/2014	0/0
133	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCOR,MULTI STATE	04/2008	2,050.00 -	- -	12/2014	0/0
134	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
135	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
136	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2015	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
137	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2015	0/0
138	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
139	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	12/2010 12/2010	03/2015	0/0
140	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 915.70	- -	03/2015	0/0
141	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	03/2015	0/0
142	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	- -	03/2015	0/0
143	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
144	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
145	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
146	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	06/2004 -	06/2015	0/0
147	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
148	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
149	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2015	0/0
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
151	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
153	KATAKHAL TO BHARABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	12/2012 -	03/2016	0/0
154	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
155	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
156	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	03/2016	0/0
157	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	03/2016	0/0
158	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	- -	03/2016	0/0
159	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	04/2012 -	03/2016	0/0
160	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	06/2016	0/0
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
162	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
163	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,213.84	03/2014 03/2016	12/2016	0/0
164	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2017	0/0
165	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
166	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
167	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2017	0/0
168	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2017	0/0
169	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
170	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
171	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	03/2009 -	03/2017	0/0
172	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	03/2007 -	03/2017	0/0
173	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	- -	03/2017	0/0
174	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	- -	03/2017	0/0
175	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
176	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
177	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
178	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2017	0/0
179	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	- 12/2017	12/2017	0/0
180	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	- -	03/2018	0/0
181	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
182	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
183	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-	0/0
184	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
185	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR, HARYANA	04/2013	400.00 -	- -	-	0/0
186	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR, MULTI STATE	04/2013	876.00 -	- -	-	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
187	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]SCR,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
188	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
189	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
190	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
191	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
192	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-	0/0
193	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-	0/0
194	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
195	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-	0/0
196	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-	0/0
197	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
198	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
199	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 162.87	- -	-	0/0
200	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-	0/0
201	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-	0/0
202	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-	0/0
203	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
204	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-	0/0
205	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-	0/0
206	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-	0/0
207	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-	0/0
208	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	- -	-	0/0
209	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
210	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 671.82	- -	-	0/0
211	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 -	02/2006 -	-	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
212	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
213	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
214	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-	0/0
215	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-	0/0
216	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-	0/0
217	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-	0/0
218	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
219	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
220	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
221	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
222	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
223	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
224	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
225	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-	0/0
226	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-	0/0
227	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
228	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
229	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
230	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
231	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
232	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
233	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
234	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-	0/0
235	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
236	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
237	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-	0/0
238	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
239	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
240	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
241	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
242	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
243	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
244	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
245	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
246	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
247	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
248	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-	0/0
249	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
250	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
251	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-	0/0
252	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
253	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
254	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
255	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
256	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
257	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-	0/0
258	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
259	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
260	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
261	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0

			(May 2014)			
			Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
262	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
263	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
264	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
265	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
266	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
267	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-	0/0
268	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
269	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
270	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
271	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-	0/0
272	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
273	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
274	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
275	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
276	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-	0/0
277	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0
278	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
279	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
280	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
281	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
282	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-	0/0
283	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
284	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-	0/0
285	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-	0/0
286	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
287	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
288	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR, MULTI STATE	04/2011	601.43 -	- -	-	0/0
289	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1999	406.99 -	- -	-	0/0
290	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	450.00 -	- -	-	0/0
291	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	- -	-	0/0
292	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	- -	-	0/0
293	BANDEL-BOINCHI 3RD LINE - [N22000221]ER, MULTI STATE	04/2011	288.35 -	- -	-	0/0
294	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	- -	-	0/0
295	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER, MULTI STATE	04/2000	157.17 -	- -	-	0/0
296	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	923.52 -	- -	-	0/0
297	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.91 -	- -	-	0/0
298	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER, MULTI STATE	04/2010	174.56 -	- -	-	0/0
299	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 -	- -	-	0/0
300	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	296.44 -	- -	-	0/0
301	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	- -	-	0/0
302	WARDHA-NANDED MAHARASHTRA - [N22000231]CR, MAHARASHTRA	04/2008	697.00 -	- -	-	0/0
303	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
304	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55 -	- -	-	0/0
305	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17 -	- -	-	0/0
306	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	267.09 -	- -	-	0/0
307	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER, MULTI STATE	04/2011	193.44 -	- -	-	0/0
308	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	- -	-	0/0
309	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	494.54 -	- -	-	0/0
310	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]ER, MULTI STATE	04/2000	297.47 -	- -	-	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
311	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
312	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
313	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-	0/0
314	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-	0/0
315	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
316	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
317	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
318	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
319	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
320	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
321	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
322	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
323	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
324	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
325	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
326	GUDUR-DURGARAJPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
327	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
328	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
329	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
330	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
331	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
332	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
333	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
334	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
335	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
336	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74	-	-	0/0
337	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34	-	-	0/0
338	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05	-	-	0/0
339	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	-	-	0/0
340	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00	-	-	0/0
341	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60	-	-	0/0
342	AKKANAPET-MEDAK - [N22000285]SCOR,TELANGANA	04/2012	153.00	-	-	0/0
343	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48	-	-	0/0
344	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49	-	-	0/0
345	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83	-	-	0/0
346	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54	-	-	0/0
347	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96	-	-	0/0
348	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00	-	-	0/0
349	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	-	-	0/0
350	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14	-	-	0/0
351	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00	-	-	0/0
352	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	-	-	0/0
353	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00	-	-	0/0
354	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	-	-	0/0
355	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93	-	-	0/0
356	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64	-	-	0/0
357	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94	01/1999	-	0/0
358	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24	01/1999	-	0/0
359	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48	01/1999	-	0/0
360	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57	01/1999	-	0/0

			(May 2014)			
			Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
361	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
362	KAKINADA-PITHAPURAM - [N22000314]SECR, ANDHRA PRADESH	03/1999	215.06 -	- -	-	0/0
363	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	- -	-	0/0
364	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	-	0/0
365	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 -	- -	-	0/0
366	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	-	0/0
	Total		154,553.47 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
367	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	02/2008	0/0
368	PUNE-SHOLAPUR, PKG1 - [N24000127]NHAI, MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012	0/0
369	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012	0/0
370	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012	0/0
371	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013	0/0
372	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013	0/0
373	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	05/2013	0/0
374	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
375	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
376	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013	0/0
377	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	11/2013 -	11/2013	0/0
378	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0
379	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
380	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0
381	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	03/2014	0/0
382	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
383	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	06/2014	0/0
384	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	06/2014	0/0
385	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	06/2014	0/0
386	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	06/2014	0/0
387	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
388	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	06/2014	0/0
389	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
390	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
391	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	07/2014	0/0
392	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	07/2014	0/0
393	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	07/2014	0/0
394	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	07/2014	0/0
395	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	08/2014	0/0
396	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	08/2014	0/0
397	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	08/2014	0/0
398	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	08/2014	0/0
399	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	08/2014	0/0
400	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	11/2008 12/2014	09/2014	0/0
401	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 09/2014	09/2014	0/0
402	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	08/2013 06/2014	09/2014	0/0
403	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	09/2014	0/0
404	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	09/2014	0/0
405	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	09/2014	0/0
406	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	09/2014	0/0
407	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	09/2014	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
408	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
409	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	04/2014 -	09/2014	0/0
410	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	09/2014 -	09/2014	0/0
411	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	04/2008 01/2015	10/2014	0/0
412	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 01/2015	10/2014	0/0
413	PANIPAT-ROHTAK - [N24000151]NHAI, HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
414	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	10/2014 -	10/2014	0/0
415	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014	0/0
416	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI, MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
417	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	11/2014	0/0
418	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	09/2007 03/2014	12/2014	0/0
419	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	09/2008 -	12/2014	0/0
420	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 361.00	02/2009 -	12/2014	0/0
421	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 167.64	11/2008 12/2014	12/2014	0/0
422	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 200.00	04/2009 12/2014	12/2014	0/0
423	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	09/2008 -	12/2014	0/0
424	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	10/2008 -	12/2014	0/0
425	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	04/2008 01/2015	12/2014	0/0
426	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	04/2008 01/2015	12/2014	0/0
427	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 331.23	07/2009 -	12/2014	0/0
428	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00 -	02/2010 -	12/2014	0/0
429	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	12/2014	0/0
430	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	10/2011 -	12/2014	0/0
431	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	12/2014	0/0
432	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	03/2013 -	12/2014	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
433	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2014	0/0
434	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2014	0/0
435	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2014	0/0
436	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2014	0/0
437	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2014	0/0
438	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	12/2014	0/0
439	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	12/2014	0/0
440	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2014	0/0
441	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	12/2014	0/0
442	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	02/2015	0/0
443	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 12/2014	03/2015	0/0
444	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	03/2015	0/0
445	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	03/2015	0/0
446	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	09/2007 -	03/2015	0/0
447	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	03/2015	0/0
448	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2015	0/0
449	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2015	0/0
450	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2015	0/0
451	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	03/2015	0/0
452	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
453	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2015	0/0
454	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	06/2015	0/0
455	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 07/2011	06/2015	0/0
456	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	06/2015	0/0
457	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	06/2015	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
458	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
459	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
460	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
461	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	09/2015	0/0
462	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
463	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
464	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
465	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	11/2015	0/0
466	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
467	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	12/2015	0/0
468	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	12/2015	0/0
469	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2015	0/0
470	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	12/2015	0/0
471	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2015	0/0
472	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2015	0/0
473	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	12/2015	0/0
474	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2015	0/0
475	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	12/2015	0/0
476	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	12/2015	0/0
477	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	12/2015	0/0
478	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2016	0/0
479	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2016	0/0
480	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
481	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	06/2016	0/0
482	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
483	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
484	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
485	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
486	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
487	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
488	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
489	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
490	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0
491	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
492	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17 -	- -	-	0/0
	Total		91,307.62 -			0/0
	<u>SHIPPING AND PORTS</u>					
493	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
494	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP., MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
495	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST, GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0
496	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP., MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
497	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST, ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0
498	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST - [N25000037]PORT TRUST, GUJARAT	04/2005	882.00 -	02/2011 -	12/2012	0/0
499	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, GUJARAT	12/2005	702.00 -	03/2011 -	03/2013	0/0
500	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST, GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0
501	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP., MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
502	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST, KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
503	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP., MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0
504	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP., MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
505	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 04/2014	04/2014	0/0
506	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014	0/0
507	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
508	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2015	0/0
509	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
510	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		15,462.28 -			0/0
	<u>TELECOMMUNICATIONS</u>					
511	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012	0/0
512	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013	0/0
513	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
514	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	06/2009 -	06/2014	0/0
515	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	06/2014	0/0
516	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	09/2014	0/0
517	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 03/2012	12/2014	0/0
518	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-	0/0
519	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEPOE EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-	0/0
520	GSM EQUIPMENT OF 4,50,000 LINES (2G) HARYANA (PHASE V.2) TELECOM CIRCLE - [N26000080]BSNL,HARYANA	09/2008	216.54 -	09/2009 -	-	0/0
521	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-	0/0
	Total		5,295.83 -			0/0
	<u>URBAN DEVELOPMENT</u>					
522	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
523	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0
524	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRC,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0

			(May 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
525	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		67,598.32 -			0/0
	<u>WATER RESOURCES</u>					
526	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		471,984.73			0/0

List of Ongoing Projects having Time and Cost Overrun w.r.t Original Schedule

(May 2014)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12	75
	Total		16,663.00 -	22,947.00				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50	24
4	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60	120
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	06/2014	49.09	60
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63	29
	Total		9,127.17 -	42,445.95				
	<u>PETROLEUM</u>							
9	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	06/2014	41.85	24
10	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	12/2014	35.29	27
11	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	06/2014	12.16	26
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00	12
13	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	04/2006 -	06/2015	536.46	110
14	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	09/2015	17.25	21
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	02/2015	54.46	40
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	06/2015	67.62	44

(May 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	06/2015	70.49	41
18	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,331.62	06/2012 -	06/2014	7.76	24
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63
20	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	12/2008 -	05/2015	15.50	77
21	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
22	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68	57
23	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85	25
	Total		48,287.85 -	105,215.98				
	<u>POWER</u>							
24	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00	16
25	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59	25
26	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79
27	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.04	01/2016 -	11/2016	62.69	10
28	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32	25
29	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31	48
30	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87
31	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14	48
32	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48	73
33	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87
	Total		28,438.70 -	144,655.97				
	<u>RAILWAYS</u>							
34	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67	60
35	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141

(May 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
36	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49	69
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65
38	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163	04/2010	146.95 -	171.02	06/2013 -	12/2014	16.38	18
39	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	184.91	03/2015 -	12/2015	23.36	9
40	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	09/2014	282.96	246
41	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66
42	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03	31
43	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.40	06/2004 -	06/2015	207.31	132
44	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
45	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50	132
46	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60	3
47	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
48	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20	96
49	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	12/2014	351.48	129
50	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,022.64	12/2010 -	03/2015	107.44	51
51	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
52	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46	35
53	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
54	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06	47
55	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
56	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12	72
57	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75	99
58	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06	36

(May 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
59	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83	24
60	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80	120
61	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
62	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62	116
63	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99	15
64	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34	96
65	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
66	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,952.58	03/2014 -	12/2016	50.05	33
	Total		23,744.20 -	220,869.60				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
67	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10	75
68	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	09/2014	80.68	70
69	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58	65
70	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75	71
71	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12	90
72	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	06/2016	2.29	76
73	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93
74	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50	40
	Total		2,649.01 -	225,521.17				
	<u>SHIPPING AND PORTS</u>							
75	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00	99
76	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75	58

(May 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	Total		1,378.00 -	228,279.33				
	<u>STEEL</u>							
77	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	06/2014	100.63	69
78	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20	37
79	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	09/2014	41.41	59
80	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	07/2014	13.61	31
	Total		23,538.89 -	257,802.18				
	<u>TELECOMMUNICATIONS</u>							
81	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42	60
	Total		149.15 -	257,960.90				
	Grand Total		153,975.97	1,505,698.08				

List of Ongoing Projects having Cost Overrun w.r.t. to Original Schedule

(May 2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77
	Total		4,086.12 -	27,943.66			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	06/2014	49.09
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
8	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
9	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50
10	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		9,767.76 -	48,131.30			
	<u>PETROCHEMICALS</u>						
14	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		5,460.61 -	57,051.30			
	<u>PETROLEUM</u>						
15	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	2,735.65	04/2006 -	06/2015	536.46
16	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	05/2015	15.50
17	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
18	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68
19	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	04/2014	54.27
20	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85
21	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
22	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	06/2014	7.76
23	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR [N16000099	03/2009	234.78 234.78	317.64	09/2012 -	12/2014	35.29
24	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	09/2015	17.25
25	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
26	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
27	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	06/2014	12.16
28	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
29	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
30	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	02/2015	54.46
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	06/2015	67.62
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	06/2015	70.49
33	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	06/2012 -	06/2014	41.85
	Total		56,965.19 -	132,313.39			
	<u>POWER</u>						

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
34	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
36	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
37	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
38	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
39	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
40	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
41	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.04	01/2016 -	11/2016	62.69
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
43	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
44	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
45	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32
46	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00
47	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	01/2011	368.72 -	913.63	07/2006 02/2015	12/2015	147.78
	Total		36,642.44 -	181,844.13			
	<u>RAILWAYS</u>						
48	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	09/2014	282.96
49	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
50	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
51	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
52	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
53	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
54	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.18	- -	03/2015	1,810.82

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
56	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
57	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	12/2014	351.48
58	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
59	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91
60	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	1,289.92	- -	01/2013	337.26
61	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
62	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
63	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
64	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
65	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
66	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2015	332.51
67	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62
68	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
69	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20
70	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.40	06/2004 -	06/2015	207.31
71	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
72	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05
73	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
74	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
75	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
76	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,022.64	12/2010 -	03/2015	107.44
77	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	05/2009	248.16
79	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47
80	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28
81	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	06/2007	35.57
82	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
83	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
84	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73
85	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75
86	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,176.10	12/2006 -	08/2010	202.58
87	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
88	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67
89	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92
90	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	1,382.78	- -	-	902.01
91	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
92	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
93	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	12/2014	324.33
94	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
95	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
96	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12
97	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
98	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04
99	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
100	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
101	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	406.92	- -	-	288.32
102	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	-	160.32
103	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]	01/2004	915.70 -	3,019.17	-	03/2015	229.71
104	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	472.00	- -	02/2013	116.33
105	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49
106	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	- -	12/2013	52.67
107	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
108	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
109	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 -	810.78	- -	-	11.53
110	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
111	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
112	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
113	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	186.92 -	261.70	02/2006 -	-	40.01
114	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
115	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
116	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
117	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
118	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
119	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
120	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
121	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
122	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	407.98	- -	03/2014	161.53

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
123	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
124	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
125	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	- -	03/2018	115.17
126	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
127	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
128	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
129	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,952.58	03/2014 -	12/2016	50.05
130	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03
131	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50
132	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06
133	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
134	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
135	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
136	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2014	81.45
137	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.46	03/2014 -	03/2014	0.04
138	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
139	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
140	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	04/2004	225.68 -	293.74	12/2010 -	12/2010	30.16
141	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
142	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
143	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
144	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
145	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
146	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34
147	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	- -	-	24.15
148	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
149	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
150	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
151	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
152	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH- UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
153	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
154	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
155	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR- BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
156	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
157	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2015	23.36
158	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	12/2014	16.38
159	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60
160	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
161	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
162	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
163	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
164	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
165	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
166	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
167	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
168	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	247.75	- -	03/2014	41.22
169	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
170	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
171	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
172	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	12/2014	285.12
173	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
174	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	545.64	- -	-	229.06
175	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,418.21	- -	-	171.08
176	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	-	47.95
177	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
178	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
179	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	697.00 -	2,501.05	- -	-	258.83
180	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
181	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
182	PANVEL PEN DOUBLING - [N22000255]	04/2006	191.00 -	260.16	- -	05/2014	36.21
183	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
184	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
185	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
186	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
187	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
188	BHANUPALI-BILASPUK BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
189	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
190	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
191	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
192	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
193	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
194	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
195	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
196	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
197	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
198	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
199	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
200	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
	Total		67,057.29 -	369,752.61			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
201	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10
202	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	03/2008 -	02/2008	16.14
203	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75
204	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	09/2014	80.68
205	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
206	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58
207	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	06/2016	2.29
208	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
209	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,815.28 -	374,597.28			

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
210	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003]	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
211	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
212	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75
213	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
214	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
215	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
216	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
217	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
218	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	386,513.94			
	<u>STEEL</u>						
219	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	09/2014	41.41
220	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20
221	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	06/2014	100.63
222	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	07/2014	13.61
223	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09
224	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	08/2006	260.00 -	349.64	12/2009 -	06/2013	34.48
225	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA [N12000079]	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
226	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	06/2015 -	06/2015	8.40
	Total		24,551.03 -	417,324.26			

(May 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>TELECOMMUNICATIONS</u>						
227	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42
228	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
229	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	418,805.71			
	<u>URBAN DEVELOPMENT</u>						
230	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
231	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX, MUMBAI - [N28000048]	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	430,587.79			
	<u>WATER RESOURCES</u>						
232	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	431,774.79			
	Grand Total		241,083.75	3,299,587.16			

LIST OF PROJECTS HAVING TIME OVERRUNS ALONG WITH REASONS FOR DELAY (AS ON 01.06.2014)

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
ATOMIC ENERGY											
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	03/2015	3492.00	5677.00	4564.17	62.57	54	NR
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2016	11459.00	11459.00	4723.00	0.00	11	Delay in supply of major equipments.
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2017	12320.00	12320.00	3001.00	0.00	3	Delay in supply of major equipments.
4	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	03/2015	13171.00	17270.00	17626.00	31.12	75	Slippage of commitments by M/s Atomstroy Export (ASE), Russian Federation.
CIVIL AVIATION											
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	AAI	02/2010	03/2014	10/2014	344.28	344.28	0.00	0.00	7	Delay in supply of equipments.
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	12/2016	309.46	309.46	272.79	0.00	71	1.Adverse weather condition. 2. Delay in diversion of roads.
COAL											
7	ASHOK EXPN.OCP -CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	471.66	341.63	99.00	0.00	72	1.Law & order problems. 2.Environmental clearance. 3. Coal evacuation problems.
8	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2015	210.98	210.98	121.20	0.00	24	1.Rehabilitation & resettlement problems. 2.Law & order problems. 3.Environmental clearance.
9	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	264.68	139.29	0.00	48	Environmental clearance.
10	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	163.51	35.52	0.00	60	Contractual issues

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
11	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	162.46	49.19	0.00	36	1.Rehabilitation & resettlement problems. 2.Environmental clearance.
12	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	179.87	59.49	0.00	60	Rehabilitation & resettlement problems.
13	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	469.78	706.40	44.65	50.37	44	Law & order problems.
14	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	153.82	33.46	0.00	24	1. Law & order problems. 2. Contractual issues.
15	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	287.17	35.49	0.00	72	Contractual issues.
16	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2015	479.63	479.63	120.15	0.00	24	Environmental clearance.
17	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2015	457.77	457.77	116.72	0.00	24	1. Environmental clearance. 2. Coal evacuation problems.
18	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2016	207.28	207.28	126.88	0.00	48	1. Environmental clearance. 2. Delay in forest land diversion.
19	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2016	172.08	172.08	131.41	0.00	72	Rehabilitation & resettlement issues.
20	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	302.96	118.59	0.00	84	Coal evacuation problem.
21	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2015	259.40	259.40	6.99	0.00	36	1. Land acquisition. 2. Rehabilitation & resettlement problems.
22	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	5907.11	341.52	0.00	28	Delay in opening and evaluation of bids.
23	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	08/2014	4904.54	6602.74	5264.42	34.63	29	1. Contractual issues. 2. Delay in civil works and erection of equipments

SN	PROJECT	IMPLIMEN TING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
24	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	06/2014	2030.78	3027.59	2991.89	49.09	60	1. Contractual issues. 2. Delay in equipment erection.
25	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2015	181.19	181.19	35.35	0.00	36	Environmental clearance
26	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2015	418.97	418.97	226.55	0.00	36	1. Land acquisition 2. Rehabilitation & resettlement problems.
27	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2016	453.63	453.63	102.04	0.00	39	1. Land acquisition. 2. Rehabilitation & resettlement problems. 3. Contractual issues. 4. Adverse geo-mining conditions.
28	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2015	212.34	1228.39	1248.88	478.50	24	1. Contractual issues. 2. Adverse geo-mining conditions.
29	CHURCHA ROUG(1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	462.35	271.88	0.00	24	Contractual issues
30	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	1943.66	1539.76	0.00	24	1. Rehabilitation & resettlements problems. 2. Delay in tendering of major HEMM.
31	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	2675.67	1535.66	0.00	24	1. Rehabilitation & resettlement problems. 2. Delay in tendering of major HEMM.
32	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2016	178.44	178.44	0.00	0.00	24	1. Rehabilitation & resettlement problems. 2. Environmental clearance.
33	JAGANNATHPOR OC	SECL	09/2008	03/2015	03/2017	152.43	152.43	21.55	0.00	24	1. Land acquisition. 2. Rehabilitation & resettlement problems
34	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2016	321.42	321.50	209.19	0.02	24	Environmental clearance.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
35	KUSMUNDA EXP.N.OCP(SECL)(15-50)MTY	SECL	06/2008	03/2013	03/2023	1188.31	7612.33	754.00	540.60	120	1. Rehabilitation & resettlement problems. 2. Environmental clearance.
36	PENGANGA OC	WCL	10/2008	03/2014	03/2016	339.77	339.77	1.50	0.00	24	Land acquisition.

SN	PROJECT	IMPLIMEN TING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
	PETROLEUM										
37	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY	BPCL	01/1999	12/2014	03/2015	1419.00	1419.00	560.47	0.00	3	Desalter and air coolers not received at site.
38	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	01/1999	12/2015	05/2016	14225.00	14225.00	2261.15	0.00	5	NR
39	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	BPCL	08/2009	04/2012	06/2014	246.81	276.83	256.97	12.16	26	Forest clearance and High Court permission for cutting mangroves were obtained in Dec'12.
40	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	03/2012	03/2015	463.32	330.47	270.55	0.00	36	Hard rocks & restricted ROU provided by forest deptt. caused delay in construction progress.
41	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	GAIL	08/2010	02/2014	08/2014	8140.00	8140.00	6603.47	0.00	6	NR
42	JHAJJAR HISSAR PIPE LINE PROJECT	GAIL	11/2007	10/2010	12/2014	281.07	281.07	4.42	0.00	50	No potential customers coming up in Sultanpur-Jhajjar- Hissar section. Anchor Load DFR Customers (RIL SEZ, TATA Power etc.) shelved off their projects. Presently the project is on hold.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
43	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2015	7596.18	7596.18	13.50	0.00	35	Execution of JHPL project would be synchronized with gas availability from various domestic sources/ customer readiness. Revival pkg. approved for Sindri and Gorakhpur fertilizer plant . HFCL revival plan is under consideration for the units at Haldia, Durgapur, and Barauni. Project activities will start after signing of GSA/ GTA by consumers.
44	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY	HPCL	03/2009	09/2011	12/2014	3284.00	2174.00	1881.89	0.00	39	In the terrain where horizontal boring is being carried out, a very hard rock strata was encountered. This strata was encountered after a progress of about 35-40 mtr and at that stage, there was no option but to continue with the same technique. No alternative technique can be adopted for further job.
45	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY	HPCL	03/2009	09/2011	07/2014	3597.00	2730.00	3128.58	0.00	34	NR
46	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	11/2012	10/2014	10/2015	309.81	309.82	67.83	0.00	12	Delay in getting statutory approvals.
47	MARKETING TERMINAL AT PARADEEP	IOCL	07/2009	06/2014	12/2014	199.75	199.75	136.46	0.00	6	NR

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
48	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	08/2015	1793.00	1793.00	983.27	0.00	35	Works regularly hampered at many locations due to frequent interruptions by activists. Station works at various locations are not progressing due to poor deployment of resources & financial crunch faced by contractors.
49	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	07/2015	12/2015	913.00	913.00	189.66	0.00	5	NR
50	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	12/2014	29777.00	32710.00	25767.00	9.85	25	1. Law & order at site, 2. Delay in construction of Power Plant by BHEL, 3. Delay in remobilization of manpower after cyclone.
51	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	02/2015	672.00	1038.00	963.51	54.46	40	Completion delayed primarily because the rectification of rock wedge failure in cavern A1 took more time and Zones of poor geology encountered during excavation of balance bench.
52	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	06/2015	732.00	1227.00	856.67	67.62	44	Order for Mangalore-Padur pipeline is yet to be placed. Recommendation awaited from EIL.
53	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	06/2015	993.00	1693.00	1242.78	70.49	41	Order for Mangalore-Padur pipeline is yet to be placed. Recommendations awaited from EIL.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
54	MRPL PHASE-III EXPANSION	MANGALORE REFIN	08/2008	01/2012	09/2014	12412.00	12160.26	11398.28	0.00	32	Project has been delayed due to slow construction progress for CPP by BHEL & slow construction progress in Unit package - Coke Handling by M/s Tecpro & Utility package -Raw Water by M/s Aqua fill Polymers.
55	POLYPROPYLENE UNIT	MANGALORE REFIN	05/2009	07/2012	06/2014	1803.78	1803.78	963.62	0.00	23	1. Project is delayed due to poor progress of piping works by M/s Simplex and inadequate deployment of skilled manpower. 2. Poor manpower mobilization by Electrical & Instrumentation contractor.
56	WAX PROJECT	NRL	06/2010	12/2013	09/2015	576.60	676.05	531.34	17.25	21	Progress is affected due to slow progress in construction activities
57	GAS TURBINE GENERATION SET	OIL	07/2009	10/2011	08/2014	216.88	216.88	177.92	0.00	34	1. Short supply of materials. 2. Delay in finalization of BoP vendor for ventilation system.
58	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	12/2014	11/2015	270.00	270.00	0.00	0.00	11	One of the bidder M/s Drillmech filed writ petition in Guwahati High Court against deviation in process of evaluation for award of LOA. Matter currently sub judice.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
59	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN	OIL	08/2006	09/2012	03/2017	374.56	374.56	10.60	0.00	54	Project site shifted to new location at Madhuban for which land in under possession of OIL.
60	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	OIL	08/2008	06/2012	06/2014	144.02	204.29	151.39	41.85	24	1.Delay in release of drawings by EPC contractor, 2. Delay in Soil filling and frequent bandhs.
61	PIPELINE REPLACEMENT PROJECT-3	ONGC	04/2012	05/2014	05/2015	2547.26	1417.00	1151.22	0.00	12	Contractor did not take up the work as per scope.
62	102 MW WIND POWER PROJECT	ONGC	07/2010	06/2012	07/2014	1106.00	678.02	113.00	0.00	25	ROW problem at site due to intervention of local villagers
63	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	12/2014	302.26	240.95	102.80	0.00	27	Slow progress in civil work and fabrication work due to less resource mobilization.
64	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV)	ONGC	11/2010	08/2013	09/2014	331.20	269.10	169.76	0.00	13	1. Delay in award of work. 2. Slow progress by the contractors
65	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA	ONGC	07/2008	08/2012	06/2014	288.04	253.66	210.07	0.00	22	Construction activities hampered due to ROU related issues. Marshy and highly undulating terrain resulting in poor progress in pipeline laying work.
66	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2015	861.79	761.68	589.37	0.00	22	Increase in scope of work and delay in procurement of steel and fabrication of legs by the contractor.
67	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2015	2465.15	2378.86	1496.19	0.00	24	Local problems and court cases by tea gardener.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
68	DEVELOPMENT OF B-46 CLUSTER FIELD	ONGC	06/2007	07/2010	05/2014	1436.21	1436.21	1165.53	0.00	46	1. Gas from B-46 Cluster Project planned to be processed at new MHN Process Platform, the completion of the project was linked with commissioning of new MHN complex. Since award of MHN project got delayed, B-46 series project was also delayed. 2. Drilling of planned wells got delayed.
69	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	03/2015	352.49	352.49	90.83	0.00	12	1. Clubbing of project facilities alongwith C-26 Cluster development project. 2. slow progress by the contractor
70	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2015	2592.17	2592.17	282.02	0.00	12	NR
71	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523.00	2523.00	1011.64	0.00	23	1. Slow progress by the contractor in laying of pipelines. 2 Delay in conversion work of Sagar Samrat to MOPU. 3. Delay in drilling of some wells due to non-availability of light rig.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
72	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	12/2015	736.65	736.65	449.94	0.00	51	1. Delay in preparation of drawing and additional model testing of Hull form in Austria . 2. Shortage of skilled manpower at contractor's end. 3. Inadequate ancillary/sub-contractors at the location. 4. Lack of planning to match resources to work targets. 5. Change in delivery location.
73	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV)	ONGC	01/2010	03/2013	06/2016	723.64	723.64	0.00	0.00	39	1. Revision in scope of work. 2. Closure of original tender due to high quoted price.
74	AHMEDABAD REDEVELOPMENT	ONGC	11/2010	12/2014	12/2016	1916.10	1916.10	784.46	0.00	24	1.Preparation of TBP and cost estimation takes too much time. 2. Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and layout of control rooms etc. 3. Preparation of pre-bid replies in view of the quantum and complexities

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
75	ANKLESWAR REDEVELOPMENT	ONGC	11/2010	12/2014	12/2016	2189.63	2189.63	1039.42	0.00	24	1. Preparation of TBP and cost estimation 2. Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and lay out of control rooms etc. 3. Preparation of pre-bid replies in view of the quantum and complexities.
76	MEHESANA REDEVELOPMENT	ONGC	11/2010	04/2015	03/2017	3823.00	3823.00	1076.07	0.00	23	1. Preparation of TBP and cost estimation 2. Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and lay out of control rooms etc. 3. Preparation of pre-bid replies in view of the quantum and complexities
77	ADDITIONAL DEV. OF D-1 FIELD	ONGC	01/2010	06/2012	06/2014	2163.64	2331.62	2182.31	7.76	24	Delay in installation of well platforms due to delay in material supply and punch through location

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
78	DEVELOPMENT OF C-SERIES FIELDS	ONGC	08/2006	12/2008	05/2015	3195.16	3690.37	3068.29	15.50	77	1. Two decks sunk into international waters which necessitated re-fabrication of the decks. 2. Delay in taking up drilling of all planned wells due to subsurface studies and re-prioritization of locations
79	DEVELOPMENT OF B-22 CLUSTER FIELDS	ONGC	01/2007	09/2010	12/2015	2323.40	2920.82	1915.45	25.71	63	1. Delay in finalization of tender due to representation by bidders in IEM and further in High Court and Supreme Court. 2. Scope optimization and preparation of new bid package during re-tendering. 3. Drilling of wells and re-prioritization of locations in view of geological surprises.
80	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR	ONGC	03/2009	09/2012	12/2014	234.78	317.64	102.78	35.29	27	Slow progress in civil and fabrication work due to less resource mobilization.
81	DEVELOPMENT OF B-193 CLUSTER FIELDS	ONGC	06/2007	08/2010	05/2015	3248.78	6000.00	5855.00	84.68	57	1. Contract terminated as contractor failed to submit PBG insurance. 2. Splitting of facility into three packages, scope optimization in view of the price rise in oil field services/equipments and preparation of fresh bid packages. 3. Increased facility.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
82	DEVELOPMENT OF CLUSTER-7 FIELDS	ONGC	03/2010	03/2013	11/2014	3241.03	6638.94	2192.69	104.84	20	Delay in award of work for project facilities (well platforms & pipelines, hiring of FPSO)
83	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	2735.65	2728.25	536.46	110	Non-cooperation by equipments suppliers, sub-contractors and consultant, delay in availability of subsea manifold and prolonged repairing work and complications in well G-1-9 and well control activities.
	POWER										
84	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.90	4653.95	2940.49	86.39	87	Adverse geo-mining & contractual issues.
85	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	09/2015	573.99	1128.38	840.66	96.59	25	Law & order, adverse weather & geo-mining condition.
86	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	11/2014	421.01	951.48	765.07	126.00	16	NR
87	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	01/2011	07/2006	12/2015	368.72	913.63	601.12	147.78	113	Ban on mining, inadequate infrastructure.
88	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	NHPC	09/2005	09/2009	03/2016	1061.38	1061.38	1502.70	0.00	78	Cash problem of civil contractor.
89	PARBATI HEP (NHPC) II	NHPC	09/2002	09/2009	07/2018	3919.59	3919.59	4474.99	0.00	106	Cash problem of contractor.
90	SUBANSIRI LOWER H.E.P (NHPC)	NHPC	09/2003	09/2010	12/2018	6285.33	6285.33	6858.57	0.00	99	Stoppage of work due to agitation by AASU.
91	KISHANGANGA HEP	NHPC	07/2007	01/2016	11/2016	2238.67	3642.04	3403.83	62.69	10	Employment issue.
92	BARH STPP STAGE -II	NTPC	02/2008	08/2013	03/2015	7341.04	7341.04	7590.00	0.00	19	Delay in supply of materials by BHEL.
93	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	07/2011	08/2016	4375.35	4375.35	4540.00	0.00	61	Contractual issues, law & order problem.
94	BARH STPP(3X660MW) NTPC	NTPC	12/2003	12/2009	03/2017	8692.97	8693.00	10036.00	0.00	87	1. Delay in supply of equipments, 2. Slow progress by implementing agencies.

SN	PROJECT	IMPLIMEN TING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
95	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	03/2017	2978.48	3846.30	2121.00	29.14	48	Adverse weather condition (flash flood & heavy rainfall)
96	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	05/2015	4527.15	7220.00	5915.00	59.48	73	Right Bank slide, Seepage problem in main dam.
97	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	06/2014	1366.34	1366.34	996.76	0.00	6	Forest clearance
98	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	06/2014	965.58	965.58	667.64	0.00	19	Severe ROW Problem.
99	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC	PGCIL	08/2008	08/2012	06/2014	7075.33	7075.33	6344.56	0.00	22	1. Environmental clearance, 2. Law & order problems.
100	SYSTEM STRENGTHENING -XII OF SR	PGCIL	02/2010	06/2012	06/2014	232.34	232.34	185.19	0.00	24	ROW Problem.
101	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP	PGCIL	02/2009	11/2011	06/2014	184.19	184.19	161.72	0.00	31	NR
102	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2014	477.69	477.69	483.89	0.00	45	ROW Problem.
103	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION)	PGCIL	03/2012	03/2014	08/2014	213.78	213.78	129.24	0.00	5	NR
104	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED	PGCIL	08/2011	10/2013	08/2014	425.51	425.51	376.82	0.00	10	ROW problem
105	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2014	487.49	487.49	287.52	0.00	3	ROW Problem.
106	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	09/2014	1961.87	1961.87	1434.25	0.00	4	Contract termination due to poor performance
107	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD	PGCIL	01/2012	01/2014	09/2014	259.28	259.28	160.62	0.00	8	Delay due to type testing of GIS equipment of substation.
108	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	09/2014	2074.86	2074.86	1544.34	0.00	18	Non- availability of shut down by OPTCL.

SN	PROJECT	IMPLIMEN TING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
109	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	PGCIL	08/2011	12/2013	11/2014	1391.97	1391.97	1380.35	0.00	11	Forest clearance
110	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	12/2014	1940.13	1940.13	1325.76	0.00	3	NR
111	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPSS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	12/2014	2127.51	2127.51	1853.33	0.00	5	Delay in forest clearance & ROW problems.
112	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	12/2014	2569.25	2569.25	2436.07	0.00	9	Wildlife sanctuary clearance awaited
113	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	PGCIL	12/2010	12/2013	12/2014	2743.19	2743.19	2122.08	0.00	12	Environmental clearance awaited.
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	12/2014	1677.57	1677.57	1037.82	0.00	20	ROW Problem.
115	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP)	PGCIL	12/2009	08/2012	12/2014	1216.83	1216.83	989.09	0.00	28	Contractual issues.
116	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	03/2015	552.44	552.44	412.30	0.00	13	ROW Problem.
117	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	03/2015	558.26	558.26	287.31	0.00	16	Environmental clearance awaited.
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	03/2015	752.64	752.64	383.12	0.00	20	Environmental clearance awaited.
119	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ.	PGCIL	03/2010	11/2012	03/2015	4672.99	4672.99	3088.37	0.00	28	Environmental clearance awaited.
120	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2015	4824.12	4824.12	3888.78	0.00	29	Environmental clearance
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	04/2015	05/2015	524.40	524.40	105.70	0.00	1	NR

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
122	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	05/2015	1746.65	1746.65	407.83	0.00	9	Environmental clearance awaited
123	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2015	3201.44	3201.44	1543.91	0.00	8	Land acquisition
124	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	06/2015	2422.66	2422.66	1026.16	0.00	10	Forest clearance awaited.
125	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	06/2015	1585.12	1585.12	1220.26	0.00	19	ROW problem.
126	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	06/2015	11130.19	11130.19	8436.00	0.00	22	ROW Problem.
127	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	06/2015	250.03	250.03	68.80	0.00	29	Land acquisition
128	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2015	2144.00	2144.00	1739.80	0.00	30	ROW Problem
129	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	06/2015	1272.80	1272.80	836.13	0.00	31	Land acquisition
130	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	12/2015	9569.76	9569.76	1902.59	0.00	6	NR
131	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B	PGCIL	04/2010	01/2015	12/2015	4404.57	4404.57	489.75	0.00	11	Wild life clearance awaited from state WL Board
132	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII	PGCIL	02/2014	08/2014	08/2016	243.53	243.53	0.00	0.00	24	NR
133	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC	PGCIL	08/2008	08/2012	09/2014	2360.95	2580.90	2120.41	9.32	25	Law & order problems.
134	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCL	08/2008	07/2014	07/2018	2491.58	3745.08	485.66	50.31	48	Rehabilitation & resettlement issues
135	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCL	07/2006	07/2010	02/2017	1657.00	2978.86	712.67	79.77	79	Ban on mining activity

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
	RAILWAYS										
136	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	12/2014	921.00	2363.00	1371.16	156.57	69	NR
137	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2116.80	367.76	98	NR
138	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	12/2014	207.52	207.52	199.88	0.00	24	NR
139	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	FOIS	03/1984	03/1995	03/2015	520.00	835.04	646.73	60.58	240	Increase in scope of work.
140	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2015	495.74	495.74	267.13	0.00	21	NR
141	MULTI MODAL TRANSPORT SYSTEM(MM TS) PHASE-II HYDERABAD	M RTP	04/2012	04/2012	03/2016	632.68	816.55	17.40	29.06	47	NR
142	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	12/2016	5300.00	7952.58	1739.04	50.05	33	NR
143	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	12/2014	401.81	1814.10	376.57	351.48	129	Fund constraints
144	ETAWAH-MAINPURI (NL),NCR	NCR	09/2001	12/2008	09/2014	120.00	245.39	227.22	104.49	69	NR
145	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	09/2014	158.77	608.02	586.81	282.96	246	Delayed due to occurrence of crack in pier
146	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	12/2014	108.00	432.72	403.29	300.67	60	Land acquisition
147	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NEFR	04/1999	03/2007	03/2017	895.00	1242.25	959.83	38.80	120	Fund constraints
148	KATAKHAL TO BHAIRABI	NEFR	04/1998	12/2012	03/2016	227.90	331.40	140.02	45.41	39	Fund constraints
149	KATIHAR - JOGBANI (GC)(NEFR)	NEFR	09/2001	12/2010	03/2015	492.98	1022.64	742.61	107.44	51	Fund constraints
150	AGARTALA SABROOM, NL, NEFR	NEFR	04/2008	03/2014	03/2017	813.34	1741.00	609.11	114.06	36	Fund constraints
151	SEVOK RANGPO, NEFR	NEFR	04/2008	12/2015	03/2017	1339.48	3375.42	85.23	151.99	15	Wild life clearance awaited.
152	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NEFR	04/2006	03/2015	03/2017	850.00	2446.57	9.23	187.83	24	Change in original alignment.
153	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NEFR	04/1996	03/2009	03/2017	1676.31	5185.44	4253.73	209.34	96	Fund constraints

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NEFR	04/2000	12/2008	03/2017	733.00	2483.04	1581.17	238.75	99	1. Fund constraints, 2. Land acquisition.
155	BHAIRABI SAIRONG, NL, NEFR	NEFR	04/2008	04/2014	03/2017	619.34	2393.48	174.83	286.46	35	Environmental clearance awaited
156	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	NEFR	09/1997	04/2008	12/2017	1000.00	4996.19	3160.19	399.62	116	Fund constraints
157	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NEFR	04/2003	03/2011	03/2017	727.56	5996.00	2216.69	724.12	72	Fund constraints
158	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1116.53	302.32	243.55	84	Court cases
159	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2017	2500.00	20000.00	8805.00	700.00	181	NR
160	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	10/2014	171.10	246.44	141.55	44.03	31	NR
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	03/2016	2298.42	2298.42	64.64	0.00	24	NR
162	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	RVNL	04/2010	03/2016	06/2016	2397.72	2397.72	84.44	0.00	3	Encroachment along the proposed alignment
163	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	795.45	16.41	69	NR
164	RAJATGARH-BARANG(LD),ECOR	RVNL	04/1999	02/2009	08/2014	166.16	288.00	307.18	73.33	66	Contractual issues
165	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	08/2014	133.41	276.00	279.04	106.88	65	Contractual issues
166	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	03/2015	393.46	445.40	180.41	13.20	96	1. Land acquisition , 2. Fund constraints.
167	TAMLUK-BASULYA-SUTAHATA DOUBLING	SER	04/2010	06/2013	12/2014	146.95	171.02	141.84	16.38	18	NR
168	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2015	149.90	184.91	58.81	23.36	9	NR
169	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	03/2016	309.44	388.67	83.91	25.60	3	Delayed due to acute sand problem & foundation problem
170	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	06/2015	194.07	596.40	378.37	207.31	132	Law & order problems.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
171	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	06/2016	293.97	1074.45	457.17	265.50	132	1. Rehabilitation & resettlement issues 2. Fund constraints.
172	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2016	111.90	1423.98	480.78	1172.55	141	1. Rehabilitation & resettlement issues 2. Fund constraints.
ROAD TRANSPORT AND HIGHWAYS											
173	KOTA BYPASS, RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	06/2014	275.00	250.39	284.10	0.00	68	NR
174	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	06/2014	1813.76	1813.76	1092.00	0.00	11	NR
175	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	06/2014	600.00	600.00	312.80	0.00	12	NR
176	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	06/2014	1693.75	1693.75	2762.00	0.00	34	NR
177	DHARAMTUL TO SONAPUR (AS-19)	NHAI	12/2003	06/2008	06/2014	200.00	200.00	268.70	0.00	72	NR
178	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	06/2014	264.72	264.72	311.60	0.00	72	NR
179	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	06/2014	245.00	245.00	491.20	0.00	75	NR
180	LUCKNOW-RAIBAREILI	NHAI	07/1999	07/2012	07/2014	635.90	635.90	567.10	0.00	24	NR
181	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	07/2014	795.00	795.00	1128.00	0.00	26	NR
182	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	08/2014	574.00	574.00	888.30	0.00	5	NR
183	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	08/2014	835.00	835.00	471.40	0.00	7	NR
184	DEOLI-KOTA	NHAI	01/2011	07/2013	08/2014	593.00	593.00	726.30	0.00	13	NR
185	AMRITSAR-PATHANKOT	NHAI	05/2010	11/2012	08/2014	705.00	705.00	2184.00	0.00	21	NR
186	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	08/2014	232.45	232.45	309.10	0.00	47	NR
187	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	NHAI	11/2011	05/2014	09/2014	909.00	909.00	963.00	0.00	4	NR
188	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	09/2014	624.00	624.00	433.30	0.00	5	NR

SN	PROJECT	IMPLIMEN TING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
189	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	12/2013	09/2014	535.00	535.00	52.18	0.00	9	NR
190	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	09/2014	1250.00	1250.00	1281.00	0.00	9	NR
191	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	09/2014	511.54	511.54	1177.00	0.00	10	NR
192	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	09/2014	571.00	571.00	0.00	0.00	11	NR
193	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	09/2014	1141.00	1141.00	2024.00	0.00	13	NR
194	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	09/2014	225.00	225.00	275.60	0.00	75	NR
195	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	NHAI	12/2003	05/2008	10/2014	160.00	160.00	211.20	0.00	77	NR
196	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	10/2014	198.16	198.16	318.50	0.00	78	NR
197	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	11/2014	953.88	953.88	856.70	0.00	16	NR
198	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2014	1100.70	1100.70	254.30	0.00	6	NR
199	JORBAT - BARAPANI	NHAI	01/2011	01/2014	12/2014	536.00	536.00	664.90	0.00	11	NR
200	4-LANING OF BRAHAMPORE- FARAKA	NHAI	02/2011	08/2013	12/2014	998.79	998.79	1524.00	0.00	16	NR
201	CUDDAPAH-MYDUKUR- KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	12/2014	1585.00	1585.00	957.80	0.00	19	NR
202	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2014	374.00	374.00	146.40	0.00	19	NR
203	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	12/2014	1175.00	1175.00	138.70	0.00	20	NR
204	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM	NHAI	09/2010	03/2013	12/2014	852.00	852.00	886.70	0.00	21	NR
205	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2014	1724.55	1724.55	1207.00	0.00	21	NR
206	SAMAIKHALI - GANDHIDHAM	NHAI	09/2010	03/2013	12/2014	805.39	805.39	813.40	0.00	21	NR
207	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2014	671.30	671.30	630.90	0.00	22	NR
208	WADNER-DEVDHARI(NS- 60/MH)(KM 94-123 KM)	NHAI	02/2011	11/2012	12/2014	193.45	193.45	63.78	0.00	25	NR
209	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2014	1509.10	1509.10	2398.00	0.00	27	NR
210	CHENNAI-TADA(SIX LANE)	NHAI	04/2009	10/2011	12/2014	353.37	353.37	446.20	0.00	38	NR
211	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	12/2014	486.00	486.00	661.90	0.00	55	NR

SN	PROJECT	IMPLIMEN TING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
212	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	NHAI	03/2005	02/2010	12/2014	557.00	557.00	1118.00	0.00	58	NR
213	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	12/2014	200.00	200.00	195.10	0.00	68	NR
214	HARANGAJO TO MAIBANG (AS- 23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	12/2014	280.00	280.00	354.10	0.00	70	NR
215	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	12/2014	167.64	167.64	114.30	0.00	73	NR
216	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	NHAI	12/2003	10/2008	12/2014	251.03	251.03	372.40	0.00	74	NR
217	FORBESGANJ TO SIMRAHI (NH- 57)(NHAI)	NHAI	12/2003	09/2008	12/2014	332.94	332.94	519.40	0.00	75	NR
218	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	12/2014	175.96	175.96	266.30	0.00	80	NR
219	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2014	208.00	208.00	320.20	0.00	80	NR
220	SILCHAR-UDARBAND (PH.II) HN- 54, KM.309 TO KM.275	NHAI	12/2003	09/2007	12/2014	157.47	157.47	262.30	0.00	87	NR
221	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	02/2015	485.00	485.00	346.20	0.00	18	NR
222	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	03/2015	828.00	828.00	683.20	0.00	6	NR
223	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	03/2015	500.29	500.29	622.10	0.00	19	NR
224	4-LANNING OF CHAPRA- HAJIPUR	NHAI	01/2011	07/2013	03/2015	575.00	575.00	824.60	0.00	20	NR
225	MURADABAD-BAREILY	NHAI	04/2010	06/2013	03/2015	1267.00	1267.00	2244.00	0.00	21	NR
226	BRAHMPUTRA BRIDGE, NH NO- 31	NHAI	12/2003	04/2010	03/2015	217.61	217.61	438.80	0.00	59	NR
227	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	12/2003	06/2008	03/2015	237.80	237.80	309.20	0.00	81	NR
228	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	NHAI	12/2003	06/2008	03/2015	195.00	195.00	267.00	0.00	81	NR
229	SIX LANNING OF NELLORE- CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	05/2015	1535.00	1535.00	1328.00	0.00	12	NR
230	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	06/2015	1078.84	1078.84	1611.00	0.00	22	NR
231	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	NHAI	05/2009	10/2011	06/2015	572.30	572.30	886.90	0.00	44	NR

SN	PROJECT	IMPLIMEN TING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
232	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	06/2015	230.00	230.00	243.40	0.00	120	NR
233	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	07/2015	2498.76	2498.76	2660.00	0.00	11	NR
234	4-LANING OF BARHI- HAZARIBAGH	NHAI	02/2012	02/2014	09/2015	398.00	398.00	457.60	0.00	19	NR
235	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	10/2015	1410.00	1410.00	701.80	0.00	13	NR
236	FOUR LANNING OF WALAYAR- VADAKKANCHERRY SECTION	NHAI	04/2011	10/2013	11/2015	682.00	682.00	562.50	0.00	25	NR
237	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	12/2015	702.16	702.16	682.00	0.00	17	NR
238	PANVEL-INDAPUR	NHAI	12/2011	06/2014	12/2015	942.69	942.69	285.80	0.00	18	NR
239	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2015	2848.00	2848.00	1042.00	0.00	21	NR
240	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2015	291.36	291.36	136.20	0.00	23	NR
241	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	NHAI	11/2011	10/2013	12/2015	478.00	478.00	310.20	0.00	26	NR
242	BAREILY-SITAPUR	NHAI	03/2011	09/2013	12/2015	1046.00	1046.00	375.40	0.00	27	NR
243	4-LANING OF RAIGANJ- DALKOLA	NHAI	02/2011	08/2013	12/2015	580.43	580.43	325.10	0.00	28	NR
244	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	12/2015	325.00	325.00	598.40	0.00	31	NR
245	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2015	754.00	754.00	589.90	0.00	33	NR
246	BHOPAL-SANCHI	NHAI	10/2011	01/2013	12/2015	209.00	209.00	38.77	0.00	35	NR
247	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	12/2015	604.00	604.00	495.40	0.00	72	NR
248	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	02/2016	867.00	867.00	598.60	0.00	12	NR
249	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240- 270KM)	NHAI	02/2010	08/2012	03/2016	617.00	617.00	155.50	0.00	43	NR
250	NASHRI CHANANI	NHAI	06/2010	06/2015	05/2016	2159.00	2159.00	512.90	0.00	11	NR
251	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987.00	1987.00	1136.00	0.00	11	NR
252	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586.00	586.00	237.60	0.00	35	NR
253	4 LANNING OF BELGUM- KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359.00	359.00	39.49	0.00	39	NR
254	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	06/2016	275.00	281.31	180.10	2.29	76	NR
255	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75- 80.06	NHAI	12/2003	09/2008	12/2014	155.00	201.66	171.80	30.10	75	NR

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
256	AGRA-BYPASS(NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	06/2015	348.16	465.50	282.50	33.70	93	NR
257	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	09/2014	155.04	280.13	167.20	80.68	70	NR
258	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	03/2015	212.00	386.10	123.00	82.12	90	NR
259	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2014	196.00	363.74	227.00	85.58	65	NR
260	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2015	199.81	385.13	127.10	92.75	71	NR
261	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2015	1108.00	2288.00	3466.00	106.50	40	NR
SHIPPING AND PORTS											
262	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	MUMBAI PORT TRU	11/2007	12/2010	10/2015	1228.00	2158.16	1005.88	75.75	58	Scrutiny of technical bid is in progress.
263	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	06/2014	150.00	600.00	139.80	300.00	99	Land acquisition.
264	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY	SHIPP.	01/2012	03/2014	08/2014	511.87	511.87	106.72	0.00	5	NR
STEEL											
265	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	NMDC	04/2011	04/2013	09/2014	572.00	572.00	381.69	0.00	17	NR
266	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	NMDC	02/2011	05/2013	01/2015	898.55	898.55	295.38	0.00	20	Re-tendering and construction delays
267	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC)	NMDC	01/2007	12/2011	01/2015	295.89	607.17	372.46	105.20	37	1. Maoist activities, 2. Fire incident.
268	AUGMENTATION OF IRON ORE STORAGE IN RMHP	RINL	07/2007	09/2009	12/2014	480.00	450.00	311.70	0.00	63	Re-tendering and lack of consultants
269	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	09/2014	8692.00	12291.00	10855.72	41.41	59	Poor mobilization by contractors
270	COKE OVEN BATTERY NO. 4 PHASE-II	RINL	06/2006	09/2008	06/2014	108.00	216.68	160.73	100.63	69	NR
271	EXPANSION OF BOKARO STEEL PLANT	SAIL	05/2010	12/2011	07/2014	6325.00	6325.00	4673.10	0.00	31	Packages approved at different times
272	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	08/2014	187.33	187.33	126.81	0.00	10	NR

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
273	EXPANSION OF ROURKELA STEEL PLANT	SAIL	08/2010	03/2013	09/2014	11812.00	11812.00	11151.97	0.00	18	NR
274	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	03/2015	17265.00	17265.00	12803.22	0.00	24	NR
275	EXPANSION OF DURGAPUR STEEL PLANT	SAIL	08/2010	12/2012	03/2015	2875.00	2875.00	2191.19	0.00	27	NR
276	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES	SAIL	11/2011	11/2013	06/2015	254.55	254.55	109.87	0.00	19	NR
277	EXPANSION OF IISCO STEEL PLANT	SAIL	06/2008	12/2011	07/2014	14443.00	16408.00	15945.82	13.61	31	1. Soil related problems. 2. Delay in approval of engineering design from railway authorities.
TELECOMMUNICATIONS											
278	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II	BSNL	07/2010	05/2011	06/2014	1148.19	964.37	251.27	0.00	37	Delay in supply by one of the vendor M/s Gemini, the PO placed 2707 BTS on the firm terminated by office of CGM STP. Presently the case is sub judice.
279	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	BSNL	06/2007	01/2009	09/2014	336.81	336.81	183.16	0.00	68	1. Municipal permission issue 2. Electric connection issue 3. Delay in permission to lay optical fiber cable from local bodies 4. Non availability of suitable sites 5. Security issue for working staff in remote area and frequent strikes.

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (%)	TIME OVERRUN (MONTHS)	REASONS FOR DELAY (AS REPORTED BY PROJECT IMPLEMENTING AGENCIES)
280	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	12/2014	384.00	384.00	29.45	0.00	50	1. Issue related to change of business process. 2. Integration issue with CDR system 3. Procurement of additional server storage 4. Issues related to vendor.
281	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL	BSNL	01/2009	06/2009	06/2014	149.15	158.72	84.81	6.42	60	The project is delayed due to difficulty in acquisition /hiring of site.
	URBAN DEVELOPMENT										
282	FARIDABAD EXTENSION	DMRC	09/2011	09/2014	05/2015	2494.00	2494.00	685.21	0.00	8	NR
